

LAS VEGAS STADIUM

Monthly Report - March 2019







LV Stadium Events Company, LLC

April 30, 2019

Mr. Steve Hill Chairman Las Vegas Stadium Authority c/o Applied Analysis 6385 S. Rainbow Blvd, Ste 105 Las Vegas, NV 89118

Dear Mr. Hill:

Enclosed is StadCo's monthly Project Status Report covering the development of the Las Vegas Stadium.

We continue to work through schedule challenges imposed by delays in the fabrication and erection of major structural steel in an effort to preserve the Substantial Completion date of July 31, 2020. Although the sequencing and durations of the schedule's 22-thousand tasks continue to change, the Project is on track for an on-time completion.

The Project also remains within its budget. Through the current funding disbursement we have spent approximately \$805 million. The public sector contribution represents 35% with StadCo and the Raiders supplying the remaining 65%.

We are evaluating a range of possible scope and other building enhancements to be undertaken and funded through proceeds of the suite and seat sales program which continues to outperform its budgeted results.

Nearly 70% of all subcontracted work has been awarded to Nevada-based firms.

The Project continues to outperform its 15% SBE contracting goal, with 19% of the subcontracted work awarded to 77 individual SBE firms.

In addition to exceeding our local Small Business contracting goal, we continue to be well above our workforce diversity goal of 38% minority and women participation. Approximately 68% of the 1.3 million construction workforce hours have been filled by minority and female workers.

Sincerely,

Don C. Webb

Chief Operating Officer







TABLE OF CONTENTS

Certification	1
Project Budget	2
Status of Design Planning	3
Permit Tracker	4
Project Schedule	5
Compliance / SBE	7
Workforce Utilization	41
Additional Information / Updates	45

CERTIFICATION

Pursuant to Article 8, Section 8.1 of the Development Agreement between Clark County Stadium Authority and LV Stadium Events Company, LLC dated March 28, 2018, I hereby certify that the information contained within this "Project Status Report" is true and accurate to the best of my knowledge.

Sincerely,

Don C. Webb Chief Operating Officer LV Stadium Events Company, LLC



Stadium Project Budget Report

LAG SCIANS STADIGGE	Initial Budget	Adjustments	Revised Budget	Total Expended	Total Expended		
Raiders Equity Contribution [1]	\$850,000,000	\$40,000,000	\$890,000,000	\$497,852,245	56%	\$392,147,755	44%
Raiders NFL G-4 Contribution [2]	\$200,000,000	\$0	\$200,000,000	\$28,919,255	14%	\$171,080,745	86%
Clark County Bond Proceeds & Room Tax Pay-Go	\$750,000,000	\$0	\$750,000,000	\$278,699,076	37%	\$471,300,924	63%
Other	\$0	\$0	\$0	\$0	0%	\$0	100%
Total Stadium Development Sources	\$1,800,000,000	\$40,000,000	\$1,840,000,000	\$805,470,576	44%	\$1,034,529,424	56%
Stadium Land Acquisition	\$77,780,128	\$12,975	\$77,793,103	\$77,793,103	100%	\$0	0%
Stadium Construction	\$1,334,455,080	\$0	\$1,334,455,080	\$522,689,016	39%	\$811,766,065	61%
Stadium Furniture, Fixtures & Equipment	\$122,854,543	\$0	\$122,854,543	\$646,389	1%	\$122,208,154	99%
Stadium Design, Engineering & Soft Costs	\$233,852,243	(\$12,975)	\$233,839,268	\$159,842,790	68%	\$73,996,477	32%
Stadium Utility & Infrastructure Costs	\$31,058,006	\$0	\$31,058,006	\$7,264,438	23%	\$23,793,568	77%
Premium Seating & Marketing Program	\$0	\$40,000,000	\$40,000,000	\$37,234,840	93%	\$2,765,160	7%
Total Stadium Development Uses	\$1,800,000,000	\$40,000,000	\$1,840,000,000	\$805,470,576	44%	\$1,034,529,424	56%

^[1] Includes closed construction debt financing pursuant to Senate Bill 1 (2016 Special Session), Section 36.1(e)(2). Raiders Equity Contribution, above, includes \$40 million in PSL sales used to fund Premium Seating & Marketing Programs.

[2] Includes approved NFL financing through the G-4 loan program of the NFL.

Excludes:

Off-Site Parking and Parking Shuttle Transportation System Development

Training Center and Team Headquarters Development

The accompanying notes to the financial report, above, are integral to this presentation and should be consulted when reviewing its contents



Summary Notes:

- 1) Initial Budget" is as of March 17, 2018
- 2) "Revised Budget" reflects adjustments under consideration & does not include all costs borne solely by StadCo or the Raiders such as costs of developing the team headquarters and training facilities
- 3) "Expended" is based upon actual costs & accrual estimates booked, including retention amounts withheld, as of April 15, 2019
- 4) "Expended" excludes certain predevelopment costs recovered through bond proceeds at closing
- 5) Excludes StadCo or Raiders payroll costs, legal & similar administrative expenses incidental to Stadium development but borne solely by StadCo or Raiders
- 6) Excludes NFL Relocation Fee
- 7) Excludes Temporary Venue Costs
- 8) Excludes certain costs associated with financing and transactional expenses borne by the Raiders
- 9) Actual Balance on individual Sources may vary from that shown above since certain sources are funded on a reimbursable, rather than advance, basis
- 10) Projections are based upon assumptions and information received from others and therefore actual results may vary and the variations may be material

STATUS OF DESIGN PLANNING

During the bi-weekly AHJ meeting with the Clark County Building and Fire Department held on Thursday, March 28, HNTB presented the NEZFC plan. The goal was to introduce the County to this area of the building, reach consensus on exiting and fire-proofing issues. This package will be submitted as an addendum to PP 6 on April 26. PP6 includes all the other premium spaces such as the clubs, suites and a select few team spaces. On March 8 and again on March 29, HNTB issued an addendum to both PP5 and PP6 primarily to address Food Service Changes – Priority A. There will be a Design Refinement Meeting early in April to review finishes and FFE for the NEZFC.

The FFE Package was released on March 19. Orders have been placed for samples of all forward facing furniture elements for a final review by Ownership.

Permits received to date include all foundations (Package 2), and all concrete construction permits (Packages 3A & 3B) and the structural steel frame package (permit package 4). All structural building permits for the project are now secured. Non-structural permits received include the Shell, Core and all non-premium spaces (Package 5). Premium spaces – clubs, typical suites and select Team spaces (Package 6).

Upcoming Milestone Dates for Design Deliverables:

April 26, 2019 - North End-Zone Field Club (NEZFC), Owner's Suite, potentially some of the Double Suites.

Second Quarter 2019 (TBD) - Package X – Main Ticket Office Building & Ticket Canopies



Phased Building Application

Proposed Permit Packages / Valuations Revised 2/1/2019






HNTB

		·			
	IT PACKAGE	DESCRIPTION / SCOPE OF WORK	Permit Submission Date (estimates in italics)	Permit Pick-up & Fee Payment Date (estimates in italics)	ANTICIPATED VALUE
No#	PAC NO				
1		EGRESS DESIGN			\$
2		FIRE PROTECTION REPORT			\$
		FIRE PROTECTION REPORT			Ş
3	1	EXCAVATION & GRADING	11/13/2017	12/19/2017	\$12,700,000
	-	EAGATITION & CLUBBING	11/15/2017	12/13/2017	ψ12), σσήσσο
4	1a	ON-SITE UTILITIES			\$5,800,000
5	2	FOUNDATIONS / DEEP UTILITIES	1/10/2018	2/20/2018	\$46,000,000
		Piles, Pile caps, dowels into first lift			
6		CABLE TRUSS ANALYSIS REVIEW			
_	20	CTDUCTURAL FRAME CONCRETE	2/12/2018	4 /C /2010	¢04 000 000
/	3a	STRUCTURAL FRAME - CONCRETE Concrete columns & walls to Level 050, Areas AFBE only	3/13/2018	4/6/2018	\$84,000,000
		Concrete columns & wans to Level 030, Areas Ar BE only			
8	3b	STRUCTURAL FRAME - CONCRETE	3/19/2018	5/10/2018	\$42,000,000
	52	Concrete to Level 0100, Areas AFBE only	3,13,2010	3/10/2010	ψ : <u>Σ</u> ,ουσ,ουσ
9	4	STRUCTURAL FRAME - STEEL / ROOF	4/6/2018	6/22/2018	\$290,200,000
		Remaining structtre in AFBE & all Areas C & D			
10	5	CONSTRUCTION PACKAGE 5 (Arch,Mech,Elect,Plumb)	7/10/2018	11/16/2018	\$552,200,000
		Core & Shell Package			
11		FINISHES DACKACE Dromain on Small	11/0/2018	2/1/2010	¢54 500 000
11	6	FINISHES PACKAGE - Premium Spaces	11/9/2018	2/1/2019	\$54,500,000
		Ancillary Permits			
		Trailer City permit (Tortoise fees paid with this permit)	10/5/2017	11/9/2017	
		On-site Utility for Trailer City	11/5/2017	11/29/2017	
		· · · · · ·			
		DEFERRED SUBMITTALS			
					444
12		STRUCTURAL PRECAST SYSTEMS			\$32,400,000
13		FIDE CLIDDECCION CODINIVIED CVCTCAC			Ć10 700 000
13		FIRE SUPRESSION SPRINKLER SYSTEMS			\$10,700,000
	L				


\$ 1,130,500,000

Permit Packages

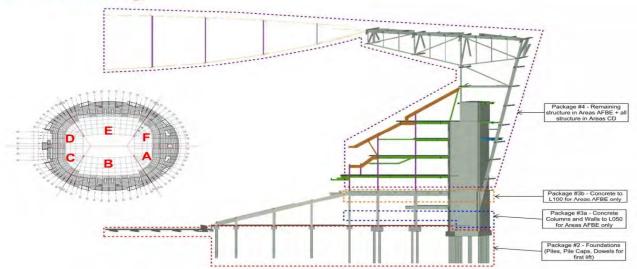

Permit Tracker

ctivity ID	Activity Name			Jan Feb Mar Apr May Jun					
A	**************************************	Oct Nov Dec	Jan	Feb	Mar	Apr	May Ju	n J	
Summary and								-	
S000-8D	Design Summary - Stadium Design to 62.5% GMP							1	
S000-8D1	Design Summary - Stadium Design to 100% GMP Pricing	1 0						1	
S000-8D2	Design Summary - Stadium Design to 100% CD							1	
S000-8D3	Design Summary - Design Construction Administration		فدوناء	-	Daniel C				
S000-8M4	Construction Summary - Mass Excavation							-	
S000-8N1	Construction Summary - Deep Foundations							i	
S000-8N2B	Construction Summary - FRP Wall/Mat Foundations								
S000-8N2C	Construction Summary - FRP Spread Footings								
S000-8N3B	Construction Summary - Foundation Walls			1					
S000-8N5A	Construction Summary - FRP Elev/Esc Pits								
S000-8P1	Construction Summary - Underground Mech/Plumbing & Elec								
S000-8P1E	Construction Summary - Slab on Grade								
S000-8P2B	Construction Summary - FRP Concrete Core Walls			1	1			÷	
S000-8P2C	Construction Summary - FRP Columns		line,	1				÷	
S000-8P2G	Construction Summary - Pan & Joist Decks		22222		1 × × 2			10	
S000-8P4D	Construction Summary - Steel Roof Truss Columns								
S000-8P4	Construction Summary - Steel Structure (Bowl Steel)							1	
S000-8P4B	Construction Summary - Structural Steel (Long Span at Field Tra	ay)						-	
S001-8P4D	Construction Summary - Steel Roof Canopy							3	
S000-8P4F2	Construction Summary - FRP Slab on Metal Deck		opries.	drawn.				Ť	
S000-8P4J	Construction Summary - Misc Structural Supports							1	
S000-8P5G	Construction Summary - Precast Stadia			1				1	
S000-8Q1F	Construction Summary - Metal Wall Panels			1			E	Ť	
S000-8Q2A	Construction Summary - Curtainwall						Ē	Ť	
SXXN-8Q3C5	Construction Summary - Storefront Glazing System			free		3		-	
S000-8Q3S	Construction Summary - Specialty Entrances Op Doors							Ė	
S000-8Q5	Construction Summary - Roof Systems							1	
SRA0-8Q52	Construction Summary - Membrane Roof Systems			1				-	
S000-8Q5J	Construction Summary - Roof Specialties & Accessories							÷	
S1B48R13	Construction Summary - Elevators		457,779	deres	1-77		 	eder.	
S000-8R3	Construction Summary - Escalators			1				1	
S1AB1-8S53	Construction Summary - Interior Rough-in			1				i	
S000-8T1B	Construction Summary - Mechanical Equipment							-	
S000-8T7	Construction Summary - Specialty Equipment			1				1	
S000-8T7P1	Construction Summary - Sports Equipment		- dice-	-	11.33			Ť	
S000-8171	Construction Summary - Drywall and Interior Finishes							-	
S000-8U8	Construction Summary - Specialties			1				-	
S000-8U9	Construction Summary - Specializes	1 1						100	
S000-809 S000-8V	Construction Summary - Seaung Construction Summary - Site Improvements							-	
				ļ				·	
S000-8X31 L001-1A50	Construction Summary - Project Close-out Substantial Completion			1				3	

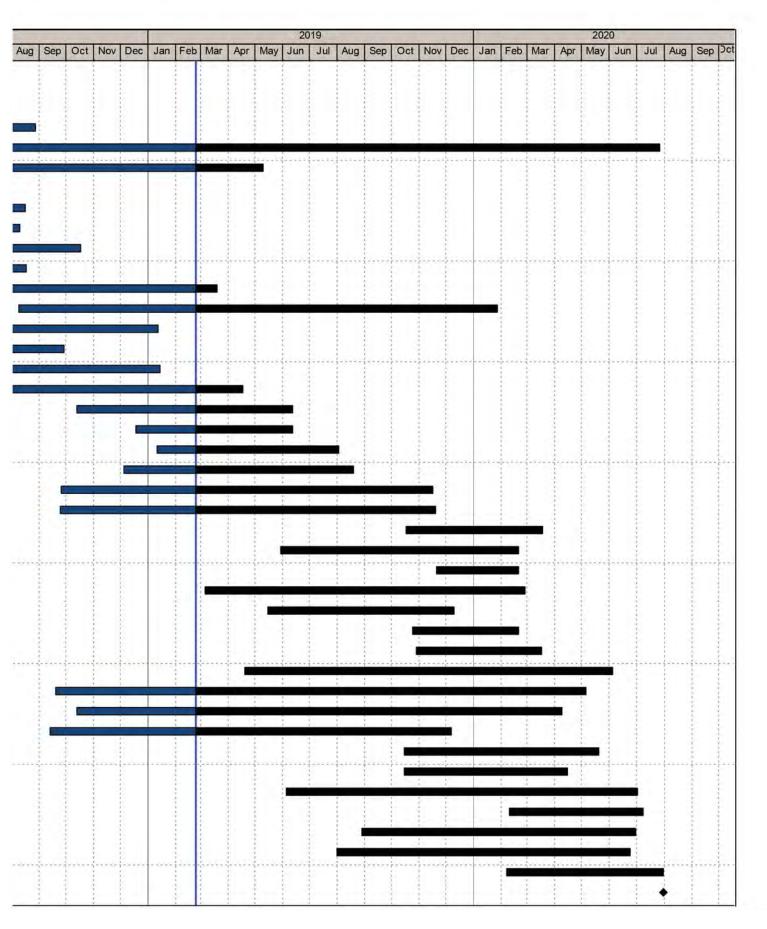

COMPLIANCE / SBE

In accordance with Section 31.5-6 of the Southern Nevada Tourism Improvement Act, Mortenson | McCarthy Las Vegas Stadium, A Joint Venture ("MMcJV") is following the process described below for verification of SBE Contractors.

SBE Contractors apply through the mmcjvlv.com website under the vendors tab. Those seeking certification as a qualified SBE contractor will then fill out and submit a self-certification form, whereas they attest to meeting the criteria for small local business classification denoted in the Senate Bill. The MMcJV Community Benefits Coordinator then reviews the information provided and utilizes the Nevada Secretary of State website: https://www.nvsos.gov/sos to verify the Act's requirements 31.5-2 section a, b, & c in regards to principal place of business, duration of business license, and that the required business license is current. Upon approval of these criteria, MMcJV will then give the contractor the designation of SBE. If firms do not meet the criteria or don't complete the process, they are not classified as SBE. A listing of all approved SBE's, or any of the above records can be provided upon request.





The Mortenson-McCarthy Joint Venture team participated in the Goodie Two Shoes Event













DATE: March 20, 2019

FROM: Lynn R. Littlejohn

RE: Las Vegas Stadium

Community Benefits Plan Report – February 2019

SBE Program

• The SBE project goal is 15%.

- The current SBE participation is 19%.
- Approximately \$924 million dollars of work has been awarded with \$179 million committed to SBE firms.
- 77 different SBE firms have been awarded work on the project; 34 with multiple contracts.
- 18 different WMBE firms have been awarded work.
- 68% of all firms awarded work on the project are Nevada based.

Workforce Diversity

- The workforce goal is 38% minority and female.
- The goal is expressed as a percentage of work hours.
- The workforce participation is 66% minority/female and 2% veteran with approximately 1,325,429 hours worked through February.

Community Engagement and Outreach

- Proposal solicitation notices are sent to community organizations.
- Participated in Kids Café Kitchen.
- Participated in the National Nevada Reading Week.

Attached are the SBE and workforce participation reports.



СС	State	Subcontractor	Scope of Work	SBE/Other	Orig Contract \$ Amount	Original SBE \$ Commitment
	NV	Lewis K. Construction	Fencing Repairs	SBE	\$ 19,360	\$ 19,360
	NV	Nevada Water Trucks	Track Out Pad Installation	SBE	\$ 10,000	\$ 10,000
	NV	Amazon Masonry	Dust Control	SBE/MBE	\$ 10,000	\$ 10,000
	NV	Tab Contractors, Inc.	Trailer Set-up & Geotech Fault Study	Other	\$ 748,450	\$ 490,567
	NV	Boulder Sand & Gravel	Aggregates	SBE		
	NV	Donovan Bros. Trucking	Trucking	SBE		
	NV	JS & S Surveying	Surveying	SBE/MBE		
	NV	M Con	Utilities	SBE/MBE		
	NV	Olson Precast Co.	Concrete Manhole	SBE		
	NV	Acme Electric	Street Light Repairs	Other		
	NV	Nevada Tap Master	Hot Taps	SBE		
	NV	Merli Concrete Pumping	Box Culvert - Concrete Pump	SBE		
	NV	National Trench Safety	Traffic Control	Other		
	NV	Wells Cargo	Cold Mix, Reject Sand, Rock	Other		
	NV	HD White Cap	Equipment Rental	Other		
	NV	Cashman Equipment	Equipment Rental	Other		
	NV	Sunstate	Sewer & Water Materials	Other		
	NV	Ferguson Waterworks	Equipment Rental	Other		
	NV	United Rentals	Concrete	Other		
	NV	Nevada Ready Mix	Equipment Rental	Other		
	NV	Ahern Rentals	Trucking Materials	Other		
	NV	Werdco	Trucking Materials	Other		
		<u> </u>		1		

Original SBE Commitment %	Current Contract \$ Amount	SBE %	Awarded SBE \$Participation	Other \$Participation	Actual SBE \$ Paid	Actual Other \$ Paid
100%	\$ 21,838	100%	\$ 21,838		\$ 21,838	\$ -
100%	\$ 9,903	100%	\$ 9,903		\$ 9,903	\$ -
100%	\$ 11,495	100%	\$ 11,495		\$ 11,495	\$ -
66%	\$ 908,200	60%				\$ 862,790
			\$ 10,900		\$ 9,815	
			\$ 7,267			
			\$ 28,190		\$ 20,088	
			\$ 402,693		\$ 401,133	
			\$ 14,738		\$ 14,738	
				\$ 4,033	\$ -	\$ 4,033
			\$ 1,560		\$ 1,560	
			\$ 595		\$ 595	
				\$ 11,767		\$ 11,767
				\$ 3,090		\$ 3,090
				\$ 9,536		\$ 9,536
				\$ 5,016		\$ 5,016
				\$ 1,793		\$ 1,793
				\$ 84,388		\$ 84,388
				\$ 20,386		\$ 20,386
				\$ 7,954		\$ 7,954
				\$ 2,474		\$ 2,474
				\$ 2,764		\$ 2,764



СС	State	Subcontractor	Scope of Work	SBE/Other	Orig Contract \$ Amount	Original SBE \$ Commitment
	NV	Diaz Trucking	Trucking Materials	Other		
	NV	Boulder Sand & Gravel	Type II	SBE		
	NV	Hernandez Trucking	Trucking Materials	Other		
	NV	HD Barricade	Traffic Control	Other		
	NV	MMC, Inc.	Vactoring	Other		
	NV	A-1 Concrete Cutting	Saw Cutting/Core Drilling/Demo	SBE/MBE		
	NV	Wells Cargo, Inc.	Asphalt Paving	Other		
	NV	Nevada Water Trucks	SWPPP & Dust Control Services	SBE	\$ 494,460	\$ 494,460
	NV	Cashman Professional	Photography	SBE	\$ 37,800	\$ 37,800
	NV	Eros Environmental	SWPPP Inspections	SBE	\$ 18,195	\$ 18,195
	NV	Preventive Measures	Site Security	SBE	\$ 100,000	\$ 100,000
	MN	Danny's Construction	Field Tray Mock-up	WBE	\$ 147,000	\$ -
	TX	Derr & Isbell Construction	Personnel Hoist	Other	\$ 2,799,134	\$ 419,870
1.01	WI	Merrill Iron & Steel	Structural Steel	Other	\$ 179,413,551	\$ 26,912,032
	TX	Derr & Isbell Construction	Steel Erection	Other		
	NV	Reliable Crane Service	Crane Operation & Maintenance	SBE		
	NV	Trinity Land Survey	Box Culvert - Survey	SBE/WBE		
	NV	Union Erectors, LLC	Steel Erection	SBE		
	NV	Steel Partners	Stair Supply	SBE		
	IL	Chicago Metal Rolled Products	Rolled Materials	Other		
	WI	Computerized Structural Design	Connection Design Services	Other		
	NV	Hershberger Bros Welding	Misc. Fabrication Services	SBE		

Original SBE Commitment %	Current Contract \$ Amount	SBE %	warded SBE Participation	Othe	r \$Participation	Å	Actual SBE \$ Paid	A	Actual Other \$ Paid
				\$	385			\$	385
			\$ 7,717			\$	7,717	\$	-
				\$	2,026			\$	2,026
				\$	8,575			\$	8,575
				\$	10,000			\$	1,950
			\$ 75,000			\$	360		
				\$	31,200			\$	29,640
100%	\$ 1,478,121	100%	\$ 1,478,121			\$	1,291,863		
100%	\$ 37,800	100%	\$ 37,800			\$	7,175		
100%	\$ 18,195	100%	\$ 18,195			\$	7,995		
100%	\$ 100,000	100%	\$ 100,000			\$	120,388		
	\$ 147,000							\$	139,650
15%	\$ 2,799,134	15%	\$ 419,870					\$	512,424
15%	\$ 208,646,295	15%						\$	111,741,008
				\$	78,613,203			\$	23,463,470
			\$ 9,900,000			\$	1,750,942		
			\$ 1,000,000			\$	514,762		
			\$ 2,500,000			\$	1,552,197		
			\$ 918,788			\$	392,852		
				\$	25,000			\$	22,420
				\$	289,438			\$	121,050
			\$ 2,494,963			\$	2,370,215		



СС	State	Subcontractor	Scope of Work	SBE/Other	Orig Contract \$ Amount	Original SBE \$ Commitment
	ОК	Hilti	Anchors/Anchor Rods	Other		
	IL	Atlas Tube	HSS Tube & Pipe	Other		
	IL	Infra Metals	W, HSS, Plate, Raw Materials	Other		
	TX	Madden Bolt Corp.	Anchor Rod Assemblies	Other		
	ОН	Nelson Stud Welding	Weld Studs	Other		
	AR	Nucor Yamato Steel	WF Beams, Raw Material	Other		
	KS	Steel & Pipe Supply	W, HSS, Plate, Raw Materials	Other		
	IN	Steel Dynamics	W, C, L, Raw Materials	Other		
	IN	Aarbee Structures	Detailing Services	Other		
	IA	Kloeckner Metals - Dubuque	Material Supplier	Other		
	IL	Kloeckner Metals - Chicago	Material Supplier	Other		
	SE	SSAB/IPSCO	Material Supplier	Other		
	NV	Fasco	Fastener Supply & Delivery	SBE		
	NV	Mori Consulting	Raw Material Procurement	SBE		
	IN	Triad Metals International	Raw Material Supply	Other		
	AL	Saginaw Pipe Company	Raw Material Supply	Other		
	СО	Brown Strauss Co.	Raw Material Supply	Other		
	IL	Leeco Steel, LLC	Raw Material Supply	Other		
	SC	Nucor Steel Berkeley	Raw Material	Other		
	SC	Erico International Corp.	Fasteners	Other		
	IL	O'Brian Steel Service Co.	Raw Material	Other		
	PA	PPG Industries	Raw Material	Other		
	WA	Corona Stud & Deck	Deck Supply & Installation	Other		
	TX	Universal Steel America	Material Supplier	Other		
	IL	Black Diamond Pipe & Tube	Raw Material Supply	Other		
	SC	Con-Serv Inc.	Raw Material Supply	Other		
	ОН	Kenilworth Steel Co.	Raw Material Supply	Other		
	МО	Tubular Steel	HSS Tube & Raw Materials	Other		
	CA	West Coast Inspections	Shop Inspection Services	Other		

Original SBE Commitment %	Current Contract \$ Amount	SBE %	Awarded SBE \$Participation	Other \$Participation	Actual SBE \$ Paid	Actual Other \$ Paid
				\$ 61,162		\$ 61,162
				\$ 1,795,486		\$ 1,795,486
				\$ 199,032		\$ 199,032
				\$ 4,528		\$ 4,528
				\$ 10,000		\$ 8,961
				\$ 3,000,000		\$ 1,457,590
				\$ 111,708		\$ 111,708
				\$ 107,303		\$ 107,303
				\$ 5,770,634		\$ 5,796,564
				\$ 90,977		\$ 100,560
				\$ 280,815		\$ 280,815
				\$ 2,500,000		\$ 2,291,648
			\$ 1,405,041		\$ 1,405,041	
			\$ 13,820,323		\$ 13,820,323	
				\$ 108,589		\$ 108,589
				\$ 94,808		\$ 94,808
				\$ 564,949		\$ 564,949
				\$ 796,960		\$ 855,322
				\$ 120,133		\$ 120,133
				\$ 40,000		\$ 17,400
				\$ 274,181		\$ 274,181
				\$ 776,643		\$ 599,964
				\$ 5,446,026		\$ 1,367,343
				\$ 50,000		\$ 13,811
				\$ 141,790		\$ 141,790
				\$ 239,190		\$ 239,190
				\$ 116,227		\$ 116,227
				\$ 3,385,010		\$ 3,385,010
				\$ 1,143,117		\$ 900,906



СС	State	Subcontractor	Scope of Work	SBE/Other	Orig Contract \$ Amount	Original SBE \$ Commitment
	MI	Alro Steel Corporation	Raw Material Supply	Other		
	DE	Arcelormittal International	Raw Material Supply	Other		
	IL	Arcelormittal USA	Raw Material Supply	Other		
	UT	Intsel Steel West	Raw Material Supply	Other		
	WI	Max Weiss	Rolled Materials	Other		
	NV	Metro Trailer Leasing	Trailer Rental	Other		
	MO	Milestone Trailer Leasing	Trailer Rental	Other		
	NV	NP Tropicana LLC	Lot Rentals	Other		
	MO	South Side Machine Works	Machining	Other		
	ОН	TQL	Freight	Other		
	FL	Worldwide Specialty Logistics	Freight	Other		
	MI	Niles Industrial Coatings	Touch-up Field Painting & Cleaning	Other		
	MT	ADF International	Various Fabrication Scope	Other		
	OR	Albina Pipe Bending	Bending Service	Other		
	NC	Armstrong Transport Group	Frieght	Other		
	TN	Avenger Logistics	Freight	Other		
	СО	AZZ Galvanizing Denver	Galvanizing	Other		
	МО	Bourne Logistics Management	Freight	Other		
	IL	Chapel Steel	Material Supply	Other		
	IL	FHS Consulting	Testing Service	Other		
	UT	Interstate Gratings	Grating Supply	Other		
	AZ	JV Driver	Fabrication Subcontractor	Other		
	KS	King of Freight LLC	Freight	Other		
	CA	McKinney Trailer Rentals	Trailer Rental	Other		
	CA	PDM Steel Services	Material Supply	Other		
	KS	PKM Steel Service	Fabrication Subcontractor	Other		
	CA	RBC Lubron Bearing Systems	Bearing Supplier	Other		
	WI	Russell Metals Williams Bahcall	Material Supply	Other		
	ОН	US Logistics LLC	Freight	Other		

Original SBE Commitment %	Current Contract \$ Amount	SBE %	Awarded SBE \$Participation	Other \$Participation	Actual SBE \$ Paid	Ac	tual Other \$ Paid
				\$ 21,253		\$	21,253
				\$ 574,162		\$	574,162
				\$ 187,422		\$	187,422
				\$ 259,319		\$	197,863
				\$ 105,825		\$	105,825
				\$ 57,968		\$	57,968
				\$ 54,437		\$	54,437
				\$ 122,500		\$	122,500
				\$ 21,050		\$	21,050
				\$ 285,320		\$	285,320
				\$ 666,775		\$	666,775
				\$ 2,403,639		\$	154,199
				\$ 5,962,828		\$	3,017,689
				\$ 28,708		\$	28,708
				\$ 190,433		\$	190,433
				\$ 358,383		\$	358,383
				\$ 26,809		\$	26,809
				\$ 16,135		\$	16,135
				\$ 134,748		\$	134,748
				\$ 16,245		\$	16,245
				\$ 357,592		\$	293,069
				\$ 1,386,780		\$	447,283
				\$ 207,703		\$	371,640
				\$ 106,625		\$	133,229
				\$ 165,307		\$	165,307
				\$ 564,606		\$	158,769
				\$ 201,219		\$	201,219
				\$ 174,905		\$	174,905
				\$ 253,804		\$	253,804



СС	State	s procurement activity through F Subcontractor	Scope of Work	SBE/Other	Orig Contract \$ Amount	Original SBE \$ Commitment
	NV	Xtra Lease LLC	Trailer Rental	Other		
	WI	ZMAC Transportation Solutions	Freight	Other		
	KS	Unique Metal Fabrications	Fabrication Subcontractor	Other		
	IL	Olympic Steel	Material Supply	Other		
	NV	Union Erectors	Field Repairs	SBE		
1.02a	NJ	Vector Foiltec	ETF Roofing System	Other	\$ 29,701,944	\$ 4,455,292
1.024	CA	Walter P Moore	Professional Engineering	Other	29,701,944	Ψ +,+35,292
	-		, ,			
	IT NV	Cimolai S.P.A.	Material Supplies	Other		
	NV	Union Erectors	Material Supplies	SBE		
	NV	Reliable Crane Services	Equipment & Storage	SBE		
1.02b	VA	Freyssinet, Inc.	Cable Net Roof Support	Other	\$ 31,600,000	\$ 4,740,000
	СН	Fatzer AG	Manufacture & Supply of Fully Locked coil Ropes	Other		
	DE	Bollinger & Grohmann International	Design Services	Other		
	МО	Thornton Tomasetti	Structural Engineering	Other		
	NV	Kordt Engineering	PE Services of Permanent Works	SBE		
	IT	CAVE S.R.L.	Manufacture & Supply of Cable Clamps	Other		
	СН	HFE	Manufacture & Supply of Cable Struts	Other		
	СН	CHINA Grand Engineering	Manufacture & Supply of Temporary Work Steel	Other		
	NV	TV Transport	Yard - Rental, Security & Storage	SBE		
	NV	Vision Construction Services	Crane Rental	SBE		
	NV	Steel Partners, LLC	Installation	SBE		
1.03	NV	Sunstate Companies, LLC	PreCast	Other	\$ 25,129,767	\$ 3,769,465
	NV	Expansion Specialties	Caulking of PreCast	SBE/VBE		
	NV	GM Construction, LLC	Erection of PreCast	Other		
	NV	GM Construction, LLC	Erection of PreCast	SBE		
	NV	GM Construction, LLC	Erection of PreCast - Upper Bowl	SBE		
	NV	Westside Building Materials	Supplier	Other		
	NV	Lowe's	Supplier	Other		
	NV	Reliable Steel	Stud & Shield Welding	SBE		
	CA	United Rentals Northwest	Rental	Other		
	ОН	Tru-Fit Products of Utah	Field Supplies	Other		
	NV	Fasteners	Field Supplies	Other		

Original SBE Commitment %	Current Contract \$ Amount	SBE %		warded SBE Participation	Othe	er \$Participation	Actual SBE \$ Paid	A	Actual Other \$ Paid
					\$	77,070		\$	77,070
					\$	18,625		\$	18,625
					\$	2,773,997		\$	2,174,244
					\$	155,736		\$	155,736
			\$	96,676			\$ 35,258		
15%	\$ 31,669,543	15%	\$	4,742,431				\$	14,471,124
					\$	740,000		\$	732,000
					\$	6,435,750		\$	2,157,006
			\$	2,000			\$ 1,969		
			\$	6,000			\$ 5,740		
15%	\$ 31,755,455	15%	\$	4,704,118				\$	11,696,820
					\$	3,839,792		\$	1,709,469
					\$	371,418		\$	343,151
					\$	173,000		\$	148,831
			\$	59,200			\$ 53,800		
					\$	276,057		\$	161,564
					\$	501,143		\$	142,416
					\$	699,356		\$	246,008
			\$	315,000			\$ 65,750		
			\$	1,615,000			\$ 2,100		
							\$ 2,500,000		
150								•	
15%	\$ 26,404,574	16%	\$	205,000				\$	11,313,750
			Φ	205,000	\$	1,348,339		\$	1,348,339
			\$	1,254,669	Ψ	1,040,000		Ψ	1,040,000
			\$	2,191,367				\$	199,500
					\$	1,000		\$	-
					\$	1,000		\$	-
			\$	260,000			\$ 191,040		
					\$	50,000		\$	4,577
					\$	11,338		\$	11,338
					\$	5,500		\$	2,519



СС	State	Subcontractor	Scope of Work	SBE/Other	Orig Contract \$ Amount	Original SBE \$ Commitment
	UT	DJB Gas Service	Fuel	Other		
	NV	Curtis Steel	Material	Other		
	CA	California Tool Welding	Weld Supplies	Other		
	NV	CES	Field Supplies	Other		
	NV	AXT Transportation	Fuel	Other		
	CA	Airgas West	Welding Gas	Other		
	NV	Ahern Rentals	Rental	Other		
	NV	Dielco Crane Services	Crane Services & Hydraulic Lifts	Other		
	NV	Abatix	Supplier	Other		
	WA	Amazon	Supplier	Other		
	NV	Concrete Accessories	Supplier	SBE		
	NV	BC Rope & Rigging	Supplier	SBE		
	NV	Copper State Bolt & Nut Co.	Supplier	Other		
	NV	Core T Trucking	Supplier	Other		
	NV	Fasteners, Inc.	Supplier	Other		
	NV	Cutting Edge	Supplier	Other		
	NV	Harbor Freight Tools	Supplier	Other		
	NV	HD Supply Waterworks	Supplier	Other		
	NV	McFadden-Dale Hardware	Supplier	Other		
	MN	M.A. Mortenson Co.	Supplier	Other		
	NV	Kuker Ranken Vegas	Supplier	Other		
	NV	McIntosh Communications	Supplier	Other		
	NV	Mobile Mini	Supplier	Other		
	NV	Mobile Materials	Supplier	Other		
	NV	Senergy Petroleum	Supplier	Other		
	NV	Silver State Rope & Rigging	Supplier	Other		
	NV	Steel Edge	Supplier	SBE		
	NV	Precision Aggregate Products	Supplier	SBE		
	OK	Hilti, Inc.	Supplier	Other		
	NV	JS&S Surveying, Inc.	Suveying	SBE/MBE		
	NV	Home Depot	Supplier	Other		
	IL	U-Line	Supplier	Other		
	NV	Monsen Engineering	Supplying Engineering Equip	Other		
	NM	Heatly Engineering	Design/Engineering of PreCast	Other		
	NV	Western Pacific Precast, LLC	Precast Elements	Other		
1.04/1.05	MN	Harris Companies	Mechanical & Plumbing	Other	\$ 121,500,000	\$ 18,225,000
	NV	Maui One Excavating	Trenching, Excating & Hauling	SBE/MBE		
	NV	Lone Mountain Excavation	Site Prep	Other		

Original SBE Commitment %	Current Contract \$ Amount	SBE %	arded SBE articipation	Other \$Participation	Actual SBE \$ Paid	A	Actual Other \$ Paid
				\$ 2,500		\$	737
				\$ 50,000		\$	619
				\$ 3,644		\$	3,644
				\$ 2,000		\$	998
				\$ 20,000		\$	1,533
				\$ 2,500		\$	526
				\$ 50,000		\$	29,408
				\$ 400,000		\$	157,110
				\$ 50,000		\$	35,719
				\$ 916		\$	916
			\$ 50,000		\$ 9,514		
			\$ 1,894		\$ 1,894		
				\$ 5,000		\$	70
				\$ 1,000		\$	350
				\$ 50,000		\$	27,035
				\$ 1,000		\$	455
				\$ 1,000		\$	348
				\$ 3,000		\$	1,419
				\$ 500		\$	190
				\$ 150,000		\$	31,649
				\$ 500		\$	182
				\$ 6,074		\$	6,074
				\$ 15,000		\$	4,492
				\$ 10,000		\$	4,425
				\$ 100,000		\$	8,298
				\$ 100,000		\$	27,183
			\$ 150,000		\$ 11,305		
			\$ 40,000		\$ 11,661		
				\$ 1,000		\$	196
			\$ 177,408		\$ 24,546		
				\$ 1,000			
				\$ 5,000		\$	2,085
				\$ 50,000		\$	26,251
				\$ 1,035,000		\$	1,018,601
				\$ 16,590,904		\$	6,638,431
15%	\$ 125,942,586	17%				\$	39,049,820
			\$ 1,594,437		\$ 1,416,222		
				\$ 943,452		\$	655,223



СС	State	Subcontractor	Scope of Work	SBE/Other	Orig Contract \$ Amount	Original SBE \$ Commitment
	NV	Trinity Land Survey	Box Culvert - Survey	SBE/WBE		
	NV	C-Los Industries	Warehouse Lease to Erect Oval Mock-up	MBE		
	NV	Mechanical Equipment Reps	Provide Computer Room AC Units	MBE		
	NV	Corporate Air Mechanical Services	Furnish 3 Pump Skids, 2 Head Exhcangers, 6 Domestic Heat Exchangers, 1 Triplex Booster Pump Package, 2 Rolairtrols	SBE		
	NV	Corporate Air Mechanical Services	Furnish 6 Cell Stainless Cooling Tower w/Free Cooling and Single Flange Inlet	SBE		
	NV	Corporate Air Mechanical Services	7 Boilers	SBE		
	NV	Corporate Air Mechanical Services	Supplies - Fans & PCU's	SBE		
	NV	Corporate Air Mechanical Services	Furnish 35 Electric Water Heaters & 7 ASME 125# Storage Tanks	SBE		
	NV	Corporate Air Mechanical Services	Provide 1 Lot Fabric Duct (Ductsox) & Associated hangers	SBE		
	NV	Corporate Air Mechanical Services	Provide 26 Fire Smoke Dampers, 48 Fire Dampers & 6 Silencers	SBE		
	NV	Corporate Air Mechanical Services	Provide 1 Lot Metal-Fab UL Listed Grease Duct, 1 Lot Metal- Fab UL Listed General Exhaust Flue, & 1 Lot Metal Fab UL Listed boiler Exhaust Flue	SBE		
	NV	LTSA, LLC	Furnish air Handling Units;VAV's & BCU's	SBE		
	NV	LTSA, LLC	Provide 26 Variable Frequency Drives with 3% Line Reactors & 20 Passive Harmonic Filters	SBE		
	MN	Trane U.S., Inc.	Furnish & Install BAS Mechanical Control System	Other		
	NV	Ideal Supply Company	Provide all Galvanized Victaulic Fittings Supplies	SBE		
	NV	Energy Mechanical Insulation	Furnish & Install Plumbing Insulation	WBE		
	NV	Energy Mechanical Insulation	Furnish & Install Piping Insulation	WBE		
	NV	Energy Mechanical Insulation	Furnish & Install Mechanical Insulation	WBE		
	NV	Energy Mechanical Insulation	Furnish & Install All Fire-Stopping on all Plumbing, Piping & Mechanical Systems	WBE		
	NV	Superior Duct Fabrication	Fabricate & Supply all round ductwork Fittings	Other		
1.06	NV	Gephart/Morse	Electrical	Other	\$ 85,793,108	\$ 13,087,750
	NV	Morse Electric				
	NV	A-1 Concrete	Concrete & Excavation	SBE/MBE		

Original SBE Commitment %	Current Contract \$ Amount	SBE %		warded SBE	Other \$Participation	Actual SBE \$ Paid	A	Actual Other \$ Paid
Commitment %	\$ Amount	5BE %	\$	Participation 50,000	Other \$Participation	\$ 13,065		\$ Paid
			\$	5,412		\$ 5,412		
			\$	246,431		<u> </u>		
			"	2 10, 10 1				
			\$	954,100		\$ 606,863		
			\$	597,274				
			\$	403,133		\$ 372,690		
			\$	1,787,727		\$ 996,318		
			\$	181,418		\$ 52,624		
			\$	1,021,488				
			\$	87,400				
			\$	2,444,744				
			\$	6,797,621		\$ 4,309,279		
			\$	280,788				
					\$ 2,760,826		\$	38,391
			\$	2,061,823		\$ 1,525,342		
			\$	596,715		\$ 12,572		
			\$	1,307,754		\$ 120,854		
			\$	723,431				
			\$	535,062		\$ 1,036		
					\$ 615,856		\$	84,679
4504	Ф 20.000.400	450/	Φ.	40.040.504			•	00.045.450
15%	\$ 89,988,426	15%	\$	10,346,501			\$	23,315,450
			\$	127,418		\$ 127,418		



СС	State	Subcontractor	Scope of Work	SBE/Other	Orig Contract \$ Amount	Original SBE \$ Commitment
	NV	MMC	Hydro Excavating	Other		
	NV	Pyrocom	Sprinkler Monitoring Dialer	SBE/WBE		
	NV	Hampton Tedder Electric	Electrical Testing	Other		
	NV	Lone Mountain Excavation	Excavation	Other		
	NV	Live Electric	Electrical	SBE/WBE		
	NV	Westland State	Parking	Other		
	NV	The Tiberti Fence Company	Drilling	SBE		
	NV	Main Electric	Electrical Supplier	Other		
	NV	Codale Energy	Electrical Supplier	Other		
	CA	Industriall Electric Mftg	Electrical Distribution	Other		
	NV	CESS	Generator/PDV's/Transfer	SBE		
	NV	National Field Services	Switches Electrical Acceptance Testing & Studies	Other		
	NV	General Design & Const.	Fabrication	SBE		
	NV	Valley Steel	Unload and set Electrical Gear	SBE/WBE		
	MN	Gephart Electric, Inc.				
	NV	Las Vegas Lighting	Feeder Cable	SBE		
1.07	NV	Desert Fire Protection, LP	Fire Protection	Other	\$ 14,200,000	\$ 2,130,000
	NV	TAB Contractors	Underground Fire Line	Other		
	NV	Jcord Construction	GPR & Core Drill	SBE		
	NV	Silver State Marketing Group	Supply bulk Fire Sprinkler Pipe	SBE		
	NV	JS&S Inc.	Fire Sprinkler Layout with Trimble	SBE/MBE		
	NV	Silver State Marketing Group	Supply Fire Hose Valves	SBE		
	NV	Lucky Transportation	Transportation	SBE		
	NV	Energy Mechanical Insulation	Fire Caulking & Insulation of Pipe	SBE		
	NV	Monsen Engineering Services	Plotter & Printing Supplies	SBE		
	NV	Silver State Marketing Group	Supply bulk Fire Sprinkler Material	SBE		
4 00/4 00	NIV /	Engles Core	Exterior Curtainwall/Ribbon	Oth a "	¢ 07.404.400	¢ 44.000.005
1.08/1.09	NV	Enclos Corp.	Rainscreen	Other	\$ 97,194,122	\$ 14,620,335
	NV	Innova Technologies	Structural Engineering/Material Mock-up	SBE/MBE		
	NV	Union Erectors	Steel Structure & Install Material Mock-up	SBE		
	NV	Affordable Federal Services	Misc. Construction Services	SBE		
	NV	Hershberger Bros Welding	Curtainwall Anchor & Steel Clips	SBE		
	NV	FASCO	Fasteners	SBE		

Original SBE Commitment %	Current Contract \$ Amount	SBE %	warded SBE Participation	Othe	er \$Participation	Actual SBE \$ Paid	Δ	ctual Other \$ Paid
				\$	10,450		\$	10,450
			\$ 8,860			\$ 7,060		
				\$	2,400		\$	1,250
				\$	1,819,531		\$	1,763,764
			\$ 71,700			\$ 71,700		
				\$	578,699		\$	578,699
			\$ 21,678			\$ 21,367		
				\$	1,202,903		\$	483,977
				\$	1,294,977		\$	334,503
				\$	5,684,804		\$	1,492,564
			\$ 1,511,959			\$ 79,349		
				\$	308,600		\$	33,055
			\$ 42,894			\$ 42,894		
			\$ 24,520					
			\$ 950,551					
15%	\$ 14,284,628	15%	\$ 1,138,217				\$	1,988,864
				\$	115,655		\$	100,475
			\$ 940			\$ 940		
			\$ 155,225					
			\$ 6,312					
			\$ 5,000					
			\$ 80,000					
			\$ 54,000					
			\$ 3,000					
			\$ 700,000					
15%	\$ 97,194,122	15%	\$ 3,057,212				\$	16,775,776
			\$ 14,618			\$ 14,618		
			\$ 20,717			\$ 20,717		
			\$ 5,785,000			\$ 32,891		
			\$ 1,100,000			\$ 432,019		
			\$ 250,000			\$ 6,858		



СС	State	Subcontractor	Scope of Work	SBE/Other	Orig Contract \$ Amount	Original SBE \$ Commitment
	TX	Baker Metal	CW Metal	Other		
	NV	Expansion Specialties	Exterior Expansion Joint System	SBE/VBE		
	NV	Union Erectors	Operable Door	SBE		
1.10	NV	KONE	Elevator & Lifts	Other	\$ 17,942,010	\$ 1,435,361
	NV	Hightower Trucking, Inc.	Warehouse/Logistics Support	MBE	Ψ 17,012,010	Ψ 1,100,001
2.01a	NV	Trinity Land Survey	Box Culvert - Survey	SBE/WBE	\$ 38,770	\$ 38,770
2.01f	NV	Marnell Masonry	Box Culvert - Masonry	SBE	\$ 33,198	\$ 33,198
2.01h	NV	Sahara Concrete	Box Culvert - Site Concrete, Paving & Hardscapes	SBE	\$ 3,678,883	\$ 3,678,883
	NV	CMC Rebar	Box Culvert - Reinforcing (Supply & Install)	Other		
	NV	Nevada Ready Mix	Box Culvert - Concrete Supplier	Other		
	NV	Dielco Crane Services	Box Culvert - Crane Work	Other		
	NV	Merli Concrete Pumping	Box Culvert - Concrete Pump	SBE		
	NV	A-1 Concrete	Demolition	SBE/MBE		
2.01k	NV	The Tiberti Fence Company	Box Culvert - Fence	SBE	\$ 256,862	\$ 256,862
	NV	Flippen's Trenching	143 Holes	SBE		
2.02/2.03	NV	Tab Contractors	Box Culvert /Earthwork/Site Utilities	Other	\$ 15,258,168	\$ 10,707,010
	NV	Brightview Landscape	Box Culvert - Landscape & Irrigation	Other		
	NV	Nelson Hiniker Striping	Stripping/Traffic Control	SBE		
	NV	Sanders Construction	Drilling & Blasting	SBE		
	NV	JS & S Surveying	Land Survey & Construction Staking	SBE/MBE		
	NV	A-1 Concrete Cutting	Core Drilling/Concrete Cutting/Demolition	SBE/MBE		
	NV	M Con, Inc.	Utility Work Installation	SBE/MBE		
	NV	MMC, Inc.	Hydro Excavating/Vactor	Other		

Original SBE Commitment %	Current Contract \$ Amount	SBE %	Awarded SBE \$Participation	Other \$Participation	Actual SBE \$ Paid	Actual Other \$ Paid
				\$ 7,773,414		\$ 478,866
			\$ 611,530			
			\$ 3,740,041			
00/	ф 47.047.070	00/	ф 700 004			¢ 5400.074
8%	\$ 17,947,272	8%	\$ 760,361 \$ 675,000		\$ 454,094	\$ 5,102,074
			0.0,000		Ψ 10 1,00 1	
100%	\$ 71,251	100%	\$ 71,251		\$ 67,689	
100%	\$ 33,198	100%	\$ 33,198		\$ 33,198	
100%	\$ 4,180,022	100%	\$ 3,919,506		\$ 3,971,021	
				\$ 794,604		\$ 754,874
				\$ 475,000		
				\$ 107,725		\$ 107,725
			\$ 78,642	\$ -	\$ 78,642	
			\$ 181,874		\$ 172,780	
100%	\$ 321,332	100%	\$ 312,609		\$ 196,305	
			\$ 8,723		\$ 8,723	
70%	\$ 26,262,956	43%				\$ 16,704,254
				\$ 21,550		\$ 21,550
			\$ 68,064		\$ 68,064	
			\$ 2,193,860		\$ 2,193,860	
			\$ 287,384		\$ 94,351	
			\$ 49,493		\$ 49,493	
			\$ 473,734		\$ 473,734	
				\$ 18,550		\$ 18,550



СС	State	Subcontractor	Scope of Work	SBE/Other	Orig Contract \$ Amount	Original SBE \$ Commitment
	NV	Nevada Ready Mix	Concrete	Other		
	NV	Nelson Hiniker Striping	Traffic Control	SBE		
	NV	Sticha Inc.	Trucking Materials	Other		
	NV	National Trench Safety	Steel Plates & Shoring	Other		
	МО	Core & Main	Water Materials	Other		
	NV	Wells Cargo, Inc.	Asphalt Paving	Other		
	NV	Merli Concrete Pumping	Pump Concrete	SBE		
	NV	MMC, Inc.	Hydro Excavating/Pot Holing	Other		
	NV	TAB Contractors	Excavating	Other		
	CA	Viking Drillers, Inc.	Abandonment (4) Monitoring Wells	Other		
	NV Acme Electric		Remove/Replace Street Lights	Other		
	NV	Boulder Sand & Gravel	Gravel base for concrete & asphalt disposal	SBE		
	NV	Elkhorn Environmental	Trucking/Street Sweeping	SBE		
	NV	Donovan Brothers Trucking	Trucking/Haul-Off	SBE		
	NV	Merli Concrete Pumping	Box Culvert - Concrete Pump	SBE		
	NV	Olson PreCast Company	Install Storm Drain & Sewer MH & Drop Inlets	SBE		
	NV	Armorock, LLC	Manhole Materials	Other		
	NV	Nevada Tap Master	Wet Tap	SBE		
	NV	Nevada Water Trucks	Water Truck	SBE		
	NV	Enco Southwest, Inc.	Pump Controls	SBE		
	NV	M Con, Inc.	Main Water Line	SBE/MBE		
	NV	Ahern Rentals	Equipment Rental	Other		
	NV	MMc Inc.	Vactor/Pothole Services	Other		
	CA	Cashman Equipment Co.	Equipment Rental	Other		
	TX	Aggregate Industries	Type II Supplier	Other		
	МО	Core & Main	Material Supplier	Other		

Original SBE Commitment %	Current Contract \$ Amount	SBE %	warded SBE Participation	Otl	ner \$Participation	,	Actual SBE \$ Paid	A	Actual Other \$ Paid
				\$	2,679			\$	2,679
			\$ 3,240			\$	3,240		
				\$	1,080			\$	1,080
				\$	285,000			\$	259,350
				\$	29,790			\$	27,992
				\$	77,527			\$	68,555
			\$ 639			\$	639		
				\$	377,038			\$	377,038
				\$	5,000				
				\$	8,800			\$	8,800
				\$	104,353			\$	104,353
			\$ 357,361			\$	175,401		
			\$ 2,384,021			\$	2,384,021		
			\$ 2,518,042			\$	2,243,058		
			\$ 10,000			\$	1,827		
			\$ 71,023			\$	71,023		
				\$	211,042			\$	206,219
			\$ 49,895						
			\$ 264,461			\$	264,461		
			\$ 208,780						
			\$ 2,178,147			\$	1,083,319		
			_,110,111	¢.	44.050	*	.,000,010	¢	44.050
				\$	11,653			\$	11,653
				\$	4,800			\$	4,800
				\$	4,478			\$	4,478
				\$	25,000			\$	16,930
				\$	675,000			\$	267,176

___



cc	State	s procurement activity through Subcontractor	Scope of Work	SBE/Other	Orig Contract \$ Amount	Original SBE \$ Commitment
	NV	National Trench Safety	Shoring/Trench Plates	Other		
	NV	Nevada Ready Mix	Concrete Supplier	Other		
	NV	Rinker Materials	RPC Onsite/Offsite	Other		
	NV	HD Barricade, Inc.	Traffic Control	Other		
	NV	Sticha Inc.	Trucking	Other		
	NV	Las Vegas Paving	Cold Mix	Other		
	CA	HD White Cap	Safety Supplies	Other		
	NV	Olson Precast Company	8" Meter Vaults	SBE		
	NV	Las Vegas Paving	Flaggers	Other		
2.05	CA	Malcolm Drilling	Deep Foundations	Other	\$ 8,630,311	\$ 1,588,177
	NV	CMC Steel	Reinforcing Steel	Other		
	NV	Steel Edge, Inc.	Piles	SBE		
	NV	Precision aggregate Products	Supply Grout for Deep Foundations	SBE		
	NV	Trinity Land Survey	Box Culvert - Survey	SBE/WBE		
	NV	Dielco Crane Service	Crane Lift Services	Other		
	NV	TAB Contractors	Load Haul-off & Dispose ACIP Spoils	Other		
	NV	Fugro USA Land	Osterberg Cell load testing equipment & services	Other		
	NV	Clark Welding & Fabricating	Welding	Other		
	NV	White Cap	General Building Materials	Other		
	NV	United Rentals	Rental Equipment	Other		
	NV	ммс	Potholing/Vac Truck Work	Other		
2.99/3.99	NV	Mortenson/McCarthy	Structural Concrete	Other	\$ 128,419,469	\$ 19,262,920
3.99a	WI	Gateway Forming Systems	Horizontal Formwork	Other		

Original SBE Commitment %	Current Contract \$ Amount	SBE %	Awarded SBE \$Participation	Other \$Participation	Actual SBE \$ Paid	Actual Other \$ Paid
				\$ 25,000		\$ 18,408
				\$ 10,000		\$ 8,844
				\$ 108,450		\$ 96,452
				\$ 2,500		\$ 2,400
				\$ 1,394		\$ 1,338
				\$ 2,500		\$ 500
				\$ 5,000		\$ 2,627
			\$ 62,99	7	\$ 20,999	
				\$ 1,000		
18%	\$ 10,729,892	26%				\$ 10,193,397
				\$ 2,200,385		\$ 2,200,385
			\$ 457,44	6	\$ 457,446	
			\$ 2,133,22	5	\$ 2,133,225	
			\$ 187,61	9	\$ 187,619	\$ -
				\$ 20,353		\$ 20,353
				\$ 221,790		\$ 221,790
				\$ 205,817		\$ 205,817
				\$ 51,702		\$ 51,702
				\$ 44,503		\$ 44,503
				\$ 20,791		\$ 20,791
				\$ 1,125		\$ 1,125
15%	\$ 128,649,716	25%				\$ 98,135,728
				\$ 15,128,319		\$ 14,371,903



CC	State	Subcontractor	Scope of Work	SBE/Other	Orig Contract \$ Amount	Original SBE \$ Commitment
	NV	Region 9 Safety	Safety Director	SBE/MBE		
	NV	Pacific Construction Services	Shoring Rental/Lumber	SBE		
3.99b	NV	CMC Rebar	Reinforcing	Other		
	NV	Steel Edge, Inc.	Reinforcing Steel	SBE		
	NV	Precision Aggregate Products	Concrete	SBE		
	NV	Merli Concrete	Concrete Pumping	SBE		
	NV	Penhall Co.	Demolition	Other		
	NV	Jcord	Demolition	SBE		
	NV	Ahern Rentals	Equipment Rental	Other		
	AZ	Sunstate Equipment	Equipment Rental	Other		
	CA	HD Supply	Supplies & Materials	Other		
	NJ	Hilti	Small Tools , Materials & Equipment	Other		
	TX	H & E Equipment	Equipment Rental	Other		
	GA	Herc Rentals	Equipment Rental	Other		
	NV	Lynco Associates	Epoxy & Rebar Enbeds	Other		
	IL	CDW Direct, LLC	Technology Equipment	Other		
	NV	Atlas Construction Supply	Column Formwork - Supplies	Other		
	NV	BC Wire Rope & Rigging	Rigging Supplies	SBE		
	NV	Pacific Construction Services	Lumber - Supplier	SBE		
	NV	Construction Testing Services	Professional Services	Other		
	NV	Concrete Accessories	Grout/Concrete - Supplier	SBE		
	MN	Curtis 1000 Inc.	Materials	Other		
	MN	ESCH Construction Supply	Materials	Other		
	NV	FASCO	Materials	SBE		
	NV	Fastenal Company	Materials	Other		
	NV	Fasteners Inc.	Thread Supplier	Other		
]	1	1		

Original SBE Commitment %	Current Contract \$ Amount	SBE %	warded SBE Participation	Other \$Participation	Actual SBE \$ Paid	A	Actual Other \$ Paid
			\$ 168,341		\$ 168,341		
			\$ 1,213,110		\$ 1,213,110		
				\$ 19,499,304		\$	12,432,253
			\$ 5,261,740		\$ 4,809,657		
			\$ 13,344,333		\$ 9,226,470		
			\$ 722,421		\$ 608,711		
				\$ 80,648		\$	80,648
			\$ 1,269,783		\$ 1,088,330		
				\$ 40,000		\$	22,144
				\$ 5,000		\$	3,694
				\$ 40,000		\$	25,480
				\$ 84,566		\$	84,566
				\$ 20,000		\$	6,934
				\$ 30,000		\$	15,116
				\$ 54,000		\$	26,002
				\$ 31,243		\$	10,933
				\$ 1,402,595		\$	272,826
			\$ 646,731		\$ 343,551		
			\$ 1,000,000		\$ 788,153		
				\$ 80,000		\$	69,239
			\$ 150,000		\$ 122,462		
				\$ 3,458		\$	494
				\$ 2,000		\$	933
			\$ 100,000		\$ 54,320		
				\$ 2,438		\$	348
				\$ 89,770		\$	97,848



СС	State	Subcontractor	Scope of Work	SBE/Other	Orig Contract \$ Amount	Original SBE \$ Commitment
	NV	Glove Connection	Safety Equipment & Small Tools	SBE		
	IL	Grainger	Construction Supplies	Other		
	NJ	Hilti	Small Tools & Epoxy	Other		
	WA	KR	Materials	Other		
	со	Smalley & Company	Water Stop Supplies	Other		
	NV	White Cap	Materials	Other		
	NV	New Life Office LLC	Workstation Materials	Other		
	PA	Norcen Industries	Materials	Other		
	NV	NOVA Geotechnical & Inspection	Professional Services	Other		
	МО	Office Essentials	Office Supplies	Other		
	NV	Staples	Office Supplies	Other		
	NV	William Vollmer	Materials	Other		
	со	RMD KWIKform North America	Materials	Other		
	NV	M.J. Dean Construction	Concrete Forming	Other		
	AZ	UFP Chandler, LLC	Materials	Other		
	IL	Uline, Inc.	Materials	Other		
	NV	Reliable Crane	Crane Rental	SBE		
	NV	Eberhard SW Roofing	Water Stop Supplies	SBE		
	NV	IQC Southwest, LLC	Quality Control - Inspections	Other		
	NV	Artkore LLC	Materials	SBE		
	NV	Commercial Scaffolding of Nevada	Stair Tower & Scaffolding	SBE		
	NV	Union Erectors	Steel Corrections	SBE		
	SD	Dakota Riggers & Tool Supply	Materials	Other		
	NV	Fiber Tech Lifting Products	Materials	Other		
	NV	Hershberger Bros Welding	Materials	SBE		

Original SBE Commitment %	Current Contract \$ Amount	SBE %	warded SBE Participation	Other \$Participation	Actual SBE \$ Paid	A	ctual Other \$ Paid
			\$ 300,000		\$ 252,140		
				\$ 6,107		\$	6,107
				\$ 119,644		\$	119,644
				\$ 8,175		\$	8,175
				\$ 10,532		\$	1,505
				\$ 800,000		\$	585,003
				\$ 41,552		\$	2,944
				\$ 19,268		\$	1,826
				\$ 19,500		\$	3,250
				\$ 2,000		\$	380
				\$ 3,534		\$	2,877
				\$ 19,292		\$	2,756
				\$ 1,300,000		\$	1,206,375
				\$ 1,200,000		\$	1,143,842
				\$ 25,500		\$	8,499
				\$ 5,000		\$	2,400
			\$ 7,000,000				
			\$ 50,000		\$ 43,434		
				\$ 500,000		\$	394,193
			\$ 1,428		\$ 602		
			\$ 150,000		\$ 113,944		
			\$ 250,000		\$ 56,517		
				\$ 3,450		\$	122
				\$ 2,000		\$	217
			\$ 2,000		\$ 1,588		



СС	State	Subcontractor	Scope of Work	SBE/Other	Orig Contract \$ Amount	Original SBE \$ Commitment
	NV	June Rose, LLC	Materials	SBE		
	MN	Mars Supply	Materials	Other		
	NV	RGR Training Center	Safety Training	Other		
	NV	Border Construction Specialties	Materials	Other		
	GA	Global Equipment Co.	Materials	Other		
	NV	Go2 Partners	Materials	Other		
3.04/3.10	NV	Eberhard Southwest Roofing	Roofing & Waterproofing	SBE	\$ 4,259,219	\$ 4,259,219
	СО	Smalley & Company	Waterproofing Materials	Other		
	NV	Construction Sealants Supply	Waterproofing Materials	SBE		
	TX	StarFoam Manufacturing	Waterproofing Materials	Other		
	CA	Sika Sarnafil	Roofing Materials	Other		
3.05	NV	Union Erectors	Misc. Metals - Stairs	SBE	\$ 974,144	\$ 974,144
	In	American Stairs Corp.	Stair Material Supplier	Other		
3.06	KS	Dimensional Innovations	Signature Tower	Other	\$ 580,823	\$ 87,123
3.08	TN	Industrial Door Contractors (IDC)	Operable Field Mechanization	Other	\$ 17,160,597	\$ 2,600,000
3.08b	NV	McKeon Door of Nevada, Inc.	Operable Field Door Mechanization	Other	\$ 475,967	\$ 126,735
	NV	Mojave Electric	Electrical	Other		
	NV	Panelfold, Inc.	Operable Wall	Other		
	NV	Clear Solutions Group	Material (glass) Supplier	SBE		
	NV	MJDean/Southwest Door & Hardware	Doors, Frames & Hardware	Other		
3.08c	CA	Show Canada Industries	Retractable Columns	Other	\$ 1,701,160	\$ 262,000
3.11/4.01	NV	Performance Contracting, Inc.	Exterior & Interior Framing/Drywall	Other	\$ 40,095,890	\$ 6,025,279

Original SBE Commitment %	Current Contract \$ Amount	SBE %	Awarded SBE \$Participation	Other \$Participation	Actual SBE \$ Paid	Actual Other \$ Paid
			\$ 37,735		\$ 9,434	
				\$ 1,000	\$ -	\$ 50
				\$ 20,000		\$ 3,360
				\$ 2,149		\$ 2,149
				\$ 1,000		\$ 118
				\$ 2,500		\$ 632
100%	\$ 4,623,517	100%	\$ 4,282,273		\$ 520,193	
				\$ 30,000		\$ 23,748
			\$ 341,244		\$ 341,244	
				\$ 50,000		\$ 48,163
				\$ 1,400,000		\$ 956
100%	\$ 1,008,456	100%	\$ 1,008,456		\$ 540,061	
				\$ 557,856		\$ 23,731
15%	\$ 2,054,393	15%	\$ 308,159			\$ 991,094
15%	\$ 17,274,896	15%	\$ 2,600,000			
27%	\$ 475,967	27%			\$ -	\$ 46,835
				\$ 29,210		
				\$ 26,555		
			\$ 126,735			
				\$ 60,186		
15%	\$ 1,701,160	15%	\$ 262,000			\$ 196,843
15%	\$ 40,095,890	15%				\$ 1,165,679



СС	State	Subcontractor	Scope of Work	SBE/Other	Orig Contract \$ Amount	Original SBE \$ Commitment
	NV	Commercial Scaffolding	Erection/dismantle of Scaffold	SBE		
	NV	Gale Building Products	Insulation and Firestopping	Other		
	NV	Lochsa Engineering	Engineering Services	Other		
	NV	R&P Supply	Framing, Drywall, Taping	SBE		
	NV	Technicoat Management	Interior Moisture Barrier	SBE		
	NV	Tomarco Fastening Systems, Inc.	Fasteners	Other		
	NV	Legacy Cast & Stone & Composites	Ceiling Shapes	SBE		
4.02	NV	CEDCO, Inc.	Masonry	Other	\$ 5,258,412	\$ 861,346
	NV	A Track-Out Solutions	Material Purchasing Delivery	WBE		
	NV	JS & S Surveying	Survey - CMU Wall Control Layout	SBE/MBE		
	NV	Technicoat Management	Fire Stop/Joint Sealants	SBE		
	NV	Region 9 Safety Compliance	Safety Coordinator	SBE/MBE		
	CA	Epic CAD Solutions	Providing 3D Modeling	Other		
	NV	Silver Star Ready Mix	Supplying of Masonry Grout	Other		
4.03	NV	American Door Installation, LP	Frames, Doors & Hardware	SBE	\$ 595,725	\$ 595,725
	NV	The Hallgren Co.	Supply Frames, Doors & Hardware	Other		
4.05	GA	Raydeo Enterprises, Inc.	Stadium Railings	Other	\$ 11,524,358	\$ 2,751,947
4.07	NV	Expansion Specialties	Expansion Joints	SBE/VBE	\$ 1,640,550	\$ 1,640,550
4.08	NV	Combont/Money	Floatrical Law Valtage	Other	\$ 452,409	\$ 67,861
4.00	NV	Gephart/Morse Morse Electric	Electrical - Low Voltage Excavation	Other	\$ 452,409	\$ 67,861
	NV	Coherent Design	AV Design Assist, Testing & Commissioning	SBE		
	NV	Johnson Controls Fire Protection	Fire Alarm System	Other		
4.09	NV	Aggregate Industries	Bituminous Pavement	Other	\$ 4,408,062	\$ 661,209
4.10b	NV	Aggregate Industries	MSE Retaining Walls	Other	\$ 5,132,049	\$ 793,792
	CA	The Reinforced Earth Company	Design/Provide MSE Wall Material	Other		

Original SBE Commitment %	Current Contract \$ Amount	SBE %		warded SBE Participation	Other \$Participation	Actual SBE \$ Paid	A	Actual Other \$ Paid
			\$	1,346,171				
					\$ 1,698,712			
					\$ 77,500		\$	69,425
			\$	4,300,000		\$ 73,487		
			\$	347,248				
					\$ 50,000		\$	15,669
			\$	31,860		\$ 14,716		
16%	\$ 5,339,031	18%					\$	1,396,330
			\$	855,500		\$ 204,812		
			\$	10,520		\$ -	\$	-
			\$	69,749				
			\$	30,000		\$ 19,201		
					\$ 36,000		\$	10,175
					\$ 280,000		\$	20,692
100%	\$ 3,181,245	100%	\$	3,181,245			\$	58,267
					\$ 2,089,951		\$	55,036
24%	\$ 11,697,224	24%	\$	2,751,947			\$	476,184
100%	\$ 1,640,550	100%	\$	1,640,550				
15%	\$ 452,409	15%	\$	11,861			\$	429,789
1370	Ψ 402,403	1370	Ψ	11,001			Ψ	425,105
			\$	56,000				
			\$	-	\$ 54,890			
15%	\$ 4,408,062	15%	\$	661,209				
15%	\$ 5,132,049	17%	\$	-			\$	374,042
					\$ 799,280		\$	429,610



СС	State	Subcontractor	Scope of Work	SBE/Other	Orig Contract \$ Amount	Original SBE \$ Commitment
	NV	Stewart & Sundell	CIP Concrete for MSE Walls	SBE		
4.12	СО	Rolling Plains Construction	Fireproofing	Other	\$ 4,378,322	\$ 667,494
	NV	Quinette King Consulting	Material Supplier	SBE		
	NV	United Rentals	Equipment Rentals	Other		
5.17b	GA	Sports Field, Inc. dba Fields	Heat System for Operable Field	Other	\$ 1,716,348	\$ 257,452
	UT	Cache Valley Electric	Electrical Installation	Other		
	1	<u> </u>	Totals		\$ 863,528,597	\$ 149,173,183
			Goal			

Current Contract Awarded SBE **Actual SBE Actual Other Original SBE** Commitment % \$ Amount SBE % \$Participation Other \$Participation \$ Paid \$ Paid \$ 30,631 873,210 \$ 394,560 15% \$ 4,378,322 15% \$ 667,494 \$ 110,471 \$ 250,000 15% \$ 1,716,348 15% \$ 257,452 \$ 79,800 \$ 299,258 17% \$ 924,792,473 19% \$ 179,749,511 \$ 235,230,943 \$ 74,471,021 \$ 481,570,729 15%



Las Vegas Stadium Workforce Utilization Summary

This report reflects the cumulative hours worked through February 2019.

This report reflects the cumulative hours worked through F
Subcontractor
Lewis K Construction
Modern Demo & Services
Total for Lewis K Construction
Geotechnical & Environmental Services
Eagle Drilling Services
Total for Geotecnical & Environmental Svs
Nevada Water Truck
Total for Nevada Water Truck
Amazon Masonry
Total for Amazon Masonry
TAB Contractors - Trailer City
Mcon
Acme Electric - Mcon TC
Olson Precast - Mcon TC
Nevada Tap Master - Mcon TC
Merli - Mcon TC MMC, Inc.
A-1 Concrete
Wells Cargo Total for TAB Contractors - Trailer City
Total for TAB Contractors - Trailer City
Sahara Concrete
CMC Rebar
Dielco Crane Service
Merli Concrete
A-1 Concrete
Total for Sahara Concrete
Marnell Masonry
Total for Marnell Masonry
TAB Contractors - Main
Brightview Landscape
Nelson Hiniker Striping
Sanders Construction
A-1 Concrete
MMC
TAB-MMC
Mcon Moon
MMC - Mcon Wells Cargo - Mcon
Merli - Mcon BC
Viking Drillers, Inc.
Acme Electric
Merli Concrete
Olson Precast
Las Vegas Paving
Nevada Tap Master
The Tiberti Fence - TAB
Total for TAB Contractors - Main
Southland - TC
Lone Mountain - Southland
Total for Southland - TC

y 2019.	Cumulative ho	urs through	h February 2019	
Total	Total	Total	Total	Total
Hours	Minority/Female	Veteran	Minority/Female %	Veteran %
			<u> </u>	•
30	30	0	100%	0%
198	198	0	100%	0%
228	228	0	100%	0%
0	0	0	0%	0%
110	33	0	30%	0%
110	33	0	30%	0%
14,088	10,673	0	76%	0%
14,088	10,673	0	76%	0%
14,000	10,073	U	7076	0 /0
99	99	0	100%	0%
99	99	0	100%	0%
2,439	605	0	25%	0%
2,333	2,076	0	89%	0%
27	12	0	44%	0%
91	91	0	100%	0%
2	2	0	100%	0%
4	0	0	0%	0%
7	7	0	100%	0%
4	4	0	100%	0%
88	44	0	50%	0%
4,993	2,838	0	57%	0%
20,543	19,614	0	95%	0%
4,450	3,347	0	75%	0%
379	0	0	0%	0%
297	0	0	0%	0%
1,346	719	0	53%	0%
27,015	23,680	0	88%	0%
100	4=		0.407	201
139	47	0	34%	0%
139	47	0	34%	0%
99,774	43,640	119	44%	0%
100	100	0	100%	0%
314	172	0	55%	0%
3,648	2,254	0	62%	0%
422	266	0	63%	0%
5,069	4,815	0	95%	0%
323	323	0	100%	0%
7,119	6,907	0	97%	0%
80	67	0	83%	0%
184	108	0	59%	0%
4	0	0	0%	0%
4	0	0	0%	0%
2,353	1,334	0	57%	0%
10	0	0	0%	0%
521	363	0	70%	0%
80	88	0	110%	0%
	0	0	0%	0%
10			4000/	00/
3	3	0	100%	0%
		0 119	100% 50%	0% 0%
3 120,015	3 60,438	119	50%	0%
3	3	_		

Workforce Utilization



Las Vegas Stadium Workforce Utilization Summary

This report reflects the cumulative hours worked through February 2019.

Subcontractor
Gephart-Morse, LLC
Morse Electric - GM
A-1 Concrete - Morse
MMC - A-1 Morse
Lone Mountain - Morse
Live Electric - Morse
Pyrocom
Gephart Electric - GM
Total for Gephart-Morse, LLC
Total for Cophart Moroc, E20
The Tiberti Fence
Flippins
Total for Tiberti Fence
Total for Tiberti Ferioc
Malcolm Drilling
CMC Rebar
Clark Welding & Fabricating
Dielco Crane
MMC
Total for Malcolm Drilling
Mortancon McCarthy
Mortenson McCarthy
Merli Concrete Pumping CMC Rebar
Gateway Concrete
Jcord
Precision
Silver Star Ready Mix
Commercial Scaffolding
Union Erectors - MMc Concrete
Reliable Crane Service - MMc
Penhall Company
MJ Dean
Total for Mortenson McCarthy Joint Venture
Eberhard SW Roofing
Eberhard SW Roofing Total for Eberhard Southwest Roofing
Total for Eberhard Southwest Roofing Sunstate
Total for Eberhard Southwest Roofing Sunstate Expansion Specialties
Total for Eberhard Southwest Roofing Sunstate Expansion Specialties GM Construction
Total for Eberhard Southwest Roofing Sunstate Expansion Specialties GM Construction Reliable Steel - GM
Total for Eberhard Southwest Roofing Sunstate Expansion Specialties GM Construction Reliable Steel - GM Dielco - GM
Total for Eberhard Southwest Roofing Sunstate Expansion Specialties GM Construction Reliable Steel - GM
Total for Eberhard Southwest Roofing Sunstate Expansion Specialties GM Construction Reliable Steel - GM Dielco - GM Total for Sunstate
Total for Eberhard Southwest Roofing Sunstate Expansion Specialties GM Construction Reliable Steel - GM Dielco - GM Total for Sunstate Harris
Total for Eberhard Southwest Roofing Sunstate Expansion Specialties GM Construction Reliable Steel - GM Dielco - GM Total for Sunstate Harris Energy Mechanical Insulation
Total for Eberhard Southwest Roofing Sunstate Expansion Specialties GM Construction Reliable Steel - GM Dielco - GM Total for Sunstate Harris Energy Mechanical Insulation Advanced Controls & Electric
Total for Eberhard Southwest Roofing Sunstate Expansion Specialties GM Construction Reliable Steel - GM Dielco - GM Total for Sunstate Harris Energy Mechanical Insulation Advanced Controls & Electric Maui One
Total for Eberhard Southwest Roofing Sunstate Expansion Specialties GM Construction Reliable Steel - GM Dielco - GM Total for Sunstate Harris Energy Mechanical Insulation Advanced Controls & Electric Maui One Lone Mountain
Total for Eberhard Southwest Roofing Sunstate Expansion Specialties GM Construction Reliable Steel - GM Dielco - GM Total for Sunstate Harris Energy Mechanical Insulation Advanced Controls & Electric Maui One
Sunstate Expansion Specialties GM Construction Reliable Steel - GM Dielco - GM Total for Sunstate Harris Energy Mechanical Insulation Advanced Controls & Electric Maui One Lone Mountain Total for Harris
Total for Eberhard Southwest Roofing Sunstate Expansion Specialties GM Construction Reliable Steel - GM Dielco - GM Total for Sunstate Harris Energy Mechanical Insulation Advanced Controls & Electric Maui One Lone Mountain Total for Harris Merrill Steel
Total for Eberhard Southwest Roofing Sunstate Expansion Specialties GM Construction Reliable Steel - GM Dielco - GM Total for Sunstate Harris Energy Mechanical Insulation Advanced Controls & Electric Maui One Lone Mountain Total for Harris Merrill Steel Corona Stud & Deck
Total for Eberhard Southwest Roofing Sunstate Expansion Specialties GM Construction Reliable Steel - GM Dielco - GM Total for Sunstate Harris Energy Mechanical Insulation Advanced Controls & Electric Maui One Lone Mountain Total for Harris Merrill Steel Corona Stud & Deck Niles Industrial Coatings
Total for Eberhard Southwest Roofing Sunstate Expansion Specialties GM Construction Reliable Steel - GM Dielco - GM Total for Sunstate Harris Energy Mechanical Insulation Advanced Controls & Electric Maui One Lone Mountain Total for Harris Merrill Steel Corona Stud & Deck Niles Industrial Coatings Union Erectors
Total for Eberhard Southwest Roofing Sunstate Expansion Specialties GM Construction Reliable Steel - GM Dielco - GM Total for Sunstate Harris Energy Mechanical Insulation Advanced Controls & Electric Maui One Lone Mountain Total for Harris Merrill Steel Corona Stud & Deck Niles Industrial Coatings
Sunstate Expansion Specialties GM Construction Reliable Steel - GM Dielco - GM Total for Sunstate Harris Energy Mechanical Insulation Advanced Controls & Electric Maui One Lone Mountain Total for Harris Merrill Steel Corona Stud & Deck Niles Industrial Coatings Union Erectors - Derr
Sunstate Expansion Specialties GM Construction Reliable Steel - GM Dielco - GM Total for Sunstate Harris Energy Mechanical Insulation Advanced Controls & Electric Maui One Lone Mountain Total for Harris Merrill Steel Corona Stud & Deck Niles Industrial Coatings Union Erectors - Derr
Sunstate Expansion Specialties GM Construction Reliable Steel - GM Dielco - GM Total for Sunstate Harris Energy Mechanical Insulation Advanced Controls & Electric Maui One Lone Mountain Total for Harris Merrill Steel Corona Stud & Deck Niles Industrial Coatings Union Erectors Derr & Isbell

Total Hours Minority/Female Veteran Winority/Female Veteran Winority/Female Veteran Winority/Female Veteran	ary 2019.	Cumulative ho	urs through	h February 2019	
0 0 0 0% 0% 57,142 39,716 5,463 70% 10% 664 293 24 44% 4% 52 52 0 100% 0% 98 98 0 100% 0% 20 0 0 0% 0% 0 0 0 0% 0% 68,007 44,568 5,487 66% 8% 1,364 1,036 142 76% 10% 77 25 0 32% 0% 1,441 1,061 142 76% 10% 18,088 6,022 0 33% 0% 2,913 2,030 0 70% 0% 108 0 0 0% 0% 5 5 0 100% 0% 2,913 2,030 0 70% 0% 167 76 0 4	Total		Total		Total
67.142 39.716 5.463 70% 10% 664 293 24 44% 4% 52 52 0 100% 0% 10,032 4,410 0 44% 0% 98 98 0 100% 0% 0 0 0 0% 0% 20 0 0 0% 0% 0 0 0 0% 0% 68,007 44,568 5,487 66% 8% 1,364 1,036 142 76% 10% 77 25 0 32% 0% 1,441 1,061 142 74% 10% 18,088 6,022 0 33% 0% 2,913 2,030 0 70% 0% 5 5 5 0 100% 0% 4,441 1,668 78% 3% 0% 21,280 8,133		Minority/Female		Minority/Female %	Veteran %
67.142 39.716 5.463 70% 10% 664 293 24 44% 4% 52 52 0 100% 0% 10,032 4,410 0 44% 0% 98 98 0 100% 0% 0 0 0 0% 0% 20 0 0 0% 0% 0 0 0 0% 0% 68,007 44,568 5,487 66% 8% 1,364 1,036 142 76% 10% 77 25 0 32% 0% 1,441 1,061 142 74% 10% 18,088 6,022 0 33% 0% 2,913 2,030 0 70% 0% 5 5 5 0 100% 0% 4,441 1,668 78% 3% 0% 21,280 8,133	0	0	0	0%	0%
664 293 24 44% 4% 52 52 0 100% 0% 98 98 0 100% 0% 20 0 0 0% 0% 0 0 0 0% 0% 0 0 0 0% 0% 0 0 0 0% 0% 0 0 0 0% 0% 0 0 0 0% 0% 0 0 0 0% 0% 1344 1,036 142 76% 10% 77 25 0 32% 0% 1441 1,061 142 74% 10% 15 0 33% 0% 0% 2,913 2,030 0 70% 0% 2,913 2,030 0 70% 0% 2,128 8 0 0 0 0%					
52					
10,032			1		
98 98 98 0 100% 0% 20 0 0 0 0 0% 0% 68,007 44,568 5,487 66% 8% 1,364 1,036 142 76% 10% 77 25 0 32% 0% 1,441 1,061 142 74% 10% 18,088 6,022 0 33% 0% 167,76 76 0 46% 0% 5 5 5 0 100% 0% 21,280 8,133 0 38% 0% 21,1280 8,133 0 38% 0% 341,481 265,162 10,648 78% 3% 2,295,72 196,028 311 85% 0% 157,670 115,629 6,686 73% 4% 8,479 6,207 0 73% 0% 0 0 0 0 0% 0% 15,363 5,967 165 39% 1% 3,939 3,939 0 100% 0% 2,1286 946 0 4% 05% 631 562 0 89% 0% 21,286 946 0 4% 05% 2,1186 946 0 4% 0% 633 7,207 0 31% 0% 633 7,207 0 91% 0% 7,776 7,755 0 100% 0% 58 48 0 83% 0% 58 48 0 83% 0% 58 48 0 83% 0% 58 393 0 0 0% 58 48 0 83% 0% 58 48 0 83% 0% 58 48 0 83% 0% 58 48 0 83% 0% 58 48 0 83% 0% 58 48 0 83% 0% 58 48 0 83% 0% 58 48 0 83% 0% 58 48 0 83% 0% 58 48 0 83% 0% 58 58 48 0 83% 0% 58 58 48 0 83% 0% 58 63,333 1,841 40% 0% 58 63,393 2,452 0 61% 0% 58 63,09 22,543 1,841 40% 3% 59,600 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0					
20					
0 0 0 0% 0% 68,007 44,568 5,487 66% 8% 1,364 1,036 142 76% 10% 77 25 0 32% 0% 1,441 1,061 142 74% 10% 18,088 6,022 0 33% 0% 2,913 2,030 0 70% 0% 167 76 0 46% 0% 108 0 0 0% 0% 5 5 0 100% 0% 21,280 8,133 0 38% 0% 2,128 486 0 23% 0% 2,128 486 0 23% 0% 15,7670 115,629 6,686 73% 4% 8,479 6,207 0 73% 0% 15,363 5,967 165 39% 1% 3,939 3,939					
1,364					
77 25 0 32% 0% 1,441 1,061 142 74% 10% 18,088 6,022 0 33% 0% 2,913 2,030 0 70% 0% 167 76 0 46% 0% 108 0 0 0% 0% 5 5 0 100% 0% 21,280 8,133 0 38% 0% 21,281 486 0 23% 0% 22,128 486 0 23% 0% 229,572 196,028 311 85% 0% 157,670 115,629 6,686 73% 4% 8,479 6,207 0 73% 0% 0 0 0 0 0 0% 15,363 5,967 165 39% 1% 3,939 3,939 0 100% 0% 21,286	68,007	44,568			
77 25 0 32% 0% 1,441 1,061 142 74% 10% 18,088 6,022 0 33% 0% 2,913 2,030 0 70% 0% 167 76 0 46% 0% 108 0 0 0% 0% 5 5 0 100% 0% 21,280 8,133 0 38% 0% 21,281 486 0 23% 0% 22,128 486 0 23% 0% 229,572 196,028 311 85% 0% 157,670 115,629 6,686 73% 4% 8,479 6,207 0 73% 0% 0 0 0 0 0 0% 15,363 5,967 165 39% 1% 3,939 3,939 0 100% 0% 21,286	1 364	1.036	1/12	76%	10%
1,441 1,061 142 74% 10% 18,088 6,022 0 33% 0% 2,913 2,030 0 70% 0% 167 76 0 46% 0% 108 0 0 0% 0% 5 5 0 100% 0% 21,280 8,133 0 38% 0% 341,481 265,162 10,648 78% 3% 2,128 486 0 23% 0% 157,670 115,629 6,686 73% 4% 8,479 6,207 0 73% 0% 15,363 5,967 165 39% 1% 3,939 3,939 0 100% 0% 2,310 584 0 25% 0% 2,1286 946 0 4% 0% 9,516 7,724 0 81% 0% 7,776 <td< td=""><td></td><td></td><td>1</td><td></td><td></td></td<>			1		
2,913 2,030 0 70% 0% 167 76 0 46% 0% 108 0 0 0% 0% 5 5 0 100% 0% 21,280 8,133 0 38% 0% 341,481 265,162 10,648 78% 3% 2,128 486 0 23% 0% 229,572 196,028 311 85% 0% 229,572 196,028 311 85% 0% 8,479 6,207 0 73% 0% 8,479 6,207 0 73% 0% 15,363 5,967 165 39% 1% 3,393 3,939 0 100% 0% 2,310 584 0 25% 0% 21,286 946 0 4% 0% 9,516 7,724 0 81% 0% 7,776 <td< td=""><td></td><td></td><td>_</td><td></td><td></td></td<>			_		
2,913 2,030 0 70% 0% 167 76 0 46% 0% 108 0 0 0% 0% 5 5 0 100% 0% 21,280 8,133 0 38% 0% 341,481 265,162 10,648 78% 3% 2,128 486 0 23% 0% 229,572 196,028 311 85% 0% 229,572 196,028 311 85% 0% 8,479 6,207 0 73% 0% 8,479 6,207 0 73% 0% 15,363 5,967 165 39% 1% 3,393 3,939 0 100% 0% 2,310 584 0 25% 0% 21,286 946 0 4% 0% 9,516 7,724 0 81% 0% 7,776 <td< td=""><td></td><td></td><td></td><td></td><td></td></td<>					
167 76 0 46% 0% 108 0 0 0% 0% 5 5 0 100% 0% 21,280 8,133 0 38% 0% 341,481 265,162 10,648 78% 3% 2,128 486 0 23% 0% 229,572 196,028 311 85% 0% 157,670 115,629 6,686 73% 4% 8,479 6,207 0 73% 0% 15,363 5,967 165 39% 1% 3,939 3,939 0 100% 0% 2,310 584 0 25% 0% 2,1,286 946 0 4% 0% 631 562 0 89% 0% 9,516 7,724 0 81% 0% 7,776 7,755 0 100% 0% 58 48					
108		-	_		
5 5 0 100% 0% 21,280 8,133 0 38% 0% 341,481 265,162 10,648 78% 3% 2,128 486 0 23% 0% 229,572 196,028 311 85% 0% 157,670 115,629 6,686 73% 4% 8,479 6,207 0 73% 0% 0 0 0 0 0% 0% 15,363 5,967 165 39% 1% 0% 3,939 3,939 0 100% 0% 21,286 946 0 4% 0% 631 562 0 89% 0% 9,516 7,724 0 81% 0% 7,776 7,755 0 100% 0% 7,963 7,207 0 91% 0% 893 0 0 0% 0% <tr< td=""><td></td><td></td><td></td><td></td><td></td></tr<>					
21,280 8,133 0 38% 0% 341,481 265,162 10,648 78% 3% 2,128 486 0 23% 0% 229,572 196,028 311 85% 0% 157,670 115,629 6,686 73% 4% 8,479 6,207 0 73% 0% 0 0 0 0 0% 0% 15,363 5,967 165 39% 1% 3,3939 100% 0% 2,310 584 0 25% 0% 21,286 946 0 4% 0% 21,286 946 0 4% 0% 0% 0% 9,516 7,724 0 81% 0% 9,516 7,724 0 81% 0% 0% 0% 0% 7,776 7,755 0 100% 0% 0% 0% 58 48 0 83% 0% 0% 0%					
341,481 265,162 10,648 78% 3% 2,128 486 0 23% 0% 229,572 196,028 311 85% 0% 157,670 115,629 6,686 73% 4% 8,479 6,207 0 73% 0% 0 0 0 0 0% 0% 15,363 5,967 165 39% 1% 3,939 3,939 0 100% 0% 2,310 584 0 25% 0% 2% 21,286 946 0 4% 0% 28 9,516 7,724 0 81% 0% 9,516 7,724 0 81% 0% 79 3,516 7,755 0 100% 0% 7,776 7,755 0 100% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0%			_		
2,128 486 0 23% 0% 229,572 196,028 311 85% 0% 157,670 115,629 6,686 73% 4% 8,479 6,207 0 73% 0% 0 0 0 0% 0% 15,363 5,967 165 39% 1% 3,939 3,939 0 100% 0% 2,310 584 0 25% 0% 21,286 946 0 4% 0% 631 562 0 89% 0% 9,516 7,724 0 81% 0% 7,776 7,755 0 100% 0% 7,776 7,755 0 100% 0% 7,963 7,207 0 91% 0% 893 0 0 0% 0% 10,540 7,835 0 74% 0% 56,309 22,5	21,280	8,133	0	38%	0%
2,128 486 0 23% 0% 229,572 196,028 311 85% 0% 157,670 115,629 6,686 73% 4% 8,479 6,207 0 73% 0% 0 0 0 0% 0% 15,363 5,967 165 39% 1% 3,939 3,939 0 100% 0% 2,310 584 0 25% 0% 21,286 946 0 4% 0% 631 562 0 89% 0% 9,516 7,724 0 81% 0% 7,776 7,755 0 100% 0% 7,776 7,755 0 100% 0% 7,963 7,207 0 91% 0% 893 0 0 0% 0% 10,540 7,835 0 74% 0% 56,309 22,5	2/1 /01	265 162	10.649	700/	30/
229,572 196,028 311 85% 0% 157,670 115,629 6,686 73% 4% 8,479 6,207 0 73% 0% 0 0 0 0% 0% 15,363 5,967 165 39% 1% 3,939 3,939 0 100% 0% 2,310 584 0 25% 0% 21,286 946 0 4% 0% 631 562 0 89% 0% 9,516 7,724 0 81% 0% 7,776 7,755 0 100% 0% 7,776 7,755 0 100% 0% 7,963 7,207 0 91% 0% 893 0 0 0% 0% 10,540 7,835 0 74% 0% 56,309 22,543 1,841 40% 3% 2,764 <					
157,670 115,629 6,686 73% 4% 8,479 6,207 0 73% 0% 0 0 0 0% 0% 15,363 5,967 165 39% 1% 3,939 3,939 0 100% 0% 2,310 584 0 25% 0% 21,286 946 0 4% 0% 631 562 0 89% 0% 9,516 7,724 0 81% 0% 7,776 7,755 0 100% 0% 7,776 7,755 0 100% 0% 7,963 7,207 0 91% 0% 1,626 580 0 36% 0% 893 0 0 0% 0% 10,540 7,835 0 74% 0% 56,309 22,543 1,841 40% 3% 2,764 1,087					
8,479 6,207 0 73% 0% 0 0 0 0% 0% 15,363 5,967 165 39% 1% 3,939 3,939 0 100% 0% 2,310 584 0 25% 0% 21,286 946 0 4% 0% 631 562 0 89% 0% 9,516 7,724 0 81% 0% 7,2375 603,233 17,809 76% 2% 7,776 7,755 0 100% 0% 7,776 7,755 0 100% 0% 58 48 0 83% 0% 7,963 7,207 0 91% 0% 893 0 0 0% 0% 893 0 0 0% 0% 893 0 0 0% 0% 893 0 0					
0 0 0 0% 0% 15,363 5,967 165 39% 1% 3,939 3,939 0 100% 0% 2,310 584 0 25% 0% 21,286 946 0 4% 0% 631 562 0 89% 0% 9,516 7,724 0 81% 0% 792,375 603,233 17,809 76% 2% 7,776 7,755 0 100% 0% 7,776 7,755 0 100% 0% 58 48 0 83% 0% 7,963 7,207 0 91% 0% 1,626 580 0 36% 0% 893 0 0 0% 0% 56,309 22,543 1,841 40% 3% 2,764 1,087 10 39% 0% 4,009 2,452					
15,363 5,967 165 39% 1% 3,939 3,939 0 100% 0% 21,286 946 0 4% 0% 631 562 0 89% 0% 9,516 7,724 0 81% 0% 792,375 603,233 17,809 76% 2% 7,776 7,755 0 100% 0% 7,963 7,207 0 91% 0% 893 0 0 0% 0% 893 0 0 0% 0% 10,540 7,835 0 74% 0% 56,309 22,543 1,841 40% 3% 2,764 1,087 10 39% 0% 4,009 2,452 0 61% 0% 4,494 1,888 0 42% 0% 67,783 27,969 1,861 41% 3% 0					
3,939 3,939 0 100% 0% 2,310 584 0 25% 0% 21,286 946 0 4% 0% 631 562 0 89% 0% 9,516 7,724 0 81% 0% 792,375 603,233 17,809 76% 2% 7,776 7,755 0 100% 0% 7,776 7,755 0 100% 0% 58 48 0 83% 0% 7,963 7,207 0 91% 0% 893 0 0 0% 0% 893 0 0 0% 0% 10,540 7,835 0 74% 0% 56,309 22,543 1,841 40% 3% 2,764 1,087 10 39% 0% 4,009 2,452 0 61% 0% 4,494 1,888 <td></td> <td></td> <td></td> <td></td> <td></td>					
2,310 584 0 25% 0% 21,286 946 0 4% 0% 631 562 0 89% 0% 9,516 7,724 0 81% 0% 792,375 603,233 17,809 76% 2% 7,776 7,755 0 100% 0% 7,776 7,755 0 100% 0% 58 48 0 83% 0% 7,963 7,207 0 91% 0% 8833 0 0 0% 0% 10,540 7,835 0 74% 0% 56,309 22,543 1,841 40% 3% 2,764 1,087 10 39% 0% 4,009 2,452 0 61% 0% 4,494 1,888 0 42% 0% 67,783 27,969 1,861 41% 3% 0 <td< td=""><td></td><td></td><td></td><td></td><td></td></td<>					
21,286 946 0 4% 0% 631 562 0 89% 0% 9,516 7,724 0 81% 0% 792,375 603,233 17,809 76% 2% 7,776 7,755 0 100% 0% 7,776 7,755 0 100% 0% 0 0 0 0% 0% 58 48 0 83% 0% 7,963 7,207 0 91% 0% 1,626 580 0 36% 0% 893 0 0 0% 0% 10,540 7,835 0 74% 0% 56,309 22,543 1,841 40% 3% 2,764 1,087 10 39% 0% 4,009 2,452 0 61% 0% 4,494 1,888 0 42% 0% 67,783 27,969 <td></td> <td></td> <td></td> <td></td> <td></td>					
631 562 0 89% 0% 9,516 7,724 0 81% 0% 792,375 603,233 17,809 76% 2% 7,776 7,755 0 100% 0% 0 0 0 0% 0% 58 48 0 83% 0% 7,963 7,207 0 91% 0% 1,626 580 0 36% 0% 893 0 0 0% 0% 10,540 7,835 0 74% 0% 56,309 22,543 1,841 40% 3% 2,764 1,087 10 39% 0% 4,009 2,452 0 61% 0% 4,494 1,888 0 42% 0% 67,783 27,969 1,861 41% 3% 0 0 0 0% 0% 2,987 349			_		
9,516 7,724 0 81% 0% 792,375 603,233 17,809 76% 2% 7,776 7,755 0 100% 0% 0 0 0 0% 0% 58 48 0 83% 0% 7,963 7,207 0 91% 0% 1,626 580 0 36% 0% 893 0 0 0% 0% 10,540 7,835 0 74% 0% 56,309 22,543 1,841 40% 3% 2,764 1,087 10 39% 0% 4,009 2,452 0 61% 0% 4,494 1,888 0 42% 0% 67,783 27,969 1,861 41% 3% 0 0 0 0% 0% 11,923 3,325 0 28% 0% 2,987 349			_		
792,375 603,233 17,809 76% 2% 7,776 7,755 0 100% 0% 7,776 7,755 0 100% 0% 0 0 0 0% 0% 58 48 0 83% 0% 7,963 7,207 0 91% 0% 1,626 580 0 36% 0% 893 0 0 0% 0% 10,540 7,835 0 74% 0% 56,309 22,543 1,841 40% 3% 2,764 1,087 10 39% 0% 4,009 2,452 0 61% 0% 4,494 1,888 0 42% 0% 67,783 27,969 1,861 41% 3% 0 0 0 0% 0% 2,987 349 27 12% 1% 204 52					
7,776 7,755 0 100% 0% 7,776 7,755 0 100% 0% 0 0 0 0% 0% 58 48 0 83% 0% 7,963 7,207 0 91% 0% 1,626 580 0 36% 0% 893 0 0 0% 0% 10,540 7,835 0 74% 0% 56,309 22,543 1,841 40% 3% 2,764 1,087 10 39% 0% 4,009 2,452 0 61% 0% 4,494 1,888 0 42% 0% 67,783 27,969 1,861 41% 3% 0 0 0 0% 0% 1,923 3,325 0 28% 0% 2,987 349 27 12% 1% 204 52			_		
7,776 7,755 0 100% 0% 0 0 0 0% 0% 58 48 0 83% 0% 7,963 7,207 0 91% 0% 1,626 580 0 36% 0% 893 0 0 0% 0% 10,540 7,835 0 74% 0% 56,309 22,543 1,841 40% 3% 2,764 1,087 10 39% 0% 4,009 2,452 0 61% 0% 4,494 1,888 0 42% 0% 67,783 27,969 1,861 41% 3% 0 0 0 0% 0% 1,923 3,325 0 28% 0% 2,987 349 27 12% 1% 204 52 0 25% 0% 108,805 48,313 <t< td=""><td></td><td>,</td><td>,</td><td></td><td></td></t<>		,	,		
0 0 0 0% 0% 58 48 0 83% 0% 7,963 7,207 0 91% 0% 1,626 580 0 36% 0% 893 0 0 0% 0% 10,540 7,835 0 74% 0% 56,309 22,543 1,841 40% 3% 2,764 1,087 10 39% 0% 207 0 10 0% 5% 4,009 2,452 0 61% 0% 4,494 1,888 0 42% 0% 67,783 27,969 1,861 41% 3% 0 0 0 0% 0% 11,923 3,325 0 28% 0% 2,987 349 27 12% 1% 204 52 0 25% 0% 108,805 48,313 0 <td></td> <td>•</td> <td>0</td> <td></td> <td></td>		•	0		
58 48 0 83% 0% 7,963 7,207 0 91% 0% 1,626 580 0 36% 0% 893 0 0 0% 0% 10,540 7,835 0 74% 0% 56,309 22,543 1,841 40% 3% 2,764 1,087 10 39% 0% 207 0 10 0% 5% 4,009 2,452 0 61% 0% 4,494 1,888 0 42% 0% 67,783 27,969 1,861 41% 3% 0 0 0 0% 0% 11,923 3,325 0 28% 0% 2,987 349 27 12% 1% 204 52 0 25% 0% 108,805 48,313 0 44% 0% 7,610 2,032	7,776	7,755	0	100%	0%
58 48 0 83% 0% 7,963 7,207 0 91% 0% 1,626 580 0 36% 0% 893 0 0 0% 0% 10,540 7,835 0 74% 0% 56,309 22,543 1,841 40% 3% 2,764 1,087 10 39% 0% 207 0 10 0% 5% 4,009 2,452 0 61% 0% 4,494 1,888 0 42% 0% 67,783 27,969 1,861 41% 3% 0 0 0 0% 0% 11,923 3,325 0 28% 0% 2,987 349 27 12% 1% 204 52 0 25% 0% 108,805 48,313 0 44% 0% 7,610 2,032	0	0	0	0%	0%
7,963 7,207 0 91% 0% 1,626 580 0 36% 0% 893 0 0 0% 0% 10,540 7,835 0 74% 0% 56,309 22,543 1,841 40% 3% 2,764 1,087 10 39% 0% 207 0 10 0% 5% 4,009 2,452 0 61% 0% 4,494 1,888 0 42% 0% 67,783 27,969 1,861 41% 3% 0 0 0 0% 0% 11,923 3,325 0 28% 0% 2,987 349 27 12% 1% 204 52 0 25% 0% 108,805 48,313 0 44% 0% 7,610 2,032 514 27% 7% 7,228 565					
1,626 580 0 36% 0% 893 0 0 0% 0% 10,540 7,835 0 74% 0% 56,309 22,543 1,841 40% 3% 2,764 1,087 10 39% 0% 207 0 10 0% 5% 4,009 2,452 0 61% 0% 4,494 1,888 0 42% 0% 67,783 27,969 1,861 41% 3% 0 0 0 0% 0% 11,923 3,325 0 28% 0% 2,987 349 27 12% 1% 204 52 0 25% 0% 108,805 48,313 0 44% 0% 7,610 2,032 514 27% 7% 7,228 565 0 8% 0%			1		
893 0 0 0% 0% 10,540 7,835 0 74% 0% 56,309 22,543 1,841 40% 3% 2,764 1,087 10 39% 0% 207 0 10 0% 5% 4,009 2,452 0 61% 0% 4,494 1,888 0 42% 0% 67,783 27,969 1,861 41% 3% 0 0 0 0% 0% 11,923 3,325 0 28% 0% 2,987 349 27 12% 1% 204 52 0 25% 0% 108,805 48,313 0 44% 0% 7,610 2,032 514 27% 7% 7,228 565 0 8% 0%					
10,540 7,835 0 74% 0% 56,309 22,543 1,841 40% 3% 2,764 1,087 10 39% 0% 207 0 10 0% 5% 4,009 2,452 0 61% 0% 4,494 1,888 0 42% 0% 67,783 27,969 1,861 41% 3% 0 0 0 0% 0% 11,923 3,325 0 28% 0% 2,987 349 27 12% 1% 204 52 0 25% 0% 108,805 48,313 0 44% 0% 7,610 2,032 514 27% 7% 7,228 565 0 8% 0%			_		
56,309 22,543 1,841 40% 3% 2,764 1,087 10 39% 0% 207 0 10 0% 5% 4,009 2,452 0 61% 0% 4,494 1,888 0 42% 0% 67,783 27,969 1,861 41% 3% 0 0 0 0% 0% 11,923 3,325 0 28% 0% 2,987 349 27 12% 1% 204 52 0 25% 0% 108,805 48,313 0 44% 0% 7,610 2,032 514 27% 7% 7,228 565 0 8% 0%					
2,764 1,087 10 39% 0% 207 0 10 0% 5% 4,009 2,452 0 61% 0% 4,494 1,888 0 42% 0% 67,783 27,969 1,861 41% 3% 0 0 0 0% 0% 11,923 3,325 0 28% 0% 2,987 349 27 12% 1% 204 52 0 25% 0% 108,805 48,313 0 44% 0% 7,610 2,032 514 27% 7% 7,228 565 0 8% 0%	10,040	.,500	_	. 170	3 70
2,764 1,087 10 39% 0% 207 0 10 0% 5% 4,009 2,452 0 61% 0% 4,494 1,888 0 42% 0% 67,783 27,969 1,861 41% 3% 0 0 0 0% 0% 11,923 3,325 0 28% 0% 2,987 349 27 12% 1% 204 52 0 25% 0% 108,805 48,313 0 44% 0% 7,610 2,032 514 27% 7% 7,228 565 0 8% 0%	56,309	22,543	1,841	40%	3%
207 0 10 0% 5% 4,009 2,452 0 61% 0% 4,494 1,888 0 42% 0% 67,783 27,969 1,861 41% 3% 0 0 0 0% 0% 11,923 3,325 0 28% 0% 2,987 349 27 12% 1% 204 52 0 25% 0% 108,805 48,313 0 44% 0% 7,610 2,032 514 27% 7% 7,228 565 0 8% 0%					
4,009 2,452 0 61% 0% 4,494 1,888 0 42% 0% 67,783 27,969 1,861 41% 3% 0 0 0 0% 0% 11,923 3,325 0 28% 0% 2,987 349 27 12% 1% 204 52 0 25% 0% 108,805 48,313 0 44% 0% 7,610 2,032 514 27% 7% 7,228 565 0 8% 0%					
67,783 27,969 1,861 41% 3% 0 0 0 0% 0% 11,923 3,325 0 28% 0% 2,987 349 27 12% 1% 204 52 0 25% 0% 108,805 48,313 0 44% 0% 7,610 2,032 514 27% 7% 7,228 565 0 8% 0%	4,009	2,452			
67,783 27,969 1,861 41% 3% 0 0 0 0% 0% 11,923 3,325 0 28% 0% 2,987 349 27 12% 1% 204 52 0 25% 0% 108,805 48,313 0 44% 0% 7,610 2,032 514 27% 7% 7,228 565 0 8% 0%	4,494	1,888	0	42%	0%
11,923 3,325 0 28% 0% 2,987 349 27 12% 1% 204 52 0 25% 0% 108,805 48,313 0 44% 0% 7,610 2,032 514 27% 7% 7,228 565 0 8% 0%	67,783		1,861		
11,923 3,325 0 28% 0% 2,987 349 27 12% 1% 204 52 0 25% 0% 108,805 48,313 0 44% 0% 7,610 2,032 514 27% 7% 7,228 565 0 8% 0%	0	0	0	00/	Λ0/
2,987 349 27 12% 1% 204 52 0 25% 0% 108,805 48,313 0 44% 0% 7,610 2,032 514 27% 7% 7,228 565 0 8% 0%					
204 52 0 25% 0% 108,805 48,313 0 44% 0% 7,610 2,032 514 27% 7% 7,228 565 0 8% 0%					
108,805 48,313 0 44% 0% 7,610 2,032 514 27% 7% 7,228 565 0 8% 0%			1		
7,610 2,032 514 27% 7% 7,228 565 0 8% 0%					
7,228 565 0 8% 0%			_		
138,756 54,634 541 39% 0%			_		



Las Vegas Stadium Workforce Utilization Summary

This report reflects the cumulative hours worked through February 2019.

This report reflects the cumulative hours worked through F Subcontractor					
Subcontractor					
Enclos					
Total for Enclos					
KONE					
Total for KONE					
Desert Fire Protection					
TAB					
Energy Mechanical Insulation - Desert Fire					
Jcord					
Total for Desert Fire					
Gephart/Morse - Low Voltage					
Morse - GM Low Voltage					
Total for Gephart/Morse - Low Voltage					
· · · · · · · · · · · · · · · · · · ·					
Performance Contracting					
Commercial Scaffolding - PCI					
Gale Building Products					
Total for Performance Contracting					
Aggregate Industries - MSE					
Total for Aggregate Industries					
Total for riggrogate maderies					
CEDCO Commercial LLC					
Total for CEDCO Commercial, LLC					
Total for CEDCO Commercial, EEC					
Dallian Diabaa Oanatuustian					
Rolling Plains Construction					
Total for Rolling Plains Construction					
Union Erectors - Core					
Total for Union Erectors - Core					
Derr & Isbell - Hoist					
Total for Derr & Isbell - Hoist					
Freyssinet					
Dielco Crane					
Vision Construction					
Dielco - Vision					
Total for Freyssinet					
American Door					
Stewart & Sundell					
Total for American Door					
Danny's Construction					
Total for Danny's Construction Co.					
•					
TOTAL HOURS					

	Cumulative hor	irs through	h February 2019	
Total	Total	Total	Total	Total
	Minority/Female			Veteran %
Hours	wimority/remaie	Veteran	Minority/Female %	veteran %
138	0	0	0%	0%
	0			
138	0	0	0%	0%
6,349	1,192	0	19%	0%
6,349	1,192	0	19%	0%
0,0.0	.,	Ū	1070	370
6,683	2,326	65	35%	1%
109	101	0	93%	0%
2	0	0	0%	0%
3	0	0	0%	0%
6,797	2,427	65	36%	1%
0	0	0	0%	0%
1,827	0	0	0%	0%
1,827	0	0	0%	0%
18,974	14,289	0	75%	0%
57	14,269 57	0	100%	0%
322	306	0	95%	0%
19,353	14,651	0	76%	0%
13,333	14,001		1070	070
5,149	2,246	134	44%	0%
5,149	2,246	134	44%	3%
0,140	2,240	104	7770	070
5,577	3,471	0	62%	0%
5,577	3,471	0	62%	0%
5,611	0 ,		V =70	3,0
1,079	613	0	57%	0%
1,079	613	0	57%	0%
, , ,				
16	0	0	0%	0%
16	0	0	0%	0%
2,897	1,404	0	48%	0%
2,897	1,404	0	48%	0%
93	0	0	0%	0%
9	0	0	0%	0%
0	0	0	0%	0%
10	0	0	0%	0%
112	0	0	0%	0%
14	14	0	100%	0%
228	223	0	98%	0%
242	237	0	98%	0%
165	99	0	60%	0%
165	99	0	60%	0%
1,325,429	879,904	26,157	66%	2%
		Goal	38%	



IN THE COMMUNITY

RAIDERS CELEBRATE NEVADA READING WEEK WITH LOCAL STUDENTS

The Raiders returned to their Resource Room at Robert L. Taylor Elementary during Nevada Reading Week to celebrate Nevada Reading Week. Raiders Alumni Leo Gray and Reggie Kinlaw presented Roaring Reader Awards to students for their literacy achievements and hosted readings with two classes with the highest participation numbers in the school's Apple Core Reading Program.

In addition, the Raiderettes and Raider Rusher joined the celebration by reading to students at John Dooley Elementary in Henderson and John Tarten Elementary in North Las Vegas.









RAIDERS DUCK, DIVE AND DODGE TO HELP LOCAL STUDENTS

Members of the Las Vegas Raiders Family Association (LVRFA) recently gathered to duck, dive and dodge to help local Las Vegas area students.

The LVRFA, which consists of Raiders staff, Alumni, sales and construction partners as well as their families and significant others who reside in Southern Nevada, supported underserved by forming a team and participating in the 5th Annual All-Star Dodgeball Tournament.

The team played in three matches, which included six games total and competed for bragging rights, prizes, a huge trophy and the title of 2019 Dodgeball Champions.

Proceeds from the fun-filled day of dodgeball benefited After-School All-Stars of Greater Las Vegas, whose mission is to provide free comprehensive after-school sports, educational, cultural and community enrichment programs that keep children safe and help them achieve in school and life.

EARTHCAM VIEW - MARCH 14, 2019






ADDITIONAL INFORMATION / UPDATES

StadCo has, and continues to, comply with Section 35 (2)(c) and 35 (2)(e) of the Act as evidenced by JLL's Report.

In accordance with Section 31- (c)(1)(2)(3) of the Act, Mortenson | McCarthy Las Vegas Stadium, A Joint Venture is following the process described below to verify the payment of applicable prevailing wages.

Contractors that are awarded construction contracts for the work are required to follow the NRS 338 requirements outlined in the Act. This section pertains to the prevailing wage for public works projects as governed by the Nevada Labor Commissioner.

Mortenson | McCarthy has implemented LCPTracker Construction Certified Payroll—Labor Compliance Software which is a widely recognized tracking and certification software for prevailing wage projects. Mortenson | McCarthy maintains and updates the required prevailing wage rates in the database, based on those published by the Nevada Labor Commissioner's website. All contractors that have received a construction contract and are subject to the prevailing wage requirements are required to report payroll hours and wages for designated workers through this system. The contractor's entries into this system verifies compliance with wages and fringes as noted in the NRS 338 requirements.

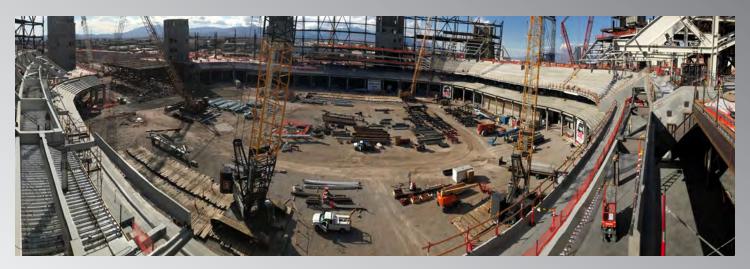

Bowl Panorama looking West from the 200 level.

Installation of the MSE wall surrounding the field tray continues. Detailing continues on steel truss columns; final thirds of the long span trusses are being installed. Bowl steel erection continues moving from North to South, working down the east and west sidelines. Steel canopy pre-assembly is ongoing around the perimeter of the building. Precast work continues installing suite tubs down both sidelines. Slab on metal deck is being placed on the 150, 200, and 300 levels of the building. Slab on grade work continues on Event level. Masonry work continues on Event level working down both sidelines. Metal stud and drywall continue being installed on Event, 050, and 100 level. Fireproofing is largely complete on the North end and continues above 100, 150, and 200 working to the South.



Above: Looking North from the top of the temporary ramp.

Below: Panorama view of canopy truss pre-assembly.



All photographs appearing in this document are the property of LV Stadium Events Company, LLC. They are protected by U.S. Copyright Laws, and are not to be shared or reproduced in any way without the written permission of LV Stadium Events Company, LLC. Copyright 2018 LV Stadium Events Company, LLC. All Rights Reserved.



Above: View from 300 level looking Southwest.

Below: View from 100 level looking Northeast.

