GUARANTEED MAXIMUM PRICE DESIGN-BUILD AGREEMENT

by and between

LV STADIUM EVENTS COMPANY, LLC
as StadCo

and

MORTENSON-MCCARTHY LAS VEGAS STADIUM, A JOINT VENTURE
as Design-Builder, comprised of M. A. Mortenson Company, a Minnesota Corporation (0072732)
and McCarthy Building Companies, Inc., a Missouri Corporation (0066125)

Dated as of February 20, 2017

(the "Effective Date")

TABLE OF CONTENTS

PAGE

ARTICLE 1. GENERAL 2
1.1 Certain Defined Terms 2
1.2 Other Terms 12
ARTICLE 2. RELATIONSHIP OF THE PARTIES 12
2.1 Stadium Authority 12
2.2 Cooperation with Project Development Team and StadCo 12
2.3 Architect of Record Services 12
2.4 Project Teaming 13
2.6 Lender Required Information 14
2.7 Cooperation with Governmental Authorities 15
2.8 Limitation of Authority 15
2.9 Representations and General Obligations 16
ARTICLE 3. PRELIMINARY DESIGN PHASE & GMP DEVELOPMENT 18
3.1 Programming and Construction Plan 18
3.2 Project Schedules 18
3.3 BIM and Design Phase Completion 19
3.4 Development of Interim GMP Drawings and Specifications Sets 19
3.5 Cost Estimates and Construction Cost Budget 19
3.6 GMP Development 20
3.7 Fast Track Procurement 21
ARTICLE 4. FINAL DESIGN AND CONSTRUCTION PHASE 21
4.1 Construction Drawings and Specifications 21
4.2 Subcontract Procurement 22
4.3 Self-Performed Work 24
4.4 Early Release Work 24
4.5 Assignment of Subcontracts 25
4.6 Project Labor Agreement 25
4.7 Meetings; Reports; Schedule Updates 25
4.8 Construction 26
4.9 Testing 28
4.10 Quality Management 29
4.11 Use of Hazardous Materials 29
4.12 Adjacent Property/Ongoing Operations 29
4.13 Checkout of Utilities; Training of Operating Personnel 30
ARTICLE 5. CONTRACT TIME 30
5.1 Time 30
5.2 Delay Liquidated Damages and Waiver of Consequential Damages 30

5.3 Extensions of Time 32
5.4 Acceleration 33
ARTICLE 6. STADCO'S RESPONSIBILITIES 33
6.1 StadCo's Representative 33
6.2 Hazardous Materials 34
6.3 Evidence of Financing 35
6.4 Work by Separate Contractors 35
ARTICLE 7. CONTRACT SUM/PAYMENT 36
7.1 Contract Sum; Design-Build Contingency 36
7.2 Allowances 38
7.3 Cost of the Work 38
7.4 Preconstruction Services and Design-Builder's Fee 42
7.5 Shared Savings 43
7.6 Accounting Records/Right to Audit 43
7.7 Progress Payments 44
7.8 Final Payment 48
7.9 Warranty of Title 49
7.10 Project Suspension or Abandonment 49
ARTICLE 8. WARRANTY/CORRECTION OF WORK 49
ARTICLE 9. INDEMNIFICATION 51
9.1 General 51
9.2 Patent Indemnification 51
9.3 Lien Indemnification 51
9.4 Professional Negligence Indemnification 52
9.5 Defense of Indemnitees 52
9.6 Indemnification Not Limited by Worker's Compensation; Disability Benefits Act 52
9.7 Environmental Indemnity 53
9.8 Exceptions 53
9.9 Limitation of Liability 53
ARTICLE 10. TERMINATION AND STADCO'S RIGHT TO PERFORM DESIGN-BUILDER'S OBLIGATIONS 54
10.1 Suspension and Termination by Design-Builder 54
10.2 StadCo's Right to Perform Design-Builder's Obligations and Termination by StadCo for Cause 54
10.3 Termination for Convenience 55
ARTICLE 11. SUCCESSORS AND ASSIGNS 55
ARTICLE 12. EXTENT OF AGREEMENT 56
12.1 Entire Agreement 56
12.2 Third-Party Rights 56
ARTICLE 13. INSURANCE/BONDS 56

13.1 Design-Builder's Insurance 56
13.2 Bonds 56
13.3 StadCo Insurance 56
ARTICLE 14. CHANGES AND RENEWED REQUESTS FOR CHANGE ORDERS 57
14.1 Change Orders 57
14.2 Changes Directed by StadCo 57
14.3 Changes other than StadCo-Directed Changes; RRCOs and Notice 57
14.4 Performance of Changed Work 58
ARTICLE 15. NOTICE OF RENEWED REQUEST FOR CHANGE ORDERS AND DISPUTES 59
15.1 Work Continuance and Payment 59
15.2 Notice of RRCO 60
15.3 Notice of Dispute 60
15.4 Good Faith Negotiations 60
15.5 Mandatory Mediation Process and Selection of Mediator 61
15.6 Notice of Intent to Arbitrate 62
15.7 Nevada Statutory Remedies (Chapters 108 and 624) 62
ARTICLE 16. BINDING ARBITRATION 63
16.1 Meet and Confer Process 63
16.2 Binding Arbitration 63
16.3 Injunctive or Equitable Relief 63
16.4 Commencement of Arbitration 63
16.5 Selection of Arbitrator; Number and Eligibility of Arbitrators; Fees 64
16.6 Administration of Arbitration 64
16.7 Flow Down Provision 65
ARTICLE 17. MISCELLANEOUS PROVISIONS 65
ARTICLE 18. OWNERSHIP OF DOCUMENTS 67
18.1 StadCo's Documents 67
18.2 Use of Documents 68
18.3 No Lien Claims 69
18.4 Termination 69
18.5 Nevada Administrative Code Sect. 623.780 69
18.6 Grant of License No Other License 69

GUARANTEED MAXIMUM PRICE DESIGN-BUILD AGREEMENT

THIS GUARANTEED MAXIMUM PRICE DESIGN-BUILD AGREEMENT is made as of the 20th day of February, 2017 ("**Effective Date**"), by and between LV Stadium Events Company, LLC, a Nevada limited liability company ("**StadCo**"), and Mortenson-McCarthy Las Vegas Stadium, a Joint Venture, comprised of M. A. Mortenson Company, a Minnesota corporation, and McCarthy Building Companies, Inc., a Missouri corporation, as design-builder ("**Design-Builder**") (individually a "**Party**" and together the "**Parties**"). StadCo and Design-Builder agree as follows:

RECITALS

A. StadCo is responsible for the development of the Las Vegas Stadium (as further defined below). The Las Vegas Stadium is intended, among other things, to be the future home of the Las Vegas Raiders, which is a professional football franchise (currently known as the Oakland Raiders) and member of the National Football League ("**NFL**").

B. In 2016, the Nevada legislature, finding that the expenditure of public money for the acquisition, construction, lease, improvement, equipping, operation and maintenance, financing, and long-term use of a multi-purpose stadium and related infrastructure as a venue for an NFL team in Nevada and a broad range of other civic, community, athletic, educational, cultural, and commercial activities serves a public purpose, enacted legislation known as Senate Bill 1 (the "**Act**") on October 17, 2016 creating the Authority (as further defined below) and establishing a method to finance the construction of a large-scale, one-of-a-kind, and state of the art stadium (the "**Stadium**") and specific stadium infrastructure directly related to the Stadium (the "**Infrastructure**") in Clark County, Nevada (the "**County**").

C. The Act provides for the creation of a Development Agreement (as further defined below) that contains Project (as further defined below) requirements and contractual requirements, among other criteria, required of the Parties. The Development Agreement addresses public financing of the Project, required contributions from Stadco, and for tax-exempt ownership of the Stadium by the Authority.

D. The Development Agreement will provide relevant terms and conditions pursuant to which StadCo's architects, designers, design-builder, and contractors will design and construct the Stadium and the Infrastructure in the County on a site more fully described on **Exhibit J** (the "**Site**").

E. In furtherance of the purposes of the Act and the anticipated obligations under the Development Agreement, StadCo retained ICON Venue Group, LLC as its representative ("**StadCo's Representative**") to assist StadCo, in providing direction, to the degree necessary, concerning the activities to be performed by AOR, AOR Consultants, as well as StadCo Consultants, Lead Design Architect, and Design-Builder (collectively the "**Project Team**"), and, in connection therewith, to provide StadCo's Representative services on behalf of StadCo. The services of StadCo's Representative shall in no way diminish Design-Builder's responsibility to perform its services in accordance with and otherwise comply with the terms of this Agreement.

F. Design-Builder understands (i) the Project is being funded with public funds pursuant to the Act and the Development Agreement, and this Agreement will be subject to the terms and requirements of the Act and approval of the Stadium Authority, (ii) StadCo will obtain funding for the private funding for the Project through the NFL, institutional lenders and through other sources (which institutional lenders or other sources are hereinafter collectively or individually referred to as "**Construction Lender(s)**") and (iii) as conditions of the Development Agreement and the Construction Lender's financing of the Project, this Agreement, and the design and construction of the Project, will be subject to the review and approval rights of the Authority, the NFL, and the Construction Lender.

NOW, THEREFORE, in consideration of the mutual covenants and conditions contained herein, StadCo and Design-Builder hereby agree to be bound by the terms set forth in this Agreement.

AGREEMENT

ARTICLE 1. GENERAL

1.1 Certain Defined Terms.

Whenever used in this Agreement, the following terms shall have the meanings specified below or as otherwise defined in this Agreement. Definitions of terms that are phrased in the singular shall be deemed to include the plural, and vice versa, where appropriate to the context or circumstances, and the use of feminine, masculine, or neuter pronouns shall each include the other. Wherever the word "including" or any variation thereof, is used herein, it shall mean "including, without limitation," and shall be construed as a term of illustration, not a term of limitation. In addition to other terms defined herein, as used in this Agreement, the following terms shall have the meanings indicated below:

1.1.1 "Act" shall mean the Southern Nevada Tourism Improvement Act, also known as Senate Bill No. 1 of the 30th Special Session (2016) of the Nevada State Legislature, as more fully described in the Recitals. In the event of any conflict between this Agreement and the Act, the Act shall take precedence.

1.1.2 "ADA" shall have the meaning set forth in the definition of Applicable Laws.

1.1.3 "Affiliate(s)" of any specified Person means any other Person directly or indirectly controlling or controlled by or under direct or indirect common control with such specified Person, or which is a director, officer, employee, or partner (limited or general) of such specified Person. For the purpose of this definition, **"control"**, when used with respect to any specified Person, means the possession, direct or indirect, of the power to vote five percent (5%) or more of the securities having ordinary voting power for the election of directors or the power to direct or cause the direction of the management and policies of such Person, directly or indirectly, whether through the ownership of voting securities, by contract or otherwise; and the terms **"controlling"** and **"controlled"** have meanings correlative to the foregoing.

1.1.4 "Agreement" shall mean this Agreement between Design-Builder and StadCo, including all Schedules and Exhibits attached hereto.

1.1.5 "AOR" or **"Architect of Record"** shall mean HNTB Nevada Inc., a Nevada corporation, and its parent company and their Affiliates, subsidiaries, partnerships, and other related entities.

1.1.6 "AOR Agreement" or **"Architect of Record Agreement"** shall mean the agreement between StadCo and AOR with respect to the design Services of the Project.

1.1.7 "AOR's Consultant(s)" or **"AOR Consultant(s)"** or **"Architect's Consultant(s)"** shall mean the Persons engaged by AOR at AOR's expense to provide certain professional services to AOR in connection with the performance of AOR's Services under the AOR Agreement, and shall include subconsultants.

1.1.8 "Applicable Law(s)" or **"applicable law(s)"** or **"Law(s)"** shall mean any applicable law, statute, code, ordinance, order, rule, regulation, or requirement of any Governmental Authority enacted or issued applicable to the Project or the Work, including but not limited to: (a) all guidelines, rules and regulations of the applicable Uniform Building Code and the International Building Code; (b) the Occupational Safety and Health Act of 1970, as amended (**"OSHA"**); (c) Nevada OSHA; (d) the Americans with Disabilities Act (**"ADA"**); (e) the Act; (f) U.S. Foreign Corrupt Practices Act of 1977, as amended; (g) Environmental Laws; (h) local life safety requirements; (i) any other applicable federal, international, or local laws, rules and regulations concerning bribery or corruption whether in force on the date hereof or enacted thereafter, but subject to the provisions of **Section 4.1.2**.

1.1.9 "Application for Final Payment" shall mean a written statement submitted by Design-Builder requesting its Final Payment for services rendered and/or materials furnished in connection with carrying out the Work following Final Completion of its Work.

1.1.10 "Application for Payment" shall mean Design-Builder's certified request for payment for completed portions of the Work pursuant to **Section 7.7** hereof and in the form required by the Contract Documents, and as set forth in **Exhibit D**.

1.1.11 "Architectural Program" shall mean the program statement to be prepared by AOR, and approved by StadCo, that sets forth general descriptions and requirements of functions, elements, systems, areas and other program elements to be incorporated into the design of the Project. The Architectural Program shall be attached to the GMP Amendment.

1.1.12 "As Builts" shall mean a set of the Construction Drawings and Specifications marked-up by Design-Builder, which shall be subject to review and reasonable verification and comment by AOR, to show the **"as-built"** condition of the Project as it materially differs from the Contract Documents including, without limitation, the locations of mechanical, electrical, plumbing, or similar portions of the Work that are shown diagrammatically in the Contract Documents.

1.1.13 "Authority" or **"Stadium Authority"** shall mean the Clark County Stadium Authority, a political subdivision of Clark County, Nevada, and a separate governmental entity established pursuant to Senate Bill 1 of the 30th Special Session of the Nevada State Legislature, also known as the **"Las Vegas Stadium Authority"** and the **"Las Vegas Stadium Authority Board"** and as may be further defined in the Development Agreement.

1.1.14 "BIM" shall have the meaning set forth in **Section 3.3.1** of this Agreement.

1.1.15 "Building Standard" shall mean a premier, first-class stadium, of similar quality as U.S. Bank Stadium, and as required by the Architectural Program, Applicable Laws, and the final Construction Documents.

1.1.16 "Change Order" shall mean a written instrument signed in accordance with the requirements of the Contract Documents describing an adjustment in the Contract Sum or Contract Time or both.

1.1.17 "Conceptual Design Documents" shall mean the document entitled **"Las Vegas Stadium, 100% Concept Design"** dated May 1, 2017.

1.1.18 "Consequential Damages" shall mean damages for losses and/or expenditures related to principal office expenses, rental expenses, loss of goodwill, damage to reputation, loss of profits or revenue, loss of opportunity, loss of use, loss of business, loss of financing, and for loss of management or employee productivity or of the services of such Persons.

1.1.19 "Construction Change Directive" shall mean a written order by StadCo to Design-Builder directing a change in the Work prior to final agreement on the adjustment, if any, to the Contract Sum or Contract Time.

1.1.20 "Construction Cost" shall mean the total cost (based on currently estimated cost) to StadCo of all elements of the Project designed or specified by Lead Design Architect, AOR, and AOR's consultants, and shall include the Cost of the Work plus the Design-Build Contingency, and AOR's compensation and expenses including AOR's consultants and subconsultants. Construction Cost does not include the following: compensation of Lead Design Architect, StadCo consultants, the cost of the land, rights-of-way costs, legal fees and costs, StadCo's administrative costs and other items not specifically contained within the Design-Builder's GMP, or financing costs.

1.1.21 "Construction Cost Budget" shall mean Construction Cost budgeted by StadCo for the Project which is One Billion Three Hundred Ninety-Nine Million Seven Hundred Ninety-Three Thousand One Hundred Thirty-Six Dollars ($1,399,793,136.00), subject to written modification by StadCo.

1.1.22 "Construction Drawings and Specifications" or **"Construction Documents"** shall mean the working drawings and specifications describing the standards, size, character, workmanship, performance requirements, design, construction, Materials, finishes, fixtures, structure and mechanical, electrical and other systems of the Project produced by AOR pursuant to the AOR Agreement, as further described in **Section 4.1** hereof, all in a manner consistent with the approved GMP Documents, this Agreement, and the terms of the AOR Agreement.

1.1.23 "Construction Phase" shall mean that phase of the Work that begins upon Design-Builder's commencement of construction at the Site and ends at Substantial Completion.

1.1.24 "Construction Plan" shall mean a plan for construction of the Project that will include: (a) the construction staging plan setting forth construction sequencing and phasing, lay down areas and storage, trailer areas, trailer locations, priorities as to Site use, ingress/egress and other similar Site logistic matters for the Project and (b) procedures for the assignment of responsibilities for safety precautions and programs.

1.1.25 "Contract Documents" shall mean (a) this Agreement, (b) the GMP Documents, (c) the Construction Drawings and Specifications when approved by StadCo, (d) any executed Change Orders, and (e) any duly executed amendments to any of the foregoing.

1.1.26 "Contract Sum" shall have the meaning set forth in **Section 7.1.1** hereof.

1.1.27 "Contract Time" shall mean the time allowed for the completion of the Project contemplated in this Agreement and the completion of each milestone or key phase or element of the Project.

1.1.28 "Cost of the Work" shall have the meaning set forth in **Section 7.3.2** hereof.

1.1.29 "County" shall mean Clark County, Nevada.

1.1.30 "Day(s)" or **"day(s)"** shall mean calendar day, including weekends and legal holidays, whether capitalized or not, unless otherwise specifically provided.

1.1.31 "Defective Work" or **"Nonconforming Work"** shall mean any Work that does not comply with the requirements of the Contract Documents.

1.1.32 "Delay" shall mean any impact or disruption to critical path activities in accordance with the applicable Master Project Schedule.

1.1.33 "Delay Liquidated Damages" shall have the meaning set forth in **Section 5.2** hereof.

1.1.34 "Design-Build Contingency" or **"Contingency"** shall have the meaning set forth in **Section 7.1.2** hereof.

1.1.35 "Design-Builder" shall mean Mortenson-McCarthy Las Vegas Stadium, a Joint Venture comprised of M. A. Mortenson Company, a Minnesota Corporation (0072732), and McCarthy Building Companies, Inc., a Missouri Corporation (0066125).

1.1.36 "Design-Builder's Fee" or **"Fee"** shall have the meaning set forth in set forth in **Section 7.4.2** hereof.

1.1.37 "Design-Build Warranty Period" or **"Warranty Period"** shall have the meaning set forth in **Section 8.1** of this Agreement.

1.1.38 "Design-Builder's Warranty Obligations" shall have the meaning set forth in **Article 8** of this Agreement.

1.1.39 "Design Consultant(s)" shall mean the Persons engaged by Design-Builder at Design-Builder's expense to provide certain professional services to Design-Builder in connection with the performance of Design-Builder's Work under this Agreement, and shall include subconsultants.

1.1.40 "Design Documents" shall mean all plans, drawings, tracings, specifications, programs, reports, calculations, models, and other material containing designs, specifications, or engineering information prepared by AOR and/or AOR's Consultants including, without limitation, computer aided design materials, electronic data files, files, and paper copies.

1.1.41 "Development Agreement" shall mean the agreement between StadCo and the Stadium Authority setting forth the Project requirements, relevant terms and conditions pertaining to design and construction of the Site, and as further described in the Recitals.

1.1.42 "Dispute(s)" shall mean any first-party dispute between the Parties to this Agreement related to breach, default, or any grievance related to the Agreement which does not including a RRCO.

1.1.43 "Drawings" shall mean the graphic and pictorial portions of the Contract Documents prepared by AOR and/or AOR's Consultants showing the design, location, and dimensions of the Work, including plans, elevations, details, schedules, and diagrams. The term Drawings may be used interchangeably with Plans.

1.1.44 "Environmental Law(s)" shall mean, without limitation, any applicable federal, state, or local laws, ordinances or regulations relating to the environment, health, and safety, Hazardous Substances (including, without limitation, the use, handling, transportation, production, disposal, discharge, or storage thereof) or to industrial hygiene or the environmental conditions on, under or about the Site, including, without limitation, soil, groundwater, and indoor and ambient air conditions, including, without limitation, the following: Comprehensive Environmental Response, Compensation and Liability Act of 1980, as amended (42 U.S.C.§§ 9601–9675), the Resource Conservation and Recovery Act, as amended (42 U.S.C. §§ 6901–6992k), the Hazardous Materials Transportation Act, as amended (49 U.S.C. § 1801 et seq.), the Federal Water Pollution Control Act, as amended (33 U.S.C. §§ 1251–1307), the Clean Air Act, as amended (42 U.S.C.§§ 7401–7671et seq.), the Toxic Substances Control Act, as amended (15 U.S.C. §§ 2601–2692), the Residential lead-Based Paint Hazard Reduction Act of 1992 (Title X), 15 U.S.C. §§ 2681-2692 and also 42 U.S.C.§§ 4851–4856, the Lead Based Paint Poisoning Prevention Act,42 U.S.C. §§ 4821–4846, the Indoor Radon Abatement Act, 15 U.S.C. §§ 2661–2671, and the Safe Drinking Water Act Amendments of 1996, Pub L. No. 104-182, 110 Stat. 1613 (1996), and all similar federal, state and local statutes and regulations.

1.1.45 "Errors and Omissions" shall mean errors, omissions, conflicts, inconsistencies, or deficiencies in any: plans; specifications; drawings; designs; responses to requests for information; Submittals or Shop Drawings; specifications or instructions furnished by or through Design-Builder, Subcontractors of any tier, or AOR; Construction Documents; or Contract Documents prepared as part of the Work.

1.1.46 "Equipment" means all equipment, tools (other than small tools), machinery, implements, and other items used in connection with the Work, but not incorporated into the permanent Work.

1.1.47 "FIFA" shall mean the Fédération Internationale de Football Association, the governing body of international soccer.

1.1.48 "Final Completion" or **"Finally Complete"** shall refer to the point at which: (i) the entirety of the Work is actually and fully completed, including all minor corrective, or Punch List items, and StadCo, in its reasonable determination, has accepted the Work in writing; (ii) Design-Builder shall have certified to StadCo in writing that, to the best of its information, knowledge, and belief, the Work, including but not limited to Punch List items which remained to be completed after Substantial Completion, has been completed in accordance with the Contract Documents; (iii) AOR shall confirm to StadCo in writing, in a form and substance reasonably satisfactory to StadCo, that the Work, including but not limited to Punch List items which remained to be completed after Substantial Completion, has been completed to the best of AOR's knowledge, information, and belief in accordance with the Contract Documents; (iv) all documents required to be submitted by Design-Builder as a condition of Final Completion of such Work have been submitted, (including, without limitation, warranties, guarantees and other Specified Documents); (v) the entirety of such Work and related areas of the Site have been thoroughly cleared of all construction debris and cleaned in accordance with the requirements of the Contract Documents, including, but not necessarily limited to removal of temporary protections; (vi) all Governmental Authorities having jurisdiction over the Project shall have inspected the Work and the Project and shall have unconditionally authorized occupancy of the Project, as it pertains to the Work, in its entirety as evidenced by the issuance of a permanent certificate of occupancy and any other Governmental Approvals which may be required for occupancy of the Project, and (vii) all conditions set forth in the Contract Documents for Final Completion of such Work have been fully satisfied. Notwithstanding anything herein to the contrary, the determination of Final Completion will not be denied if any permits, approvals, or certificates are withheld or delayed for reasons unrelated to Design-Builder's performance of the Work or its duties under the Contract Documents.

1.1.49 "Force Majeure" shall mean acts of God, wars, civil disturbances, fires, floods, strikes, seismic activity, freight embargoes, excessive and abnormal adverse rain and snow conditions, excessive heat, sandstorms, and any acts or other causes beyond the Design-Builder's control.

1.1.50 "General Conditions Work" shall mean the services to be provided by Design-Builder as identified in the exhibit attached to the GMP Amendment.

1.1.51 "GMP" or **"Guaranteed Maximum Price"** shall mean the guaranteed maximum price set forth in the GMP Amendment.

1.1.52 "GMP Amendment" shall mean an amendment to this Agreement, in the form of Amendment No. 1 attached hereto as **Exhibit C**, to establish and memorialize the final GMP as part of this Agreement.

1.1.53 "GMP Documents" shall mean the GMP Drawings and Specifications, the Prose Statement, the GMP Qualifications and Assumptions, and the other documents set forth in the GMP Amendment.

1.1.54 "GMP Drawings and Specifications" shall mean the drawings, specifications and other design documents that satisfy the criteria set forth in the GMP Amendment. For purposes of the Master Project Schedule and delivery of design deliverables up to the delivery of the GMP Drawings and Specifications, the Project's design will be delivered as twenty-five percent (25%) GMP Drawings and Specifications, sixty-two and a half percent (62.5%) GMP Drawings and Specifications, and Final one-hundred percent (100%) GMP Drawings and Specifications.

1.1.55 "GMP Qualifications and Assumptions" shall mean the written statement of qualifications and assumptions prepared by Design-Builder, based upon the GMP Drawings and Specifications and Prose Statement and approved by the Parties and AOR pursuant to **Section 3.6** hereof.

1.1.56 "Governmental Approval(s)" shall mean any and all governmental permits, filings, approvals, certificates, exceptions, variances, and authorizations of every kind (including but not limited to zoning approvals or variances, environmental permits, building permits, conditional use permits, and subdivision approvals) required from Governmental Authorities having jurisdiction over the development and construction of the Project.

1.1.57 "Governmental Authority(ies)" shall mean any and all federal, state, county, and city governments, and quasi-governmental authorities, including but not limited to the Stadium Authority, all agencies, subdivisions, and special purpose districts thereof, having jurisdiction over the development, design, and construction of the Work, Site, or Project, or governmental authorities or special purpose districts with whom StadCo has entered into agreements for funding or other incentives

1.1.58 "Guaranteed Substantial Completion Date" means July 31st, 2020, or such other date as may be set forth in the GMP Amendment, as the same may be amended from time to time pursuant to the terms of this Agreement.

1.1.59 "Hazardous Materials" shall mean any material, waste, substance or chemical deemed to be hazardous under applicable federal, state, and local laws, codes, ordinances, rules, regulations, orders, and decrees of any government or quasi government entity having jurisdiction over the Project or Site, the practices involved in the Project or Site, or any Work, or regulating the handling, storage, remediation, or disposal of such material and includes, but is not limited to any hazardous, ignitable, corrosive, caustic, reactive, toxic, or polluting waste or substance; a **"hazardous waste"** (as defined in the regulations adopted under the Resource Conservation and Recovery Act of 1976); oil or petroleum products; asbestos; polychlorinated biphenyls; formaldehyde compounds, explosives, and radioactive materials.

1.1.60 "Indemnitees" shall mean StadCo, the Team, StadCo's Representative, the Authority, Lender, the County, Third-Party Beneficiaries, and each of their respective subsidiaries, Affiliates, parent companies and their respective members, officers, trustees, shareholders, public officials, members, partners, employees, successors and assigns, heirs, administrators, and personal representatives, and any Person who has a financial or operating interest in the Project whom StadCo reasonably requests be added as an Indemnitee hereunder.

1.1.61 "Lead Design Architect" shall mean Manica Architecture, a Kansas professional association.

1.1.62 "Lead Design Architect's Sub-consultants" shall mean, collectively, those architectural and engineering consultants engaged by Lead Design Architect.

1.1.63 "League Rules" shall mean, to the extent they are in writing and current as of the date of the GMP Amendment, the constitution, by-laws, rules, regulations, standards and recommendations of each of the NFL and NCAA Division I Football (and NCAA Division I Basketball and FIFA to the extent StadCo selects a NCAA Division I Basketball or FIFA compliant Stadium as part of the final GMP Amendment), as they apply to the design, construction, security and operation of new venues as further described in the Architectural Program that will be completed with the express understanding that the Project will (a) be the home venue of one of an NFL franchise, (b) host an NFL championship game, currently known as the Super Bowl, (c) be the home venue of an NCAA Division I football program, (d) to host an NCAA Division I Basketball Final Four Championship, and (e) host a World Cup soccer match, or similar international soccer event. When compliance with the League Rules are required pursuant to this Agreement, priority of precedence shall be given in the order listed in the preceding sentence. AOR shall confirm the applicable League Rules in writing no later than the date of the GMP Amendment.

1.1.64 "Lease" shall mean that certain Lease Agreement by and between StadCo and the Authority, as the same may from time to time be amended in accordance with its terms.

1.1.65 "Lender(s)" or **"Construction Lender(s)"** shall mean any bank, insurance company, trust, corporation, association, firm, partnership, Person, any funding trust or similar entity created for the purpose of financing the StadCo Contribution Amount, or other entity that has, directly or indirectly through the trust, loaned or agreed to lend or otherwise provide funds or credit enhancement to enable StadCo to build the Project, and includes, without limitation, any collateral agent acting on behalf of any of the foregoing entities. **"Lender"** shall also include any financing entity which serves to further the financing structure in connection with a financing transaction that utilizes other Lenders for the purpose of financing, collateral assignment, guaranty, participation, and other functions which coordinate and cooperate with other Lenders.

1.1.66 "Letter Agreement" shall mean the Letter of Intent and Limited Authorization to Perform, dated as of February 20, 2017, and any amendments thereto, by and between StadCo and Design-Builder authorizing the commencement of certain preconstruction and construction services set forth therein.

1.1.67 "Master Project Schedule" shall mean a detailed and comprehensive Project schedule, prepared by Design-Builder, using a critical path method that is in conformance with accepted industry standards for projects of this size, scope, and complexity, that identifies, coordinates, and integrates the design tasks and the construction schedule, StadCo's responsibilities, Government Authority reviews, and other activities as necessary for the timely completion of the Project. The Master Project Schedule shall include the various phases of AOR's Services and Design-Builder's Work. The Master Project Schedule is attached hereto as **Exhibit K**.

1.1.68 "Materials" means all materials, supplies, appliances, equipment, fixtures, and other items to be incorporated into the Work or consumed in connection with the Work.

1.1.69 "NCAA" shall mean the National Collegiate Athletic Association.

1.1.70 "NFL" shall mean the National Football League.

1.1.71 "NFL Season" means the football season established by the NFL, including the pre-season and post-season games to the extent that Team are participants.

1.1.72 "Non-Allowable Cost of Work" or **"Non-Allowable Cost"** shall have the meaning set forth in **Section 7.3.4**.

1.1.73 "Non-Game Event" shall mean any event that is not an NFL football game event and shall have any additional meaning set forth in **Section 5.2.1.3**.

1.1.74 "OCIP" shall have the meaning set forth in **Section 13.3.1** hereof.

1.1.75 "Person" or **"Persons"** shall mean any individual, corporation, partnership, joint venture, association, joint stock company, trust, limited liability company, unincorporated organization, Governmental Authority, or any other form of entity.

1.1.76 "Prime Rate" shall mean the rate of interest per annum published in the money rates section of *The Wall Street Journal* as the U.S. prime rate (sometimes referred to as the base rate) as of the date interest begins to accrue.

1.1.77 "Product Data" shall mean illustrations, standard schedules, performance charts, instructions, brochures, diagrams, or other information furnished by Design-Builder or Subcontractor of any tier to illustrate a material, product, or system for some portion of the Work.

1.1.78 "Project" shall mean the design and construction of a multi-purpose first-class, premier stadium and related on-Site infrastructure to be used as a venue for an NFL team, University of

Nevada, Las Vegas football team, broad range of other civic, community, athletic, educational, cultural, and commercial activities as further described in the GMP Documents.

1.1.79 "Project Closeout Documents" means the As-Built Drawings, all maintenance and operating manuals, warranties, guarantees, training manuals, and records that are required to be furnished by the Design-Builder to StadCo under the Contract Documents.

1.1.80 "Project Development Team" shall mean, collectively, StadCo, StadCo's Representative, StadCo's Design Team, Design-Builder, AOR, and such members as may be selected by StadCo from time to time.

1.1.81 "Project Report" shall mean the monthly report to be prepared by Design-Builder in the form approved by StadCo pursuant to **Section 4.7.4** hereof.

1.1.82 "Prose Statement" shall mean the detailed listing or narrative developed by AOR in coordination with Lead Design Architect to describe all known incomplete design elements contained in the GMP Drawings and Specifications and AOR's statement of intended scope with respect to such incomplete elements. The Prose Statement shall be reviewed and approved by AOR.

1.1.83 "Punch List" shall mean the list prepared by Design-Builder and reviewed and approved by StadCo and AOR containing minor items of incomplete Work to be completed and/or corrected after Substantial Completion.

1.1.84 "Renewed Request for Change Order" or **"RRCO"** shall have the meaning set forth in **Section 15.2**.

1.1.85 "Responsibility Matrix" shall mean the work and services identified in **Exhibit A**.

1.1.86 "Samples" shall mean physical examples, mock-ups, or specimens intended to illustrate Materials, equipment, or workmanship and/or to establish standards by which the Work will be judged, submitted by Design-Builder to StadCo for its review and approval.

1.1.87 "Savings" shall mean the difference arrived at when subtracting the final Cost of the Work and the final Design-Builder's Fee from the final GMP. Savings, if any, shall be calculated as of the date of Final Completion.

1.1.88 "Schedule of Values" shall mean the statement furnished by Design-Builder reflecting the portions of the Contract Sum allocated to the various portions of the Work and, when approved by StadCo, to be used as a basis for reviewing Applications for Payment.

1.1.89 "Self-Performed Work" shall mean the following categories of Work in which a substantial portion thereof is performed directly by Design-Builder's own labor forces or the labor forces of any Affiliate of Design-Builder (including the joint venture partners of Design-Builder), and not through Subcontracts or purchase orders with third-party contractors or Suppliers: (1) cast-in-place concrete, (2) general conditions and Site services, as will be defined in the GMP Documents, (3) rough carpentry and finish carpentry (including, without limitation, installation of millwork and installation of cabinetry), and (4) such other trades as StadCo may approve.

1.1.90 "Separate Contractors" shall mean any Persons or firms other than Design-Builder performing work for the Project that are under direct contract with StadCo.

1.1.91 "Services" shall mean AOR's services as described in the AOR Agreement, design assist services and design services provided by Subcontractors, and Design-Builder's construction management services.

1.1.92 "Shop Drawings" means drawings, diagrams, illustrations, schedules, performance charts and other data specifically prepared for the Project by Design-Builder or any Subcontractor, manufacturer, Supplier or distributor that illustrates how specific portions of the Work shall be fabricated and/or installed.

1.1.93 "Site" or **"Project Site"** shall mean the area of land on which the Project is located, the boundaries of which are shown on **Exhibit J**.

1.1.94 "StadCo" shall mean the LV Stadium Events Company, LLC, a Nevada limited liability company.

1.1.95 "StadCo's Consultant" shall mean any Person who provides design or design consulting services to StadCo and who is not a subcontractor or subconsultant of AOR.

1.1.96 "StadCo's Design Team" shall mean, collectively, AOR, AOR's subconsultants, Lead Design Architect, and Lead Design Architect's subconsultants.

1.1.97 "StadCo Contribution Amount" shall have the meaning set forth in the Development Agreement.

1.1.98 "StadCo's Representative" shall mean ICON Venue Group, LLC, or such other Person as shall be designated from time to time by StadCo in a similar capacity.

1.1.99 "Stadium" shall mean the premier, first-class venue to be constructed on the Site for professional football and a broad range of other civic, community, athletic, educational, cultural, and commercial activities used primarily for hosting Team games.

1.1.100 "Standard of Care" shall mean the standard of professional care, technical knowledge, skill, diligence, effort, and quality prevailing among nationally recognized design-build firms, architectural firms, and engineering firms including, but not limited to, those with a national reputation for design of professional sport stadiums that contemporaneously or within the past ten (10) years have been engaged in the planning, design, engineering, preconstruction, and construction administration, management, implementation, and design integration of large scale and complex projects of similar scope, function, size, quality, complexity, and detail, including contemporary sports stadiums similar to the Project throughout the United States.

1.1.101 "Subcontract" shall mean any subcontract for the various categories of Work between Design-Builder and a Subcontractor.

1.1.102 "Subcontractor(s)" shall mean a Person who has a direct contract with Design-Builder to perform any of the Work (including Equipment leases and Material purchase agreements) at the Site, but does not include Design-Builder's consultants, AOR, or AOR's consultants.

1.1.103 "Submittals" shall mean Samples, Shop Drawings, and other detailed designs, samples, exemplars, product data, fabrication and installation drawings, lists, graphs, operating instructions, and other similar documents required to be submitted by a Design-Builder or a Subcontractor or Vendor under the Contract Documents.

1.1.104 "Substantial Completion" or **"Substantially Complete"** shall mean the stage in the progress of the Work when all of the following are achieved: (a) the Work (or separable areas, units or phases as provided in the Contract Documents) is complete in accordance with the Contract Documents and all Applicable Law, such that the Project is ready for opening to the general public and for use and enjoyment by StadCo, the Team and their employees and such Work can be beneficially occupied and utilized by StadCo for its intended purpose, notwithstanding a minor amount of work, as determined by and at the reasonable discretion of StadCo and set forth on the Punch List, such as installation of minor

accessories or items, a minor amount of painting, minor replacement of Defective Work, or completion of minor exterior work that cannot be completed due to weather conditions; (b) StadCo is in receipt of all permits and certificates necessary for its occupancy and use of the Project, including but not necessarily limited to a temporary certificate of occupancy (or equivalent) for the Project issued by the appropriate Governmental Authorities having jurisdiction over the Project; (c) all systems included in the Work of the Project are operational pursuant to the Contract Documents and can be used as intended, all designated or required governmental inspections and certifications have been made and posted; (d) Design-Builder has instructed StadCo's personnel in the operation of the systems included in the Work and provided StadCo with all operation and maintenance manuals for equipment and systems installed in the Work; (e) AOR and Design-Builder shall have certified to StadCo, in writing, that, to the best of AOR and Design-Builder's information, knowledge, and belief, all of the Services and Work have been completed in accordance with the Contract Documents and all Applicable Laws, except for insubstantial work of a Punch List nature which is not yet completed but which can be completed thereafter without substantial or material interference with the occupancy or utilization of space in the Project by the occupants thereof and StadCo has, in writing, accepted the Work as Substantially Complete; (f) all consents and approvals from the NFL necessary to hold an NFL game in the Stadium shall have been received; and (g) all consents and approvals from the NCAA necessary to hold an NCAA football game in the Stadium shall have been received. For purposes of Substantial Completion, specified areas of the entire Work or Project may be individually judged as Substantially Complete. To the extent reasonably required by the Construction Lender or any Governmental Authorities, AOR will provide any certifications at Substantial Completion reasonably required of the AOR. AOR's aforementioned certification, if required by any Construction Lender, shall be in form and substance reasonably acceptable to the Construction Lender. AOR's aforementioned certifications to StadCo shall be in form and substance reasonably acceptable to StadCo. Notwithstanding anything herein to the contrary, the determination of Substantial Completion will not be denied if any permits, approvals, or certificates are withheld or delayed for reasons unrelated to Design-Builder's (or any Person that Design-Builder is legally or contractually responsible for) performance of the Work or its duties under the Contract Documents.

1.1.105 "Sub-subcontractor(s)" shall mean any Person, including materialmen, Suppliers and Vendors, who has a direct contract with a Subcontractor to perform any of the Work.

1.1.106 "Supplier(s)" or **"Materialman"** or **"Vendor(s)"** means a Person who has an agreement with Design-Builder or its Subcontractors to supply by sale or lease, directly or indirectly, any Materials or equipment for the Work.

1.1.107 "Team" shall mean the Oakland Raiders or any successor owner of the NFL franchise currently known as the Oakland Raiders, to be renamed as the Las Vegas Raiders.

1.1.108 "Third-Party Beneficiaries" shall have the meaning set forth in **Section 12.2.1**.

1.1.109 "Warranty Management Fund" shall mean funds held on account by or for StadCo with a portion of available Savings, as agreed to by the Parties, to be used to pay Costs of the Work incurred by Design-Builder in connection with performing the Design-Builder's Warranty Obligations.

1.1.110 "Work" shall mean the construction, design, and other activities required by the Contract Documents, and includes the furnishing of all Material, labor, detailing, layout, Equipment, supplies, plants, tools, scaffolding, transportation, temporary construction, superintendence, demolition, and all other services, facilities and items, reasonably necessary for the full and proper performance and completion of the requirements of the Contract Documents and items reasonably inferable from and consistent with the Contract Documents for the proper execution and completion of this Agreement, whether provided or to be provided by Design-Builder or a Subcontractor, AOR (when under contract with Design-Builder), or any other entity for whom Design-Builder is responsible, and whether or not performed or located on or off of the Site. The Work shall include the work and services designated in the Responsibility Matrix as being the responsibility of Design-Builder but excludes the work and services designated in the Responsibility Matrix as being the responsibility of others.

1.2 Other Terms.

1.2.1 Unless otherwise defined in this **Article 1** or further in this Agreement, terms in this Agreement that have well-known technical or construction industry meanings are used in the Agreement with such recognized meanings.

ARTICLE 2. RELATIONSHIP OF THE PARTIES

2.1 Stadium Authority.

2.1.1 Pursuant to the Lease Agreement and the Development Agreement, StadCo intends to lease the Site from the Stadium Authority and is responsible for the design, construction and development of the Project.

2.2 Cooperation with Project Development Team and StadCo.

2.2.1 Throughout the term of this Agreement and through expiration of the Warranty Period, Design-Builder shall coordinate the Work with StadCo, StadCo's Representative, StadCo's Design Team and the other members of the Project Development Team and public agencies having jurisdiction over the Project. StadCo may from time to time designate in writing other Persons or entities as being part of the Project Development Team.

2.2.2 Design-Builder agrees to meet with StadCo, AOR, and Lead Design Architect, as required during each of the design phases, to enable Design-Builder to perform such cost estimating and scheduling functions as required hereunder. Design-Builder and StadCo shall communicate and cooperate with each other and StadCo's Design Team during the design and construction of the Project.

2.2.3 The Parties shall work in good faith to amend this Agreement to incorporate changes required by the Development Agreement as the Parties mutually agree are necessary. The Parties' respective consent to amend this Agreement to incorporate changes required by the Development Agreement shall not be unreasonably withheld.

2.3 Architect of Record Services.

2.3.1 AOR shall be the **"**architect of record**"** for the Project and Lead Design Architect shall be credited as the **"**design architect**"** for the Project.

2.3.2 StadCo shall cause Lead Design Architect and AOR, pursuant to their respective contracts with StadCo, to provide all design and engineering Services necessary to produce the GMP Drawings and Specifications. After the Parties' execution of the GMP Amendment, the AOR Agreement shall be assigned to Design-Builder and AOR shall no longer be under contract with StadCo. Following assignment, AOR shall provide all design and engineering Services necessary to produce the Construction Drawings and Specifications and complete any other Services required pursuant to its applicable contract. The contract between Design-Builder and AOR shall be upon terms that are reasonably acceptable to Design-Builder and AOR and shall conform to the AOR Agreement and Assumption and Assignment Agreement, which is attached hereto as **Exhibit R**.

2.3.3 The Parties acknowledge that some of Lead Design Architect's Sub-consultants on the Project may, at the option of Design-Builder, be assigned to Design-Builder and/or AOR. As part of any assignment, StadCo, Lead Design Architect, and the applicable sub-consultant shall warrant and represent to Design-Builder or, as the case may be, AOR, that there are no outstanding defaults under the assigned agreements and that there are no outstanding amounts due or payable at the time of assignment. In lieu of accepting assignment of the sub-consultants' agreements, Design-Builder or AOR may elect to enter into separate contracts directly with such sub-consultants upon terms that are acceptable to Design-Builder or, as the case may be, AOR.

2.4 Project Teaming.

2.4.1 Design-Builder and StadCo shall participate in Project facilitations involving all members of the Project Development Team. The Project facilitation process shall be developed by Design-Builder, but shall be subject to the written approval of StadCo. Each participant shall bear its own cost and expense of attendance. Sessions will include AOR and major Subcontractors identified by the Parties. The costs of the facilitator and any rental for the facility where the Project teaming session will be held shall be a Cost of the Work.

2.5 Confidentiality.

2.5.1 Design-Builder agrees to hold in confidence all information designated **"confidential"**, **"proprietary"** or any similar designation that it obtains from StadCo, and or other members of the Project Development Team and their respective Affiliates and parent companies (whether obtained directly from the such parties or through any agent, employee or consultant of such parties) (collectively referred to as **"Confidential Information"**), and Design-Builder shall not use such Confidential Information other than for the performance of its Services under this Agreement, and shall cause any of its employees, consultants or Subcontractors to whom such Confidential Information is transmitted (including AOR) to be bound to the same obligation of confidentiality to which Design-Builder is bound. Design-Builder shall not communicate Confidential Information to any third-party without the prior written consent of StadCo, except to Subcontractors, AOR, and other consultants performing Work and otherwise as necessary to perform its contractual responsibilities, such as but not limited to, pre-proposal conferences and Project procurement documents prepared by the Design-Builder. Confidential Information does not include any information that:

2.5.1.1 was at the time of disclosure, or thereafter became, part of the public domain through no act or omission of the recipient;

2.5.1.2 became available to the recipient from a third-party who did not acquire such information under an obligation of confidentiality either directly or indirectly from the disclosing party; or

2.5.1.3 is, in the opinion of the recipient's legal counsel, required to be disclosed by Applicable Law; provided, however, the Team or StadCo shall be given prior written notification of recipient's intent to so disclose within ten (10) days prior to disclosure of any such proprietary information.

2.5.2 Upon Final Completion of the Work or earlier termination of this Agreement, at the request of StadCo, Design-Builder shall return all Confidential Information to StadCo, provided that Design-Builder may retain a record of such Confidential Information. In addition, StadCo acknowledges the difficulty involved in removing such Confidential Information from automatic backup systems for digital data and therefore agrees that Design-Builder may continue to retain Confidential Information in such backup systems so long as Design-Builder agrees to maintain the confidentiality of such Confidential Information as required herein.

2.5.3 Notwithstanding any provisions of the Contract Documents to the contrary, StadCo will use reasonable efforts to keep confidential estimates prepared by Design-Builder and other information designated as **"confidential"** or **"proprietary"** by Design-Builder; provided that StadCo may share such estimates and other confidential or proprietary Design-Builder information with (a) its lenders, advisors and consultants upon the written agreement of such parties to comply with the requirement of this Section, and (b) with the Stadium Authority to the extent necessary or appropriate pursuant to any agreements between StadCo and the Authority provided that the Stadium Authority agrees to keep such information confidential pursuant to the Act and the Development Agreement. StadCo shall take reasonable steps to protect the confidentiality of such Design-Builder information pursuant to the requirements of Applicable Law relating to public records requests. StadCo shall promptly notify Design-Builder if a public records request is related to any Design-Builder information in a timely manner so that Design-Builder can participate in any response to such public records request. StadCo shall act timely in involving Design-Builder so as to preserve all arguments and positions with respect to exemptions and exceptions to public records requests.

2.5.4 StadCo and Design-Builder understand and agree all information and documents submitted as part of any RRCO or Dispute pursuant to **Article 15** and **Article 16** shall be deemed strictly confidential and not published to the public or disclosed to any parties, other than Mediators (as defined below), the Arbitrator(s) (as defined below), and necessary participants. In the event either Party believes it is necessary to disclose such information outside of the dispute resolution process detailed in **Article 15** and **Article 16**, the Parties shall discuss the issue prior to disclosure and mutually agree upon the scope of such disclosure, if any. In the event the Parties are unable to agree upon the scope or necessity of any such disclosure, the Party seeking disclosure shall request relief from an arbitrator through JAMS and request declaratory relief concerning the appropriateness and necessity of any proposed disclosure. Both Parties agree to be bound by the scope of any disclosures deemed necessary by the arbitrator in any such proceeding, which proceeding itself shall be subject to the confidentiality provisions in this Agreement. In any such arbitration procedure for declaratory relief under this Section, each Party shall bear its own costs and fees.

2.6 Lender Required Information.

2.6.1 Design-Builder shall cooperate with Lender's construction consultant and shall furnish any and all Lenders providing funds for the construction or other financing of the Project with such documents, instruments, and certificates with respect to the Project as may reasonably be required by Lender in a form acceptable to Lender, but subject to the Design-Builder's reasonable review, provided that nothing in such document materially increases the Design-Builder's liability under the Contract Documents or the cost of the Design-Builder's performance hereunder, which may include, without limitation:

2.6.1.1 a consent and agreement pursuant to which Design-Builder agrees, among other things, it will discharge and remove mechanics' liens (pursuant to this Agreement), allow a Lender to cure any defaults by StadCo, obtain such Lender's consent to certain modifications, attorn to such Lender, and allow such Lender commercially reasonable rights to terminate pursuant to this Agreement;

2.6.1.2 a collateral assignment of this Agreement to such Lender;

2.6.1.3 Design-Builder's résumé and a current financial statement;

2.6.1.4 a breakdown of the cost of each class of work included in the construction of the Project certified by Design-Builder to be true and complete;

2.6.1.5 a disbursement schedule (in form and content reasonably acceptable to Lender) setting forth the dates on which Design-Builder expects to request payment and specifying the portion(s) of the Work, Materials, and other costs to be covered by such requests for payment, which disbursement schedule shall be subject to change as the Work progresses;

2.6.1.6 certificates that, to the best of Design-Builder's information, knowledge and belief, the Work has, to date, been designed and constructed in accordance with the Contract Documents and the Master Project Schedule and that the Work will be substantially completed on or before the Guaranteed Substantial Completion Date and finally completed on or before the date of Final Completion;

2.6.1.7 a certificate of Substantial Completion;

2.6.1.8 a temporary certificate of occupancy issued by the government authorities having jurisdiction over the Project;

2.6.1.9 to the extent the same are part of Design-Builder's Scope of Work, all reports and other information regarding environmental matters relating to the Site and Project, including but not limited to satisfactory evidence that all compliance tests, emissions tests, certifications and program

applications, reviews, findings or notices required by any Environmental Laws or Governmental Authority shall have been completed and there has been no material breach by Design-Builder under any such Environmental Laws, and, to the best of Design-Builder's information, knowledge and belief, there are no pending or threatened environmental claims relating thereto which could reasonably be expected to have a material adverse effect on the construction, use, or operation of the Project, or, if any such claims exist, a description of such claims;

2.6.1.10 to the extent the same are part of Design-Builder's Scope of Work, satisfactory evidence that all easements, rights-of-way, and licenses necessary for the use and operation of the Project have been obtained and are in full force and effect and there has been no known material breach under any such easement, right-of-way or license, and there are no known pending or threatened claims or proceedings relating thereto which could reasonably be expected to have a material adverse effect on the use and operation of the Project;

2.6.1.11 certificates of insurance evidencing all required insurance coverages of the Design-Builder and its Subcontractors outlined herein;

2.6.1.12 to the extent of payments made to Design-Builder, lien waivers as permitted by Applicable Law from all Subcontractors and any Vendor performing Work on the Project that has filed a prelien notice or notice of furnishing;

2.6.1.13 a certificate of Final Completion;

2.6.1.14 if applicable, final certificates issued by the government authorities having jurisdiction over the Project; and

2.6.1.15 any other information or certificates reasonably requested by any Lender to evidence compliance by Design-Builder with all the material provisions of the Development Agreement and this Agreement.

2.6.2 Design-Builder shall agree to reasonable modifications of the Contract Documents including, without limitation, **Article 7** hereof (with respect to the payments to Design-Builder) as may reasonably be required by any Lender. If Design-Builder concludes that Lender's modifications materially increase the Design-Builder's liability under the Contract Documents or the cost of the Design-Builder's performance hereunder, then Design-Builder shall submit any and all requests for modifications (including, as appropriate, adjustments to the GMP and the Contract Time) to StadCo pursuant to the Change Order process contained in **Article 14**.

2.7 Cooperation with Governmental Authorities.

2.7.1 Design-Builder agrees to work with, and cooperate with, any and all Governmental Authorities in the conduct of the Work and agrees to accommodate all legal requirements of these authorities as they relate to the Work.

2.8 Limitation of Authority.

2.8.1 Design-Builder shall not have any authority to bind StadCo for the payment of any costs or expenses without the express prior written approval of StadCo. Design-Builder shall have authority to act on behalf of StadCo only to the extent provided herein. In the event of an emergency affecting the safety of Persons, the Project or adjacent property, Design-Builder, without special instruction or authorization, shall act reasonably to prevent or minimize any threatened damage, injury or loss. Design-Builder's authority to act on behalf of StadCo shall be modified only by an amendment in accordance with the terms hereof.

2.9 **Representations and General Obligations**. Design-Builder warrants and represents to StadCo as follows:

2.9.1 Design-Builder is financially solvent, able to pay its debts as they mature, and possessed of sufficient working capital to complete the Work;

2.9.2 Design-Builder is able to furnish the tools, Materials, supplies, Equipment, and labor necessary to complete the Work;

2.9.3 Design-Builder has substantial experience in constructing projects similar to the Project, is experienced in the construction of new NFL stadiums in major metropolitan areas in the United States and related support facilities and is familiar with and knowledgeable regarding the components that are properly and customarily included within such a project, including the requirements of Building Standards and trade practices and construction standards and practices as to the types and quantities of components, items, systems, Materials and methods of construction to be included in the Project in order to produce a first-class, large scale, one-of-a-kind, premier, and state of the art NFL stadium;

2.9.4 Design-Builder is authorized to do business in the County, and is licensed with the Nevada Contractor's Board and holds, or will obtain, a license, permit, or other special license to perform the Work, as and if required by Applicable Laws;

2.9.5 Design-Builder is a joint venture between M. A. Mortenson Company, a Minnesota Corporation, and McCarthy Building Companies, Inc., a Missouri Corporation, which entities, by individually executing this Agreement, agree on behalf of themselves and their respective insurers, guarantors and sureties to be jointly and severally responsible and liable to StadCo for all of Design-Builders' duties and obligations under the Contract Documents and for all claims, damages, costs, expenses, and all other liability arising out of or relating to the performance or failure to perform any of Design-Builder's duties or obligations under the Contract Documents or otherwise arising out of the Project. StadCo has been provided a copy of Design-Builder's joint venture agreement;

2.9.6 Design-Builder acknowledges anti-corruption Laws apply to this Agreement (**"Anti-Corruption Laws"**) and it, and its directors, officers, employees, and where applicable, any Subcontractors (collectively **"Principals"**), are knowledgeable regarding the Anti-Corruption Laws, and it and its Principals will take appropriate steps to ensure compliance therewith and will not cause or request any actions which would cause StadCo to be in violation thereof. Design-Builder further represents, warrants, and agrees it, and its Principals, have not and shall not engage in any conduct that contravenes any applicable Anti-Corruption Laws and further that it, and its Principals, have not and shall not make any expenditure for any unlawful purpose in the performance of this Agreement. Design-Builder and its Principals shall not make any offer, payment, or promise to pay, or authorize any offer, payment, or promise to pay anything of value to any official, officer, employee, or representative of (a) any government; (b) any wholly or partly government owned or controlled company; (c) any public international organization (e.g., the World Bank); (d) any political party or political candidate; or (e) any spouses or family relatives of the above (collectively, **"Government Officials"**), for the purposes of obtaining or retaining business or any improper advantage in connection with this Agreement;

2.9.7 Design-Builder represents and warrants none of its Principals is a Government Official, or that it has disclosed such relationship fully in writing to StadCo. Design-Builder agrees to notify StadCo of any change in this representation;

2.9.8 Design-Builder represents it and its Principals have never been convicted of, or pleaded guilty to, an offense involving fraud, corruption or other dishonest conduct, and it is not debarred, suspended, proposed for suspension or debarment, or otherwise ineligible for procurement by any government. Design-Builder agrees to notify StadCo of any change in this representation;

2.9.9 Subject to Design-Builder's rights under the Agreement, Design-Builder covenants with StadCo to achieve and protect StadCo's interests in the Project by furnishing Design-Builder's skill and judgment to StadCo and the Project Development Team. Design-Builder shall furnish efficient business administration and supervision and shall furnish at all times an appropriate and adequate supply of workers and Materials to complete the Project in an expeditious and economical manner consistent with the Contract Documents. Design-Builder shall perform its design services and other professional services under this Agreement in accordance with the professional Standard of Care and skill for design-build firms experienced and specializing in the design and other professional services of new NFL stadiums in major metropolitan areas in the United States;

2.9.10 Design-Builder shall assign sufficient numbers of duly qualified professional and technical personnel to the Project to the extent necessary to ensure that its obligations under this Agreement are timely carried out with respect to the performance of the Work. Such personnel shall include the personnel described in **Exhibit E** hereof. The personnel identified in **Exhibit E** will not be removed or replaced by Design-Builder without StadCo's prior written consent unless said personnel becomes incapacitated or ceases to be employed by Design-Builder. If StadCo's consent is required, then such consent shall not be unreasonably withheld, conditioned or delayed;

2.9.11 Upon assignment to Design-Builder or AOR and execution of an appropriate agreement as described in **Section 2.3.2**, Lead Design Architect's Sub-consultants, or firms later added by amendment to this Agreement, shall be part of Design-Builder's design/engineering team and shall not be changed without the prior written approval of StadCo. Design-Builder acknowledges that certain of Lead Design Architect's Sub-consultants have previously provided design/engineering services to the Project and are pre-qualified by StadCo to provide engineering/construction services. By pre-approving such consultants, StadCo does not acquire any responsibility for the consultant or its qualifications. Design-Builder has investigated, for its own benefit, the reputation and qualifications of such firms and has satisfied itself of their ability to satisfactorily perform the work or services assigned. Design-Builder, however, is not obligated to utilize the Lead Design Architect's subconsultants;

2.9.12 Design-Builder shall comply with (and shall cause all Subcontractors to comply with) the employment and wage law requirements, to the degree set forth in Sections 338.013 to 338.090 of the Nevada Revised Statutes, as modified by the Act, and Chapter 608 of the Nevada Revised Statutes, as amended (the **"NRS"**). StadCo shall work cooperatively with Design-Builder and assist Design-Builder as necessary in connection with Design-Builder's compliance with these regulatory requirements (including assisting Design-Builder with obtaining information or performing obligations required to be performed by public authorities under such provisions). Design-Builder shall be responsible for penalties as provided in Section 338.060 of the NRS (if applicable and assessed in connection with Design-Builder's performance of the Work), and the provisions of Section 338.060 are specifically incorporated herein to the extent necessary to effectuate the foregoing. All other contractual provisions and stipulations that are required to be included in a contract for public work pursuant to the provisions of Section 338.013 to 338.090 of the NRS are deemed incorporated herein to the extent required by Applicable Law;

2.9.13 In the hiring of employees for the performance of Work, Design-Builder, its Subcontractors, and any Person acting on behalf of Design-Builder or a Subcontractor, shall not, by reason of race, religion, national origin, age, sex, disability, war veteran status, or color, discriminate against any citizen in the employment of labor or workers who are qualified and available to perform the Work to which the employment relates. Design-Builder, its Subcontractors, and any Person acting on behalf of Design-Builder or any Subcontractor shall not, in any manner, discriminate against or intimidate any employee hired for the performance of Work on account of race, religion, national origin, age, sex, disability, veteran status or color;

2.9.14 Design-Builder shall specifically require its Subcontractors and all Suppliers to comply with the terms of **Section 2.9.12** and **Section 2.9.13**;

2.9.15 Except as otherwise specifically provided in this Agreement, Design-Builder shall not enter into any agreement with a design consultant, Subcontractor, or Vendor with which Design-Builder

is affiliated without StadCo's prior written approval and express acknowledgment of the affiliated relationship. This includes any entity related to or affiliated with or having common ownership or management with Design-Builder or with respect to which Design-Builder has direct or indirect ownership or control, including, without limitation, any entity owned in whole or part by Design-Builder or any of its officers, directors, or members (or any of their respective family members), or any holder of issued and outstanding shares of, or the holder of any interest in, Design-Builder. Any Materials, Equipment, or services provided by any such entity without the advance written approval of StadCo shall be a Non-Allowable Cost;

2.9.16 By execution of this Agreement, Design-Builder represents Design-Builder has visited and investigated the Site, including but not limited to reasonable investigation of adjacent properties directly impacted by Design-Builder's Work, and become familiar with reasonably ascertainable local conditions under which the Work is to be performed. Design-Builder also acknowledges it has reasonably satisfied itself as to the character, quality, and quantity of surface and subsurface materials or obstacles to be encountered in so far as this information is reasonably ascertainable from geotechnical soils reports and other environmental reports provided by StadCo or AOR. Subject to **Section 14.3.3**, any failure of Design-Builder to take the actions described and acknowledged in this Section will not relieve Design-Builder from responsibility for estimating the difficulty and cost of successfully performing its Work or for proceeding to successfully perform its Work without additional expense to StadCo. StadCo shall provide to Design-Builder all information in StadCo's possession or control relating to the Site, including any geotechnical soils report and environmental reports.

ARTICLE 3. PRELIMINARY DESIGN PHASE & GMP DEVELOPMENT

3.1 Programming and Construction Plan.

3.1.1 Design-Builder shall be responsible for all planning activities and other preconstruction services that Design-Builder has provided pursuant to the Letter Agreement, and all such services shall be subject to the terms and conditions of this Agreement.

3.1.2 On or before the date set forth in the Master Project Schedule, Design-Builder shall develop and submit to StadCo its Construction Plan that will include: (a) the construction staging plan setting forth construction scheduling, lay down areas and storage, trailer areas, trailer locations, priorities as to Site use, ingress/egress and other similar Site logistic matters for the Project and (b) procedures for the assignment of responsibilities for safety precautions and programs (collectively, the **"Construction Plan"**).

3.2 Project Schedules.

3.2.1 The Master Project Schedule is attached hereto as **Exhibit K**. Concurrent with the delivery of its GMP proposal, Design-Builder shall update, revise and otherwise modify and deliver a Master Project Schedule substantially in accordance with the Master Project Schedule attached as **Exhibit K** for AOR's review and StadCo's review and approval.

3.2.2 Design-Builder shall investigate and recommend a schedule for the purchase of Materials and Equipment requiring long lead time procurement, and shall coordinate the procurement schedule with the preparation of the Master Project Schedule. The Master Project Schedule shall be updated throughout the duration of the Project to accurately reflect progress to date, remaining durations, and any new or revised logic or activities.

3.2.2.1 The Master Project Schedule has sufficient detail to: (a) show that the Work is efficiently planned; (b) enable the Work to be accurately monitored; and (c) show predecessor and successor activities with accompanying lags and start projections. StadCo's review and approval of the Master Project Schedule shall not be deemed to modify or extend the Guaranteed Substantial Completion Date. Design-Builder shall not change the Guaranteed Substantial Completion Date other than pursuant to a Change Order signed by StadCo.

3.3 BIM and Design Phase Completion.

3.3.1 StadCo, Lead Design Architect, Design-Builder, and AOR have agreed to use building information modeling (**"BIM"**) to assist in the design and construction of the Project. The BIM protocols to be followed are set forth in the Building Information Modeling Implementation Plan attached hereto as **Exhibit M** (the **"BIM Implementation Plan"**). StadCo shall incorporate the BIM Implementation Plan into its agreements with Lead Design Architect, the AOR and any other consultants providing design, engineering or similar professional services and who will be participating in the development of any part of the BIM model or who may be using the BIM Model in connection with Services they are providing as part of the Project. Design-Builder shall incorporate the BIM Implementation Plan into its agreements with AOR and any other consultants providing design, engineering or similar professional services and who will be participating in the development of any part of the BIM model or who may be using the BIM Model in connection with Services they are providing as part of the Project.

3.3.2 The BIM Implementation Plan makes reference to **"Levels of Development"** or **"LODs."** The LODs do not supplant the documentation requirements and descriptions contained in this Agreement for the various design phases, but rather the LODs define when a design stage is considered complete based on the level of development of the of the various model elements.

3.4 Development of Interim GMP Drawings and Specifications Sets.

3.4.1 Design-Builder has received and reviewed the Conceptual Design Documents, the twenty-five percent (25%) GMP Drawings and Specifications, the sixty-two and a half percent (62.5%) GMP Drawings and Specifications, and the one-hundred percent (100%) GMP Drawings and Specifications as of the execution date of this Agreement.

3.4.2 As of the execution date of this Agreement, StadCo has caused Lead Design Architect and AOR to prepare and deliver to Design-Builder the 100% GMP Drawings and Specifications (together with the twenty-five percent (25%) GMP Drawings and Specifications and the sixty-two and a half percent (62.5%) GMP Drawings and Specifications). The GMP Drawings and Specifications are based on the Conceptual Design Documents. Design-Builder has reviewed the GMP Drawings and Specifications as they were completed by Lead Design Architect and AOR. Design-Builder has provided recommendations on relative feasibility of construction methods, availability of Materials and labor, time requirements for procurement, installation and construction, and factors related to cost including, but not limited to, costs of alternative designs or Materials and possible economies.

3.4.3 During the preparation of the GMP Drawings and Specifications, StadCo, Lead Design Architect, AOR, and Design-Builder have met and Lead Design Architect and AOR have, at such meetings, notified StadCo and Design-Builder of any material modifications in quantities or qualities from the documents previously issued by Lead Design Architect and AOR. If there were any such material modifications, then Design-Builder has update its Construction Cost estimate. Lead Design Architect, AOR, Design-Builder, and StadCo have actively coordinate their efforts and cooperate with each other during this phase.

3.4.4 Design-Builder has analyzed the types and quantities of labor required for the Project and has reviewed the availability of appropriate categories of labor required for critical phases and has made recommendations for and executed actions designed to minimize adverse effects of labor shortages.

3.5 Cost Estimates and Construction Cost Budget.

3.5.1 Design-Builder has delivered to StadCo a detailed estimate of the Construction Cost based on the one hundred percent (100%) GMP Drawings and Specifications. At milestones in the development of the design as designated in the Master Project Schedule, Design-Builder shall update the Construction Cost estimate as described in this Agreement using recognized and accepted cost estimating

techniques in the construction industry. Design-Builder, StadCo, Lead Design Architect and AOR will meet to review the updates and to compare them against the Construction Cost Budget. In the event Design-Builder's update exceeds the Construction Cost Budget, Design-Builder, StadCo, Lead Design Architect and AOR will discuss what cost reduction suggestions and revisions, if any, have to be made to the documents so that Design-Builder and StadCo can establish a mutually acceptable GMP.

3.5.2 After delivery of the GMP Drawings and Specifications, Design-Builder shall update its Construction Cost estimate based the GMP Drawings and Specifications. The updated estimate shall be delivered to StadCo no later than the dates set forth in the Master Project Schedule, and the Project Development Team shall meet promptly after issuance of the updated Construction Cost estimate to review, comment and approve the GMP Drawings and Specifications and accompanying Construction Cost estimate.

3.5.3 The Project Development Team shall work in good faith to achieve a GMP that complies with the Construction Cost Budget. To that end and to the extent necessary, Design-Builder, AOR, and the Lead Design Architect shall explore cost reduction alternatives to cause the Construction Cost estimates to be within the Construction Cost Budget. However, StadCo acknowledges that the Construction Cost Budget may increase based on various factors during the development of the design.

3.6 GMP Development.

3.6.1 On or before the date set forth in the Master Project Schedule, StadCo shall cause AOR to prepare and deliver to Design-Builder the GMP Drawings and Specifications and the Prose Statement. On or before the date set forth in the Master Project Schedule, the Design-Builder shall submit to StadCo and AOR the Design-Builder's proposed GMP and the GMP Qualifications and Assumptions (including proposed alternates, if applicable), based on the GMP Drawings and Specifications and the Prose Statement. On or before the date set forth in the Master Project Schedule, Design-Builder, StadCo and AOR shall meet to reconcile any questions, discrepancies or disagreements relating to the GMP proposal, the GMP Qualifications and Assumptions, and the Prose Statement. The reconciliation shall be documented by agreed upon revisions to the GMP Qualifications and Assumptions, which shall be approved in writing by StadCo, AOR, and Design-Builder. On or before the date set forth in the Master Project Schedule, Design-Builder shall submit to StadCo Design-Builder's proposed final GMP, based upon the agreed upon GMP Qualifications and Assumptions and the Prose Statement, and contingent on StadCo's approval of the final GMP, the Parties will enter into the GMP Amendment. If StadCo disapproves of the proposed GMP, then StadCo may terminate this Agreement without cause pursuant to **Article 10** hereof.

3.6.1.1 The GMP may be either a Cost of the Work plus Fee with a **"not-to-exceed"** maximum price or a fixed, lump sum price. At the time Design-Builder presents its GMP proposal to StadCo, the Design-Builder shall propose both pricing alternatives for StadCo's consideration. Each pricing proposal shall (a) be developed and calculated in the same "open book" manner and StadCo will be entitled to review all backup documentation used to establish each pricing proposal, (b) be based upon, and subject to, substantially the same GMP Qualifications and Assumptions, Construction Drawings and Specifications, Prose Statement, Allowances (as defined in **Section 7.2.1**) and alternates, and (c) will include an adequate Design-Build Contingency generally consistent in amount with **Section 7.1.2** hereof, except that in the fixed, lump sum pricing option such Design-Build Contingency would be for the benefit of the Design-Builder. The GMP Amendment executed by the Parties shall set forth the selected pricing option, and if the fixed, lump sum price option is selected by StadCo, then the GMP Amendment shall include an appropriate monthly payment schedule for the fixed/lump sum price, along with such other contract modifications to this Agreement as are consistent with a fixed, lump sum price as opposed to a Cost of the Work plus fee, not-to-exceed price.

3.6.2 Following the establishment of the GMP, and during the development of the Construction Drawings and Specifications, if any member of the Project Development Team becomes aware of any facts that would cause the GMP to exceed the Construction Cost Budget, then they shall give prompt written notice to all other Project Development Team members.

3.6.3 The Construction Drawings and Specifications prepared by AOR will include additional or more fully developed plans, sections or details not included in the GMP Documents. Design-Builder will make no claim against StadCo for an increase in the GMP or extension of the Contract Time based upon such additional or more fully developed plans, sections, or details subject to general consistency with the Design-Builder's GMP Qualifications and Assumptions or information reasonably inferable from the GMP Documents, and subject to StadCo not requesting additions or inconsistent changes that increase cost or time required for the Work.

3.6.4 The GMP, once established by the Parties' execution of the GMP Amendment, shall be revised only upon the issuance of a properly authorized Change Order. The GMP shall be based upon completion of the Work pursuant to the Guaranteed Substantial Completion Date and the date of Final Completion set forth in the GMP Amendment. The GMP shall include a separately detailed breakout of the Cost of the Work for Design-Builder's General Conditions Work and for Design-Builder's Self-Performed Work.

3.7 Fast Track Procurement.

3.7.1 The Parties acknowledge and agree that this Project is on a fast-track and procurement must occur rapidly in order to achieve Substantial Completion on or before the Guaranteed Substantial Completion Date. StadCo shall cooperate with Design-Builder as necessary to promptly review and approve interim design and procurement packages so that Design-Builder can maintain the fast-track schedule.

3.7.2 At Design-Builder's election, Design-Builder may request StadCo approve interim or preliminary GMPs based on interim GMP Drawings and Specifications in order to maintain the procurement schedule for early release Work authorized pursuant to **Section 4.4**.

ARTICLE 4. FINAL DESIGN AND CONSTRUCTION PHASE

4.1 Construction Drawings and Specifications.

4.1.1 Upon execution of the GMP Amendment, Design-Builder shall cause AOR to produce and deliver Construction Drawings and Specifications to StadCo for review, comment, and approval by StadCo. Design-Builder, pursuant to the Master Project Schedule, shall present StadCo with all proposed Construction Documents. StadCo shall be given a commercially reasonable period of time pursuant to the Master Project Schedule to review and approve such documents. Design-Builder shall incorporate all reasonably requested revisions of StadCo and shall submit the revised documents to StadCo for review and approval, which review and approval shall be for the purpose of confirming the requested revisions were incorporated. Upon StadCo's approval of the revised documents, those documents shall be Construction Documents.

4.1.2 The Construction Drawings and Specifications shall comply with Applicable Laws and League Rules. To the extent there are changes to Applicable Laws or League Rules enacted after the date of acceptance of the GMP Amendment that cause an increase in the Cost of the Work or impact the Master Project Schedule, Design-Builder shall be entitled to a Change Order for costs incurred and/or impact on the Master Project Schedule to comply with such changes in Applicable Laws or League Rules pursuant to the provisions of **Article 14**.

4.1.3 StadCo shall review the Construction Drawings and Specifications for conformance with the design concept expressed in the GMP Documents. Regardless of whether StadCo reviews drawings, specifications or other documents prepared by Design-Builder, Design-Builder shall make no material change in nor omit any of the Work shown or reasonably implied in the GMP Documents, unless StadCo shall approve in writing such change or omission.

4.1.4 Failure to review the Construction Drawings and Specifications by StadCo shall not relieve Design-Builder of its obligation to prepare the Construction Drawings and Specifications properly and completely in accordance with the terms of the Contract Documents. Should StadCo discover any error or omission in the Construction Drawings and Specifications when compared to the GMP Documents, such error or omission shall be brought promptly to Design-Builder's attention. In such event, Design-Builder shall complete, correct, and/or modify the Construction Drawings and Specifications in question and shall resubmit such Construction Drawings and Specifications to StadCo.

4.1.5 Design-Builder's design and construction shall fully take into account the results of any and all tests and investigations so that the Project will be structurally stable, suitable for StadCo's intended purposes, and in compliance with all Applicable Laws the Contract Documents.

4.1.6 Conflicts or discrepancies among the Contract Documents shall be resolved in the following order of priority so that the precedence of the documents shall be that the first listed document below shall have precedence over the later listed document to the extent necessary to resolve such conflict or discrepancy: (a) executed Change Orders and duly executed amendments (including the GMP Amendment) to the Contract Documents (with later date having greater priority); (b) the Construction Drawings and Specifications with detailed drawings taking precedence over large scale drawings; and (c) the Agreement.

4.1.7 Design-Builder hereby acknowledges and agrees that Design-Builder has a duty to refer all questions or concerns regarding the intent or appropriate interpretation of the Contract Documents to StadCo for StadCo's decision. Subject to **Section 4.1.6**, if there is any inconsistency within the Construction Drawings and Specifications, then Design-Builder shall provide the better quality or greater quantity of Work or Materials, as applicable, unless StadCo directs otherwise in writing.

4.1.8 Design-Builder shall, within three (3) days after Design-Builder becomes aware of any errors, discrepancies, omissions, duplications, conflicts, or inconsistencies in the Contract Documents (as amended from time to time), notify StadCo of same in writing.

4.1.9 If a portion of the Work is covered contrary to the requirements of the Contract Documents, then Design-Builder shall, if requested by StadCo, uncover such portion of the Work for observation and, thereafter, recover such portion of the Work, without any right to any increase in the GMP or Contract Time. If StadCo engages a consultant for quality assurance or quality control purposes and such consultant timely notifies Design-Builder of the portions of the Work that will be inspected or tested, Design-Builder shall not cover any identified portions of the Work without providing an opportunity for such consultant to review the Work.

4.1.10 Requests for substitution of products or processes different than those specified in the Contract Documents, shall be timely, fully documented in writing, and will be accompanied by information about the proposed substitution including: (a) quality and serviceability of the specified item; (b) changes in details and construction of related work; (c) design and artistic effect; and (d) any impact of the proposed substitution on the Master Project Schedule, or costs, or costs of maintenance, or impact on useful life. Each request for substitution shall be accompanied by a complete description and performance data concerning the specified item and the proposed substitution plus any Samples required by StadCo. Design-Builder's submission of a request for substitution shall be deemed its representation that the substitution meets or exceeds the standards and qualities of the specified item being substituted (including, without limitation, scope and length of warranties or guarantee periods). Adjustments if any, to the GMP shall be described in an accompanying request for Change Order pursuant to **Article 14**.

4.2 Subcontract Procurement.

4.2.1 Design-Builder and StadCo have jointly developed a community benefits plan to encourage meaningful participation by segments of the local community in the economic opportunities available in connection with the design and construction of the Project, which plan includes a participation goal that at least fifteen percent (15%) of the value of the subcontracted construction work be awarded to

small local businesses (as defined in Section 31.5(2) of the Act). Design-Builder shall comply with the provisions of Section 31 and Section 31.5 of the Act unless such compliance is waived by the Stadium Authority. Design-Builder shall retain all records demonstrating compliance with Section 31 and Section 31.5 of the Act for not less than six (6) years after the Guaranteed Substantial Completion Date. StadCo agrees to work cooperatively with Design-Builder to seek a limited waiver of such requirements, where appropriate, if requested by Design-Builder. The community benefits plan is attached hereto as **Exhibit Q**. Design-Builder shall implement the community benefits plan and shall actively develop Subcontractors' interest in the Project.

4.2.2 Design-Builder shall establish subcontracting schedules and furnish to StadCo in writing a list of prospective Subcontractors for each scope of work package. All Subcontractors shall be reputable, qualified firms with an established record of successful performance in their respective trades. Prior to Design-Builder soliciting interest from potential Subcontractors, StadCo shall promptly reply to Design-Builder, stating whether StadCo rejects any proposed Subcontractor on the list. Design-Builder shall not request proposals from, or contract with, any proposed Subcontractor that StadCo has for reasonable cause rejected.

4.2.2.1 Design-Builder will award Subcontracts for construction using a competitive best value selection process developed by Design-Builder, approved by StadCo and consistent with the requirements of Section 31(2) of the Act. StadCo agrees to work cooperatively with Design-Builder to seek a limited waiver of such requirements, if requested by Design-Builder. AOR and Design-Builder's other consultants are excluded from the requirements of this Section.

4.2.2.2 Subcontracts shall be priced on a lump sum or guaranteed maximum price basis, however certain design assist Subcontractors may be selected based on their qualifications and their commitment to provide a lump sum or guaranteed maximum price consistent with the budget or target price established for their scope of work in the then current estimate of the Construction Cost Budget. Any firms selected under the "target price/design assist" methodology may be terminated for convenience if their proposed lump sum or guaranteed maximum price exceeds the target price, in which event the Subcontract for that construction work will be procured and awarded using the competitive best value selection process referenced in **Section 4.2.2.1**.

4.2.3 Design-Builder hereby acknowledges the Project shall be an "open book" project and, therefore, all bids or proposals (including Design-Builder pricing for any proposed Self-Performed Work) shall be reviewed in an "open book" fashion together with StadCo. Design-Builder shall receive bids or proposals, prepare bid and proposal analyses and consult with StadCo and the Design Team regarding the award of Subcontracts or rejection of bids or proposals. Bid analysis and proposal analysis shall include a budget comparison with budget assumptions for those aspects of the Work not included due to bidder qualifications and appropriate budget contingencies. StadCo shall be entitled to full access to all Subcontractor bids, proposals, and underlying documentation establishing the GMP. After analyzing the bids and proposals, Design-Builder shall submit copies of the bids and proposals to StadCo with recommendations as to whom Design-Builder intends to award each of the bid and proposal packages based upon Design-Builder's reasonable determination of the bid and proposal that represents the best value to the Project, which recommendations are subject to StadCo's approval, not to be unreasonably withheld or delayed. StadCo shall approve, deny, or request further information regarding the bid or proposal within seven (7) days of receiving the bid or proposal. Design-Builder shall not select any consultant, Subcontractor, or Vendor to perform any part of the Work without StadCo's prior written approval. StadCo may condition such approval upon receiving more complete information regarding a potential consultant, Subcontractor's or Vendor's proposal. Design-Builder shall also comply with the process and procedures included in its Procurement Plan attached hereto as **Exhibit B**.

4.2.4 Prior to the establishment of the GMP, Design-Builder shall not, without the prior written approval of StadCo, which shall not be unreasonably withheld, (i) enter into any contract with a consultant, Subcontractor, or Vendor with respect to the Project, or (ii) amend any Subcontract previously approved by StadCo.

4.2.5 Each Subcontract shall: (a) require the consultant, Subcontractor, or Vendor (as applicable) to be bound to Design-Builder by the terms of the Contract Documents (including, without limitation, this Agreement), and to assume toward Design-Builder all the obligations and responsibilities which Design-Builder, by the Contract Documents (including, without limitation, this Agreement), assumes toward StadCo; and (b) specify the Subcontractor's maximum allowable mark-up for overhead and profit in the event of a Change Order in accordance with **Section 4.2.6**.

4.2.6 Subcontractor and Design-Builder Self-Performed Work Mark-Up. The mark-up for overhead and profit to a consultant, Subcontractor or Vendor on fixed price, lump sum, or **"cost plus"** Subcontracts will be as negotiated with each Subcontractor as part of the bidding process to ensure the best available price for Work subject to Subcontracts. The allowable mark-up for overhead and profit for Work shall be as follows:

4.2.6.1 For Subcontractor Work performed under Change Order, the Subcontract shall specify the maximum allowable mark-up to the Subcontractor for overhead and profit, which maximum mark-up must be mutually agreeable to both Design-Builder and StadCo, but in no event greater than ten percent (10%) for work performed by first-tiered Subcontractors and five percent (5%) for Sub-subcontractors, and in no event greater than fifteen percent (15%) total mark-up for Subcontractors and Vendors of all tiers, including Subcontractor, unless otherwise approved in writing by StadCo.

4.2.6.2 For Self-Performed Work by Design-Builder performed under a Change Order, the Change Order shall specify the maximum allowable mark-up to the Design-Builder for overhead and profit, which maximum mark-up shall be twelve percent (12%) for Self-Performed Work and in no event greater than fifteen percent (15%) total mark-up for Subcontractors and Vendors of all tiers, unless otherwise approved in writing by StadCo.

4.3 Self-Performed Work.

4.3.1 Design-Builder or its Affiliates may only submit a proposal for Self-Performed Work upon providing evidence reasonably acceptable to StadCo that its price for such Self-Performed Work is competitive for similar work in Las Vegas, Nevada.

4.3.1.1 Design-Builder shall not be permitted to use Design-Build Contingency for Self-Performed Work without the express written approval of StadCo, but such approval shall not be unreasonably withheld if the proposed use is on the same terms and conditions on which the Design-Build Contingency may be used for Subcontractor Work generally.

4.3.1.2 Unless expressly noted in the bid or proposal approved by StadCo, neither Design-Builder nor its Affiliates shall use any of the General Conditions Work to support the Self-Performed Work or use the General Conditions Work for Self-Performed Work on any terms or conditions different from the terms or conditions on which such General Conditions Work are made available to all other Subcontractors.

4.4 Early Release Work.

4.4.1 With StadCo's prior written approval and pursuant to terms and procedures approved by StadCo and Design-Builder, Design-Builder may commence construction of specified portions of the Work prior to execution of the GMP Amendment. For each early release work package, the following shall apply: (a) AOR shall have prepared sufficiently detailed drawings and specifications for such Work so as to allow Design-Builder to apply for and obtain permits and other approvals necessary to commence such Work; (b) Subcontractors for such Work shall be competitively procured in accordance with **Section 4.2**; (c) Design-Builder shall have submitted, for StadCo's review and written approval, a fixed lump sum price or GMP for such Work; and (d) such Work shall be performed pursuant to all other terms and conditions of this Agreement.

4.5 Assignment of Subcontracts.

4.5.1 Design-Builder hereby conditionally grants, transfers and assigns to StadCo all the rights, title and interest of Design-Builder in, to and under any and all Subcontracts, which are now or hereafter entered into by Design-Builder in connection with the performance of the Work. The foregoing assignment shall be exercisable by StadCo, at its election, in the event that StadCo has exercised its right to terminate this Agreement in whole or in part or to take control of, or cause control to be taken of, the Work, or any portion thereof, provided that StadCo pays Design-Builder for all undisputed amounts due under this Agreement for Work performed in accordance with the Contract Documents.

4.6 Project Labor Agreement.

4.6.1 Design-Builder may enter into a Project Labor Agreement to govern labor relations for the Project and for purposes of establishing binding rules and methods for the efficient employment of workers and assignment of work, and the prompt settlement of all misunderstandings, disputes, grievances and jurisdictional problems that might arise during construction of the Project in order to ensure uninterrupted operations and maintenance of harmonious and peaceful labor relations for all Parties to this Agreement. Design-Builder shall follow and enforce the terms and conditions of such Project Labor Agreement (as the same may be modified and amended from time to time), if applicable, for the benefit of the Project.

4.7 Meetings; Reports; Schedule Updates.

4.7.1 Design-Builder shall schedule and conduct preconstruction, construction, and progress meetings to discuss such matters as procedures, progress, problems and scheduling. Design-Builder shall hold progress and coordination meetings with StadCo throughout the construction period, including weekly Project updates to StadCo. Design-Builder shall have, at a minimum, monthly meetings with selected Subcontractors to review the following with each Subcontractor (as applicable): (a) actual construction progress as compared against Subcontractor's schedule; (b) status of major components of Subcontractor's Work; (c) progress made on critical activities of Subcontractor's Work; (d) explanation for any lack of work on any critical path items; (e) permit processing; and (f) quality control, testing and inspection issues. Design-Builder shall prepare and distribute minutes of all meetings to StadCo and to all other Persons in attendance. StadCo will be notified in writing sufficiently in advance and may, at its option, attend any meetings.

4.7.2 Design-Builder shall update and distribute, on a monthly basis, the Master Project Schedule incorporating the activities of Subcontractors on the Project, including processing of Shop Drawings and similar required Submittals and delivery of products requiring long lead time procurement and showing current conditions and revisions required by actual experience. Design-Builder shall include the Project occupancy requirements showing portions of the Project having occupancy priority, as directed by StadCo.

4.7.3 Design-Builder shall maintain the progress of all Work in accordance with the currently approved Master Project Schedule. If at any time the Work is not proceeding in accordance with the critical path required by the Master Project Schedule, Design-Builder shall take such measures and/or adopt such methods as may be necessary to maintain adherence to the Master Project Schedule, without any increase to the GMP unless otherwise allowed pursuant to this Agreement.

4.7.4 Design-Builder shall submit to StadCo a form of the monthly Project Report for use on the Project for StadCo's review, comment and acceptance. Upon acceptance by StadCo, the form of monthly Project Report shall establish the standard for detail required for the remainder of the Project. At a minimum, the monthly Project Report will contain the following: (a) listing of actual costs for completed activities and estimates for uncompleted tasks; (b) progress photos; (c) an executive summary; (d) a discussion of pending items and existing or anticipated problems, status of RFIs; (e) a safety and accident report; (f) such other relevant information as may be reasonably required by StadCo from time to time; and

(g) graphic representation of the Master Project Schedule with such reports as requested by StadCo that are typically available through the use of Design-Builder's software programs.

4.8 Construction.

4.8.1 Design-Builder shall develop and submit to StadCo the Construction Plan in accordance with **Section 3.1.2** not later than sixty (60) days prior to commencement of construction.

4.8.2 Design-Builder shall cause the Work to be performed in accordance with the requirements of the Contract Documents and all Applicable Laws.

4.8.3 Design-Builder shall provide and update the schedules and reports required pursuant to **Section 4.7** hereof. Design-Builder shall provide administrative, management and related services as required to coordinate, supervise and direct the performance of the Work by all Subcontractors with each other and with the activities and responsibilities of StadCo to complete the Project in accordance with the Contract Documents. Design-Builder shall be responsible for implementing the Construction Plan. Design-Builder shall coordinate all aspects of the Work with all Governmental Authorities. Design-Builder shall be responsible for timely notification to, and coordination with, all utility companies in connection with all utility services to be provided to the Project. Design-Builder shall inform StadCo at once when StadCo's participation is required. Connections for utilities required for the Work are the responsibility of Design-Builder to the extent set forth in the GMP Documents.

4.8.4 Design-Builder shall provide sufficient organization, personnel and management to carry out the requirements of this Agreement. Design-Builder shall take all steps necessary and appropriate to enforce agreements with Subcontractors when appropriate for the benefit of the Project. Design-Builder shall be responsible to StadCo for acts and omissions of Design-Builder's employees, Subcontractors and their agents and employees, including, without limitation, AOR and its agents and employees (when AOR is under contract with Design-Builder).

4.8.5 Design-Builder shall provide and/or supervise the General Conditions Work. Design-Builder shall provide and maintain, in good order, office and conference space for the use of StadCo and StadCo's Representative.

4.8.6 Design-Builder shall comply with its written Site-specific health and safety plan (**"HASP"**) in coordination with the administrator of the OCIP, for the Project. At minimum, Design-Builder's HASP shall meet the requirements of 29 C.F.R. 1926, and all Applicable Laws, consistent with Design-Builder's Construction Plan. StadCo bears no responsibility for either the quality of such plans or enforcement thereof. As required by law, each contractor is responsible for protecting the health and safety of its employees and the general public while ensuring they create a safe and healthful place to work. The HASP shall: (i) set forth the safety requirements for the Work; (ii) be provided to StadCo; and (iii) be incorporated into this Agreement by reference. At all times during the Work, Design-Builder shall take reasonable measures pursuant to the Contract Documents to secure the Site and any adjoining areas. Each of the Subcontractors shall remain controlling employer responsible for the safety programs and precautions applicable to its own work and the activities of others' work in areas designated to be controlled by such Subcontractors.

4.8.6.1 Design-Builder shall take reasonable precautions for safety of, and shall provide reasonable protection to prevent damage, including injury or loss, to any of the following: (a) workers on the Site and other Persons who may be affected by the Work, including the public; (b) the Work, Materials, and equipment to be incorporated therein, whether in storage on or off the Site or under the care, custody or control of Design-Builder or Design-Builder's Subcontractors, Vendors or Sub-subcontractors; and (c) other property at the Site or adjacent thereto, including, but not limited to, trees, shrubs, lawns, walks, pavements, roadways, structures and utilities not designated for removal.

4.8.6.2 Design-Builder will employ all necessary protective Equipment and devices required by law and the HASP. Design-Builder further warrants that during construction, Design-Builder and each of its Subcontractor's employees shall be fully trained by a qualified trainer in all local, state, and federally mandated training, including, but not limited to, OSHA, Environmental Protection Agency (**"EPA"**), and Department of Transportation (**"DOT"**), and that said employees are able to efficiently and safely operate Site machinery, vehicles and Equipment and perform the Work.

4.8.6.3 Design-Builder shall designate on-Site safety representatives who will provide on-Site safety management (the **"Safety Representative"**). Design-Builder's Safety Representative shall meet the requirements of a **"Competent Person"** as defined by the OSHA Standard 29 C.F.R. 1926.32(f), for all phases of construction Work. Design-Builder's Safety Representative must have a minimum of three (3) years' construction safety experience and hold an OSHA 30-hour card and/or be approved by StadCo's designated safety director. Design-Builder's Safety Representative must also be trained in first aid and cardiopulmonary resuscitation.

4.8.7 Design-Builder shall be responsible to StadCo for the thoroughness of all construction means, methods, techniques, and procedures employed in the performance of the Work, and for coordinating all portions of the Work.

4.8.8 Design-Builder shall keep the Site and surrounding areas free from accumulation of waste materials or rubbish caused by Design-Builder's operations. At the completion of the Work, Design-Builder shall remove from and about the Site and surrounding areas Design-Builder's tools, construction Equipment, machinery, surplus materials, waste materials, and rubbish. Design-Builder shall implement daily Site cleaning.

4.8.9 Design-Builder shall prepare the application for and obtain the general building permit and other construction permits required for the Work. StadCo shall pay for such permits directly to the permitting authority or reimburse Design-Builder but in either event the costs of such permits are not part of the GMP or the Construction Cost Budget.

4.8.10 Design-Builder shall coordinate all testing provided by others as required by the technical sections of the Construction Drawings and Specifications and/or Applicable Laws. Design-Builder shall keep an accurate record of all tests, inspections conducted, findings, and test reports.

4.8.11 Design-Builder shall develop, in conjunction with StadCo, procedures acceptable to StadCo for implementing, documenting, reviewing, and processing field questions and responses, field variance authorizations and directives, minor changes, and Change Orders. Design-Builder shall cooperate with StadCo to develop an "online" system to be used by Design-Builder and StadCo to facilitate quick and accurate communications and to provide for an up-to-date submittal log accessible to the Project Development Team, which system shall be the ProCore Project Management software or such other system as approved by StadCo. All requests for information by Design-Builder shall be submitted to StadCo in good faith and shall contain Design-Builder's proposed solution to the request.

4.8.12 Design-Builder shall receive from each Subcontractor, review for conformance, approve, or take other appropriate action and submit to AOR for approval or "approval as noted" together with copies to StadCo, such Shop Drawings, Product Data, Samples, As-Built Drawings and other Submittals as set forth in a Submittal schedule agreed to by the Parties. In collaboration with StadCo, Design-Builder shall establish and implement procedures for expediting the processing and approval of Shop Drawings, Product Data, Samples, mockups, and other Submittals, but in no event shall the time period for StadCo's initial review of a single submittal exceed seven (7) days after submittal, except as may be otherwise agreed to by the Parties in the submittal schedule. StadCo's review of Submittals by Design-Builder shall be limited to review of an initial submittal and two re-Submittals for conformance with the design concepts expressed in the Construction Drawings and Specification. Design-Builder shall not be relieved of responsibility for errors or omissions in Shop Drawings, Product Data, Samples or similar Submittals by StadCo's review thereof.

4.8.13 Design-Builder shall maintain at the Site (or such other place as approved in writing by StadCo), on a current basis: (a) a record copy of all contracts (including this Agreement and all Subcontracts), Drawings, Specifications, Addenda, Change Orders and other Modifications, in good order and marked to record all changes made during construction; (b) Shop Drawings; Product Data; Samples; (c) As-Built Drawings; (d) the most recent Master Project Schedule; (e) applicable handbooks; (f) maintenance and operating manuals and instructions; (g) all reports and meeting minutes required in **Section 4.7** hereof; and (h) other related documents that arise out of the contracts or the Work. Design-Builder shall maintain a current roster of all Subcontractors who have or are working on the Project with names and telephone numbers of key personnel and shall deliver this list to StadCo monthly. At the completion of the Project, Design-Builder shall deliver to StadCo a reproducible set of As-Built Drawings, which shall be provided in an electronic format in such version of CADD or other medium as agreed to by StadCo and Design-Builder or in such other medium or format as necessary to be utilized with the BIM model.

4.8.14 When Design-Builder considers the Work or a designated portion thereof Substantially Complete, Design-Builder shall prepare a draft of the Punch List for review and written approval by StadCo. The Punch List will be complete, detailed and thorough, and in a form and level of detail approved by StadCo. Design-Builder shall promptly complete, or have completed, all items of incomplete Work and perform, or have performed, any corrective Work as required by the Punch List.

4.8.14.1 Design-Builder shall develop in conjunction with StadCo a schedule setting forth anticipated dates for inspections of various portions of the Work by StadCo in order to determine Substantial Completion and Final Completion of the Work or designated portions thereof. It is anticipated that StadCo shall make an initial visit and one re-inspection for each area of the Work designated on the schedule developed by Design-Builder and StadCo.

4.8.15 If an accident or incident involving personal injury or damage to property, Equipment, or personnel of Design-Builder (or any Design Consultants, Subcontractors, Vendors, agents or business invitees) occurs on or off the Site, or while traveling to or from the Site, which arises out of, results from, or is any way connected with the Work, Design-Builder shall immediately notify StadCo of such accident or incident. Design-Builder shall provide StadCo access upon reasonable request with a copy of every report of such accident or incident that Design-Builder is required to submit, or submits, to any entity, including, without limitation, any government agency or body. Design-Builder shall provide StadCo a monthly incident report containing the details of all such accidents or incidents. Design-Builder agrees to cooperate fully with StadCo in investigating any such accident or incident.

4.9 Testing.

4.9.1 StadCo shall engage the services of an independent testing agency to verify compliance with the testing requirements contained in the Contract Documents. StadCo's testing laboratories will perform independent inspections and tests, interpret and evaluate the results of such tests for compliance with the Contract Documents, record observations and submit reports. StadCo shall provide Design-Builder with copies of such reports.

4.9.2 Design-Builder shall coordinate the activities of all Persons conducting tests and shall cooperate fully with such Persons to facilitate all tests and inspections.

4.9.3 Testing by StadCo shall be at StadCo's cost and expense. If any test by StadCo indicates Defective Work and Design-Builder disagrees with StadCo's conclusions based on StadCo's test, StadCo shall have the right to require additional testing of the part of the Work in question. Such additional tests shall be paid for by StadCo in the event such additional tests prove that no Defective Work exists. However, should such additional tests indicate Defective Work, Design-Builder shall, without adjustment to the GMP: (a) correct the Defective Work in accordance with the provisions of the Contract Documents; and (b) pay all costs related to such additional tests.

4.10 Quality Management.

4.10.1 Design-Builder shall develop and implement a comprehensive Construction Quality Management and Assurance Plan (the **"QM/QA Plan"**). The goal of the QM/QA Plan shall be to help ensure that construction of all components of the Work are in accordance with the requirements of the Contract Documents. The QM/QA Plan shall also ensure that appropriate procedures are implemented to verify and document compliance with the Contract Documents. The QM/QA Plan shall include, but shall not be limited to, the following: (a) allocation of quality control and assurance responsibilities to the various participants in the Project; (b) an inspection and testing plan for each critical component of the Work; (c) field monitoring and inspection reports, documenting the results of inspection; (d) audit plan to audit Subcontractor's quality control and assurance efforts; (e) identification and reporting procedures for Nonconforming Work; and (f) tracking system to monitor correction of Nonconforming Work.

4.10.2 As part of the QM/QA Plan, Design-Builder shall review the Work of Subcontractors to evaluate whether the Work of each Subcontractor is being performed in accordance with the requirements of the Contract Documents, and to evaluate whether there are any defects and deficiencies in the Work. Design-Builder shall promptly bring all such defects and deficiencies discovered to the attention of the applicable Subcontractor. Communications between Design-Builder and Subcontractors with regard to quality management and assurance shall not in any way be construed as releasing Design-Builder or its Subcontractors from performing their Work in accordance with the terms of the Contract Documents.

4.11 Use of Hazardous Materials.

4.11.1 Design-Builder shall not use, in connection with the Work, any Hazardous Materials in such manner as would violate any Applicable Laws or cause liability to StadCo. The foregoing shall not be deemed to prohibit Design-Builder from using in the Work any item specified by name in the Contract Documents or any Materials commonly used in construction so long as such Materials are handled and used in accordance with all Applicable Laws.

4.12 Adjacent Property/Ongoing Operations.

4.12.1 Design-Builder shall provide protection to prevent damage, injury, or loss as set forth in **Section 4.8.6** hereof. Without limiting the generality of the foregoing, Design-Builder agrees as follows: To use only those entrances or routes for the transportation of Materials and access of workers to the Site and staging areas, and to otherwise comply with a comprehensive transportation management plan, all as jointly determined by StadCo and Design-Builder prior to commencement of construction. Design-Builder acknowledges that some portions of the transportation management plan may be requirements of Governmental Authorities and Design-Builder agrees to abide by any such requirements;

4.12.2 To take customary construction precautions and erect such partitions, barricades, fencing, walkways, and other devices and other installations as are reasonably necessary to separate areas where the Work is being performed from areas being used by respective patrons, tenants, employees, guests, licensees, and invitees of the Team and owners of adjacent property;

4.12.3 To cause, if required by the transportation management plan, or other governmental requirements, its employees and the employees of the Subcontractors and Suppliers to park off-Site; and

4.12.4 To coordinate, supervise, and schedule all construction activities in accordance with this Agreement and the Contract Documents, including service interruptions, in advance and with the written approval of StadCo.

4.13 Checkout of Utilities; Training of Operating Personnel.

4.13.1 With StadCo's maintenance personnel, Design-Builder shall coordinate, schedule, and observe the checkout of utilities, operations of systems, and equipment for readiness and the initial start-up, calibration and trial testing of such systems by the applicable Subcontractors, and suggested preventative maintenance logs. Design-Builder shall make certain that the applicable Subcontractors coordinate the training of StadCo's maintenance personnel in accordance with the Contract Documents. During the first three events held in the Stadium, Design-Builder shall have appropriate personnel **"on call"** to deal with major systems.

ARTICLE 5. CONTRACT TIME

5.1 Time. TIME IS OF THE ESSENCE.

5.1.1 Design-Builder shall complete the Work pursuant to the Guaranteed Substantial Completion Date and the Final Completion date, as those dates may be amended from time to time pursuant to the terms of this Agreement.

5.1.2 Phased beneficial occupancy dates shall be established through mutual agreement between StadCo and Design-Builder.

5.1.3 StadCo shall provide Design-Builder a written notice to proceed and unencumbered access to the Site for commencement of construction in accordance with the following:

Activity	Date
Commence Box Culvert Work	See Master Project Schedule
Commence Early Release Work (including mass excavation, underground utilities, etc.)	See Master Project Schedule
Commence Work in Furtherance of the Executed GMP Amendment	See Master Project Schedule

5.1.3.1 If StadCo provides such written notices to proceed after each of the dates required in the table above, then Design-Builder shall have a day for day extension of the Guaranteed Substantial Completion Date; provided, however, that if such delay is due to the failure to act or omission of Design-Builder, then the Guaranteed Substantial Completion Date shall remain unchanged.

5.1.4 StadCo shall cause the Team to request, to the extent reasonably practicable, from the NFL that the first and second pre-season games of the Team's 2020 NFL Season not be played at the Project.

5.2 Delay Liquidated Damages and Waiver of Consequential Damages.

5.2.1 If the date of Substantial Completion of the Work occurs after the Guaranteed Substantial Completion Date (as such date may be extended pursuant to the terms of this Agreement) and such delay is not caused by StadCo, then Design-Builder shall pay to StadCo the following liquidated damages for StadCo's economic losses (collectively referred to herein as the **"Delay Liquidated Damages"**):

5.2.1.1 Five Million Dollars ($5,000,000.00) for each Team NFL pre-season or regular season home game originally scheduled by the NFL that is not played at the Stadium to be built pursuant to this Agreement; and

5.2.1.2 Twenty Thousand Dollars ($20,000.00) per day, commencing on the sixteenth (16th) Day after the Guaranteed Substantial Completion Date. The per diem Delay Liquidated Damages set forth in this **Section 5.2.1.2** shall commence on the sixteenth (16th) day after the Guaranteed Substantial Completion Date and shall accumulate until the date that Substantial Completion of the Work is achieved.

5.2.1.3 Five Hundred Thousand Dollars ($500,000.00) for each for-profit Non-Game Event, not to exceed three (3) Non-Game Events in total, scheduled to be held at the Stadium to be built pursuant to this Agreement, so long as:

(a) Design-Builder had prior written notice of the Non-Game Event at least ninety (90) days before the Non-Game Event was scheduled to be held; and

(b) The scheduled date for the Non-Game Event is at least ten (10) Days after the Guaranteed Substantial Completion Date; as of the date when the Non-Game Event was scheduled; and

(c) The reasonably expected paid attendance for the Non-Game Event is at least ten thousand (10,000) Persons; and

(d) The expenses incurred by StadCo exceed One Hundred Thousand Dollars ($100,000.00).

5.2.2 The Parties acknowledge and agree that because of the unique nature of the Project and the expense involved in playing in a substitute facility, it is difficult or impossible to determine with precision the amount of damages that would or might be incurred by StadCo as a result of Design-Builder's failure to achieve Substantial Completion. It is understood and agreed by the Parties that: (a) StadCo shall be damaged by failure of Design-Builder to meet such obligations; (b) it would be impracticable or extremely difficult to fix the actual economic damages resulting therefrom; (c) any sums that would be payable under **Section 5.2.1** are in the nature of liquidated damages, and not a penalty, and are fair and reasonable; and (d) such payment represents a reasonable estimate of fair compensation for the damages that may reasonably be anticipated from such failure. The Delay Liquidated Damages shall, without duplication, subject to the exceptions below, be the sole and exclusive measure of damages to, and the sole and exclusive remedy of, StadCo and any Indemnitee or any Third-Party Beneficiary, collectively, with respect to any failure by Design-Builder to achieve Substantial Completion on or before the Guaranteed Substantial Completion Date. The Delay Liquidated Damages are the aggregate amount payable to StadCo and any Indemnitee or any Third-Party Beneficiary collectively with respect to any failure by Design-Builder to achieve Substantial Completion on or before the Guaranteed Substantial Completion Date. StadCo's election to enforce the liquidated damages provision in this Agreement to compensate StadCo for Delay Liquidated Damages **shall not waive** or impact any other damages incurred by StadCo arising out of breach of this Agreement other than the failure to achieve Substantial Completion by the Guaranteed Substantial Completion Date (including without limitation damages relating to latent or patent defects in the Work), or any rights that StadCo has under this Agreement, or allowed by any Applicable Law, or in equity, including, without limitation, damages and remedies arising from Design-Builder's indemnity and defense obligations, and all other rights and remedies available to StadCo, any Third-Party Beneficiary or any other Indemnitee under this Agreement, including, without limitation any right to terminate the Agreement, or part hereof. Notwithstanding the foregoing, no insurance coverage required in this Agreement shall be impacted or limited by such liquidated damages and shall not constitute a waiver as it relates to potential coverage pursuant to any policy. In addition, any insurance carrier providing coverage or policies pursuant to the requirements of **Exhibit G** shall not be entitled to utilize the language contained in this **Section** as a basis for denial of coverage.

5.2.3 Notwithstanding anything in the Contract Documents to the contrary, the maximum amount of cumulative Delay Liquidated Damages payable by Design-Builder under the Contract Documents shall not exceed [redacted]; provided, however, there shall be no maximum amount of overall cap on Delay Liquidated Damages if: (a) Design-Builder abandons the Project or otherwise fails to use commercially reasonable efforts to prosecute the Work to Substantial Completion; or (b) Design-Builder's surety or the guarantor has failed to commence commercially reasonable efforts to prosecute the Work within ten (10) days after having been given notice of Design-Builder's abandonment or failure to prosecute the Work. At StadCo's option, StadCo may deduct, withhold and/or set off from or against any amounts then or thereafter payable or due to Design-Builder by StadCo, up to the amount of any Delay Liquidated Damages payable by Design-Builder under the Contract.

5.2.3.1 To the extent the delay resulting in a failure to achieve Substantial Completion by the Guaranteed Substantial Completion Date is not caused by Design-Builder, but is caused by any one or more Subcontractors, and provided that Design-Builder shall use commercially reasonable efforts to collect all amounts the responsible Subcontractor(s) is liable for under the applicable Subcontract(s), then Design-Builder's liability for Delay Liquidated Damages in such instance shall be limited to the amounts actually recovered from the Subcontractor(s) plus one-half (1/2) the difference of:

(a) The actual Liquidated Damages that would otherwise have been assessed pursuant to **Section 5.2**, and

(b) The amounts recovered by Design-Builder against the Subcontractor(s) causing the delay.

5.2.4 Notwithstanding anything in the Contract Documents to the contrary, Delay Liquidated Damages shall not be assessed unless the Parties have entered into the GMP Amendment.

5.2.5 **Mutual Waiver of Consequential Damages**. Design-Builder and StadCo mutually waive the right to recover against one another Consequential Damages arising out of or relating to this Agreement, except for the following, which are not waived: (a) any Consequential Damages that may be included within Delay Liquidated Damages payable under this Agreement; and (b) Consequential Damages covered by and paid under the insurance required to be provided by StadCo pursuant to **Section 13.3.1** and within the limits expressly required in **Exhibit H**; (c) Consequential Damages covered by and paid under the insurance required to be provided by Design-Builder pursuant to **Exhibit G** and within the limits of the insurance that are specifically required pursuant to **Exhibit G**, and (d) Consequential Damages covered by and paid under insurance required to be provided by the AOR, any of the AOR's subconsultants at any tier, or any Subcontractors or Vendors.

5.3 **Extensions of Time**.

5.3.1 If there is no material impact, as further defined in Section 5.3.3, to the critical path activities required by the applicable Master Project Schedule, then Design-Builder shall not be entitled to an extension of time.

5.3.2 A Force Majeure Delay shall not be deemed to have occurred unless Design-Builder notifies StadCo in writing of a Force Majeure event giving rise to a Delay within fourteen (14) days after such Force Majeure Delay, and Design-Builder provides StadCo with the details of such event and the length of the anticipated Delay within an additional five (5) Days thereafter. Such notice from Design-Builder shall include a general description of the impact of any such Delay on critical path activities, the Master Project Schedule, and Contract Time. Notwithstanding the foregoing, if Design-Builder fails to deliver StadCo notice of a Force Majeure event no later than seventeen (17) days after the occurrence of the Force Majeure Delay, Design-Builder shall be required, as a condition to entitlement to a Change Order, to demonstrate that a material change and/or impact to the GMP has occurred or a material change and/or impact to the Master Project Schedule has occurred.

5.3.3 There will be no adjustment in the Contract Time except as provided in this **Section 5.3** or in **Section 14.3.3** and **Section 14.3.4** and any other provision in this Agreement that expressly provides for an adjustment to the Contract Time. If Design-Builder experiences Delay due to Force Majeure or otherwise, then the Contract Time will be extended by Change Order to the extent of the resulting delay to the critical path activities, provided that: (1) for weather related Force Majeure experienced at the Project Site during the Contract Time must be found to be unusually severe as compared to the ten-year average for the same period based on records of the National Oceanic and Atmospheric Administration (**"NOAA"**); (2) the Force Majeure event must actually affect the performance of Work shown to be the critical path of the Master Project Schedule (meaning the Force Majeure event must actually prevent Work on critical path activities for fifty (50) or more percent of Design-Builder's scheduled work Day); (3) the aforesaid causes did not result from the fault or negligence of Design-Builder or its Subcontractors; and (4) Design-Builder has taken (and shall cause each Subcontractor to take) all reasonable steps to continue the Work utilizing methods and procedures generally accepted in the construction industry for such Force Majeure event; provided, however, that such extension of Contract Time shall be net of any delays caused by the fault or negligence of Design-Builder or which are otherwise the responsibility of Design-Builder provided, further, Design-Builder shall not be entitled to the time extensions pursuant hereto by reason of mechanical failure of Design-Builder's Equipment, financial conditions of Design-Builder, failure of Suppliers to deliver Materials ordered by Design-Builder, unless such delay in delivery is caused by a Force Majeure event. To the extent Design-Builder is seeking additional compensation, it shall do so pursuant to **Section 14.3**.

5.3.4 Design-Builder is obligated to mitigate Delays and impacts to the tasks contained in the Master Project Schedule and shall, using all commercially reasonable means: (1) sequence tasks to maintain completion dates; (2) accommodate change within the float; and (3) notify StadCo of any risks concerning the timely completion of critical path tasks. Design-Builder's efforts and activities to mitigate Delays and impacts to tasks required in the Master Project Schedule shall be compensable as Cost of the Work under the GMP as adjusted by Change Order.

5.4 Acceleration.

5.4.1 If Design-Builder is not maintaining a schedule consistent with its obligations under this Agreement, then, at the request of StadCo, Design-Builder shall increase its efforts on the Project, including, without limitation, the addition of more personnel or increased utilization of personnel during regular times and during periods of time for which "overtime" or shift premium may be required. If Design-Builder is required to work overtime as a result of an inexcusable Delay, correction of deficient work, or other coordination problems caused by Design-Builder or anyone Design-Builder is responsible for, any and all costs of Design-Builder to eliminate such Delay shall be compensable as Cost of the Work under the GMP, however, Design-Builder shall not be entitled to an increase in the GMP.

5.4.2 In the event StadCo desires to accelerate the Master Project Schedule for reasons other than Delays caused by or attributable to Design-Builder, StadCo shall so notify Design-Builder in writing by a Construction Change Directive. Upon receipt of such written instruction, Design-Builder shall, if practical, require its personnel and Design Consultants, Subcontractors, and Vendors to work such overtime hours and/or to increase their respective work forces as are reasonably necessary to meet StadCo's acceleration goals. In the event such an acceleration is ordered by StadCo, Design-Builder shall be entitled to request an adjustment in the GMP determined in accordance with **Article 14**.

ARTICLE 6. STADCO'S RESPONSIBILITIES

6.1 StadCo's Representative.

6.1.1 StadCo has designated StadCo's Representative as a representative authorized to act on StadCo's behalf with respect to the Project. Design-Builder and other members of the Project Development Team shall have the right to rely on the instructions, written directions, or other information provided by StadCo's Representative, and all such actions, instructions, directions, and information shall be deemed to be from StadCo provided, however, StadCo's Representative shall not have the authority to

provide any approvals required of StadCo under the Contract Documents. StadCo reserves the right to change its representative, and StadCo shall notify Design-Builder in writing within seven (7) days of such change. StadCo's Representative has no design or construction management responsibilities of any nature and none of the activities of StadCo's Representative supplant or conflict with any services or responsibilities customarily furnished by AOR, Lead Design Architect, and/or required of Design-Builder. StadCo's Representative shall have authority to establish procedures, consistent with this Agreement, to be followed by Design-Builder, AOR, and Subcontractors.

6.1.2 StadCo shall render approvals and decisions within the time frame set forth in this Agreement or any schedules approved by StadCo or, in the absence thereof, promptly, to avoid delay in the orderly progress of Design-Builder's services and the Work of Design-Builder. It shall be Design-Builder's responsibility to timely advise StadCo of all time requirements and restraints with respect to such approvals and decisions.

6.1.3 The Design-Builder's obligations and responsibilities pursuant to the Contract Documents are not limited by any provision of the Contract Documents that provides for any approval, review, or similar participation by StadCo or Governmental Authorities.

6.1.4 StadCo shall provide Design-Builder with evidence of the individuals who are authorized to contractually bind StadCo.

6.1.5 StadCo represents and warrants that: (a) this Agreement constitutes a valid, legal, and binding obligation of StadCo, enforceable in accordance with the terms hereof, except as the enforceability may be limited by applicable bankruptcy, insolvency, reorganization, moratorium, or other similar laws affecting creditors' rights generally; (b) except as previously disclosed in writing, there are no actions, suits, or proceeding pending or, to StadCo's knowledge, threatened against or affecting StadCo before any court or administrative body or arbitral tribunal that might materially adversely affect the ability of StadCo to meet and carry out its obligations under this Agreement; (c) the execution, delivery and performance by StadCo of this Agreement has been duly authorized by all requisite corporate action, and will not contravene any provision of, or constitute a default under, any other agreement or instrument to which it is a party or by which it or its property may be bound; and (d) this Agreement complies with all Applicable Laws.

6.2 Hazardous Materials.

6.2.1 StadCo represents and warrants that the Site has obtained required public approvals and necessary easements and the Site does not contain Hazardous Materials above permitted levels of any Applicable Laws. StadCo shall be deemed to be the generator of all Hazardous Materials that existed at the Site prior to the commencement of the Work (including for Hazardous Materials that are specifically identified by type and location to be part of the Work), and StadCo shall sign all manifests (as owner or generator, as indicated on the manifest) required to accompany the transportation and disposal of such Hazardous Materials. StadCo shall be responsible for the remediation of any such Hazardous Materials, all in accordance with Applicable Laws and pursuant to a schedule agreed to by the Parties. Design-Builder shall not be responsible for Hazardous Materials encountered at the Site, including Delays arising from encountering such other Hazardous Materials, except for those Hazardous Materials (a) specifically identified by type and location in the Contract Documents to be part of the Work, or (b) brought to the Site by Design-Builder or its Subcontractors and negligently handled or stored by Design-Builder or its Subcontractors. StadCo expressly agrees Design-Builder is not responsible for any pre-existing Hazardous Materials at the Site that are not specifically identified by type and location in the Contract Documents to be part of the Work or any Hazardous Materials brought to the Site by anyone other than Design-Builder or its Subcontractors.

6.2.2 Should Design-Builder encounter any Hazardous Materials at the Site, it shall have the right to immediately stop Work in the affected area and report the condition to StadCo in writing. Upon receipt of Design-Builder's written notice, StadCo shall obtain the services of a licensed laboratory to verify the presence or absence of the material or substance reported by Design-Builder and, in the event such

material or substance is found to be present, to cause it to be rendered harmless (which shall be deemed to mean remediated, removed, or otherwise addressed as required by applicable regulations or authorities). Unless otherwise required by the Contract Documents, StadCo shall furnish in writing to Design-Builder the names and qualifications of Persons or entities who are to perform tests verifying the presence or absence of such material or substance or who are to perform the task of removal or safe containment of such material or substance. Design-Builder will promptly reply to StadCo in writing stating whether or not either has reasonable objection to the Persons or entities proposed by StadCo. If Design-Builder has an objection to a Person proposed by StadCo, then StadCo shall propose another to whom Design-Builder has no reasonable objection. When the material or substance has been rendered harmless, Work in the affected area shall resume upon written agreement of StadCo and Design-Builder. By Change Order, the Contract Time shall be extended appropriately and the GMP shall be increased in the amount of Design-Builder's reasonable additional costs of shut-down, Delay, and start-up. Except with respect to Hazardous Materials identified as Design-Builder's responsibility in **Section 6.2.1** above, Design-Builder shall not be required to perform any additional or changed Work related to the presence of a Hazardous Material at the Site.

6.2.3 To the fullest extent permitted by Applicable Law, StadCo shall indemnify, defend and hold harmless Design-Builder, AOR, Design-Builder's other consultants, Subcontractors, and agents and employees of any of them from and against claims, damages, losses and expenses, including but not limited to reasonable attorneys' fees, fines, judgments, and penalties arising out of or resulting from performance of the Work in any area affected by Hazardous Materials that existed at the Site prior to the commencement of the Work (except with respect to Hazardous Materials identified as Design-Builder's responsibility in **Section 6.2.1** above) if in fact the material or substance directly results in bodily injury, sickness, disease or death, or injury to or destruction of tangible property (other than the Work itself) and has not been rendered harmless, provided that such claim, damage, loss or expense is attributable to bodily injury, sickness, disease or death, or to injury to or destruction of tangible property (other than the Work itself) and provided that such damage, loss or expense is not due to the negligence of the party seeking indemnity. StadCo shall procure and maintain insurance to cover its obligations in this paragraph.

6.2.4 If Design-Builder is held liable for the cost of remediation of a Hazardous Material or substance solely by reason of performing Work as required by the Contract Documents, StadCo shall defend, indemnify and hold Design-Builder harmless for all cost and expense (including but not limited to attorneys' fees, fines, judgments and penalties) thereby incurred, except to the extent that such damage, loss or expense is due to the negligence of the Design-Builder.

6.3 Evidence of Financing.

6.3.1 StadCo shall, upon request, furnish to Design-Builder reasonably satisfactory evidence that financial arrangements have been made to fulfill the obligations of StadCo under this Agreement. StadCo shall furnish such evidence as a condition precedent to commencement or continuation of the Work or the portion of the Work affected by a material change. After StadCo furnishes the evidence, StadCo shall promptly notify Design-Builder of any future material changes.

6.4 Work by Separate Contractors.

6.4.1 StadCo reserves the right to hire Separate Contractors in connection with the Project. With respect to each part of the Project as to which StadCo may enter into separate contracts with Separate Contractors, Design-Builder shall, as part of the Work, afford Separate Contractors reasonable opportunity for introduction and storage of their materials, and for the execution of their services and, as may be required by the Contract Documents, shall properly connect and coordinate the Work with the services of such Separate Contractors. In addition, Design-Builder shall cooperate with StadCo and Separate Contractors in the scheduling and coordination of services to be performed by such Separate Contractor with the Work to be performed by Design-Builder or its Subcontractors. Design-Builder shall cooperate with StadCo and all Separate Contractors, their subcontractors and any other entity involved in the performance of any separate services for the Project. In order to cause the Work and any separate services to be performed by Separate Contractors to be completed in an expeditious manner, Design-Builder agrees that it will use all reasonable efforts in order to ensure that such Separate Contractors have

a reasonable opportunity to complete their services as and when required. StadCo assumes responsibility for the failure of Separate Contractors that StadCo has hired to perform their work properly, and shall require in any agreement it may have with a Separate Contractor that the Separate Contractor shall cooperate with Design-Builder and its Subcontractors in the performance of the Work. StadCo shall require that any and all Separate Contractors comply with any applicable Project Labor Agreement and comply with Design-Builder's safety program and rules of the Site. If StadCo's Separate Contractors materially interfere with or cause damage to the Work, Design-Builder shall be entitled to request a Change Order pursuant to **Article 14**. StadCo shall cause the Lead Design Architect or any other designer or consultant responsible for the design of the work to be performed by Separate Contractors to coordinate such design with Design-Builder and AOR so that the Work and the work of such Separate Contractors can be fully coordinated and connected. Neither Design-Builder nor AOR shall be responsible for errors or omissions in the design of the work, if any, to be performed by Separate Contractors.

6.4.2 If any part of the Work depends upon the proper performance of work of any Separate Contractor, Design-Builder shall prior to proceeding with that portion of the Work, inspect and measure the work of the Separate Contractor and promptly report to StadCo any apparent discrepancy or defects in such other work except for latent or concealed defects.

6.4.3 Subject to the provisions of **Section 6.4.1**, if Design-Builder causes damage to the Work or the property of StadCo, Design-Builder shall promptly remedy such damage and shall promptly attempt to settle any resulting dispute or claim with such Separate Contractor. If a Separate Contractor or its subcontractor shall assert any claim against StadCo on account of any damage or loss alleged to have been sustained as a result of the fault or negligence of Design-Builder, or by anyone for whom Design-Builder is responsible, StadCo shall notify Design-Builder.

6.4.4 StadCo recognizes and accepts the Master Project Schedule is predicated upon StadCo securing all material and legal agreements for the Site such that Design-Builder is provided an unencumbered notice to proceed pursuant to **Section 5.1.3** hereof. StadCo shall be responsible to meet those milestone dates identified in the Schedule as being the responsibility of StadCo. If such milestone dates cannot be met by StadCo and the critical path of the Project has been adversely impacted by no fault of the Design-Builder, then Design-Builder shall be entitled to request an extension of time and an increase in the GMP as reasonably justified under **Section 5.3** and **Article 14** hereof.

ARTICLE 7. CONTRACT SUM/PAYMENT

7.1 Contract Sum; Design-Build Contingency.

7.1.1 Except as otherwise provided herein, StadCo, shall pay at the times and in the manner provided for in this **Article 7**, amounts constituting the Cost of the Work (as defined in **Section 7.3.2**), General Conditions Work, Design-Build Contingency (to the extent used to pay any Cost of the Work), and Design-Builder's Fee (collectively referred to as the **"Contract Sum"**), which amount shall not exceed the GMP. Design-Builder shall be responsible for all costs in excess of the GMP.

7.1.1.1 Certain preconstruction and construction services were previously authorized and provided by Design-Builder pursuant to the Letter Agreement. StadCo shall pay all amounts left due under the Letter Agreement within thirty (30) days after execution of this Agreement. All payments made for services and work provided pursuant to the Letter Agreement shall be credited against the Contract Sum. Pursuant to its terms, the Letter Agreement shall be superseded and replaced with this Agreement upon execution of this Agreement, and all services and work performed by Design-Builder under the Letter Agreement shall be subject to the terms and conditions of this Agreement.

7.1.2 **Design-Build Contingency**. The amount of the Design-Build Contingency shall be equal to [redacted] of the sum of the Cost of the Work (actual plus estimated, including the AOR's compensation) plus the Design-Builder's Fee. Design-Builder may expend funds from the Design-Build Contingency to pay for Cost of the Work incurred for completion of the Work, including: (a) increased or additional costs for design completion; (b) increased or additional costs relating to

ambiguities or inconsistencies in the Construction Documents; (c) for any costs or expenses attributable to Errors and Omissions, or damages caused by professional negligence excluding AOR fees or other costs otherwise included in the AOR Agreement; (d) scope differences; (e) Subcontractor defaults; (f) overtime; (g) acceleration; (h) repairing or correcting damaged, improperly executed, or Nonconforming Work; and (i) unanticipated price or labor cost escalations. The Design-Build Contingency will not be used to pay for any cost or expense that provides a betterment, upgrade, or enhancement of the Project; instead, Design-Builder shall be entitled to request an increase in the GMP for such costs and expenses pursuant to **Article 14**.

7.1.2.1 Whenever any use of Contingency relates to costs attributable to those listed above in **Section 7.1.2** or for amounts that could potentially be covered by Design-Builder's Protective Professional Indemnity Coverage required by **Exhibit G**, then Design-Builder shall:

(a) Provide prompt written notice to StadCo outlining, in reasonable detail, what event or events triggered the use of Contingency. Such notice shall include but not be limited to: the amount of Contingency used and the purposes for which it was used;

(b) Confer with StadCo to analyze, among other things, the likely implications of pursuing claim(s) or demand(s) against potential parties and insurance carriers that might be responsible for reimbursing or covering any and all costs related to the use of Contingency;

(c) Upon receipt of direction from StadCo to Design-Builder to pursue a claim, file a claim or demand against parties or insurance policies potentially responsible for reimbursing or covering any and all costs related to the use of the Contingency, including any of StadCo's policies, Design-Builder's policies, AOR's policies, and/or Design-Builder's Subcontractors' and/or subconsultants' policies;

(d) Provide monthly updates on the status of any claims or demands against all applicable insurance carriers or parties responsible for any Liabilities (as defined in **Section 9.1**) relating to the use of Contingency; and

(e) Replenish the Contingency with any and all amounts received from any party or applicable insurance carrier.

7.1.2.2 Each allocation and/or reallocation to or from the Design-Build Contingency shall be reflected (with a detailed narrative explanation), in a manner acceptable to StadCo, on the respective Application for Payment during which such allocation and application is made. Notwithstanding anything herein to the contrary, Design-Builder must obtain prior written approval from StadCo for any use of the Design-Build Contingency in excess of Two Hundred and Fifty Thousand Dollars ($250,000.00) on any Application for Payment, which approval is for the limited purpose of ensuring the Design-Build Contingency is being used as required by **Section 7.1.2**. Design-Builder shall keep a log of the status of the Design-Build Contingency and shall report to StadCo on a monthly basis the purposes for which the Design-Build Contingency was used.

7.1.3 Design-Build Contingency Reduction. Quarterly, after the execution of the GMP Amendment, Design-Builder and StadCo shall meet and confer to analyze the Design-Build Contingency and determine methods and timing of potentially reducing the Design-Build Contingency for the benefit of StadCo for use on the Project to implement scope changes to the Work or otherwise to make the Design-Build Contingency available for StadCo's use. Design-Builder shall use commercially reasonable efforts to ascertain actual or known potential claims against Design-Builder or actual or reasonably anticipated events that constitute permissible uses of the Design-Build Contingency. If the Parties agree to release a portion of the Design-Build Contingency, then Design-Builder shall release such portion and any such release shall be evidenced by Change Order; the amount released shall be considered Savings and Design-Builder shall receive a percentage of such Savings pursuant to **Section 7.5.1** hereof, except that Design-Builder shall be entitled to payment of this portion of such Savings with the next monthly progress payment to be made to Design-Builder after the execution of the Change Order evidencing such release.

7.1.4 The Design-Build Contingency shall be increased or decreased, as the case may require, to reflect net savings or net losses resulting from the award of Subcontracts. The amount of the adjustment to the Design-Build Contingency shall be determined by subtracting the amount of each Subcontract at the time the Subcontract is entered into from the amount allocated by Design-Builder in the initial Schedule of Values of the Work approved by StadCo to be performed by such Subcontract. If the resulting calculation is a positive number, the Design-Build Contingency will be increased by such amount, and if the resulting product is a negative number, the Design-Build Contingency will be decreased by such amount. In addition, Design-Build Contingency shall be increased or decreased, as the case may require, to reflect other net savings or net losses resulting from the actual execution of the Work.

7.1.5 Design-Builder may apply, use, or allocate from the Design-Build Contingency any amounts for Delay Liquidated Damages.

7.1.6 The Parties acknowledge (a) that when Design-Build Contingency is used as a Cost of the Work Design-Builder shall not be entitled to charge or receive any fee in addition to Design-Builder's Fee on the Design-Build Contingency used and (b) that there shall not be any deduction from the Design-Builder's Fee if there remains any unallocated or unused Design-Build Contingency amounts at Final Completion.

7.2 Allowances.

7.2.1 The GMP Amendment may, with the approval of StadCo, contain allowances for items of Work that StadCo agrees are not detailed enough for Design-Builder to provide a definitive price (**"Allowances"**). For these Allowances, Design-Builder may propose estimates of costs that are properly reimbursable as Costs of the Work. The Allowance shall include: all estimated labor, Material, Equipment, taxes, transportation, General Conditions Costs, Design-Builder's Fee, and all Subcontractor overhead and profit, associated with each Allowance item. Design-Builder shall develop a final price for portions of the Work covered by Allowances promptly after StadCo has finalized its selection of items, if any. Design-Builder shall give notice to StadCo of the final amount. StadCo thereafter shall promptly elect to either:

7.2.1.1 Issue a Change Order increasing the GMP by the amount agreed upon by Design-Builder and StadCo to furnish or construct the Allowance item in excess of the Allowance amount, if necessary, already included within the GMP, and the GMP shall only be increased or decreased by the amount of delta from actual cost and the allowance amount; and/or

7.2.1.2 Direct Design-Builder to undertake the redesign of the Allowance item or any other item of Work in such a manner that the Allowance item can be designed and installed without the Master Project Schedule being extended, if reasonably possible. If StadCo elects to so redesign, Design-Builder agrees to cooperate with StadCo in order to reduce the cost of constructing or furnishing the Allowance item or any other item of Work, but in all events Design-Builder shall be entitled to an adjustment in the GMP for additional design costs plus a fee equal to three point nine percent (3.9%) of such costs.

7.2.2 If the Cost of the Work of any Allowance item is less than the Allowance for that item, Design-Builder shall promptly notify StadCo in writing and an appropriate Change Order shall be prepared reducing the GMP and a corresponding reduction in Design-Builder's Fee.

7.2.3 Design-Builder shall not be entitled to charge or receive any Fee on unallocated or unused Allowance amounts.

7.3 Cost of the Work.

7.3.1 Design-Builder shall be responsible for, and shall pay without reimbursement from StadCo, all Cost of the Work in excess of the GMP, as may be adjusted by Change Order.

7.3.2 **Cost of the work**. Each of the following costs described in this **Section 7.3.2** shall be a reimbursable **"Cost of the Work,"** subject to the GMP, when actually incurred by Design-Builder during or in connection with performance of the Work. These costs shall include only actual costs incurred by Design-Builder, less all discounts, rebates and salvage proceeds taken by Design-Builder:

7.3.2.1 Subcontracts and Purchase Agreements: All costs incurred in connection with Work performed and Materials provided pursuant to Subcontracts, purchased pursuant to purchase agreements, or provided pursuant to written agreements with consultants providing professional services in connection with the Project (including the fees and reasonable reimbursable expenses of Design-Builder's consultants and AOR and its consultants) retained on a "fixed price" or "lump sum basis" or "hourly basis." To the extent any Subcontractors or consultants are retained on a "cost plus fee" basis, then the costs chargeable by said Subcontractor or consultant shall only be included in the Cost of the Work if they are of the type expressly provided for in this **Section 7.3**.

7.3.2.2 Personnel Expenses:

(a) Wages paid by Design-Builder for construction labor in Design-Builder's direct employ (including foremen and general foremen) consistent with prevailing wage requirements as referenced in the Act. Cost of the Work shall include benefits payable under applicable union agreements or applicable Project Labor Agreement with respect to the wages described in the preceding sentence. Such hourly rates shall not exceed the rates required to be paid under any applicable union agreements or applicable Project Labor Agreement unless approved by StadCo, and such approval shall not be unreasonably withheld. Upon request by StadCo, Design-Builder shall provide StadCo with copies of all applicable union agreements evidencing the cost of labor employed to work on the Project by Design-Builder and its Subcontractors.

(b) Compensation paid to supervisory staff engaged on the Project (on or off Site) and performing services directly related to the Project to the extent of hours devoted to the Project pursuant to the Rate Schedule attached hereto as **Exhibit F**. With respect to Design-Builder's employees described in this subparagraph (b) of this **Section 7.3.2.2**, Cost of the Work shall include the costs identified in **Exhibit F**. Design-Builder will bill for 80 hours per two-week pay period each week when supervisory personnel are assigned full-time to the Project. For supervisory personnel assigned part-time to the Project, Design-Builder will bill for actual hours up to 80 hours per two-week pay period.

7.3.2.3 Self-Performed Work: Self-Performed Work shall be subject to the requirements of **Section 4.3** and shall include only those costs identified in this **Section 7.3.2**. Design-Builder's mark-up on Self-Performed Work, if any, shall not exceed the mark-up percentage set forth in **Section 4.2.6**.

7.3.2.4 Materials: The amounts Design-Builder paid for Materials, whether or not incorporated into the Work, purchased by Design-Builder directly relating to the Work, including transportation thereof, cost of inspection, testing, storage, or handling.

7.3.2.5 Equipment and Tools: Design-Builder will bill for Equipment and tools used in connection with the Work at the rates set forth on **Exhibit F**, which may be updated by Change Order. Design-Builder will bill for Equipment and tools used in connection with the Work that are not identified in **Exhibit F** at cost.

7.3.2.6 Equipment Operation, Maintenance and Repair: All costs for the operation, maintenance, and repair of Equipment furnished by Design-Builder.

7.3.2.7 Transportation: Except as hereinafter provided, all loading, unloading, freight, express, trucking, and demurrage charges directly incurred for the Project, including costs of assembling, erecting, moving and dismantling construction Equipment at the Site.

7.3.2.8 Applicable Laws: All costs of compliance with all Applicable Laws directly related to the Project, including, without limitation, permit fees, licenses, royalties, inspection and testing costs, tests, except any liability for payment of any citation or penalty imposed as the result of an act or omission by Design-Builder, any Subcontractor or their respective employees, licensees or agents.

7.3.2.9 Temporary Facilities, Supplies and Utilities: Costs of fuel, power, light and water used for performance of the Work at the Site, temporary fences, guard rails, scaffolding, hoists, temporary storage, temporary protection and repairs to adjacent property, office and sanitary facilities used in connection with the Work.

7.3.2.10 Job-Related Travel: Expenses incurred for job related travel costs for Design-Builder's personnel in accordance with the Travel Policy, attached hereto as **Exhibit P**.

7.3.2.11 Administrative Expenses: Cost of the Work shall include job-related expenses incurred such as rental of property for storage, job office or other purposes, rental of temporary office space and utility expenses associated with maintaining a temporary office complex, long distance telephone calls, office equipment (including printers, monitors, copy machines, phone headsets, etc.), computers, software, supplies, furniture, telephone service at the Site, expressage, blueprinting or other reproduction expenses, postage, messenger service, progress photographs, fees, permits, surveys and rental deposits.

7.3.2.12 Cleaning: Cost of removal of waste material or rubbish from the Site.

7.3.2.13 Emergencies: Costs not reimbursed by insurance that are reasonably incurred due to any emergency affecting the safety of Persons and/or property, provided that such emergency is not caused by the negligence or failure to fulfill a specific responsibility of Design-Builder to StadCo set forth in the Contract Documents.

7.3.2.14 Casualty Losses: Costs reasonably incurred in connection with any casualty loss, including personal injury or property damage, affecting the Project, to the extent such costs are not compensated by insurance.

7.3.2.15 Safety and Quality Program Costs: Costs associated with the administration of the Design-Builder's and StadCo's safety and quality programs.

7.3.2.16 Miscellaneous StadCo-Approved Cost Items: Miscellaneous expenditures not otherwise covered in this **Section 7.3.2** that are incurred or payable in connection with the rendering of services or the performance of the Work and that are not excluded under **Section 7.3.3** hereof, if approved in writing by StadCo, which approval may be withheld at StadCo's reasonable discretion.

7.3.2.17 Taxes: All sales, use and gross receipts taxes imposed by a Governmental Authority to the extent related to the Work.

7.3.2.18 Deductibles. Deductibles shall be reimbursable Cost of the Work pursuant to **Exhibit G**.

7.3.3 **Other Costs**: Subject to the provisions of this Agreement, the following costs shall be compensable to Design-Builder as other costs (**"Other Costs"**) at the actual amount charged, without addition or mark-up for the Design-Builder's Fee:

7.3.3.1 Expenses or Damages Not Compensated: Expenses or damages, to the extent not compensated by insurance or otherwise (including settlements made with the written approval of StadCo), except to the extent any such damage or expense is caused by the negligent supervision on the part of Design-Builder's employees charged with the supervision of the Project.

7.3.3.2 General Conditions Work: General Conditions Work items as outlined in the GMP Amendment.

7.3.3.3 Legal Fees: Any legal cost or fees incurred related to any disputes with any Subcontractor or Vendor related to this Agreement, the Project, or the Work; however, Design-Builder shall provide written notice to StadCo prior to incurring any legal costs or fees.

7.3.3.4 Parent Guaranty or Bond: Parent Guaranty (in the form attached hereto as **Exhibit L**) or bond rates shall be subject to adjustment annually and shall be considered compensable Other Costs as follows:

(a) Costs of any corporate or parent guarantees from Design-Builder related to its performance (as may be agreed to by StadCo), furnished by Design-Builder for the Project shall be [redacted]. In the event of a Change Order, the costs of any corporate or parent guarantees from Design-Builder related to its performance, shall be charged or calculated at the rate of [redacted]; or

(b) Performance and payment bonds obtained by Design-Builder for the Project, if any, as required by StadCo, shall be paid at the rate of [redacted] based upon the current Construction Cost Budget.

7.3.3.5 Document Record Retention Costs: Costs associated with compliance with any document record retention requirements applicable to the Project, to be billed by Design-Builder without markup to StadCo.

7.3.3.6 Fees and assessments for building permits, licenses and inspections for which Design-Builder is required to pay under the Contract Documents.

7.3.4 Non-Allowable Costs: Except as otherwise expressly agreed to by StadCo in writing or otherwise permitted under **Section 7.3.2** hereof, costs incurred in connection with the following shall not be Cost of the Work (**"Non-Allowable Cost of Work"**) and no payment shall be made by StadCo in connection therewith other than as part of Design-Builder's Fee:

7.3.4.1 The services and related expenses, except as otherwise provided in **Section 7.3.2.2** above, of any officers or corporate office supervisory personnel of Design-Builder and of personnel in Design-Builder's human resources, accounting, legal, labor relations, insurance and tax departments and all other costs of doing business, services and related expenses required to maintain and operate Design-Builder's corporate offices and any established branch offices;

7.3.4.2 Overhead expense, general expenses and home office expense of Design-Builder;

7.3.4.3 Expenses (including interest) of Design-Builder's capital employed for the Project;

7.3.4.4 Amounts required to be paid by Design-Builder for federal, state or local income, franchise, or similar taxes;

7.3.4.5 Costs incurred to the extent that such costs result in the GMP being exceeded;

7.3.4.6 All costs of business and/or operating permits, licenses, fees and taxes, required by any local, state or federal government authorities or labor agreements to enable Design-Builder, its Subcontractor or Vendors of any tier, to be qualified to do business and/or perform trade

activities and/or any Work pursuant to the Contract Documents, other than those set forth in **Section 7.3.3.6**;

7.3.4.7 Except as provided in **Exhibit G**: (i) insurance premium in excess of the insurance required by StadCo pursuant to **Exhibit G**; or (ii) self-insured retentions or deductibles paid by Design-Builder associated with any loss claimed under Design-Builder's insurance policies associated with the Project or the Work pursuant to **Exhibit G**;

7.3.4.8 At StadCo's written approval, costs of any discretionary bonus to Design-Builder's or any Subcontractor's employees not included in the Rate Schedule attached hereto as **Exhibit F**;

7.3.4.9 Any pension or employee benefit contributions unless such sums are actually paid to, or on behalf of, an employee working on the Project not included in the Rate Schedule attached hereto as **Exhibit F**;

7.3.4.10 Any and all dues and assessments imposed on Design-Builder or any Subcontractor by construction organizations, unions, or associations, unless such dues and assessments are incurred solely due to the performance of Work and not as a penalty imposed on Design-Builder or any Subcontractor, or otherwise as a result of StadCo's actions;

7.3.4.11 Any cost incurred responding to the request for proposal, review or negotiation of the Agreement, or legal fees related to reviewing this Agreement;

7.3.4.12 Any legal cost, fees, or mediator fees incurred by Design-Builder related to any Disputes or RRCOs with StadCo for which mediation or arbitration is conducted pursuant to **Article 15** and **Article 16**; and

7.3.4.13 Any costs specifically stated in this Agreement as not reimbursable to Design-Builder or not included in the Cost of Work.

7.3.5 Notwithstanding the breakdown or categorization of any costs to be reimbursed in this **Article 7** or elsewhere in the Contract Documents, there shall be no duplication of payment if any particular item for which payment is requested can be characterized as falling into more than one of the types of compensable or reimbursable categories.

7.3.6 Whenever Design-Builder has been paid, as a Cost of the Work, amounts that are otherwise recoverable from any other source (e.g., a Subcontractor, an insurer or other third parties), Design-Builder shall diligently pursue such recovery and any recovered amounts shall be used to replenish the Design-Build Contingency as required by **Section 7.1.2.1**.

7.3.7 Except where the Cost of the Work is defined by rates, the actual Cost of the Work shall be adjusted to reflect any and all discounts, including trade and cash discounts, rebates, refunds and other similar considerations, provided that StadCo provides any funds when needed to obtain such considerations.

7.3.8 Upon Substantial Completion, Design-Builder shall submit a list of any tools, Equipment, and Materials purchased for the Project that have been paid by StadCo as a Cost of the Work. If StadCo so elects, any tools or extra Materials and/or Equipment purchased for the Project that have been paid by StadCo as a Cost of the Work shall be returned to StadCo at the end of the Project.

7.4 Preconstruction Services and Design-Builder's Fee.

7.4.1 Design-Builder shall be paid on a time a materials basis for preconstruction services, which shall be invoiced and paid on a monthly basis during preconstruction phase.

7.4.2 In addition to the payments for preconstruction services, Design-Builder shall be paid a fee equal to [redacted] (**"Design-Builder's Fee"**).

7.4.3 The Design-Builder's Fee shall be paid proportionately to the percentage of Work completed on a monthly basis.

7.4.4 Except for material changes to the Architectural Program, Design-Builder agrees it shall not be entitled to payment of Fee on the first [redacted] worth of Change Orders in excess of the GMP (**"Excess GMP"**).

7.4.5 In the event of an Excess GMP, then Design-Builder shall be entitled to an increase to the Design-Builder's Fee calculated at the rate of three point nine percent (3.9%) on the portion of the Cost of the Work which is greater than the Excess GMP.

7.5 Shared Savings.

7.5.1 If at Final Completion there are Savings, the Savings (exclusive of Savings used to fund the Warranty Management Fund) shall be allocated as follows: twenty-five percent (25%) to Design-Builder and seventy-five percent (75%) to StadCo; provided, however, in no event shall Design-Builder's portion of the Savings exceed [redacted]. The Savings shall be calculated and paid as part of the Final Payment; provided, however, that Design-Builder's share of Savings on any funds remaining in the Warranty Management Fund at the end of the Design-Build Warranty Period shall be calculated and paid to Design-Builder within thirty (30) days after the expiration of the Design-Build Warranty Period. Design-Builder shall not be entitled to any portion of the Savings if either Party terminates this Agreement. At the time of any release of Contingency, the Savings will also be calculated and paid as set forth in **Section 7.1.3**.

7.6 Accounting Records/Right to Audit.

7.6.1 StadCo will have the right, upon prior written notice to Design-Builder, to designate an independent auditor to audit from time to time the books, records, receipts, vouchers and other documentation (**"Books and Records"**) necessary to document Design-Builder's requests for payment and to verify Design-Builder's compliance with the requirements of the Contract Documents. Design-Builder shall cause such files, records and accounts of expenditures for Materials, Equipment, employees and Subcontracts and the like and other costs of rendering services or performing Work hereunder to be kept as necessary for the proper administration of the Contract Documents. Such records shall be kept on the basis of generally-accepted accounting principles and in accordance with the Contract Documents. Until the expiration of six (6) years after Final Completion, Design-Builder will make available upon the written request of StadCo or any of its duly authorized representatives, copies of any books, documents, records and other data of Design-Builder that are necessary to certify and audit the nature and extent of Cost of the Work incurred by Design-Builder in connection with the Project at Design-Builder's storage facility located at 700 Meadow Lane North, Minneapolis, MN 55422. In those situations where books, documents, records and other data have been generated from computerized data (whether mainframe, mini-computer, or PC based computer systems), StadCo shall be provided with extracts of data files in computer readable format on data disks or suitable alternative computer exchange formats. Notwithstanding anything in the Contract Documents to the contrary, any rates established in this Agreement or the GMP Amendment (or otherwise agreed to by the Parties) are not subject to audit, including labor rates, billing rates for Equipment rental, insurance rates (such as commercial general and excess liability, builder's risk, and SDI) and bond rates.

7.6.2 Design-Builder shall require all Subcontractors to comply with the provisions of this **Section 7.6** by insertion of this **"Accounting Records/Right to Audit"** provision into each respective related Subcontract and purchase order of all tiers relating to the Work.

7.6.3 StadCo's approval and payment of invoices, billings and Change Orders, shall not preclude a post-approval adjustment to the extent StadCo discovers inaccuracies in such invoices, billings or Change Orders as a result of an audit of the Books and Records, or otherwise. Specifically, StadCo shall have the right to reduce any payments to Design-Builder or any Subcontractor or Vendor by any amounts attributable to incorrect or otherwise defective cost data. If an audit inspection or examination conducted in accordance with this **Article 7** discloses overcharges of any nature by Design-Builder (or any Design Consultant, Subcontractor or Vendor), Design-Builder shall: (i) reimburse StadCo with the total amount of such overcharges; and (ii) reimburse, or cause such Subcontractor or Vendor to reimburse, StadCo for the total actual cost of StadCo's audit if such overcharge is in excess of five percent (5%) of the total invoice, including but not limited to the actual costs of outside auditors and/or the use of StadCo's internal auditor at internal billing rates. To the extent that the amount of such overcharges exceeds the remaining balance of any Retention held by StadCo in connection with the Work so audited, Design-Builder shall, within thirty (30) days after receiving written notice of the audit results, reimburse StadCo with the amount of such excess.

7.7 Progress Payments.

7.7.1 Design-Builder shall submit to StadCo Applications for Payments for Work completed as set forth below. StadCo shall make progress payments on account of the Contract Sum as provided below and elsewhere in the Contract Documents. Each Application for Payment shall be certified as accurate by Design-Builder to the best of its knowledge, consistent with the process established in **Section 7.7.5**.

7.7.2 Each Application for Payment shall be based upon the most recent Schedule of Values submitted by Design-Builder and approved by StadCo in accordance with the Contract Documents. The Schedule of Values shall allocate the entire GMP among the various portions of the Work, except that Design-Builder's Fee and the Design-Build Contingency shall be shown as separate line items.

7.7.3 Applications for Payment shall show the actual percentage completion of each portion of the Work of each trade as of the end of the period covered by the Application for Payment. Unless the GMP is a fixed price, the percentage completion shall be the lesser of (1) the percentage of that portion of the Work that has actually been completed or (2) the percentage obtained by dividing (a) the Cost of the Work that has actually been incurred by Design-Builder on account of that portion of the Work for which Design-Builder has made or intends to make actual payment prior to the next Application for Payment by (b) the share of the GMP allocated to that portion of the Work in the then current Schedule of Values. Allocations of the GMP in the Schedule of Values are for administrative purposes only and do not represent individual limits on recoverable Cost of the Work.

7.7.4 Design-Builder shall furnish with each Application for Payment the following:

7.7.4.1 a partial waiver of claims and lien (in each case consistent with Applicable Law in the forms attached hereto as **Exhibit O**) for itself effective through the date of the current application, as well as a similar waiver for each Subcontractor effective through the date of the prior application to the extent of payment received from StadCo;

7.7.4.2 Design-Builder's certification of the extent to which each portion of the Work set forth on the Schedule of Values has been completed as of the end of the time period to which the Application for Payment relates (the **"Percent Complete"**); provided, however, the Percent Complete shall be subject to verification upon review of the Work by StadCo;

7.7.4.3 the amount due for Work satisfactorily completed prior to the date of the Application for Payment, as measured by Design-Builder's direct and actual costs incurred or owed in accordance with the Cost of Work; provided, however, that the aggregate amount due to Design-Builder under any Application for Payment shall not exceed the product of multiplying (i) the GMP, by (ii) the Percent Complete as of the date of the applicable Application for Payment;

7.7.4.4 for each category and portion of the Work as shown on the Schedule of Values: (i) the amount requested on all previous Applications for Payments; (ii) the amount requested on the current Application for Payment; and (iii) the amount allocated to the Work yet to be completed;

7.7.4.5 Design-Builder's Fee earned as a result of Work that is the subject of the Application for Payment and the total of all Design-Builder's Fee paid since the Effective Date;

7.7.4.6 any amounts allocated to or from Design-Builder's Design-Build Contingency for Work that is the subject of the Application for Payment and the total amount allocated to or from Design-Build Contingency since the Commencement Date;

7.7.4.7 all amounts allocated to the Retention (defined in **Section 7.7.6**) for Work that is the subject of the Application for Payment and the aggregate of all amounts allocated to the Retention since the Effective Date;

7.7.4.8 Design-Builder's detailed Project accounting report and certified payroll ledger, as well as copies of all invoices received from Design Consultants, Subcontractors and Vendors;

7.7.4.9 a cash flow projection, illustrating the timing and sequence of expected payments to be made under the Agreement;

7.7.4.10 a statement listing (a) the names of all first and second tier Subcontractors furnishing Materials, labor, or services in connection with the Work in excess of $50,000 in the current application, (b) the Materials, labor, or services to be furnished by each such party throughout its entire Subcontract, (c) the amounts actually paid to date to each party furnishing Materials, labor, or services, and (d) the amounts due or to become due to each such party in the current application;

7.7.4.11 the updated Schedule of Values showing all committed contracts and expenses of Design-Builder to date; and

7.7.4.12 such additional information and documentation regarding the progress of the Work as StadCo may reasonably require.

7.7.5 The period covered by each Application for Payment shall be one calendar month ending on the last day of the month. On or before the 27th day of any given month, Design-Builder shall submit to and review with StadCo a preliminary, draft version of Design-Builder's Application for Payment, together with the required supporting data (the **"Pencil Draft"**). On or before the 6th day of the following month, Design-Builder and StadCo shall meet to review the Pencil Draft. Design-Builder shall revise the Pencil Draft in accordance with any objection or recommendation of StadCo that is consistent with the requirements of the Contract Documents. Such revised Pencil Draft shall be resubmitted by Design-Builder to StadCo as the Application for Payment due on or before the 9th day of the month immediately following the month in which the Pencil Draft was first submitted. On or before the last day of the month in which StadCo receives the approved Application for Payment, StadCo shall deliver to Design-Builder payment and Design-Builder shall, within the Nevada statutory requirements from Design-Builder's receipt of payment from StadCo, make available to each Subcontractor its payment for its respective application for payment. Notwithstanding the foregoing, StadCo shall endeavor to have its Lender reduce the above payment cycle to twenty (20) days.

7.7.6 Except as hereinafter provided, StadCo will retain five percent (5%) (**"Retention"**) from all payments of the Contract Sum otherwise due and payable. There shall not, however, be retainage on Design-Builder's Fee, the fees of AOR and its consultants or the Cost of the Work relating to the General Conditions Work items listed in the GMP Amendment. Upon written request of Design-Builder after satisfactory completion of the Work performed by a particular Subcontractor, StadCo may, in its reasonable discretion, release from retainage a sum sufficient to increase the total payments to 100% of the cost of the

portion of the Work performed by such Subcontractor. In addition, StadCo will give special consideration to reducing or eliminating retainage requirements for small local businesses (as defined in Section 31.5(2) of the Act) so as to encourage greater participation of such firms. Within thirty (30) Days after Substantial Completion of the Work, StadCo will release all retainage less an amount equal to the reasonable estimated cost of the remaining Punch List work or other incomplete Work. Thereafter, StadCo shall pay Design-Builder monthly the amount retained for such items as each item is completed.

7.7.7 Subject to other provisions of the Contract Documents, the amount of each progress payment shall be computed as follows:

7.7.7.1 Take that portion of the GMP properly allocable to completed Work as determined by multiplying the percentage completion of each portion of the Work by the share of the GMP allocated to that portion of the Work in the Schedule of Values. StadCo shall make payment for the estimated value of the Work authorized by a Construction Change Directive.

7.7.7.2 Add that portion of the GMP properly allocable to Materials and equipment delivered and suitably stored at the Site for subsequent incorporation in the Work or, if approved by StadCo, suitably stored off the Site at a location agreed upon in writing.

7.7.7.3 Add Design-Builder's Fee, in accordance with **Section 7.4.3** hereof.

7.7.7.4 Subtract the aggregate of previous payments made by StadCo.

7.7.7.5 Subtract the positive difference, if any, between the amount determined in **Sections 7.7.7.1** through **Section 7.7.7.4** and the Cost of the Work incurred during the current period.

7.7.7.6 Subtract retainage in accordance with **Section 7.7.6** hereof.

7.7.7.7 Subtract any overpayments from previous Applications for Payment that were inadvertently paid by StadCo or billed by Design-Builder that either Party discovered in their review of any Application for Payment.

7.7.8 Undisputed payments due but remaining unpaid shall bear compound interest at a rate per annum equal to the Prime Rate plus two percent (2%) from the date that is thirty (30) Days after the payment due date until such time payment is received by Design-Builder.

7.7.9 Discounts and Rebates. Cash discounts or rebates obtained on payments made by Design-Builder shall accrue to StadCo, and Design-Builder shall make provisions so that they can be secured. Discounts and rebates that accrue to StadCo shall be credited to StadCo as a deduction from the Cost of Work. Design-Builder shall use all commercially reasonable efforts to identify applicable discounts and rebates in connection with the Cost of Work. If Design-Builder fails to obtain such discounts or rebates, then Design-Builder shall credit StadCo with the amount of such discount or rebate.

7.7.10 Withholding. In addition to the Retention applicable thereto, StadCo may withhold all or any part of any payment otherwise due to Design-Builder, in an amount StadCo reasonably believes necessary to protect StadCo for any of the following: (i) Work not progressing in accordance with the Contract Documents; (ii) Work that is the subject of a Dispute or Action (as defined in **Section 9.1**); (iii) failure to materially comply with any other provisions of this Agreement; (iv) claims filed or when StadCo has actual notice that a claim will be filed against StadCo or the Site by any party related to Design-Builder's Agreement or related to the Work provided by Design-Builder; (v) failure of Design-Builder or a Subcontractor to make timely payments that are due and owing to its Subcontractors; (vi) to cover third-party liens filed on the property by claimants under this Agreement; (vii) the payment or otherwise of third-party liens that StadCo has actual notice will be filed against the property by claimants related to this Agreement, including but not limited to the Work or Design-Builder's Subcontractor agreements; and

(viii) any other reason permitted by Applicable Law or this Agreement. If StadCo intends to withhold any amount under this **Section 7.7.10**, then the Parties hereto shall adhere to the following procedures:

7.7.10.1 StadCo must deliver to Design-Builder, on or before the date that payment is due, a written notice (**"Notice of Withholding"**), signed by an authorized representative of StadCo and including: (a) the amount that will be withheld from Design-Builder (including any applicable Design-Builder's Fee); and (b) a reasonably detailed explanation of the reason for StadCo having withheld that amount, including, without limitation, StadCo's determination of any Work that has not been performed but for which payment is being sought by Design-Builder, and/or a specific reference to the provision or section of the applicable Contract Documents or the Applicable Laws or regulation with which Design-Builder has failed to comply, if any.

7.7.10.2 Upon Design-Builder's correction of any condition described in the Notice of Withholding as the reason for withholding payment due to Design-Builder, Design-Builder shall deliver written notice (**"Notice of Correction"**) to StadCo identifying the scope and manner of the corrective measures undertaken by Design-Builder. Upon StadCo's receipt of a Notice of Correction, StadCo shall: (a) pay to Design-Builder the amount withheld on or before the date the next payment is due to Design-Builder hereunder, if the conditions for withholding payment have been corrected to StadCo's reasonable satisfaction; or (b) deliver to Design-Builder, on or before the date the next payment is due to Design-Builder hereunder, a written notice objecting to the scope and manner of the corrective measures taken by Design-Builder and including a detailed explanation for such objection (**"Notice of Rejection"**).

7.7.10.3 If Design-Builder does not dispute the amount StadCo is withholding and authorizes StadCo in writing to backcharge Design-Builder for such amount, StadCo and the Design-Builder shall execute a deductive Change Order memorializing such withholding.

7.7.10.4 If Design Consultants, Subcontractors or Vendors have the right under any Applicable Laws to dispute, in good faith, any amount withheld under this **Section 7.7.10** or the grounds for such withholding, then, prior to enforcing any rights that Design Consultants, Subcontractors, or Vendors may have under such Applicable Laws to suspend the Work or terminate this Agreement (or part hereof) as a result of such withholding, Design-Builder shall provide StadCo with written notice setting forth, in detail, the Design Consultant's, Subcontractor's or Vendor's reasons for disputing the amount of, or grounds for, the withholding. Upon receipt of such written notice, StadCo may require Design-Builder to pay the amount in dispute to the applicable Design Consultant, Subcontractor or Vendor "under protest," and Design-Builder must pay such amount within five (5) days after receipt of written direction from StadCo, provided that such written direction is received by Design-Builder within three (3) days after Design-Builder's written notice to StadCo. If Design-Builder continues to withhold the amount in dispute (or any portion thereof) and, as a result of such withholding, the applicable Design Consultant, Subcontractor or Vendor elects to terminate its Subcontract, then Design-Builder shall be solely responsible for any and all damages payable to such Subcontractor or Vendor as a result of such termination, and such damages shall be deemed a Non-Allowable Cost of Work. StadCo's failure to issue any written instructions to Design-Builder following StadCo's receipt of a Subcontractor's or Vendor's notice of intent to terminate shall not be deemed to be StadCo's authorization to pay the amount in dispute to such Design Consultant, Subcontractor or Vendor. StadCo's election to require payment to Subcontractor or Vendor shall be for the sole purpose of avoiding potential Delay or impact to the Project and shall not be a waiver of any Design-Builder or StadCo claims against Design Consultant, Subcontractor and Vendor.

7.7.11 **Off-Site Equipment and Materials**. If Design-Builder is requesting payment for Materials and equipment stored off-Site, payment for such Materials and equipment shall be contingent upon Design-Builder providing StadCo with at least fifteen (15) days' advance written notice of Design-Builder's intention to request such payment from StadCo together with appropriate information and documentation, satisfactory to StadCo and evidencing the following (in addition to any requirements and conditions that may be imposed by Lender):

7.7.11.1 that the Materials and equipment are suitably stored off the Site in a segregated area at a location approved by StadCo in writing;

7.7.11.2 the Materials and equipment shall have clearly visible markings identifying the Materials and equipment as belonging to StadCo for use in connection with the Project;

7.7.11.3 StadCo's title to and interest in such Materials and equipment is adequately protected;

7.7.11.4 applicable insurance (with coverage limits acceptable to StadCo) for storage of the Materials and equipment of the Site, and for the transportation of the Materials and equipment to the Site, which insurance shall be evidenced by a certificate of insurance showing StadCo as a loss payee; and

7.7.11.5 date stamped photographs of such Materials and equipment stored off the Site.

7.8 Final Payment.

7.8.1 Final payment (**"Final Payment"**) shall not be due Design-Builder until it has furnished the following items to StadCo:

7.8.1.1 an affidavit that payrolls, bills for Materials and equipment, and other indebtedness (including all union dues, health, welfare, pension plan and other labor-associated contributions) connected with the Work for which StadCo, or the Project might be responsible or encumbered (less amounts withheld by StadCo) have been paid or will be paid out of the proceeds of Final Payment or Design-Builder has made satisfactory arrangements for payment;

7.8.1.2 a certificate evidencing that any insurance required to remain in force after Final Payment is currently in effect and will not be canceled or allowed to expire until at least six years (6) prior written notice has been given to StadCo;

7.8.1.3 a written statement that Design-Builder knows of no substantial reason that the insurance will not be renewable to cover the period required by the Contract Documents;

7.8.1.4 all warranties, guaranties, operations and maintenance manuals, other documentation required by the commissioning procedures, and the other Project Closeout Documents, as required by the Contract Documents;

7.8.1.5 consent of surety, if any, to final payment;

7.8.1.6 a final and complete accounting of the total aggregate Cost of Work, together with all backup documentation reasonably required by StadCo; and

7.8.1.7 a final waiver and release of mechanics' liens (conditioned upon receipt of payment) and other claims by the applicable Subcontractor that is consistent with Applicable Law.

7.8.2 Acceptance of Final Payment shall constitute a waiver of claims by Design-Builder except those previously made in writing and identified by Design-Builder as unsettled at the time of the final Application for Payment, and except for claims for contribution or indemnity arising out of future claims by third parties who are not directly or indirectly under contract with the Design-Builder.

7.8.3 Any payment made to Design-Builder under this **Article 7** shall not constitute acceptance by StadCo of the quality of the Work that is the subject of such payment, nor shall it be deemed a waiver with respect to any claims that StadCo may have with respect to such Work. The making of Final Payment shall not constitute a waiver of any claims by StadCo including, without limitation, any claims arising from or relating to: (i) liens, claims, security interests or encumbrances arising out of the Contract Documents and which are unsettled; (ii) the failure of the Work to comply with the requirements of the

Contract Documents; (iii) the terms of any express or implied warranties, or special warranties required by the Contract Documents; and (iv) an audit of Design-Builder's Design Consultants or any Subcontractor's or Vendor's books and records.

7.9 Warranty of Title.

7.9.1 Design-Builder warrants and guarantees that title to all Work, Materials, and equipment covered by an Application for Payment, regardless whether then incorporated in the Project, will pass to StadCo, upon Design-Builder's receipt of payment, free and clear of all liens, claims, security interests or encumbrances.

7.10 Project Suspension or Abandonment.

7.10.1 If the Project is suspended or abandoned in whole or in part by StadCo for more than ninety (90) Days during the preconstruction phase of the Project, or more than sixty (60) Days during the Construction Phase of the Project, then Design-Builder shall be compensated for all Work performed prior to receipt of written notice from StadCo of such suspension or abandonment, including retainage (in the case of abandonment), reasonable and actual demobilization costs, costs associated with the termination or cancellation of contracts, and Design-Builder's Fee earned to the date of such suspension or abandonment. If the Project is resumed after being suspended beyond the applicable time periods set forth above, and Design-Builder is re-engaged by StadCo, then Design-Builder's compensation shall be equitably adjusted (including any demobilization and remobilization costs). If the Project is suspended beyond the applicable time periods set forth above and later resumed, StadCo acknowledges that Design-Builder may not be able to provide continuity of all Project personnel listed in **Exhibit E** and referenced in **Section 2.9.10** and **Section 2.9.11** hereof.

ARTICLE 8. WARRANTY/CORRECTION OF WORK

The following warranty obligations (**"Design-Builder's Warranty Obligations"**) shall apply to the Work:

8.1 Design-Builder warrants and guarantees that all Materials and equipment incorporated into the Project under this Agreement shall be of good quality and new unless otherwise agreed to in writing by StadCo, and that all Work will be free from faults or defects in Materials or workmanship, and in accordance with requirements of the Contract Documents; provided, however, that all design services and other professional services shall be held only to the Standard of Care set forth in **Section 1.1.100**. Design-Builder agrees to remove or correct all Work performed by it under this Agreement that StadCo reasonably finds to be defective in material or workmanship or not in conformance with the Contract Documents within a period of one (1) year from the date of Substantial Completion of the Work (the **"Warranty Period"**). Design-Builder also agrees to remove or correct any portions of the Work that may be damaged or destroyed by such Defective Work or by the removal or correction of such Defective Work. The Work shall be completed in accordance with the following: (a) the Contract Documents and the Standard of Care set forth in **Section 1.1.100**; (b) all requirements of any warranties applicable to the Work; and (c) all Applicable Law.

8.2 Any portion of the Work not conforming to the requirements of the Contract Documents and the warranty set forth in **Section 8.1** shall be considered defective or incomplete and shall be referred to in this Agreement as **"Nonconforming Work."** Design-Builder's Warranty Obligations hereunder shall not apply to defects caused by ordinary wear and tear, lack of maintenance, abuse or misuse.

8.3 Nothing contained in this **Article 8** shall be construed to establish a period of limitation with respect to any other obligation that Design-Builder might have under the Contract Documents. The establishment of any time period after the date of Substantial Completion relates only to the specific obligation of Design-Builder to correct the Work, and does not relate to the time within which Design-Builder's obligation to comply with the Contract Documents may be sought to be enforced, nor the time

within which proceedings may be commenced to establish Design-Builder's liability with respect to its obligations.

8.4 Design-Builder shall collect all written guaranties, warranties, operations and maintenance manuals and equipment manuals from all Subcontractors and Suppliers required under the Contract Documents to be delivered to StadCo, and shall deliver them to StadCo, in a single, organized set of binders, in a form reasonably acceptable to StadCo, upon Substantial Completion of the Project.

8.5 All warranties arising from Design-Builder from this **Article 8** and elsewhere in the Contract Documents shall run directly to StadCo. All warranties and guarantees of Subcontractors, manufacturers or Suppliers shall run directly to Design-Builder and StadCo (unless provided otherwise in the Contract Documents) and shall otherwise be fully assignable to StadCo's designee (including, without limitation, any owner or tenant of the Project). Design-Builder shall provide reasonable assistance to StadCo in enforcement of long-term warranties or guaranties from manufacturers or Suppliers.

8.6 Following the correction or replacement of any of the Work, Design-Builder shall correct any defects or deficiencies in the corrected or replaced Materials and workmanship that are found within the longer of the balance of the initial one year warranty period or six (6) months after the date of correction or replacement, whichever is longer.

8.7 Upon Design-Builder's receipt of StadCo's written notice of any Nonconforming Work at any time during the course of the Work or during the Warranty Period, or such other period of time as may be prescribed by any Applicable Laws, Design-Builder shall promptly perform all corrective services (including, without limitation, furnishing all labor, Materials, equipment, and other services at the Site and elsewhere) to StadCo's reasonable satisfaction as may be necessary to remedy any defects or omissions in the Work. Such work shall be compensable as a Cost of the Work subject to the GMP.

8.8 All costs associated with the performance of Design-Builder's Warranty Obligations under this **Article 8** in excess of the GMP shall be solely Design-Builder's responsibility for which Design-Builder shall pay, including, without limitation, additional testing and inspections and compensation for the services of any professionals, consultants, or Subcontractors or Vendors made necessary thereby. Design-Builder shall, as part of Design-Builder's Warranty Obligations, repair or replace any other damaged components, material, finishes, furnishings and other Work or portions of the Project or other property damaged or affected by any defective, incomplete, or otherwise Nonconforming Work, and to return the same to their original condition.

8.9 Design-Builder shall use all commercially reasonable efforts to commence with any required corrective Work and fully perform all Design-Builder's Warranty Obligations within ten (10) days after the receipt of written notice from StadCo of Nonconforming Work. If Design-Builder's Warranty Obligations require more than ten (10) days for completion, Design-Builder shall submit, within ten (10) days after receipt of StadCo's written notice, a reasonably detailed written proposal itemizing all corrective actions necessary which Design-Builder is prepared to and shall immediately undertake and diligently pursue to enable the Work to achieve compliance with the Contract Documents, including the latest Drawings and Specifications. In performing such corrective Work, Design-Builder shall perform its Work so as to cause the least inconvenience and disruption to StadCo's business, which may require performance of Work at hours when StadCo's business is least active.

8.10 In the event Design-Builder fails to timely correct Nonconforming Work following delivery of StadCo's written notice described above, StadCo shall have the right to correct or arrange for the correction of any Nonconforming Work and the costs and expenses incurred by

8.11 StadCo shall be deducted from the GMP; and to the extent the GMP is exceeded Design-Builder shall be liable for such cost and expense. Such costs incurred by StadCo in correcting such Nonconforming Work, may include, but are not limited to, additional costs for redesigns by the architect and other design consultants, replacement Design-Builders, Materials, equipment, and all services provided by StadCo's and its manager's personnel. StadCo shall be entitled to withhold and offset all costs incurred

during any such corrective work against any funds otherwise due, or which may become payable, to Design-Builder hereunder. If payments then, or thereafter, due Design-Builder are insufficient to cover such amount, Design-Builder shall immediately, upon demand, pay the difference to StadCo.

8.12 At the time of contract close-out and as part of Final Payment, Design-Builder and StadCo shall meet and allocate a portion of any available Savings towards a warranty work account (the "Warranty Management Fund") to be maintained by StadCo. The Parties shall agree on the funding amount as part of the Application for Final Payment but the establishment of a Warranty Management Fund shall not affect the making of Final Payment pursuant to **Section 7.8**. The Warranty Management Fund shall be used to pay Costs of the Work incurred by Design-Builder in connection with performing Design-Builder's Warranty Obligations. Disbursements from the Warranty Management Fund shall be made upon the same terms and conditions applicable to all other Costs of the Work, including, without limitation, the same documentation required by this Agreement.

ARTICLE 9. INDEMNIFICATION

9.1 **General**. DESIGN-BUILDER SHALL INDEMNIFY, DEFEND, AND HOLD HARMLESS THE INDEMNITEES FROM ALL THIRD PARTY (I.E. FROM PERSONS THAT ARE NOT SIGNATORY TO THIS AGREEMENT) CLAIMS, DEMANDS, ACTIONS, ARBITRATIONS, SUITS (COLLECTIVELY REFERRED TO AS **"CLAIMS"**) AND ALL LIABILITIES TO THIRD PARTIES, SUCH AS FINES, DAMAGES, LOSSES, COSTS, AND EXPENSES, INCLUDING BUT NOT LIMITED TO, REASONABLE ATTORNEYS' FEES AND OTHER PROFESSIONALS' FEES SUBJECT TO **SECTION 9.5** (COLLECTIVELY REFERRED TO AS **"LIABILITIES"**) TO THE EXTENT SUCH CLAIMS OR LIABILITIES ARE CAUSED BY:

(a) THE NEGLIGENT ACTS OR OMISSION OF DESIGN-BUILDER, AOR, SUBCONSULTANTS, SUBCONTRACTORS, SUPPLIERS OR ANY OTHER PERSON FOR WHOM DESIGN-BUILDER IS RESPONSIBLE FOR OR LEGALLY LIABLE, THAT RESULTS IN BODILY INJURY, SICKNESS, DISEASE, OR DEATH OR INJURY TO PROPERTY OR DESTRUCTION OF PROPERTY (OTHER THAN THE WORK) IN ANY WAY RELATING TO THE PROJECT; OR

(b) DESIGN-BUILDER'S DEFAULT UNDER, BREACH OF, OR FAILURE TO PERFORM IN ACCORDANCE WITH THIS AGREEMENT.

9.1.1 NOTWITHSTANDING ANYTHING HEREIN TO THE CONTRARY, THE INDEMNITY AND DEFENSE OBLIGATIONS OF DESIGN-BUILDER SET FORTH IN THIS SECTION SHALL NOT APPLY TO CLAIMS AND LIABILITIES FOR PROFESSIONAL NEGLIGENCE THAT ARE COVERED BY **SECTION 9.4**.

9.2 **Patent Indemnification**.

9.2.1 DESIGN-BUILDER SHALL INDEMNIFY, DEFEND AND HOLD HARMLESS THE INDEMNITEES FROM AND AGAINST ANY AND ALL CLAIMS WHATSOEVER IN WHOLE OR PART CAUSED BY OR ARISING OUT OF AN INFRINGEMENT OF PATENTS OR THE IMPROPER USE OF OTHER PROPRIETARY RIGHTS THAT MAY OCCUR IN CONNECTION WITH THE PERFORMANCE OF THE WORK AND THE OWNERSHIP OR USE OF THE EQUIPMENT AND MATERIALS EXCEPTING, HOWEVER, (A) THOSE ARISING FROM PARTICULAR PRODUCTS, SYSTEMS, MATERIALS, OR EQUIPMENT SPECIFIED IN WRITING BY STADCO, AND (B) CONSEQUENTIAL DAMAGES RELATING TO SUCH CLAIMS.

9.3 **Lien Indemnification**.

9.3.1 TO THE EXTENT OF PAYMENTS MADE TO DESIGN-BUILDER, DESIGN-BUILDER SHALL INDEMNIFY, DEFEND (WITH COUNSEL REASONABLY ACCEPTABLE TO STADCO), AND HOLD HARMLESS INDEMNITEES FROM ANY CLAIMS OR MECHANIC'S LIENS BROUGHT

AGAINST STADCO OR AGAINST THE PROJECT BY ANY CONSULTANT, SUBCONTRACTORS OR VENDORS AS A RESULT OF THE FAILURE OF DESIGN-BUILDER, OR THOSE FOR WHOSE ACTS IT IS RESPONSIBLE, TO PAY FOR ANY SERVICES, MATERIALS, LABOR, EQUIPMENT, TAXES OR OTHER ITEMS OR OBLIGATIONS FURNISHED OR INCURRED FOR OR IN CONNECTION WITH THE WORK. WITHIN SEVEN (7) DAYS AFTER RECEIVING WRITTEN NOTICE FROM STADCO THAT SUCH A CLAIM OR MECHANIC'S LIEN HAS BEEN FILED, DESIGN-BUILDER SHALL COMMENCE TO TAKE THE STEPS NECESSARY TO DISCHARGE SAID CLAIM OR LIEN, INCLUDING, IF NECESSARY, THE FURNISHING OF A MECHANIC'S LIEN BOND. IF DESIGN-BUILDER FAILS TO DO SO, STADCO WILL HAVE THE RIGHT TO DISCHARGE THE CLAIM OR LIEN AND HOLD DESIGN-BUILDER LIABLE FOR COSTS AND EXPENSES INCURRED, INCLUDING ATTORNEYS' FEES AND ANY BOND PREMIUMS.

9.4 Professional Negligence Indemnification.

9.4.1 DESIGN-BUILDER SHALL REIMBURSE AND INDEMNIFY AND HOLD HARMLESS THE INDEMNITEES FROM AND AGAINST ANY AND ALL CLAIMS AND LIABILITIES CAUSED BY OR ARISING OUT OF OR INCIDENT TO DESIGN-BUILDER'S PROFESSIONAL NEGLIGENCE IN THE PERFORMANCE OF THE WORK PURSUANT TO THE STANDARD OF CARE UNDER THIS AGREEMENT. DESIGN-BUILDER SHALL NOT BE LIABLE HEREUNDER TO THE EXTENT THE ACTION IS CAUSED BY THE NEGLIGENCE OF AN INDEMNITEE. THE INDEMNIFICATION AND DEFENSE OBLIGATIONS PROVIDED BY DESIGN-BUILDER PURSUANT TO THIS AGREEMENT SHALL NOT BE CONSTRUED AS BEING FOR THE BENEFIT OF ANY CONTRACTORS, SUBCONTRACTORS, OR MATERIAL SUPPLIERS.

9.5 Defense of Indemnitees.

9.5.1 IF CLAIMS ARE ASSERTED AGAINST ANY INDEMNITEE (WHETHER OR NOT ANY ACTION, ARBITRATION, OR SUIT IS FILED) ON ANY THEORY THAT ARISES FROM OR RELATES TO, DIRECTLY OR INDIRECTLY, IN WHOLE OR IN PART, AN ALLEGATION INVOLVING ANY OF THE INDEMNIFIED MATTERS SET FORTH IN **SECTION 9.1**, **SECTION 9.2**, **SECTION 9.3**, AND **SECTION 9.7**, AND IF SUCH INDEMNITEE(S) REQUESTS DESIGN-BUILDER DEFEND INDEMNITEE(S) ON SUCH CLAIMS AND THERE IS NO ACTUAL CONFLICT, OR NO CONFLICT OF INTEREST THAT HAS NOT BEEN WAIVED, PREVENTING THE ATTORNEYS DEFENDING DESIGN-BUILDER FROM DEFENDING BOTH DESIGN-BUILDER AND THE INDEMNITEE(S), THEN DESIGN-BUILDER SHALL DEFEND THE INDEMNITEE(S) ON SUCH CLAIMS WITH LEGAL COUNSEL ACCEPTABLE TO, AND APPROVED IN ADVANCE BY THE INDEMNITEE(S), WHICH ACCEPTANCE AND APPROVAL SHALL NOT BE UNREASONABLY WITHHELD. IF A CONFLICT OF INTEREST PREVENTS THE ATTORNEYS DEFENDING DESIGN-BUILDER FROM DEFENDING BOTH DESIGN-BUILDER AND ANY INDEMNITEE, THEN SUCH INDEMNITEE SHALL RETAIN ITS OWN ATTORNEYS AND PAY FOR ITS OWN DEFENSE BUT SHALL BE ENTITLED TO REIMBURSEMENT FROM DESIGN-BUILDER OF ITS REASONABLE LEGAL FEES AND COSTS TO THE EXTENT THE CLAIM WAS CAUSED BY ANY OF THE INDEMNIFIED MATTERS SET FORTH IN **SECTION 9.1**, **SECTION 9.2**, **SECTION 9.3**, AND **SECTION 9.7**. IF DESIGN-BUILDER FAILS TO PERFORM ITS INDEMNITY AND DEFENSE OBLIGATIONS HEREIN, THE INDEMNITEES SHALL BE ENTITLED TO REIMBURSEMENT FOR ANY AND ALL REASONABLE COSTS AND FEES INCURRED TO ENFORCE DESIGN-BUILDER'S INDEMNITY AND DEFENSE OBLIGATIONS HEREIN.

9.6 Indemnification Not Limited by Worker's Compensation; Disability Benefits Act.

9.6.1 ANY CLAIMS MADE AGAINST AN INDEMNITEE BY AN EMPLOYEE OF ANY DESIGN-BUILDER PARTY OR ANYONE FOR WHOSE ACTS THEY MAY BE LIABLE, ARE INCLUDED IN THE INDEMNIFICATION OBLIGATIONS IMPOSED UPON DESIGN-BUILDER UNDER **SECTION 9.1** ABOVE AND SHALL NOT BE LIMITED BY ANY LIMITATION ON THE AMOUNT OR TYPE OF DAMAGES, COMPENSATION OR BENEFITS PAYABLE BY, OR ON BEHALF OF, ANY DESIGN-BUILDER PARTY UNDER ANY WORKER'S COMPENSATION LAWS, DISABILITY BENEFITS ACTS OR ANY OTHER EMPLOYEE BENEFIT PROVIDED BY THIS AGREEMENT, BY APPLICABLE LAW OR BY

THE AMOUNT OF ANY INSURANCE MAINTAINED OR REQUIRED TO BE MAINTAINED BY ANY DESIGN-BUILDER PARTY.

9.7 Environmental Indemnity.

9.7.1 DESIGN-BUILDER'S OBLIGATIONS TO DEFEND, INDEMNIFY, AND HOLD HARMLESS THE INDEMNITEES UNDER **SECTION 9.1** INCLUDES (BUT IS NOT LIMITED TO) ANY AND ALL TORT LIABILITY; LIABILITY ARISING UNDER STATE, FEDERAL, OR LOCAL ENVIRONMENTAL STATUTES AND REGULATIONS TO THE EXTENT ARISING OUT OF OR RESULTING FROM DESIGN-BUILDER'S NEGLIGENT ACTS OR OMISSIONS.

9.8 Exceptions.

9.8.1 NOTWITHSTANDING ANYTHING TO THE CONTRARY IN THIS **ARTICLE 9**, DESIGN-BUILDER'S DUTY TO INDEMNIFY UNDER **SECTION 9.1** AND **SECTION 9.4.1** SHALL NOT APPLY TO ANY CONSEQUENTIAL DAMAGES OF ANY THIRD-PARTY BENEFICIARIES OR INDEMNITEES EXCEPT (A) CONSEQUENTIAL DAMAGES ASSERTED AGAINST A THIRD-PARTY BENEFICIARY OR INDEMNITEE BY A PERSON WHO IS NOT A THIRD-PARTY BENEFICIARY OR AN INDEMNITEE; OR (B) TO THE EXTENT SUCH CONSEQUENTIAL DAMAGES WOULD BE RECOVERABLE BY STADCO UNDER, AND WITHIN THE LIMITS SET FORTH IN, **SECTION 5.2.5** (WHICH LIMITS SHALL APPLY TO STADCO, THE INDEMNITEES, AND THE THIRD-PARTY BENEFICIARIES IN THE AGGREGATE).

9.9 Limitation of Liability.

9.9.1 Subject to the exclusions contained in **Section 9.9.2**, Design-Builder's aggregate liability to StadCo and Indemnitees for any and all claims, losses (excluding any amounts recoverable for Delay Liquidated Damages pursuant to **Section 5.2**), costs, direct, indirect, or Consequential Damages caused by professional errors and omissions in the performance of Design-Builder's Services (as explicitly defined in **Section 1.1.91**), including Services provided by the AOR and other Persons for whom AOR is responsible for or legally liable, shall not exceed the following:

(a) to the extent the professional liability is attributable to Design-Builder separate and apart from the AOR and AOR's Consultants, Fifty Million Dollars ($50,000,000.00), plus amounts actually paid by Design-Builder's Subcontractors' professional liability insurance; and

(b) to the extent the professional liability is attributable to AOR and AOR's Consultants, the insurance proceeds actually paid to or on behalf of the Design-Builder by the applicable insurance carriers pursuant to the professional liability policies of AOR as required by **Exhibit J** of the AOR Agreement, including amounts paid by AOR's professional liability insurance or actually paid to or on behalf of any Subconsultants' professional liability insurance.

9.9.1.1 The above limitation of liability shall apply whether such Claims are pleaded in the form of negligence, professional errors or omissions, strict liability, breach of contract, or breach of warranty.

9.9.1.2 Design-Builder shall use all commercially reasonable efforts to recover all insurance proceeds available from the professional liability insurance required to be provided by Design-Builder pursuant to **Exhibit G**, the insurance proceeds available from the professional liability policies of AOR required by **Exhibit J** of the AOR Agreement, and insurance proceeds available under any subconsultants' professional liability insurance policies.

9.9.1.3 The above limitation of liability shall not apply if Design-Builder abandons the Project or is terminated for cause after being provided all opportunities to cure its defaults as allowed by this Agreement.

9.9.2 **Exclusions from the Limitation of Liability Defined in Section 9.9.1**. Notwithstanding the limitation of liability defined in **Section 9.9.1**, the following items listed below shall not be covered by and are in addition to such limitation:

(a) any amounts recoverable for Delay Liquidated Damages pursuant to **Section 5.2**;

(b) any amounts recoverable in the case of gross negligence or intentional misconduct of Design-Builder, Design-Builder's Subcontractors, Suppliers, Vendors, the AOR, and other Persons for whom Design-Builder is responsible for or legally liable; and,

(c) any amounts recoverable for Claims and Liabilities of Design-Builder arising from or related to Design-Builder's Work or the Work of Design-Builder's Subcontractors, Suppliers, Vendors, or Persons for whom Design-Builder is responsible for or legally liable (explicitly excluding Services as defined in **Section 1.1.91**, which shall remain subject to the limitation in **Section 9.9.1**).

9.9.3 In the event Design-Builder fails to continuously renew and maintain the professional liability insurance as required in **Exhibit G**, or to the extent the liability limits available to this Project under such policy are decreased by payments made on account of claims arising from other projects of Design-Builder or any of its joint venture partners, Design-Builder shall be responsible for paying any sums that would have been paid under the terms of that policy if it had been in full force and effect, less any attorneys' fees that would have otherwise been payable under the professional liability insurance.

ARTICLE 10. TERMINATION AND STADCO'S RIGHT TO PERFORM DESIGN-BUILDER'S OBLIGATIONS

10.1 Suspension and Termination by Design-Builder.

10.1.1 If StadCo fails to pay when due any amounts owed and due to Design-Builder under this Agreement in excess of Five Million Dollars ($5,000,000.00) in the aggregate, then Design-Builder may, upon ten (10) days' written notice to StadCo, during which time StadCo fails to make such payment or fails to provide reason for non-payment or withholding pursuant to this Agreement or NRS, suspend the Work. Thereafter, if StadCo fails to pay Design-Builder any amounts owed upon fifteen (15) days' written notice to StadCo and StadCo's continued failure to pay or failure to provide reason for non-payment or withholding pursuant to this Agreement or NRS, Design-Builder may terminate this Agreement and recover from StadCo payment for all Work executed and the portion of Design-Builder's Fee earned prior to the date of termination (based on the percentage of Work completed as of such date), all Cost of the Work actually and reasonably incurred by Design-Builder as a result of such termination.

10.1.2 The above remedies are in addition to the rights and remedies provided for under Sections 624.606 to 624.630 of the NRS.

10.2 StadCo's Right to Perform Design-Builder's Obligations and Termination by StadCo for Cause.

10.2.1 If Design-Builder fails to perform any if its obligations under this Agreement, StadCo may, after twenty (20) days' written notice to Design-Builder and its surety(ies), during which period Design-Builder fails to perform such obligations (including, without limitation, the obligation to maintain a safe Site), without prejudice to and cumulative of any other remedy StadCo may have, make good such deficiencies. No action taken hereunder by StadCo shall be deemed a termination of this Agreement or relieve Design-Builder from any consequences or liabilities arising from such actions or omissions. All costs and expenses incurred by StadCo in correcting such deficiencies shall be deducted from the GMP. If such costs and expenses exceed the unpaid balance of the GMP, Design-Builder shall be liable for such excess.

10.2.2 If Design-Builder is adjudged to be bankrupt, or if it makes a general assignment for the benefit of its creditors, or if a receiver is appointed on account of its insolvency, or if it fails to timely supply enough properly skilled workers or proper Materials, or if it fails to make payments owed to Subcontractors or for Materials or labor, or fails to comply with Applicable Laws, or if it otherwise breaches this Agreement, then, subject to the surety(ies) rights, StadCo may, without prejudice to any right or remedy and after giving Design-Builder and its surety(ies) ten (10) days' written notice, during which period Design-Builder fails to cure the violation (or to take adequate steps to promptly correct or cure the problem), terminate the employment of Design-Builder and take possession of the Site and of all Materials, equipment, tools, construction Equipment and machinery thereon owned and/or leased by Design-Builder and may finish the Work by whatever method that StadCo may deem expedient. In such case, Design-Builder shall not be entitled to receive any further payment until the Work is finished nor shall it be relieved from its obligations under this Agreement.

10.2.3 If StadCo terminates this Agreement pursuant to **Section 10.2.2** and then completes the Work, and the unpaid balance of the GMP exceeds the cost of finishing the Work, including StadCo's additional costs, compensation for additional services of StadCo's Consultants, and all losses, actual damages, costs and expenses, including attorney's fees, sustained or incurred by reason of Design-Builder's failure to complete the Work, StadCo shall pay Design-Builder only for the Work Design-Builder actually performed. If such cost to StadCo to complete the Work exceeds such unpaid balance, then Design-Builder shall pay the difference to StadCo upon demand. This obligation for payment shall survive the termination of this Agreement.

10.2.4 In the event that a termination by StadCo under the provisions of this **Section 10.2** shall be deemed wrongful or unjustified, then such termination shall be deemed a termination for StadCo's convenience under **Section 10.3.1** hereof and Design-Builder's sole and liquidated remedy shall be limited to the amounts payable by StadCo under **Section 10.3.1**.

10.3 Termination for Convenience.

10.3.1 In addition to any other rights StadCo may have at law or under this Agreement with respect to cancellation or termination, StadCo may, without cause and in its sole discretion, terminate this Agreement upon not less than fourteen (14) days written notice to, if StadCo determines that a termination is appropriate for its convenience. StadCo shall terminate by delivering to Design-Builder a notice of termination for convenience specifying the extent and the effective date of termination. Neither Design-Builder nor any Subcontractor, Supplier, or Materialman shall be entitled to anticipated profits on Work unperformed or on Materials or equipment unfurnished. Design-Builder shall be entitled to the following as termination expenses: (i) reimbursement for all Costs of the Work incurred by Design-Builder prior to the date of termination; (ii) reasonable costs to demobilize, provided that such costs be incurred by Design-Builder within thirty (30) Days following the effective date of the termination; (iii) payment of any Design-Builder's Fees due and payable with respect to the Cost of the Work incurred prior to the date of termination; and (iv) reasonable attorney's fees, costs, and expenses in connection with such termination.

ARTICLE 11. SUCCESSORS AND ASSIGNS

11.1 StadCo and Design-Builder, respectively, bind themselves and their successors and assigns to the other party to this Agreement.

11.2 Design-Builder may not assign, or transfer its interest in the Contract Documents or delegate its obligations thereunder, or Subcontract the Work either in part, as a whole or in the aggregate, without the prior written approval of StadCo, which may be withheld in StadCo's sole and absolute discretion.

11.3 StadCo may assign this Agreement at any time with the consent of Design-Builder, which consent shall not be unreasonably withheld or delayed (provided that Design-Builder shall have no right of consent if Design-Builder is in default hereunder at the time consent to assignment is requested, subject to any applicable notice and cure periods).

ARTICLE 12. EXTENT OF AGREEMENT

12.1 Entire Agreement.

12.1.1 This Agreement represents the entire and integrated agreement between StadCo and Design-Builder and supersedes all prior negotiations, representations or agreements, either written or oral. This Agreement may be amended only by written instrument signed by both StadCo and Design-Builder.

12.2 Third-Party Rights.

12.2.1 Except as set forth in the next sentence of this **Section 12.2.1**, nothing contained herein shall be deemed to give any third-party other than StadCo any claim or right of action against StadCo or Design-Builder that does not otherwise exist without regard to this Agreement. The Parties acknowledge and agree that the Lender and the Stadium Authority are intended Third-Party Beneficiaries under this Agreement (collectively, the **"Third-Party Beneficiaries"**) and that each of the Third-Party Beneficiaries shall have an independent right to enforce the terms of this Agreement. The rights of the Third-Party Beneficiaries established under this Agreement shall be subject to the same exceptions, limitations, and waivers as are applicable to StadCo's rights under this Agreement.

ARTICLE 13. INSURANCE/BONDS

13.1 Design-Builder's Insurance.

13.1.1 Design-Builder shall purchase and maintain, at its own expense, the types of insurance set forth on **Exhibit G** attached hereto, with limits of coverage as set forth on said **Exhibit G**. Design-Builder shall purchase such insurance from companies that are rated at a minimum A-VII by Best's Key Rating Guide and shall maintain such insurance through and until the expiration of all applicable statutes of limitation and statues of repose applicable to the Work.

13.2 Bonds.

13.2.1 If required by StadCo, Design-Builder shall submit to StadCo an irrevocable performance and payment bond (the **"Bond"**) for the Work, in compliance with the requirements specified in **Exhibit G** or a parent guaranty in lieu of a Bond.

13.2.2 Design-Builder shall provide subcontractor default insurance (**"SDI"**) in lieu of traditional bonding for the Project. The premium cost for the SDI shall be charged as a Cost of the Work, at the rate of 1.5% (one and a half percent), and shall not be included for the purpose of calculating Design-Builder's Fee.

13.2.3 For Subcontractors not enrolled in the SDI program, Design-Builder shall procure payment and performance bonds for Subcontractors and/or Vendors performing Work on the Site as directed by StadCo. The cost of procuring payment and performance bonds shall be compensable and considered a Cost of Work as set forth in **Section 7.3.2**, provided that such bonds are consistent with market prices. Design-Builder may, upon prior written approval from StadCo, elect to not procure payment and performance bonds for certain Subcontractors. Design-Builder shall cause StadCo, Lender, and all Third-Party Beneficiaries to be named as additional obliges on all such bonds.

13.3 StadCo Insurance.

13.3.1 StadCo has procured and will administer an Owner Controlled Insurance Program (**"OCIP"**). The OCIP manual is attached hereto as **Exhibit H**. Design-Builder shall participate in and require the eligible consultants, Subcontractors, and Vendors to participate in the OCIP.

13.3.2 StadCo shall procure and maintain the Contractor's Pollution Liability insurance described in **Exhibit G** attached hereto.

13.3.3 StadCo shall procure and maintain the Builder's Risk (inland marine) commercial property insurance described in **Exhibit G** attached hereto.

ARTICLE 14. CHANGES AND RENEWED REQUESTS FOR CHANGE ORDERS

14.1 Change Orders.

14.1.1 All Change Orders shall be executed in writing by StadCo and Design-Builder and shall contain a description of the changes, and any adjustments of the GMP, Guaranteed Substantial Completion Date and any other modification to this Agreement.

14.2 Changes Directed by StadCo.

14.2.1 StadCo may direct a change that would alter, add to or deduct from the scope of Work, by submitting to Design-Builder a written request setting forth in reasonable detail the nature of the requested change. If Design-Builder determines that such change directed by StadCo will: (a) increase or decrease Design-Builder's cost of performing the Work; (b) adversely affect or enhance Design-Builder's ability to meet the Guaranteed Substantial Completion Date; or (c) adversely affect Design-Builder's ability to comply with the warranties provided in this Agreement, then Design-Builder shall furnish StadCo with the information specified in **Section 14.3** hereof with respect to such changed Work. If StadCo then elects to proceed with the changed Work, then it shall issue a written Change Order to Design-Builder authorizing such modification as shall have been agreed to by StadCo and Design-Builder.

14.3 Changes other than StadCo-Directed Changes; RRCOs and Notice.

14.3.1 Adjustment to GMP The Parties agree Design-Builder shall be entitled to an increase in the GMP and/or an extension of the Guaranteed Substantial Completion Date to the extent (a) there is an event outside of Design-Builder's control that impacts the critical path of the Project and then only to the extent that the Delay affects the critical path, unless Design-Builder can demonstrate a greater impact to the Master Project Schedule; or (b) there is a change caused by or requested by StadCo that materially alters the scope of Work as expressed in the GMP Amendment; or (c) there occurs any of the events listed in **Section 4.1.2**, **Section 5.3**, or **Section 6.4.1**; and (d) any other provision of this Agreement that expressly entitles Design-Builder to a Change Order. If Design-Builder believes it is entitled to an extension of time or additional compensation, then Design-Builder shall pursue all such requests for Change Orders in accordance with the requirements of this **Article 14**. If StadCo and Design-Builder cannot agree on an adjustment to the GMP or extension of time at issue in any requests for Change Orders, then the requests for Change Order shall be submitted to dispute resolution as provided in this Agreement and become a RRCO. Notwithstanding the foregoing, however, the Parties expressly agree that the Design-Builder's rights and remedies in this **Article 14** and **Article 15** are in addition to and do not limit any of Design-Builder's rights and remedies provided for under Sections 624.606 to 624.630 of the NRS.

14.3.2 Procedure for RRCOs and Notice Requirements. Each Party shall give written notice to the other of any RRCO within the timeframes specified in this Agreement, or if no timeframe is specified, a reasonable time after discovery of the circumstances giving rise to the RRCO.

14.3.2.1 Any RRCO for extension of time or any RRCO for additional compensation shall, to the extent practicable, specify the length of delay in the Guaranteed Substantial Completion Date and, as applicable, the additional compensation claimed. If it is impracticable to specify the length of such delay or amount of the RRCO at the time the notice is delivered, then Design-Builder shall provide StadCo with periodic supplemental notices during the period over which the event continues. Such supplemental notices shall keep StadCo informed of any change, development, progress or other

relevant information concerning the event of which Design-Builder is aware. Notice shall be given within twenty-one (21) Days after Design-Builder became aware of such RRCO.

14.3.2.2 Notwithstanding the foregoing or anything to the contrary in the Contract Documents, the Parties agree that notice given by either Party in accordance with change management procedures established by Design-Builder and approved by StadCo shall satisfy the requirements of this **Section 14.3.2** and any other provision of the Contract Documents or Applicable Law that requires notice of a RRCO.

14.3.3 Concealed, Unknown or Unforeseen Conditions. If conditions are encountered at the Site that are (1) subsurface or otherwise concealed physical conditions that differ materially from those indicated in the Contract Documents, (2) unknown physical conditions of an unusual nature, that differ materially from those ordinarily found to exist and generally recognized as inherent in construction activities of the character provided for in the Contract Documents, or (3) unforeseen as of the execution of the GMP Amendment, then notice by the observing party shall be given to the other party promptly before conditions are disturbed (to the extent practicable) and in no event later than twenty-one (21) days after first observance of the conditions. StadCo will promptly investigate such conditions and, if they differ materially and cause an increase in the cost of, or time required for, performance of any part of the Work, Design-Builder shall be entitled to an adjustment in the GMP or Master Project Schedule (inclusive of the Guaranteed Substantial Completion Date), or both, and shall submit a RRCO to StadCo for such adjustments pursuant to **Section 14.3.2** (provided that Design-Builder shall not be deemed to have been made aware of such RRCO until after StadCo has given written notice of its decision). If StadCo determines that the conditions at the Site are not materially different from those indicated in the Contract Documents and that no change is justified, then StadCo shall so notify Design-Builder in writing, stating the reasons, Design-Builder may then immediately purse its RRCO through the dispute resolution provisions of **Article 15**.

14.3.4 Human Remains and Archaeological Artifacts. If, in the course of the Work, the Design-Builder or any Subcontractor encounters human remains or recognizes the existence of burial markers, archaeological sites or wetlands not indicated in the Contract Documents, the Design-Builder shall suspend any operations that would affect them and shall notify StadCo. Upon receipt of such notice, StadCo shall promptly take any action necessary to obtain Governmental Authorization required to resume the operations. The Design-Builder shall continue to suspend such operations until otherwise instructed by StadCo but shall continue with all other operations that do not affect those remains or features. Design-Builder shall be entitled to an adjustment to the extent any operations are affected or impacted by such events. Requests for adjustments in the Contract Sum and Contract Time arising from the existence of such remains or features shall be made as RRCOs pursuant to **Section 14.3.1** and **Section 14.3.2** (provided that Design-Builder shall not be deemed to have been made aware of such RRCO until StadCo notifies Design-Builder or its intended actions).

14.3.5 StadCo Review of RRCO Notices. StadCo shall promptly review each RRCO for extension of time or RRCO for additional compensation proposed by Design-Builder, and shall, no later than thirty (30) days after receipt of such RRCO, either (a) issue a Change Order to Design-Builder adjusting the Contract Sum or GMP, as applicable, or (b) pursuant to Section 624.610 of the NRS, issue a written notice to Design-Builder setting forth in detail the reasons why the RRCO for a Change Order was denied.

14.4 Performance of Changed Work. If the Parties are unable to agree on the final adjustment to the GMP or Master Project Schedule applicable to a Change Order, and if directed by StadCo, then Design-Builder shall proceed to perform such changed Work so long as Design-Builder is paid on a time and Materials basis in accordance with the pricing set forth in **Exhibit I**. If the Parties cannot ultimately reach an agreement, then either Party may refer the issue to dispute resolution as provided in this Agreement.

14.4.1 Price and Schedule Adjustments for Change Order Work. Each Change Order incorporating the agreed GMP adjustment shall be accompanied by a modified payment schedule reflecting

such adjustment and each Change Order incorporating the agreed extension of the Guaranteed Substantial Completion Date shall be accompanied by a modified Master Project Schedule reflecting such adjustment.

GENERAL PROVISIONS APPLYING TO ARTICLES 15 AND 16

Dispute Resolution Acknowledgement. The Parties, except to the extent expressly reserved in this Agreement, agree to utilize an alternative dispute resolution process for any and all RRCOs (as defined in **Section 1.1.84**) and Disputes (as defined in **Section 1.1.42**) that arise from or relate to the Work and this Agreement. The Parties agree that all Disputes and all RRCOs will be subject to the process outlined in **Article 15** and **Article 16**. The Parties have evaluated the attributes associated with resolving RRCOs and Disputes through an alternative dispute resolution process, in comparison to resolving RRCOs and Disputes in a court of competent jurisdiction; and the Parties have affirmatively, intentionally, knowingly and voluntarily agreed that **Article 15** and **Article 16** accurately describe how all RRCOs and Disputes arising from the Work, the Project, or this Agreement will be addressed, managed and resolved. Each of the Parties hereto further acknowledges and agrees it has reviewed or had the opportunity to review its decision to adopt the alternative dispute resolution process contained in **Article 15** and **Article 16** with its respective legal counsel, and that it affirmatively agrees to utilize the process outlined **Article 15** and **Article 16** to resolve any and all RRCOs and Disputes. All settlements and resolutions of any kind obtained pursuant to **Article 15** or **Article 16**, including but not limited to settlements related to any RRCOs or Dispute, shall only be valid and binding if they are agreed to in writing by the Parties.

____ StadCo **____ Design-Builder**

ACKNOWLEDGEMENT OF PROCESS AND PROCEDURES. AS A RESULT OF THE PARTIES' ELECTION TO RESOLVE ALL RRCOS AND DISPUTES PURSUANT TO **ARTICLES 15** AND **16**, EACH OF THE PARTIES HERETO HEREBY IRREVOCABLY WAIVES ITS RIGHT TO A JURY TRIAL OF ANY RRCO, DISPUTE, OR CAUSE OF ACTION ARISING OUT OF OR RELATING TO THIS AGREEMENT, THE WORK, THE PROJECT OR ANY DEALINGS BETWEEN THE PARTIES HERETO RELATING TO THE SUBJECT MATTER HEREOF. THE SCOPE OF THIS WAIVER IS INTENDED TO BE ALL-ENCOMPASSING OF ANY AND ALL RRCOS AND DISPUTES THAT COULD HAVE BEEN FILED IN ANY COURT AND THAT COULD RELATE TO THE SUBJECT MATTER OF THIS AGREEMENT, THE WORK, OR THE PROJECT, INCLUDING, BUT NOT LIMITED TO, CONTRACT CLAIMS, EQUITABLE CLAIMS, TORT CLAIMS, BREACH OF DUTY CLAIMS, AND ALL OTHER COMMON LAW AND STATUTORY CLAIMS. EACH OF THE PARTIES HERETO ACKNOWLEDGES THAT THIS WAIVER IS A MATERIAL INDUCEMENT TO ENTER INTO THIS AGREEMENT. EACH OF THE PARTIES HERETO HEREBY FURTHER ACKNOWLEDGES AND AGREES THAT IT HAS REVIEWED OR HAD THE OPPORTUNITY TO REVIEW THIS WAIVER WITH ITS RESPECTIVE LEGAL COUNSEL, AND THAT IT KNOWINGLY AND VOLUNTARILY WAIVES ITS JURY TRIAL RIGHTS FOLLOWING CONSULTATION WITH SUCH LEGAL COUNSEL.

____ StadCo **____ Design-Builder**

ARTICLE 15. NOTICE OF RENEWED REQUEST FOR CHANGE ORDERS AND DISPUTES

15.1 Work Continuance and Payment. Unless otherwise agreed in writing and except as provided in **Section 10.1.1**, Design-Builder shall continue to perform its obligations under this Agreement and pursue Final Completion of the Work in accordance with the Schedule of the Work during any dispute resolution proceedings initiated pursuant to this Section. If Design-Builder continues to perform its full and complete obligations hereunder, StadCo shall continue to make payments of all undisputed amounts in accordance with this Agreement.

15.2 **Notice of RRCO**. If the Design-Builder disputes StadCo's decision to deny a Change Order pursuant to **Section 14.3.2** the subject matter thereof shall be deemed a Renewed Request for Change Order (**"Renewed Request for Change Order"** or **"RRCO"**) and Design-Builder shall submit a notice of RRCO (**"Notice of RRCO"**) to StadCo and StadCo's Representative within twenty-one (21) days after a denial of a Change Order.

15.2.1 Design-Builder agrees and acknowledges if it fails to submit a Notice of RRCO within this timeframe it is accepting and agreeing to StadCo's denial of the Change Order. Design-Builder agrees it shall have no further rights to appeal and shall not seek further adjudication or resolution of such RRCO.

15.2.2 Design-Builder shall submit separate Notices of RRCO for each discrete issue and Design-Builder shall not combine two or more discrete issues into a single Notice of RRCO.

15.2.3 A Notice of RRCO shall include, at a minimum, the following information related to the relief sought by the Design-Builder: (i) the basis for the RRCO; (ii) the amount of dollars requested; (iii) additional time and schedule adjustment requested; (iv) Agreement provisions that support the relief sought in the RRCO; and (v) companies involved or affected by the facts underlying the RRCO.

15.3 **Notice of Dispute**.

15.3.1 The Party submitting a Notice of Dispute shall submit separate Notices of Dispute for each discrete issue and the Party shall not combine two or more discrete issues into a single Notice of Dispute.

15.3.2 A Notice of Dispute shall include, at a minimum, the following information related to the relief sought by the Party: (i) the basis for the Dispute; (ii) the amount of dollars requested, if applicable; (iii) additional time and schedule adjustment requested, if applicable; (iv) Agreement provisions that support the relief sought in the Dispute; and (v) companies involved or affected by the facts underlying the Dispute, if applicable.

15.4 **Good Faith Negotiations**. Upon receipt of a Notice of RRCO under **Section 15.2**, or a Notice of Dispute under **Section 15.3**, the Parties shall meet at the Project Site for the purpose of resolving the RRCO or Dispute through the following good faith negotiation process:

15.4.1 Every calendar month, except as otherwise agreed by StadCo and Design-Builder in writing, the senior representatives of StadCo, Design-Builder, Architect, StadCo's Representative, and such other parties as deemed appropriate by StadCo shall meet at the Project Site to discuss the current status of the Construction Cost Budget, Master Project Schedule, and other Project issues, including any outstanding RRCOs and Disputes (**"Executive Meeting"**). If there are any outstanding RRCOs or Disputes to be discussed, the Parties shall attempt to resolve such RRCOs at the Executive Meeting. To the extent that discussion or negotiations over any RRCOs and Disputes are not resolved during an Executive Meeting, the Parties shall continue to work toward a mutually acceptable resolution of any such unresolved RRCOs and Disputes.

15.4.2 If a RRCO is not resolved within sixty (60) days after the date the Notice of RRCO was initially delivered, then StadCo shall issue a written Denial of RRCO outlining: (a) any portion of the RRCO StadCo denies, (b) the basis for such denial, (c) Agreement provisions that support the denial, (d) Persons with knowledge of the facts underlying the denial, and (e) any offsetting or mitigating circumstances (**"Denial of RRCO"**). Failure of StadCo to issue a written Denial of RRCO shall be deemed to be a Denial of RRCO. In the event StadCo does not provide a Denial of RRCO and mediation is requested, StadCo shall provide Design-Builder a Denial of RRCO fifteen (15) days prior to mediation. In no event shall a Request for Mediation occur more than one hundred and five (105) days after the date the Notice of RRCO was initially delivered.

15.4.3 If the Design-Builder disputes a Denial of RRCO under **Section 15.4.2**, the Design-Builder must submit a Notice of Dispute of RRCO Denial and Request for Mediation to StadCo, with a copy to StadCo's Representative.

15.4.4 In the event a Dispute is not resolved within sixty (60) days after the date of the Executive Meeting during which such Dispute was discussed, or if a Dispute is not resolved within hundred and five (105) days after the date the Notice of Dispute was initially delivered, whichever first occurs, then a Party may submit a Request for Mediation to the other Party.

15.4.5 Within seven (7) days after such submission, the Parties shall coordinate selection of a mediator and mediation date through JAMS Dispute Resolution.

15.4.6 Design-Builder understands if it fails to submit a Notice of RRCO or Request for Mediation within one hundred and five (105) days after the date of the Notice of RRCO was initially delivered, it is accepting and agreeing to StadCo's Denial of RRCO, unless the Parties otherwise agree to modify this Section in writing.

15.5 Mandatory Mediation Process and Selection of Mediator.

15.5.1 Upon receipt of a Request for Mediation, the Parties shall coordinate selection of a mediator mutually agreeable to the Design-Builder and StadCo from the following list: (1) Ty Laurie of NADN, Chicago, Illinois; (2) Kenneth Gibbs of JAMS, Los Angeles, California; (3) Bruce Edwards of JAMS, Las Vegas, Nevada; or (4) Hon. Daniel Weinstein of JAMS, San Francisco, California. The Parties shall coordinate setting a date to mediate such Dispute within ninety (90) days of the Request for Mediation, unless otherwise mutually agreed to by the Parties.

15.5.1.1 A Request for Mediation shall include the following information: (i) the Change Proposal or Notice of Correction, as the case may be; (ii) StadCo's applicable Denial of a Change Proposal or Notice of Rejection; (iii) the Notice of RRCO or Notice of Dispute and all backup documentation included with the Notice of RRCO or Notice of Dispute; and (iv) a legal memorandum of Points and Authorities, if applicable.

15.5.1.2 A separate Request for Mediation shall be submitted for each Denial of RRCO or Notice of Dispute. The Parties may combine more than one RRCO or Dispute into a single Mediation if confirmed by mutual written agreement.

15.5.2 Within twenty (20) days after receipt of a Request for Mediation, the responding party shall submit a written response, including all facts, documents, and legal authorities in support of its position.

15.5.3 Both Design-Builder and StadCo shall attend any mediation with a business representative physically present who has full settlement authority and with any project representatives with knowledge necessary to resolve such RRCO or Dispute.

15.5.4 Design-Builder and StadCo shall equally divide any fees associated with mediation, including the mediator fees and the administrative fees. In the event that Design-Builder fails to pay its portion of the mediation fees within thirty (30) days from the date of request, StadCo shall withhold such fees from Design-Builder's next application for payment.

15.5.5 If Mediation does not result in the complete resolution of a RRCO or Dispute and either Party desires to seek further relief or remedies related to an unresolved RRCO or Dispute, then the Party shall deliver to the other Party a Notice of Unresolved RRCO or Dispute within twenty (20) days after the Mediation concludes.

15.6 Notice of Intent to Arbitrate.

15.6.1 Either Party may seek further resolution by requesting binding arbitration (**"Arbitration"**), within twenty (20) days after receipt of the Notice of Unresolved RRCO or Dispute. Any Arbitration shall proceed as provided herein and in accordance with the arbitration procedure outlined in **Article 16**.

15.6.2 To encourage the timely resolution of RRCOs or Disputes, the Parties agree they will comply with the timeframes outlined in **Article 15** and **Article 16**, and shall timely commence any Arbitration, if necessary, to effectuate the final and binding resolution of any RRCO or Dispute within the timeframes identified herein. If additional RRCOs or Disputes arise after commencement of an Arbitration, those RRCOs or Disputes shall be resolved separate from the pending Arbitration(s) in accordance with the Mediation and Arbitration provisions of **Article 15** and **Article 16**. The Parties understand and agree each RRCO or Dispute shall be pursued in a separate and distinct Arbitration (unless consolidated as described below); and that multiple Arbitrations for distinct RRCOs or Disputes may be active at same time.

15.6.3 Failure of Design-Builder to File a Notice of Intent to Arbitrate as outlined in this Section 15.6 shall constitute an abandonment of such RRCO, unless otherwise mutually agreed to in writing.

15.7 Nevada Statutory Remedies (Chapters 108 and 624). Nothing in **Article 15** or **Article 16** shall limit any rights or remedies any party may have under NRS Chapters 108 and 624.

15.7.1 In the event a Contractor or Subcontractor seeks to file a mechanic's lien under NRS Chapter 108, the Contractor or Subcontractor shall abide by the time frames to file such notice and foreclose such notice outlined in NRS Chapter 108.

15.7.2 Pursuant to this Agreement, any action commenced in any court pursuant to NRS Chapter 108 shall be stayed pending the results of Arbitration pursuant to this Agreement.

15.7.2.1 Any Party filing an action outside of the Arbitration process outlined in this Agreement shall complete all necessary tasks to stay any court actions until a final Arbitration award has been published.

15.7.2.2 Upon the conclusion of any Arbitration, any prevailing claimant shall present the Arbitration decision (including all offsets for payments received) to the appropriate court and request foreclosure of the mechanic's lien, if any, in accordance with the result of any Arbitration decision.

15.7.3 Nothing in **Article 15** or **Article 16** seeks to require any contractor to waive, release, or extinguish any claim or right that any contractor may otherwise possess or acquire under NRS 108.2453 or NRS 624.622 that cannot by law be waived, released or extinguished, including rights to: (i) file a mechanic's lien or other right authorized under NRS 108.221 to 108.246; or (ii) claim for delay, acceleration, disruption or impact damages or an extension of time for delays incurred, arising from any delay, acceleration, disruption or impact event which was unreasonable under the circumstances, not within the contemplation of the Parties at the time the Agreement was entered into, or for which any contractor is not responsible. Rather, the procedures in **Article 15** and **Article 16** establish a mutually acceptable forum to resolve any such Disputes or RRCOs throughout the course of design and construction so that any such Disputes and RRCOs do not accumulate or remain unresolved until the end of the Project. To the extent that any Party contends any provision of this Agreement violates any provision of the Laws, including but not limited to any section of NRS Chapters 108 or 624, the Parties agree to submit such Dispute to Arbitration for declaratory judgment in accordance with the procedure provided in **Article 16**.

ARTICLE 16. BINDING ARBITRATION

16.1 Meet and Confer Process. In the event a RRCO or Dispute cannot be resolved through an Executive Meeting or Mediation above, any Dispute or RRCO between Design-Builder and StadCo arising out of or related to this Agreement shall initially be presented in writing to the other Party pursuant to the Specific Arbitration Procedures set forth in **Exhibit N**. Subject to **Section 16.3**, the resolution of such RRCO or Dispute shall first be subject to the following meet and confer process:

16.1.1 for a period of seven (7) days after the Dispute is presented, discussions shall be held between the principal decision maker(s) of Design-Builder and StadCo (as designated by the respective Parties) in an effort to resolve the RRCO or Dispute; or

16.1.2 if the RRCO or Dispute is not resolved and reduced to a written settlement agreement within such seven (7) day period, then either Party may request arbitration as provided below.

16.2 Binding Arbitration. StadCo and Design-Builder agree that, subject to **Section 16.3** below, any Dispute or RRCO arising out of or relating to this Agreement or the breach, termination, enforcement, interpretation or validity thereof, including the determination of the scope or applicability of this Agreement to arbitrate, and which cannot be resolved pursuant to **Section 16.1** above, shall be submitted to JAMS, or its successor, for final and binding arbitration. Multiple Arbitrations may be simultaneously pending, each involving a different RRCO, Dispute, or consolidated RRCOs or Disputes. The provisions of this **Article 16** shall apply to each Arbitration. All Arbitrations shall be final and binding and shall be conducted at a location determined by the Arbitrator (as defined below) in Clark County, Nevada.

16.2.1 The Parties acknowledge and agree that during the course of the Project, RRCOs or Disputes may arise from time to time which have a small dollar value and that it would not be an efficient use of the Parties' respective resources to arbitrate each such RRCO or Dispute individually. Therefore, notwithstanding anything to the contrary in this **Section 16.2** or elsewhere in this Agreement, neither Party shall have the right or obligation, prior to Substantial Completion or the earlier termination of this Agreement, to initiate arbitration proceedings against the other unless the aggregate amount of such Party's RRCO(s) or Dispute(s) is at least Two Hundred Thousand Dollars ($200,000.00). All RRCOs or Disputes that are not in excess of this threshold shall be subject to **Article 15**, but preserved until such time as the Party elects to pursue such RRCO or Dispute.

16.2.2 The arbitration will be administered by and in accordance with the rules set forth in **Section 16.6** below and otherwise in accordance with the Engineering and Construction Arbitration Rules and Procedures developed by JAMS. To the degree there is a conflict, the rules and procedures set forth in this Agreement shall take precedence over any JAMS Engineering and Construction Arbitration Rules and Procedures.

16.2.3 The award issued by the Arbitrator shall be final, and judgment may be entered upon it in accordance with applicable law in any court having jurisdiction thereof. Either Party shall retain the right to enforce these arbitration provisions in a court of appropriate jurisdiction.

16.3 Injunctive or Equitable Relief. StadCo and Design-Builder expressly agree that notwithstanding the agreement to arbitrate included herein, the Parties shall have the right to seek injunctive or equitable relief as specifically set forth herein from a Court of competent jurisdiction in order to protect from irreparable harm and that StadCo's exercise of such rights shall not be considered, or construed to waive, impair, or release the agreement to arbitrate set forth herein regarding any other aspect of any RRCO or Dispute that arise from the Work and this Agreement.

16.4 Commencement of Arbitration.

16.4.1 Either Party may commence the arbitration process called for in this Agreement by filing a written demand for arbitration (a **"Demand for Arbitration"**) with the JAMS office located at 3800 Howard Hughes Parkway, 11th Floor, Las Vegas, Nevada 89169, with a copy to the other Party to the Agreement, as follows:

16.4.1.1 The Party filing a notice of Demand for Arbitration must assert in the demand all RRCOs and Disputes then known to that Party on which arbitration is permitted to be demanded. A Demand for Arbitration may not be made after the date when the institution of legal or equitable proceedings based on the RRCO or Dispute would be barred by the applicable statute of limitations. For statute of limitations purposes, receipt of a Demand for Arbitration by JAMS shall constitute the institution of legal or equitable proceedings based on the RRCO or Dispute.

16.5 **Selection of Arbitrator; Number and Eligibility of Arbitrators; Fees**. The Parties shall cooperate with JAMS and with one another in selecting one or more arbitrators as mutually agreed to by the Parties to adjudicate Disputes pursuant to this **Article 16**.

16.5.1 **Number of Arbitrators**:

16.5.1.1 For Disputes involving a RRCO(s) or Dispute(s) in an amount less than Two Million Five Hundred Thousand Dollars ($2,500,000), one (1) arbitrator (**"Arbitrator"**) shall be selected to preside over the proceeding.

16.5.1.2 For Disputes involving a RRCO(s) or Dispute(s) in an amount equal to or greater than Two Million Five Hundred Thousand Dollars ($2,500,000), three (3) arbitrators (**"Arbitrators or Arbitration Panel"**) shall be selected to preside over the proceeding

16.5.1.3 Any Dispute regarding the number of Arbitrators to hear a given RRCO or Dispute shall be determined by a single Arbitrator appointed by JAMS, on an expedited basis.

16.5.2 Within ten (10) days after receiving a list of Arbitrators from JAMS, the Parties shall select the Arbitrator(s) from JAMS', each Party shall select their preferred Arbitrators and submit to JAMS. If the Parties are unable or unwilling to agree on the Arbitrator, JAMS shall select the Arbitrator(s).

16.5.3 The Arbitrator's fees and other costs in connection with any such arbitration proceeding shall initially be shared equally among the Parties to such proceeding, but shall be subject to reallocation by the Arbitrator in accordance with any other provision under this Agreement.

16.6 **Administration of Arbitration**. All Arbitrations shall be administered by JAMS pursuant to its Engineering and Construction Arbitration Rules and Procedures and pursuant to the rules and procedures set forth in this Agreement.

16.6.1 Arbitration is commenced by the filing of a Demand for Arbitration as authorized by **Section 16.4** with JAMS.

16.6.2 Judgment to enforce any final Arbitration award (the **"Final Award"**) may be entered in any court having jurisdiction.

16.6.3 The Final Award in any Arbitration shall award to the prevailing Party or Parties in the arbitration that Party's reasonable legal fees and costs, including but not limited to the fees and costs charged by the Arbitrator(s).

16.6.4 Arbitrators shall utilize applicable statutes in Title 4, Witnesses and Evidence, of the NRS.

16.6.5 Arbitrators shall enforce Rule 68 of the Nevada Rules of Civil Procedure and Chapter 17 of the NRS to the extent any Offers of Judgment are served on the Parties.

16.7 **Flow Down Provision**. The Design-Builder and its Subcontractors, Vendors, and consultants shall be bound by the terms of this Agreement to the extent the provisions of this Agreement apply to the work of the Subcontractor, Vendors, and consultants.

16.7.1 Specifically, Design-Builder shall cause all contracts relating to the Work (including, without limitation, all Subcontracts) to include in twelve-point bold font (to be initialed by both Parties thereto): (i) the arbitration provisions set forth in this **Article 16** such that all claims or controversies arising out of or relating to any such contract shall be governed by such provisions; and (ii) the acknowledgement and agreement of each party to such contracts to allow joinder to and consolidation with any arbitration proceedings initiated pursuant to this Agreement. If Design-Builder: (a) fails to ensure that such arbitration provisions are included in any such contract and a Dispute arises with respect to work, services or Materials provided pursuant to such contract; and (b) StadCo is made a party to a lawsuit relating to such Dispute and is unable to compel the filing party to arbitrate its claims, then Design-Builder shall reimburse StadCo for all legal fees and costs incurred by them in connection with the defense of any such lawsuit. Nothing herein shall be construed as prohibiting Design-Builder and its Subcontractors, Vendors, and consultants from using dispute resolution procedures different from those set forth in this **Article 16** where the dispute or controversy does not involve StadCo or a claim that would be presented to StadCo.

ARTICLE 17. MISCELLANEOUS PROVISIONS

17.1 This Agreement shall be governed by the laws of the State of Nevada without regard to principles of conflicts of law. Any litigation under this Agreement shall be brought in any court having proper jurisdiction that is located in the County, and all Parties hereto consent to personal jurisdiction and venue in such court.

17.2 If any provision of this Agreement is held to be unenforceable, no other provision shall be affected thereby, and the remainder of the Agreement shall be interpreted as if it did not contain the unenforceable provision.

17.3 The captions contained in this Agreement are for convenience and reference only and in no way define, describe, extend or limit the scope or intent of this Agreement or the intent of any provision contained herein.

17.4 Any notice, demand, offer, or other written instrument required or permitted to be given pursuant to this Agreement shall be in writing signed by the Party giving such notice and shall be hand delivered or sent by overnight courier, messenger or registered letter, email or fax, to the other Party at the address set forth below:

If delivered to StadCo:

LV Stadium Events Company, LLC
6623 Las Vegas Blvd. South, Suite 380
Las Vegas, NV 89119
Attn.: Don Webb

With a copy to:

(a) Oakland Raiders
1220 Harbor Bay Parkway
Alameda, CA 94502
Attn: Dan Ventrelle

(b) Holland & Hart
9555 Hillwood Drive
Las Vegas, NV 89134
Attn: Greg Gilbert

If delivered to Design-Builder:

Mortenson-McCarthy Las Vegas Stadium, a Joint Venture
700 Meadow Lane North
Minneapolis, Minnesota 55422
Attn: John V. Wood, Senior Vice President

With a copy to:

(a) M. A. Mortenson Company
700 Meadow Lane North
Minneapolis, Minnesota 55422
Attn: Dwight A. Larson, SVP & General Counsel

(b) McCarthy Building Companies, Inc.
6225 No. 24th Street, Ste. 200
Phoenix, Arizona 85016
Attn: Alison Stahl, Regional Counsel

Each Party shall have the right to change the place to which notice shall be sent or delivered by sending a similar notice to the others in like manner. The effective date of any notice issued pursuant to this Agreement shall be as of the addressee's receipt of such notice. Any notice given by fax shall also be deposited in regular U.S. mail (or more expedient delivery) no later than the next business day after the fax was sent.

17.5 All exhibits, schedules or other attachments referenced in this Agreement are hereby incorporated into this Agreement by such reference as if fully rewritten herein and are deemed to be an integral part of this Agreement.

17.6 Design-Builder is an independent contractor and shall not be deemed an agent, employee or partner of StadCo. Nothing contained in this Agreement shall be construed as constituting a joint venture or partnership between Design-Builder and StadCo.

17.7 This Agreement may be executed by the Parties in separate counterparts, each of which when so executed and delivered shall be an original, but all such counterparts shall together constitute but one and the same instrument. The counterparts of this Agreement may be executed and delivered by facsimile or other electronic signature by any of the Parties to any other Party and the receiving Party may rely on the receipt of such document so executed and delivered by facsimile or other electronic means as if the original had been received.

17.8 Except as otherwise provided herein, all rights and remedies provided in this Agreement are in addition to all other rights and remedies available at law or in equity.

17.9 Design-Builder and StadCo each has full power and authority to enter into this Agreement and the Persons signing on behalf of the respective Parties hereto are authorized to do so.

17.10 Design-Builder shall not, without the express prior written consent of StadCo, which consent may be withheld in StadCo's sole discretion, advertise, publish, issue a press release or otherwise make known (i) its affiliation with the Project, StadCo and/or (ii) any aspect of the Project, including but not limited to, representations of the design of the Project, including photographs of the exterior or interior (hereinafter, **"Prohibited Advertising"**). Additionally, Design-Builder shall not, without the express prior

written consent of StadCo, include representations of the Project, including photographs of the exterior or interior, among Design-Builder's promotional materials, or otherwise publish press releases or make known Design-Builder's involvement with the Project or affiliation with StadCo (**"Prohibited Publicity"**). Design-Builder hereby represents and agrees that it will not engage in, nor permit any consultant, agent, servant, employee, Subcontractor or representative to engage in, any Prohibited Publicity or Prohibited Advertising. Design-Builder's materials shall not include confidential or proprietary information of StadCo, any Third-Party Beneficiary, or their respective Affiliates.

17.11 Notwithstanding the provisions of **Article 16** herein, in the event of any action or proceeding at law or in equity between StadCo and Design-Builder to enforce or interpret any provision of the Contract Documents, the unsuccessful Party to such action or proceeding shall pay to the prevailing Party all costs and expenses, including without limitation reasonable legal fees and expenses (including, without limitation, fees, costs and expenses of experts and consultants), incurred in connection with such action or proceeding and in any appeal in connection therewith. If such prevailing Party obtains a judgment in any such action, proceeding or appeal, such costs, expenses and legal fees shall be included in and as a part of such judgment.

17.12 Except as expressly authorized in this Agreement, because of the special experience Design-Builder has represented it has and the unique nature of the services Design-Builder will render under the Contract Documents, Design-Builder shall not assign, or transfer its interest in the Contract Documents or delegate its obligations thereunder, or Subcontract the Work either in part, as a whole or in the aggregate, without the prior written approval of StadCo, which may be withheld in StadCo's sole and absolute discretion. Any purported assignment or transfer without such prior approval shall be null and void. StadCo has relied upon the ownership and control of Design-Builder as a material condition in determining to award this Agreement to Design-Builder. Any change in control or beneficial interest in Design-Builder, including but not limited to any sale of Design-Builder or its interests to another entity, shall give StadCo, in its sole and absolute discretion, the option to immediately terminate this Agreement. StadCo may, at any time upon notice to Design-Builder, but without Design-Builder's prior approval, assign or transfer this Agreement or delegate all or some of its rights and obligations hereunder to: (i) an Affiliate or subsidiary of StadCo; (ii) an entity that acquires all or substantially all of StadCo's interest in the Project; or all or substantially all of the assets of StadCo, or (iii) a lender in connection with providing financing for the Project. So long as StadCo's assignee or transferee assumes all StadCo's obligations and liabilities under the Contract Documents, StadCo shall be released from its obligations and liabilities under the Contract Documents from and after the date of such assignment or transfer.

17.13 Design-Builder understands, acknowledges, and agrees that StadCo may require certain Materials, Equipment, fixtures, systems, or other property from a Project sponsor (**"Sponsor Materials"**) be used in connection with the Work. As applicable, Design-Builder shall use reasonable efforts to cause AOR to review the Sponsor Materials and confirm the Sponsor Materials conform to the Contract Drawings and Specifications. If directed by StadCo, Design-Builder further agrees that, in StadCo's sole discretion, Design-Builder shall use or cause its Subcontractors to use the Sponsor Materials in the construction of the Project. Such Sponsor Materials may be provided in kind, at no out-of-pocket expense to Design-Builder, or at a preferred price below the fair market value of like Materials, in which case only the actual cost, if any, of such Sponsor Materials shall be payable to Design-Builder as a Cost of the Work. To the extent that installation of the Sponsor Materials increases the cost of, or time required for, performance of any part of the Work, then Design-Builder shall be entitled to an adjustment in the GMP and the Master Project Schedule. Design-Builder's Fee related to any Sponsor Materials provided in kind or at reduced costs and used in the Project shall not exceed the lesser of (a) the amount set forth in the GMP for such Materials, and (b) the fair market value of such Materials as reasonably demonstrated by StadCo. Upon StadCo's request, Design-Builder shall, and shall cause its Subcontractors to, meet with any sponsor to discuss other opportunities for use of such sponsor's tools, services, and products beyond the use in the Project.

ARTICLE 18. OWNERSHIP OF DOCUMENTS

18.1 **StadCo's Documents**. Design-Builder agrees that the design of the Project, all Design Documents, Construction Documents, models, renderings, presentation materials and other work product

required to be delivered by Design-Builder pursuant to this Agreement (the foregoing are collectively referred to as **"Design-Builder Work Product"**), together with all intellectual property (rights including copyrights) to the Design-builder Work Product, shall be considered "work for hire," shall be the property of StadCo and shall be owned "royalty-free" by StadCo, whether the Project is constructed or not, provided StadCo pays amounts due under this Agreement. Without limitation to the foregoing, StadCo shall hold, and Design-Builder shall be deemed to have irrevocably assigned to StadCo in perpetuity with no reserved or retained rights in any other Person or entities, all common law, statutory and other reserved rights, including the copyrights to the Design-Builder Work Product. Therefore, StadCo shall have the right to assign all ownership rights to the Design-Builder Work Product, including, but not limited to, assignment to any applicable Governmental Authority and assignments for security purposes to any Construction Lender. StadCo hereby grants to Design-Builder and the Design-Builder's Subcontractors and Design Consultants a license, revocable at the will of StadCo, to use and copy the Design-Builder Work Product during the term of this Agreement, for the sole purpose of performing the Work required under this Agreement. In the event of any infringement by a third-party of the Material copyrights, Design-Builder shall at the request of StadCo cooperate with StadCo in the enforcement of such copyrights against the infringer, and StadCo shall bear the expenses of any such enforcement requested by StadCo. Design-Builder shall not use any the Design-Builder Work Product for any reason other than in furtherance of the Project on behalf of StadCo without the prior written consent of StadCo. Notwithstanding anything contained herein to the contrary, any and all existing tools, systems, or information owned and used by Design-Builder or Design-Builder's Subcontractors and Design Consultants to provide Work hereunder, including computer software (object code and source code), know-how, methodologies, equipment, or processes, and the intellectual property inherent therein and appurtenant thereto, shall remain the sole and exclusive property of Design-Builder or Design-Builder's Subcontractors or Design Consultants.

18.2 **Use of Documents**. Without intending to limit in any way StadCo's rights of ownership, Design-Builder acknowledges that by virtue of StadCo's ownership of the Design-Builder Work Product: (a) StadCo may use the Design-Builder Work Product in expansions, additions, renovations and remodelings of the Project, all without any obligation to pay any additional compensation to Design-Builder, (b) StadCo may use the Design-Builder Work Product to reconstruct or restore the Project in case of any damage or destruction of the Project, and (c) in the event of a termination of this Agreement prior to completion of the Work, StadCo may use the Design-Builder Work Product through the date of termination for purposes of completion of the Project and may have another architect finish the design and Construction Documents and utilize any or all the Design-Builder Work Product with respect to the Project for such purposes. Unless Design-Builder is engaged to design any expansions, additions, or remodelings of the Project or update the Construction Documents and provide contract administration for any restoration or reconstruction in the case of damage or destruction, Design-Builder shall have no liability for the use of the Design-Builder Work Product for such expansions, additions or remodelings, restoration or reconstruction, and Design-Builder and Design-Builder's Subcontractors or Design Consultants shall be indemnified and held harmless from any claims, liabilities, losses, damages, costs and expenses, including but not limited to attorney's fees, court costs and litigation expenses and liabilities to third parties by the Person so utilizing the Design-Builder Work Product arising out of such use of the design features of the Project or such use of the Construction Documents for such restoration or reconstruction or for any modifications made to the Construction Documents without the written verification or adaptation by Design-Builder for the intended purpose. Design-Builder shall not use or recreate any distinctive original features of the exterior design of the Project material to the image of the Project in the design of any other buildings or projects by Design-Builder without the prior approval of StadCo. If requested by Design-Builder at any time following Substantial Completion, StadCo will identify in writing to Design-Builder, including drawings or photos where appropriate, any features of the exterior design of the Project which StadCo reasonably considers to be material to the image of the Project and distinctive within sixty (60) days after receipt by StadCo of a request therefor from Design-Builder, and StadCo shall thereafter be estopped from claiming that any other exterior design feature of the Project not so identified to Design-Builder is a material and distinctive feature of the exterior design of the Project. However, StadCo's determination respecting the materiality of any exterior design feature to the image of the Project shall not be conclusive. Design-Builder and Design-Builder's Subcontractors or Design Consultants may (a) retain copies, including reproducible copies, of the Design-Builder Work Product for its records, but shall not use the Design-Builder Work Product in their entirety for other projects, (b) display photos, renderings and models of the Project in its offices, and (c) with StadCo's

prior written approval, use portions of the Design-Builder Work Product for educational and marketing purposes. Notwithstanding anything contained herein to the contrary, any use or reuse of Design-Builder's and Design-Builder's Subcontractors' or Design Consultants' deliverables by StadCo or any third-party other than the specific purpose intended under this Agreement will be at the user's sole risk and without legal exposure to Design-Builder and Design-Builder's Subcontractors or Design Consultants. StadCo shall indemnify and hold harmless Design-Builder from any claims, liabilities, losses, damages, costs and expenses, including, but not limited to, attorney's fees, court costs and litigation expenses and liabilities arising out of such use or reuse by StadCo or any third-party.

18.3 **No Lien Claims**. Design-Builder represents and warrants to StadCo that all Design-Builder Work Product will be, at the time of delivery, free and clear of any and all liens, claims, or rights of any type whatsoever, and the production or exploitation of the materials in the exercise of StadCo's rights hereunder will not infringe upon the intellectual property rights of any other Person. Design-Builder will obtain a written release or assignment from any Person required to make this representation and warranty true, complete and correct, or to otherwise permit Design-Builder to assign all rights to the StadCo Documents to StadCo.

18.4 **Termination**. In the event of termination of this Agreement by either party for any reason, Design-Builder shall promptly provide to StadCo all Design-Builder Work Product prepared to the date of termination. Any Dispute regarding the amount of any payment to be made by StadCo under this Agreement shall not diminish the rights of StadCo to own, receive and use such documents as provided herein.

18.5 **Nevada Administrative Code Sect. 623.780**. Notwithstanding anything in this Section to the contrary, Design-Builder shall retain ownership rights in the Design Documents in accordance with NAC § 623.780, including, but not limited to, the requirements that (i) all drawings and specifications remain the property of the design professional, and copies of the drawings and specifications retained by StadCo may be utilized only for his or her use and for occupying the Project for which they were prepared, and not for the construction of any other Project and (ii) that the AOR shall retain possession of all original plans, drawings and specifications issued for official use; the plans, drawings and specifications must be printed on paper or stored in an electronic form.

18.6 **Grant of License No Other License**. If the rights granted to StadCo pursuant to **Section 18.1** of this Agreement are deemed unenforceable for any reason, Design-Builder grants to StadCo a perpetual, irrevocable, and royalty-free exclusive license to use and reproduce Design-Builder's Instruments of Service, as that term is used by the AIA, for purposes including, but not limited to, constructing, using, operating and maintaining the Project. Design-Builder shall obtain similar exclusive licenses from Design-Builder's Subcontractors consistent with this Agreement. Except for the licenses granted above, no other license or right shall be deemed granted or implied under this Agreement.

18.7 Lead Design Architect shall provide Design-Builder all Design Documents, CADD Documents and Technical Specifications in an acceptable CADD format (or in such other medium or format as necessary to be utilized with the BIM model), along with all calculations and other pertinent data related to the design for use by either Design-Builder, its Subcontractors, or AOR.

18.8 Notwithstanding any provisions of the Contract Documents to the contrary, StadCo acknowledges and agrees that StadCo shall have no ownership, title, license, or other rights to any intellectual property (including, without limitation, copyrights, patents, trademarks, trade secrets, know-how, and other proprietary rights) that was either (a) owned, controlled, or developed on or before February 20, 2017, by or on behalf of Design-Builder, any Subcontractor, or any Sub-subcontractor or (b) was created outside the scope of services hereunder (the **"Background IP"**), by or on behalf of Design-Builder, AOR or any Subcontractor, even if the Background IP was used in developing within any of the Design Documents prepared by or on behalf of Design-Builder for the Project and regardless of whether the Background IP has been registered with the appropriate governing body having jurisdiction, is protected under common law, has been reduced to practice, has been perfected, or otherwise. Design-Builder grants StadCo a non-revocable, non-exclusive, non-transferable, perpetual license to use the Background IP as expressed in the Design Documents for any purpose and without any obligation to pay additional compensation to Design-Builder.

[SIGNATURES ON NEXT PAGE]

This Agreement is entered into as of the date first above written.

STADCO:

LV STADIUM EVENTS COMPANY, LLC

By: _____
Name: _____
Title: _____

[Signatures continued on next page]

DESIGN-BUILDER:

MORTENSON-MCCARTHY LAS VEGAS STADIUM,
A JOINT VENTURE
M. A. Mortenson Company,
a Minnesota Corporation, (0072732)

By: _____
Name: _____
Title: _____

MORTENSON-MCCARTHY LAS VEGAS STADIUM,
A JOINT VENTURE
McCarthy Building Companies, Inc.,
a Missouri Corporation (0066125)

By: _____
Name: _____
Title: _____

[End of signature pages]

LIST OF EXHIBITS

EXHIBIT A	Responsibility Matrix
EXHIBIT B	Design-Builder's Procurement Plan
EXHIBIT C	Form of Amendment Establishing Guaranteed Maximum Price
EXHIBIT D	Monthly Pay Application Schedule
EXHIBIT E	Design-Builder's Key Personnel
EXHIBIT F	Rate Schedule of Project Staff, Rates for Labor, and Equipment Rate Schedule
EXHIBIT G	Insurance Requirements
EXHIBIT H	OCIP Manual
EXHIBIT I	Change Order Pricing
EXHIBIT J	Site Boundaries
EXHIBIT K	Master Project Schedule
EXHIBIT L	Parent Guaranty or Payment and Performance Bond
EXHIBIT M	BIM Implementation Plan
EXHIBIT N	Specific Arbitration Procedures
EXHIBIT O	Release of Claims or Liens Forms
EXHIBIT P	Travel Policy
EXHIBIT Q	Community Benefits Plan
EXHIBIT R	Architect of Record Assumption and Assignment Agreement

[Remainder of this page intentionally blank]

EXHIBIT A

Responsibility Matrix

Included in the GMP Amendment.

EXHIBIT B

Design-Builder's Procurement Plan

Subcontract Procurement Process
Las Vegas Stadium

Introduction

The Mortenson | McCarthy Joint Venture (MMcJV) team will award Subcontracts to Trade Partners using a competitive best value selection process, as described below. Subcontracts will be awarded based on a determination of the proposal that will provide the best value to the Project, taking into account price, ability to meet schedule, financial strength, safety record, organizational strength, team members to be assigned to the Project, community benefits approach, and Local Small Business Enterprise (SBE) participation and other criteria that may be identified in the applicable request for proposal. The MMcJV team will obtain the approval of Stadco for any deviations from these processes.

Designer Assist Target Value Budget Procurement

1. Overview
    a. This process will be used for the procurement of Designer Assist Trade Partners for the Las Vegas Stadium, which will provide preconstruction services, including design document review and input related to price, schedule, and constructability, and budgeting efforts at different milestones throughout preconstruction including providing input for the establishment of a Target Value Budget (TVB) (to the extent it may change from that set forth in the subcontract) that may be used for creating the overall budget of the cost estimate. Based on the overall performance of preconstruction services by the Design Assist Trade Partners and their ability to maintain or beat the established TVB, the selected trade partner may or may not continue into the Construction Services portion of the Work.
2. Procurement Process
    a. The Design Assist Trade Partner procurement process will consist of the following steps for each Subcontract Category:
        i. Request for Proposal (RFP) Documents will be prepared and will include the following items:
            1. Proposal Requirements which introduce the project and the purpose behind the RFP, and overview of the proposal requirements including instructions to proposers and the criteria to be used for selection.
            2. The Confidentiality Agreement and Non-Disclosure Agreement will be provided to interested firms prior to obtaining full document packages and must be executed and returned to the MMcJV team.
            3. Some or all of the following General Contracting Requirements for Subcontractors may be included as needed:
                a. Draft Version of Mortenson | McCarthy Joint Venture Subcontract Agreement

b. Supplemental Terms and Conditions
c. Site Logistics Plan
d. Exhibit A.0 - Designer Assist Scope of Work
e. Exhibit C - Project Schedule
f. Exhibit D - Contract Documents
g. Exhibit E - Project Safety & Health Programs
    i. Site-Specific Safety and Health Plan
    ii. Zero Injury Training Project Manual
h. Exhibit F – Quality Program Requirements
i. Exhibit G – Community Benefits Program / SBE & Workforce Requirements.
j. Exhibit H – Project Labor Agreement & Collective Bargaining / Prevailing Wage Rates
k. Exhibit I – Insurance Requirements and Controlled Insurance Program (CIP)
l. Exhibit J – VDC / BIM
m. Exhibit K – Subcontractor Default Insurance (SDI)

4. Subcontractor Category (SC) Scope of Work & Proposal Forms, as needed.
5. A proposed TVB or other pricing information.
6. Plans, specifications, narratives and any other pertinent information regarding the Subcontractor Category.

ii. Advertising and Public Notices

1. Notices of each Request for Proposal will be placed in the Las Vegas Review Journal (minimum of once per week) and some or all of the following
    a. El Tiempo – (Spanish language local newspaper, published weekly on Wednesday's)
    b. Construction Notebook (Published weekly on Fridays)
    c. Local Nevada Plan Rooms
2. Local Design Assist Trade Partners and Specific Specialty trade partners may also be notified via iSQFT, an online Solicitation Service.
    a. Trade Partners, Small Business Enterprises (SBE's) and others that have signed up through the project website www.mmcjvlv.com may be notified via iSQFT using the information provided under the Vendors tab provided.
3. Selected Local Small Business and Disadvantaged groups will be notified regarding the Request for Proposal.

4. Proposals will be due no sooner than 20 calendar days after the first notice is published in the Las Vegas Review Journal.

iii. Proposal Pre-Bid Meeting
    1. A non-mandatory Pre-bid Meeting may or may not be held within 7-14 days of the 1st publication in the Las Vegas Review Journal.
        a. The time and place will be announced in the advertisement with instructions to RSVP if interested in attending.
        b. Anyone interested in attending will be welcome.
        c. The Pre-Bid Meeting consists of high level information regarding the overall project, project logistics and schedule, bid process and proposal requirements, Community Benefits and Small Business Requirement, Nevada Certificate of Eligibility.
        d. Question and Answer Session will be held at the end of the meeting for anyone to ask questions regarding the project or Procurement Package.

iv. Proposal Submissions
    1. MMcJV may request hard copies and an electronic copy of the RFP response be submitted at the specified location, time and date indicated.
        a. Late submissions may or may not be accepted at the discretion of the MMcJV Team. They may be marked late and may be taken into consideration if less than 3 complete proposals are received for a specific Subcontractor Category.
        b. Submissions will be opened privately by the MMcJV team and copies of the submissions will be made available to the owner's representatives.
        c. If requested by owner, owner or its representatives may be present at all submission openings.

v. Proposal Evaluations
    1. Proposals will be evaluated by the MMCJV Team with input from the Design Team. Each submission will be scored by participating members of the MMcJV Team and the Design Team.
        a. Regarding the Nevada Certificate of Eligibility for Preference, 5 points out of the 100 available for the proposal response will be awarded to each proposer that includes the certificate issued by the Nevada State Contractors Board and is valid at the time of submission.
    2. Points for each submission will be averaged across all those reviewing the proposal responses.

3. All proposers are prohibited from engaging in bid-shopping, in the event bid-shopping is discovered, the proposer shall be disqualified from the bidding process.

vi. Interview Evaluations

1. A short list (2 or more) of proposers with the potential to provide the best value to the Project may be created and those shortlisted proposers may be invited to be interviewed by the MMcJV Team, in some cases with participation by Design Team and owners representatives.
    a. The purpose of the interviews is to gather information relevant to the evaluation of the proposals and, if necessary, to check for and reconcile any scope differences among proposers.
    b. Prior to the interview, each firm may be contacted with the interview expectations and items that need to be specifically addressed when they attend the meetings.

2. After each interview those in attendance will be asked to rank the interviews for each of the interviewed proposers.
    a. If interviews are held, a maximum of 25 points will be available to be awarded to each firm based on the numbers of interviews held and the rank of each firm interviewed.
3. After the interviews have been completed, each short-listed proposer may be asked by the MMcJV Team to respond to a list of follow-up items prior to final selection.

vii. Best and Final Offer

1. Each short-listed proposer interviewed will be asked to submit a Best and Final Offer of the TVB. Each short-listed proposers Best and Final Offer will be awarded points based on how close, as a percentage, the firm is to the MMcJV Team budget as per the table below:

Price Points	
% over Budget	**Point Value**
<=2%	25
>2%, <=4%	20
>4%, <=6%	15
>6%, <=8%	10
>8%, <=10%	5
>10%	0

viii. Proposer Recommendations

1. The total scores for each proposer are tallied with:
    a. 100 Points available for the Proposal Response
    b. 25 Points available for the Interview (if held)
    c. 25 Points available for the Best and Final Offer
2. MMcJV will make a determination of the short-listed proposer that offers the best value to the Project based on the criteria identified in the Request for Proposal. The point scoring described above will be used as a guide but will not be used solely in making that determination.
3. MMcJV will notify StadCo of its intention to award a contract to the proposer it has determined will provide the best value to the project. MMcJV's determination will be subject to the approval of StadCo, which approval will not be unreasonably withheld and will be given (or not) within seven days.

ix. Award as a Design Assist Trade Partner

1. An award to the selected proposer will be made for preconstruction services only.

2. If the selected Trade Partner, in providing updated cost estimates as a part of its preconstruction services, is unable to maintain or improve upon the TVB, then MMcJV may elect, in its discretion, to a), obtain new competitive proposals from other firms that originally competed for the work, (some or all) or b), to re- advertise the bid package and re-solicit new proposals. If the latter option is chosen at the conclusion of the design assist period and the design has progressed satisfactorily to MMcJV, then proposals will be solicited under the Design/Bid/Build Procurement process that is described elsewhere herein.

Design / Bid / Build Procurement

1. Overview

This process is intended for procurement of Subcontractor Trade Partners for the Las Vegas Stadium to provide Construction Services other than those selected under the Designer Assist Target Value Budget Procurement process set forth above.

2. Procurement Process
    a. The Subcontractor Trade Partner procurement process will consist of the following steps for each Subcontractor Category:
        i. Request for Proposal (RFP) Documents will be prepared and will include the following items:
            1. Proposal Requirements which introduce the project and the purpose behind the RFP, and overview of the proposal requirements including instructions to proposers and how proposals will be evaluated.
            2. The Confidentiality Agreement and Non-Disclosure Agreement will be provided to interested firms prior to obtaining full document packages and must be executed and returned to the MMcJV team.
            3. Some or all of the following General Contracting Requirements for Subcontractors are to be included as needed:
                a. Draft Version of Mortenson | McCarthy Joint Venture Subcontract Agreement
                b. Supplemental Terms and Conditions
                c. Site Logistics Plan
                d. Exhibit A – Scope of Work (for contract)
                e. Exhibit B – Subcontract Price (for contract)
                f. Exhibit C - Project Schedule
                g. Exhibit D - Contract Documents
                h. Exhibit E - Project Safety & Health Programs
                    i. Site-Specific Safety and Health Plan
                    ii. Zero Injury Training Project Manual
                i. Exhibit F – Quality Program Requirements
                j. Exhibit G – Community Benefits Program / SBE & Workforce Requirements
                k. Exhibit H – Project Labor Agreement & Collective Bargaining / Prevailing Wage Rates
                l. Exhibit I – Insurance Requirements and Controlled Insurance Program (CIP)
                m. Exhibit J – VDC / BIM
                n. Exhibit K – Subcontractor Default Insurance (SDI)

4. Subcontractor Category (SC) Scopes of Work & Proposal Forms
    a. Scopes of Work (Exhibit A) and Proposal Forms (Exhibit B) are prepared for each procurement package and issued with the proposal documents for Trade Partners. The MMcJV team may elect to ask for Lump Sum Prices, Unit Prices or other items as it deems necessary to procure the work associated with each Subcontractor Category.
    b. The Subcontractor Categories is issued for proposals based on the project schedule and as deemed necessary by the MMcJV team and the current needs of the project.
5. Plans, specifications, narratives and any other pertinent information regarding the Subcontractor Category.

ii. Advertising and Public Notices

1. Notices of each Request for Proposal will be placed in the Las Vegas Journal (minimum of once per week) and some or all of the following:

    a. El Tiempo (Advertisements will be published on Wednesdays during the proposal period.)

    b. Construction Notebook (Published weekly on Fridays)

    c. Local Nevada Plan Rooms.

2. Based on the Subcontractor Categories currently available for bidding Subcontractor Trade Partners will be notified via iSQFT an online Solicitation Service.
    a. Trade Partners, Small Business Enterprises (SBE's) and others that have signed up through the project website www.mmcjvlv.com will be notified via iSQFT using the information provided under the Vendors tab provided.

3. Local Small Business and Disadvantaged groups may be notified regarding the Request for Proposal.

4. Proposals will be due no sooner than 20 calendar days after the first notice is published in the Las Vegas Review Journal.

iii. Proposal Pre-Bid Meeting

1. A non-mandatory Pre-bid Meeting may be held at the discretion of the MMcJV team within 7-14 days of the 1st publication in the Las Vegas Review Journal.

a. The time and place will be announced in the advertisement with instructions to RSVP if interested in attending.
b. Anyone interested in attending will be welcome.
c. The Pre-Bid Meeting may consist of high level information regarding the overall project, project logistics and schedule, bid process and proposal requirements, Community Benefits and Small Business Requirement, Nevada Certificate of Eligibility.
d. A Question and Answer Session may be held at the end of the meeting for anyone to ask questions regarding the project or Procurement Package.

iv. Proposal Submissions
1. MMcJV will request hard copies and an electronic copy of the RFP response be submitted at the specified location, time and date indicated.
a. Late submissions may or may not be accepted at the discretion of the MMcJV Team. They may be marked late and taken into consideration if less than 3 complete proposals are received for a specific Subcontractor Category.
b. Submissions will be opened privately by the MMcJV team and copies of the submissions will be made available to the owner's representatives.
c. If requested by owner, owner or its representatives may be present at all submission openings.

v. Proposal Evaluations and Selections
1. Proposals will be evaluated by the MMCJV Team.
2. Proposers will be evaluated individually against the scope of work, completeness of the proposals, safety record, acceptance of the contract, proposed pricing, any Nevada Certificate of Eligibility provided, and any Local Small Business Enterprise (SBE) participation that may be provided.
3. Subcontractors may be invited to participate in in-person interviews or conference calls, at the discretion of the MMcJV team.
a. The purpose of the interviews or conference calls, if held, is to gather information relevant to the evaluation of the proposals and, if necessary, to check for and reconcile any scope differences among proposers
3. After the interviews or conference calls (if any) have been completed, each firm interviewed may be asked for a Best and Final Offer to be submitted along with any other follow-up information requested by the MMcJV Team for final evaluation of the proposal.

4. Credit will also be given for the firm's community benefits approach and meeting the required minimum 15% Local Small Business Enterprise (SBE) participation.
    a. MMcJV Reserves the right to select the vendor or trade partner that most closely aligns with requirements for the SBE participation with the Senate Bill 1.
5. For proposers to receive preference the Nevada Certificate of Eligibility for the subcontractor must be included with the proposal submission at time of bid.
    a. The certificate must be issued by the Nevada State Contractors Board and be valid at the time of proposal submission.
6. Proposers who submit a valid Certificate of Eligibility at the time of bid will be given a 5% advantage on the final evaluated price over those proposers that do not provide a Certificate of Eligibility.
7. All proposers are prohibited from engaging in bid-shopping, in the event bid-shopping is discovered, the proposer shall be disqualified from the bidding process.

vi. Proposer Recommendations
    1. MMcJV will make a determination of the proposer that offers the best value to the Project based on the criteria identified in the Request for Proposal.
    2. MMcJV will notify StadCo of its intention to award a contract to the proposer it has determined will provide the best value to the project. MMcJV's determination will be subject to the approval of StadCo, which approval will not be unreasonably withheld and will be given (or not) within seven days

EXHIBIT C

Form of Amendment Establishing Guaranteed Maximum Price

AMENDMENT NO. 1 TO GUARANTEED MAXIMUM PRICE DESIGN-BUILD AGREEMENT

Pursuant to **Section 4.6** of the Guaranteed Maximum Price Design-Build Agreement (the **"Agreement"**) dated as of February 20, 2017, by and between LV Stadium Events Company, LLC (**"StadCo"**) and Mortenson-McCarthy Las Vegas Stadium, a Joint Venture (**"Design-Builder"**) (individually a **"Party"** and together the **"Parties"**), StadCo and Design-Builder desire to establish a GMP for the Work described in the Agreement and enter into this Amendment No. 1 to the Agreement (the **"Amendment"**). Therefore, StadCo and Design-Builder agree as follows:

ARTICLE 1, GUARANTEED MAXIMUM PRICE

A. Design-Builder's GMP for the Work described in the Agreement (the **"GMP"**) is an amount equal to the Cost of the Work, Design-Builder's Fee, and Design-Build Contingency, not to exceed _____. The following Attachments and supplemental reference documents, which shall not be inconsistent with this Amendment No. 1, are a part of the Agreement as if each were physically incorporated therein:

i. **ATTACHMENT A**: GMP Cost Itemization, dated _____, and supplemental reference documents.

ii. **ATTACHMENT B**: GMP Drawings, dated _____, and supplemental reference documents.

iii. **ATTACHMENT C**: GMP Specifications & Prose Statement, dated _____, and supplemental reference documents.

iv. **ATTACHMENT D**: Construction Schedule, dated _____, and supplemental reference documents.

v. **ATTACHMENT E**: GMP Clarifications and supplemental reference documents.

vi. **ATTACHMENT F**: Responsibility Matrix and supplemental reference documents.

ARTICLE 2, DATE OF SUBSTANTIAL COMPLETION

A. The Guaranteed Substantial Completion Date is _____. The Project Schedule indicates that a Certificate of Occupancy will be received by _____.

ARTICLE 3, MISCELLANEOUS

A. The Parties acknowledge that the GMP is subject to the GMP Qualifications and Assumptions and that the GMP and the Contract Time will be adjusted, in accordance with **Article 14**, to the extent any of the events or circumstances noted in GMP Qualifications and Assumptions are triggered.

B. By execution of this Amendment, Design-Builder and StadCo acknowledge that, as of the date of this Amendment, both Parties are not aware of, and have not reserved, any Claims against the other Party.

C. Capitalized words and phrases herein shall have the same meanings as are ascribed to such words in the Agreement.

D. Any failure of Design-Builder to take the actions described and acknowledged in **Section 2.9.16** of the Agreement will not relieve Design-Builder from responsibility for estimating the difficulty and cost of successfully performing its Work or for proceeding to successfully perform its Work without additional expense to StadCo. StadCo shall provide to Design-Builder all information in StadCo's possession or control relating to the Site, including any geotechnical soils report and environmental reports.

This Amendment is entered as of the ____ day of _____.

STADCO:

LV STADIUM EVENTS COMPANY, LLC

By: _____
Name: _____
Title: _____

DESIGN-BUILDER:

**MORTENSON-MCCARTHY LAS VEGAS STADIUM,
A JOINT VENTURE**

By: _____
Name: _____
Title: _____

EXHIBIT D

Monthly Pay Application Schedule

LV Raider Stadium
Monthly Draw Schedule

Billing Month	Draw #	All Invoices Due to ICON	Comments due to MMcJV	Pencil Draft Review ICON, JV, JLL	Final Pay App to ICON	Raiders Approval Needed	Draw Pkg sent to JLL	JLL Submits to Bank	Bank Funds Draw	Raiders Cuts Checks
November '17	4	11/27	12/1	12/4	12/8	12/13	12/14	12/21	12/29	1/1
December '17	5	12/22	12/29	1/3	1/8	1/12	1/15	1/22	1/30	2/1
January '18	6	1/25	2/2	2/6	2/9	2/13	2/14	2/21	2/28	3/1
February '18	7	2/26	3/2	3/6	3/9	3/14	3/15	3/22	3/30	4/2
March '18	8	3/23	3/30	4/3	4/9	4/12	4/13	4/20	4/30	5/1
April '18	9	4/25	4/27	5/1	5/7	5/10	5/14	5/21	5/30	6/1
May '18	10	5/25	6/1	6/5	6/8	6/13	6/13	6/21	6/29	7/2
June '18	11	6/25	6/28	7/2	7/9	7/11	7/12	7/23	7/30	8/1
July '18	12	7/25	7/27	7/31	8/7	8/9	8/13	8/21	8/29	9/3
August '18	13	8/24	8/31	9/4	9/7	9/12	9/13	9/21	9/28	10/1
September '18	14	9/25	9/28	10/2	10/8	10/10	10/12	10/22	10/30	11/1
October '18	15	10/25	11/2	11/6	11/9	11/13	11/14	11/21	11/30	12/3
November '18	16	11/26	11/30	12/4	12/7	12/11	12/12	12/19	12/28	1/1

Required Documents	Responsible Party
Funding Notice	Raiders
Sources/Uses	Raiders
Payment Application	MMcJV
Releases	MMcJV/JLL/ICON
Summary of Costs	Raiders/ICON
Disbursement Request Summary	ICON

Print Date: 3/16/2018

EXHIBIT E

Design-Builder's Key Personnel

Name	Firm	Role
John Wood	MMJV	Principal in Charge
Paul Dudzinski	MMJV	Project Director
Brian Fitzpatrick	MMJV	Construction Executive
Adam Hardy	MMJV	Construction Executive
Jason Hopper	MMJV	Director of Design Phase
Dave Mansell	MMJV	Field Operation Manager
Jason Brown	MMJV	General Superintendent
Lynn Littlejohn	MMJV	Diversity Coordinator

EXHIBIT F

Rate Schedule of Project Staff, Rates for Labor, and Equipment Rate Schedule

Las Vegas Stadium
Professional Staff Billing Rates
Publish Date: December 15, 2017

For Supervisory Labor Prior to 1/1/2018

Position	2017
[redacted]	

Las Vegas Stadium
Professional Staff Billing Rates
Publish Date: December 15, 2017

Mortenson construction | McCARTHY



Las Vegas Stadium
Professional Staff Billing Rates
Publish Date: December 15, 2017

Mortenson construction

McCARTHY



Mortenson | McCARTHY

MORTENSON/McCARTHY PROVIDED EQUIPMENT & TOOLS
2018 MASTER BILLING RATE SCHEDULE
March 1, 2018

All rates include sales tax and are billed on a 12 month cycle. (Not industry standard 28 days)
Fuel, repairs and freight are not included in the rates and will be billed seperately.

ITEM #	DESCRIPTION	DAY	WEEK	MONTH
[redacted]				

Mortenson | McCARTHY

MORTENSON/McCARTHY PROVIDED EQUIPMENT & TOOLS
2018 MASTER BILLING RATE SCHEDULE
March 1, 2018

All rates include sales tax and are billed on a 12 month cycle. (Not industry standard 28 days)
Fuel, repairs and freight are not included in the rates and will be billed seperately.

ITEM #	DESCRIPTION	DAY	WEEK	MONTH
[redacted]				

Mortenson | McCARTHY

MORTENSON/McCARTHY PROVIDED EQUIPMENT & TOOLS
2018 MASTER BILLING RATE SCHEDULE
March 1, 2018

All rates include sales tax and are billed on a 12 month cycle. (Not industry standard 28 days)
Fuel, repairs and freight are not included in the rates and will be billed seperately.

ITEM #	DESCRIPTION	DAY	WEEK	MONTH
[redacted]				

Mortenson | McCARTHY

MORTENSON/McCARTHY PROVIDED EQUIPMENT & TOOLS
2018 MASTER BILLING RATE SCHEDULE
March 1, 2018

All rates include sales tax and are billed on a 12 month cycle. (Not industry standard 28 days)
Fuel, repairs and freight are not included in the rates and will be billed seperately.

ITEM #	DESCRIPTION	DAY	WEEK	MONTH
[redacted]				

Mortenson | McCARTHY

MORTENSON/McCARTHY PROVIDED EQUIPMENT & TOOLS
2018 MASTER BILLING RATE SCHEDULE
March 1, 2018

All rates include sales tax and are billed on a 12 month cycle. (Not industry standard 28 days)
Fuel, repairs and freight are not included in the rates and will be billed seperately.

ITEM #	DESCRIPTION	DAY	WEEK	MONTH
[redacted]				

Mortenson | McCARTHY

MORTENSON/McCARTHY PROVIDED EQUIPMENT & TOOLS
2018 MASTER BILLING RATE SCHEDULE
March 1, 2018

All rates include sales tax and are billed on a 12 month cycle. (Not industry standard 28 days)
Fuel, repairs and freight are not included in the rates and will be billed seperately.

ITEM #	DESCRIPTION	DAY	WEEK	MONTH
[redacted]				

MORTENSON/McCARTHY PROVIDED EQUIPMENT & TOOLS
2018 MASTER BILLING RATE SCHEDULE
March 1, 2018

All rates include sales tax and are billed on a 12 month cycle. (Not industry standard 28 days)
Fuel, repairs and freight are not included in the rates and will be billed seperately.

ITEM #	DESCRIPTION	DAY	WEEK	MONTH
[redacted]				

Mortenson | McCARTHY

MORTENSON/McCARTHY PROVIDED EQUIPMENT & TOOLS
2018 MASTER BILLING RATE SCHEDULE
March 1, 2018

All rates include sales tax and are billed on a 12 month cycle. (Not industry standard 28 days)
Fuel, repairs and freight are not included in the rates and will be billed seperately.

ITEM #	DESCRIPTION	DAY	WEEK	MONTH
[redacted]				

Mortenson | McCARTHY

MORTENSON/McCARTHY PROVIDED EQUIPMENT & TOOLS
2018 MASTER BILLING RATE SCHEDULE
March 1, 2018

All rates include sales tax and are billed on a 12 month cycle. (Not industry standard 28 days)
Fuel, repairs and freight are not included in the rates and will be billed seperately.

ITEM #	DESCRIPTION	DAY	WEEK	MONTH
[redacted]				

MORTENSON/McCARTHY PROVIDED EQUIPMENT & TOOLS
2018 MASTER BILLING RATE SCHEDULE
March 1, 2018

All rates include sales tax and are billed on a 12 month cycle. (Not industry standard 28 days)
Fuel, repairs and freight are not included in the rates and will be billed seperately.

ITEM #	DESCRIPTION	DAY	WEEK	MONTH
[redacted]				

Mortenson | McCARTHY

MORTENSON/McCARTHY PROVIDED EQUIPMENT & TOOLS
2018 MASTER BILLING RATE SCHEDULE
March 1, 2018

All rates include sales tax and are billed on a 12 month cycle. (Not industry standard 28 days)
Fuel, repairs and freight are not included in the rates and will be billed seperately.

ITEM #	DESCRIPTION	DAY	WEEK	MONTH
[redacted]				

MORTENSON/McCARTHY PROVIDED EQUIPMENT & TOOLS
2018 MASTER BILLING RATE SCHEDULE
March 1, 2018

All rates include sales tax and are billed on a 12 month cycle. (Not industry standard 28 days)
Fuel, repairs and freight are not included in the rates and will be billed seperately.

ITEM #	DESCRIPTION	DAY	WEEK	MONTH
[redacted]				

Mortenson | McCARTHY

MORTENSON/McCARTHY PROVIDED EQUIPMENT & TOOLS
2018 MASTER BILLING RATE SCHEDULE
March 1, 2018

All rates include sales tax and are billed on a 12 month cycle. (Not industry standard 28 days)
Fuel, repairs and freight are not included in the rates and will be billed seperately.

ITEM #	DESCRIPTION	DAY	WEEK	MONTH
[redacted]				

Mortenson | McCARTHY

MORTENSON/McCARTHY PROVIDED EQUIPMENT & TOOLS
2018 MASTER BILLING RATE SCHEDULE
March 1, 2018

All rates include sales tax and are billed on a 12 month cycle. (Not industry standard 28 days)
Fuel, repairs and freight are not included in the rates and will be billed seperately.

ITEM #	DESCRIPTION	DAY	WEEK	MONTH
[redacted]				

Mortenson | McCARTHY

MORTENSON/McCARTHY PROVIDED EQUIPMENT & TOOLS
2018 MASTER BILLING RATE SCHEDULE
March 1, 2018

All rates include sales tax and are billed on a 12 month cycle. (Not industry standard 28 days)
Fuel, repairs and freight are not included in the rates and will be billed seperately.

ITEM #	DESCRIPTION	DAY	WEEK	MONTH
[redacted]				

Mortenson | McCARTHY

MORTENSON/McCARTHY PROVIDED EQUIPMENT & TOOLS
2018 MASTER BILLING RATE SCHEDULE
March 1, 2018

All rates include sales tax and are billed on a 12 month cycle. (Not industry standard 28 days)
Fuel, repairs and freight are not included in the rates and will be billed seperately.

ITEM #	DESCRIPTION	DAY	WEEK	MONTH
[redacted]				

Mortenson | McCARTHY

MORTENSON/McCARTHY PROVIDED EQUIPMENT & TOOLS
2018 MASTER BILLING RATE SCHEDULE
March 1, 2018

All rates include sales tax and are billed on a 12 month cycle. (Not industry standard 28 days)
Fuel, repairs and freight are not included in the rates and will be billed seperately.

ITEM #	DESCRIPTION	DAY	WEEK	MONTH
[redacted]				

Mortenson | McCARTHY

MORTENSON/McCARTHY PROVIDED EQUIPMENT & TOOLS
2018 MASTER BILLING RATE SCHEDULE
March 1, 2018

All rates include sales tax and are billed on a 12 month cycle. (Not industry standard 28 days)
Fuel, repairs and freight are not included in the rates and will be billed seperately.

ITEM #	DESCRIPTION	DAY	WEEK	MONTH
[redacted]				

Mortenson | McCARTHY

MORTENSON/McCARTHY PROVIDED EQUIPMENT & TOOLS
2018 MASTER BILLING RATE SCHEDULE
March 1, 2018

All rates include sales tax and are billed on a 12 month cycle. (Not industry standard 28 days)
Fuel, repairs and freight are not included in the rates and will be billed seperately.

ITEM #	DESCRIPTION	DAY	WEEK	MONTH
[redacted]				

Mortenson | McCARTHY

MORTENSON/McCARTHY PROVIDED EQUIPMENT & TOOLS
2018 MASTER BILLING RATE SCHEDULE
March 1, 2018

All rates include sales tax and are billed on a 12 month cycle. (Not industry standard 28 days)
Fuel, repairs and freight are not included in the rates and will be billed seperately.

ITEM #	DESCRIPTION	DAY	WEEK	MONTH
[redacted]				

MORTENSON/McCARTHY PROVIDED EQUIPMENT & TOOLS
2018 MASTER BILLING RATE SCHEDULE
March 1, 2018

All rates include sales tax and are billed on a 12 month cycle. (Not industry standard 28 days)
Fuel, repairs and freight are not included in the rates and will be billed seperately.

ITEM #	DESCRIPTION	DAY	WEEK	MONTH
[redacted]				

EXHIBIT G

Insurance and Bond Requirements

A. Insurance Requirements

1.1 The Design-Builder shall purchase and maintain such insurance as will protect the Design-Builder from any claims which may arise out of or result from the performance of the Work and/or Services hereunder, which insurance coverage shall be retroactive to the Effective Date of this Agreement. All insurance coverage must be provided by insurance companies with a current A.M. Best Rating of at least A- VII. The types of insurance and limits of liability of the Design-Builder's insurance required herein shall meet or exceed the requirements stated below:

- Workers' Compensation and Employers' Liability, the amount and scope of which shall be the following:

Workers' Compensation:	Statutory Limits
Employers' Liability:	$1,000,000 Each Accident
	$1,000,000 Each Employee by Disease
	$1,000,000 Policy Limit by Disease

  Coverage must apply in the State(s) where Work and/or services are to be performed. The policy shall also include coverage under the USL&H and/or Jones Act where such exposure exists listing the state in which Work and/or services are to be performed. Stop Gap coverage must be provided if Work and/or services are to be performed in a monopolistic state. The workers' compensation and employers' liability policy shall include coverage for sole proprietors, partners, executive/corporate officers or LLC members.

- **Commercial General Liability (Offsite only, including products liability coverage provided under a standard CG 00 01 04 13 policy for products manufactured, assembled or otherwise worked upon away from the Project's Site), with coverage in the amounts set forth below:**
  - $2,000,000 General Aggregate
  - $2,000,000 Products/Completed Operations Aggregate
  - $1,000,000 Personal Injury & Advertising Liability
  - $1,000,000 Each Occurrence
  - $ 300,000 Damage to Rented Premises

  Such insurance shall include the following:

  - Current ISO edition of CG 00 01 or its equivalent;
  - The general aggregate limits apply per project and location;
  - Claims-Made coverage is not acceptable;
  - The personal injury contractual liability exclusion shall be deleted, or shall provide coverage under CG 22 74; and
  - Electronic Data Liability endorsement ISO CG 04 37 with coverage to the full limits of the policy.
  -

  The following exclusions/limitations or their equivalent(s) are prohibited:

  - Contractual Liability Limitation (CG 21 39);
  - Amendment of Insured Contract Definition (CG 24 26);
  - Limitation of Coverage to Designated Premises or Project (CG 21 44);
  - Exclusion-Damage to Work Performed by Subcontractors on Your Behalf (CG 22 94 or CG 22 95);

- Exclusion-Explosion, Collapse and Underground Property Damage Hazard (CG 21 42 or CG 21 43);
- Any Classification or Business Description limitation;
- Any Construction Defect Completed Operations exclusion;
- Any endorsement modifying the Employer's Liability exclusion or deleting the exception to it;
- Any "Insured vs. Insured" exclusion except Named Insured vs. Named Insured;
- Any Subsidence exclusion;
- Any exclusion of EIFS/DEFS;
- Any exclusion for punitive, exemplary or multiplied damages; and
- Any exclusion for unknown pre-existing injury, loss or damage.

- **Business Automobile Liability**, with coverage in the following amounts:

  - $1,000,000 Combined Single Limit each accident; or
  - If Design-Builder's Work includes Hazardous Materials Transporter services, Design-Builder also shall obtain a (i) MCS-90 endorsement and (ii) Sudden and Accidental Pollution endorsement with limits of liability of at least $1,000,000 for each occurrence and $2,000,000 general aggregate.

  Such insurance shall include:

  - Current ISO edition of CA 00 01 or its equivalent
  - Arising out of any auto (Symbol 1), including owned, hired and non-owned autos.

- **Umbrella/Excess Liability** materially follow form excess of above required Commercial General Liability, Business Automobile Liability and Employers' Liability with coverage in the following amounts:

  - $50,000,000 Each Occurrence Limit
  - $50,000,000 Aggregate Limit

  Such insurance shall include:

  - Drop-down coverage for reduction and/or exhaustion of underlying aggregate limits.
  - The same inception date as the policies to which it materially follows form.
  - A duty to defend provision.

- **Contractors Professional Liability** which shall include coverage for all design and construction management services rendered by the Design-Builder (including vicarious liability of the Design-Builder arising out of the activities of their consultants, and their subcontractors). Coverage shall be on a claims made basis with a retroactive date no later than the first date of design services, with coverage to be continuously renewed and maintained through the applicable statute of repose:

  This insurance shall include the following coverages:

  - Errors and Omissions Liability
  - Contractors Protective Indemnity
  - Rectification Coverage

  Coverage shall be in the following minimum amounts

  - $50,000,000 Each Claim
  - $50,000,000 Aggregate

Coverage shall apply to negligent acts, errors or omissions arising from the Design-Builder's professional services that will be defined to include, at a minimum, architecture, engineering, surveying, and construction management.

- **Contractors Equipment Insurance** including "all risk" coverage for any equipment, tools or machinery used for the Project, including flood and earthquake coverage. Design Builder shall also require its Subcontractors of every tier to procure and maintain the same coverage. Design Builder and its Subcontractors of every tier shall each be responsible for any loss or damage to its equipment, tools, machinery of any kind or its loss of use, regardless of cause.

- **Other Required Insurance Coverage where Exposure Exists**. The following insurance shall be required by the Design-Builder and/or Subcontractors under terms and conditions consistent with Design-Builder's standard subcontract provisions to the extent that such activities exist in the performance of Work under this Agreement.

  a. Watercraft Liability and Indemnity Insurance.
  b. Aircraft Liability (including but not limited to the use of helicopters or unmanned aircraft).
  c. Railroad Protective Liability.

1.2 The Design-Builder shall maintain its products/completed operations coverage under its Commercial General, and Umbrella/Excess insurance policies as required by the terms of this Agreement until the expiration of any applicable statutes of repose including without limitation the applicable Law where the Work and/or services are performed. In the event that there is no statute specifically applicable to the construction of improvements to real property, the coverages shall be maintained in full force and effect by the Design-Builder for a minimum of six (6) years from the Guaranteed Substantial Completion Date as defined in the Agreement.

1.3 Insurance coverage provided by the Design-Builder shall not be limited to the liability assumed under the indemnification provisions of this Agreement.

1.4 The Indemnitees in no way warrant that the minimum limits contained herein are sufficient to protect Design-Builder from liabilities that might arise out of the performance of the Work and/or services under this Agreement by the Design-Builder, its agents, representatives, employees, Subcontractors or Vendors and Design-Builder is free to purchase such additional insurance as may be determined necessary.

1.5 The Indemnitees are all to be named as "Additional Insureds" for both ongoing and completed operations under all insurance policies maintained by Design-Builder hereunder, except Workers' Compensation. As respects the Commercial General Liability and Umbrella/Excess Liability policies, the Additional Insured Endorsements shall be on ISO Form CG 20 10 10/01 plus CG 20 37 10/01.

1.6 With the exception of those policies of insurance being purchased by the Owner (including, but not limited to, general liability and excess liability through Owner Controlled Insurance Program, Contractors Pollution Liability Insurance and Builder's Risk the Design-Builder's insurance coverage shall be primary insurance with respect to the Indemnitees. Any insurance or self-insurance maintained by the Indemnitees, other than those policies of insurance being purchased by the Owner (including, but not limited to, general liability and excess liability through an Owner Controlled Insurance Program, Contractors Pollution Liability Insurance, and Builder's Risk),shall be in excess of the Design-Builder's insurance and shall not contribute to it. All applicable policies of insurance shall provide for such primary and non-contributory coverage by endorsement and shall provide evidence of the same on all certificates of insurance.

1.7 All policies of insurance maintained by Design-Builder shall include waivers of subrogation in favor of the Indemnitees, except professional liability. All policies of insurance shall provide for such

waivers by endorsement or otherwise, and shall incorporate such waivers on all certificates of insurance, except professional liability.

1.8 Upon execution of this Agreement and prior to commencing any Work and/or services, the Design-Builder shall furnish certificates of insurance along with the additional insured, primary and non-contributory and waiver of subrogation endorsements evidencing the insurance required above. The Design-Builder's policies of insurance shall contain a provision that thirty (30) days prior written notice shall be given to StadCo in the event of cancellation or non-renewal of such insurance. Upon execution of this Agreement and prior to commencing any Work and/or services, the certificates of insurance and additional insured, primary and non-contributory and waiver of subrogation endorsements shall be sent via e-mail and U.S. Mail to the following:

LV Stadium Events Company, LLC
6623 Las Vegas Blvd. South, Suite 380
Las Vegas, NV 89119
Att: Don Webb
dwebb@lvstadiumcompany.com

Willis of Minnesota, Inc.
1600 Utica Avenue, Suite 600St.
Louis Park, MN 55416
Attn: Scott Labat
scott.labat@willistowerswatson.com

CAA ICON
6623 Las Vegas Blvd. South, Suite 380
Las Vegas, NV 89119
Attn.: Sam Bottoms
Sam.bottoms@caaicon.com

With copy to:
CAA ICON
5075 S. Syracuse St., Suite 700
Denver, CO 80237
Attn: Charlie Thornton
Charlie.thornton@caaicon.com

Failure of StadCo to demand such certificate or other evidence of full compliance with these insurance requirements or failure of StadCo to identify any deficiency from evidence that is provided shall not be construed as a waiver of the Design-Builder's obligation to maintain such insurance.

1.9 Should the Design-Builder fail to provide or maintain the insurance set forth in this Agreement, StadCo may at its sole discretion, declare the Design-Builder in material breach of this Agreement and withhold payment, or StadCo may elect to purchase such insurance so as to maintain the required coverage and deduct the premiums for such insurance from any payment due the Design-Builder; provided, however, that StadCo's failure to do so and/or failure to maintain such coverage shall not in any manner affect, reduce, or limit StadCo's ability to recover from Design-Builder for any loss, costs, damages, expenses, or other actions for Design-Builder's failure to comply with the insurance requirements contained herein.

1.10 Commencement of Work and/or services without provision of the required certificate of insurance, evidence of insurance and/or required endorsements, or without compliance with any other provision of this Agreement, shall not constitute a waiver by StadCo of any rights. StadCo has the right, but not the obligation, of prohibiting the Design-Builder or any Subcontractor/ Vendor from performing any Work and/or services until such certificate of insurance, evidence of insurance and/or required endorsements are received and approved by StadCo.

1.11 The Design-Builder is responsible for assuring that all Subcontractors and Vendors provide Commercial General Liability, Business Automobile Liability, and Workers' Compensation including Employers Liability coverage equal to the Design-Builder's required coverage terms and conditions as required in Design-Builder's Standard Subcontract Terms and Conditions. The Design-Builder's Subcontractors and Vendors shall maintain total combined limits of Commercial General and Umbrella/Excess liability limits of at least those required by the subcontract agreement with Design Builder. Design Builder is also responsible for assuring that all Subcontractors and Vendors insurance policies required in this Section 1.11 of this Exhibit comply with the additional insured, primary and non-contributory and waiver of subrogation provisions shown in this Exhibit. If requested by Stadco, Design-Builder shall provide StadCo with certificates of insurance and additional insured, primary and non-contributory and waiver of subrogation endorsements for the insurance required in this Section of this Exhibit for all of its Subcontractors and Vendors performing Work and/or services in connection with this Agreement.

1.12 Subsequent to the assignment of the AOR agreement to Design-Builder, Design-Builder shall ensure all insurance required under the AOR agreement remains in full force and effect.

B. Bond Requirements

2.1 If required by StadCo for this Project pursuant to **Section 13.2** of the Agreement, the Bond referenced in **Section 13.2** of the Agreement shall be issued by a surety company acceptable to StadCo, as security for the proper and complete fulfillment of Design-Builder's obligations hereunder, in an amount to be mutually agreed to by StadCo and Design-Builder. It is understood that delivery of the Bond shall not be required until the GMP is accepted, the Project is funded, and a notice to proceed is issued to Design-Builder such that the obligations of the sureties do not begin until after construction starts and those obligations are limited to the construction timeframe. The Bond shall be in a form reasonably acceptable to StadCo. The minimum requirement for approval of a surety shall be that the surety is listed by the United States Treasury Department as acceptable for bonding Federal projects and that the amount of the Bond is within the limit set by the Treasury Department as the net limit on any single risk. There shall be no affiliation between Design-Builder and the bonding agent or agency unless, after full disclosure to StadCo of all facts StadCo deems relevant, StadCo consents to such affiliation. If the Contract Sum is increased by a duly executed Change Order, then the face amount of the Bond shall also increase and StadCo shall pay the premium cost charged due to such increase.

C. StadCo Insurance

3.1 Builder's Risk Insurance. StadCo shall purchase and maintain, at its own expense, builder's risk insurance for the Work at the Project. Such insurance shall be maintained through Substantial Completion (at which time permanent property insurance will be in full force and effect). The insurance shall be in the amount of the total value for the entire Work at the Project and shall be written on a repair or replacement cost basis. This insurance shall include the respective interests of StadCo, Design-Builder and Subcontractors of every tier in the Work until Substantial Completion. Design-Builder and Subcontractors of every tier shall be Additional Insureds under the builder's risk insurance, but then only as their respective interests may appear.

The builder's risk insurance shall be on an "all-risk" form and shall include insurance against the perils of fire (with extended coverage) and physical loss or damage including, without duplication of coverage, theft, vandalism, malicious mischief, terrorism (as provided under TRIA), rigging and hoisting, collapse, earthquake, flood, windstorm, falsework, testing and startup, named storm, temporary buildings, debris removal including demolition expenses, increased cost of repair occasioned by enforcement of any applicable law or ordinance, and shall cover reasonable compensation for Architect's and Design-Builder's services and expenses required as a result of such insured loss, subject to sublimits stated in the builder's risk insurance. The builder's risk insurance shall cover portions of the Work at temporary offsite storage locations, and also portions of the Work in transit (only in U.S.), subject to sublimits stated in the builder's risk insurance.

Partial occupancy or use shall not commence until the insurance company or companies providing the builder's risk insurance have consented to such partial occupancy or use by endorsement or otherwise. StadCo and Design-Builder shall take reasonable steps to obtain consent of the insurance company or companies, and shall, without mutual written consent, take no action with respect to partial occupancy or use that would cause cancellation, lapse or reduction in insurance.

The builder's risk insurance shall have a deductible of $100,000 Physical loss of or damage to Covered Property.

For any builder's risk loss that is covered by the builder's risk insurance provided by StadCo, it shall be the responsibility of Design-Builder, or any contractor, subcontractor or vendor which caused the builder's risk loss to pay the applicable deductible(s) (the **"Builder's Risk Deductible"**). The Builder's Risk Deductible amount shall be the actual costs associated with the covered loss or $25,000 per occurrence (whichever is less). Design-Builder shall recover the Builder's Risk Deductible from the party responsible for the event triggering the builder's risk loss. If the Builder's Risk Deductible is recovered by Design-Builder then the Builder's Risk Deductible shall be paid to StadCo within ten (10) days after receipt of the Builder's Risk Deductible. In the event Design-Builder cannot recover the Builder's Risk Deductible from the party who bears responsibility for the event triggering the builder's risk loss then the Builder's Risk Deductible shall be a Cost of Work pursuant to the terms of the Agreement.

A loss insured under the builder's risk insurance shall be adjusted by the Builder's Risk Insurer's designated adjuster and made payable to StadCo for the insureds, as their interests may appear, subject to requirements of any applicable mortgagee clause. Upon receipt of insurance proceeds from Builders' Risk carrier, StadCo shall pay Design-Builder their just shares of insurance proceeds within ten (10) calendar days. The Design-Builder shall pay Subcontractors their just shares of insurance proceeds received by the Design-Builder, and by appropriate agreements, written where legally required for validity, shall require Subcontractors to make payments to their Sub-subcontractors in similar manner.

Upon request, StadCo shall provide Design-Builder and Subcontractors with a Certificate of Insurance and/or a copy of each builder's risk policy for the Project.

If during the Project construction period StadCo insures properties, real or personal or both, at or adjacent to the Site by property insurance, or if after final payment property insurance is to be provided on the completed Work, StadCo shall waive all rights in accordance with the terms of the waiver set forth below for damages caused by fire or other causes of loss covered by this property insurance. All policies shall provide this waiver of subrogation by endorsement or otherwise.

Design-Builder and Subcontractors shall conduct their own independent analysis and evaluation of the builder's risk insurance. StadCo makes no representations, warranties or guarantees regarding the adequacy of the builder's risk insurance.

StadCo and Design-Builder waive all rights against (1) each other, each third party beneficiary and Indemnitee established pursuant to this Agreement, and any of their subcontractors, sub-subcontractors, agents and employees, each of the others, and (2) the Lead Design Architect, the Architect of Record, and any of their respective consultants, separate contractors, subcontractors, sub-subcontractors, agents and employees, if any, for damages caused by fire or other causes of loss to the extent covered by property insurance obtained pursuant to this Section or other property insurance applicable to the Work, except such rights as they have to proceeds of such insurance. StadCo or Design-Builder, as appropriate, shall require of the Lead Design Architect and the Architect of Record, by appropriate agreements, written where legally required for validity, similar waivers each in favor of other parties enumerated herein. The policies shall provide such waivers of subrogation by endorsement or otherwise. A waiver of subrogation shall be effective as to a person or entity even though that person or entity would otherwise have a duty of indemnification, contractual or otherwise, did not pay the insurance premium directly or indirectly, and whether or not the person or entity had an insurable interest in the property damaged.

3.2 Project Contractors Pollution Liability Insurance. StadCo shall purchase and maintain, at its own expense, and maintain so long as Work is performed on the Project, a Contractors Pollution Liability Insurance Policy for the Project (**"Project Contractors Pollution Liability Insurance"**) written on an occurrence basis with limits of $25,000,000 per pollution condition and $25,000,000 aggregate for all pollution conditions subject to a deductible amount of $100,000 per pollution condition. Defense Expenses shall erode limits of liability and any applicable deductible. Contractors and subcontractors of any tier shall be additional named insureds to the extent there is a written and executed contract. Completed operations coverage shall be provided for 10 years after the Guaranteed Substantial Completion Date.

StadCo shall be responsible for any deductible owed under the Project Pollution Liability Insurance.

Upon request, StadCo shall provide Design-Builder and Subcontractors with a Certificate of Insurance and/or a copy of the Project Contractors Pollution Liability Insurance policy.

Design-Builder and Subcontractors shall conduct their own independent analysis and evaluation of the Project Contractors Pollution Liability Insurance. StadCo makes no representations, warranties or guarantees regarding the adequacy of the Project Contractors Pollution Liability Insurance.

3.3. OCIP. StadCo has elected to implement an Owner Controlled Insurance Program (OCIP) on the Project to include General Liability and Excess/Umbrella Liability coverage. StadCo will be responsible for any deductibles owed under the OCIP. Design-Builder agrees to be bound to the terms of the OCIP Manual, and further agrees to bind its Subcontractors to the same. A copy of the OCIP Manual is included as **Exhibit H**.

3.4 Earthquake Coverage. Effective on or about Substantial Completion of the Project, StadCo shall procure and keep in effect, or continuously renew, through the applicable Statute of Repose (the **"Earthquake Coverage Period"**), property insurance on an "all-risk", "special form causes of loss" or equivalent policy form, insuring the completed Project and of all StadCo's office furniture, trade fixtures, office equipment and all other items of StadCo's property on the premises, with loss or damage payable to StadCo as named insured, or other parties as their interest may appear (the "**Property Insurance**"). Said policy, or said policy in combination with excess earthquake policies, shall also provide coverage for the peril of an earthquake and any ensuing peril due to the peril of an earthquake including a repair or replace valuation clause and with limits of no less than $200,000,000 per occurrence and annual aggregate (the "**Earthquake Coverage**").

During the Earthquake Coverage Period, StadCo hereby waives all claims against Design-Builder (and the respective individual partners, M. A. Mortenson Company, and McCarthy Building Companies, Inc.), and any of their subcontractors and consultants, agents and employees to the extent any loss is paid by the Earthquake Coverage , including any associated earthquake deductibles or self-insured retentions (if any) (the **"StadCo Earthquake Waiver"**). Further, the Property Insurance policy, and any excess earthquake policies if applicable, shall contain either a provision, or endorsement stating in effect that the insurer(s) will not acquire any rights of recovery against other parties that StadCo, as named insured, has expressly waived, or waived in writing, prior to a loss (the **"Waiver of Subrogation"**).

Within 15 days following Substantial Completion, and annually thereafter during the Earthquake Coverage Period, StadCo shall deliver to Design-Builder a certificate of insurance evidencing that the Property Insurance is in place and includes the Waiver of Subrogation.

EXHIBIT H

OCIP Manual

Willis Towers Watson

Las Vegas Stadium Project
OCIP Project Insurance Manual

Owner: LV Stadium Events Company, LLC

Design Builder: Mortenson/McCarthy Las Vegas Stadium, a Joint Venture

Dated: November 10, 2017
Updated as of December 12, 2017

Table of Contents

1 Introduction

2 Project Insurance Directory

3 Definitions

4 General Provisions

5 Insurance Provided by the Owner

6 Insurance Provided by Design Builder, Contractor and all Subcontractors of every tier

7 Enrolling in the OCIP – Completion of the Enrollment Form

8 OCIP Forms

9 General Liability Claim Reporting

1. Introduction

This OCIP Project Insurance Manual (the "Insurance Manual") describes the insurance requirements for the Project. LV Stadium Events Company, LLC ("Owner") intends to procure and maintain certain insurance coverages on behalf of certain project participants. These coverages will include Builders Risk, Contractors Pollution Liability, and an Owner Controlled Insurance Program ("OCIP") providing General Liability and Excess Liability (collectively the "Project Insurance Program").

The OCIP will provide General Liability and Excess Liability insurance for the Design Builder, Contractors and Subcontractors of every tier (each a "Contractor" and collectively "Contractors") working on the Project who are enrolled in the OCIP. Participation will be mandatory, except for those identified as Excluded Parties, **BUT IT IS NOT AUTOMATIC**. Each Eligible Contractor will be required to follow the enrollment procedures as described herein.

In consideration of the OCIP provided by the Owner, each Eligible Contractor shall submit its bid, pricing and any subsequent change orders excluding its General Liability and Umbrella Liability insurance costs (Bid Net Program).

All terms and conditions of this Insurance Manual, including but not limited to Contractor's rights and responsibilities as stated herein, are incorporated by reference into Contractor's Contract, as defined in section 3 Definitions. You are required to bind all your lower tiered subcontractors to the terms, conditions and requirements of this manual.

Any questions regarding the particulars of this Insurance Manual can be discussed at pre-bid and pre-award meetings, or by contacting the OCIP Program Manager (see directory).

This Insurance Manual does not, and is not intended to, provide coverage interpretations or complete information about coverages. The terms and conditions of the respective insurance policies will govern how coverage is applied.

2. Directory

Owner

LV Stadium Events Company, LLC

OCIP Administrator

Willis Towers Watson
Willis of Minnesota, Inc.
1600 Utica Avenue South
Suite 600
Minneapolis, MN 55416

Scott Labat
Sr. Vice President, Client Advocate
Willis Towers Watson

Direct: 763-302-7166
Mobile: 612-325-1272
Email: scott.labat@willistowerswatson.com

OCIP Program Manager

Denise Wishcop
Vice President, Sr. Client Service Specialist
Willis Towers Watson

Direct: 763-302-7101
Mobile: 612-417-0888
Email: denise.wishcop@willistowerswatson.com

OCIP Administration

Wrap-up Data Center
Dallas, TX
Email: wrapup.dallas@willistowerswatson.com

OCIP Claims Manager

Marty Berger
Claim Advocate
Direct: 763-302-7154
Mobile: 612-812-9474
Email: marty.berger@willistowerswatson.com

3. Definitions

Bid Net Program: Contractor's original scope of work and subsequent change orders will be bid excluding any General Liability and Excess Liability insurance costs.

Contract: The written agreement between one or more of the Owner, Design Builder, Contractors, Subcontractors and their Subcontractors of every tier.

Owner: LV Stadium Events Company, LLC.

Design Builder: Mortenson-McCarthy Las Vegas Stadium, a Joint Venture, comprised of M.A. Mortenson Company, Inc., a Minnesota Corporation, and McCarthy Building Companies, Inc., a Missouri Corporation.

Contractor: Any individual, firm, or corporation undertaking construction or other services under a Contract with the Owner or Design Builder to furnish labor, services, materials and/or equipment, and/or perform operations at the Project sites. Subcontractor is also a Contractor.

Subcontractor: Any individual, firm, or corporation undertaking construction or other services under a Contract with the Owner, Design Builder or Contractor (or their Subcontractors) to furnish labor, services, materials and/or equipment, and/or perform operations at the Project sites.

Enrolled Contractor(s): The Design Builder, Contractors or Subcontractors of any tier who have been awarded work and meet the requirements to become enrolled in the OCIP as evidenced by an OCIP certificate of insurance issued by the OCIP Program Manager.

Eligible Contractors: Contractors and Subcontractors of all tiers performing labor or services at the project site are eligible to be enrolled in the OCIP. Suppliers and vendors that perform or subcontract installation, temporary labor services, employee leasing companies providing direct labor, joint ventures and all joint venture partners are considered Eligible Contractors. The Owner may, at its discretion, include a Contractor who otherwise, by definition, would be an Excluded Party.

***Excluded / Ineligible Parties*:** Contractors or companies excluded from the OCIP:

- Vendors, suppliers (who do not perform or subcontract installation at the Project Site), material dealers, manufacturing representatives, equipment and rental companies who perform equipment maintenance (does not apply to those who provide operators);
- Contract haulers or truckers (or others who merely transport, pick up, deliver or carry materials, personnel, parts or equipment or any other items or persons to or from the project site);
- Mobile crane owners and/or operators whose sole scope of work involves the lifting or placement of materials or equipment for other contractors;

- Asbestos abatement or other hazardous materials remediation;
- Architects, engineers, surveyors, soil testing contractors and their consultants;
- Contractors whose sole scope of work includes Exterior Insulation and Finish Systems;
- Contractors whose sole scope of work includes guard services, janitorial services and food services;
- Contractors providing temporary services; and
- The Owner may at its discretion exclude others from the OCIP, provided that prompt notice is given to Contractor or Subcontractor.

Project Site: Las Vegas Stadium Project, Las Vegas, NV
The Project Site defined in the contract documents, and any scheduled offsite location or structure if dedicated to the Project and approved by the Owner. Includes, but not limited to, lay down areas, parking lots, trailers, mock up and staging areas, model units, Project Site offices and any operations necessary and incidental to the designated project. This will not include the Enrolled Contractors' regularly established workplace, plant, factory, office, shop, warehouse, or permanent yard.

Offsite: Premises other than the Project Site.

Onsite: See Project Site definition.

Project: Las Vegas Stadium – Las Vegas, NV

Project Managers: The individuals assigned by the Design Builder with overall Project responsibility.

OCIP: Owner Controlled Insurance Program. A program under which General Liability and Excess Liability Insurance is procured by the Owner for all Eligible Enrolled Contractors of every tier while performing operations at the Project Sites.

OCIP Administrator: Willis Towers Watson – Willis of Minnesota, Inc.

OCIP Program Manager: The individual who is responsible for the day-to-day administration of the OCIP and the OCIP enrollments.

OCIP Administration: Responsible for project certificate issuance and enrollment reporting

4. General Provisions

All Enrolled Parties are required to reasonably cooperate with the Owner, the OCIP Administrator, and the OCIP insurance carrier(s) in all aspects of the OCIP operation and administration. Enrolled Parties' responsibilities include, but are not limited to:

1. **Mandatory Compliance**
   OCIP participation is mandatory, except for those identified as Excluded Parties. OCIP contract provisions and requirements must be included in all subcontracts.

2. **Meeting Attendance**
   At the request of the Owner or the Design Builder, Contractors and their Subcontractors shall attend any meetings held to explain and discuss the Project Insurance Program.

3. **Insurance Manual Incorporated into Bid Specifications and Contract**
   This Insurance Manual will be a part of the bid specifications and bidders are expected to be familiar with the requirements prior to submitting their bid. In addition, this Insurance Manual will be incorporated by reference into the successful bidders awarding Contract and accordingly, all provisions require mandatory compliance. Each Subcontractor must be provided with a copy of this Insurance Manual.

4. **Commencement of Work**
   Contractors or Subcontractors shall not commence work at the Project Sites until:
   - **a)** If enrolled under the OCIP, having received an OCIP certificate of insurance issued by the OCIP Program Manager, and providing evidence of offsite GL/Excess coverage and other coverage as required in this Insurance Manual and elsewhere in their Contract.
   - **b)** If excluded under the OCIP, having provided a certificate of insurance as evidence of coverage as required in this Insurance Manual and elsewhere in their Contract.
   - **c)** They have met all the other insurance requirements of this Insurance Manual and in their respective Contracts.

5. **Additional Contractor Responsibilities**
   In addition the Design Builder, Contractor and Subcontractor are responsible to comply with all of the following requirements:
   - Enforcing the Bid Net process for enrollment of all Subcontractors, except for those identified as Excluded / Ineligible parties, as participation by Eligible Contractors is mandatory;
   - Notifying the OCIP Administrator of all subcontracts awarded by submitting the Notice of Contract Award, included in this Insurance Manual.
   - Complying with insurance requirements in contract and Section 9, Insurance Claims Procedures;

- Each Contractor shall submit its bid, pricing and any subsequent change orders excluding its General Liability and Umbrella Liability insurance costs (Bid Net Program).

5. Insurance Provided by the Owner

The Owner will procure and maintain the insurance described in this section at its own expense. The limits of liability purchased apply collectively to all Insureds. Enrolled Parties shall refer to the actual policies for details concerning coverages, exclusions and limitations. Owner makes no representations, warranties, or guarantees regarding the adequacy of the OCIP. Each Enrolled Party shall conduct its own independent analysis and evaluation of the OCIP coverages. Policies are available for review upon request to the OCIP Administrator.

While the OCIP provides uniform coverages and reasonable limits for work performed at the Project Site, the OCIP is not intended to meet all the insurance needs of the Enrolled Parties. Eligible Parties shall discuss the OCIP with its insurance agent/broker or consultant to ensure that proper coverages are maintained. Eligible Parties shall notify their agent/broker or consultant that the work performed on-site will be insured under the OCIP once enrolled. This notification is to inform the Enrolled Parties' standard insurance company(ies) that the insurance coverages provided under the OCIP are primary and non-contributory on the Project Site.

Summaries of the insurance coverages and terms that are provided by the Owner are as follows:

1. **Commercial General Liability ("CGL") and Excess Liability Insurance**
   Owner Controlled Insurance Program (OCIP) providing General Liability and Excess Liability insurance for the Owner, Design Builder, Contractors, and Subcontractors of every tier working on the Project at the Project Site who are either specifically named on the policies or are enrolled in the OCIP. The Owner will maintain the OCIP until final completion, but in no event beyond the expiration date of the policies as noted on the project certificates of insurance. A single policy will be issued for all Enrolled Contractors naming all Enrolled Contractors as Additional Named Insureds. Coverage provided is primary and non-contributory with respect to any other insurance carried by Enrolled Contractor. As defined in the policy, Products/Completed Operations coverage is extended through the Statute of Repose, or ten (10) years, whichever is less, of where the Project is located. In addition, this program includes an extended warranty/repair work provision which extends operations coverage through the Statute of Repose, or ten (10) years, whichever is less, of where the Project is located in the event an Enrolled Contractor returns to the project site to perform warranty or repair work as defined by the OCIP policy.

a. Commercial General Liability (CGL)

Limits of Liability: (to be shared by all insureds)

$2,000,000	Each Occurrence
$4,000,000	General Aggregate
$4,000,000	Products/Completed Operations Aggregate*
$2,000,000	Personal Injury and Advertising Liability
$100,000	Each Loss – Fire Damage Liability
Excluded	Each Loss – Medical Payments

* *The Products/Completed Operations Aggregate is a single limit for the entire policy term inclusive of the extension period.*

- Coverage for off-site operations is excluded unless locations are scheduled and approved by the owner and OCIP Insurance carriers.
- Defense costs are outside of the policy limits.
- Primary and non-contributing insurance
- Waiver of Subrogation
- Policy provides Completed Operations Extension coverage through the applicable Statute of Repose or 10 (ten) years, whichever is less, per policy terms and conditions.
- The OCIP provides coverage for general liability claims which result from repair work to correct, replace or repair work that was completed during the policy period for the period of time allowed by the applicable statue of repose as provided by the controlling law of the jurisdiction where it is located and expires.

A single CGL policy will be issued and will include all Enrolled Contractors as Named Insureds and is available for review upon written request to the OCIP Administrator.

b. Excess Liability Insurance

Excess Liability insurance (above the CGL insurance) will be provided with limits of $200 million each occurrence and in the aggregate. The limits are excess of the primary limits described in Item a. above. These limits will be shared by all insureds.

- Excess Follow-Form primary Commercial General Liability per policy terms and conditions of the primary OCIP CGL policy only.
- Policy provides Completed Operations Extension coverage through the applicable Statute of Repose or 10 (ten) years, whichever is less, per policy terms and conditions.

A single lead excess and layered Excess Liability policy will be issued and will include all Enrolled Contractors as Named Insureds and is available for review upon written request to the OCIP Administrator.

2. OCIP Cancellation, Termination or Modification

Notwithstanding any other provision in this Insurance Manual, it is the Owner's intent to keep the OCIP in force throughout the term of the Project. However, the Owner reserves the right to cancel, terminate, modify the OCIP, or terminate the enrollment of any Enrolled Contractor. To exercise this option, the Owner would provide 90 days advance, written notice to the Design Builder and each Enrolled Contractor.

Enrolled Contractors would be required to effect replacement insurance coverage, equivalent to what is currently required for Offsite and Excluded Parties, or consistent with other contractual obligations. The reimbursement for the cost of such replacement insurance would be calculated on a pro-rata portion of the remaining contract value as a change order to the Owner. Written evidence of such replacement insurance must be provided to the Owner prior to the actual cancellation or termination date of the OCIP.

3. Builder's Risk

Builder's Risk insurance provides "all risk" coverage on the buildings, structure or work, and property of the Owner in the care, custody and control of a Contractor. Coverage is provided for the Owner, Design Builder, Contractors, Subcontractors of every tier, tenants at the project site, architects and engineers, all as required by any contract or subcontract and including any other entity as required by the named insured and then only as to their respective financial interest in the covered property are included as additional insureds under this policy as respects to manufacturers and suppliers their interest is limited to their respective financial interest in the covered property at the project site only.

The policy will cover structures and materials during the course of construction that are part of the Project. Coverage is also provided for materials while in domestic transit, or while stored temporarily away from the Project site, subject to policy sub-limits. Any domestic transit or offsite storage expected to exceed the applicable sub-limits requires prior notice to the OCIP Program Manager, who will request coverage approval from the carriers.

Owner and Contractors, Subcontractors of every tier and any party who is a named or additional insured waive all rights against each other for damages caused by fire or other perils to the extent covered by the Builder's Risk insurance or by any other property insurance applicable to the work.

CAUTION: There will be no coverage under this policy for International shipments. If needed,

the Owner will purchase this Ocean Cargo coverage separately after detailed information is provided to the OCIP Program Manager by the Design Builder or Subcontractors within a 60 day time period prior to these shipments.

4. Contractors Pollution Liability

Contractors Pollution Liability insurance for the Owner, Design Builder, Contractors, and Subcontractors for the duration of this contract for onsite activities and 10 years completed operations. The policy will be written with a limit of at least $25,000,000 per claim and in the aggregate.

5. Certificates of Insurance

The OCIP Program Manager will issue OCIP certificates of insurance to the Design Builder and each Enrolled Contractor to evidence coverage provided by the OCIP and the Owner.

6. Project Insurance Program Policies

The summary of coverages contained in this Insurance Manual is prepared for the convenience of those involved in the Project and should not be construed in any way as an exact and binding analysis of coverage. In case of any claim or question with respect to coverage, the original policies will prevail as the sole binding documents. Specimen CGL and Excess Liability policies are available upon written request.

7. Project Insurance Program Premiums

The Owner will be responsible for the payment of the project insurance program premiums. All return insurance premiums, insurance dividends, or monies due or to become due in connection with the project insurance program would be to the benefit of (or be the responsibility of) the Owner and are hereby assigned to the Owner.

8. Waiver of Subrogation

Project participants covered under the project insurance program hereby waive all rights of recovery against one another for their on-site activities only.

9. Other Insurance Needed As Determined by Contractors

The project insurance program including the OCIP, as previously outlined, is intended to afford broad coverage and relatively high limits of liability, but will not provide all the insurance needed. Contractors should have their insurance agent, broker or consultant review the coverages and limits outlined herein and in your contract for adequacy against your existing program.

10. Coverages Not Part of OCIP or provided by the Owner

Contractors and Subcontractors acknowledge that any loss not covered by Commercial General Liability and Excess shown above is the responsibility of the Contractors and Subcontractors including but not limited to the following:

- Workers' Compensation/Employer's Liability
- Automobile Liability
- Automobile Physical Damage
- Property coverage, including but not limited to Contractors' Equipment, rented, leased or borrowed Equipment, Tools, or Personal Property
- General Liability/Excess Liability for Off-Site Activities
- Employment Practices Liability
- Professional Liability/Errors and Omissions
- Jones Act Coverage (Crew Members) if applicable
- Protection and Indemnity (Operations of Vessels) if applicable
- Marine Liability if applicable
- Aircraft including Unmanned Aircraft/Drones
- Surety Bonds

6. Insurance Provided by Design Builder, Contractors and Subcontractors of every tier

All Contractors, whether enrolled or excluded, are required to maintain as a reimbursable cost of the work and for the duration of their Contract, insurance limits and requirements pursuant to each Enrolled or Excluded Parties' Contract.

Prior to coming on the Project Site, Contractor must provide a certificate of insurance evidencing all requirements to the appropriate party. The limits shown in the Contract are minimum limits and are not intended to limit the Contractors' liability.

1. **Self-Insured Retentions**
   The funding of deductibles and self-insured retentions for any required insurance maintained by Contractor shall be the sole responsibility of Contractor, including any deductibles or self-insured retentions applicable to claims involving the additional insureds.

2. **Certificate of Insurance**
   Prior to commencing any work at the Project Site and annually thereafter for so long as insurance is required to remain in effect, the Design Builder and all Eligible Contractors and Subcontractors of every tier must provide the Owner and OCIP Program Manager with a Certificate of Insurance confirming that all the requirements in this Insurance Manual have been met. Failure of any party to provide such certificates of insurance will not be relief from the responsibility to carry and maintain such insurance. Upon request, a Contractor shall submit to the Owner copies of the provisions in its insurance policies complying with the requirements in this exhibit.

3. **Wrap up Exclusion**
   If any party's insurance includes an exclusion tied to Owner Controlled Insurance Programs (a.k.a."Wrap-ups" or "CIPs") or other project-specific insurance, it may apply only to the extent of coverage available to that party under the OCIP or other Contractor-provided insurance. Such exclusion may not be broader than what the OCIP or such other Contractor-provided insurance actually covers.

4. **Indemnity Obligations**
   The insurance coverages maintained by Contractor shall not limit any of the Contractor's indemnity obligations or other liabilities under the Contract Documents.

Certificate of Insurance must include the following:

Additional Insureds / Primary and Non-Contributory

Project: LV Stadium Events Company, LLC, Stadium Authority, ICON Venue Group, LLC, Clark County Stadium Authority, the Team, each Lender and their respective members, officers, directors, trustees, shareholders, public officials, members, partners, agents, employees, successors and assigns, and all others as required by contract; shall be included as additional insureds on the CGL, Automobile Liability, Pollution Liability, and Umbrella/Excess Liability policies, with respect to liabilities arising out of both the ongoing and completed operations of Contractor relative to offsite coverages and exposures. For CGL and Umbrella / Excess Liability, such additional insured coverage shall be subject to the terms of ISO additional insured endorsement forms CG 20 10 (ongoing operations) and form CG 20 37 (products-completed operations), or substitute form(s) providing equivalent coverage as required by contract. Additional insured coverage shall be primary and non-contributing with respect to any insurance or self-insurance maintained by the additional insureds.

Notice of Cancellation:

All required policies shall be endorsed to provide that notice of cancellation shall be given to Owner by insurance agent/broker or carrier; or if unavailable, Contractors must provide Owner with thirty (30) days advance written notice of cancellation or non-renewal ten (10) days in the event of cancellation for non-payment of premium.

Waiver of Subrogation

All required insurance except Professional Liability, shall include a waiver of subrogation in favor of the Owner, Design Builder, and any applicable lenders, or other parties as required and their respective affiliates, officers, directors and employees. The required insurance shall support and not prohibit the foregoing waiver. Any deductibles or self-insured retentions shall be borne by the respective Contractor at its sole expense, without reimbursement by Owner, and shall be treated as “insurance” for purposes of the waiver in this Section.

Certificate Holder is:

LV Stadium Events Company, LLC
c/o Willis of Minnesota, Inc.
OCIP Administrator
1600 Utica Avenue South, Suite 600
Minneapolis, MN 55416

7. Enrolling in the OCIP

Enrollment Procedures:

What Forms are required?

Complete the following forms within the time frames specified below:

- OCIP Enrollment Form- Prior to starting work on Project Site for original contract, to identify cost of additional contract(s), or as determined by the Owner.

How Do I Complete the OCIP Enrollment form?

Enrollment into the OCIP program is mandatory but **NOT** automatic. Access to the Project Site will not be granted until enrollment is completed. Unenrolled/Excluded Party or Parties do not have any insurance coverage under the OCIP.

- Each Eligible Party working at the Project Site shall complete the Enrollment Form.
- If an Enrolled Party is awarded more than one Agreement on the Project, the Enrolled Party is required to complete a separate Enrollment Form for each Agreement.
- Eligible, Enrolled and Excluded Parties shall also provide certificate(s) of insurance and endorsements as required in each Contractors' or Subcontractors' Agreement.

8. OCIP Forms

- Notice of Contract Award – Request for Insurance
- Sample Certificate of Insurance

Las Vegas Stadium Project

Notice of Contract Award and Request for Insurance

☐ Initial Enrollment ☐ Additional Contract

Enrolled Contractor Information

Contractor Legal Name: _____ Individual: ☐ Partnership: ☐ Corp: ☐ J/V: ☐

Legal Address: _____ TIN#: _____

City: _____ St: _____ Zip Code: _____

Site Contact: _____ Site Address: _____

Phone: ( ) - Cell: ( ) - Fax: ( ) - Email: _____

Office Contact: _____ Phone: ( ) - Fax: ( ) - Email: _____

Insurance Contact: _____ Phone: ( ) - Fax: ( ) - Email: _____

Are you using a Leasing Company? ☐ YES ☐ NO If yes Leasing Company Name: _____

Are you a Leasing Company? ☐ YES ☐ NO

Contract Information

Type of Work: _____ Contract #: _____ Contract Value: $ _____

Project Description: _____ Off-site Work within scope of contract: ☐ YES ☐ NO

Awarding Contractor: _____ Prime Contractor: _____

Award Date: _____ Est. Start Date: _____ Est. Completion Date: _____ Self-Performed: _____ %

Subcontracted _____ % Est. # of Subcontractors: _____

Agreement

It is each Enrolled Contractors responsibility to notify its own insurance carrier that work to be performed at the Project Site, under this contract will be covered by the OCIP subject to policy terms and conditions, on a primary and non-contributory basis.

Any and all returns of premiums, dividends, discounts or other adjustments to any OCIP policy is assigned, transferred and set over absolutely to Owner. This assignment is valid for insurance policies whose premiums have been paid by the Owner on behalf of such Contractors.

This agreement shall be effective when signed below or in counterpart, and photocopy, facsimile, electronic or other copies shall have the same effect for all purposes as an ink-signed original.

Signed: _____ *Title:* _____ *Date:* _____

Subcontractor shall submit this form for enrollment to**:**

Mortenson-McCarthy
Attention: Jalon Brooks
3920 W. Hacienda Ave.
Las Vegas, NV 89118

Email: Jalon.Brooks@mmcjvlv.com

Subcontractor shall submit this form for all **sub-tier** enrollment to**:**

Willis of Minnesota, Inc.
Attention: OCIP Administrator
1600 Utica Avenue South
Minneapolis, MN 55416

Fax: 763-302-7200
Direct: 763-302-7101
Email: denise.wishcop@willistowerswatson.com
cc: julie.sarkauskas@willistowerswatson.com;

CERTIFICATE OF LIABILITY INSURANCE

DATE (MM/DD/YYY)

THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AFFIRMATIVELY OR NEGATIVELY AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW. THIS CERTIFICATE OF INSURANCE DOES NOT CONSTITUTE A CONTRACT BETWEEN THE ISSUING INSURER(S), AUTHORIZED REPRESENTATIVE OR PRODUCER, AND THE CERTIFICATE HOLDER.

IMPORTANT: If the certificate holder is an ADDITIONAL INSURED, the policy(ies) must be endorsed. If SUBROGATION IS WAIVED, subject to the terms and conditions of the policy, certain policies may require an endorsement. A statement on this certificate does not confer rights to the certificate holder in lieu of such endorsement(s).

PRODUCER	CONTACT NAME:	
INSURANCE AGENT'S NAME **ADDRESS** **CITY, STATE ZIP CODE** **TELEPHONE NO. (INCLUDING AREA CODE)**	PHONE (A/C, No. Ext):	FAX (A/C, No):
	E-MAIL ADDRESS:	
	INSURER(S) AFFORDING COVERAGE	NAIC#
INSURED	INSURER A : ABC Insurance Company	
YOUR COMPANY NAME **ADDRESS** **CITY, STATE, ZIP CODE** **TELEPHONE NO. (INCLUDING AREA CODE)**	INSURER B : DEF Insurance Company	
	INSURER C : GHI Insurance Company	
	INSURER D : JKL Insurance Company	
	INSURER E :	
	INSURER F:	

COVERAGES CERTIFICATE NUMBER: REVISION NUMBER:

THIS IS TO CERTIFY THAT THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATE MAY BE ISSUED OR MAY PERTAIN. THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS.

INSR LTR	TYPE OF INSURANCE	ADDL INSR	SUBR WVD	POLICY NUMBER	POLICY EFF (MM/DD/YYY)	POLICY EXP (MM/DD/YY)	LIMITS	
A	GENERAL LIABILITY COMMERCIAL GENERAL LIABILITY CLAIMS-MADE [ ] OCCUR [X] GEN'L AGGREGATE LIMIT APPLIES PER: POLICY [ ] PRO-JECT [x] LOC [ ]	x	x	Policy Number	MO/DAY/YR	MO/DAY/YR	EACH OCCURRENCE DAMAGES TO RENTED PREMISES(Ea occurrence) MED EXP (Any one person) PERSONAL & ADV INJURY GENERAL AGGREGATE PRODUCTS-COMP/OP AGG	PER CONTRACT PER CONTRACT $ PER CONTRACT PER CONTRACT PER CONTRACT
B	AUTOMOBILE LIABILITY [ ] ANY AUTO [x] ALL OWNED AUTOS [x] HIRED AUTOS [ ] SCHEDULED AUTOS [X] NON-OWNED AUTOS	x	x	Policy Number	MO/DAY/YR	MO/DAY/YR	COMBINED SINGLE LIMIT (Ea accident) BODILY INJURY(Per person) BODILY INJURY(Per accident) PROPERTY DAMAGE (Per accident)	PER CONTRACT $ $ $
C	[ ] UMBRELLA LIAB [x] EXCESS LIAB [ ] CLAIMS-MADE [ ] DED [ ] RETENTION $	x	x	Policy Number	MO/DAY/YR	MO/DAY/YR	EACH OCCURRENCE AGGREGATE	PER CONTRACT Requirements
D	WORKERS COMPENSATION AND EMPLOYERS ' LIABILITY Y/N [ ] ANY PROPRIETOR/PARTNER/EXECUTIVE OFFICER/MEMBER EXCLUDED? **(Mandatory in NH)** If yes, describe under DESCRIPTION OF OPERATIONS below	N/A	x	Policy Number	MO/DAY/YR	MO/DAY/YR	[X] WC Statutory Limits [ ] OTH-ER E.L. EACH ACCIDENT E.L. DISEASE – EA EMPLOYEE E.L. DISEASE – POLICY LIMIT	 PER CONTRACT PER CONTRACT PER CONTRACT
A	Professional Liability(if required)						(See contract requirements)	

DESCRIPTION OF OPERATIONS/LOCATIONS/VEHICLES (Attach ACORD 101, Additional Remarks Schedule, if more space is required)

Project: Las Vegas Stadium Project. LV Stadium Events Company, LLC, Stadium Authority, ICON Venue Group, LLC, Clark County Stadium Authority, the Team, each Lender and their respective members, officers, directors, trustees, shareholders, public officials, members, partners, agents, employees, successors and assigns, and all others as required by contract; shall be included as additional insureds on the General Liability, Automobile Liability, Pollution Liability, and Excess Liability policies, with respect to liabilities arising out of both the ongoing and completed operations of Contractor relative to offsite coverages and exposures. For General Liability and Excess Liability, such additional insured coverage shall be subject to the terms of ISO additional insured endorsement forms CG 20 10 (ongoing operations) and form CG 20 37 (products-completed operations), or substitute form(s) providing equivalent coverage as required by contract. Additional insured coverage shall be primary and non-contributing with respect to any insurance or self-insurance maintained by the additional insureds. Waiver of subrogation in favour of LV Stadium Events Company, LLC and all other required parties applies to General Liability, Excess Liability, Auto Liability and Workers' Compensation policies as required by written contract, written agreement or permit and executed prior to loss. General Liability insurance shall apply to locations away from the project site as defined in the OCIP manual.

CERTIFICATE HOLDER	**CANCELLATION**
LV Stadium Events Company, LLC c/o **Willis of Minnesota, Inc.** **OCIP Administrator** **1600 Utica Avenue South, Suite 600** **Minneapolis, MN 55411**	SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, NOTICE WILL BE DELIVERED IN ACCORDANCE WITH THE POLICY PROVISIONS. AUTHORIZED REPRESENTATIVE

9. General Liability Claim Reporting

Enrolled Contractors will:

Report all Project Site incidents/accidents resulting in property damage or bodily injury (other than injuries covered by worker's compensation insurance) to your Project Manager, who will promptly notify Ryan Kane of Mortenson's Risk Management Department for proper reporting to insurance companies.

Owner and Contractors will assist in the handling, investigation, and mitigation of all incidents/accidents (other than injuries covered by worker's compensation insurance) regardless of whether the incident results in an injury or insurance claim.

The following persons shall be immediately notified by e-mail or telephone upon service of any lawsuits or citations filed against Enrolled Parties or upon receipt of a letter of representation:

Design Builder

Ryan Kane
M.A. Mortenson

Direct: 763-287-5126
Mobile: 612-812-3900
Email: ryan.kane@mortenson.com

Willis Towers Watson

Marty Berger
Willis of Minnesota, Inc.

Direct: 763-302-7154
Mobile: 612-812-9474
Email: marty.berger@willistowerswatson.com

Failure to timely answer a lawsuit may result in a default judgment. The Enrolled Party served with the lawsuit will be financially responsible for all judgments and expenses associated with a default judgment to the extent such default judgment was the result of untimely notice of lawsuit to the OCIP general liability and excess liability insurers.

OCIP Project Insurance Manual Updates:

11/01/2017 – Original Manual

11/10/207 – Version #1

- Correction to “Section 9 Heading” and amended direct claim reporting to reflect “your” project manager in lieu of “the” project manager.
- Included Completed Ops language from GL and XL policy.
- Updated list of Additional Insureds on page 15 to be included on Certificate of Insurance.
- Removed Unemployment ID Number on Notice of Award Form
- Added City, State and Zip Code to Notice of Award Form

12/12/2017 – Version #2

- Added Jalon Brooks to distribution for Notice of Contract Award
- Revised Certificate of Insurance requirements – sample certificate description box

EXHIBIT I

Change Order Pricing

1. The increase or decrease in the GMP shall be determined in one of the following ways and, unless otherwise approved or directed by StadCo, in the precedence of the order listed:

(a) by an accepted unit price proposed in the GMP Amendment and incorporated in the Agreement.

(b) by a lump sum increase or decrease, as applicable, agreed to by StadCo and Design-Builder based on Design-Builder's submission of reasonable supporting data, including Subcontractor pricing details, plus allowances for design and construction contingencies for the applicable Work and a fee pursuant to **Section 7.4.5** of this Agreement equal to three point nine percent (3.9%) of the actual Cost of the Work.

(c) by mutually agreeable unit prices for the Work, with allowance for Design-Builder's profit and overhead.

(d) on the actual Cost of the Work, plus allowances for design and construction contingencies for the applicable Work and a fee a fee pursuant to **Section 7.4.5** of this Agreement equal to [redacted] of the actual Cost of the Work.

2. Except for unit prices included in the GMP Amendment, and unless otherwise approved by StadCo, for proposed changes in the Work Design-Builder shall submit an itemized list of quantities with the applicable unit cost and extended price for each, in such form and detail as required by StadCo.

3. On changes where the value or extent of Work cannot be reasonable pre-determined or agreed upon, StadCo may authorize Work to proceed on an agreed upon cost plus basis, not to exceed a maximum amount. In such cases, the basic costs and mark-up for overhead, profit and markup will be in accordance with this Exhibit.

4. Except for material changes to the Architectural Program, Design-Builder agrees it shall not be entitled to payment of Fee on the first [redacted] worth of Change Orders in excess of the GMP.

EXHIBIT J

Site Boundaries

Off-site scope is contained within the red and blue lines.

Excluded from on-site and off-site.

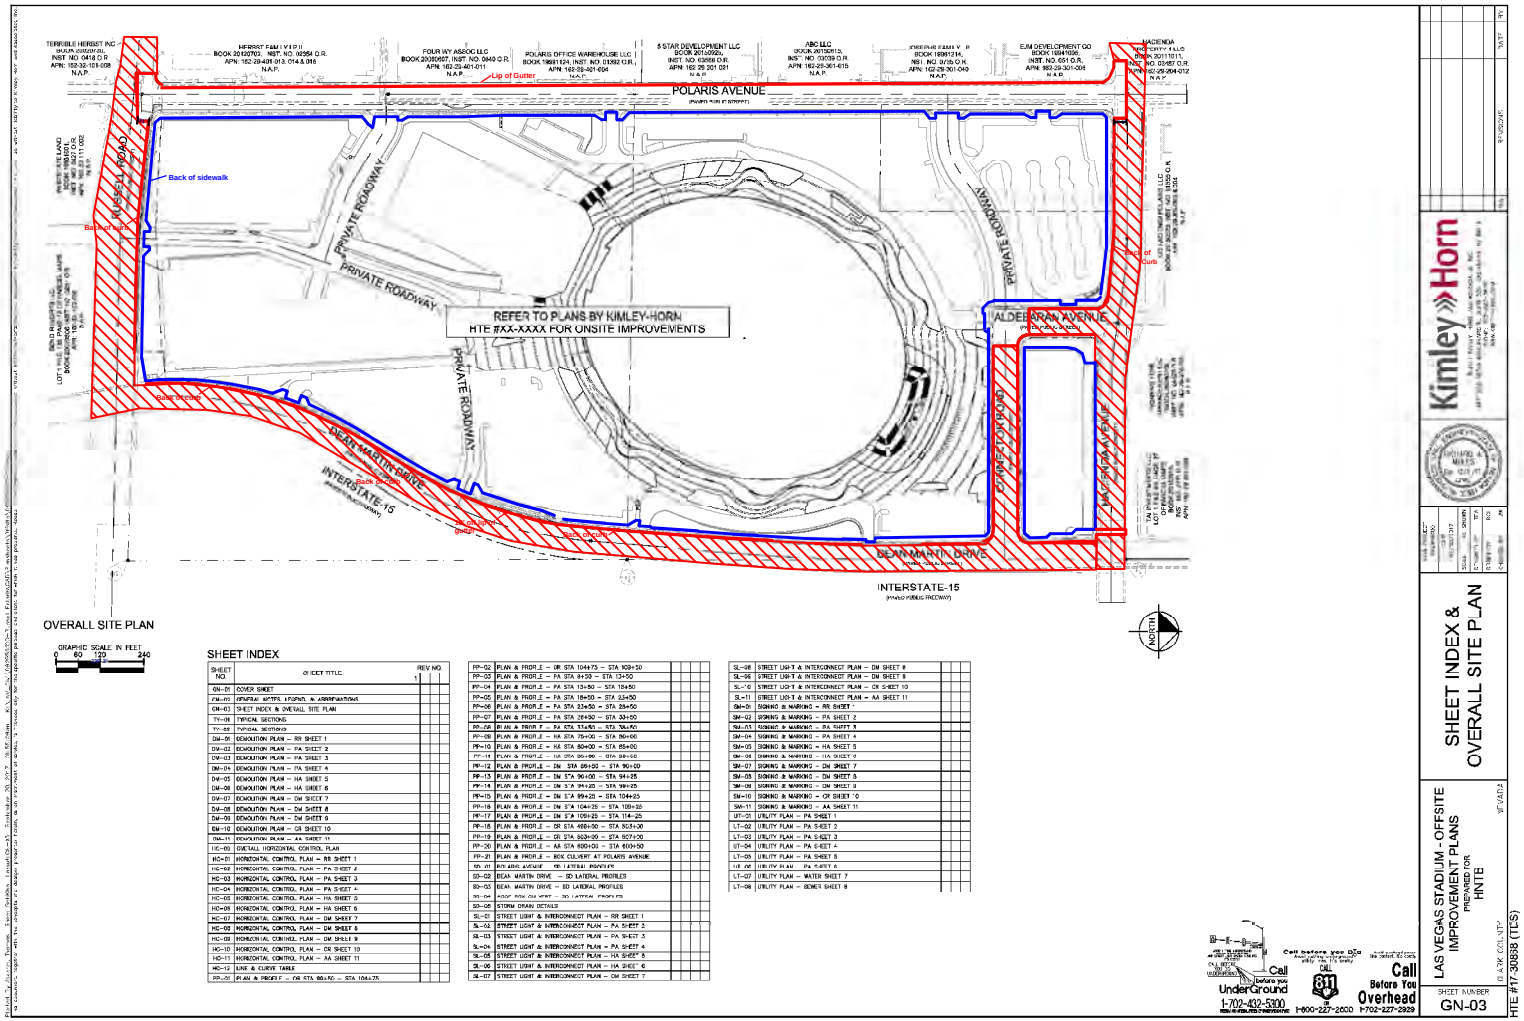

OVERALL SITE PLAN

GRAPHIC SCALE IN FEET
0 60 120 240

SHEET INDEX

SHEET NO.	SHEET TITLE	REV NO.
GN-01	COVER SHEET	
GN-02	GENERAL NOTES, LEGEND, & ABBREVIATIONS	
GN-03	SHEET INDEX & OVERALL SITE PLAN	
TY-01	TYPICAL SECTIONS	
TY-02	TYPICAL SECTIONS	
DM-01	DEMOLITION PLAN – RR SHEET 1	
DM-02	DEMOLITION PLAN – PA SHEET 2	
DM-03	DEMOLITION PLAN – PA SHEET 3	
DM-04	DEMOLITION PLAN – PA SHEET 4	
DM-05	DEMOLITION PLAN – HA SHEET 5	
DM-06	DEMOLITION PLAN – HA SHEET 6	
DM-07	DEMOLITION PLAN – DM SHEET 7	
DM-08	DEMOLITION PLAN – DM SHEET 8	
DM-09	DEMOLITION PLAN – DM SHEET 9	
DM-10	DEMOLITION PLAN – CR SHEET 10	
DM-11	DEMOLITION PLAN – AA SHEET 11	
HC-00	OVERALL HORIZONTAL CONTROL PLAN	
HC-01	HORIZONTAL CONTROL PLAN – RR SHEET 1	
HC-02	HORIZONTAL CONTROL PLAN – PA SHEET 2	
HC-03	HORIZONTAL CONTROL PLAN – PA SHEET 3	
HC-04	HORIZONTAL CONTROL PLAN – PA SHEET 4	
HC-05	HORIZONTAL CONTROL PLAN – HA SHEET 5	
HC-06	HORIZONTAL CONTROL PLAN – HA SHEET 6	
HC-07	HORIZONTAL CONTROL PLAN – DM SHEET 7	
HC-08	HORIZONTAL CONTROL PLAN – DM SHEET 8	
HC-09	HORIZONTAL CONTROL PLAN – DM SHEET 9	
HC-10	HORIZONTAL CONTROL PLAN – CR SHEET 10	
HC-11	HORIZONTAL CONTROL PLAN – AA SHEET 11	
HC-12	LINE & CURVE TABLE	
PP-01	PLAN & PROFILE – CR STA 95+50 – STA 104+75	
PP-02	PLAN & PROFILE – DR STA 104+75 – STA 109+50	
PP-03	PLAN & PROFILE – PA STA 9+50 – STA 13+50	
PP-04	PLAN & PROFILE – PA STA 13+50 – STA 18+50	
PP-05	PLAN & PROFILE – PA STA 18+50 – STA 23+50	
PP-06	PLAN & PROFILE – PA STA 23+50 – STA 28+50	
PP-07	PLAN & PROFILE – PA STA 28+50 – STA 33+50	
PP-08	PLAN & PROFILE – PA STA 33+50 – STA 38+50	
PP-09	PLAN & PROFILE – HA STA 75+00 – STA 80+00	
PP-10	PLAN & PROFILE – HA STA 80+00 – STA 85+00	
PP-11	PLAN & PROFILE – HA STA 85+00 – STA 89+00	
PP-12	PLAN & PROFILE – DM STA 85+00 – STA 90+00	
PP-13	PLAN & PROFILE – DM STA 90+00 – STA 94+25	
PP-14	PLAN & PROFILE – DM STA 94+25 – STA 99+25	
PP-15	PLAN & PROFILE – DM STA 99+25 – STA 104+25	
PP-16	PLAN & PROFILE – DM STA 104+25 – STA 109+25	
PP-17	PLAN & PROFILE – DM STA 109+25 – STA 114+25	
PP-18	PLAN & PROFILE – CR STA 488+50 – STA 503+00	
PP-19	PLAN & PROFILE – CR STA 503+00 – STA 507+00	
PP-20	PLAN & PROFILE – AA STA 600+00 – STA 609+00	
PP-21	PLAN & PROFILE – BOX CULVERT AT POLARIS AVENUE	
SD-01	BY ABC AVENUE – SD LATERAL PROFILE	
SD-02	DEAN MARTIN DRIVE – SD LATERAL PROFILES	
SD-03	DEAN MARTIN DRIVE – SD LATERAL PROFILES	
SD-04	ADDITIONAL BOX CULVERT – SD LATERAL PROFILES	
SD-05	STORM DRAIN DETAILS	
SL-01	STREET LIGHT & INTERCONNECT PLAN – RR SHEET 1	
SL-02	STREET LIGHT & INTERCONNECT PLAN – PA SHEET 2	
SL-03	STREET LIGHT & INTERCONNECT PLAN – PA SHEET 3	
SL-04	STREET LIGHT & INTERCONNECT PLAN – PA SHEET 4	
SL-05	STREET LIGHT & INTERCONNECT PLAN – HA SHEET 5	
SL-06	STREET LIGHT & INTERCONNECT PLAN – HA SHEET 6	
SL-07	STREET LIGHT & INTERCONNECT PLAN – DM SHEET 7	
SL-08	STREET LIGHT & INTERCONNECT PLAN – DM SHEET 8	
SL-09	STREET LIGHT & INTERCONNECT PLAN – DM SHEET 9	
SL-10	STREET LIGHT & INTERCONNECT PLAN – CR SHEET 10	
SL-11	STREET LIGHT & INTERCONNECT PLAN – AA SHEET 11	
SM-01	SIGNING & MARKING – RR SHEET	
SM-02	SIGNING & MARKING – PA SHEET 2	
SM-03	SIGNING & MARKING – PA SHEET 3	
SM-04	SIGNING & MARKING – PA SHEET 4	
SM-05	SIGNING & MARKING – HA SHEET 5	
SM-06	SIGNING & MARKING – HA SHEET 6	
SM-07	SIGNING & MARKING – DM SHEET 7	
SM-08	SIGNING & MARKING – DM SHEET 8	
SM-09	SIGNING & MARKING – DM SHEET 9	
SM-10	SIGNING & MARKING – CR SHEET 10	
SM-11	SIGNING & MARKING – AA SHEET 11	
UT-01	UTILITY PLAN – PA SHEET 1	
LT-02	UTILITY PLAN – PA SHEET 2	
LT-03	UTILITY PLAN – PA SHEET 3	
LT-04	UTILITY PLAN – PA SHEET 4	
LT-05	UTILITY PLAN – PA SHEET 5	
LT-06	UTILITY PLAN – PA SHEET 6	
LT-07	UTILITY PLAN – WATER SHEET 7	
LT-08	UTILITY PLAN – SEWER SHEET 8	

Call before you Dig
Call Before You UnderGround 1-702-422-5300
Call 811
Call Before You Overhead 1-702-227-2929

HTE #17-30838 (TLCS)

LAS VEGAS STADIUM - OFFSITE IMPROVEMENT PLANS
PREPARED FOR
HNTB

SHEET NUMBER
GN-03

SHEET INDEX & OVERALL SITE PLAN

LAS VEGAS NFL STADIUM

KEYPLAN

PLAN NORTH: TRUE NORTH:

DATE 1/19/2017
ISSUED FOR 62.5% GMP
PROJECT NO. 65787
ISSUED BY NHTB
DRAWN BY BMM
CHECKED BY TEK
APPROVED BY RAM

REV	DATE	DESCRIPTION

SHEET TITLE & NUMBER
SHEET INDEX & OVERALL SITE PLAN
GN-03

Copyright HNTB Nevada Inc. 2017

EXHIBIT K

Master Project Schedule

March 7, 2018

Re: Las Vegas Stadium
February 2018 Schedule Update

Tom Blanda:

Enclosed, please find a Time Scaled Critical Path Network representing the February 2018 Schedule Update of the above referenced Project. Also enclosed is the February 2018 Schedule Narrative.

This Schedule was developed and updated to represent Mortenson/McCarthy Las Vegas Stadium, A Joint Venture's (MMCJV) understanding of the information received from various potential Subcontractors, Design Team members and Owner's Representatives. Please note that the project schedule will continue to be developed and updated with your assistance as design durations, permitting durations, lead times and deliverable dates are refined. MMCJV will continue to review the start dates for various activities with you as the start dates approach.

Please notify MMCJV within five (5) working days upon receipt of this issuance in the event of any oversight and/or omissions.

If you should have any questions pertaining to the enclosed, please contact me at your earliest convenience.

Respectfully,

Heidi Brown

Attachments:
Schedule Narrative – February 2018
Schedule Update – February 2018

CC: File

Schedule Narrative – February 2018
Las Vegas Stadium

1.0 Project Status Overview

The project schedule has been updated with progress through March 4, 2018.

Upon inputting progress made in the Design and Development portions of schedule, and the impacts of known and potential changes, the overall total float of the Project is (0) working day(s).

Actual progress through March 4, 2018, considering the planned durations, supports the certificate of occupancy date of July 1, 2020 and substantial completion date of July 31, 2020.

2.0 Anticipated Project Critical Paths

The Project's critical path runs through the design and permit approval. Following deep foundations and concrete structure, the path continues through the steel building structure, precast, cable net roof systems, lower bowl precast, the interior bowl equipment and finishes, playing field installation to support completion of the start-up, testing and inspection of the building prior to occupancy.

3.0 Upcoming Critical Milestones / Activities

To support the above path, the following activities will be critical to ensure the Project Schedule is maintained:

- Receive approval for Permit Package 3a on 26Mar18
- Issue design documents and submit Permit Package 3b to CC for review on 12Mar18 - receive permit for Permit Package 3b on 11May18
- Receive GMP approval on 12Mar18
- Issue design documents and submit Permit Package 4 to CC for review on 02Apr18 – receive permit for Permit Package 4 on 05Jun18

4.0 Logic & Duration Revisions Incorporated In This Schedule

The following revisions were made to the schedule to identify and track potential and real impacts, better define the work required, or split an activity into more detail to better track items of work:

- MMCJV has incorporated the following additional detail into the schedule and will continue to revise as design progresses:
    - Steel submittal sequences to match the erection sequence have been revised in the February update.
    - Elevator installation activities have been added
    - SOMD rebar shop drawings have been included in more detail
    - Steel pan stair installation in the cores has been added
    - NVE shoofly fragnet has been added
    - Names of all core activities have been revised to match the names in the architectural drawings

Las Vegas Stadium

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
Summary and Milestones					
Project Summary					
L000-1A10	Design	731	02-Dec-16 A	04-Jan-19	117
L000-1A11	Construction	972	28-Dec-17 A	31-Jul-20	0
Scheduled Events					
L001-1A3A	2017 NFL Draft	0	27-Apr-17 A		
L002-1A3A	2017 NFL Draft	0	28-Apr-17 A		
L003-1A3A	2017 NFL Draft	0	29-Apr-17 A		
L004-1A3A	2017/18 - Preseason - Week 1 (Away at Cardinals)	0	12-Aug-17 A		
L005-1A3A	2017/18 - Preseason - Week 2 (Home vs Rams)	0	19-Aug-17 A		
L006-1A3A	2017/18 - Preseason - Week 3 (Away at Cowboys)	0	26-Aug-17 A		
L007-1A3A	2017/18 - Preseason - Week 4 (Home vs Seahawks)	0	31-Aug-17 A		
L008-1A3A	2017/18 - Season - Week 1 (Away at Titans)	0	10-Sep-17 A		
L009-1A3A	2017/18 - Season - Week 2 (Home vs Jets)	0	17-Sep-17 A		
L010-1A3A	2017/18 - Season - Week 3 (Away at Redskins)	0	24-Sep-17 A		
L011-1A3A	2017/18 - Season - Week 4 (Away at Broncos)	0	01-Oct-17 A		
L012-1A3A	2017/18 - Season - Week 5 (Home vs Ravens)	0	08-Oct-17 A		
L013-1A3A	2017/18 - Season - Week 6 (Home vs Chargers)	0	15-Oct-17 A		
L014-1A3A	2017/18 - Season - Week 7 (Home vs Chiefs)	0	19-Oct-17 A		
L015-1A3A	2017/18 - Season - Week 8 (Away at Bills)	0	29-Oct-17 A		
L016-1A3A	2017/18 - Season - Week 9 (Away at Dolphins)	0	05-Nov-17 A		
L017-1A3A	2017/18 - Season - Week 10 (Bye)	0	12-Nov-17 A		
L018-1A3A	2017/18 - Season - Week 11 (Home vs Patriots)	0	19-Nov-17 A		
L019-1A3A	2017/18 - Season - Week 12 (Home vs Broncos)	0	26-Nov-17 A		
L020-1A3A	2017/18 - Season - Week 13 (Home vs Giants)	0	03-Dec-17 A		
L021-1A3A	2017/18 - Season - Week 14 (Away at Chiefs)	0	10-Dec-17 A		
L022-1A3A	2017/18 - Season - Week 15 (Home vs Cowboys)	0	17-Dec-17 A		
L023-1A3A	2017/18 - Season - Week 16 (Away at Eagles)	0	25-Dec-17 A		
L024-1A3A	2017/18 - Season - Week 17 (Away at Chargers)	0	31-Dec-17 A		
L025-1A3A	2017/18 - Playoffs	30	07-Jan-18 A	04-Feb-18 A	
Milestones					
L000-1A50	Construction Manager Selected	0		23-Dec-16 A	
L000-1A51	Issue LATP for Box-Culvert	0	17-Nov-17 A		
L000-1A52	Issue LATP for Demo/Site Clearing/Mass Excavation	0	27-Nov-17 A		
L000-1A54	Issue LATP for Deep Foundations	0	12-Dec-17 A		
L000-1A70	Place Mill Order - Truss Columns	0	22-Feb-18 A		
L000-1A57	GMP Established	0		12-Mar-18	3
L000-1A58	Place Mill Order - Structural Frame	0	17-Apr-18		12
L000-1A72	Place Mill Order - Canopy	0	17-Apr-18		81
L000-1A71	Place Mill Order - Long Span at Operable Field	0	17-Apr-18		61
L000-1A189	Start Box Culvert Work	0	01-Dec-17 A		
L000-1A53	Start Demo / Site Preparation	0	19-Dec-17 A		
L000-1A55	Start Construction (Earthwork under LATP)	0	28-Dec-17 A		
L000-1A56	Start Construction (Deep Foundations)	0	20-Feb-18 A		
L000-1A79	Start Foundations	0	12-Mar-18		3
L000-1A89	Start Elevated Concrete Structure	0	16-Apr-18		2
L000-1A190	Place First Pan & Joist Deck	0	14-May-18		0
L000-1A191	Start Slab on Grade Construction	0	27-Jul-18		31

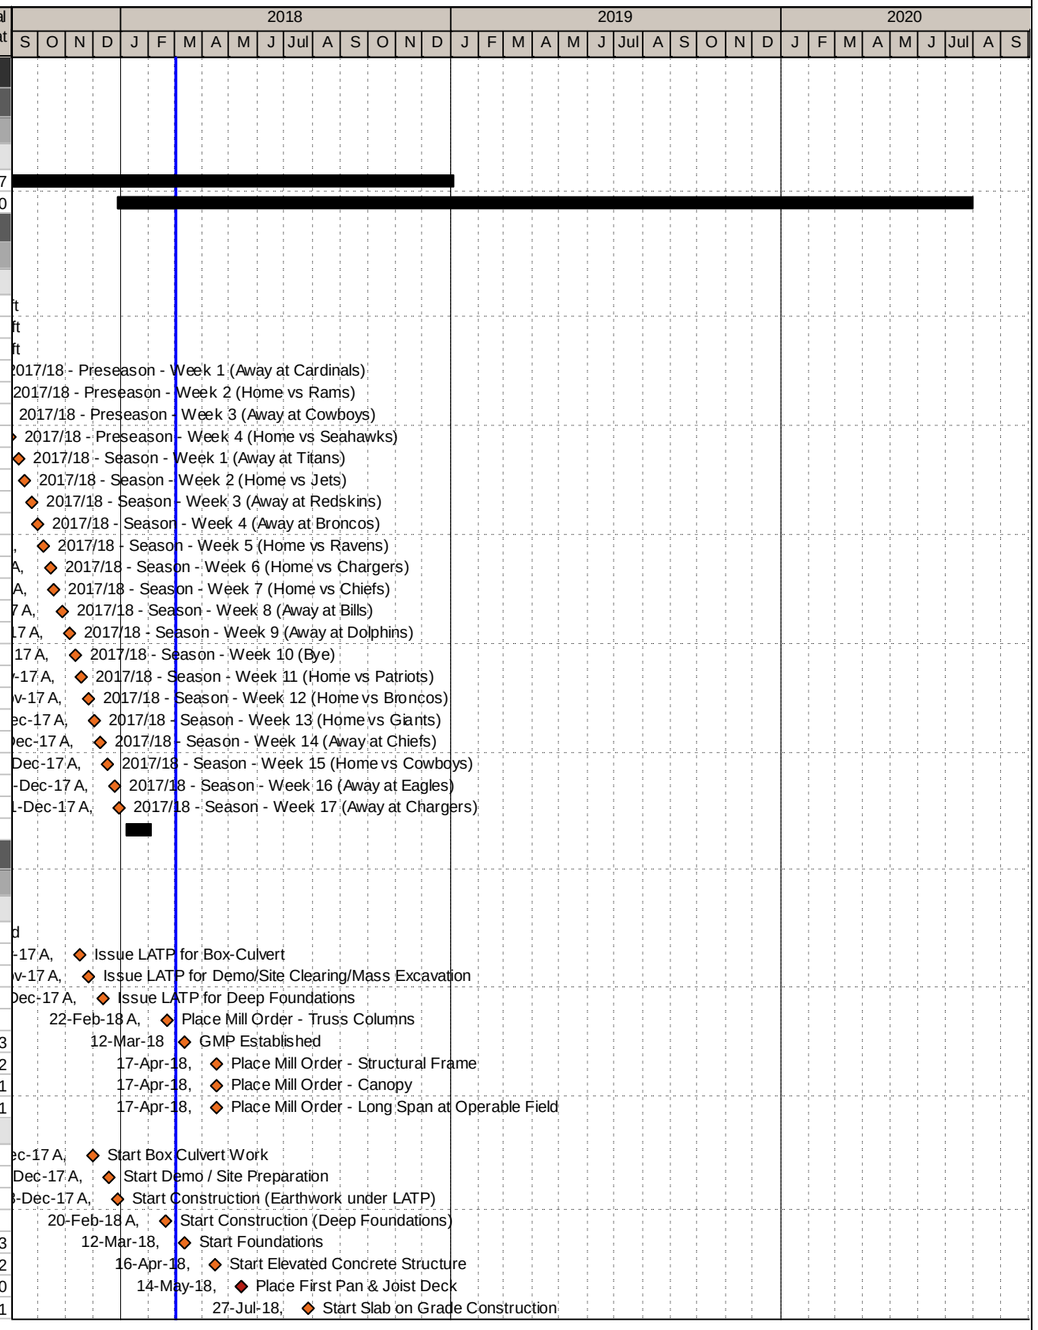

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
L000-1A99	Start Structural Steel Erection - Truss Columns	0	09-Aug-18		7
L000-1A109	Start Precast Stadia Erection	0	12-Sep-18		0
L000-1A179	Start Structural Steel Erection - Structural Frame	0	27-Sep-18		1
L000-1A119	Start Interior Rough-in	0	24-Oct-18		48
L000-1A192	Start Structural Steel Erection - Roof Canopy	0	02-Jan-19		16
L000-1A193	Complete Structural Steel Erection - Structural Frame	0		15-Mar-19	16
L000-1A129	Start Drywall and Interior Finishes	0	21-Mar-19		47
L000-1A194	Start Vertical Enclosure Curtainwall Unit Installation	0	22-May-19		6
L000-1A159	Steel Roof Canopy Complete	0		24-May-19	22
L000-1A69	Permament Power to Stadium	0		31-Jul-19*	46
L000-1A195	Complete Cable Net Big Lift	0		08-Aug-19	21
L000-1A196	Start ETFE Roofing Installation	0	14-Aug-19		3
L000-1A197	Complete Precast Stadia Erection	0		21-Oct-19	65
L000-1A149	Building Vertical Enclosure Complete	0		25-Nov-19	18
L000-1A139	Building Roof Systems Complete	0		18-Dec-19	4
L000-1A198	Complete Concrete Slab on Grade Construction	0		03-Feb-20	41
L000-1A59	Certificate of Occupancy	0		01-Jul-20*	0
L001-1A50	Substantial Completion	0		31-Jul-20*	0
Planning and Development					
Planning and Development					
L000-2B10	Legislative Approval Process	20	03-Oct-16 A	28-Oct-16 A	
L001-2B10	Approval of $750M Budget	0		28-Oct-16 A	
L002-2B10	Site Selection Process	20	02-Dec-16 A	30-Dec-16 A	
L003-2B10	Site Selection	0		31-Dec-16 A	
L004-2B10	Entitlement Process	181	01-May-17 A	13-Sep-17 A	
L001-2B20	Form Public Stadium Authority	60	15-Nov-16 A	13-Jan-17 A	
L000-2B20	Prepare Formal Relocation Application	90	15-Oct-16 A	13-Jan-17 A	
L003-2B20	File League Relocation Application	0	19-Jan-17 A		
L002-2B20	Stadium Authority Hires Legal Counsel	31	14-Jan-17 A	13-Feb-17 A	
L004-2B20	NFL League Office Relocation Review and Approval	31	19-Jan-17 A	18-Feb-17 A	
L005-2B20	NFL Owners Relocation Review	30	19-Feb-17 A	20-Mar-17 A	
L006-2B20	Relocation Application Approved	0		27-Mar-17 A	
L007-2B20	Detail Agency Agreements / Lease & Related Documents	90	28-Mar-17 A	15-Dec-17 A	
L000-2B30	Rusell Road Site Initial Due Diligence	30	06-Sep-16 A	05-Oct-16 A	
L002-2B30	Close on Russel Road Site Acquisition	0		01-May-17 A	
L001-2B30	Prepare & File High Impact Project Report	46	28-Mar-17 A	21-Jun-17 A	
Reviews & Approvals					
Design & Budget Review & Approval					
SA00-3D10	Raiders Review & Approval - Conceptual Plan	6	01-May-17 A	30-May-17 A	
SA01-3D10	Raiders Review & Approval - 25% GMP Scope/Design/Budget	7	10-Aug-17 A	01-Sep-17 A	
SA02-3D10	Raiders Review & Approval - 60% GMP Scope/Design/Budget	5	16-Nov-17 A	30-Nov-17 A	
SA04-3D10	Raiders Review & Approval - GMP Scope/Design/Budget	7	06-Mar-18	12-Mar-18	3
Trade Partner Procurement Review & Approval					
SA01-3D20	Raiders Review & Approval - RFP Package	5	30-Jun-17 A	05-Jul-17 A	
Design and Pre-Construction					
Design					
Design Team Selection					
SD10-3D10	Authorization to Proceed with Conceptual Design	114	04-Dec-16 A	27-Mar-17 A	
SD11-3D10	Full Release to Proceed with Design	0	28-Mar-17 A		
Programming & Concept Design					
SD20-3D10	Draft Comprehensive Stadium Program & Outline Spec	34	29-Mar-17 A	28-Apr-17 A	

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
SD21-3D10	Resume & Complete Conceptual Stadium & Site Design	34	29-Mar-17 A	28-Apr-17 A	
Field Exploration					
SD30-3D10	Exploratory Drilling	30	23-Mar-17 A	31-Mar-17 A	
SD32-3D10	Pressuremeter Testing	6	30-Mar-17 A	31-Mar-17 A	
SD31-3D10	Down-Hole Seismic Testing	4	30-Mar-17 A	24-Apr-17 A	
Groundwater Study					
SD40-3D10	Well Paperwork Approval (Raiders)	7	30-Mar-17 A	04-Apr-17 A	
SD41-3D10	Well Permits	7	05-Apr-17 A	17-Apr-17 A	
SD42-3D10	Monitoring Well Construction	8	18-Apr-17 A	21-Apr-17 A	
SD43-3D10	GW Monitoring Well Observation & Sampling Commences	1	21-Apr-17 A	21-Apr-17 A	
SD44-3D10	Groundwater Laboratory Testing for Permitting	12	21-Apr-17 A	02-Jun-17 A	
SD45-3D10	Discharge Permit	9	05-Sep-17 A	15-Sep-17 A	
SD49-3D10	Aquifer Testing	5	18-Sep-17 A	22-Sep-17 A	
Geotechnical Report					
SD51-3D10	Geotechnical Report for Early Structural System Consideration	5	10-Apr-17 A	14-Apr-17 A	
SD50-3D10	Laboratory Testing Part 1	30	31-Mar-17 A	28-Apr-17 A	
SD52-3D10	Engineering Analysis	30	27-Apr-17 A	05-May-17 A	
SD53-3D10	Draft Geotechnical Report	33	01-May-17 A	08-May-17 A	
SD54-3D20	Geotechnical Report (Phase 2) - Drilling	15	07-Jun-17 A	13-Jul-17 A	
SD54-3D30	Geotechnical Report (Phase 2) - Lab Testing	5	14-Jul-17 A	21-Jul-17 A	
SD54-3D10	Geotechnical Report (Phase 2) - Fault Study	24	20-Jul-17 A	18-Aug-17 A	
SD54-3D40	Geotechnical Report (Phase 2) - Engineering Analysis and Draft Report	10	14-Jul-17 A	03-Nov-17 A	
SD54-3D60	Geotechnical Report (Phase 2) - Issue Final Report	4	06-Nov-17 A	09-Nov-17 A	
Entitlements					
SD60-3D10	HNTB/Manica Prepare Submittal Items	59	30-Mar-17 A	21-Jun-17 A	
SD61-3D10	KH RISE Reports	30	30-Mar-17 A	21-Jun-17 A	
SD62-3D10	Submit Entitlements to Planning	5	22-Jun-17 A	28-Jun-17 A	
SD63-3D10	Entitlements - Filing Deadline	0		28-Jun-17 A	
SD64-3D10	Entitlements - Town Board Hearing	1	08-Aug-17 A	08-Aug-17 A	
SD65-3D20	Entitlements - Hold for FAA	1	09-Aug-17 A	05-Sep-17 A	
SD65-3D10	Entitlements - BCC Hearing	1	06-Sep-17 A	06-Sep-17 A	
SD66-3D10	Entitlements - Appeal Period	5	07-Sep-17 A	13-Sep-17 A	
SD67-3D10	Entitlements - Approved	0		13-Sep-17 A	
Tentative Map					
SD70-3D10	Prepare Tentative Map	29	25-May-17 A	20-Jun-17 A	
SD71-3D10	Submit Tentaive Map	2	21-Jun-17 A	22-Jun-17 A	
SD72-3D10	Tentative Map - Filing Deadline	0		28-Jun-17 A	
SD73-3D10	Tentative Map - Town Board Hearing	1	26-Jul-17 A	26-Jul-17 A	
SD74-3D10	Tentative Map - BCC Hearing	1	15-Aug-17 A	15-Aug-17 A	
SD75-3D10	Tentative Map - Appeal Period	5	16-Aug-17 A	22-Aug-17 A	
SD76-3D10	Tentative Map - Approved	0		22-Aug-17 A	
Entitlement Traffic Study					
SD80-3D10	Entitlement Traffic Study - Prepare Study	40	30-Mar-17 A	24-May-17 A	
SD81-3D10	Entitlement Traffic Study - Team Meeting to Review Impacts	2	25-May-17 A	26-May-17 A	
SD82-3D10	Entitlement Traffic Study - Submit to Planning	2	26-May-17 A	30-May-17 A	
SD83-3D10	Entitlement Traffic Study - County Review Prior to Entitlements	28	31-May-17 A	11-Jul-17 A	
Phase 1 Only Traffic Study					
SD850-3D10	Phase 1 Traffic Study - Reviewed by Ownership	5	07-Dec-17 A	13-Dec-17 A	
SD851-3D10	Phase 1 Traffic Study - KH Submits Study to Clark County & NDOT for Review	1	14-Dec-17 A	14-Dec-17 A	
SD852-3D10	Phase 1 Traffic Study - Clark County Review Process for Traffic Study Phase 1 (Expedited)	30	15-Dec-17 A	29-Jan-18 A	
SD853-3D10	Phase 1 Traffic Study - NDOT Review Process for Traffic Study Update for Phase 1	30	15-Dec-17 A	29-Jan-18 A	
SD855-3D10	Phase 1 Traffic Study - Approved	0		29-Jan-18 A	
Final Traffic Study					

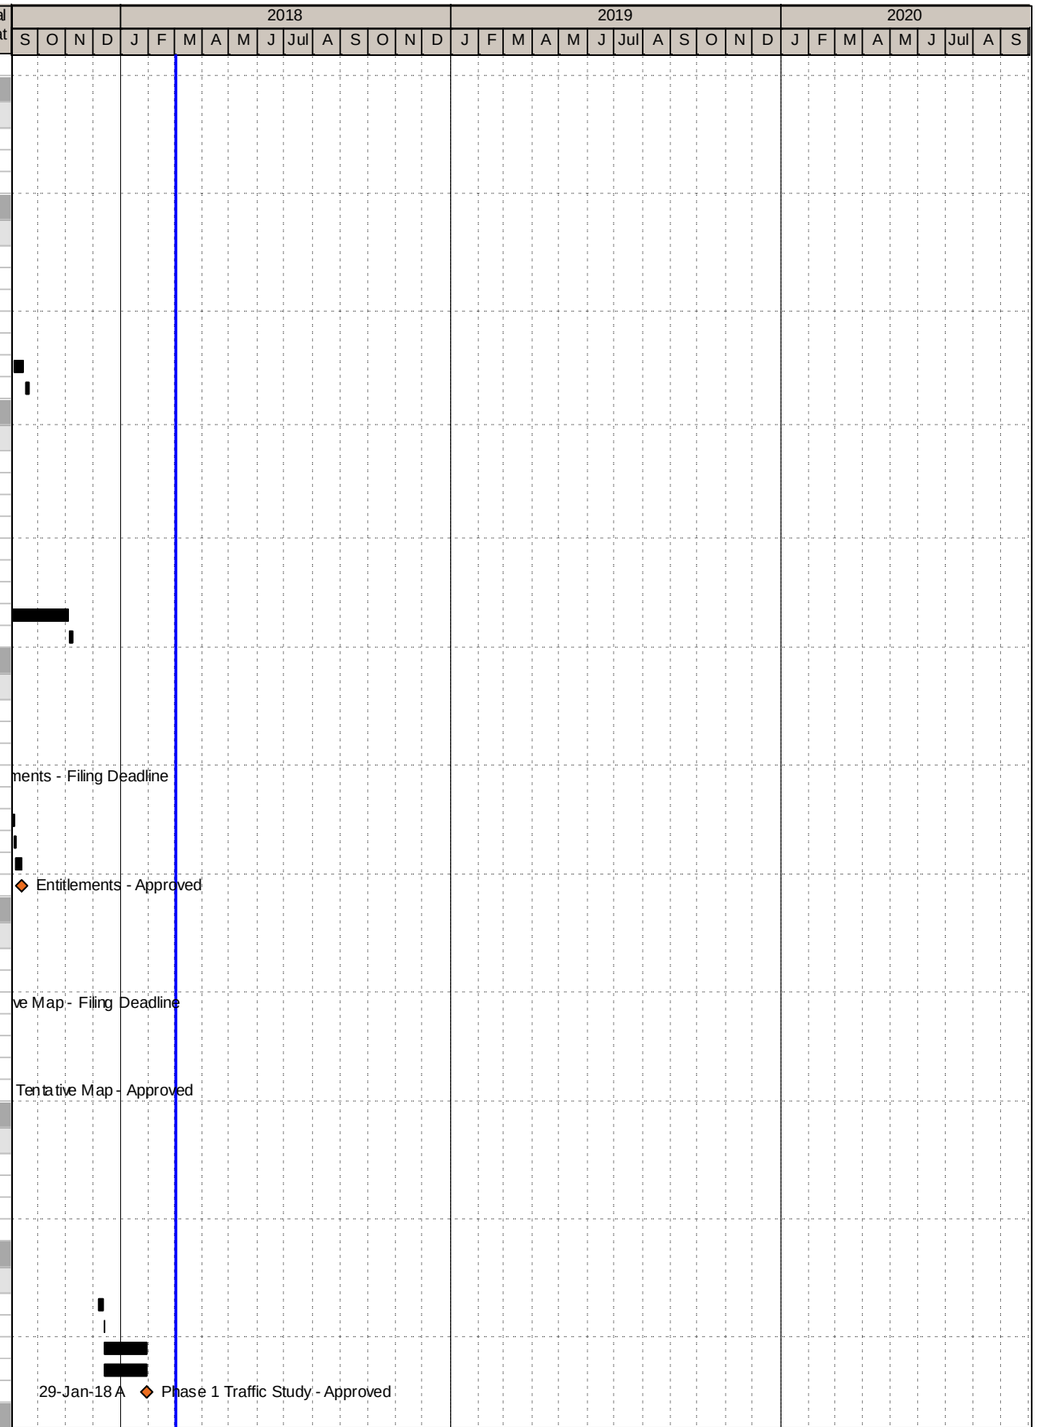

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
SD90-3D10	Final Traffic Study - Prepare Study	40	01-Feb-18 A	28-Mar-18	40
SD91-3D10	Final Traffic Study - Review	40	29-Mar-18	23-May-18	40
SD92-3D10	Final Traffic Study - Approved	0		23-May-18	40
Technical Drainage Study - Regional Facility					
SDA0-3D10	TDS Regional Fac - Box Re-Alignment Design & Prepare TDS	20	30-Mar-17 A	26-Apr-17 A	
SDA1-3D10	TDS Regional Fac - KH Submits Drainage Study to County for Review	0		26-Apr-17 A	
SDA2-3D10	TDS Regional Fac - Clark County Drainage Study Review	8	27-Apr-17 A	08-May-17 A	
SDA3-3D10	TDS Regional Fac - KH Receives Drainage Study Review Comments	0		08-May-17 A	
SDA4-3D10	TDS Regional Fac - KH Prepares Addendum #1 to the Drainage Study	5	08-May-17 A	15-May-17 A	
SDA5-3D10	TDS Regional Fac - Clark County Drainage Study Add #1 Review	7	15-May-17 A	24-May-17 A	
SDA6-3D10	TDS Regional Fac - Drainage Study Approval	0		25-May-17 A	
SDA7-3D10	TDS Regional Fac - CCRFCD Concurrence	28	26-May-17 A	17-Aug-17 A	
SDA8-3D10	TDS Regional Fac - Army Corp of Engineers Approval	110	01-Jun-17 A	15-Dec-17 A	
SDA8-3D20	TDS Regional Fac - Army Corp of Engineers Approval	0		15-Dec-17 A	
SDA8-3D30	TDS Regional Fac - Civil Plans for Box Culvert Relocation Process Concurrent with Army Corp	110	07-Jul-17 A	15-Dec-17 A	
Technical Drainage Study - On & Off Sites					
SDB0-3D10	TDS On & Off Sites - KH Prepares Preliminary Drainage Analysis	20	18-May-17 A	14-Jun-17 A	
SDB1-3D10	TDS On & Off Sites - KH Submits Drainage Study to County for Review	0		29-Jun-17 A	
SDB2-3D10	TDS On & Off Sites - Design Development Plans Completed for TDS	11	15-Jun-17 A	29-Jun-17 A	
SDB3-3D10	TDS On & Off Sites - Clark County Drainage Study Review	9	30-Jun-17 A	13-Jul-17 A	
SDB4-3D10	TDS On & Off Sites - KH Receives Drainage Study Review Comments	0		13-Jul-17 A	
SDB5-3D10	TDS On & Off Sites - KH Prepares Addendum #1 to the Drainage Study	10	14-Jul-17 A	27-Jul-17 A	
SDB6-3D40	TDS On & Off Sites - KH Receives Addendum #1 Comments	1	28-Jul-17 A	28-Jul-17 A	
SDB6-3D50	TDS On & Off Sites - KH Prepares Addendum #2 to the Drainage Study	5	28-Jul-17 A	03-Aug-17 A	
SDB6-3D60	TDS On & Off Sites - KH Submits Addendum #2 to CC	1	04-Aug-17 A	04-Aug-17 A	
SDB6-3D70	TDS On & Off Sites - Verbal Comments / KH Submits Addendum #3 to CC	1	07-Aug-17 A	23-Aug-17 A	
SDB6-3D120	TDS On & Off Sites - VE Site Plan Notice to Proceed	6	24-Aug-17 A	24-Aug-17 A	
SDB6-3D80	TDS On & Off Sites - CC Review of Addendum #3	5	23-Aug-17 A	30-Aug-17 A	
SDB6-3D90	TDS On & Off Sites - KH Receives Drainage Study Review Comments	1	30-Aug-17 A	30-Aug-17 A	
SDB6-3D100	TDS On & Off Sites - KH Prepares Addendum #4 to the Drainage Study	4	30-Aug-17 A	05-Sep-17 A	
SDB6-3D110	TDS On & Off Sites - CC Review of Addendum #4	6	06-Sep-17 A	13-Sep-17 A	
SDB7-3D10	TDS On & Off Sites - Drainage Study Approval	0		14-Sep-17 A	
SDB6-3D130	TDS On & Off Sites - Pending Revised Grading Concept to Start TDS Update	1	14-Sep-17 A	14-Sep-17 A	
SDB6-3D140	TDS On & Off Sites - Prepare Techincal Drainage Study Update	15	14-Sep-17 A	04-Oct-17 A	
SDB6-3D150	TDS On & Off Sites - KH Submits TDS Update to CC for Review	1	05-Oct-17 A	05-Oct-17 A	
SDB6-3D160	TDS On & Off Sites - CC Review of TDS Update #1 (Epedited)	5	06-Oct-17 A	12-Oct-17 A	
SDB6-3D170	TDS On & Off Sites - KH Receives Comments on TDS Update #1	1	13-Oct-17 A	13-Oct-17 A	
SDB6-3D180	TDS On & Off Sites - KH Prepares Addendum #1 to TDS Update #1	4	06-Nov-17 A	09-Nov-17 A	
SDB6-3D190	TDS On & Off Sites - KH Submits TDS Addendum #1 to TDS Update #1	1	09-Nov-17 A	09-Nov-17 A	
SDB6-3D200	TDS On & Off Sites - CC Review of Add #1 to TDS Update #1 (Epedited)	5	10-Nov-17 A	16-Nov-17 A	
SDB7-3D20	TDS On & Off Sites - TDS Update #1 to TDS Approved by CC	0		08-Dec-17 A	
SDB6-3D30	TDS On & Off Sites - NDOT Concurrence	38	11-Dec-17 A	02-Feb-18 A	
Civil Improvement Plans (On-Site Rough & Finish Grade / Utilities)					
SDC0-3D10	CIP (OSEG) - Schematic Design - Coordinated Design Team Integrated Design	14	17-May-17 A	27-Jun-17 A	
SDC1-3D10	CIP (OSEG) - Schematic Design - Schematic Design Workshop	5	28-Jun-17 A	05-Jul-17 A	
SDC2-3D10	CIP (OSEG) - Schematic Design - Finalize Schematic Design	14	05-Jul-17 A	25-Jul-17 A	
SDC3-3D10	CIP (OSEG) - Design Development - Civil On-Site Plans	20	26-Jul-17 A	22-Aug-17 A	
SDC4-3D10	CIP (OSEG) - Design Development - Design Development Workshop	5	23-Aug-17 A	29-Aug-17 A	
SDC4-3D20	CIP (OSEG) - Design Development - Revise Base Plan, Grading Plan & Utility Plan	20	24-Aug-17 A	20-Sep-17 A	
SDC5-3D20	CIP (OSEG) - Design Development - Finalize Procurement Package	25	21-Sep-17 A	09-Oct-17 A	
SDC5-3D10	CIP (OSEG) - Design Development - Finalize Design Development Plans (Design Package 1a)	25	21-Sep-17 A	25-Oct-17 A	
SDC6-3D10	CIP (OSEG) - Construction Documents - Finalize On-Site Plans for Submittal to Clark County	5	26-Oct-17 A	01-Nov-17 A	
SDC6-3D20	CIP (OSEG) - Construction Documents - Final Preparation for Grading Bid Package	5	02-Nov-17 A	08-Nov-17 A	
SDC7-3D10	CIP (OSEG) - Construction Documents - KH Submits Early Grading Permit to CCBD	0		09-Nov-17 A	
SDC8-3D10	CIP (OSEG) - Construction Documents - CCBD Review (Permit #1) (Expedited)	13	10-Nov-17 A	30-Nov-17 A	
SDC9-3D10	CIP (OSEG) - Construction Documents - Early Grading & Foundation Permit Approved (Permit #1)	2	06-Dec-17 A	18-Dec-17 A	
SDC9-3D11	Stop Work Order Issued Pending Early Grading & Foundation Permit Approved (Permit #1)	5	12-Dec-17 A	18-Dec-17 A	
Utility Agency Approvals - Las Vegas Water District (On-Site Only)					

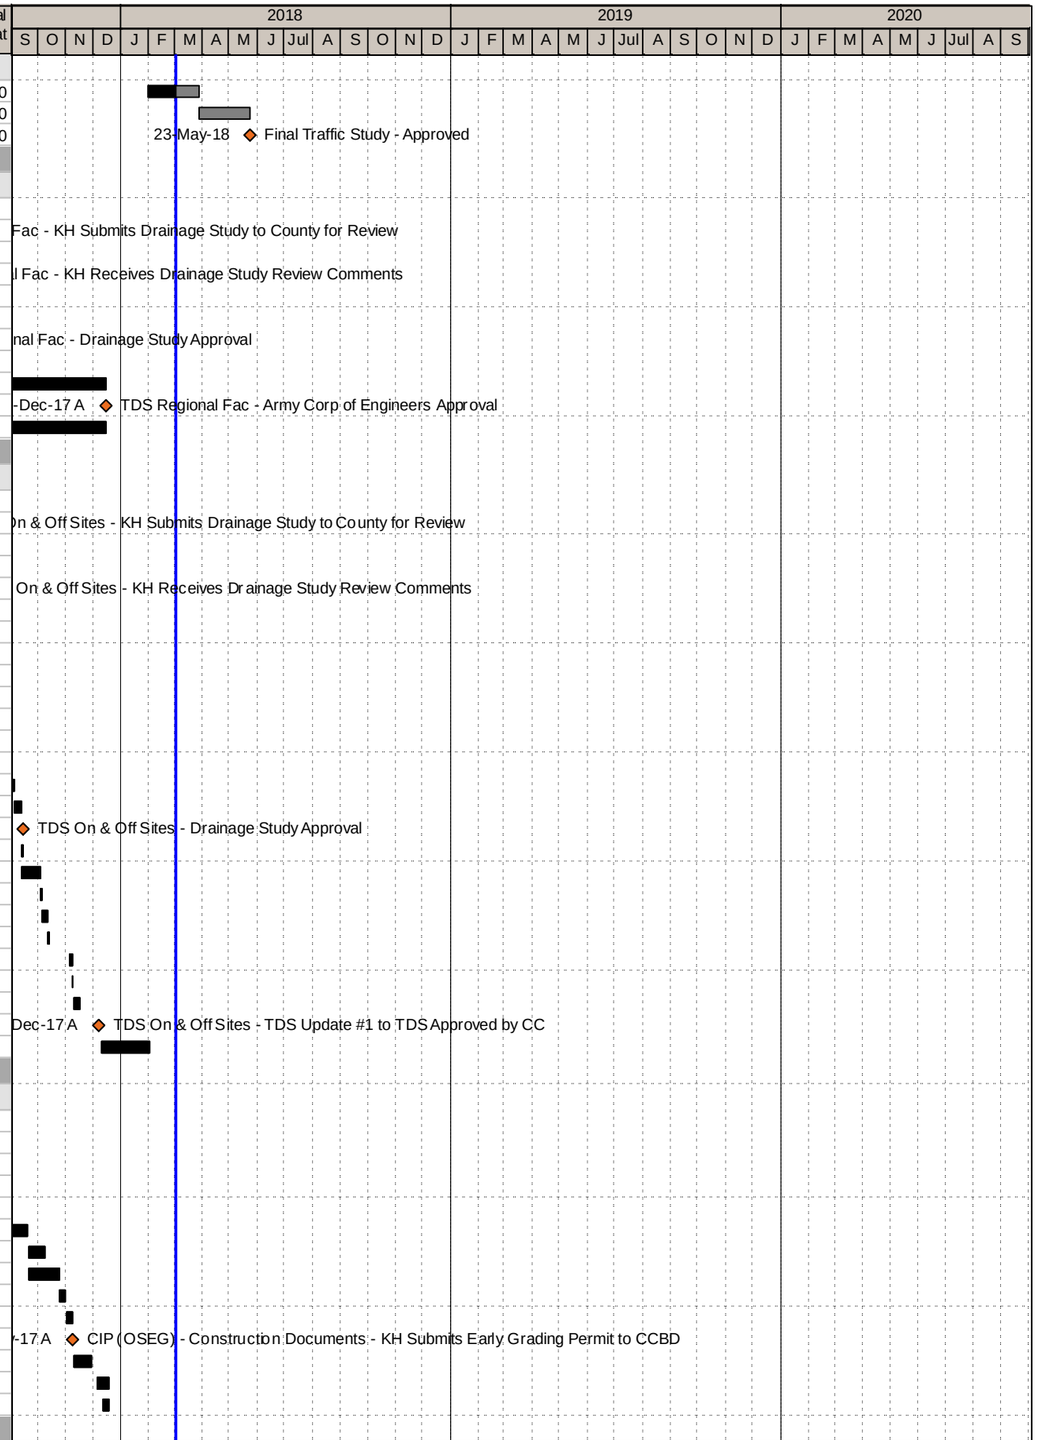

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
SDD0-3D10	Request Plan Check Fees from Client	1	03-Nov-17 A	03-Nov-17 A	
SDD1-3D10	Fees/Application Received from Owner	0		06-Nov-17 A	
SDD2-3D10	KH Receives Plumbing Plan for Submittal	0		06-Nov-17 A	
SDD3-3D10	Submit Plans & Network Analysis to LVVWD	0		06-Nov-17 A	
SDD5-3D10	Need Plumbing Plan for Purposes of LVVWD Review	0		06-Dec-17 A	
SDD4-3D10	LVVWD Review of Plans (Expedited)	13	07-Nov-17 A	19-Dec-17 A	
SDD6-3D10	Redlines Received from LVVWD	1	21-Dec-17 A	21-Dec-17 A	
SDD6-3D11	KH Addresses LVVWD Redlines	10	22-Dec-17 A	16-Jan-18 A	
SDD7-3D10	LVVWD Back Check and Easement Review	10	17-Jan-18 A	30-Jan-18 A	
SDD8-3D10	KH Address Comments	5	31-Jan-18 A	06-Feb-18 A	
SDD9-3D10	Pay Fees/Obtain Final Signature	5	07-Mar-18	13-Mar-18	5
SDDA-3D10	Water Plans Approved	0		16-Mar-18	5
Utility Agency Approvals - Clark County Water Reclamation District (On-Site Only)					
SDE0-3D10	Submit Plans to CCWRD	0		07-Nov-17 A	
SDE1-3D10	CCWRD Review	28	08-Nov-17 A	05-Dec-17 A	
SDE2-3D10	KH Receives Comments from CCWRD	2	05-Dec-17 A	05-Dec-17 A	
SDE5-3D10	KH Address Redlines	22	06-Dec-17 A	16-Jan-18 A	
SDE6-3D10	CCWRD Review #2	10	17-Jan-18 A	30-Jan-18 A	
SDE7-3D10	KH Receives Final Comments from CCWRD	1	31-Jan-18 A	31-Jan-18 A	
SDE8-3D10	KH Addresses Final CCWRD Comments	5	01-Feb-18 A	07-Feb-18 A	
SDE3-3D10	CCWRD Approves Mylars	5	12-Mar-18	16-Mar-18	5
SDE4-3D10	Early Utilities Permitted (On-Site Only)	0		16-Mar-18	5
Civil Improvement Plans (Off-Site - Adjacent to Project)					
SDF0-3D10	CIP (Off-Site) - Schematic Design - Coordinated Design Team Integrated Design	39	31-May-17 A	25-Jul-17 A	
SDF1-3D10	CIP (Off-Site) - Schematic Design - Schematic Design Workshop	5	26-Jul-17 A	01-Aug-17 A	
SDF2-3D10	CIP (Off-Site) - Schematic Design - Finalize Schematic Design	20	02-Aug-17 A	29-Aug-17 A	
SDF3-3D10	CIP (Off-Site) - Design Development - Civil On & Off-Site Design	19	30-Aug-17 A	26-Sep-17 A	
SDF4-3D10	CIP (Off-Site) - Design Development - Design Development Workshop	5	27-Sep-17 A	03-Oct-17 A	
SDF5-3D10	CIP (Off-Site) - Design Development - Finalize Design Development Plans	10	04-Oct-17 A	17-Oct-17 A	
SDF6-3D10	CIP (Off-Site) - Construction Documents - Finalize On & Off-Site Plans for Submittal to Clark County Public Works	1	18-Oct-17 A	18-Oct-17 A	
SDF7-3D10	CIP (Off-Site) - Construction Documents - Submit On & Off-Site Plans to CCPW for Review	1	19-Oct-17 A	19-Oct-17 A	
SDF8-3D10	CIP (Off-Site) - Construction Documents - CCPW Review	10	20-Oct-17 A	28-Nov-17 A	
SDF9-3D10	CIP (Off-Site) - Construction Documents - KH Receives 1st Review	1	29-Nov-17 A	29-Nov-17 A	
SDFA-3D10	CIP (Off-Site) - Construction Documents - KH Addresses Comments	13	30-Nov-17 A	18-Dec-17 A	
SDFB-3D10	CIP (Off-Site) - Construction Documents - KH Submits for 2nd Review	5	18-Dec-17 A	18-Dec-17 A	
SDFC-3D10	CIP (Off-Site) - Construction Documents - CCPW 2nd Review	5	19-Dec-17 A	05-Jan-18 A	
SDFD-3D10	CIP (Off-Site) - Construction Documents - Bond Approved	0		05-Jan-18 A	
SDFG-3D10	CIP (Off-Site) - Construction Documents - Bond Posted By Owner	0		26-Feb-18 A	
SDFE-3D10	CIP (Off-Site) - Construction Documents - KH Addresses Comments & Plots Mylars	2	12-Mar-18	13-Mar-18	49
SDFF-3D10	CIP (Off-Site) - Construction Documents - Mylars Routed for Final Signature	5	14-Mar-18	20-Mar-18	49
SDFH-3D10	CIP (Off-Site) - Construction Documents - Final Mylars Signed by Clark County Public Works	5	21-Mar-18	27-Mar-18	49
Utility Agency Approvals - Las Vegas Water District (Off-Site)					
SDG0-3D10	Request Plan Check Fees from Client	1	20-Sep-17 A	20-Sep-17 A	
SDG1-3D10	Fees/Application Received from Owner	0		06-Nov-17 A	
SDG2-3D10	KH Receives Plumbing Plan for Submittal	0		06-Nov-17 A	
SDG3-3D10	Submit Plans & Network Analysis to LVVWD	0		06-Nov-17 A	
SDG5-3D10	Building Permit Submitted by Arch to CCBD	0		20-Dec-17 A	
SDG4-3D10	LVVWD Review of Plans	13	07-Nov-17 A	21-Dec-17 A	
SDG6-3D10	Redlines Received from LVVWD & KH Addresses Comments	10	22-Dec-17 A	15-Jan-18 A	
SDG7-3D10	LVVWD Back Check and Easement Review	10	16-Jan-18 A	29-Jan-18 A	
SDG8-3D10	KH Address Comments	5	30-Jan-18 A	05-Feb-18 A	
SDG9-3D10	Pay Fees/Obtain Final Signature	5	12-Mar-18	16-Mar-18	54
SDGA-3D10	Water Plans Approved	0		16-Mar-18	54
Utility Agency Approvals - Clark County Water Reclamation District (Off-Site)					
SDH0-3D10	Submit Plans to CCWRD	0		06-Nov-17 A	
SDH2-3D10	KH Receives Comments from CCWRD	2	05-Dec-17 A	06-Dec-17 A	
SDH1-3D10	CCWRD Review	26	06-Nov-17 A	15-Dec-17 A	

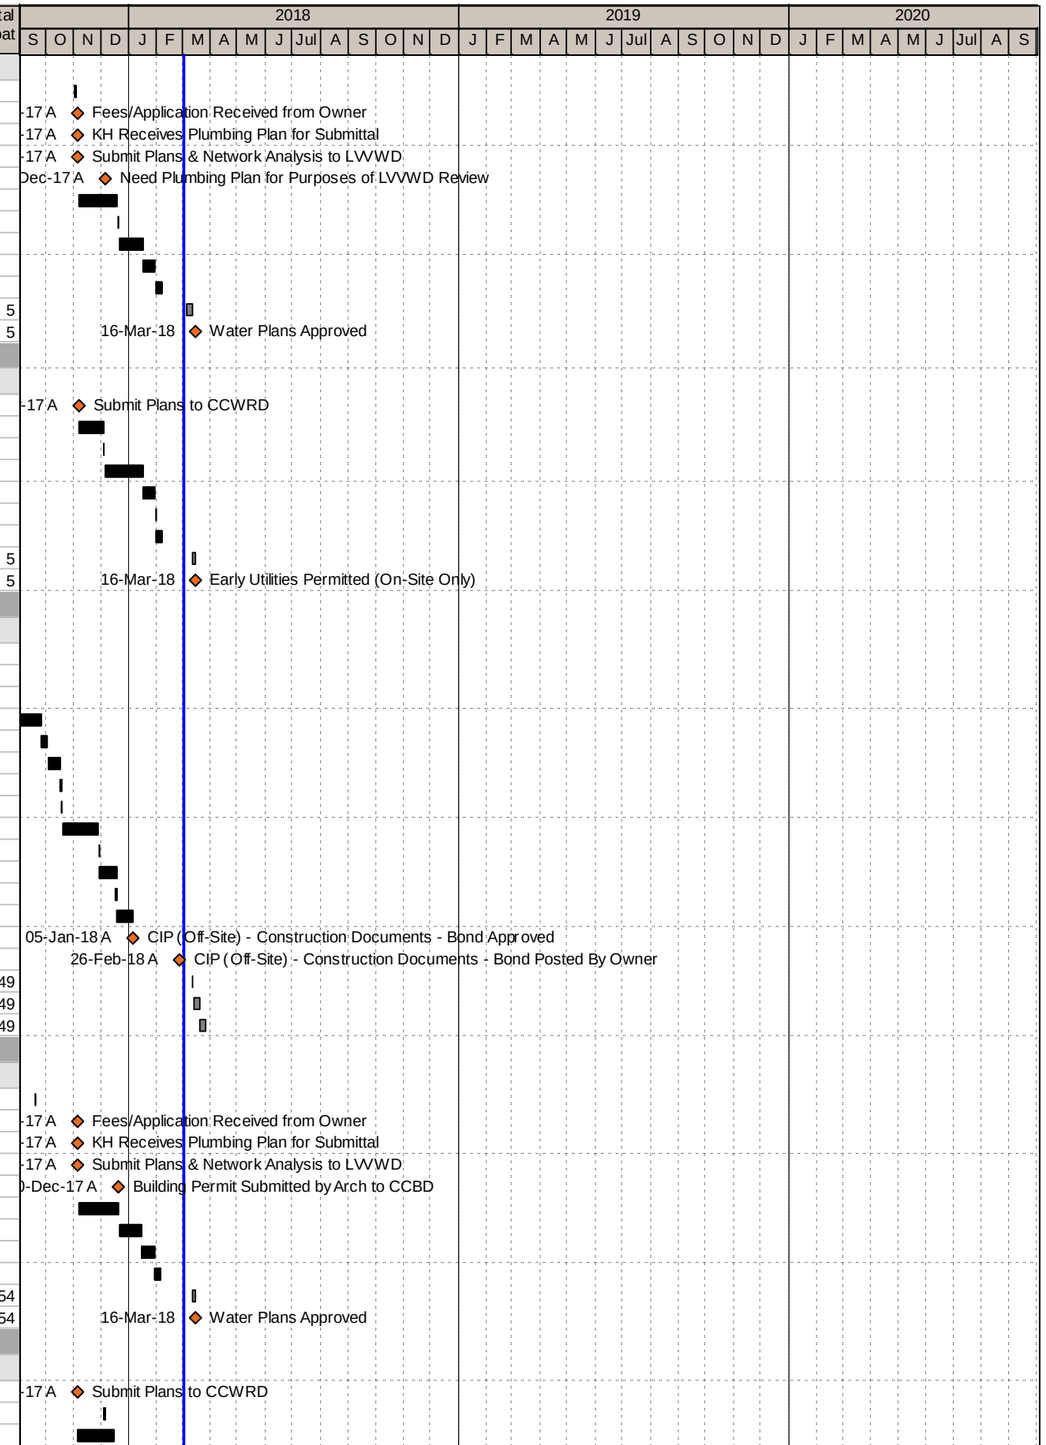

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
SDH4-3D10	KH Addresses Comments from CCWRD	20	07-Dec-17 A	22-Jan-18 A	
SDH5-3D10	CCWRD Review #2	15	16-Jan-18 A	05-Feb-18 A	
SDH3-3D10	CCWRD Approves Mylars	5	14-Mar-18	20-Mar-18	54
Civil Improvement Plans (Non-Adjacent Site Improvements)					
SDJ0-3D10	CIP (MI&SD) - Schematic Design - Coordinated Design Team Integrated Design	57	28-Jun-17 A	01-Feb-18 A	
SDJ1-3D10	CIP (MI&SD) - Schematic Design - Schematic Design Workshop	5	02-Feb-18 A	08-Feb-18 A	
SDJ2-3D10	CIP (MI&SD) - Schematic Design - Finalize Schematic Design	20	09-Feb-18 A	08-Mar-18	11
SDJ3-3D10	CIP (MI&SD) - Design Development - Civil Major Infrastructure Design	40	09-Mar-18	03-May-18	11
SDJ4-3D10	CIP (MI&SD) - Design Development - Design Development Workshop	5	04-May-18	10-May-18	11
SDJ5-3D10	CIP (MI&SD) - Design Development - Finalize Design Development Plans	38	11-May-18	05-Jul-18	11
SDJ6-3D10	CIP (MI&SD) - Construction Documents - Finalize Major Infrastructure Plans for Submittal to Clark County	20	06-Jul-18	02-Aug-18	11
SDJ7-3D10	CIP (MI&SD) - Construction Documents - Submit Major Infrastructure Plans to Clark County for Review	2	03-Aug-18	06-Aug-18	11
SDJ8-3D10	CIP (MI&SD) - Construction Documents - CCBD Review of Major Infrastructure Plans	24	07-Aug-18	10-Sep-18	406
SDJ9-3D10	CIP (MI&SD) - Construction Documents - KH Receives 1st Review	1	11-Sep-18	11-Sep-18	406
SDJA-3D10	CIP (MI&SD) - Construction Documents - KH Addresses Comments	15	12-Sep-18	02-Oct-18	406
SDJB-3D10	CIP (MI&SD) - Construction Documents - KH Submits for 2nd Review	5	03-Oct-18	09-Oct-18	406
SDJC-3D10	CIP (MI&SD) - Construction Documents - CCBD 2nd Review	10	10-Oct-18	23-Oct-18	406
SDJD-3D10	CIP (MI&SD) - Construction Documents - Bond Approved	0		23-Oct-18	406
SDJE-3D10	CIP (MI&SD) - Construction Documents - KH Addresses Comments & Plots Mylars	10	24-Oct-18	06-Nov-18	406
SDJF-3D10	CIP (MI&SD) - Construction Documents - Bond Posted by Owner	10	07-Nov-18	20-Nov-18	406
SDJG-3D10	CIP (MI&SD) - Construction Documents - Bond Approved	0		20-Nov-18	406
SDJH-3D10	CIP (MI&SD) - Construction Documents - Final Mylars Signed by Clark County	3	21-Nov-18	27-Nov-18	406
NDOT Permit for Major Infrastructure					
SDK0-3D10	Submit NDOT Encroachment Permit	2	07-Aug-18	08-Aug-18	11
SDK1-3D10	NDOT Encroachment Permit Review	77	09-Aug-18	28-Nov-18	11
SDK2-3D10	NDOT Permit Obtained	5	29-Nov-18	05-Dec-18	11
Final Subdivision Map					
SDL0-3D10	Prepare Final Map	14	23-Aug-17 A	12-Sep-17 A	
SDL1-3D20	Revise Final Map for VE Changes	2	13-Sep-17 A	14-Sep-17 A	
SDL1-3D10	Submit Final Map for Review	2	15-Sep-17 A	18-Sep-17 A	
SDL2-3D10	Final Map Processing	40	19-Sep-17 A	13-Nov-17 A	
SDL3-3D10	Decomissioning Agreement Done/Bond Posted	1	26-Feb-18 A	26-Feb-18 A	
SDL4-3D10	Record Final Map	14	26-Jan-18 A	29-Mar-18	47
SDL5-3D10	Final Map Recorded	0		29-Mar-18	47
25% GMP Design					
SDM0-3D10	Design - 25% GMP Design Documents	44	01-May-17 A	30-Jun-17 A	
SDM0-3D20	Issue Design - 25% GMP Design Documents	0		30-Jun-17 A	
60% GMP Design					
SDN0-3D30	Design - 60% GMP Design Documents	44	03-Jul-17 A	02-Oct-17 A	
SDN0-3D40	Issue Design - 60% GMP Design Documents	0		02-Oct-17 A	
SDN0-3D50	Issue Design - 60% GMP Design Documents (ARUP Part A)	0		06-Oct-17 A	
SDN0-3D60	Issue Design - 60% GMP Design Documents (ARUP Part B)	0		20-Oct-17 A	
100% GMP Design					
SDQ0-3D10	Design - 100% GMP Design Documents	61	03-Oct-17 A	29-Dec-17 A	
SDQ0-3D20	Issue Design - 100% GMP Design Documents	0		29-Dec-17 A	
Design Package 1 - Demo / Grading / Excavation					
SDR0-3D10	Design - Prepare Design Package 1a (Demo / Grading / Excavation)	109	05-May-17 A	09-Nov-17 A	
SDR1-3D10	Issue Design - Prepare Design Package 1a (Demo / Grading / Excavation)	0		09-Nov-17 A	
Design Package 1b - Site Finish Grading Construction Documents					
SDS0-3D10	Design - Prepare Design Package 1b (Site Finish Grading Construction Documents)	42	10-Oct-17 A	11-Dec-17 A	
SDS1-3D10	Issue Design - Prepare Design Package 1b (Site Finish Grading Construction Documents)	0		11-Dec-17 A	
Design Package 2 - Foundations / Deep Utilities / Hydrotherapy					

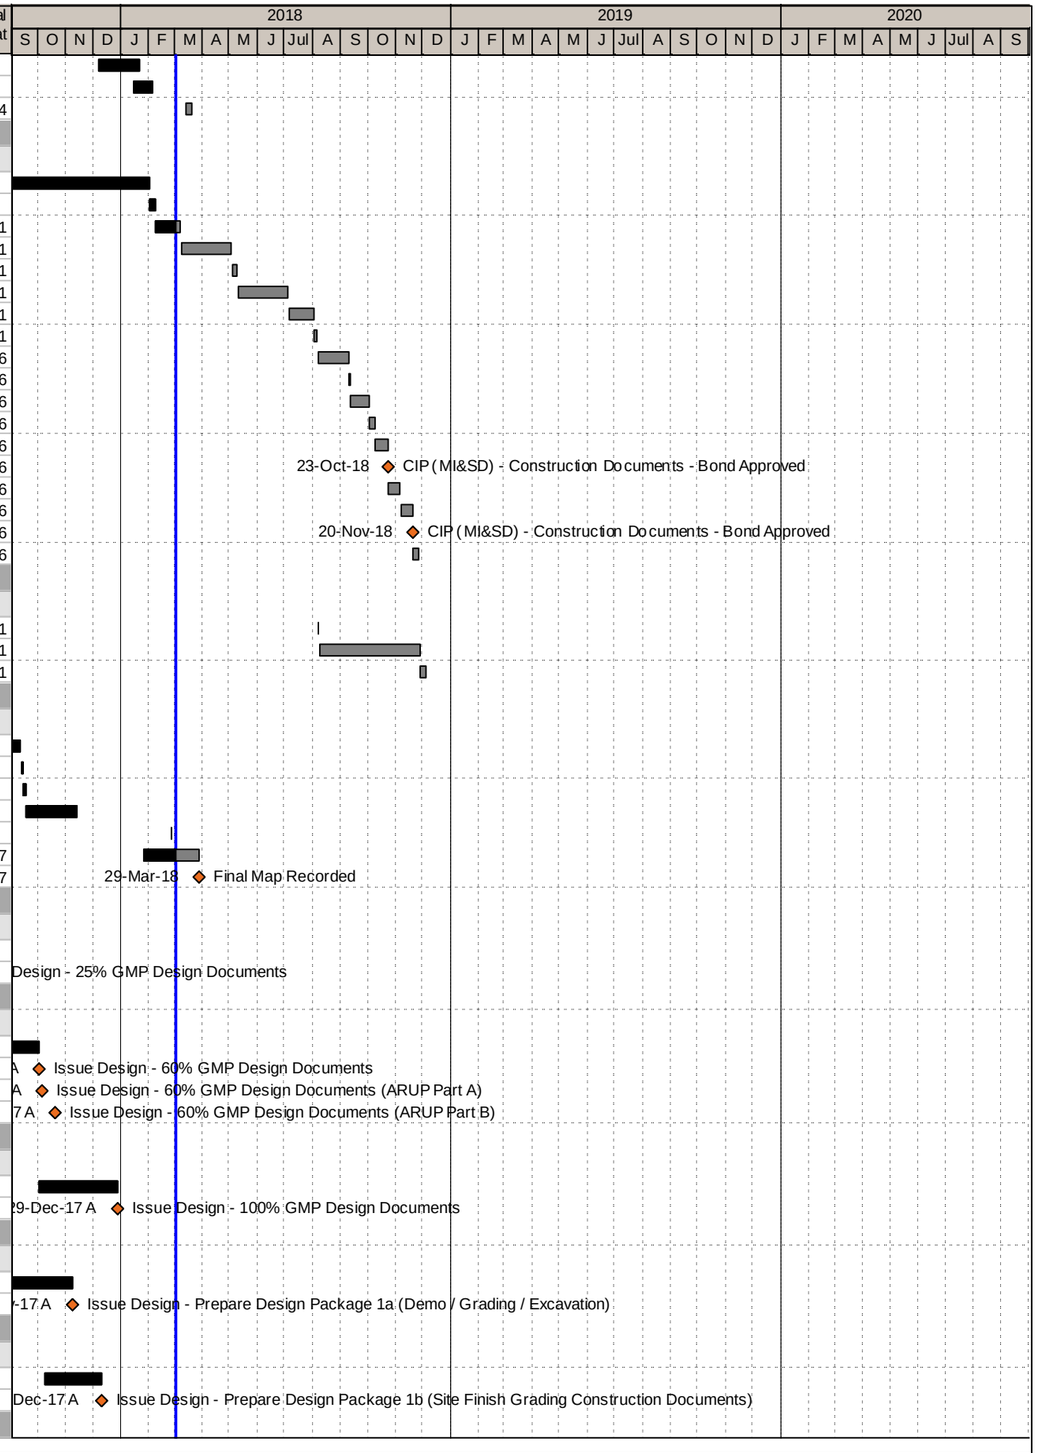

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
SDT0-3D10	Issue Design - Prepare Design Package 2 (Foundations / Deep Utilities / Hydotherapy) - Procurement Package	0		09-Oct-17 A	
SDT2-3D10	Begin Shop Drawings & Coordination - Design Package 2 (Foundations / Deep Utilities / Hydotherapy)	0		18-Dec-17 A	
SDT1-3D10	Design - Prepare Design Package 2 (Foundations / Deep Utilities / Hydrotherapy)	111	03-Jul-17 A	05-Jan-18 A	
SDT3-3D10	Issue Design for Permit - Design Package 2 (Foundations / Deep Utilities / Hydotherapy)	0	08-Jan-18 A		
Design Package 3a - Concrete / Precast Construction Documents					
SDU1-3D10	Begin Shop Drawings & Coordination - Design Package 3a (Concrete / Precast Construction Documents)	0	05-Feb-18 A		
SDU0-3D10	Design - Prepare Design Package 3a (Concrete / Precast Construction Documents)	149	03-Jul-17 A	05-Mar-18	3
SDU2-3D10	Issue Design for Permit - Design Package 3a (Concrete / Precast Construction Documents)	0		05-Mar-18	3
Design Package 3b - Steel Mill Order / Construction Documents					
SDV0-3D10	Issue Design - Mill Order Design Package/Connections (Truss Columns)	0		07-Feb-18 A	
SDV1-3D10	Design - Prepare Design Package 3b (Steel Mill Order / Construction Documents)	190	03-Jul-17 A	02-Apr-18	9
SDV2-3D10	Issue Design - Prepare Design Package 3b (Structural Construction Documents)	0		02-Apr-18	12
SDV3-3D10	Issue Design - Mill Order Design Package (Roof Structure)	0		02-Apr-18	15
Design Package 4a/b/c/5a/bc - Final Architectural Construction Documents					
SDW0-3D10	Design - Prepare Design Package 4a/4b/4c/5a/5c (Final Architectural Construction Documents)	213	05-Sep-17 A	06-Jul-18	1
SDW1-3D10	Issue Design - Prepare Design Package 4a/4b/4c/5a/5c (Final Architectural Construction Documents)	0		06-Jul-18	1
Design Package 5b - Long Lead Items					
SDX0-3D10	Design - Prepare Design Package 5b (Long Lead Items)	81	05-Sep-17 A	29-Dec-17 A	
SDX1-3D10	Issue Design - Prepare Design Package 5b (Long Lead Items)	0		29-Dec-17 A	
Design Package 6 - Interior Finishes Construction Documents					
SDZ0-3D10	Design - Prepare Design Package 6 (Interior Finishes Construction Documents)	203	05-Jan-18 A	19-Oct-18	10
SDZ1-3D10	Issue Design - Prepare Design Package 6 (Interior Finishes Construction Documents)	0		19-Oct-18	10
Design Package 7a - Field Tray and Mechanism Construction Documents					
SDAA0-3D10	Design - Prepare Design Package 7a (Field Tray and Mechanism Construction Documents)	149	03-Jul-17 A	05-Mar-18	66
SDAA1-3D10	Issue Design - Prepare Design Package 7a (Field Tray and Mechanism Construction Documents)	0		05-Mar-18	66
Design Package 7b - Operable Doors and Mechanism Construction Documents					
SDBB0-3D10	Design - Prepare Design Package 7b (Operable Door and Mechanism Construction Documents)	190	03-Jul-17 A	02-Apr-18	96
SDBB1-3D10	Issue Design - Prepare Design Package 7b (Operable Door and Mechanism Construction Documents)	0		02-Apr-18	96
Design Package 8 - Hardscape and Landscape					
SDCC0-3D10	Design - Prepare Design Package 8 (Hardscape and Landscape Construction Documents)	129	05-Jan-18 A	06-Jul-18	1
SDCC1-3D10	Issue Design - Prepare Design Package 8 (Hardscape and Landscape Construction Documents)	0		06-Jul-18	1
Design Package 9 - FF&E					
SDDD0-3D10	Design - Prepare Design Package 9 (FF&E)	254	05-Jan-18 A	04-Jan-19	83
SDDD1-3D10	Issue Design - Prepare Design Package 9 (FF&E)	0		04-Jan-19	83
Budgeting and Estimating					
Preconstruction					
SE00-3E10	Prepare Raiders Winter Meeting Presentation Materials	67	24-Dec-16 A	28-Feb-17 A	
Concept Cost Estimate					
SE10-3E10	Concept Cost Estimate	30	27-Mar-17 A	04-May-17 A	
Project Budget Validation - 25% GMP					
SE20-3E10	Budget Validation (25% GMP Documents)	20	03-Jul-17 A	09-Aug-17 A	
Project Budget Validation - 60% GMP					
SE30-3E10	Budget Validation (60% GMP Documents)	33	03-Oct-17 A	15-Nov-17 A	
Final GMP Estimate					

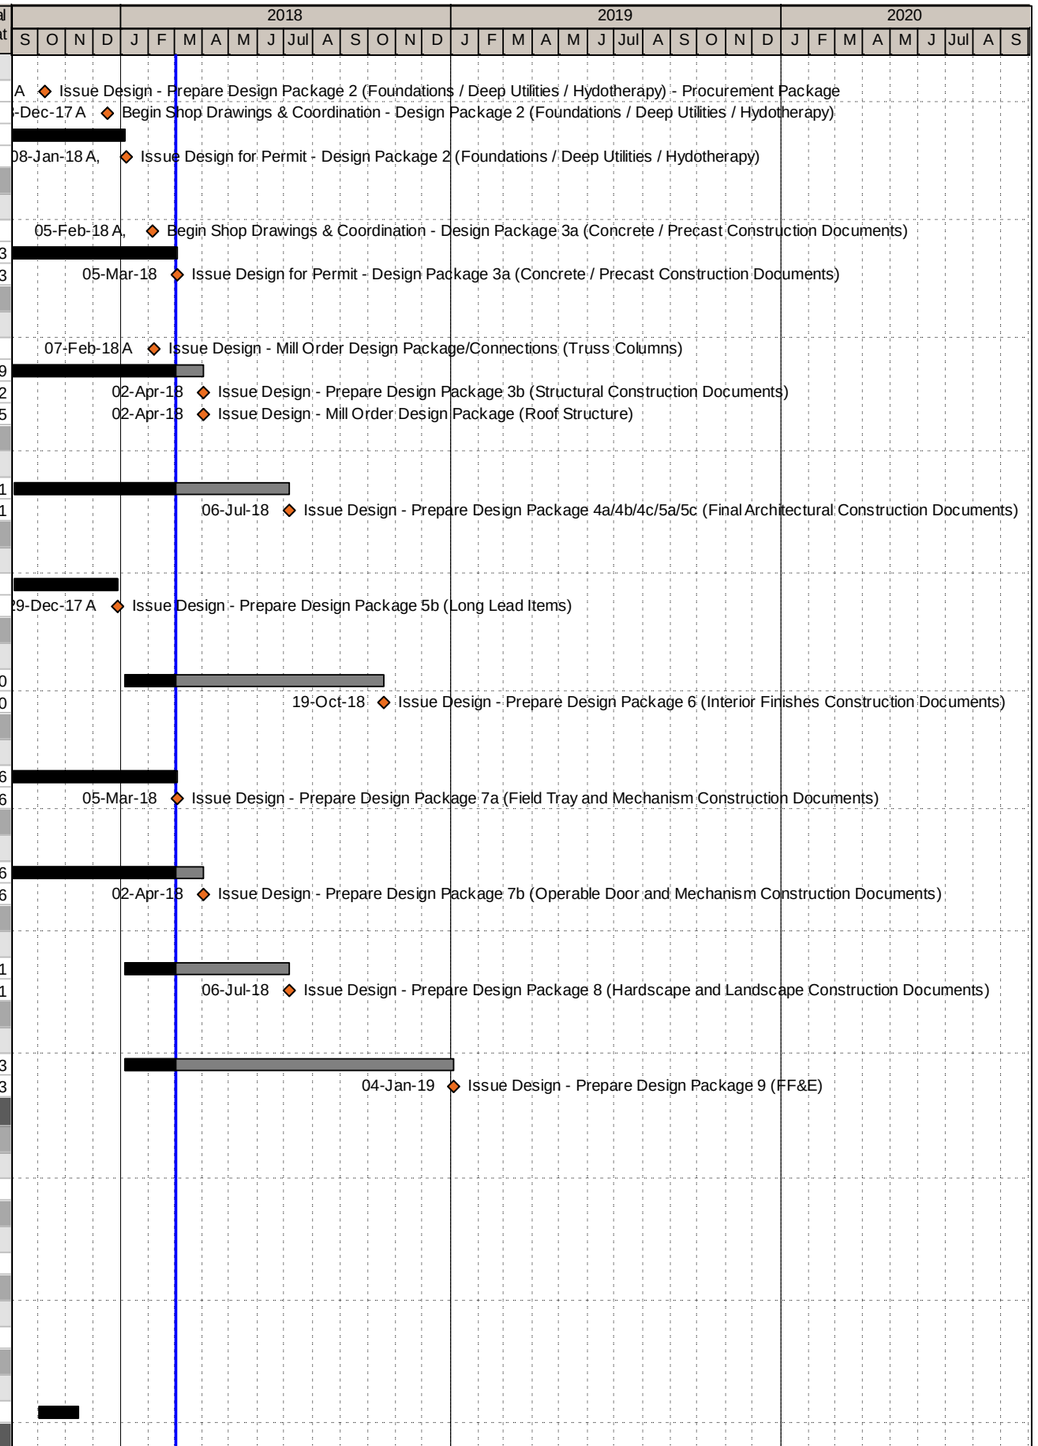

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S000-SE10	Prepare GMP Estimate	34	02-Jan-18 A	16-Feb-18 A	
S001-SE10	Reconcile GMP	11	20-Feb-18 A	05-Mar-18	3
MEP Coordination					
Design Assist Coordination					
S100-3E21	VDC - Design Assist Coordination - Event Lvl	65	06-Nov-17 A	19-Feb-18 A	
S200-3E21	VDC - Design Assist Coordination - Lower Mezz Lvl	75	06-Nov-17 A	27-Feb-18 A	
S300-3E21	VDC - Design Assist Coordination - Main Conc	105	06-Nov-17 A	02-Apr-18	32
S400-3E21	VDC - Design Assist Coordination - Lower Suite Lvl	140	06-Nov-17 A	22-May-18	32
S500-3E21	VDC - Design Assist Coordination - Upper Suite Lvl	140	06-Nov-17 A	22-May-18	32
S600-3E21	VDC - Design Assist Coordination - Mid Bowl Mezz Lvl	140	06-Nov-17 A	22-May-18	32
S700-3E21	VDC - Design Assist Coordination - Upper Conc	140	06-Nov-17 A	22-May-18	32
S900-3E21	VDC - Design Assist Coordination - Press Lvl	140	06-Nov-17 A	22-May-18	32
Riser & Mech/Elec Spaces Coord (Tied to Deck Rebar & Steel)					
SEA1-3E10	VDC - Shaft Coordination (Coordinate) - Area A	20	26-Jan-18 A	16-Feb-18 A	
SEF1-3E10	VDC - Shaft Coordination (Coordinate) - Area F	20	26-Jan-18 A	16-Feb-18 A	
SEB1-3E10	VDC - Shaft Coordination (Coordinate) - Area B	15	19-Feb-18 A	09-Mar-18	16
SEE1-3E10	VDC - Shaft Coordination (Coordinate) - Area E	15	19-Feb-18 A	09-Mar-18	22
SEC1-3E10	VDC - Shaft & Mech/Elec Spaces Coordination (Coordinate) - Area C	20	12-Mar-18	06-Apr-18	36
SED1-3E10	VDC - Shaft & Mech/Elec Spaces Coordination (Coordinate) - Area D	20	12-Mar-18	06-Apr-18	44
Precast Stadia Penetrations / Inserts (Tied to Precast)					
SEV40-3E10	VDC - Precast Stadia Penetrations / Inserts (Coordinate) - Area A	15	03-Apr-18	23-Apr-18	35
SEV40-3E20	VDC - Precast Stadia Penetrations / Inserts (Review and Finalize) - Area A	10	24-Apr-18	07-May-18	35
VDC - 000 Event Level - General Coordination					
S1A60-3E10	VDC - General Coordination (Coordinate) - Quad A Event Lvl	15	20-Feb-18 A	12-Mar-18	19
S1B60-3E10	VDC - General Coordination (Coordinate) - Quad B Event Lvl	15	13-Mar-18	02-Apr-18	19
S1C60-3E10	VDC - General Coordination (Coordinate) - Quad C Event Lvl	15	03-Apr-18	23-Apr-18	31
S1D60-3E10	VDC - General Coordination (Coordinate) - Quad D Event Lvl	15	24-Apr-18	14-May-18	31
VDC - 000 Event Level - Underground / Foundation Coordination					
SEA2-3E10	VDC - Deep Underground Coordination (Coordinate) - Quad A	30	12-Jan-18 A	23-Jan-18 A	
SEB2-3E10	VDC - Deep Underground Coordination (Coordinate) - Quad B	30	12-Jan-18 A	23-Jan-18 A	
SEC2-3E10	VDC - Deep Underground Coordination (Coordinate) - Quad C	27	29-Jan-18 A	06-Mar-18	20
SED2-3E10	VDC - Deep Underground Coordination (Coordinate) - Quad D	27	29-Jan-18 A	06-Mar-18	31
SED2-3E11	VDC - Deep Underground Coordination (Coordinate) - Quad E	30	07-Mar-18	17-Apr-18	60
SEA2-3E11	VDC - Shallow Underground Coordination (Coordinate) - Quad A	30	10-Apr-18	21-May-18	52
SEB2-3E11	VDC - Shallow Underground Coordination (Coordinate) - Quad B	30	10-Apr-18	21-May-18	52
SEC2-3E11	VDC - Shallow Underground Coordination (Coordinate) - Quad C	30	22-May-18	03-Jul-18	57
SED2-3E12	VDC - Shallow Underground Coordination (Coordinate) - Quad D	30	22-May-18	03-Jul-18	88
SED2-3E13	VDC - Shallow Underground Coordination (Coordinate) - Quad E	30	09-Jul-18	17-Aug-18	217
S1A3-3E30	VDC - Lift Drawing (Prepare Draft) - Wall/Mat Foundations - Event A3	10	24-Jan-18 A	05-Feb-18 A	
S1F3-3E30	VDC - Lift Drawing (Prepare Draft) - Wall/Mat Foundations - Event F3	10	24-Jan-18 A	05-Feb-18 A	
S1A1-3E30	VDC - Lift Drawing (Prepare Draft) - Wall/Mat Foundations - Event A1	10	30-Jan-18 A	12-Feb-18 A	
S1F1-3E30	VDC - Lift Drawing (Prepare Draft) - Wall/Mat Foundations - Event F1	10	31-Jan-18 A	13-Feb-18 A	
S1A2-3E30	VDC - Lift Drawing (Prepare Draft) - Wall/Mat Foundations - Event A2	10	05-Feb-18 A	16-Feb-18 A	
S1F2-3E30	VDC - Lift Drawing (Prepare Draft) - Wall/Mat Foundations - Event F2	10	07-Feb-18 A	20-Feb-18 A	
S1A4-3E30	VDC - Lift Drawing (Prepare Draft) - Wall/Mat Foundations - Event A4	10	09-Feb-18 A	22-Feb-18 A	
S1F4-3E30	VDC - Lift Drawing (Prepare Draft) - Wall/Mat Foundations - Event F4	10	14-Feb-18 A	27-Feb-18 A	
S1B2-3E30	VDC - Lift Drawing (Prepare Draft) - Wall/Mat Foundations - Event B2	10	15-Feb-18 A	28-Feb-18 A	
S1B1-3E30	VDC - Lift Drawing (Prepare Draft) - Wall/Mat Foundations - Event B1	10	21-Feb-18 A	06-Mar-18	27
S1E2-3E30	VDC - Lift Drawing (Prepare Draft) - Wall/Mat Foundations - Event E2	10	21-Feb-18 A	06-Mar-18	26
S1B3-3E30	VDC - Lift Drawing (Prepare Draft) - Wall/Mat Foundations - Event B3	10	26-Feb-18 A	09-Mar-18	31

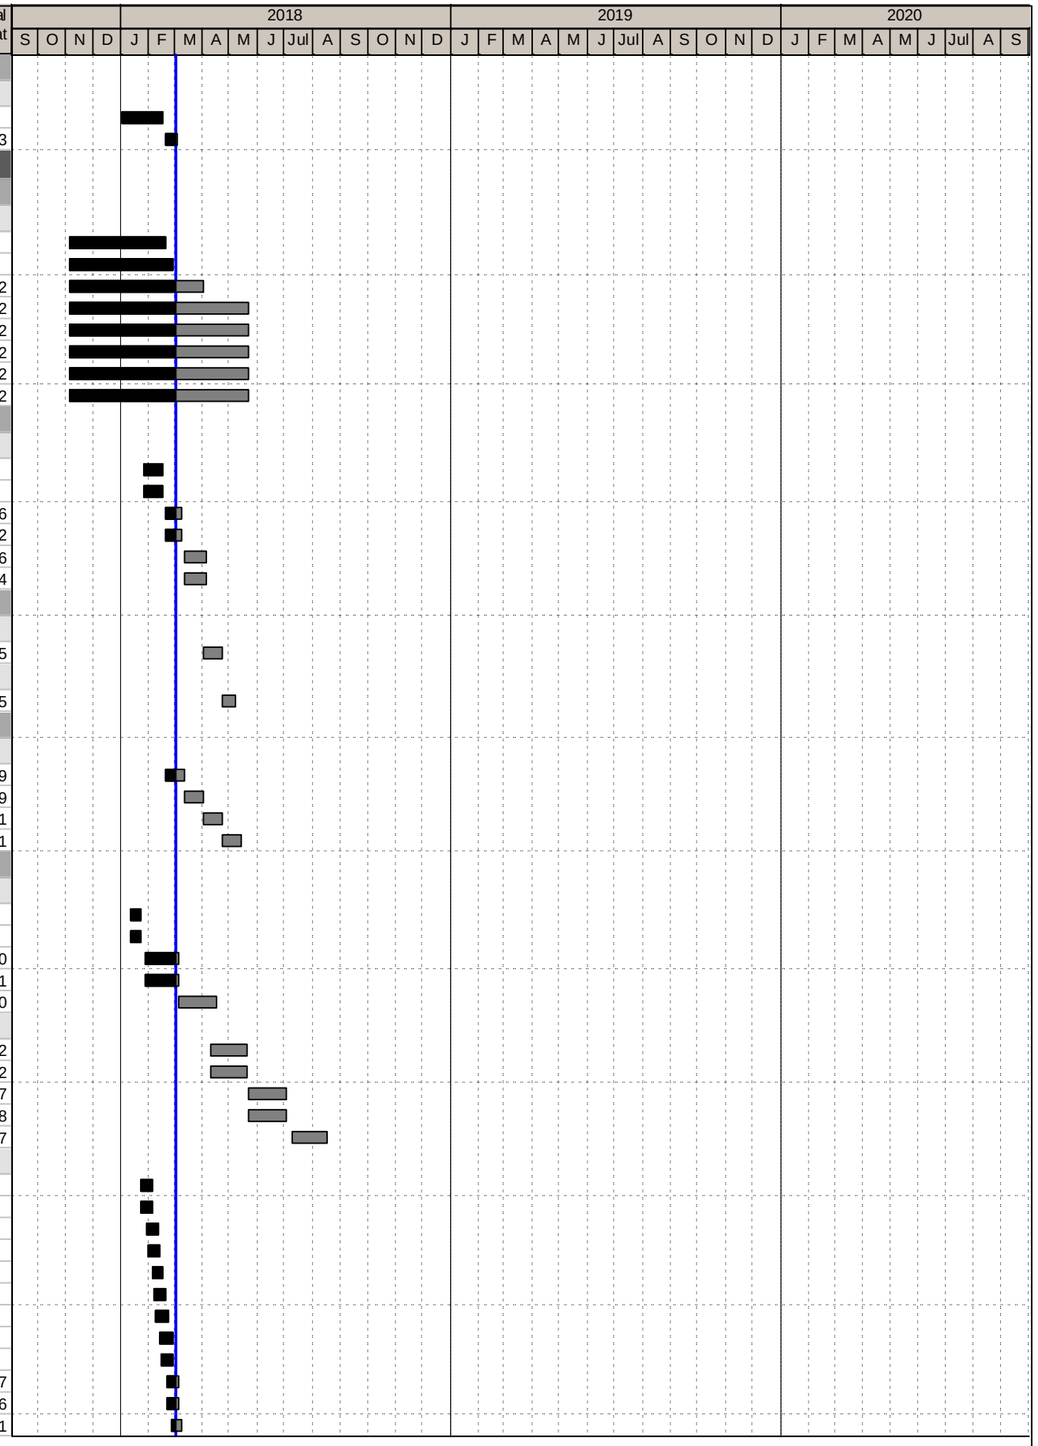

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S1E1-3E30	VDC - Lift Drawing (Prepare Draft) - Wall/Mat Foundations - Event E1	10	28-Feb-18 A	13-Mar-18	26
S1B5-3E30	VDC - Lift Drawing (Prepare Draft) - Wall/Mat Foundations - Event B5	10	07-Mar-18	20-Mar-18	35
S1E3-3E30	VDC - Lift Drawing (Prepare Draft) - Wall/Mat Foundations - Event E3	10	07-Mar-18	20-Mar-18	26
S1B4-3E30	VDC - Lift Drawing (Prepare Draft) - Wall/Mat Foundations - Event B4	10	12-Mar-18	23-Mar-18	35
S1E5-3E30	VDC - Lift Drawing (Prepare Draft) - Wall/Mat Foundations - Event E5	10	14-Mar-18	27-Mar-18	26
S1B6-3E30	VDC - Lift Drawing (Prepare Draft) - Wall/Mat Foundations - Event B6	10	15-Mar-18	28-Mar-18	50
S1C1-3E30	VDC - Lift Drawing (Prepare Draft) - Wall/Mat Foundations - Event C1	10	20-Mar-18	02-Apr-18	51
S1E4-3E30	VDC - Lift Drawing (Prepare Draft) - Wall/Mat Foundations - Event E4	10	21-Mar-18	03-Apr-18	26
S1C2-3E30	VDC - Lift Drawing (Prepare Draft) - Wall/Mat Foundations - Event C2	10	23-Mar-18	05-Apr-18	55
S1C3-3E30	VDC - Lift Drawing (Prepare Draft) - Wall/Mat Foundations - Event C3	10	28-Mar-18	10-Apr-18	55
S1E6-3E30	VDC - Lift Drawing (Prepare Draft) - Wall/Mat Foundations - Event E6	10	28-Mar-18	10-Apr-18	39
S1C4-3E30	VDC - Lift Drawing (Prepare Draft) - Wall/Mat Foundations - Event C4	10	02-Apr-18	13-Apr-18	55
S1D1-3E30	VDC - Lift Drawing (Prepare Draft) - Wall/Mat Foundations - Event D1	10	04-Apr-18	17-Apr-18	43
S1D2-3E30	VDC - Lift Drawing (Prepare Draft) - Wall/Mat Foundations - Event D2	10	11-Apr-18	24-Apr-18	43
S1D3-3E30	VDC - Lift Drawing (Prepare Draft) - Wall/Mat Foundations - Event D3	10	18-Apr-18	01-May-18	43
S1D4-3E30	VDC - Lift Drawing (Prepare Draft) - Wall/Mat Foundations - Event D4	10	25-Apr-18	08-May-18	43
S1A3-3E60	VDC - Lift Drawing (Comment Period) - Wall/Mat Foundations - Event A3	5	06-Feb-18 A	12-Feb-18 A	
S1F3-3E60	VDC - Lift Drawing (Comment Period) - Wall/Mat Foundations - Event F3	5	06-Feb-18 A	12-Feb-18 A	
S1A1-3E100	VDC - Lift Drawing (Comment Period) - Wall/Mat Foundations - Event A1	5	13-Feb-18 A	19-Feb-18 A	
S1F1-3E100	VDC - Lift Drawing (Comment Period) - Wall/Mat Foundations - Event F1	5	14-Feb-18 A	20-Feb-18 A	
S1A2-3E100	VDC - Lift Drawing (Comment Period) - Wall/Mat Foundations - Event A2	5	19-Feb-18 A	23-Feb-18 A	
S1F2-3E100	VDC - Lift Drawing (Comment Period) - Wall/Mat Foundations - Event F2	5	21-Feb-18 A	27-Feb-18 A	
S1A4-3E60	VDC - Lift Drawing (Comment Period) - Wall/Mat Foundations - Event A4	5	23-Feb-18 A	01-Mar-18 A	
S1F4-3E60	VDC - Lift Drawing (Comment Period) - Wall/Mat Foundations - Event F4	5	28-Feb-18 A	06-Mar-18	23
S1B2-3E100	VDC - Lift Drawing (Comment Period) - Wall/Mat Foundations - Event B2	5	01-Mar-18 A	07-Mar-18	28
S1B1-3E100	VDC - Lift Drawing (Comment Period) - Wall/Mat Foundations - Event B1	5	07-Mar-18	13-Mar-18	27
S1E2-3E100	VDC - Lift Drawing (Comment Period) - Wall/Mat Foundations - Event E2	5	07-Mar-18	13-Mar-18	28
S1B3-3E100	VDC - Lift Drawing (Comment Period) - Wall/Mat Foundations - Event B3	5	12-Mar-18	16-Mar-18	31
S1E1-3E100	VDC - Lift Drawing (Comment Period) - Wall/Mat Foundations - Event E1	5	14-Mar-18	20-Mar-18	26
S1B5-3E70	VDC - Lift Drawing (Comment Period) - Wall/Mat Foundations - Event B5	5	21-Mar-18	27-Mar-18	35
S1E3-3E100	VDC - Lift Drawing (Comment Period) - Wall/Mat Foundations - Event E3	5	21-Mar-18	27-Mar-18	28
S1B4-3E70	VDC - Lift Drawing (Comment Period) - Wall/Mat Foundations - Event B4	5	26-Mar-18	30-Mar-18	35
S1E5-3E70	VDC - Lift Drawing (Comment Period) - Wall/Mat Foundations - Event E5	5	28-Mar-18	03-Apr-18	28
S1B6-3E60	VDC - Lift Drawing (Comment Period) - Wall/Mat Foundations - Event B6	5	29-Mar-18	04-Apr-18	50
S1C1-3E100	VDC - Lift Drawing (Comment Period) - Wall/Mat Foundations - Event C1	5	03-Apr-18	09-Apr-18	51
S1E4-3E70	VDC - Lift Drawing (Comment Period) - Wall/Mat Foundations - Event E4	5	04-Apr-18	10-Apr-18	26
S1C2-3E100	VDC - Lift Drawing (Comment Period) - Wall/Mat Foundations - Event C2	5	06-Apr-18	12-Apr-18	55
S1C3-3E60	VDC - Lift Drawing (Comment Period) - Wall/Mat Foundations - Event C3	5	11-Apr-18	17-Apr-18	55
S1E6-3E60	VDC - Lift Drawing (Comment Period) - Wall/Mat Foundations - Event E6	5	11-Apr-18	17-Apr-18	39
S1C4-3E60	VDC - Lift Drawing (Comment Period) - Wall/Mat Foundations - Event C4	5	16-Apr-18	20-Apr-18	55
S1D1-3E100	VDC - Lift Drawing (Comment Period) - Wall/Mat Foundations - Event D1	5	18-Apr-18	24-Apr-18	44
S1D2-3E100	VDC - Lift Drawing (Comment Period) - Wall/Mat Foundations - Event D2	5	25-Apr-18	01-May-18	47
S1D3-3E60	VDC - Lift Drawing (Comment Period) - Wall/Mat Foundations - Event D3	5	02-May-18	08-May-18	45
S1D4-3E60	VDC - Lift Drawing (Comment Period) - Wall/Mat Foundations - Event D4	5	09-May-18	15-May-18	43
S1A3-3E70	VDC - Lift Drawing (Finalize) - Wall/Mat Foundations - Event A3	5	13-Feb-18 A	19-Feb-18 A	
S1F3-3E70	VDC - Lift Drawing (Finalize) - Wall/Mat Foundations - Event F3	5	13-Feb-18 A	19-Feb-18 A	
S1A1-3E110	VDC - Lift Drawing (Finalize) - Wall/Mat Foundations - Event A1	5	20-Feb-18 A	26-Feb-18 A	
S1F1-3E110	VDC - Lift Drawing (Finalize) - Wall/Mat Foundations - Event F1	5	21-Feb-18 A	27-Feb-18 A	
S1A2-3E110	VDC - Lift Drawing (Finalize) - Wall/Mat Foundations - Event A2	5	26-Feb-18 A	02-Mar-18 A	
S1F2-3E110	VDC - Lift Drawing (Finalize) - Wall/Mat Foundations - Event F2	5	28-Feb-18 A	06-Mar-18	18
S1A4-3E70	VDC - Lift Drawing (Finalize) - Wall/Mat Foundations - Event A4	5	02-Mar-18 A	08-Mar-18	27
S1F4-3E70	VDC - Lift Drawing (Finalize) - Wall/Mat Foundations - Event F4	5	07-Mar-18	13-Mar-18	23
S1B2-3E110	VDC - Lift Drawing (Finalize) - Wall/Mat Foundations - Event B2	5	08-Mar-18	14-Mar-18	28
S1B1-3E110	VDC - Lift Drawing (Finalize) - Wall/Mat Foundations - Event B1	5	14-Mar-18	20-Mar-18	27
S1E2-3E110	VDC - Lift Drawing (Finalize) - Wall/Mat Foundations - Event E2	5	14-Mar-18	20-Mar-18	28
S1B3-3E110	VDC - Lift Drawing (Finalize) - Wall/Mat Foundations - Event B3	5	19-Mar-18	23-Mar-18	31
S1E1-3E110	VDC - Lift Drawing (Finalize) - Wall/Mat Foundations - Event E1	5	21-Mar-18	27-Mar-18	26
S1B5-3E80	VDC - Lift Drawing (Finalize) - Wall/Mat Foundations - Event B5	5	28-Mar-18	03-Apr-18	35
S1E3-3E110	VDC - Lift Drawing (Finalize) - Wall/Mat Foundations - Event E3	5	28-Mar-18	03-Apr-18	28
S1B4-3E80	VDC - Lift Drawing (Finalize) - Wall/Mat Foundations - Event B4	5	02-Apr-18	06-Apr-18	35
S1E5-3E80	VDC - Lift Drawing (Finalize) - Wall/Mat Foundations - Event E5	5	04-Apr-18	10-Apr-18	28

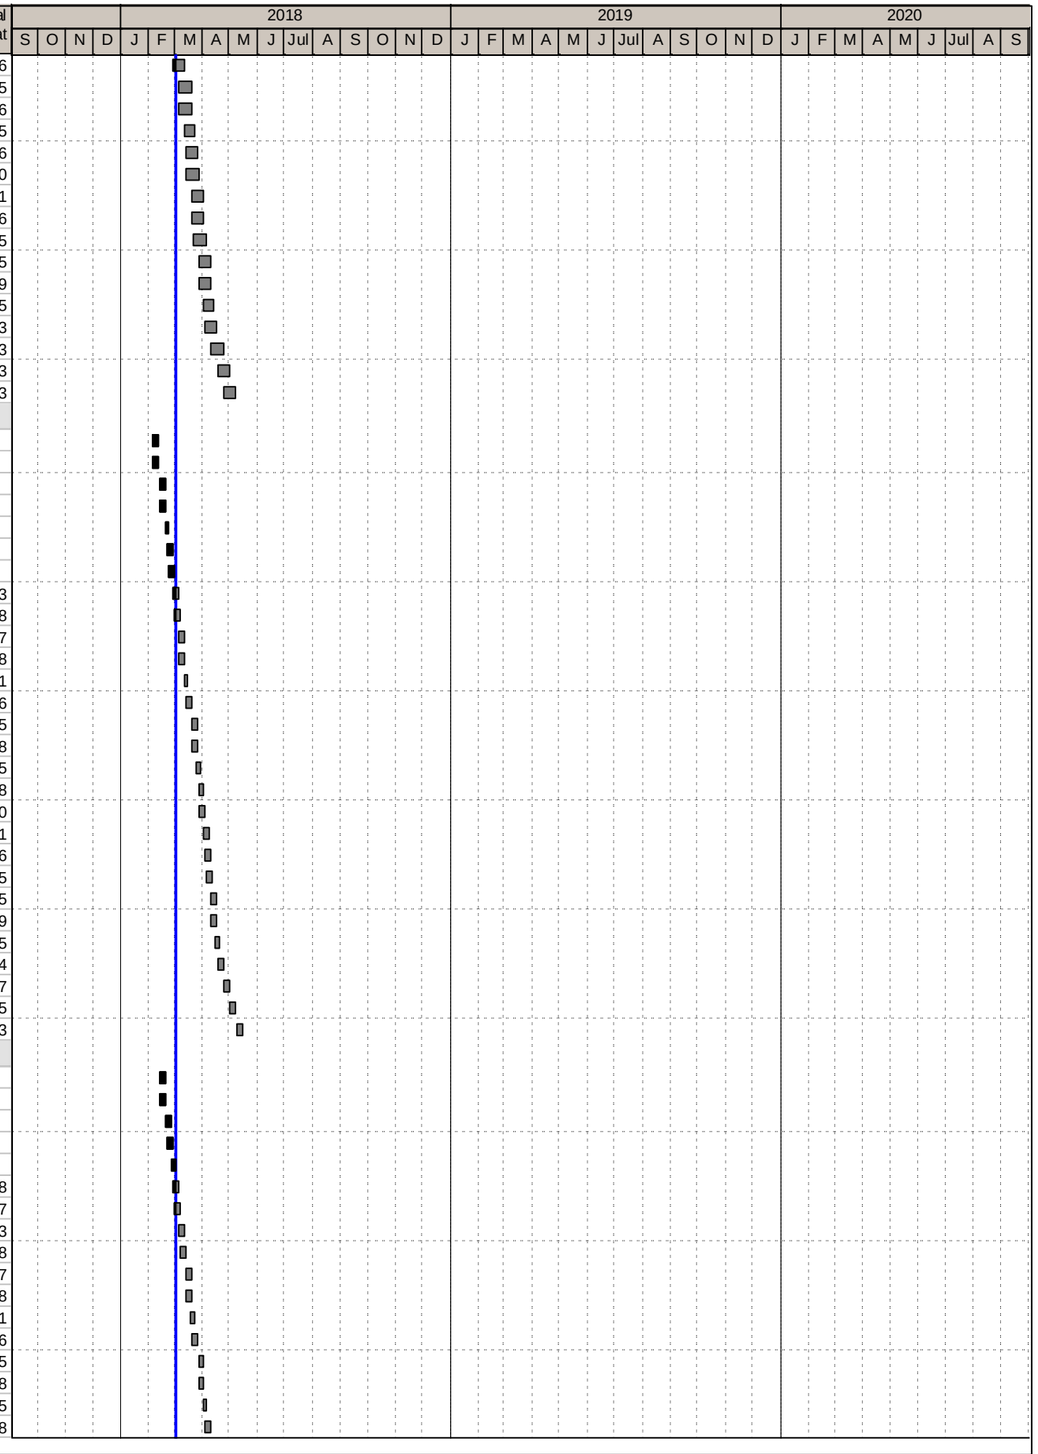

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S1B6-3E70	VDC - Lift Drawing (Finalize) - Wall/Mat Foundations - Event B6	5	05-Apr-18	11-Apr-18	50
S1C1-3E110	VDC - Lift Drawing (Finalize) - Wall/Mat Foundations - Event C1	5	10-Apr-18	16-Apr-18	51
S1E4-3E80	VDC - Lift Drawing (Finalize) - Wall/Mat Foundations - Event E4	5	11-Apr-18	17-Apr-18	26
S1C2-3E110	VDC - Lift Drawing (Finalize) - Wall/Mat Foundations - Event C2	5	13-Apr-18	19-Apr-18	55
S1C3-3E70	VDC - Lift Drawing (Finalize) - Wall/Mat Foundations - Event C3	5	18-Apr-18	24-Apr-18	55
S1E6-3E70	VDC - Lift Drawing (Finalize) - Wall/Mat Foundations - Event E6	5	18-Apr-18	24-Apr-18	39
S1C4-3E70	VDC - Lift Drawing (Finalize) - Wall/Mat Foundations - Event C4	5	23-Apr-18	27-Apr-18	55
S1D1-3E110	VDC - Lift Drawing (Finalize) - Wall/Mat Foundations - Event D1	5	25-Apr-18	01-May-18	44
S1D2-3E110	VDC - Lift Drawing (Finalize) - Wall/Mat Foundations - Event D2	5	02-May-18	08-May-18	47
S1D3-3E70	VDC - Lift Drawing (Finalize) - Wall/Mat Foundations - Event D3	5	09-May-18	15-May-18	45
S1D4-3E70	VDC - Lift Drawing (Finalize) - Wall/Mat Foundations - Event D4	5	16-May-18	22-May-18	43
S1A1-3E40	VDC - Lift Drawing (Prepare Draft) - Spread Footings - Event A1	10	24-Jan-18 A	05-Feb-18 A	
S1F1-3E40	VDC - Lift Drawing (Prepare Draft) - Spread Footings - Event F1	10	24-Jan-18 A	05-Feb-18 A	
S1A2-3E40	VDC - Lift Drawing (Prepare Draft) - Spread Footings - Event A2	10	31-Jan-18 A	13-Feb-18 A	
S1F2-3E40	VDC - Lift Drawing (Prepare Draft) - Spread Footings - Event F2	10	31-Jan-18 A	13-Feb-18 A	
S1A3-3E40	VDC - Lift Drawing (Prepare Draft) - Spread Footings - Event A3	10	07-Feb-18 A	20-Feb-18 A	
S1F3-3E40	VDC - Lift Drawing (Prepare Draft) - Spread Footings - Event F3	10	07-Feb-18 A	20-Feb-18 A	
S1F4-3E40	VDC - Lift Drawing (Prepare Draft) - Spread Footings - Event F4	10	07-Feb-18 A	20-Feb-18 A	
S1B1-3E40	VDC - Lift Drawing (Prepare Draft) - Spread Footings - Event B1	10	14-Feb-18 A	27-Feb-18 A	
S1E1-3E40	VDC - Lift Drawing (Prepare Draft) - Spread Footings - Event E1	10	14-Feb-18 A	27-Feb-18 A	
S1B2-3E40	VDC - Lift Drawing (Prepare Draft) - Spread Footings - Event B2	10	21-Feb-18 A	06-Mar-18	41
S1E2-3E40	VDC - Lift Drawing (Prepare Draft) - Spread Footings - Event E2	10	21-Feb-18 A	06-Mar-18	47
S1B3-3E40	VDC - Lift Drawing (Prepare Draft) - Spread Footings - Event B3	10	28-Feb-18 A	13-Mar-18	53
S1E3-3E40	VDC - Lift Drawing (Prepare Draft) - Spread Footings - Event E3	10	28-Feb-18 A	13-Mar-18	50
S1B4-3E40	VDC - Lift Drawing (Prepare Draft) - Spread Footings - Event B4	10	07-Mar-18	20-Mar-18	53
S1E4-3E40	VDC - Lift Drawing (Prepare Draft) - Spread Footings - Event E4	10	07-Mar-18	20-Mar-18	55
S1B5-3E40	VDC - Lift Drawing (Prepare Draft) - Spread Footings - Event B5	10	14-Mar-18	27-Mar-18	54
S1E5-3E40	VDC - Lift Drawing (Prepare Draft) - Spread Footings - Event E5	10	14-Mar-18	27-Mar-18	56
S1C1-3E40	VDC - Lift Drawing (Prepare Draft) - Spread Footings - Event C1	10	21-Mar-18	03-Apr-18	55
S1D1-3E40	VDC - Lift Drawing (Prepare Draft) - Spread Footings - Event D1	10	21-Mar-18	03-Apr-18	57
S1C2-3E40	VDC - Lift Drawing (Prepare Draft) - Spread Footings - Event C2	10	28-Mar-18	10-Apr-18	56
S1D2-3E40	VDC - Lift Drawing (Prepare Draft) - Spread Footings - Event D2	10	28-Mar-18	10-Apr-18	60
S1C3-3E40	VDC - Lift Drawing (Prepare Draft) - Spread Footings - Event C3	10	04-Apr-18	17-Apr-18	57
S1D3-3E40	VDC - Lift Drawing (Prepare Draft) - Spread Footings - Event D3	10	04-Apr-18	17-Apr-18	61
S1A1-3E120	VDC - Lift Drawing (Comment Period) - Spread Footings - Event A1	5	06-Feb-18 A	12-Feb-18 A	
S1F1-3E120	VDC - Lift Drawing (Comment Period) - Spread Footings - Event F1	5	06-Feb-18 A	12-Feb-18 A	
S1A2-3E120	VDC - Lift Drawing (Comment Period) - Spread Footings - Event A2	5	14-Feb-18 A	20-Feb-18 A	
S1F2-3E120	VDC - Lift Drawing (Comment Period) - Spread Footings - Event F2	5	14-Feb-18 A	20-Feb-18 A	
S1A3-3E80	VDC - Lift Drawing (Comment Period) - Spread Footings - Event A3	5	21-Feb-18 A	27-Feb-18 A	
S1F3-3E80	VDC - Lift Drawing (Comment Period) - Spread Footings - Event F3	5	21-Feb-18 A	27-Feb-18 A	
S1F4-3E120	VDC - Lift Drawing (Comment Period) - Spread Footings - Event F4	5	21-Feb-18 A	27-Feb-18 A	
S1B1-3E120	VDC - Lift Drawing (Comment Period) - Spread Footings - Event B1	5	28-Feb-18 A	06-Mar-18	31
S1E1-3E120	VDC - Lift Drawing (Comment Period) - Spread Footings - Event E1	5	28-Feb-18 A	06-Mar-18	36
S1B2-3E120	VDC - Lift Drawing (Comment Period) - Spread Footings - Event B2	5	07-Mar-18	13-Mar-18	41
S1E2-3E120	VDC - Lift Drawing (Comment Period) - Spread Footings - Event E2	5	07-Mar-18	13-Mar-18	47
S1B3-3E120	VDC - Lift Drawing (Comment Period) - Spread Footings - Event B3	5	14-Mar-18	20-Mar-18	54
S1E3-3E120	VDC - Lift Drawing (Comment Period) - Spread Footings - Event E3	5	14-Mar-18	20-Mar-18	50
S1B4-3E90	VDC - Lift Drawing (Comment Period) - Spread Footings - Event B4	5	21-Mar-18	27-Mar-18	53
S1E4-3E90	VDC - Lift Drawing (Comment Period) - Spread Footings - Event E4	5	21-Mar-18	27-Mar-18	55
S1B5-3E90	VDC - Lift Drawing (Comment Period) - Spread Footings - Event B5	5	28-Mar-18	03-Apr-18	54
S1E5-3E90	VDC - Lift Drawing (Comment Period) - Spread Footings - Event E5	5	28-Mar-18	03-Apr-18	56
S1C1-3E120	VDC - Lift Drawing (Comment Period) - Spread Footings - Event C1	5	04-Apr-18	10-Apr-18	55
S1D1-3E120	VDC - Lift Drawing (Comment Period) - Spread Footings - Event D1	5	04-Apr-18	10-Apr-18	57
S1C2-3E120	VDC - Lift Drawing (Comment Period) - Spread Footings - Event C2	5	11-Apr-18	17-Apr-18	56
S1D2-3E120	VDC - Lift Drawing (Comment Period) - Spread Footings - Event D2	5	11-Apr-18	17-Apr-18	60
S1C3-3E80	VDC - Lift Drawing (Comment Period) - Spread Footings - Event C3	5	18-Apr-18	24-Apr-18	57
S1D3-3E80	VDC - Lift Drawing (Comment Period) - Spread Footings - Event D3	5	18-Apr-18	24-Apr-18	61
S1A1-3E130	VDC - Lift Drawing (Finalize) - Spread Footings - Event A1	5	13-Feb-18 A	19-Feb-18 A	
S1F1-3E130	VDC - Lift Drawing (Finalize) - Spread Footings - Event F1	5	13-Feb-18 A	19-Feb-18 A	
S1A2-3E130	VDC - Lift Drawing (Finalize) - Spread Footings - Event A2	5	21-Feb-18 A	27-Feb-18 A	

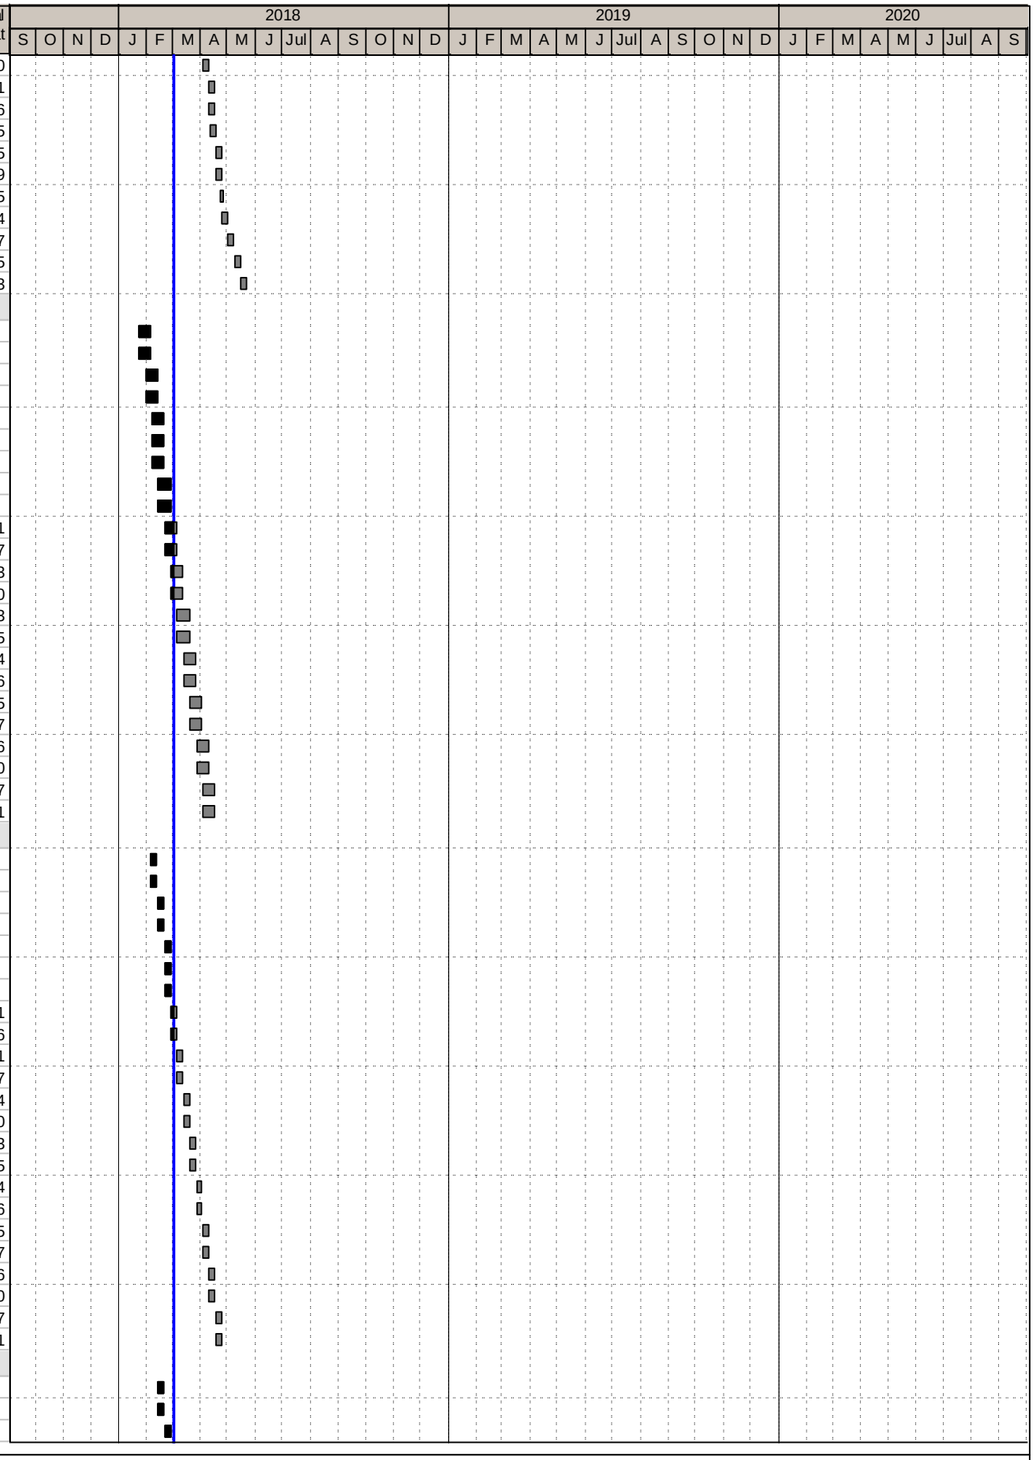

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S1F2-3E130	VDC - Lift Drawing (Finalize) - Spread Footings - Event F2	5	21-Feb-18 A	27-Feb-18 A	
S1A3-3E90	VDC - Lift Drawing (Finalize) - Spread Footings - Event A3	5	28-Feb-18 A	06-Mar-18	30
S1F3-3E90	VDC - Lift Drawing (Finalize) - Spread Footings - Event F3	5	28-Feb-18 A	06-Mar-18	32
S1F4-3E130	VDC - Lift Drawing (Finalize) - Spread Footings - Event F4	5	28-Feb-18 A	06-Mar-18	35
S1B1-3E130	VDC - Lift Drawing (Finalize) - Spread Footings - Event B1	5	07-Mar-18	13-Mar-18	31
S1E1-3E130	VDC - Lift Drawing (Finalize) - Spread Footings - Event E1	5	07-Mar-18	13-Mar-18	36
S1B2-3E130	VDC - Lift Drawing (Finalize) - Spread Footings - Event B2	5	14-Mar-18	20-Mar-18	41
S1E2-3E130	VDC - Lift Drawing (Finalize) - Spread Footings - Event E2	5	14-Mar-18	20-Mar-18	47
S1B3-3E130	VDC - Lift Drawing (Finalize) - Spread Footings - Event B3	5	21-Mar-18	27-Mar-18	54
S1E3-3E130	VDC - Lift Drawing (Finalize) - Spread Footings - Event E3	5	21-Mar-18	27-Mar-18	50
S1B4-3E100	VDC - Lift Drawing (Finalize) - Spread Footings - Event B4	5	28-Mar-18	03-Apr-18	53
S1E4-3E100	VDC - Lift Drawing (Finalize) - Spread Footings - Event E4	5	28-Mar-18	03-Apr-18	55
S1B5-3E100	VDC - Lift Drawing (Finalize) - Spread Footings - Event B5	5	04-Apr-18	10-Apr-18	54
S1E5-3E100	VDC - Lift Drawing (Finalize) - Spread Footings - Event E5	5	04-Apr-18	10-Apr-18	56
S1C1-3E130	VDC - Lift Drawing (Finalize) - Spread Footings - Event C1	5	11-Apr-18	17-Apr-18	55
S1D1-3E130	VDC - Lift Drawing (Finalize) - Spread Footings - Event D1	5	11-Apr-18	17-Apr-18	57
S1C2-3E130	VDC - Lift Drawing (Finalize) - Spread Footings - Event C2	5	18-Apr-18	24-Apr-18	56
S1D2-3E130	VDC - Lift Drawing (Finalize) - Spread Footings - Event D2	5	18-Apr-18	24-Apr-18	60
S1C3-3E90	VDC - Lift Drawing (Finalize) - Spread Footings - Event C3	5	25-Apr-18	01-May-18	57
S1D3-3E90	VDC - Lift Drawing (Finalize) - Spread Footings - Event D3	5	25-Apr-18	01-May-18	61
S1A1-3E60	VDC - Lift Drawing (Coordinate/Prepare Draft) - Elev/Esc Pits - Event A1	10	01-Feb-18 A	19-Feb-18 A	
S1F1-3E60	VDC - Lift Drawing (Coordinate/Prepare Draft) - Elev/Esc Pits - Event F1	10	01-Feb-18 A	19-Feb-18 A	
S1B1-3E60	VDC - Lift Drawing (Coordinate/Prepare Draft) - Elev/Esc Pits - Event B1	10	09-Feb-18 A	21-Feb-18 A	
S1E2-3E60	VDC - Lift Drawing (Coordinate/Prepare Draft) - Elev/Esc Pits - Event E2	10	09-Feb-18 A	21-Feb-18 A	
S1B2-3E60	VDC - Lift Drawing (Coordinate/Prepare Draft) - Elev/Esc Pits - Event B2	10	19-Feb-18 A	02-Mar-18 A	
S1B5-3E60	VDC - Lift Drawing (Coordinate/Prepare Draft) - Elev/Esc Pits - Event B5	10	07-Mar-18	20-Mar-18	83
S1E3-3E60	VDC - Lift Drawing (Coordinate/Prepare Draft) - Elev/Esc Pits - Event E3	10	07-Mar-18	20-Mar-18	53
S1E5-3E60	VDC - Lift Drawing (Coordinate/Prepare Draft) - Elev/Esc Pits - Event E5	10	14-Mar-18	27-Mar-18	63
S1D1-3E60	VDC - Lift Drawing (Coordinate/Prepare Draft) - Elev/Esc Pits - Event D1	10	21-Mar-18	03-Apr-18	63
S1F2-3E60	VDC - Lift Drawing (Coordinate/Prepare Draft) - Elev/Esc Pits - Event F @ Core #2	10	09-Apr-18	20-Apr-18	95
S1A2-3E60	VDC - Lift Drawing (Coordinate/Prepare Draft) - Elev/Esc Pits - Event A @ Core #3	10	13-Apr-18	26-Apr-18	71
S1E1-3E60	VDC - Lift Drawing (Coordinate/Prepare Draft) - Elev/Esc Pits - Event E @ Core #1	10	23-Apr-18	04-May-18	116
S1B3-3E60	VDC - Lift Drawing (Coordinate/Prepare Draft) - Elev/Esc Pits - Event B @ Core #4	10	27-Apr-18	10-May-18	81
S1E4-3E60	VDC - Lift Drawing (Coordinate/Prepare Draft) - Elev/Esc Pits - Event E @ Core #8	10	07-May-18	18-May-18	116
S1B4-3E60	VDC - Lift Drawing (Coordinate/Prepare Draft) - Elev/Esc Pits - Event B @ Core #5	10	11-May-18	24-May-18	81
S1D2-3E60	VDC - Lift Drawing (Coordinate/Prepare Draft) - Elev/Esc Pits - Event D @ Core #7	10	21-May-18	04-Jun-18	166
S1C1-3E60	VDC - Lift Drawing (Coordinate/Prepare Draft) - Elev/Esc Pits - Event C @ Core #6	10	25-May-18	08-Jun-18	132
S1A1-3E140	VDC - Lift Drawing (Comment Period) - Elev/Esc Pits - Event A1	5	20-Feb-18 A	26-Feb-18 A	
S1F1-3E140	VDC - Lift Drawing (Comment Period) - Elev/Esc Pits - Event F1	5	20-Feb-18 A	26-Feb-18 A	
S1B1-3E140	VDC - Lift Drawing (Comment Period) - Elev/Esc Pits - Event B1	5	22-Feb-18 A	28-Feb-18 A	
S1E2-3E140	VDC - Lift Drawing (Comment Period) - Elev/Esc Pits - Event E2	5	22-Feb-18 A	28-Feb-18 A	
S1B2-3E140	VDC - Lift Drawing (Comment Period) - Elev/Esc Pits - Event B2	5	05-Mar-18	09-Mar-18	49
S1B5-3E110	VDC - Lift Drawing (Comment Period) - Elev/Esc Pits - Event B5	5	21-Mar-18	27-Mar-18	83
S1E3-3E140	VDC - Lift Drawing (Comment Period) - Elev/Esc Pits - Event E3	5	21-Mar-18	27-Mar-18	53
S1E5-3E110	VDC - Lift Drawing (Comment Period) - Elev/Esc Pits - Event E5	5	28-Mar-18	03-Apr-18	77
S1D1-3E140	VDC - Lift Drawing (Comment Period) - Elev/Esc Pits - Event D1	5	04-Apr-18	10-Apr-18	63
S1F2-3E140	VDC - Lift Drawing (Comment Period) - Elev/Esc Pits - Event F @ Core #2	5	23-Apr-18	27-Apr-18	95
S1A2-3E140	VDC - Lift Drawing (Comment Period) - Elev/Esc Pits - Event A @ Core #3	5	27-Apr-18	03-May-18	71
S1E1-3E140	VDC - Lift Drawing (Comment Period) - Elev/Esc Pits - Event E @ Core #1	5	07-May-18	11-May-18	126
S1B3-3E140	VDC - Lift Drawing (Comment Period) - Elev/Esc Pits - Event B @ Core #4	5	11-May-18	17-May-18	91
S1E4-3E110	VDC - Lift Drawing (Comment Period) - Elev/Esc Pits - Event E @ Core #8	5	21-May-18	25-May-18	116
S1B4-3E110	VDC - Lift Drawing (Comment Period) - Elev/Esc Pits - Event B @ Core #5	5	25-May-18	01-Jun-18	81
S1D2-3E140	VDC - Lift Drawing (Comment Period) - Elev/Esc Pits - Event D @ Core #7	5	05-Jun-18	11-Jun-18	166
S1C1-3E140	VDC - Lift Drawing (Comment Period) - Elev/Esc Pits - Event C @ Core #6	5	11-Jun-18	15-Jun-18	132
S1A1-3E150	VDC - Lift Drawing (Finalize) - Elev/Esc Pits - Event A1	5	27-Feb-18 A	05-Mar-18	30
S1F1-3E150	VDC - Lift Drawing (Finalize) - Elev/Esc Pits - Event F1	5	27-Feb-18 A	05-Mar-18	31
S1B1-3E150	VDC - Lift Drawing (Finalize) - Elev/Esc Pits - Event B1	5	01-Mar-18 A	07-Mar-18	41
S1E2-3E150	VDC - Lift Drawing (Finalize) - Elev/Esc Pits - Event E2	5	01-Mar-18 A	07-Mar-18	57
S1B2-3E150	VDC - Lift Drawing (Finalize) - Elev/Esc Pits - Event B2	5	12-Mar-18	16-Mar-18	49
S1B5-3E120	VDC - Lift Drawing (Finalize) - Elev/Esc Pits - Event B5	5	28-Mar-18	03-Apr-18	83

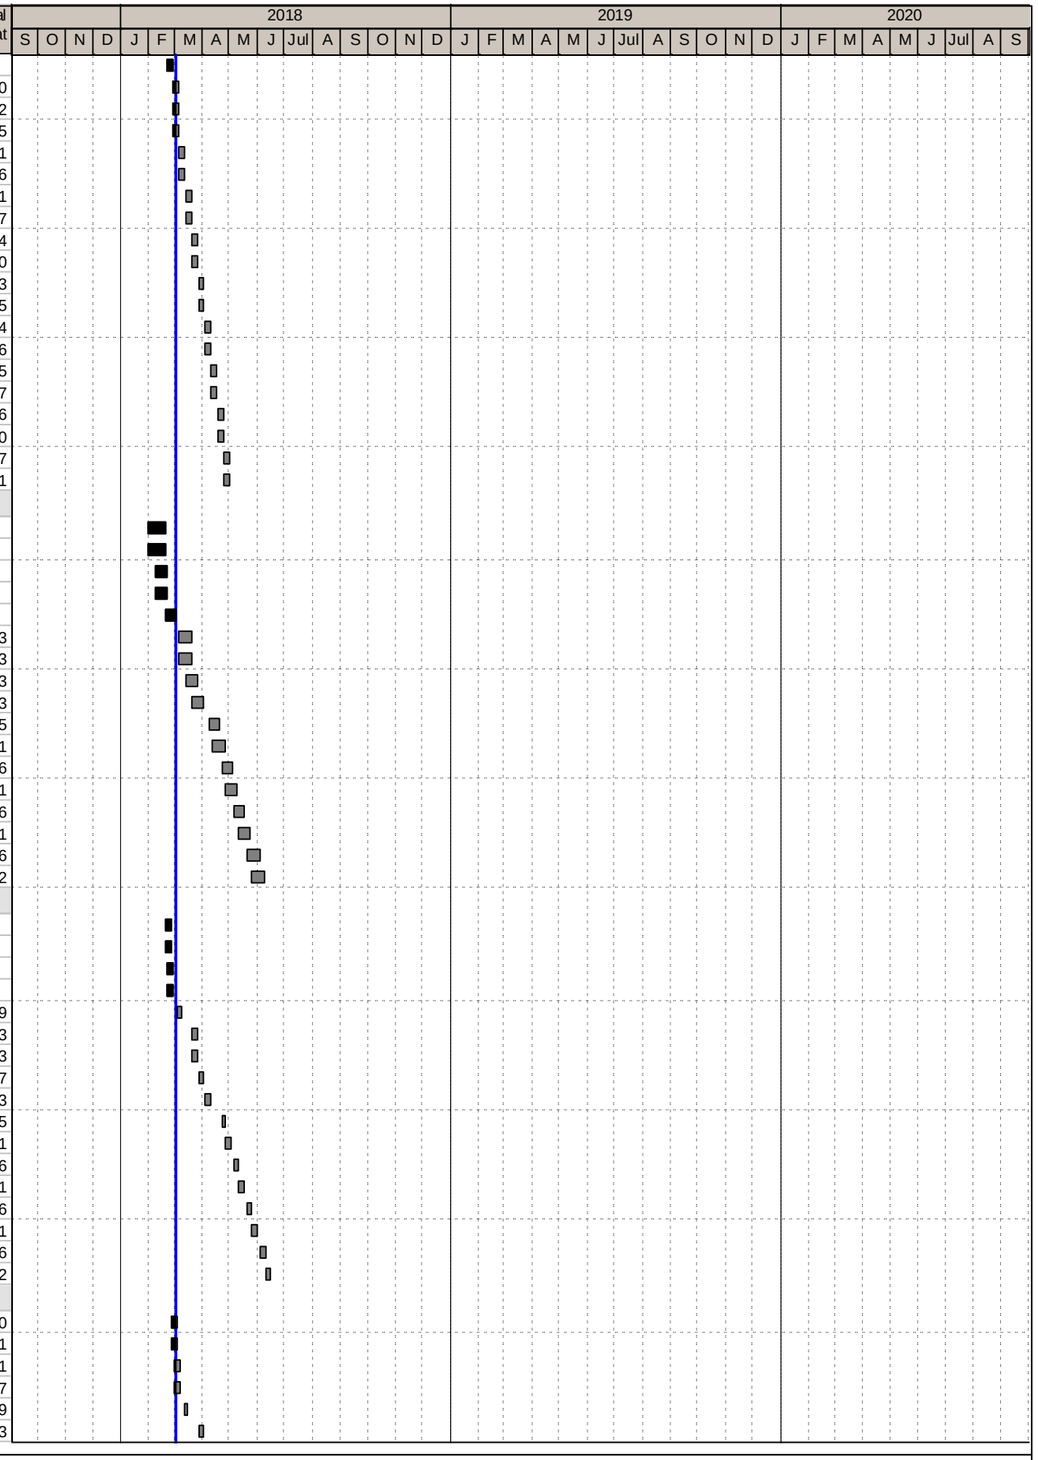

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S1E3-3E150	VDC - Lift Drawing (Finalize) - Elev/Esc Pits - Event E3	5	28-Mar-18	03-Apr-18	53
S1E5-3E120	VDC - Lift Drawing (Finalize) - Elev/Esc Pits - Event E5	5	04-Apr-18	10-Apr-18	77
S1D1-3E150	VDC - Lift Drawing (Finalize) - Elev/Esc Pits - Event D1	5	11-Apr-18	17-Apr-18	63
S1F2-3E150	VDC - Lift Drawing (Finalize) - Elev/Esc Pits - Event F @ Core #2	5	30-Apr-18	04-May-18	95
S1A2-3E150	VDC - Lift Drawing (Finalize) - Elev/Esc Pits - Event A @ Core #3	5	04-May-18	10-May-18	71
S1E1-3E150	VDC - Lift Drawing (Finalize) - Elev/Esc Pits - Event E @ Core #1	5	14-May-18	18-May-18	126
S1B3-3E150	VDC - Lift Drawing (Finalize) - Elev/Esc Pits - Event B @ Core #4	5	18-May-18	24-May-18	91
S1E4-3E120	VDC - Lift Drawing (Finalize) - Elev/Esc Pits - Event E @ Core #8	5	29-May-18	04-Jun-18	116
S1B4-3E120	VDC - Lift Drawing (Finalize) - Elev/Esc Pits - Event B @ Core #5	5	04-Jun-18	08-Jun-18	81
S1D2-3E150	VDC - Lift Drawing (Finalize) - Elev/Esc Pits - Event D @ Core #7	5	12-Jun-18	18-Jun-18	166
S1C1-3E150	VDC - Lift Drawing (Finalize) - Elev/Esc Pits - Event C @ Core #6	5	18-Jun-18	22-Jun-18	132
VDC - 000 Event Level - Concrete Wall Coordination					
S1A1-3E50	VDC - Lift Drawing (Prepare Draft) - Fndn Wall- Event A1	10	26-Feb-18 A	09-Mar-18	4
S1F1-3E50	VDC - Lift Drawing (Prepare Draft) - Fndn Wall- Event F1	10	26-Feb-18 A	09-Mar-18	6
S1A2-3E50	VDC - Lift Drawing (Prepare Draft) - Fndn Wall- Event A2	10	05-Mar-18	16-Mar-18	4
S1F2-3E50	VDC - Lift Drawing (Prepare Draft) - Fndn Wall- Event F2	10	05-Mar-18	16-Mar-18	6
S1A3-3E50	VDC - Lift Drawing (Prepare Draft) - Fndn Wall- Event A3	10	12-Mar-18	23-Mar-18	4
S1F3-3E50	VDC - Lift Drawing (Prepare Draft) - Fndn Wall- Event F3	10	12-Mar-18	23-Mar-18	6
S1A4-3E50	VDC - Lift Drawing (Prepare Draft) - Fndn Wall- Event A4	10	19-Mar-18	30-Mar-18	4
S1F4-3E50	VDC - Lift Drawing (Prepare Draft) - Fndn Wall- Event F4	10	19-Mar-18	30-Mar-18	6
S1A5-3E50	VDC - Lift Drawing (Prepare Draft) - Fndn Wall- Event A5	10	26-Mar-18	06-Apr-18	4
S1F5-3E50	VDC - Lift Drawing (Prepare Draft) - Fndn Wall- Event F5	10	26-Mar-18	06-Apr-18	7
S1B1-3E50	VDC - Lift Drawing (Prepare Draft) - Fndn Wall- Event B1	10	02-Apr-18	13-Apr-18	4
S1E1-3E50	VDC - Lift Drawing (Prepare Draft) - Fndn Wall- Event E1	10	02-Apr-18	13-Apr-18	7
S1B2-3E50	VDC - Lift Drawing (Prepare Draft) - Fndn Wall- Event B2	10	06-Apr-18	19-Apr-18	4
S1E2-3E50	VDC - Lift Drawing (Prepare Draft) - Fndn Wall- Event E2	10	09-Apr-18	20-Apr-18	7
S1B3-3E50	VDC - Lift Drawing (Prepare Draft) - Fndn Wall- Event B3	10	12-Apr-18	25-Apr-18	5
S1E3-3E50	VDC - Lift Drawing (Prepare Draft) - Fndn Wall- Event E3	10	16-Apr-18	27-Apr-18	7
S1B4-3E50	VDC - Lift Drawing (Prepare Draft) - Fndn Wall- Event B4	10	18-Apr-18	01-May-18	11
S1E4-3E50	VDC - Lift Drawing (Prepare Draft) - Fndn Wall- Event E4	10	20-Apr-18	03-May-18	10
S1B5-3E50	VDC - Lift Drawing (Prepare Draft) - Fndn Wall- Event B5	10	24-Apr-18	07-May-18	11
S1E5-3E50	VDC - Lift Drawing (Prepare Draft) - Fndn Wall- Event E5	10	26-Apr-18	09-May-18	10
S1B6-3E50	VDC - Lift Drawing (Prepare Draft) - Fndn Wall- Event B6	10	30-Apr-18	11-May-18	16
S1E6-3E50	VDC - Lift Drawing (Prepare Draft) - Fndn Wall- Event E6	10	02-May-18	15-May-18	15
S1B7-3E50	VDC - Lift Drawing (Prepare Draft) - Fndn Wall- Event B7	10	04-May-18	17-May-18	16
S1E7-3E50	VDC - Lift Drawing (Prepare Draft) - Fndn Wall- Event E7	10	08-May-18	21-May-18	15
S1B8-3E50	VDC - Lift Drawing (Prepare Draft) - Fndn Wall- Event B8	10	10-May-18	23-May-18	16
S1E8-3E50	VDC - Lift Drawing (Prepare Draft) - Fndn Wall- Event E8	10	14-May-18	25-May-18	15
S1C1-3E50	VDC - Lift Drawing (Prepare Draft) - Fndn Wall- Event C1	10	16-May-18	30-May-18	17
S1D1-3E50	VDC - Lift Drawing (Prepare Draft) - Fndn Wall- Event D1	10	18-May-18	01-Jun-18	19
S1C2-3E50	VDC - Lift Drawing (Prepare Draft) - Fndn Wall- Event C2	10	22-May-18	05-Jun-18	17
S1D2-3E50	VDC - Lift Drawing (Prepare Draft) - Fndn Wall- Event D2	10	24-May-18	07-Jun-18	19
S1C3-3E50	VDC - Lift Drawing (Prepare Draft) - Fndn Wall- Event C3	10	29-May-18	11-Jun-18	17
S1D3-3E50	VDC - Lift Drawing (Prepare Draft) - Fndn Wall- Event D3	10	31-May-18	13-Jun-18	19
S1C4-3E50	VDC - Lift Drawing (Prepare Draft) - Fndn Wall- Event C4	10	04-Jun-18	15-Jun-18	57
S1D4-3E50	VDC - Lift Drawing (Prepare Draft) - Fndn Wall- Event D4	10	06-Jun-18	19-Jun-18	53
S1C5-3E50	VDC - Lift Drawing (Prepare Draft) - Fndn Wall- Event C5	10	08-Jun-18	21-Jun-18	57
S1D5-3E50	VDC - Lift Drawing (Prepare Draft) - Fndn Wall- Event D5	10	12-Jun-18	25-Jun-18	53
S1C6-3E50	VDC - Lift Drawing (Prepare Draft) - Fndn Wall- Event C6	10	14-Jun-18	27-Jun-18	57
S1D6-3E50	VDC - Lift Drawing (Prepare Draft) - Fndn Wall- Event D6	10	18-Jun-18	29-Jun-18	53
S1C7-3E50	VDC - Lift Drawing (Prepare Draft) - Fndn Wall- Event C7	10	20-Jun-18	03-Jul-18	57
S1D7-3E50	VDC - Lift Drawing (Prepare Draft) - Fndn Wall- Event D7	10	22-Jun-18	06-Jul-18	53
S1A1-3E160	VDC - Lift Drawing (Comment Period) - Fndn Wall - Event A1	5	12-Mar-18	16-Mar-18	6
S1F1-3E160	VDC - Lift Drawing (Comment Period) - Fndn Wall - Event F1	5	12-Mar-18	16-Mar-18	8
S1A2-3E160	VDC - Lift Drawing (Comment Period) - Fndn Wall - Event A2	5	19-Mar-18	23-Mar-18	4
S1F2-3E160	VDC - Lift Drawing (Comment Period) - Fndn Wall - Event F2	5	19-Mar-18	23-Mar-18	6
S1A3-3E100	VDC - Lift Drawing (Comment Period) - Fndn Wall - Event A3	5	26-Mar-18	30-Mar-18	7
S1F3-3E100	VDC - Lift Drawing (Comment Period) - Fndn Wall - Event F3	5	26-Mar-18	30-Mar-18	8
S1A4-3E80	VDC - Lift Drawing (Comment Period) - Fndn Wall - Event A4	5	02-Apr-18	06-Apr-18	7
S1F4-3E80	VDC - Lift Drawing (Comment Period) - Fndn Wall - Event F4	5	02-Apr-18	06-Apr-18	6
S1A5-3E60	VDC - Lift Drawing (Comment Period) - Fndn Wall - Event A5	5	09-Apr-18	13-Apr-18	5

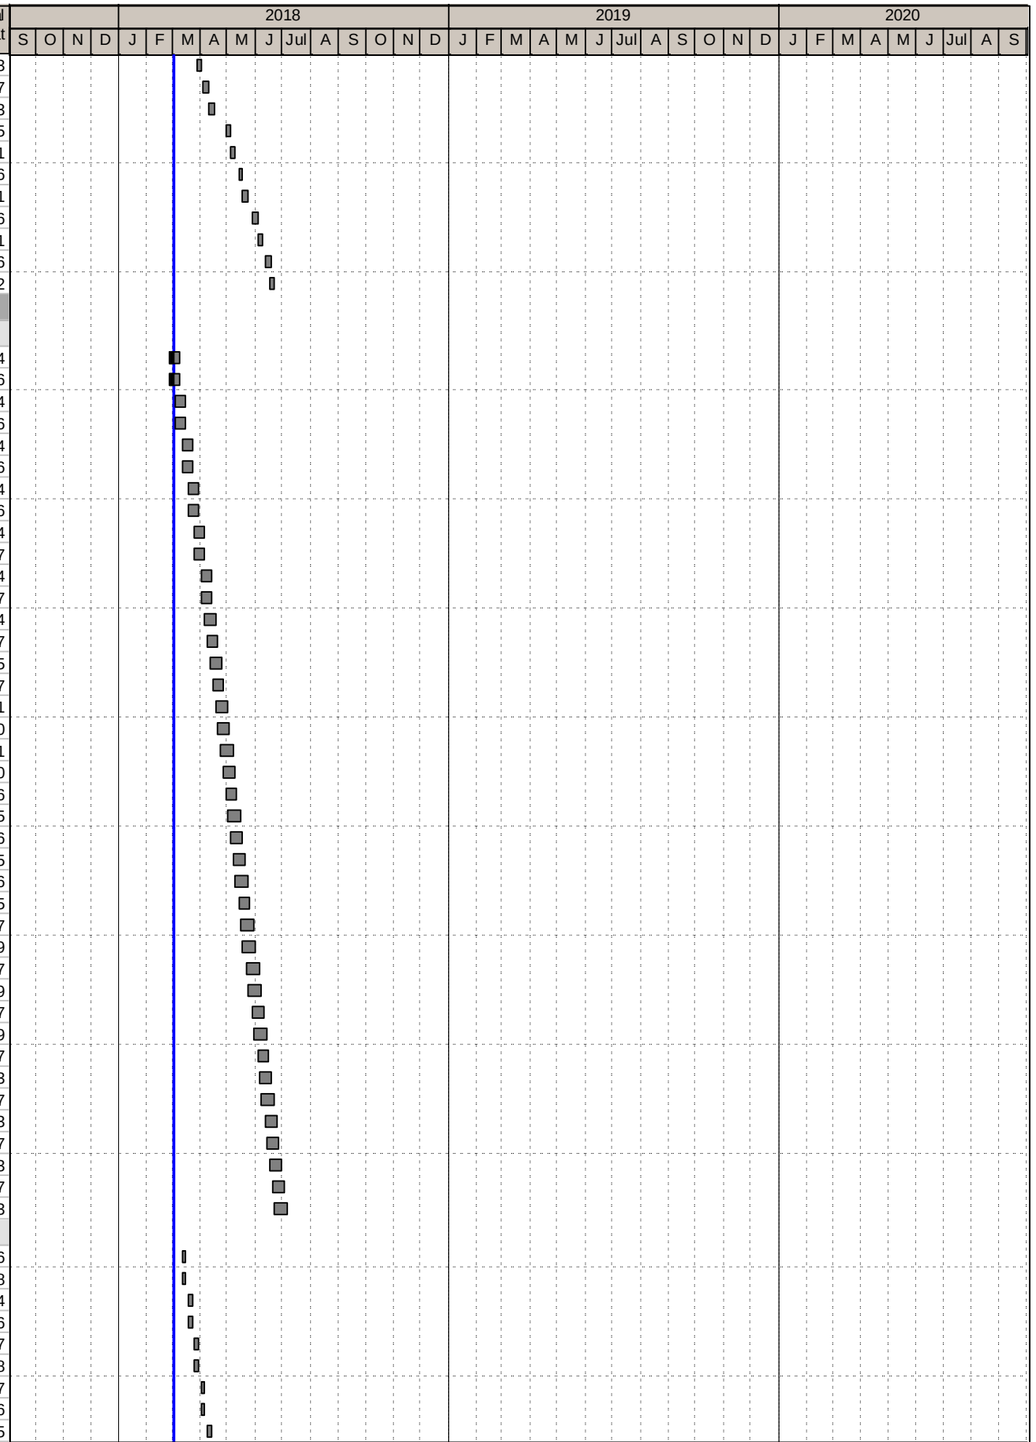

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S1F5-3E60	VDC - Lift Drawing (Comment Period) - Fndn Wall - Event F5	5	09-Apr-18	13-Apr-18	9
S1B1-3E160	VDC - Lift Drawing (Comment Period) - Fndn Wall - Event B1	5	16-Apr-18	20-Apr-18	5
S1E1-3E160	VDC - Lift Drawing (Comment Period) - Fndn Wall - Event E1	5	16-Apr-18	20-Apr-18	9
S1B2-3E160	VDC - Lift Drawing (Comment Period) - Fndn Wall - Event B2	5	20-Apr-18	26-Apr-18	4
S1E2-3E160	VDC - Lift Drawing (Comment Period) - Fndn Wall - Event E2	5	23-Apr-18	27-Apr-18	7
S1B3-3E160	VDC - Lift Drawing (Comment Period) - Fndn Wall - Event B3	5	26-Apr-18	02-May-18	5
S1E3-3E160	VDC - Lift Drawing (Comment Period) - Fndn Wall - Event E3	5	30-Apr-18	04-May-18	7
S1B4-3E130	VDC - Lift Drawing (Comment Period) - Fndn Wall - Event B4	5	02-May-18	08-May-18	12
S1E4-3E130	VDC - Lift Drawing (Comment Period) - Fndn Wall - Event E4	5	04-May-18	10-May-18	11
S1B5-3E130	VDC - Lift Drawing (Comment Period) - Fndn Wall - Event B5	5	08-May-18	14-May-18	11
S1E5-3E130	VDC - Lift Drawing (Comment Period) - Fndn Wall - Event E5	5	10-May-18	16-May-18	10
S1B6-3E80	VDC - Lift Drawing (Comment Period) - Fndn Wall - Event B6	5	14-May-18	18-May-18	16
S1E6-3E80	VDC - Lift Drawing (Comment Period) - Fndn Wall - Event E6	5	16-May-18	22-May-18	15
S1B7-3E60	VDC - Lift Drawing (Comment Period) - Fndn Wall - Event B7	5	18-May-18	24-May-18	17
S1E7-3E60	VDC - Lift Drawing (Comment Period) - Fndn Wall - Event E7	5	22-May-18	29-May-18	16
S1B8-3E60	VDC - Lift Drawing (Comment Period) - Fndn Wall - Event B8	5	24-May-18	31-May-18	16
S1E8-3E60	VDC - Lift Drawing (Comment Period) - Fndn Wall - Event E8	5	29-May-18	04-Jun-18	15
S1C1-3E160	VDC - Lift Drawing (Comment Period) - Fndn Wall - Event C1	5	31-May-18	06-Jun-18	17
S1D1-3E160	VDC - Lift Drawing (Comment Period) - Fndn Wall - Event D1	5	04-Jun-18	08-Jun-18	19
S1C2-3E140	VDC - Lift Drawing (Comment Period) - Fndn Wall - Event C2	5	06-Jun-18	12-Jun-18	18
S1D2-3E160	VDC - Lift Drawing (Comment Period) - Fndn Wall - Event D2	5	08-Jun-18	14-Jun-18	20
S1C3-3E100	VDC - Lift Drawing (Comment Period) - Fndn Wall - Event C3	5	12-Jun-18	18-Jun-18	17
S1D3-3E100	VDC - Lift Drawing (Comment Period) - Fndn Wall - Event D3	5	14-Jun-18	20-Jun-18	19
S1C4-3E80	VDC - Lift Drawing (Comment Period) - Fndn Wall - Event C4	5	18-Jun-18	22-Jun-18	58
S1D4-3E80	VDC - Lift Drawing (Comment Period) - Fndn Wall - Event D4	5	20-Jun-18	26-Jun-18	54
S1C5-3E60	VDC - Lift Drawing (Comment Period) - Fndn Wall - Event C5	5	22-Jun-18	28-Jun-18	57
S1D5-3E60	VDC - Lift Drawing (Comment Period) - Fndn Wall - Event D5	5	26-Jun-18	02-Jul-18	53
S1C6-3E60	VDC - Lift Drawing (Comment Period) - Fndn Wall - Event C6	5	28-Jun-18	05-Jul-18	58
S1D6-3E60	VDC - Lift Drawing (Comment Period) - Fndn Wall - Event D6	5	02-Jul-18	09-Jul-18	54
S1C7-3E60	VDC - Lift Drawing (Comment Period) - Fndn Wall - Event C7	5	05-Jul-18	11-Jul-18	57
S1D7-3E60	VDC - Lift Drawing (Comment Period) - Fndn Wall - Event D7	5	09-Jul-18	13-Jul-18	53
S1A1-3E170	VDC - Lift Drawing (Finalize) - Fndn Wall - Event A1	5	19-Mar-18	23-Mar-18	6
S1F1-3E170	VDC - Lift Drawing (Finalize) - Fndn Wall - Event F1	5	19-Mar-18	23-Mar-18	8
S1A2-3E170	VDC - Lift Drawing (Finalize) - Fndn Wall - Event A2	5	26-Mar-18	30-Mar-18	4
S1F2-3E170	VDC - Lift Drawing (Finalize) - Fndn Wall - Event F2	5	26-Mar-18	30-Mar-18	6
S1A3-3E110	VDC - Lift Drawing (Finalize) - Fndn Wall - Event A3	5	02-Apr-18	06-Apr-18	7
S1F3-3E110	VDC - Lift Drawing (Finalize) - Fndn Wall - Event F3	5	02-Apr-18	06-Apr-18	8
S1A4-3E90	VDC - Lift Drawing (Finalize) - Fndn Wall - Event A4	5	09-Apr-18	13-Apr-18	7
S1F4-3E90	VDC - Lift Drawing (Finalize) - Fndn Wall - Event F4	5	09-Apr-18	13-Apr-18	6
S1A5-3E70	VDC - Lift Drawing (Finalize) - Fndn Wall - Event A5	5	16-Apr-18	20-Apr-18	5
S1F5-3E70	VDC - Lift Drawing (Finalize) - Fndn Wall - Event F5	5	16-Apr-18	20-Apr-18	9
S1B1-3E170	VDC - Lift Drawing (Finalize) - Fndn Wall - Event B1	5	23-Apr-18	27-Apr-18	5
S1E1-3E170	VDC - Lift Drawing (Finalize) - Fndn Wall - Event E1	5	23-Apr-18	27-Apr-18	9
S1B2-3E170	VDC - Lift Drawing (Finalize) - Fndn Wall - Event B2	5	27-Apr-18	03-May-18	4
S1E2-3E170	VDC - Lift Drawing (Finalize) - Fndn Wall - Event E2	5	30-Apr-18	04-May-18	7
S1B3-3E170	VDC - Lift Drawing (Finalize) - Fndn Wall - Event B3	5	03-May-18	09-May-18	5
S1E3-3E170	VDC - Lift Drawing (Finalize) - Fndn Wall - Event E3	5	07-May-18	11-May-18	7
S1B4-3E140	VDC - Lift Drawing (Finalize) - Fndn Wall - Event B4	5	09-May-18	15-May-18	12
S1E4-3E140	VDC - Lift Drawing (Finalize) - Fndn Wall - Event E4	5	11-May-18	17-May-18	11
S1B5-3E140	VDC - Lift Drawing (Finalize) - Fndn Wall - Event B5	5	15-May-18	21-May-18	11
S1E5-3E140	VDC - Lift Drawing (Finalize) - Fndn Wall - Event E5	5	17-May-18	23-May-18	10
S1B6-3E90	VDC - Lift Drawing (Finalize) - Fndn Wall - Event B6	5	21-May-18	25-May-18	16
S1E6-3E90	VDC - Lift Drawing (Finalize) - Fndn Wall - Event E6	5	23-May-18	30-May-18	15
S1B7-3E70	VDC - Lift Drawing (Finalize) - Fndn Wall - Event B7	5	25-May-18	01-Jun-18	17
S1E7-3E70	VDC - Lift Drawing (Finalize) - Fndn Wall - Event E7	5	30-May-18	05-Jun-18	16
S1B8-3E70	VDC - Lift Drawing (Finalize) - Fndn Wall - Event B8	5	01-Jun-18	07-Jun-18	16
S1E8-3E70	VDC - Lift Drawing (Finalize) - Fndn Wall - Event E8	5	05-Jun-18	11-Jun-18	15
S1C1-3E170	VDC - Lift Drawing (Finalize) - Fndn Wall - Event C1	5	07-Jun-18	13-Jun-18	17
S1D1-3E170	VDC - Lift Drawing (Finalize) - Fndn Wall - Event D1	5	11-Jun-18	15-Jun-18	19
S1C2-3E150	VDC - Lift Drawing (Finalize) - Fndn Wall - Event C2	5	13-Jun-18	19-Jun-18	18
S1D2-3E170	VDC - Lift Drawing (Finalize) - Fndn Wall - Event D2	5	15-Jun-18	21-Jun-18	20
S1C3-3E110	VDC - Lift Drawing (Finalize) - Fndn Wall - Event C3	5	19-Jun-18	25-Jun-18	17

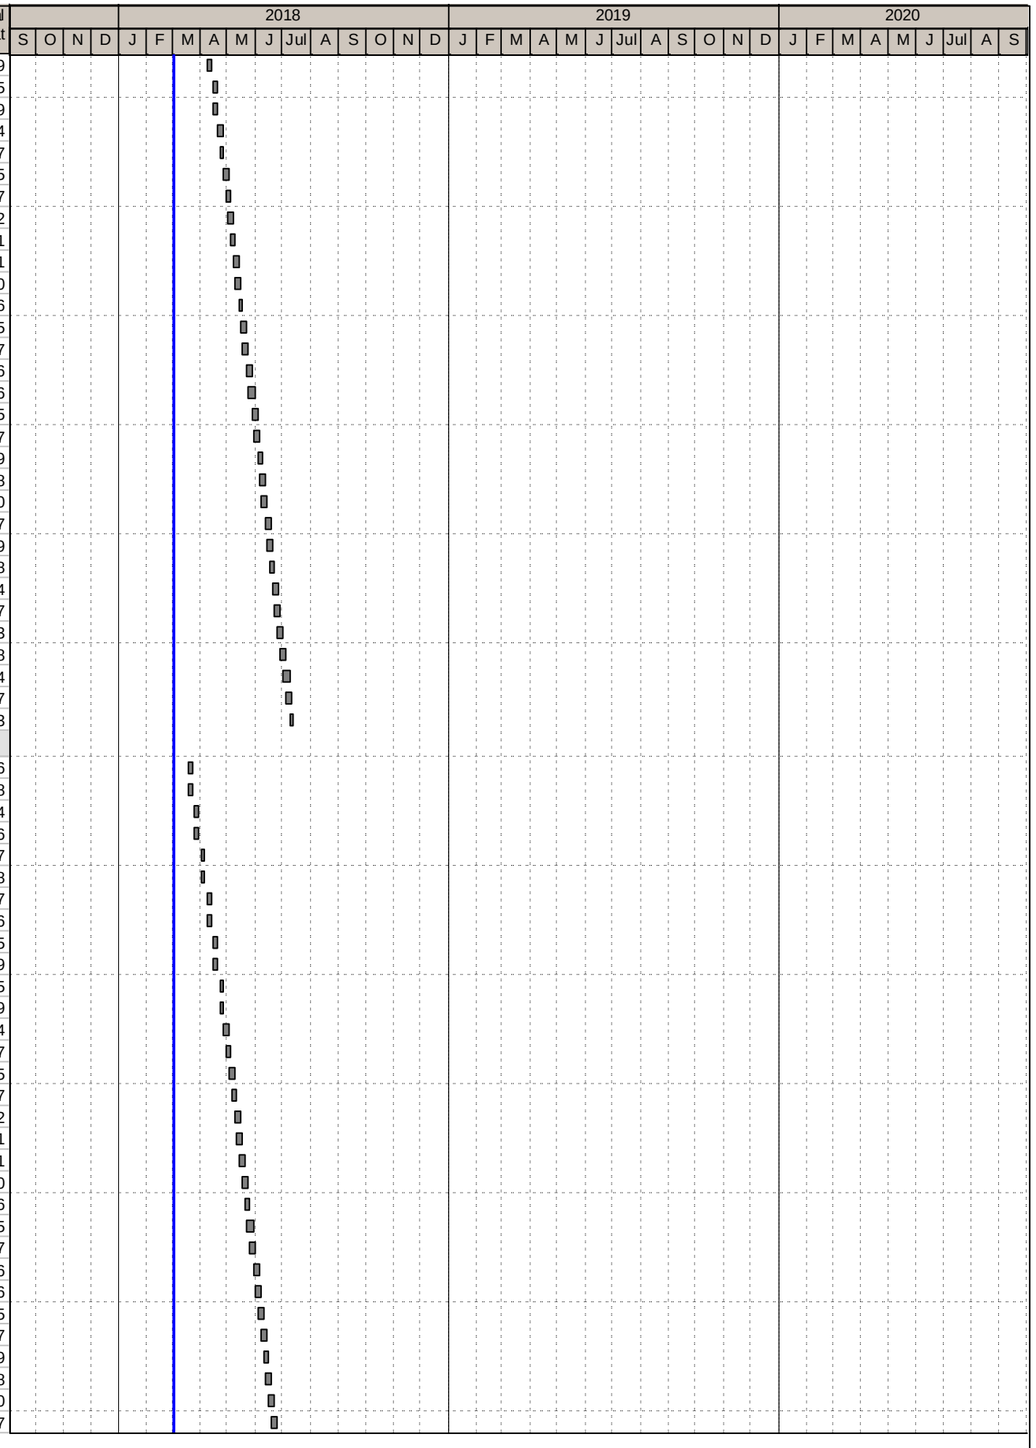

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S1D3-3E110	VDC - Lift Drawing (Finalize) - Fndn Wall - Event D3	5	21-Jun-18	27-Jun-18	19
S1C4-3E90	VDC - Lift Drawing (Finalize) - Fndn Wall - Event C4	5	25-Jun-18	29-Jun-18	58
S1D4-3E90	VDC - Lift Drawing (Finalize) - Fndn Wall - Event D4	5	27-Jun-18	03-Jul-18	54
S1C5-3E70	VDC - Lift Drawing (Finalize) - Fndn Wall - Event C5	5	29-Jun-18	06-Jul-18	57
S1D5-3E70	VDC - Lift Drawing (Finalize) - Fndn Wall - Event D5	5	03-Jul-18	10-Jul-18	53
S1C6-3E70	VDC - Lift Drawing (Finalize) - Fndn Wall - Event C6	5	06-Jul-18	12-Jul-18	58
S1D6-3E70	VDC - Lift Drawing (Finalize) - Fndn Wall - Event D6	5	10-Jul-18	16-Jul-18	54
S1C7-3E70	VDC - Lift Drawing (Finalize) - Fndn Wall - Event C7	5	12-Jul-18	18-Jul-18	57
S1D7-3E70	VDC - Lift Drawing (Finalize) - Fndn Wall - Event D7	5	16-Jul-18	20-Jul-18	53
VDC - 000 Event Level - Concrete Core Coordination					
S1AC5-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Event to Lower Mezz Core #3	10	12-Feb-18 A	23-Feb-18 A	
S1FC4-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Event to Lower Mezz Core #2	10	05-Mar-18	16-Mar-18	13
S1BC6-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Event to Lower Mezz Core #4	10	12-Mar-18	23-Mar-18	25
S1EC3-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Event to Lower Mezz Core #1	10	19-Mar-18	30-Mar-18	24
S1BC7-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Event to Lower Mezz Core #5	10	26-Mar-18	06-Apr-18	38
S1EC2-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Event to Lower Mezz Core #8	10	02-Apr-18	13-Apr-18	37
S1CC8-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Event to Lower Mezz Core #6	10	09-Apr-18	20-Apr-18	57
S1DC1-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Event to Lower Mezz Core #7	10	16-Apr-18	27-Apr-18	57
S1AC5-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Event to Lower Mezz Core #3	5	02-Mar-18 A	08-Mar-18	23
S1FC4-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Event to Lower Mezz Core #2	5	19-Mar-18	23-Mar-18	13
S1BC6-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Event to Lower Mezz Core #4	5	26-Mar-18	30-Mar-18	25
S1EC3-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Event to Lower Mezz Core #1	5	02-Apr-18	06-Apr-18	24
S1BC7-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Event to Lower Mezz Core #5	5	09-Apr-18	13-Apr-18	38
S1EC2-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Event to Lower Mezz Core #8	5	16-Apr-18	20-Apr-18	37
S1CC8-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Event to Lower Mezz Core #6	5	23-Apr-18	27-Apr-18	57
S1DC1-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Event to Lower Mezz Core #7	5	30-Apr-18	04-May-18	57
S1AC5-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Event to Lower Mezz Core #3	5	09-Mar-18	15-Mar-18	23
S1FC4-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Event to Lower Mezz Core #2	5	26-Mar-18	30-Mar-18	13
S1BC6-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Event to Lower Mezz Core #4	5	02-Apr-18	06-Apr-18	25
S1EC3-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Event to Lower Mezz Core #1	5	09-Apr-18	13-Apr-18	24
S1BC7-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Event to Lower Mezz Core #5	5	16-Apr-18	20-Apr-18	38
S1EC2-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Event to Lower Mezz Core #8	5	23-Apr-18	27-Apr-18	37
S1CC8-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Event to Lower Mezz Core #6	5	30-Apr-18	04-May-18	57
S1DC1-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Event to Lower Mezz Core #7	5	07-May-18	11-May-18	57
VDC - 000 Event Level - Concrete Column Coordination					
S1A1-3E90	VDC - Lift Drawing (Prepare Draft) - Columns - Event A1	10	19-Feb-18 A	02-Mar-18 A	
S1F1-3E90	VDC - Lift Drawing (Prepare Draft) - Columns - Event F1	10	19-Feb-18 A	02-Mar-18 A	
S1A2-3E90	VDC - Lift Drawing (Prepare Draft) - Columns - Event A2	10	26-Feb-18 A	09-Mar-18	17
S1F2-3E90	VDC - Lift Drawing (Prepare Draft) - Columns - Event F2	10	26-Feb-18 A	09-Mar-18	18
S1B1-3E90	VDC - Lift Drawing (Prepare Draft) - Columns - Event B1	10	12-Mar-18	23-Mar-18	17
S1E1-3E90	VDC - Lift Drawing (Prepare Draft) - Columns - Event E1	10	12-Mar-18	23-Mar-18	22
S1B2-3E90	VDC - Lift Drawing (Prepare Draft) - Columns - Event B2	10	19-Mar-18	30-Mar-18	29
S1E2-3E90	VDC - Lift Drawing (Prepare Draft) - Columns - Event E2	10	19-Mar-18	30-Mar-18	34
S1B3-3E90	VDC - Lift Drawing (Prepare Draft) - Columns - Event B3	10	26-Mar-18	06-Apr-18	45
S1E3-3E90	VDC - Lift Drawing (Prepare Draft) - Columns - Event E3	10	26-Mar-18	06-Apr-18	37
S1C1-3E90	VDC - Lift Drawing (Prepare Draft) - Columns - Event C1	10	09-Apr-18	20-Apr-18	48
S1D1-3E90	VDC - Lift Drawing (Prepare Draft) - Columns - Event D1	10	09-Apr-18	20-Apr-18	50
S1C2-3E90	VDC - Lift Drawing (Prepare Draft) - Columns - Event C2	10	16-Apr-18	27-Apr-18	77
S1D2-3E90	VDC - Lift Drawing (Prepare Draft) - Columns - Event D2	10	16-Apr-18	27-Apr-18	82
S1A1-3E180	VDC - Lift Drawing (Comment Period) - Columns - Event A1	5	05-Mar-18	09-Mar-18	10
S1F1-3E180	VDC - Lift Drawing (Comment Period) - Columns - Event F1	5	05-Mar-18	09-Mar-18	11
S1A2-3E180	VDC - Lift Drawing (Comment Period) - Columns - Event A2	5	12-Mar-18	16-Mar-18	17
S1F2-3E180	VDC - Lift Drawing (Comment Period) - Columns - Event F2	5	12-Mar-18	16-Mar-18	18
S1B1-3E180	VDC - Lift Drawing (Comment Period) - Columns - Event B1	5	26-Mar-18	30-Mar-18	17
S1E1-3E180	VDC - Lift Drawing (Comment Period) - Columns - Event E1	5	26-Mar-18	30-Mar-18	22
S1B2-3E180	VDC - Lift Drawing (Comment Period) - Columns - Event B2	5	02-Apr-18	06-Apr-18	29
S1E2-3E180	VDC - Lift Drawing (Comment Period) - Columns - Event E2	5	02-Apr-18	06-Apr-18	34

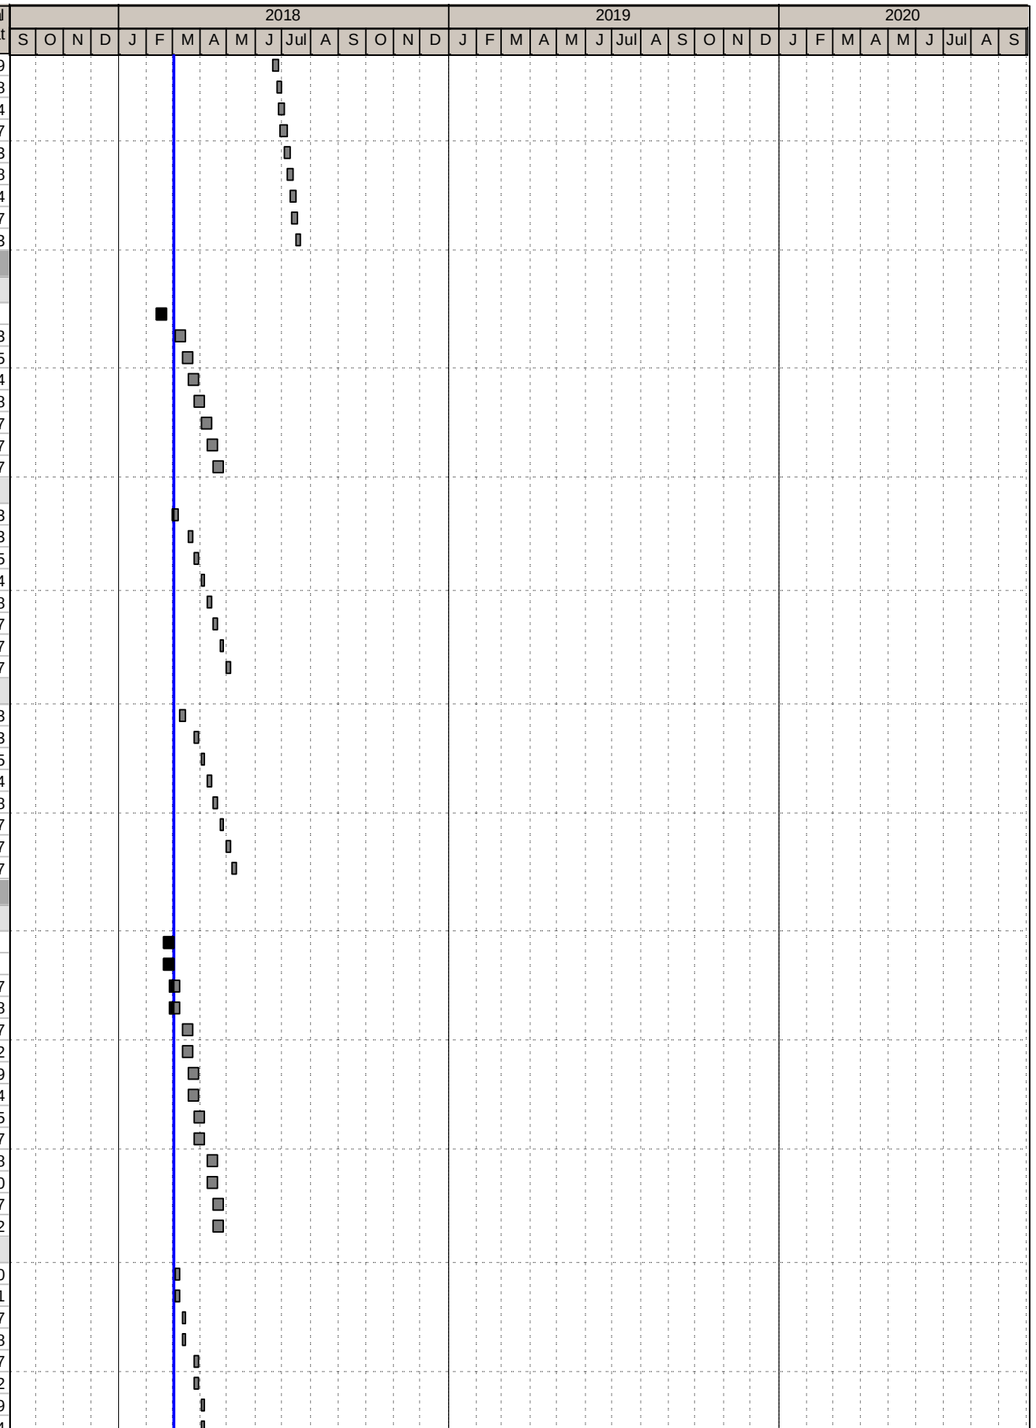

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S1B3-3E180	VDC - Lift Drawing (Comment Period) - Columns - Event B3	5	09-Apr-18	13-Apr-18	45
S1E3-3E180	VDC - Lift Drawing (Comment Period) - Columns - Event E3	5	09-Apr-18	13-Apr-18	37
S1C1-3E180	VDC - Lift Drawing (Comment Period) - Columns - Event C1	5	23-Apr-18	27-Apr-18	48
S1D1-3E180	VDC - Lift Drawing (Comment Period) - Columns - Event D1	5	23-Apr-18	27-Apr-18	50
S1C2-3E160	VDC - Lift Drawing (Comment Period) - Columns - Event C2	5	30-Apr-18	04-May-18	77
S1D2-3E180	VDC - Lift Drawing (Comment Period) - Columns - Event D2	5	30-Apr-18	04-May-18	82
S1A1-3E190	VDC - Lift Drawing (Finalize) - Columns - Event A1	5	12-Mar-18	16-Mar-18	10
S1F1-3E190	VDC - Lift Drawing (Finalize) - Columns - Event F1	5	12-Mar-18	16-Mar-18	11
S1A2-3E190	VDC - Lift Drawing (Finalize) - Columns - Event A2	5	19-Mar-18	23-Mar-18	17
S1F2-3E190	VDC - Lift Drawing (Finalize) - Columns - Event F2	5	19-Mar-18	23-Mar-18	18
S1B1-3E190	VDC - Lift Drawing (Finalize) - Columns - Event B1	5	02-Apr-18	06-Apr-18	17
S1E1-3E190	VDC - Lift Drawing (Finalize) - Columns - Event E1	5	02-Apr-18	06-Apr-18	22
S1B2-3E190	VDC - Lift Drawing (Finalize) - Columns - Event B2	5	09-Apr-18	13-Apr-18	29
S1E2-3E190	VDC - Lift Drawing (Finalize) - Columns - Event E2	5	09-Apr-18	13-Apr-18	34
S1B3-3E190	VDC - Lift Drawing (Finalize) - Columns - Event B3	5	16-Apr-18	20-Apr-18	45
S1E3-3E190	VDC - Lift Drawing (Finalize) - Columns - Event E3	5	16-Apr-18	20-Apr-18	37
S1C1-3E190	VDC - Lift Drawing (Finalize) - Columns - Event C1	5	30-Apr-18	04-May-18	48
S1D1-3E190	VDC - Lift Drawing (Finalize) - Columns - Event D1	5	30-Apr-18	04-May-18	50
S1C2-3E170	VDC - Lift Drawing (Finalize) - Columns - Event C2	5	07-May-18	11-May-18	77
S1D2-3E190	VDC - Lift Drawing (Finalize) - Columns - Event D2	5	07-May-18	11-May-18	82
VDC - 000 Event Level - Slab on Grade Coordination					
S1A0-3E70	VDC - Lift Drawing (Prepare Draft) - Slab On Grade - Event A	10	22-Jun-18	06-Jul-18	35
S1F0-3E70	VDC - Lift Drawing (Prepare Draft) - Slab On Grade - Event F	10	22-Jun-18	06-Jul-18	55
S1E0-3E70	VDC - Lift Drawing (Prepare Draft) - Slab On Grade - Event E	10	09-Jul-18	20-Jul-18	86
S1B0-3E70	VDC - Lift Drawing (Prepare Draft) - Slab On Grade - Event B	10	09-Jul-18	20-Jul-18	55
S1D0-3E70	VDC - Lift Drawing (Prepare Draft) - Slab On Grade - Event D	10	23-Jul-18	03-Aug-18	137
S1C0-3E70	VDC - Lift Drawing (Prepare Draft) - Slab On Grade - Event C	10	23-Jul-18	03-Aug-18	106
S1L1-3E70	VDC - Lift Drawing (Prepare Draft) - Slab On Grade/Field Rail Install - Exterior Field Tray	10	20-Aug-18	31-Aug-18	217
S1L5-3E70	VDC - Lift Drawing (Prepare Draft) - Slab On Grade - Inner Bowl A/F	10	04-Sep-18	17-Sep-18	217
S1L3-3E70	VDC - Lift Drawing (Prepare Draft) - Slab On Grade - Inner Bowl	10	18-Sep-18	01-Oct-18	232
S1L4-3E70	VDC - Lift Drawing (Prepare Draft) - Slab On Grade/Field Rail Install - Interior Field Tray	10	02-Oct-18	15-Oct-18	258
S1L2-3E70	VDC - Lift Drawing (Prepare Draft) - Slab On Grade/Field Rail Install - Under Structure C/D	10	16-Oct-18	29-Oct-18	289
S1A0-3E100	VDC - Lift Drawing (Comment Period) - Slab On Grade - Event A	5	09-Jul-18	13-Jul-18	35
S1F0-3E100	VDC - Lift Drawing (Comment Period) - Slab On Grade - Event F	5	09-Jul-18	13-Jul-18	55
S1E0-3E100	VDC - Lift Drawing (Comment Period) - Slab On Grade - Event E	5	23-Jul-18	27-Jul-18	86
S1B0-3E100	VDC - Lift Drawing (Comment Period) - Slab On Grade - Event B	5	23-Jul-18	27-Jul-18	55
S1D0-3E100	VDC - Lift Drawing (Comment Period) - Slab On Grade - Event D	5	06-Aug-18	10-Aug-18	137
S1C0-3E100	VDC - Lift Drawing (Comment Period) - Slab On Grade - Event C	5	06-Aug-18	10-Aug-18	106
S1L1-3E80	VDC - Lift Drawing (Comment Period) - Slab On Grade/Field Rail Install - Exterior Field Tray	5	04-Sep-18	10-Sep-18	222
S1L5-3E80	VDC - Lift Drawing (Comment Period) - Slab On Grade - Inner Bowl A/F	5	18-Sep-18	24-Sep-18	217
S1L3-3E80	VDC - Lift Drawing (Comment Period) - Slab On Grade - Inner Bowl	5	02-Oct-18	08-Oct-18	232
S1L4-3E80	VDC - Lift Drawing (Comment Period) - Slab On Grade/Field Rail Install - Interior Field Tray	5	16-Oct-18	22-Oct-18	258
S1L2-3E80	VDC - Lift Drawing (Comment Period) - Slab On Grade/Field Rail Install - Under Structure C/D	5	30-Oct-18	05-Nov-18	289
S1A0-3E110	VDC - Lift Drawing (Finalize) - Slab On Grade - Event A	5	16-Jul-18	20-Jul-18	35
S1F0-3E110	VDC - Lift Drawing (Finalize) - Slab On Grade - Event F	5	16-Jul-18	20-Jul-18	55
S1E0-3E110	VDC - Lift Drawing (Finalize) - Slab On Grade - Event E	5	30-Jul-18	03-Aug-18	86
S1B0-3E110	VDC - Lift Drawing (Finalize) - Slab On Grade - Event B	5	30-Jul-18	03-Aug-18	55
S1D0-3E110	VDC - Lift Drawing (Finalize) - Slab On Grade - Event D	5	13-Aug-18	17-Aug-18	137
S1C0-3E110	VDC - Lift Drawing (Finalize) - Slab On Grade - Event C	5	13-Aug-18	17-Aug-18	106
S1L1-3E90	VDC - Lift Drawing (Finalize) - Slab On Grade/Field Rail Install - Exterior Field Tray	5	11-Sep-18	17-Sep-18	222
S1L5-3E90	VDC - Lift Drawing (Finalize) - Slab On Grade - Inner Bowl A/F	5	25-Sep-18	01-Oct-18	217
S1L3-3E90	VDC - Lift Drawing (Finalize) - Slab On Grade - Inner Bowl	5	09-Oct-18	15-Oct-18	232
S1L4-3E90	VDC - Lift Drawing (Finalize) - Slab On Grade/Field Rail Install - Interior Field Tray	5	23-Oct-18	29-Oct-18	258
S1L2-3E90	VDC - Lift Drawing (Finalize) - Slab On Grade/Field Rail Install - Under Structure C/D	5	06-Nov-18	12-Nov-18	289
VDC - 050 Lower Mezz lvl - General Coordination					
S2A60-3E10	VDC - General Coordination (Coordinate) - Quad A Lower Mezz Lvl	15	03-Apr-18	23-Apr-18	14
S2B60-3E10	VDC - General Coordination (Coordinate) - Quad B Lower Mezz Lvl	15	24-Apr-18	14-May-18	14

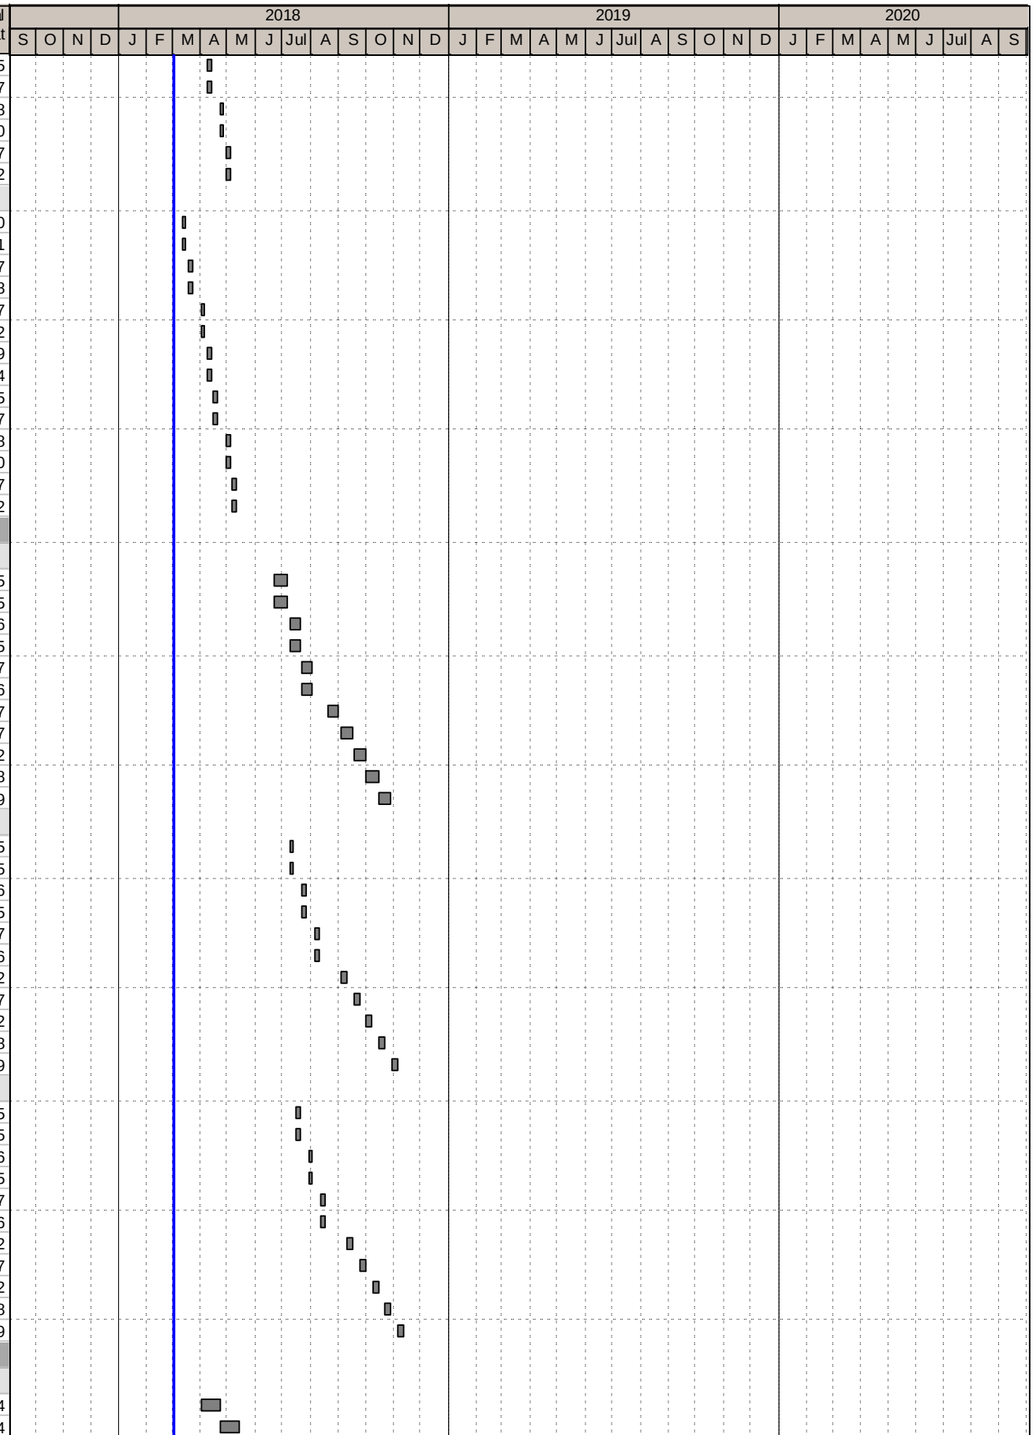

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S2C60-3E10	VDC - General Coordination (Coordinate) - Quad C Lower Mezz Lvl	15	15-May-18	05-Jun-18	36
S2D60-3E10	VDC - General Coordination (Coordinate) - Quad D Lower Mezz Lvl	15	06-Jun-18	26-Jun-18	36
VDC - 050 Lower Mezz Lvl - Structural Deck Coordination					
S2A50-3E10	VDC - Slab Penetrations / Embedded Conduit (Coordinate) - Area A Lower Mezz Lvl	10	05-Feb-18 A	16-Feb-18 A	
S2F50-3E62	VDC - Slab Penetrations / Embedded Conduit (Coordinate) - Area F Lower Mezz Lvl	10	05-Feb-18 A	16-Feb-18 A	
S2B50-3E42	VDC - Slab Penetrations / Embedded Conduit (Coordinate) - Area B Lower Mezz Lvl (Rebar Support)	15	19-Feb-18 A	09-Mar-18	34
S2E50-3E72	VDC - Slab Penetrations / Embedded Conduit (Coordinate) - Area E Lower Mezz Lvl (Rebar Support)	15	19-Feb-18 A	09-Mar-18	39
S2C50-3E52	VDC - Slab Penetrations / Embedded Conduit (Coordinate) - Area C Lower Mezz Lvl (Rebar Support)	15	12-Mar-18	30-Mar-18	66
S2D50-3E82	VDC - Slab Penetrations / Embedded Conduit (Coordinate) - Area D Lower Mezz Lvl (Rebar Support)	15	12-Mar-18	30-Mar-18	71
S2A1-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Lower Mezz A1	10	08-Mar-18	21-Mar-18	17
S2F1-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Lower Mezz F1	10	08-Mar-18	21-Mar-18	18
S2A2-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Lower Mezz A2	10	15-Mar-18	28-Mar-18	22
S2F2-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Lower Mezz F2	10	15-Mar-18	28-Mar-18	24
S2A3-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Lower Mezz A3	10	22-Mar-18	04-Apr-18	24
S2F3-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Lower Mezz F3	10	22-Mar-18	04-Apr-18	27
S2B1-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Lower Mezz B1	10	29-Mar-18	11-Apr-18	24
S2E1-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Lower Mezz E1	10	29-Mar-18	11-Apr-18	27
S2B2-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Lower Mezz B2	10	05-Apr-18	18-Apr-18	24
S2E2-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Lower Mezz E2	10	05-Apr-18	18-Apr-18	27
S2B3-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Lower Mezz B3	10	12-Apr-18	25-Apr-18	32
S2E3-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Lower Mezz E3	10	12-Apr-18	25-Apr-18	34
S2B4-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Lower Mezz B4	10	19-Apr-18	02-May-18	36
S2E4-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Lower Mezz E4	10	19-Apr-18	02-May-18	39
S2B5-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Lower Mezz B5	10	26-Apr-18	09-May-18	39
S2E5-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Lower Mezz E5	10	26-Apr-18	09-May-18	39
S2C1-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Lower Mezz C1	10	10-May-18	23-May-18	40
S2D1-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Lower Mezz D1	10	10-May-18	23-May-18	45
S2C2-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Lower Mezz C2	10	24-May-18	07-Jun-18	40
S2D2-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Lower Mezz D2	10	24-May-18	07-Jun-18	45
S2A1-3E100	VDC - Lift Drawing (Comment Period) - P&J Deck - Lower Mezz A1	5	22-Mar-18	28-Mar-18	17
S2F1-3E100	VDC - Lift Drawing (Comment Period) - P&J Deck - Lower Mezz F1	5	22-Mar-18	28-Mar-18	18
S2A2-3E100	VDC - Lift Drawing (Comment Period) - P&J Deck - Lower Mezz A2	5	29-Mar-18	04-Apr-18	22
S2F2-3E100	VDC - Lift Drawing (Comment Period) - P&J Deck - Lower Mezz F2	5	29-Mar-18	04-Apr-18	24
S2A3-3E100	VDC - Lift Drawing (Comment Period) - P&J Deck - Lower Mezz A3	5	05-Apr-18	11-Apr-18	26
S2F3-3E100	VDC - Lift Drawing (Comment Period) - P&J Deck - Lower Mezz F3	5	05-Apr-18	11-Apr-18	31
S2B1-3E100	VDC - Lift Drawing (Comment Period) - P&J Deck - Lower Mezz B1	5	12-Apr-18	18-Apr-18	25
S2E1-3E100	VDC - Lift Drawing (Comment Period) - P&J Deck - Lower Mezz E1	5	12-Apr-18	18-Apr-18	29
S2B2-3E100	VDC - Lift Drawing (Comment Period) - P&J Deck - Lower Mezz B2	5	19-Apr-18	25-Apr-18	24
S2E2-3E100	VDC - Lift Drawing (Comment Period) - P&J Deck - Lower Mezz E2	5	19-Apr-18	25-Apr-18	27
S2B3-3E100	VDC - Lift Drawing (Comment Period) - P&J Deck - Lower Mezz B3	5	26-Apr-18	02-May-18	32
S2E3-3E100	VDC - Lift Drawing (Comment Period) - P&J Deck - Lower Mezz E3	5	26-Apr-18	02-May-18	34
S2B4-3E100	VDC - Lift Drawing (Comment Period) - P&J Deck - Lower Mezz B4	5	03-May-18	09-May-18	36
S2E4-3E100	VDC - Lift Drawing (Comment Period) - P&J Deck - Lower Mezz E4	5	03-May-18	09-May-18	40
S2B5-3E100	VDC - Lift Drawing (Comment Period) - P&J Deck - Lower Mezz B5	5	10-May-18	16-May-18	39
S2E5-3E100	VDC - Lift Drawing (Comment Period) - P&J Deck - Lower Mezz E5	5	10-May-18	16-May-18	39
S2C1-3E100	VDC - Lift Drawing (Comment Period) - P&J Deck - Lower Mezz C1	5	24-May-18	31-May-18	42
S2D1-3E100	VDC - Lift Drawing (Comment Period) - P&J Deck - Lower Mezz D1	5	24-May-18	31-May-18	46
S2C2-3E100	VDC - Lift Drawing (Comment Period) - P&J Deck - Lower Mezz C2	5	08-Jun-18	14-Jun-18	40
S2D2-3E100	VDC - Lift Drawing (Comment Period) - P&J Deck - Lower Mezz D2	5	08-Jun-18	14-Jun-18	45
S2A1-3E110	VDC - Lift Drawing (Finalize) - P&J Deck - Lower Mezz A1	5	29-Mar-18	04-Apr-18	17
S2F1-3E110	VDC - Lift Drawing (Finalize) - P&J Deck - Lower Mezz F1	5	29-Mar-18	04-Apr-18	18
S2A2-3E110	VDC - Lift Drawing (Finalize) - P&J Deck - Lower Mezz A2	5	05-Apr-18	11-Apr-18	22
S2F2-3E110	VDC - Lift Drawing (Finalize) - P&J Deck - Lower Mezz F2	5	05-Apr-18	11-Apr-18	24
S2A3-3E110	VDC - Lift Drawing (Finalize) - P&J Deck - Lower Mezz A3	5	12-Apr-18	18-Apr-18	26
S2F3-3E110	VDC - Lift Drawing (Finalize) - P&J Deck - Lower Mezz F3	5	12-Apr-18	18-Apr-18	31
S2B1-3E110	VDC - Lift Drawing (Finalize) - P&J Deck - Lower Mezz B1	5	19-Apr-18	25-Apr-18	25
S2E1-3E110	VDC - Lift Drawing (Finalize) - P&J Deck - Lower Mezz E1	5	19-Apr-18	25-Apr-18	29
S2B2-3E110	VDC - Lift Drawing (Finalize) - P&J Deck - Lower Mezz B2	5	26-Apr-18	02-May-18	24
S2E2-3E110	VDC - Lift Drawing (Finalize) - P&J Deck - Lower Mezz E2	5	26-Apr-18	02-May-18	27

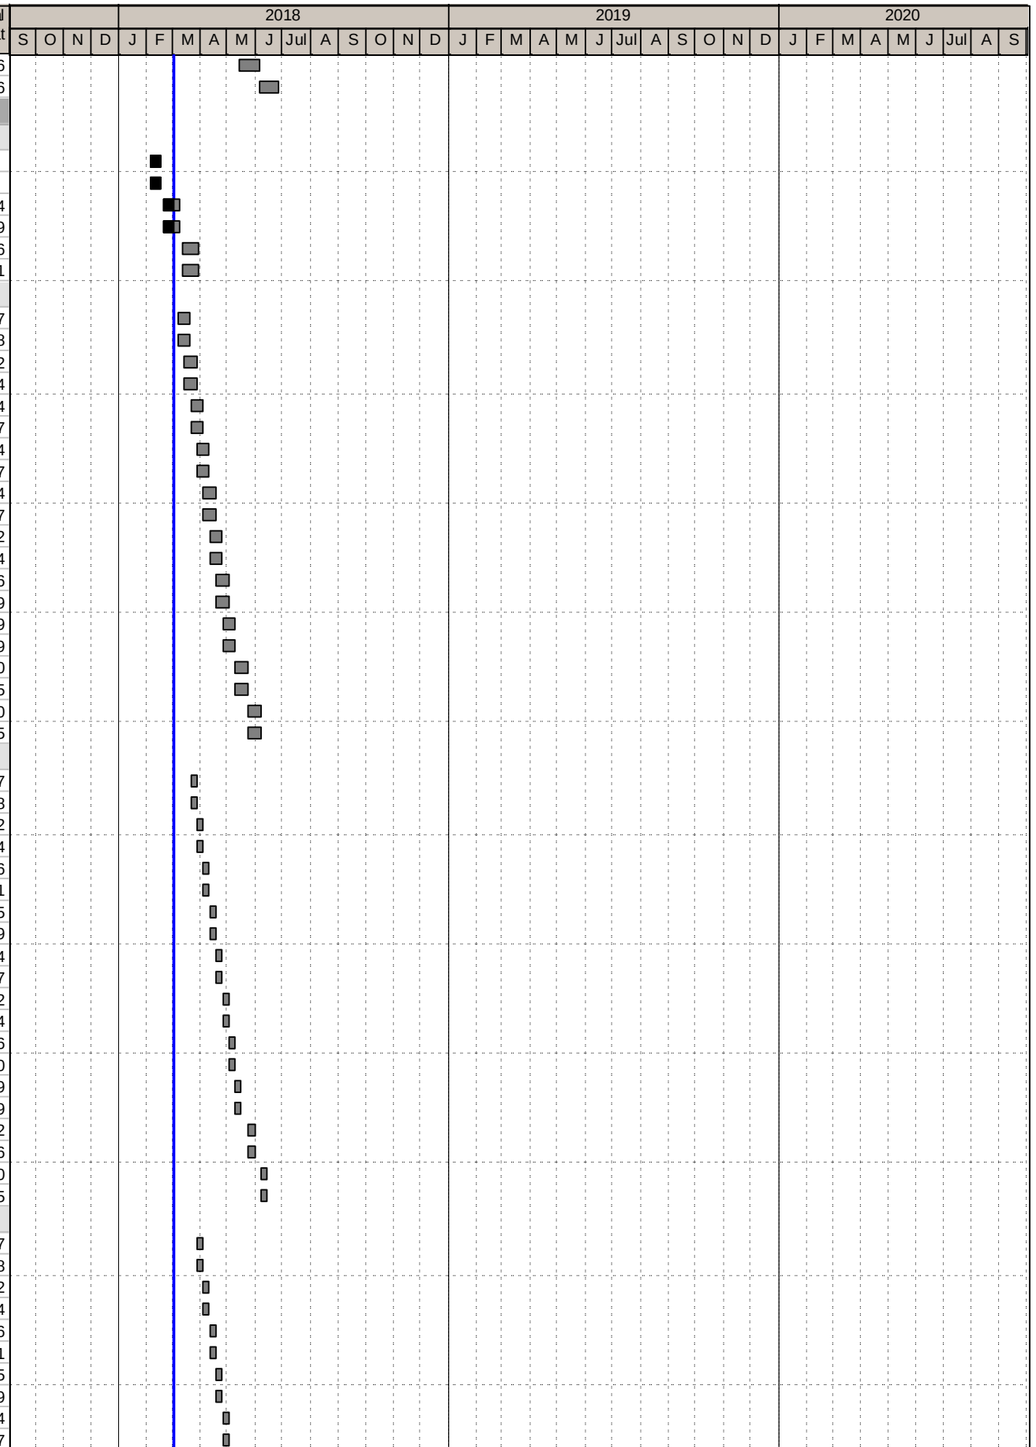

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S2B3-3E110	VDC - Lift Drawing (Finalize) - P&J Deck - Lower Mezz B3	5	03-May-18	09-May-18	32
S2E3-3E110	VDC - Lift Drawing (Finalize) - P&J Deck - Lower Mezz E3	5	03-May-18	09-May-18	34
S2B4-3E110	VDC - Lift Drawing (Finalize) - P&J Deck - Lower Mezz B4	5	10-May-18	16-May-18	36
S2E4-3E110	VDC - Lift Drawing (Finalize) - P&J Deck - Lower Mezz E4	5	10-May-18	16-May-18	40
S2B5-3E110	VDC - Lift Drawing (Finalize) - P&J Deck - Lower Mezz B5	5	17-May-18	23-May-18	39
S2E5-3E110	VDC - Lift Drawing (Finalize) - P&J Deck - Lower Mezz E5	5	17-May-18	23-May-18	39
S2C1-3E110	VDC - Lift Drawing (Finalize) - P&J Deck - Lower Mezz C1	5	01-Jun-18	07-Jun-18	42
S2D1-3E110	VDC - Lift Drawing (Finalize) - P&J Deck - Lower Mezz D1	5	01-Jun-18	07-Jun-18	46
S2C2-3E110	VDC - Lift Drawing (Finalize) - P&J Deck - Lower Mezz C2	5	15-Jun-18	21-Jun-18	40
S2D2-3E110	VDC - Lift Drawing (Finalize) - P&J Deck - Lower Mezz D2	5	15-Jun-18	21-Jun-18	45
VDC - 050 Lower Mezz lvl - Concrete Column Coordination					
S2A1-3E90	VDC - Lift Drawing (Prepare Draft) - Columns - Lower Mezz A1	10	27-Mar-18	09-Apr-18	15
S2F1-3E90	VDC - Lift Drawing (Prepare Draft) - Columns - Lower Mezz F1	10	27-Mar-18	09-Apr-18	15
S2A2-3E90	VDC - Lift Drawing (Prepare Draft) - Columns - Lower Mezz A2	10	03-Apr-18	16-Apr-18	19
S2F2-3E90	VDC - Lift Drawing (Prepare Draft) - Columns - Lower Mezz F2	10	03-Apr-18	16-Apr-18	21
S2A3-3E90	VDC - Lift Drawing (Prepare Draft) - Columns - Lower Mezz A3	10	10-Apr-18	23-Apr-18	25
S2F3-3E90	VDC - Lift Drawing (Prepare Draft) - Columns - Lower Mezz F3	10	10-Apr-18	23-Apr-18	29
S2B1-3E90	VDC - Lift Drawing (Prepare Draft) - Columns - Lower Mezz B1	10	17-Apr-18	30-Apr-18	26
S2E1-3E90	VDC - Lift Drawing (Prepare Draft) - Columns - Lower Mezz E1	10	17-Apr-18	30-Apr-18	30
S2B2-3E90	VDC - Lift Drawing (Prepare Draft) - Columns - Lower Mezz B2	10	24-Apr-18	07-May-18	27
S2E2-3E90	VDC - Lift Drawing (Prepare Draft) - Columns - Lower Mezz E2	10	24-Apr-18	07-May-18	31
S2B3-3E90	VDC - Lift Drawing (Prepare Draft) - Columns - Lower Mezz B3	10	01-May-18	14-May-18	29
S2E3-3E90	VDC - Lift Drawing (Prepare Draft) - Columns - Lower Mezz E3	10	01-May-18	14-May-18	31
S2B4-3E90	VDC - Lift Drawing (Prepare Draft) - Columns - Lower Mezz B4	10	08-May-18	21-May-18	33
S2E4-3E90	VDC - Lift Drawing (Prepare Draft) - Columns - Lower Mezz E4	10	08-May-18	21-May-18	37
S2B5-3E90	VDC - Lift Drawing (Prepare Draft) - Columns - Lower Mezz B5	10	15-May-18	29-May-18	42
S2E5-3E90	VDC - Lift Drawing (Prepare Draft) - Columns - Lower Mezz E5	10	15-May-18	29-May-18	42
S2C1-3E90	VDC - Lift Drawing (Prepare Draft) - Columns - Lower Mezz C1	10	22-May-18	05-Jun-18	45
S2D1-3E90	VDC - Lift Drawing (Prepare Draft) - Columns - Lower Mezz D1	10	22-May-18	05-Jun-18	48
S2C2-3E90	VDC - Lift Drawing (Prepare Draft) - Columns - Lower Mezz C2	10	30-May-18	12-Jun-18	54
S2D2-3E90	VDC - Lift Drawing (Prepare Draft) - Columns - Lower Mezz D2	10	30-May-18	12-Jun-18	58
S2A1-3E120	VDC - Lift Drawing (Comment Period) - Columns - Lower Mezz A1	5	10-Apr-18	16-Apr-18	15
S2F1-3E120	VDC - Lift Drawing (Comment Period) - Columns - Lower Mezz F1	5	10-Apr-18	16-Apr-18	15
S2A2-3E120	VDC - Lift Drawing (Comment Period) - Columns - Lower Mezz A2	5	17-Apr-18	23-Apr-18	19
S2F2-3E120	VDC - Lift Drawing (Comment Period) - Columns - Lower Mezz F2	5	17-Apr-18	23-Apr-18	21
S2A3-3E120	VDC - Lift Drawing (Comment Period) - Columns - Lower Mezz A3	5	24-Apr-18	30-Apr-18	25
S2F3-3E120	VDC - Lift Drawing (Comment Period) - Columns - Lower Mezz F3	5	24-Apr-18	30-Apr-18	29
S2B1-3E120	VDC - Lift Drawing (Comment Period) - Columns - Lower Mezz B1	5	01-May-18	07-May-18	26
S2E1-3E120	VDC - Lift Drawing (Comment Period) - Columns - Lower Mezz E1	5	01-May-18	07-May-18	30
S2B2-3E120	VDC - Lift Drawing (Comment Period) - Columns - Lower Mezz B2	5	08-May-18	14-May-18	27
S2E2-3E120	VDC - Lift Drawing (Comment Period) - Columns - Lower Mezz E2	5	08-May-18	14-May-18	32
S2B3-3E120	VDC - Lift Drawing (Comment Period) - Columns - Lower Mezz B3	5	15-May-18	21-May-18	29
S2E3-3E120	VDC - Lift Drawing (Comment Period) - Columns - Lower Mezz E3	5	15-May-18	21-May-18	31
S2B4-3E120	VDC - Lift Drawing (Comment Period) - Columns - Lower Mezz B4	5	22-May-18	29-May-18	33
S2E4-3E120	VDC - Lift Drawing (Comment Period) - Columns - Lower Mezz E4	5	22-May-18	29-May-18	37
S2B5-3E120	VDC - Lift Drawing (Comment Period) - Columns - Lower Mezz B5	5	30-May-18	05-Jun-18	42
S2E5-3E120	VDC - Lift Drawing (Comment Period) - Columns - Lower Mezz E5	5	30-May-18	05-Jun-18	42
S2C1-3E120	VDC - Lift Drawing (Comment Period) - Columns - Lower Mezz C1	5	06-Jun-18	12-Jun-18	45
S2D1-3E120	VDC - Lift Drawing (Comment Period) - Columns - Lower Mezz D1	5	06-Jun-18	12-Jun-18	48
S2C2-3E120	VDC - Lift Drawing (Comment Period) - Columns - Lower Mezz C2	5	13-Jun-18	19-Jun-18	54
S2D2-3E120	VDC - Lift Drawing (Comment Period) - Columns - Lower Mezz D2	5	13-Jun-18	19-Jun-18	58
S2A1-3E130	VDC - Lift Drawing (Finalize) - Columns - Lower Mezz A1	5	17-Apr-18	23-Apr-18	15
S2F1-3E130	VDC - Lift Drawing (Finalize) - Columns - Lower Mezz F1	5	17-Apr-18	23-Apr-18	15
S2A2-3E130	VDC - Lift Drawing (Finalize) - Columns - Lower Mezz A2	5	24-Apr-18	30-Apr-18	19
S2F2-3E130	VDC - Lift Drawing (Finalize) - Columns - Lower Mezz F2	5	24-Apr-18	30-Apr-18	21
S2A3-3E130	VDC - Lift Drawing (Finalize) - Columns - Lower Mezz A3	5	01-May-18	07-May-18	25
S2F3-3E130	VDC - Lift Drawing (Finalize) - Columns - Lower Mezz F3	5	01-May-18	07-May-18	29
S2B1-3E130	VDC - Lift Drawing (Finalize) - Columns - Lower Mezz B1	5	08-May-18	14-May-18	26
S2E1-3E130	VDC - Lift Drawing (Finalize) - Columns - Lower Mezz E1	5	08-May-18	14-May-18	30
S2B2-3E130	VDC - Lift Drawing (Finalize) - Columns - Lower Mezz B2	5	15-May-18	21-May-18	27

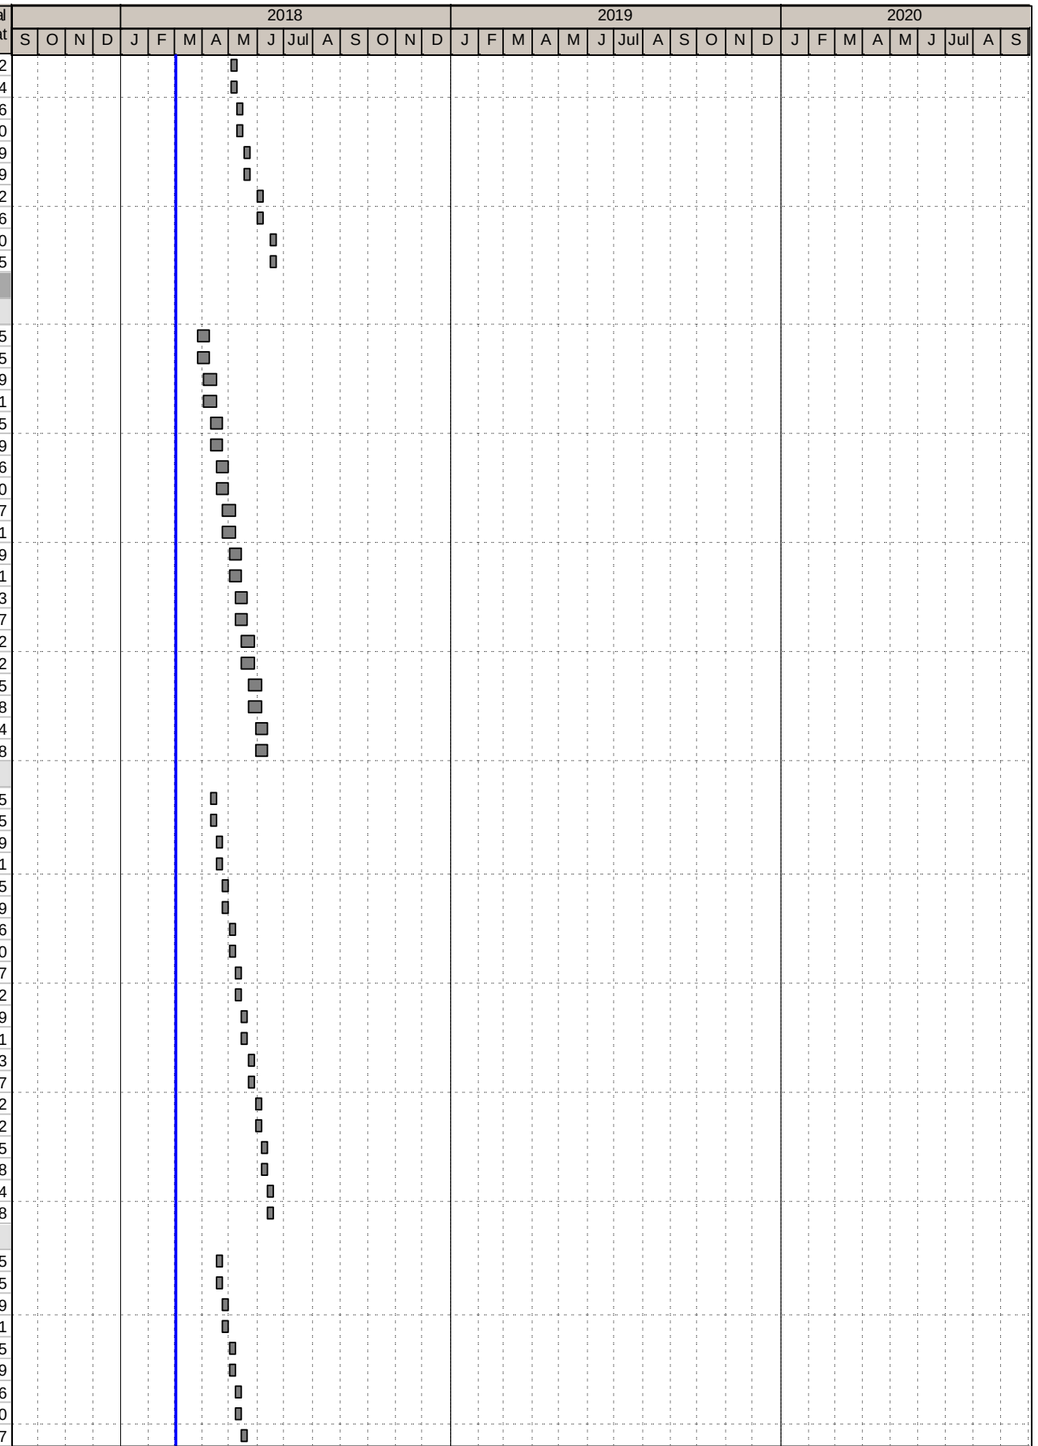

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S2E2-3E130	VDC - Lift Drawing (Finalize) - Columns - Lower Mezz E2	5	15-May-18	21-May-18	32
S2B3-3E130	VDC - Lift Drawing (Finalize) - Columns - Lower Mezz B3	5	22-May-18	29-May-18	29
S2E3-3E130	VDC - Lift Drawing (Finalize) - Columns - Lower Mezz E3	5	22-May-18	29-May-18	31
S2B4-3E130	VDC - Lift Drawing (Finalize) - Columns - Lower Mezz B4	5	30-May-18	05-Jun-18	33
S2E4-3E130	VDC - Lift Drawing (Finalize) - Columns - Lower Mezz E4	5	30-May-18	05-Jun-18	37
S2B5-3E130	VDC - Lift Drawing (Finalize) - Columns - Lower Mezz B5	5	06-Jun-18	12-Jun-18	42
S2E5-3E130	VDC - Lift Drawing (Finalize) - Columns - Lower Mezz E5	5	06-Jun-18	12-Jun-18	42
S2C1-3E130	VDC - Lift Drawing (Finalize) - Columns - Lower Mezz C1	5	13-Jun-18	19-Jun-18	45
S2D1-3E130	VDC - Lift Drawing (Finalize) - Columns - Lower Mezz D1	5	13-Jun-18	19-Jun-18	48
S2C2-3E130	VDC - Lift Drawing (Finalize) - Columns - Lower Mezz C2	5	20-Jun-18	26-Jun-18	54
S2D2-3E130	VDC - Lift Drawing (Finalize) - Columns - Lower Mezz D2	5	20-Jun-18	26-Jun-18	58
VDC - 050 Lower Mezz lvl - Concrete Core Coordination					
S2AC5-8P2B13	VDC - Lift Drawing (Prepare Draft) - Core Walls - Lower Mezz to Main Conc Core #3	10	10-Apr-18	20-Apr-18	18
S2FC4-8P2B13	VDC - Lift Drawing (Prepare Draft) - Core Walls - Lower Mezz to Main Conc Core #2	10	16-Apr-18	26-Apr-18	18
S2BC6-8P2B13	VDC - Lift Drawing (Prepare Draft) - Core Walls - Lower Mezz to Main Conc Core #4	10	27-Apr-18	08-May-18	20
S2EC3-8P2B13	VDC - Lift Drawing (Prepare Draft) - Core Walls - Lower Mezz to Main Conc Core #1	10	09-May-18	19-May-18	20
S2BC7-8P2B13	VDC - Lift Drawing (Prepare Draft) - Core Walls - Lower Mezz to Main Conc Core #5	10	21-May-18	01-Jun-18	33
S2EC2-8P2B13	VDC - Lift Drawing (Prepare Draft) - Core Walls - Lower Mezz to Main Conc Core #8	10	02-Jun-18	13-Jun-18	33
S2CC8-8P2B13	VDC - Lift Drawing (Prepare Draft) - Core Walls - Lower Mezz to Main Conc Core #6	10	14-Jun-18	25-Jun-18	44
S2DC1-8P2B13	VDC - Lift Drawing (Prepare Draft) - Core Walls - Lower Mezz to Main Conc Core #7	10	26-Jun-18	07-Jul-18	44
S2AC5-8P2B23	VDC - Lift Drawing (Comment Period) - Core Walls - Lower Mezz to Main Conc Core #3	5	21-Apr-18	26-Apr-18	20
S2FC4-8P2B23	VDC - Lift Drawing (Comment Period) - Core Walls - Lower Mezz to Main Conc Core #2	5	27-Apr-18	02-May-18	18
S2BC6-8P2B23	VDC - Lift Drawing (Comment Period) - Core Walls - Lower Mezz to Main Conc Core #4	5	09-May-18	14-May-18	26
S2EC3-8P2B23	VDC - Lift Drawing (Comment Period) - Core Walls - Lower Mezz to Main Conc Core #1	5	21-May-18	25-May-18	20
S2BC7-8P2B23	VDC - Lift Drawing (Comment Period) - Core Walls - Lower Mezz to Main Conc Core #5	5	02-Jun-18	07-Jun-18	43
S2EC2-8P2B23	VDC - Lift Drawing (Comment Period) - Core Walls - Lower Mezz to Main Conc Core #8	5	14-Jun-18	19-Jun-18	33
S2CC8-8P2B23	VDC - Lift Drawing (Comment Period) - Core Walls - Lower Mezz to Main Conc Core #6	5	26-Jun-18	30-Jun-18	49
S2DC1-8P2B23	VDC - Lift Drawing (Comment Period) - Core Walls - Lower Mezz to Main Conc Core #7	5	09-Jul-18	13-Jul-18	44
S2AC5-8P2B33	VDC - Lift Drawing (Finalize) - Core Walls - Lower Mezz to Main Conc Core #3	5	27-Apr-18	02-May-18	20
S2FC4-8P2B33	VDC - Lift Drawing (Finalize) - Core Walls - Lower Mezz to Main Conc Core #2	5	03-May-18	08-May-18	18
S2BC6-8P2B33	VDC - Lift Drawing (Finalize) - Core Walls - Lower Mezz to Main Conc Core #4	5	15-May-18	19-May-18	26
S2EC3-8P2B33	VDC - Lift Drawing (Finalize) - Core Walls - Lower Mezz to Main Conc Core #1	5	26-May-18	01-Jun-18	20
S2BC7-8P2B33	VDC - Lift Drawing (Finalize) - Core Walls - Lower Mezz to Main Conc Core #5	5	08-Jun-18	13-Jun-18	43
S2EC2-8P2B33	VDC - Lift Drawing (Finalize) - Core Walls - Lower Mezz to Main Conc Core #8	5	20-Jun-18	25-Jun-18	33
S2CC8-8P2B33	VDC - Lift Drawing (Finalize) - Core Walls - Lower Mezz to Main Conc Core #6	5	02-Jul-18	07-Jul-18	49
S2DC1-8P2B33	VDC - Lift Drawing (Finalize) - Core Walls - Lower Mezz to Main Conc Core #7	5	14-Jul-18	19-Jul-18	44
VDC - 100 Main Concourse - General Coordination					
S3A60-3E10	VDC - General Coordination (Coordinate) - Quad A Main Conc	15	06-Jun-18	26-Jun-18	54
S3B60-3E10	VDC - General Coordination (Coordinate) - Quad B Main Conc	15	27-Jun-18	18-Jul-18	90
S3C60-3E10	VDC - General Coordination (Coordinate) - Quad C Main Conc	15	19-Jul-18	08-Aug-18	90
S3D60-3E10	VDC - General Coordination (Coordinate) - Quad D Main Conc	15	09-Aug-18	29-Aug-18	90
VDC - 100 Main Concourse - Structural Deck Coordination					
S3A50-3E10	VDC - Slab Penetrations / Embedded Conduit (Coordinate) - Area A Main Conc (Rebar Support)	15	05-Mar-18	23-Mar-18	22
S3F50-3E40	VDC - Slab Penetrations / Embedded Conduit (Coordinate) - Area F Main Conc (Rebar Support)	15	05-Mar-18	23-Mar-18	35
S3B50-3E50	VDC - Slab Penetrations / Embedded Conduit (Coordinate) - Area B Main Conc (Rebar Support)	15	26-Mar-18	13-Apr-18	39
S3E50-3E70	VDC - Slab Penetrations / Embedded Conduit (Coordinate) - Area E Main Conc (Rebar Support)	15	26-Mar-18	13-Apr-18	44
S3C50-3E60	VDC - Slab Penetrations / Embedded Conduit (Coordinate) - Area C Main Conc (Rebar Support)	15	16-Apr-18	04-May-18	74
S3D50-3E80	VDC - Slab Penetrations / Embedded Conduit (Coordinate) - Area D Main Conc (Rebar Support)	15	16-Apr-18	04-May-18	73
S3A1-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Main Concourse A1	10	10-Apr-18	23-Apr-18	15
S3F1-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Main Concourse F1	10	10-Apr-18	23-Apr-18	27
S3A2-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Main Concourse A2	10	19-Apr-18	02-May-18	15
S3F2-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Main Concourse F2	10	19-Apr-18	02-May-18	27
S3A3-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Main Concourse A3	10	30-Apr-18	11-May-18	15
S3F3-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Main Concourse F3	10	30-Apr-18	11-May-18	27
S3A4-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Main Concourse A4	10	09-May-18	22-May-18	15
S3E1-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Main Concourse E1	10	09-May-18	22-May-18	27

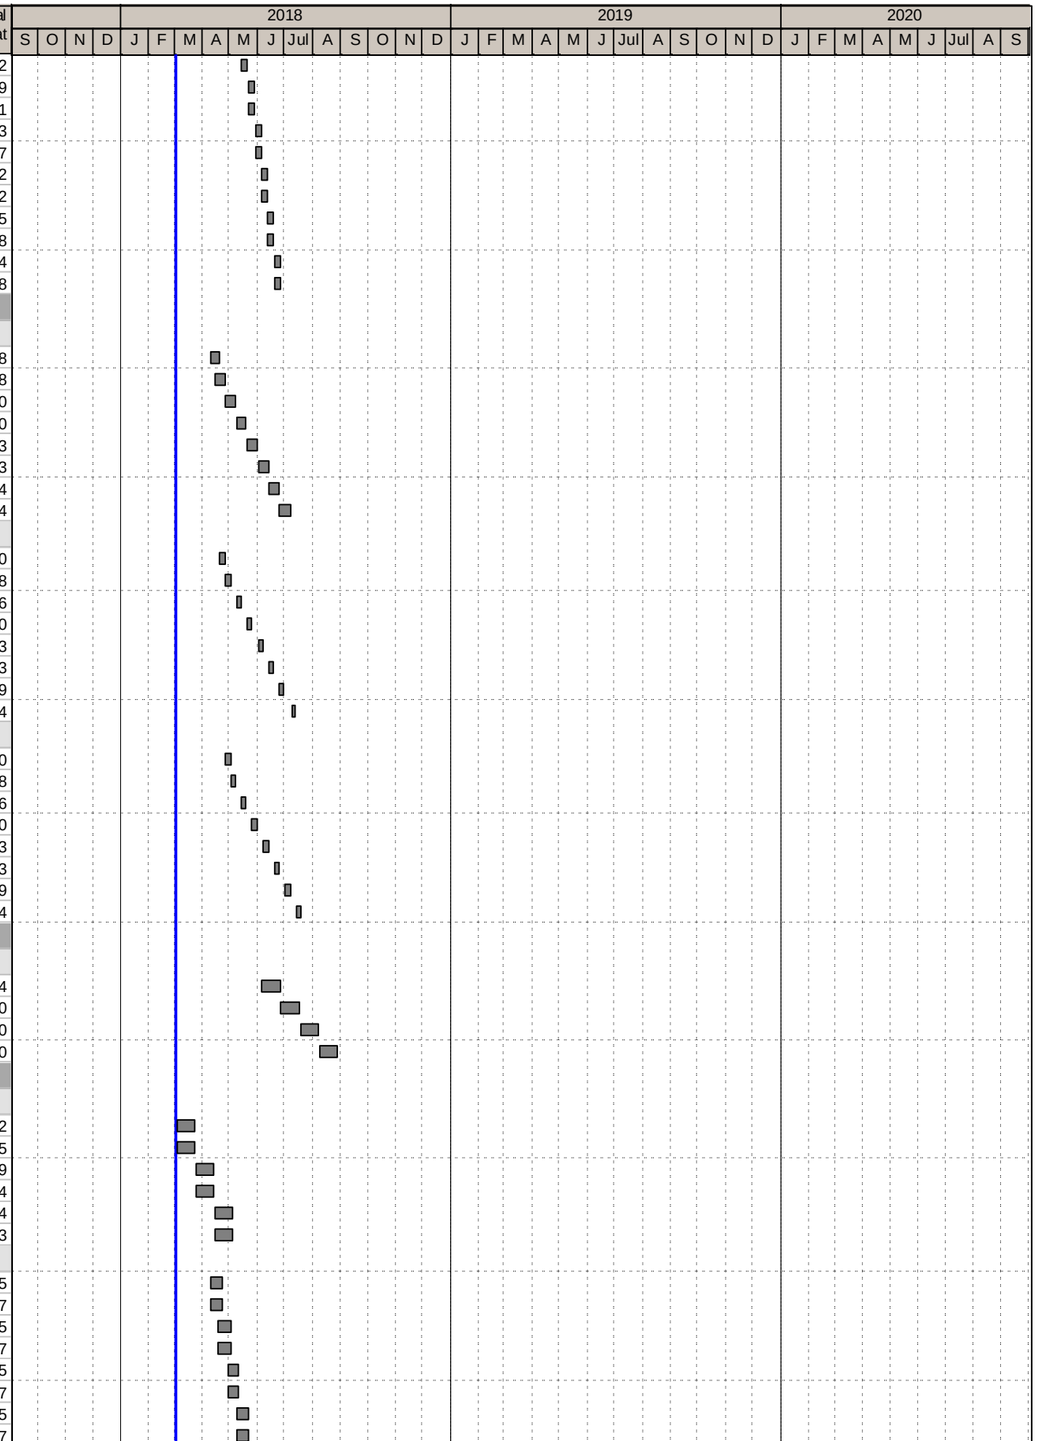

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S3B1-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Main Concourse B1	10	18-May-18	01-Jun-18	15
S3E2-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Main Concourse E2	10	18-May-18	01-Jun-18	27
S3B2-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Main Concourse B2	10	30-May-18	12-Jun-18	15
S3E3-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Main Concourse E3	10	30-May-18	12-Jun-18	27
S3B3-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Main Concourse B3	10	08-Jun-18	21-Jun-18	15
S3E4-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Main Concourse E4	10	08-Jun-18	21-Jun-18	29
S3B4-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Main Concourse B4	10	19-Jun-18	02-Jul-18	17
S3E5-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Main Concourse E5	10	19-Jun-18	02-Jul-18	30
S3B5-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Main Concourse B5	10	28-Jun-18	12-Jul-18	24
S3E6-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Main Concourse E6	10	28-Jun-18	12-Jul-18	30
S3B6-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Main Concourse B6	10	10-Jul-18	23-Jul-18	24
S3D1-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Main Concourse D1	10	10-Jul-18	23-Jul-18	33
S3C1-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Main Concourse C1	10	19-Jul-18	01-Aug-18	24
S3D2-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Main Concourse D2	10	19-Jul-18	01-Aug-18	35
S3C2-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Main Concourse C2	10	30-Jul-18	10-Aug-18	24
S3D3-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Main Concourse D3	10	30-Jul-18	10-Aug-18	35
S3C3-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Main Concourse C3	10	08-Aug-18	21-Aug-18	30
S3D4-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Main Concourse D4	10	08-Aug-18	21-Aug-18	35
S3C4-3E10	VDC - Lift Drawing (Prepare Draft) - P&J Deck - Main Concourse C4	10	17-Aug-18	30-Aug-18	30
S3A1-3E20	VDC - Lift Drawing (Comment Period) - P&J Deck - Main Concourse A1	5	24-Apr-18	30-Apr-18	19
S3F1-3E20	VDC - Lift Drawing (Comment Period) - P&J Deck - Main Concourse F1	5	24-Apr-18	30-Apr-18	33
S3A2-3E20	VDC - Lift Drawing (Comment Period) - P&J Deck - Main Concourse A2	5	03-May-18	09-May-18	21
S3F2-3E20	VDC - Lift Drawing (Comment Period) - P&J Deck - Main Concourse F2	5	03-May-18	09-May-18	35
S3A3-3E20	VDC - Lift Drawing (Comment Period) - P&J Deck - Main Concourse A3	5	14-May-18	18-May-18	22
S3F3-3E20	VDC - Lift Drawing (Comment Period) - P&J Deck - Main Concourse F3	5	14-May-18	18-May-18	33
S3A4-3E20	VDC - Lift Drawing (Comment Period) - P&J Deck - Main Concourse A4	5	23-May-18	30-May-18	21
S3E1-3E20	VDC - Lift Drawing (Comment Period) - P&J Deck - Main Concourse E1	5	23-May-18	30-May-18	31
S3B1-3E20	VDC - Lift Drawing (Comment Period) - P&J Deck - Main Concourse B1	5	04-Jun-18	08-Jun-18	19
S3E2-3E20	VDC - Lift Drawing (Comment Period) - P&J Deck - Main Concourse E2	5	04-Jun-18	08-Jun-18	29
S3B2-3E20	VDC - Lift Drawing (Comment Period) - P&J Deck - Main Concourse B2	5	13-Jun-18	19-Jun-18	17
S3E3-3E20	VDC - Lift Drawing (Comment Period) - P&J Deck - Main Concourse E3	5	13-Jun-18	19-Jun-18	27
S3B3-3E20	VDC - Lift Drawing (Comment Period) - P&J Deck - Main Concourse B3	5	22-Jun-18	28-Jun-18	15
S3E4-3E20	VDC - Lift Drawing (Comment Period) - P&J Deck - Main Concourse E4	5	22-Jun-18	28-Jun-18	29
S3B4-3E20	VDC - Lift Drawing (Comment Period) - P&J Deck - Main Concourse B4	5	03-Jul-18	10-Jul-18	17
S3E5-3E20	VDC - Lift Drawing (Comment Period) - P&J Deck - Main Concourse E5	5	03-Jul-18	10-Jul-18	32
S3B5-3E20	VDC - Lift Drawing (Comment Period) - P&J Deck - Main Concourse B5	5	13-Jul-18	19-Jul-18	27
S3E6-3E20	VDC - Lift Drawing (Comment Period) - P&J Deck - Main Concourse E6	5	13-Jul-18	19-Jul-18	30
S3B6-3E20	VDC - Lift Drawing (Comment Period) - P&J Deck - Main Concourse B6	5	24-Jul-18	30-Jul-18	24
S3D1-3E30	VDC - Lift Drawing (Comment Period) - P&J Deck - Main Concourse D1	5	24-Jul-18	30-Jul-18	33
S3C1-3E30	VDC - Lift Drawing (Comment Period) - P&J Deck - Main Concourse C1	5	02-Aug-18	08-Aug-18	27
S3D2-3E30	VDC - Lift Drawing (Comment Period) - P&J Deck - Main Concourse D2	5	02-Aug-18	08-Aug-18	36
S3C2-3E30	VDC - Lift Drawing (Comment Period) - P&J Deck - Main Concourse C2	5	13-Aug-18	17-Aug-18	24
S3D3-3E20	VDC - Lift Drawing (Comment Period) - P&J Deck - Main Concourse D3	5	13-Aug-18	17-Aug-18	35
S3C3-3E20	VDC - Lift Drawing (Comment Period) - P&J Deck - Main Concourse C3	5	22-Aug-18	28-Aug-18	31
S3D4-3E20	VDC - Lift Drawing (Comment Period) - P&J Deck - Main Concourse D4	5	22-Aug-18	28-Aug-18	35
S3C4-3E20	VDC - Lift Drawing (Comment Period) - P&J Deck - Main Concourse C4	5	31-Aug-18	07-Sep-18	30
S3A1-3E30	VDC - Lift Drawing (Finalize) - P&J Deck - Main Concourse A1	5	01-May-18	07-May-18	19
S3F1-3E30	VDC - Lift Drawing (Finalize) - P&J Deck - Main Concourse F1	5	01-May-18	07-May-18	33
S3A2-3E30	VDC - Lift Drawing (Finalize) - P&J Deck - Main Concourse A2	5	10-May-18	16-May-18	21
S3F2-3E30	VDC - Lift Drawing (Finalize) - P&J Deck - Main Concourse F2	5	10-May-18	16-May-18	35
S3A3-3E30	VDC - Lift Drawing (Finalize) - P&J Deck - Main Concourse A3	5	21-May-18	25-May-18	22
S3F3-3E30	VDC - Lift Drawing (Finalize) - P&J Deck - Main Concourse F3	5	21-May-18	25-May-18	33
S3A4-3E30	VDC - Lift Drawing (Finalize) - P&J Deck - Main Concourse A4	5	31-May-18	06-Jun-18	21
S3E1-3E30	VDC - Lift Drawing (Finalize) - P&J Deck - Main Concourse E1	5	31-May-18	06-Jun-18	31
S3B1-3E30	VDC - Lift Drawing (Finalize) - P&J Deck - Main Concourse B1	5	11-Jun-18	15-Jun-18	19
S3E2-3E30	VDC - Lift Drawing (Finalize) - P&J Deck - Main Concourse E2	5	11-Jun-18	15-Jun-18	29
S3B2-3E30	VDC - Lift Drawing (Finalize) - P&J Deck - Main Concourse B2	5	20-Jun-18	26-Jun-18	17
S3E3-3E30	VDC - Lift Drawing (Finalize) - P&J Deck - Main Concourse E3	5	20-Jun-18	26-Jun-18	27
S3B3-3E30	VDC - Lift Drawing (Finalize) - P&J Deck - Main Concourse B3	5	29-Jun-18	06-Jul-18	15
S3E4-3E30	VDC - Lift Drawing (Finalize) - P&J Deck - Main Concourse E4	5	29-Jun-18	06-Jul-18	29
S3B4-3E30	VDC - Lift Drawing (Finalize) - P&J Deck - Main Concourse B4	5	11-Jul-18	17-Jul-18	17

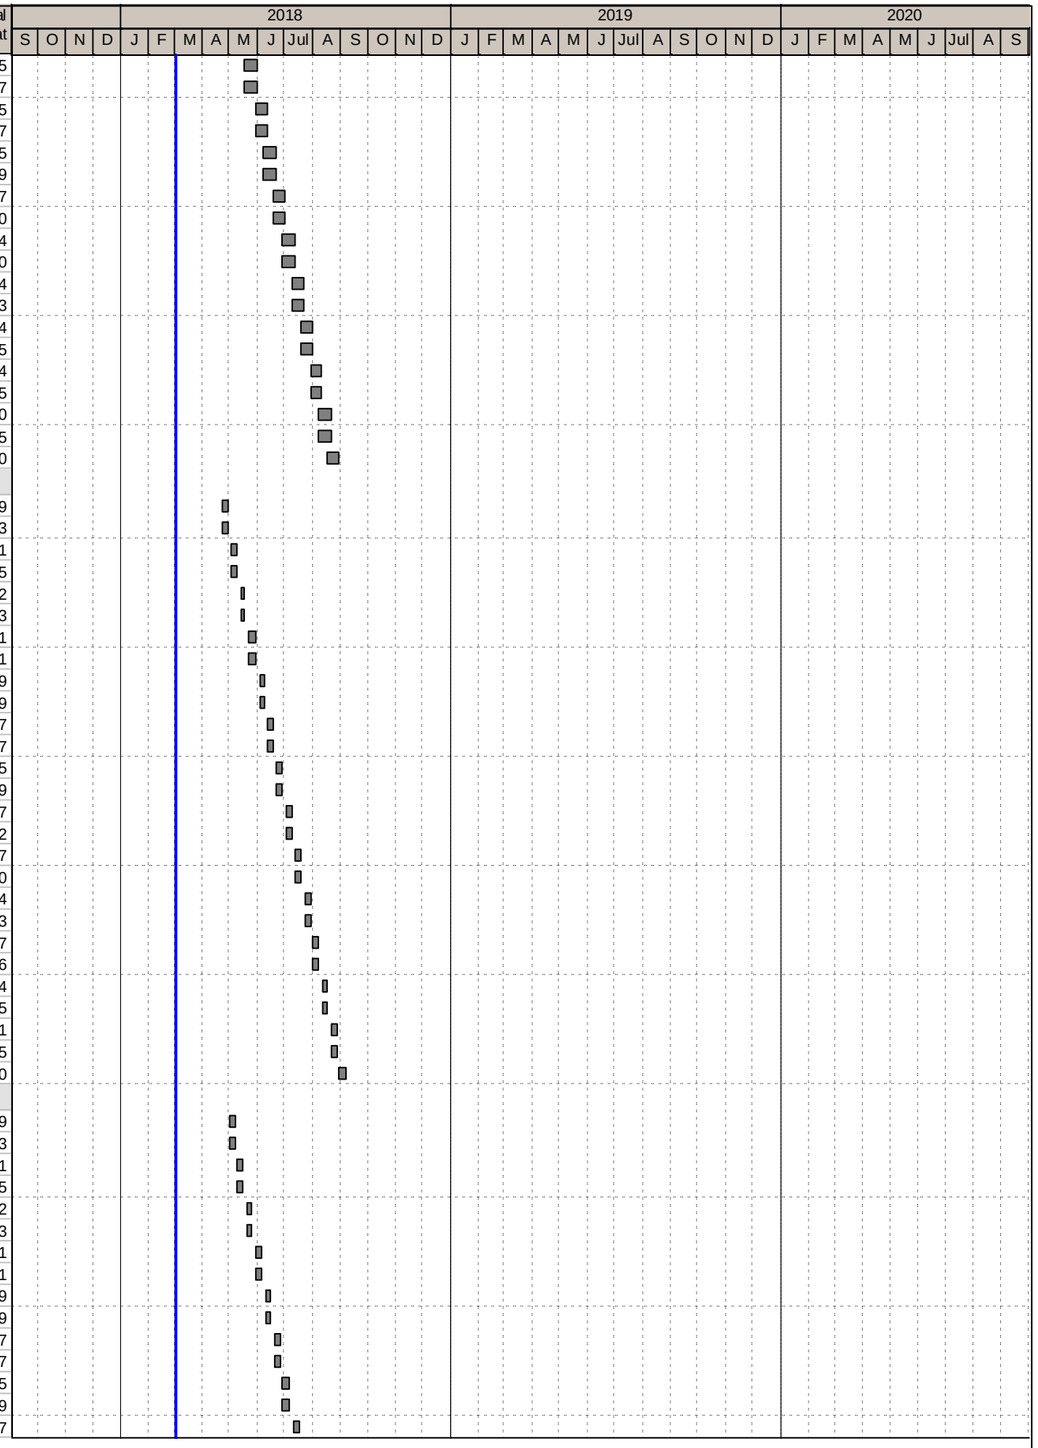

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S3E5-3E30	VDC - Lift Drawing (Finalize) - P&J Deck - Main Concourse E5	5	11-Jul-18	17-Jul-18	32
S3B5-3E30	VDC - Lift Drawing (Finalize) - P&J Deck - Main Concourse B5	5	20-Jul-18	26-Jul-18	27
S3E6-3E30	VDC - Lift Drawing (Finalize) - P&J Deck - Main Concourse E6	5	20-Jul-18	26-Jul-18	30
S3B6-3E30	VDC - Lift Drawing (Finalize) - P&J Deck - Main Concourse B6	5	31-Jul-18	06-Aug-18	24
S3D1-3E40	VDC - Lift Drawing (Finalize) - P&J Deck - Main Concourse D1	5	31-Jul-18	06-Aug-18	33
S3C1-3E40	VDC - Lift Drawing (Finalize) - P&J Deck - Main Concourse C1	5	09-Aug-18	15-Aug-18	27
S3D2-3E40	VDC - Lift Drawing (Finalize) - P&J Deck - Main Concourse D2	5	09-Aug-18	15-Aug-18	36
S3C2-3E40	VDC - Lift Drawing (Finalize) - P&J Deck - Main Concourse C2	5	20-Aug-18	24-Aug-18	24
S3D3-3E30	VDC - Lift Drawing (Finalize) - P&J Deck - Main Concourse D3	5	20-Aug-18	24-Aug-18	35
S3C3-3E30	VDC - Lift Drawing (Finalize) - P&J Deck - Main Concourse C3	5	29-Aug-18	05-Sep-18	31
S3D4-3E30	VDC - Lift Drawing (Finalize) - P&J Deck - Main Concourse D4	5	29-Aug-18	05-Sep-18	35
S3C4-3E30	VDC - Lift Drawing (Finalize) - P&J Deck - Main Concourse C4	5	10-Sep-18	14-Sep-18	30
VDC - 100 Main Concourse to TOC - Concrete Core Coordination					
S3AC5-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 1 Core #3	10	09-May-18	19-May-18	35
S3FC4-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 1 Core #2	10	09-May-18	19-May-18	30
S4AC5-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 2 Core #3	10	15-May-18	25-May-18	35
S4FC4-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 2 Core #2	10	15-May-18	25-May-18	30
S5AC5-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 3 Core #3	10	21-May-18	01-Jun-18	35
S5FC4-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 3 Core #2	10	21-May-18	01-Jun-18	30
S6AC5-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 4 Core #3	10	26-May-18	07-Jun-18	35
S6FC4-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 4 Core #2	10	26-May-18	07-Jun-18	30
S7AC5-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 5 Core #3	10	02-Jun-18	13-Jun-18	35
S7FC4-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 5 Core #2	10	02-Jun-18	13-Jun-18	30
S3BC6-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 1 Core #4	10	08-Jun-18	19-Jun-18	36
S8FC4-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 6 Core #2	10	08-Jun-18	19-Jun-18	30
S8AC5-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 6 Core #3	10	08-Jun-18	19-Jun-18	35
S3BC7-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 1 Core #5	10	14-Jun-18	25-Jun-18	66
S3EC3-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 1 Core #1	10	14-Jun-18	25-Jun-18	30
S4BC6-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 2 Core #4	10	14-Jun-18	25-Jun-18	36
S4BC7-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 2 Core #5	10	20-Jun-18	30-Jun-18	66
S4EC3-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 2 Core #1	10	20-Jun-18	30-Jun-18	30
S5BC6-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 3 Core #4	10	20-Jun-18	30-Jun-18	36
S5BC7-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 3 Core #5	10	26-Jun-18	07-Jul-18	66
S5EC3-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 3 Core #1	10	26-Jun-18	07-Jul-18	30
S6BC6-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 4 Core #4	10	26-Jun-18	07-Jul-18	36
S6BC7-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 4 Core #5	10	02-Jul-18	13-Jul-18	66
S6EC3-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 4 Core #1	10	02-Jul-18	13-Jul-18	30
S7BC6-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 5 Core #4	10	02-Jul-18	13-Jul-18	36
S3CC8-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 1 Core #6	10	09-Jul-18	19-Jul-18	62
S7BC7-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 5 Core #5	10	09-Jul-18	19-Jul-18	66
S7EC3-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 5 Core #1	10	09-Jul-18	19-Jul-18	30
S4CC8-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 2 Core #6	10	14-Jul-18	25-Jul-18	62
S8EC3-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 6 Core #1	10	14-Jul-18	25-Jul-18	30
S3EC2-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 1 Core #8	10	20-Jul-18	31-Jul-18	38
S5CC8-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 3 Core #6	10	20-Jul-18	31-Jul-18	62
S9EC3-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 7 Core #1	10	20-Jul-18	31-Jul-18	30
S4EC2-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 2 Core #8	10	26-Jul-18	06-Aug-18	38
S6CC8-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 4 Core #6	10	26-Jul-18	06-Aug-18	62
S5EC2-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 3 Core #8	10	01-Aug-18	11-Aug-18	38
S7CC8-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 5 Core #6	10	01-Aug-18	11-Aug-18	62
S6EC2-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 4 Core #8	10	07-Aug-18	17-Aug-18	38
S7EC2-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 5 Core #8	10	13-Aug-18	23-Aug-18	38
S8EC2-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 6 Core #8	10	18-Aug-18	29-Aug-18	38
S3DC1-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 1 Core #7	10	24-Aug-18	05-Sep-18	38
S9EC2-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 7 Core #8	10	24-Aug-18	05-Sep-18	38
S4DC1-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 2 Core #7	10	30-Aug-18	11-Sep-18	38
S5DC1-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 3 Core #7	10	06-Sep-18	17-Sep-18	38
S6DC1-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 4 Core #7	10	12-Sep-18	22-Sep-18	38
S7DC1-3E80	VDC - Lift Drawing (Prepare Draft) - Core Walls - Main Conc to Top Lift 5 Core #7	10	18-Sep-18	28-Sep-18	38
S3AC5-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 1 Core #3	5	21-May-18	25-May-18	35
S3FC4-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 1 Core #2	5	21-May-18	25-May-18	52

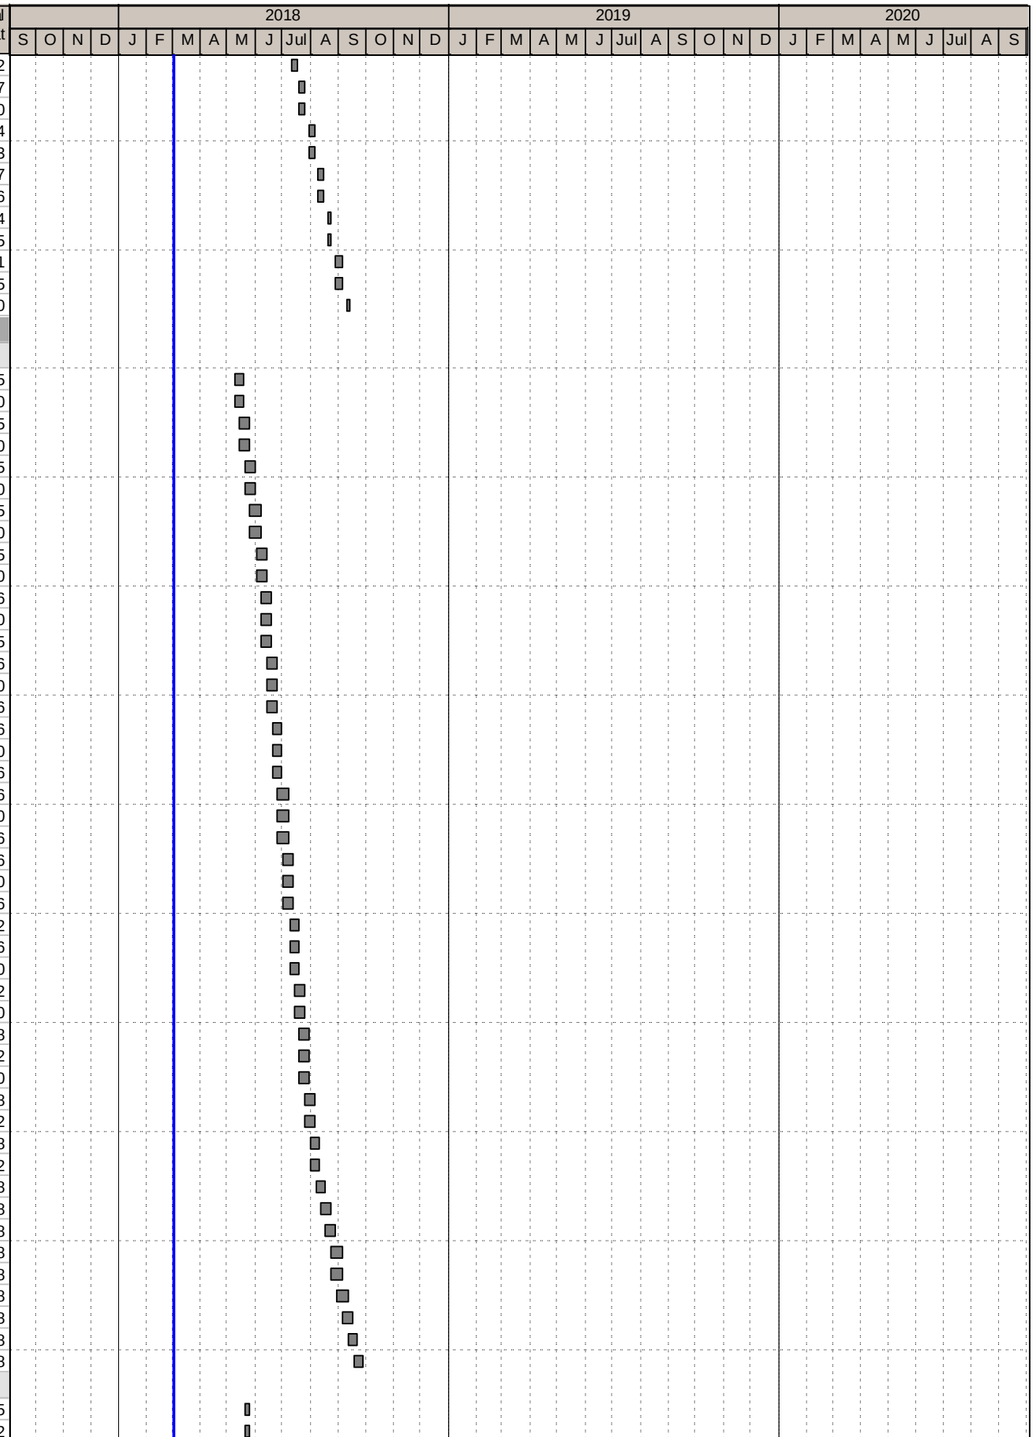

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S4AC5-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 2 Core #3	5	26-May-18	01-Jun-18	35
S4FC4-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 2 Core #2	5	26-May-18	01-Jun-18	52
S5AC5-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 3 Core #3	5	02-Jun-18	07-Jun-18	35
S5FC4-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 3 Core #2	5	02-Jun-18	07-Jun-18	52
S6AC5-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 4 Core #3	5	08-Jun-18	13-Jun-18	35
S6FC4-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 4 Core #2	5	08-Jun-18	13-Jun-18	52
S7AC5-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 5 Core #3	5	14-Jun-18	19-Jun-18	35
S7FC4-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 5 Core #2	5	14-Jun-18	19-Jun-18	52
S3BC6-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 1 Core #4	5	20-Jun-18	25-Jun-18	36
S8FC4-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 6 Core #2	5	20-Jun-18	25-Jun-18	52
S8AC5-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 6 Core #3	5	20-Jun-18	25-Jun-18	35
S3BC7-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 1 Core #5	5	26-Jun-18	30-Jun-18	66
S3EC3-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 1 Core #1	5	26-Jun-18	30-Jun-18	30
S4BC6-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 2 Core #4	5	26-Jun-18	30-Jun-18	36
S4BC7-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 2 Core #5	5	02-Jul-18	07-Jul-18	66
S4EC3-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 2 Core #1	5	02-Jul-18	07-Jul-18	30
S5BC6-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 3 Core #4	5	02-Jul-18	07-Jul-18	36
S5BC7-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 3 Core #5	5	09-Jul-18	13-Jul-18	66
S5EC3-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 3 Core #1	5	09-Jul-18	13-Jul-18	30
S6BC6-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 4 Core #4	5	09-Jul-18	13-Jul-18	36
S6BC7-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 4 Core #5	5	14-Jul-18	19-Jul-18	66
S6EC3-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 4 Core #1	5	14-Jul-18	19-Jul-18	30
S7BC6-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 5 Core #4	5	14-Jul-18	19-Jul-18	36
S3CC8-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 1 Core #6	5	20-Jul-18	25-Jul-18	62
S7BC7-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 5 Core #5	5	20-Jul-18	25-Jul-18	66
S7EC3-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 5 Core #1	5	20-Jul-18	25-Jul-18	30
S4CC8-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 2 Core #6	5	26-Jul-18	31-Jul-18	62
S8EC3-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 6 Core #1	5	26-Jul-18	31-Jul-18	30
S3EC2-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 1 Core #8	5	01-Aug-18	06-Aug-18	38
S5CC8-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 3 Core #6	5	01-Aug-18	06-Aug-18	62
S9EC3-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 7 Core #1	5	01-Aug-18	06-Aug-18	30
S4EC2-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 2 Core #8	5	07-Aug-18	11-Aug-18	38
S6CC8-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 4 Core #6	5	07-Aug-18	11-Aug-18	62
S5EC2-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 3 Core #8	5	13-Aug-18	17-Aug-18	38
S7CC8-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 5 Core #6	5	13-Aug-18	17-Aug-18	62
S6EC2-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 4 Core #8	5	18-Aug-18	23-Aug-18	38
S7EC2-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 5 Core #8	5	24-Aug-18	29-Aug-18	38
S8EC2-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 6 Core #8	5	30-Aug-18	05-Sep-18	38
S3DC1-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 1 Core #7	5	06-Sep-18	11-Sep-18	38
S9EC2-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 7 Core #8	5	06-Sep-18	11-Sep-18	38
S4DC1-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 2 Core #7	5	12-Sep-18	17-Sep-18	38
S5DC1-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 3 Core #7	5	18-Sep-18	22-Sep-18	38
S6DC1-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 4 Core #7	5	24-Sep-18	28-Sep-18	38
S7DC1-3E90	VDC - Lift Drawing (Comment Period) - Core Walls - Main Conc to Top Lift 5 Core #7	5	29-Sep-18	04-Oct-18	38
S3AC5-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 1 Core #3	5	26-May-18	01-Jun-18	35
S3FC4-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 1 Core #2	5	26-May-18	01-Jun-18	52
S4AC5-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 2 Core #3	5	02-Jun-18	07-Jun-18	35
S4FC4-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 2 Core #2	5	02-Jun-18	07-Jun-18	52
S5AC5-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 3 Core #3	5	08-Jun-18	13-Jun-18	35
S5FC4-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 3 Core #2	5	08-Jun-18	13-Jun-18	52
S6AC5-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 4 Core #3	5	14-Jun-18	19-Jun-18	35
S6FC4-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 4 Core #2	5	14-Jun-18	19-Jun-18	52
S7AC5-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 5 Core #3	5	20-Jun-18	25-Jun-18	35
S7FC4-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 5 Core #2	5	20-Jun-18	25-Jun-18	52
S3BC6-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 1 Core #4	5	26-Jun-18	30-Jun-18	36
S8FC4-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 6 Core #2	5	26-Jun-18	30-Jun-18	52
S8AC5-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 6 Core #3	5	26-Jun-18	30-Jun-18	35
S3BC7-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 1 Core #5	5	02-Jul-18	07-Jul-18	66
S3EC3-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 1 Core #1	5	02-Jul-18	07-Jul-18	30
S4BC6-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 2 Core #4	5	02-Jul-18	07-Jul-18	36
S4BC7-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 2 Core #5	5	09-Jul-18	13-Jul-18	66
S4EC3-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 2 Core #1	5	09-Jul-18	13-Jul-18	30

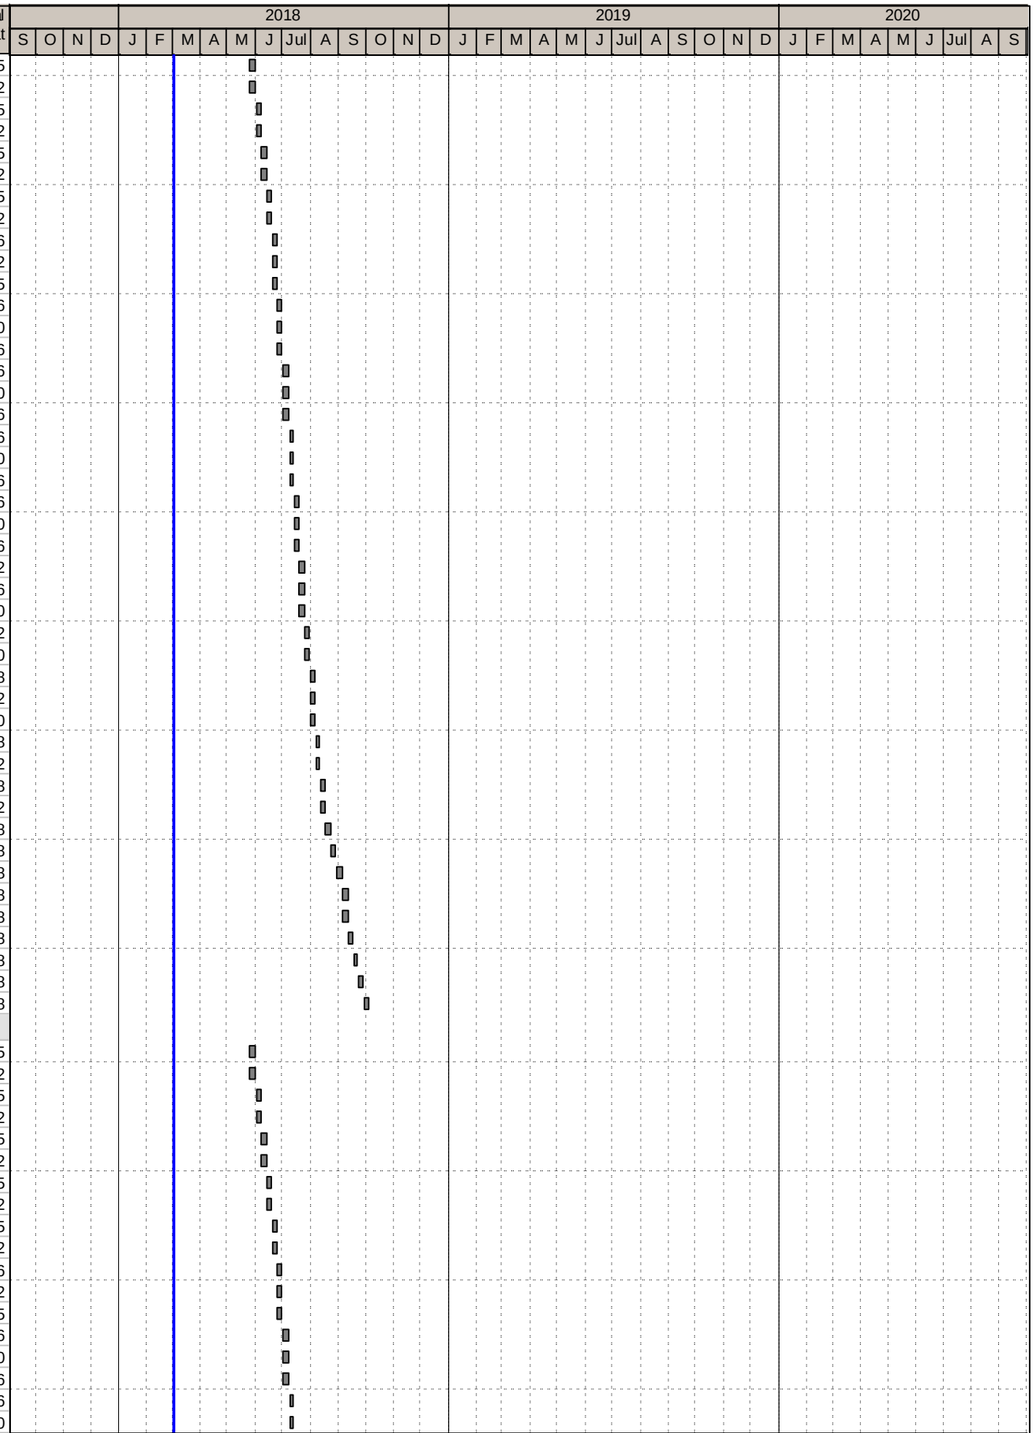

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S5BC6-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 3 Core #4	5	09-Jul-18	13-Jul-18	36
S5BC7-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 3 Core #5	5	14-Jul-18	19-Jul-18	66
S5EC3-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 3 Core #1	5	14-Jul-18	19-Jul-18	30
S6BC6-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 4 Core #4	5	14-Jul-18	19-Jul-18	36
S6BC7-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 4 Core #5	5	20-Jul-18	25-Jul-18	66
S6EC3-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 4 Core #1	5	20-Jul-18	25-Jul-18	30
S7BC6-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 5 Core #4	5	20-Jul-18	25-Jul-18	36
S3CC8-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 1 Core #6	5	26-Jul-18	31-Jul-18	62
S7BC7-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 5 Core #5	5	26-Jul-18	31-Jul-18	66
S7EC3-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 5 Core #1	5	26-Jul-18	31-Jul-18	30
S4CC8-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 2 Core #6	5	01-Aug-18	06-Aug-18	62
S8EC3-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 6 Core #1	5	01-Aug-18	06-Aug-18	30
S3EC2-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 1 Core #8	5	07-Aug-18	11-Aug-18	38
S5CC8-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 3 Core #6	5	07-Aug-18	11-Aug-18	62
S9EC3-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 7 Core #1	5	07-Aug-18	11-Aug-18	30
S4EC2-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 2 Core #8	5	13-Aug-18	17-Aug-18	38
S6CC8-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 4 Core #6	5	13-Aug-18	17-Aug-18	62
S5EC2-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 3 Core #8	5	18-Aug-18	23-Aug-18	38
S7CC8-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 5 Core #6	5	18-Aug-18	23-Aug-18	62
S6EC2-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 4 Core #8	5	24-Aug-18	29-Aug-18	38
S7EC2-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 5 Core #8	5	30-Aug-18	05-Sep-18	38
S8EC2-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 6 Core #8	5	06-Sep-18	11-Sep-18	38
S3DC1-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 1 Core #7	5	12-Sep-18	17-Sep-18	38
S9EC2-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 7 Core #8	5	12-Sep-18	17-Sep-18	38
S4DC1-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 2 Core #7	5	18-Sep-18	22-Sep-18	38
S5DC1-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 3 Core #7	5	24-Sep-18	28-Sep-18	38
S6DC1-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 4 Core #7	5	29-Sep-18	04-Oct-18	38
S7DC1-3E100	VDC - Lift Drawing (Finalize) - Core Walls - Main Conc to Top Lift 5 Core #7	5	05-Oct-18	10-Oct-18	38
VDC - 100 Main Concourse - SOMD Coordination					
S3C1-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Main Concourse C1	10	22-Oct-18	02-Nov-18	129
S3D1-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Main Concourse D1	10	22-Oct-18	02-Nov-18	135
S3C2-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Main Concourse C2	10	05-Nov-18	16-Nov-18	129
S3D2-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Main Concourse D2	10	05-Nov-18	16-Nov-18	135
S3C1-3E50	VDC - Lift Drawing (Comment Period) - SOMD - Main Concourse C1	5	05-Nov-18	09-Nov-18	136
S3D1-3E50	VDC - Lift Drawing (Comment Period) - SOMD - Main Concourse D1	5	05-Nov-18	09-Nov-18	142
S3C2-3E50	VDC - Lift Drawing (Comment Period) - SOMD - Main Concourse C2	5	19-Nov-18	27-Nov-18	129
S3D2-3E50	VDC - Lift Drawing (Comment Period) - SOMD - Main Concourse D2	5	19-Nov-18	27-Nov-18	135
S3C1-3E60	VDC - Lift Drawing (Finalize) - SOMD - Main Concourse C1	5	12-Nov-18	16-Nov-18	136
S3D1-3E60	VDC - Lift Drawing (Finalize) - SOMD - Main Concourse D1	5	12-Nov-18	16-Nov-18	142
S3C2-3E60	VDC - Lift Drawing (Finalize) - SOMD - Main Concourse C2	5	28-Nov-18	04-Dec-18	129
S3D2-3E60	VDC - Lift Drawing (Finalize) - SOMD - Main Concourse D2	5	28-Nov-18	04-Dec-18	135
VDC - 150 Lower Suite Lvl - General Coordination					
S4A60-3E10	VDC - General Coordination (Coordinate) - Quad A Lower Suite Lvl	15	27-Jun-18	18-Jul-18	54
S4B60-3E10	VDC - General Coordination (Coordinate) - Quad B Lower Suite Lvl	15	19-Jul-18	08-Aug-18	75
S4C60-3E10	VDC - General Coordination (Coordinate) - Quad C Lower Suite Lvl	15	09-Aug-18	29-Aug-18	75
S4D60-3E10	VDC - General Coordination (Coordinate) - Quad D Lower Suite Lvl	15	30-Aug-18	20-Sep-18	75
VDC - 150 Lower Suite Lvl - SOMD Coordination					
S4A50-3E10	VDC - Slab Penetrations / Embedded Conduit (Coordinate) - Lower Suite Lvl	15	03-Apr-18	23-Apr-18	16
S4A1-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Lower Suite A1	10	13-Aug-18	24-Aug-18	41
S4F1-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Lower Suite F1	10	13-Aug-18	24-Aug-18	37
S4E1-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Lower Suite E1	10	27-Aug-18	10-Sep-18	37
S4B1-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Lower Suite B1	10	27-Aug-18	10-Sep-18	41
S4B2-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Lower Suite B2	10	11-Sep-18	24-Sep-18	41
S4E2-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Lower Suite E2	10	11-Sep-18	24-Sep-18	37
S4B3-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Lower Suite B3	10	25-Sep-18	08-Oct-18	41
S4E3-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Lower Suite E3	10	25-Sep-18	08-Oct-18	37

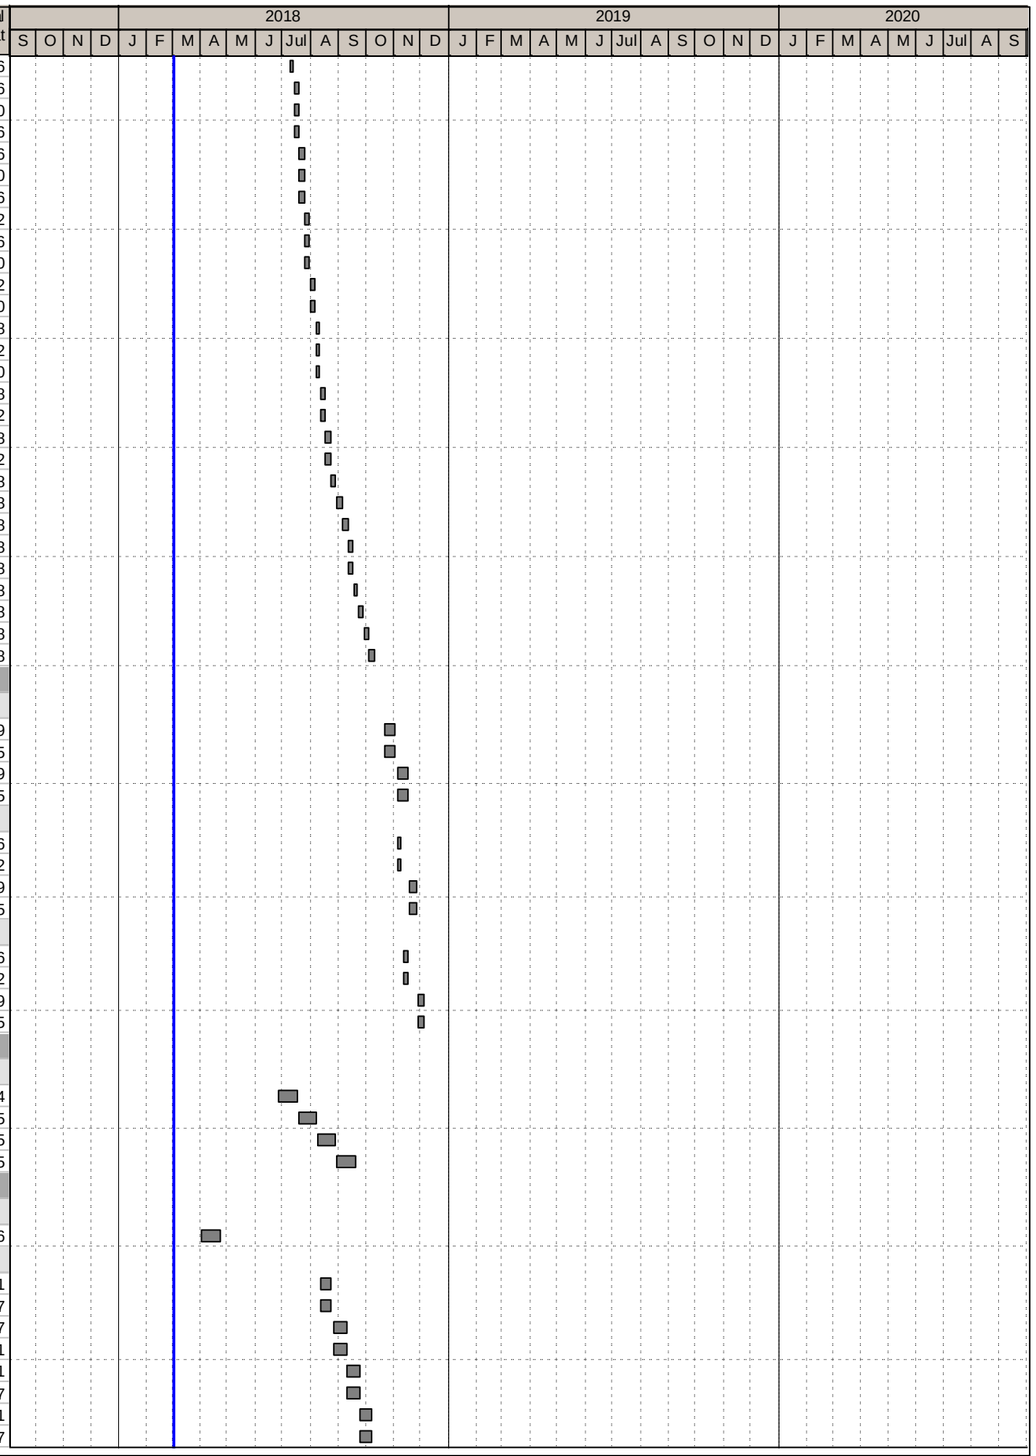

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S4B4-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Lower Suite B4	10	09-Oct-18	22-Oct-18	41
S4E4-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Lower Suite E4	10	09-Oct-18	22-Oct-18	37
S4B5-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Lower Suite B5	10	23-Oct-18	05-Nov-18	41
S4E5-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Lower Suite E5	10	23-Oct-18	05-Nov-18	37
S4D1-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Lower Suite D1	10	06-Nov-18	19-Nov-18	80
S4C1-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Lower Suite C1	10	06-Nov-18	19-Nov-18	119
S4C2-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Lower Suite C2	10	20-Nov-18	05-Dec-18	119
S4D2-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Lower Suite D2	10	20-Nov-18	05-Dec-18	129
S4C3-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Lower Suite C3	10	06-Dec-18	19-Dec-18	124
S4A1-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Lower Suite A1	5	27-Aug-18	31-Aug-18	55
S4F1-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Lower Suite F1	5	27-Aug-18	31-Aug-18	55
S4E1-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Lower Suite E1	5	11-Sep-18	17-Sep-18	69
S4B1-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Lower Suite B1	5	11-Sep-18	17-Sep-18	64
S4B2-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Lower Suite B2	5	25-Sep-18	01-Oct-18	67
S4E2-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Lower Suite E2	5	25-Sep-18	01-Oct-18	61
S4B3-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Lower Suite B3	5	09-Oct-18	15-Oct-18	59
S4E3-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Lower Suite E3	5	09-Oct-18	15-Oct-18	53
S4B4-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Lower Suite B4	5	23-Oct-18	29-Oct-18	49
S4E4-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Lower Suite E4	5	23-Oct-18	29-Oct-18	45
S4B5-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Lower Suite B5	5	06-Nov-18	12-Nov-18	41
S4E5-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Lower Suite E5	5	06-Nov-18	12-Nov-18	37
S4D1-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Lower Suite D1	5	20-Nov-18	28-Nov-18	80
S4C1-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Lower Suite C1	5	20-Nov-18	28-Nov-18	127
S4C2-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Lower Suite C2	5	06-Dec-18	12-Dec-18	119
S4D2-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Lower Suite D2	5	06-Dec-18	12-Dec-18	129
S4C3-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Lower Suite C3	5	20-Dec-18	27-Dec-18	124
S4A1-3E40	VDC - Lift Drawing (Finalize) - SOMD - Lower Suite A1	5	04-Sep-18	10-Sep-18	55
S4F1-3E40	VDC - Lift Drawing (Finalize) - SOMD - Lower Suite F1	5	04-Sep-18	10-Sep-18	55
S4E1-3E40	VDC - Lift Drawing (Finalize) - SOMD - Lower Suite E1	5	18-Sep-18	24-Sep-18	69
S4B1-3E40	VDC - Lift Drawing (Finalize) - SOMD - Lower Suite B1	5	18-Sep-18	24-Sep-18	64
S4B2-3E40	VDC - Lift Drawing (Finalize) - SOMD - Lower Suite B2	5	02-Oct-18	08-Oct-18	67
S4E2-3E40	VDC - Lift Drawing (Finalize) - SOMD - Lower Suite E2	5	02-Oct-18	08-Oct-18	61
S4B3-3E40	VDC - Lift Drawing (Finalize) - SOMD - Lower Suite B3	5	16-Oct-18	22-Oct-18	59
S4E3-3E40	VDC - Lift Drawing (Finalize) - SOMD - Lower Suite E3	5	16-Oct-18	22-Oct-18	53
S4B4-3E40	VDC - Lift Drawing (Finalize) - SOMD - Lower Suite B4	5	30-Oct-18	05-Nov-18	49
S4E4-3E40	VDC - Lift Drawing (Finalize) - SOMD - Lower Suite E4	5	30-Oct-18	05-Nov-18	45
S4B5-3E40	VDC - Lift Drawing (Finalize) - SOMD - Lower Suite B5	5	13-Nov-18	19-Nov-18	41
S4E5-3E40	VDC - Lift Drawing (Finalize) - SOMD - Lower Suite E5	5	13-Nov-18	19-Nov-18	37
S4D1-3E40	VDC - Lift Drawing (Finalize) - SOMD - Lower Suite D1	5	29-Nov-18	05-Dec-18	80
S4C1-3E40	VDC - Lift Drawing (Finalize) - SOMD - Lower Suite C1	5	29-Nov-18	05-Dec-18	127
S4C2-3E40	VDC - Lift Drawing (Finalize) - SOMD - Lower Suite C2	5	13-Dec-18	19-Dec-18	119
S4D2-3E40	VDC - Lift Drawing (Finalize) - SOMD - Lower Suite D2	5	13-Dec-18	19-Dec-18	129
S4C3-3E40	VDC - Lift Drawing (Finalize) - SOMD - Lower Suite C3	5	28-Dec-18	04-Jan-19	124
VDC - 200 Upper Suite Lvl - General Coordination					
S5A60-3E10	VDC - General Coordination (Coordinate) - Quad A Upper Suite Lvl	15	26-Jul-18	15-Aug-18	54
S5B60-3E10	VDC - General Coordination (Coordinate) - Quad B Upper Suite Lvl	15	16-Aug-18	06-Sep-18	69
S5C60-3E10	VDC - General Coordination (Coordinate) - Quad C Upper Suite Lvl	15	07-Sep-18	27-Sep-18	72
S5D60-3E10	VDC - General Coordination (Coordinate) - Quad D Upper Suite Lvl	15	28-Sep-18	18-Oct-18	72
VDC - 200 Upper Suite Lvl - SOMD Coordination					
S5A50-3E10	VDC - Slab Penetrations / Embedded Conduit (Coordinate) - Upper Suite Lvl	15	10-Apr-18	30-Apr-18	16
S5A1-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Suite A1	10	13-Aug-18	24-Aug-18	21
S5F1-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Suite F1	10	13-Aug-18	24-Aug-18	17
S5A2-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Suite A2	10	27-Aug-18	10-Sep-18	21
S5F2-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Suite F2	10	27-Aug-18	10-Sep-18	17
S5A3-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Suite A3	10	11-Sep-18	24-Sep-18	21
S5F3-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Suite F3	10	11-Sep-18	24-Sep-18	17
S5E1-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Suite E1	10	25-Sep-18	08-Oct-18	17

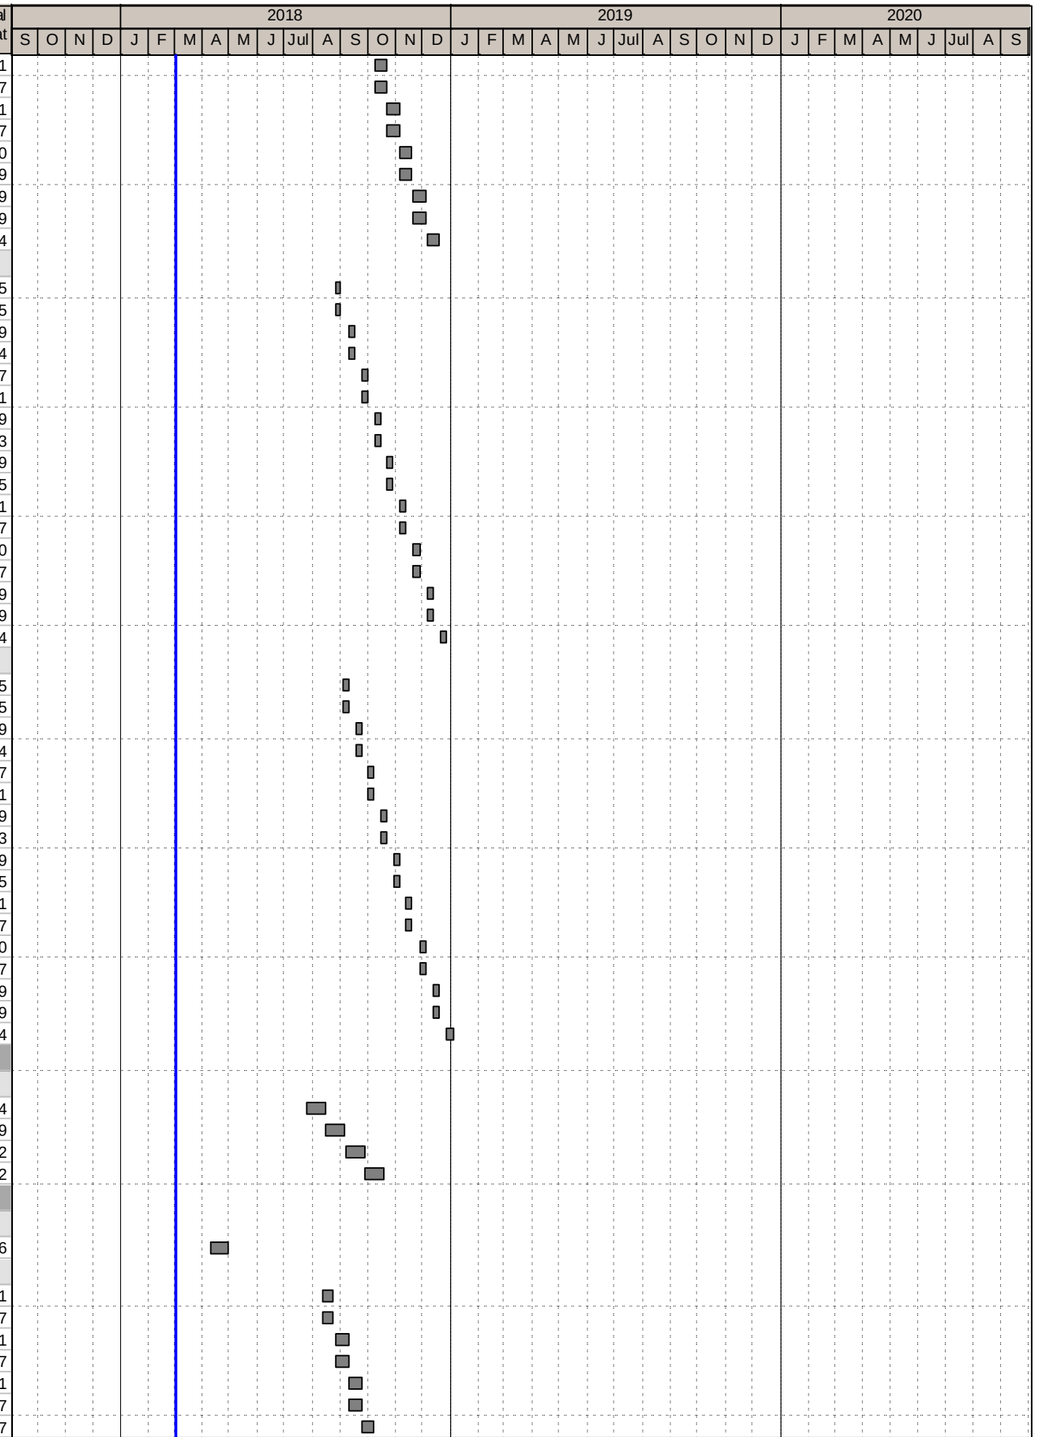

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S5B1-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Suite B1	10	25-Sep-18	08-Oct-18	21
S5B2-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Suite B2	10	09-Oct-18	22-Oct-18	21
S5E2-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Suite E2	10	09-Oct-18	22-Oct-18	17
S5B3-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Suite B3	10	23-Oct-18	05-Nov-18	21
S5E3-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Suite E3	10	23-Oct-18	05-Nov-18	17
S5B4-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Suite B4	10	06-Nov-18	19-Nov-18	21
S5E4-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Suite E4	10	06-Nov-18	19-Nov-18	17
S5B5-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Suite B5	10	20-Nov-18	05-Dec-18	21
S5E5-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Suite E5	10	20-Nov-18	05-Dec-18	17
S5D1-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Suite D1	10	06-Dec-18	19-Dec-18	50
S5C1-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Suite C1	10	06-Dec-18	19-Dec-18	53
S5C2-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Suite C2	10	20-Dec-18	04-Jan-19	53
S5D2-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Suite D2	10	20-Dec-18	04-Jan-19	50
S5C3-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Suite C3	10	07-Jan-19	18-Jan-19	103
S5A1-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Suite A1	5	27-Aug-18	31-Aug-18	60
S5F1-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Suite F1	5	27-Aug-18	31-Aug-18	60
S5A2-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Suite A2	5	11-Sep-18	17-Sep-18	52
S5F2-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Suite F2	5	11-Sep-18	17-Sep-18	52
S5A3-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Suite A3	5	25-Sep-18	01-Oct-18	45
S5F3-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Suite F3	5	25-Sep-18	01-Oct-18	45
S5E1-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Suite E1	5	09-Oct-18	15-Oct-18	49
S5B1-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Suite B1	5	09-Oct-18	15-Oct-18	53
S5B2-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Suite B2	5	23-Oct-18	29-Oct-18	45
S5E2-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Suite E2	5	23-Oct-18	29-Oct-18	41
S5B3-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Suite B3	5	06-Nov-18	12-Nov-18	37
S5E3-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Suite E3	5	06-Nov-18	12-Nov-18	33
S5B4-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Suite B4	5	20-Nov-18	28-Nov-18	29
S5E4-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Suite E4	5	20-Nov-18	28-Nov-18	25
S5B5-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Suite B5	5	06-Dec-18	12-Dec-18	21
S5E5-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Suite E5	5	06-Dec-18	12-Dec-18	17
S5D1-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Suite D1	5	20-Dec-18	27-Dec-18	58
S5C1-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Suite C1	5	20-Dec-18	27-Dec-18	61
S5C2-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Suite C2	5	07-Jan-19	11-Jan-19	53
S5D2-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Suite D2	5	07-Jan-19	11-Jan-19	50
S5C3-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Suite C3	5	21-Jan-19	25-Jan-19	103
S5A1-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Suite A1	5	04-Sep-18	10-Sep-18	60
S5F1-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Suite F1	5	04-Sep-18	10-Sep-18	60
S5A2-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Suite A2	5	18-Sep-18	24-Sep-18	52
S5F2-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Suite F2	5	18-Sep-18	24-Sep-18	52
S5A3-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Suite A3	5	02-Oct-18	08-Oct-18	45
S5F3-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Suite F3	5	02-Oct-18	08-Oct-18	45
S5E1-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Suite E1	5	16-Oct-18	22-Oct-18	49
S5B1-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Suite B1	5	16-Oct-18	22-Oct-18	53
S5B2-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Suite B2	5	30-Oct-18	05-Nov-18	45
S5E2-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Suite E2	5	30-Oct-18	05-Nov-18	41
S5B3-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Suite B3	5	13-Nov-18	19-Nov-18	37
S5E3-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Suite E3	5	13-Nov-18	19-Nov-18	33
S5B4-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Suite B4	5	29-Nov-18	05-Dec-18	29
S5E4-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Suite E4	5	29-Nov-18	05-Dec-18	25
S5B5-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Suite B5	5	13-Dec-18	19-Dec-18	21
S5E5-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Suite E5	5	13-Dec-18	19-Dec-18	17
S5D1-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Suite D1	5	28-Dec-18	04-Jan-19	58
S5C1-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Suite C1	5	28-Dec-18	04-Jan-19	61
S5C2-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Suite C2	5	14-Jan-19	18-Jan-19	53
S5D2-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Suite D2	5	14-Jan-19	18-Jan-19	50
S5C3-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Suite C3	5	28-Jan-19	01-Feb-19	103
VDC - 250 Mid Bowl Mezz Lvl - General Coordination					
S6A60-3E10	VDC - General Coordination (Coordinate) - Quad A Mid Bowl Mezz Lvl	15	16-Aug-18	06-Sep-18	54
S6B60-3E10	VDC - General Coordination (Coordinate) - Quad B Mid Bowl Mezz Lvl	15	07-Sep-18	27-Sep-18	54
S6C60-3E10	VDC - General Coordination (Coordinate) - Quad C Mid Bowl Mezz Lvl	15	28-Sep-18	18-Oct-18	57

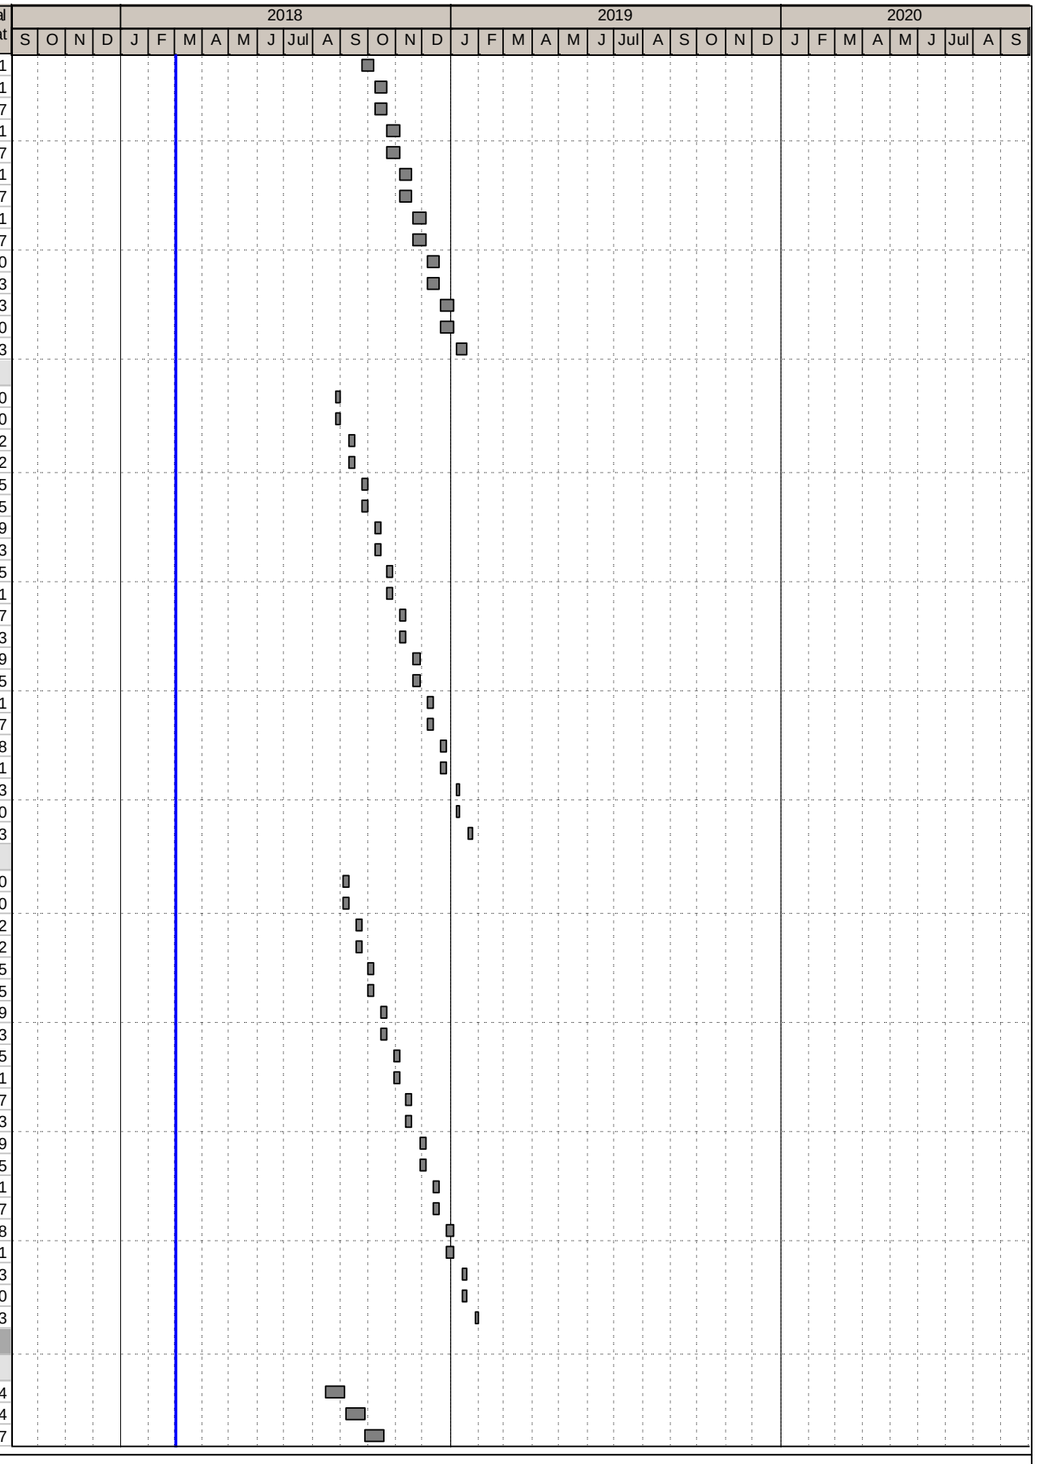

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S6D60-3E10	VDC - General Coordination (Coordinate) - Quad D Mid Bowl Mezz Lvl	15	19-Oct-18	08-Nov-18	57
VDC - 250 Mid Bowl Mezz Lvl - SOMD Coordination					
S5A50-3E20	VDC - Slab Penetrations / Embedded Conduit (Coordinate) - Mid Bowl Mezz	15	17-Apr-18	07-May-18	25
S6E1-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Mid Bowl Mezzanine E1	10	04-Sep-18	17-Sep-18	78
S6B1-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Mid Bowl Mezzanine B1	10	04-Sep-18	17-Sep-18	71
S6B2-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Mid Bowl Mezzanine B2	10	18-Sep-18	01-Oct-18	71
S6E2-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Mid Bowl Mezzanine E2	10	18-Sep-18	01-Oct-18	78
S6D1-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Mid Bowl Mezzanine D1	10	02-Oct-18	15-Oct-18	98
S6C1-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Mid Bowl Mezzanine C1	10	02-Oct-18	15-Oct-18	107
S6D2-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Mid Bowl Mezzanine D2	10	16-Oct-18	29-Oct-18	98
S6E1-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Mid Bowl Mezzanine E1	5	18-Sep-18	24-Sep-18	80
S6B1-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Mid Bowl Mezzanine B1	5	18-Sep-18	24-Sep-18	73
S6B2-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Mid Bowl Mezzanine B2	5	02-Oct-18	08-Oct-18	71
S6E2-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Mid Bowl Mezzanine E2	5	02-Oct-18	08-Oct-18	78
S6D1-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Mid Bowl Mezzanine D1	5	16-Oct-18	22-Oct-18	106
S6C1-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Mid Bowl Mezzanine C1	5	16-Oct-18	22-Oct-18	107
S6D2-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Mid Bowl Mezzanine D2	5	30-Oct-18	05-Nov-18	98
S6E1-3E40	VDC - Lift Drawing (Finalize) - SOMD - Mid Bowl Mezzanine E1	5	25-Sep-18	01-Oct-18	80
S6B1-3E40	VDC - Lift Drawing (Finalize) - SOMD - Mid Bowl Mezzanine B1	5	25-Sep-18	01-Oct-18	73
S6B2-3E40	VDC - Lift Drawing (Finalize) - SOMD - Mid Bowl Mezzanine B2	5	09-Oct-18	15-Oct-18	71
S6E2-3E40	VDC - Lift Drawing (Finalize) - SOMD - Mid Bowl Mezzanine E2	5	09-Oct-18	15-Oct-18	78
S6D1-3E40	VDC - Lift Drawing (Finalize) - SOMD - Mid Bowl Mezzanine D1	5	23-Oct-18	29-Oct-18	106
S6C1-3E40	VDC - Lift Drawing (Finalize) - SOMD - Mid Bowl Mezzanine C1	5	23-Oct-18	29-Oct-18	107
S6D2-3E40	VDC - Lift Drawing (Finalize) - SOMD - Mid Bowl Mezzanine D2	5	06-Nov-18	12-Nov-18	98
VDC - 300 Upper Concourse - General Coordination					
S7A60-3E10	VDC - General Coordination (Coordinate) - Quad A Upper Conc	15	07-Sep-18	27-Sep-18	54
S7B60-3E10	VDC - General Coordination (Coordinate) - Quad B Upper Conc	15	28-Sep-18	18-Oct-18	54
S7C60-3E10	VDC - General Coordination (Coordinate) - Quad C Upper Conc	15	19-Oct-18	08-Nov-18	88
S7D60-3E10	VDC - General Coordination (Coordinate) - Quad D Upper Conc	15	09-Nov-18	03-Dec-18	88
VDC - 300 Upper Concourse - SOMD Coordination					
S7A50-3E10	VDC - Slab Penetrations / Embedded Conduit (Coordinate) - Upper Conc	15	01-May-18	21-May-18	25
S7A1-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Concourse A1	10	27-Aug-18	10-Sep-18	35
S7F1-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Concourse F1	10	27-Aug-18	10-Sep-18	52
S7E1-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Concourse E1	10	11-Sep-18	24-Sep-18	52
S7B1-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Concourse B1	10	11-Sep-18	24-Sep-18	35
S7B2-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Concourse B2	10	25-Sep-18	08-Oct-18	35
S7E2-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Concourse E2	10	25-Sep-18	08-Oct-18	52
S7B3-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Concourse B3	10	09-Oct-18	22-Oct-18	35
S7E3-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Concourse E3	10	09-Oct-18	22-Oct-18	52
S7B4-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Concourse B4	10	23-Oct-18	05-Nov-18	35
S7E4-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Concourse E4	10	23-Oct-18	05-Nov-18	52
S7D1-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Concourse D1	10	06-Nov-18	19-Nov-18	65
S7B5-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Concourse B5	10	06-Nov-18	19-Nov-18	35
S7C1-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Concourse C1	10	20-Nov-18	05-Dec-18	55
S7D2-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Concourse D2	10	20-Nov-18	05-Dec-18	65
S7C2-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Concourse C2	10	06-Dec-18	19-Dec-18	55
S7D3-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Concourse D3	10	06-Dec-18	19-Dec-18	65
S7C3-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Concourse C3	10	20-Dec-18	04-Jan-19	55
S7A1-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Concourse A1	5	11-Sep-18	17-Sep-18	57
S7F1-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Concourse F1	5	11-Sep-18	17-Sep-18	64
S7E1-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Concourse E1	5	25-Sep-18	01-Oct-18	76
S7B1-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Concourse B1	5	25-Sep-18	01-Oct-18	58
S7B2-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Concourse B2	5	09-Oct-18	15-Oct-18	50

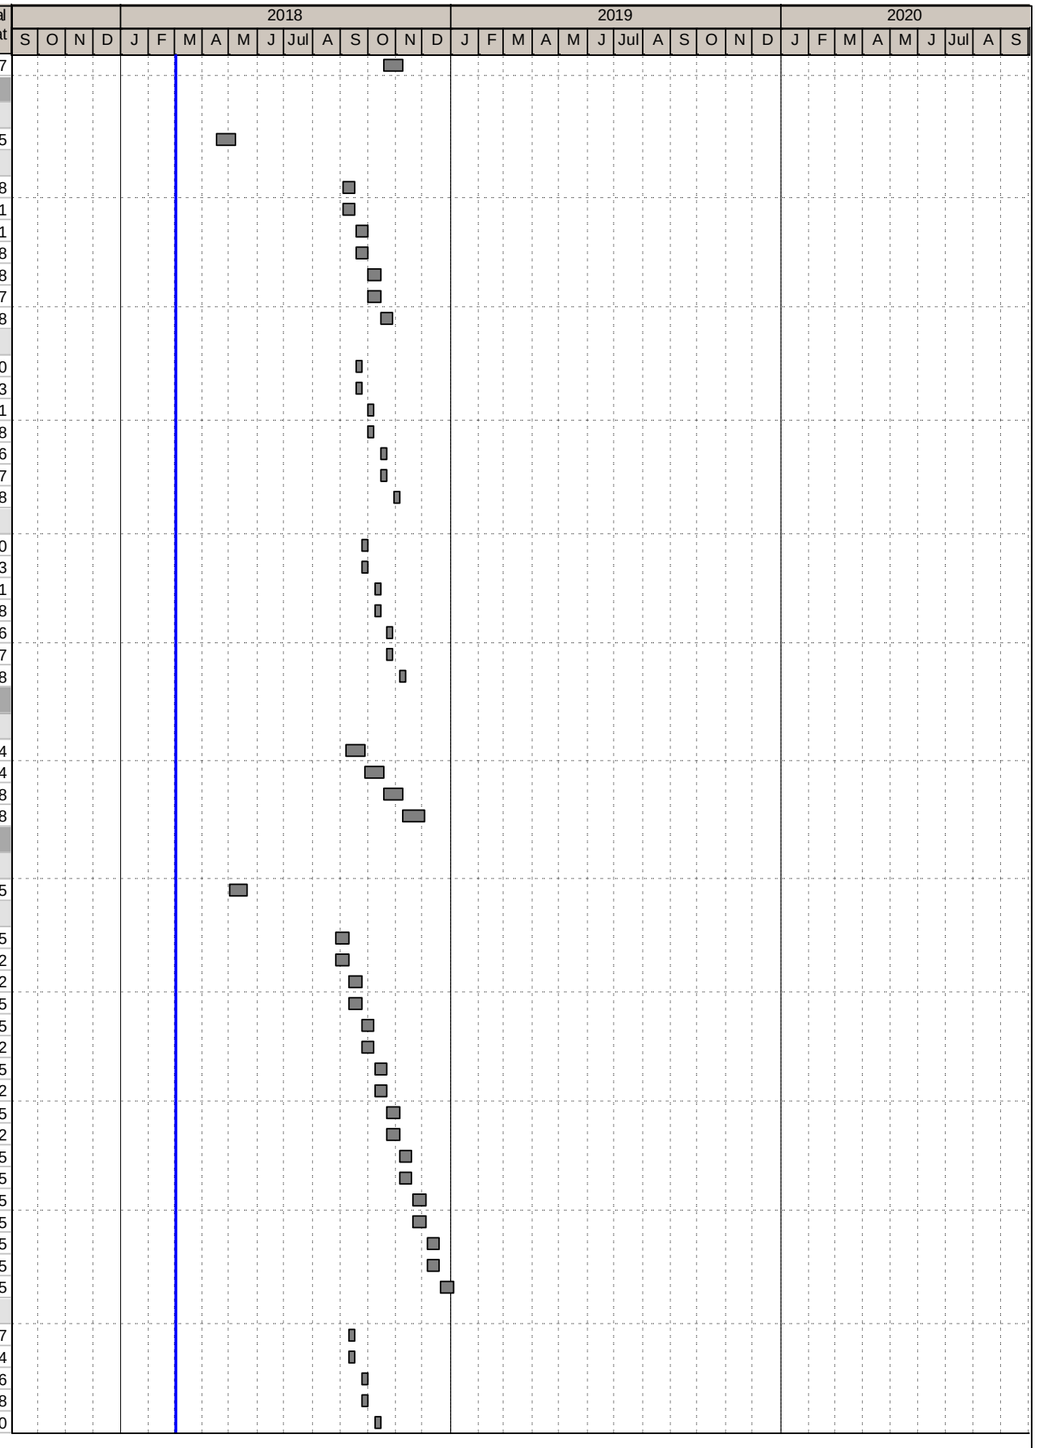

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S7E2-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Concourse E2	5	09-Oct-18	15-Oct-18	68
S7B3-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Concourse B3	5	23-Oct-18	29-Oct-18	51
S7E3-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Concourse E3	5	23-Oct-18	29-Oct-18	60
S7B4-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Concourse B4	5	06-Nov-18	12-Nov-18	43
S7E4-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Concourse E4	5	06-Nov-18	12-Nov-18	52
S7D1-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Concourse D1	5	20-Nov-18	28-Nov-18	79
S7B5-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Concourse B5	5	20-Nov-18	28-Nov-18	35
S7C1-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Concourse C1	5	06-Dec-18	12-Dec-18	69
S7D2-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Concourse D2	5	06-Dec-18	12-Dec-18	71
S7C2-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Concourse C2	5	20-Dec-18	27-Dec-18	61
S7D3-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Concourse D3	5	20-Dec-18	27-Dec-18	65
S7C3-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Concourse C3	5	07-Jan-19	11-Jan-19	55
S7A1-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Concourse A1	5	18-Sep-18	24-Sep-18	57
S7F1-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Concourse F1	5	18-Sep-18	24-Sep-18	64
S7E1-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Concourse E1	5	02-Oct-18	08-Oct-18	76
S7B1-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Concourse B1	5	02-Oct-18	08-Oct-18	58
S7B2-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Concourse B2	5	16-Oct-18	22-Oct-18	50
S7E2-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Concourse E2	5	16-Oct-18	22-Oct-18	68
S7B3-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Concourse B3	5	30-Oct-18	05-Nov-18	51
S7E3-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Concourse E3	5	30-Oct-18	05-Nov-18	60
S7B4-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Concourse B4	5	13-Nov-18	19-Nov-18	43
S7E4-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Concourse E4	5	13-Nov-18	19-Nov-18	52
S7D1-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Concourse D1	5	29-Nov-18	05-Dec-18	79
S7B5-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Concourse B5	5	29-Nov-18	05-Dec-18	35
S7C1-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Concourse C1	5	13-Dec-18	19-Dec-18	69
S7D2-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Concourse D2	5	13-Dec-18	19-Dec-18	71
S7C2-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Concourse C2	5	28-Dec-18	04-Jan-19	61
S7D3-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Concourse D3	5	28-Dec-18	04-Jan-19	65
S7C3-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Concourse C3	5	14-Jan-19	18-Jan-19	55
VDC -xxx Upper Mezz Lvl - SOMD Coordination					
S6A50-3E10	VDC - Slab Penetrations / Embedded Conduit (Coordinate) - Upper Mezz Lvl	15	24-Apr-18	14-May-18	25
S8A1-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Mezzanine A1	10	27-Aug-18	10-Sep-18	70
S8F1-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Mezzanine F1	10	11-Sep-18	24-Sep-18	70
S8C1-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Mezzanine C1	10	20-Nov-18	05-Dec-18	66
S8D1-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Upper Mezzanine D1	10	06-Dec-18	19-Dec-18	66
S8A1-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Mezzanine A1	5	11-Sep-18	17-Sep-18	72
S8F1-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Mezzanine F1	5	25-Sep-18	01-Oct-18	70
S8C1-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Mezzanine C1	5	06-Dec-18	12-Dec-18	76
S8D1-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Upper Mezzanine D1	5	20-Dec-18	27-Dec-18	66
S8A1-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Mezzanine A1	5	18-Sep-18	24-Sep-18	72
S8F1-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Mezzanine F1	5	02-Oct-18	08-Oct-18	70
S8C1-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Mezzanine C1	5	13-Dec-18	19-Dec-18	76
S8D1-3E40	VDC - Lift Drawing (Finalize) - SOMD - Upper Mezzanine D1	5	28-Dec-18	04-Jan-19	66
VDC - 350 Press Lvl - General Coordination					
S9A60-3E10	VDC - General Coordination (Coordinate) - Quad A Press Lvl	15	28-Sep-18	18-Oct-18	87
S9B60-3E10	VDC - General Coordination (Coordinate) - Quad B Press Lvl	15	19-Oct-18	08-Nov-18	87
S9C60-3E10	VDC - General Coordination (Coordinate) - Quad C Press Lvl	15	09-Nov-18	03-Dec-18	87
S9D60-3E10	VDC - General Coordination (Coordinate) - Quad D Press Lvl	15	04-Dec-18	24-Dec-18	87
VDC - 350 Press Lvl - SOMD Coordination					
S9A50-3E10	VDC - Slab Penetrations / Embedded Conduit (Coordinate) - Press Lvl	15	22-May-18	12-Jun-18	41
S9A1-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Press A1	10	27-Aug-18	10-Sep-18	61
S9F1-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Press F1	10	11-Sep-18	24-Sep-18	61
S9E1-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Press E1	10	25-Sep-18	08-Oct-18	61

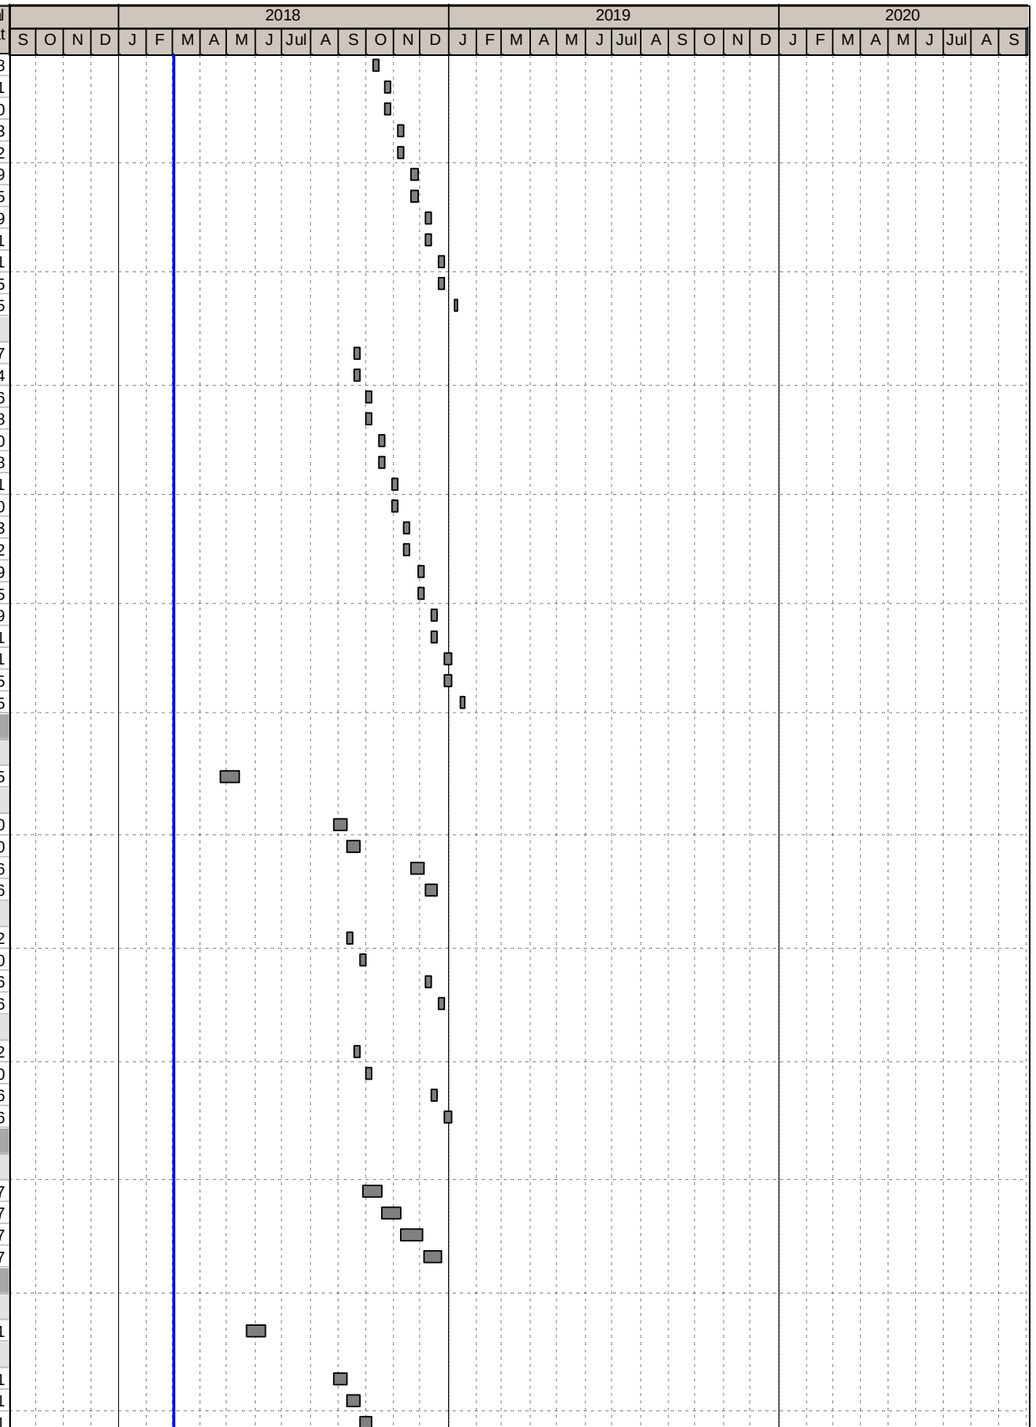

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S9E2-3E20	VDC - Lift Drawing (Prepare Draft) - SOMD - Press E2	10	09-Oct-18	22-Oct-18	61
S9A1-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Press A1	5	11-Sep-18	17-Sep-18	73
S9F1-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Press F1	5	25-Sep-18	01-Oct-18	73
S9E1-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Press E1	5	09-Oct-18	15-Oct-18	68
S9E2-3E30	VDC - Lift Drawing (Comment Period) - SOMD - Press E2	5	23-Oct-18	29-Oct-18	61
S9A1-3E40	VDC - Lift Drawing (Finalize) - SOMD - Press A1	5	18-Sep-18	24-Sep-18	73
S9F1-3E40	VDC - Lift Drawing (Finalize) - SOMD - Press F1	5	02-Oct-18	08-Oct-18	73
S9E1-3E40	VDC - Lift Drawing (Finalize) - SOMD - Press E1	5	16-Oct-18	22-Oct-18	68
S9E2-3E40	VDC - Lift Drawing (Finalize) - SOMD - Press E2	5	30-Oct-18	05-Nov-18	61
Obtain Permits					
Pre-Meeting					
SE50-3E10	Pre-Meeting with Building Department	0		20-Apr-17 A	
Basis of Design					
TE80-3E50	Basis of Design Submission/Review - Initial - (Clark County/Peer Review)	20	15-Jan-18 A	09-Feb-18 A	
TE81-3E30	Approval/Receipt - Basis of Design	0		19-Feb-18 A	
TE80-3E60	Basis of Design Submission/Review (Final Approval of Basis of Design)	5	12-Feb-18 A	19-Feb-18 A	
Permit Package #1 - Rough Grade / Mass Exc / Finish Grading / Utilities					
SE60-3E10	Permit Submission/Review - Package #1 - Rough Grade / Mass Exc / Finigh Grading / Utilities	20	13-Nov-17 A	19-Dec-17 A	
SE61-3E10	Permit Approval/Receipt - Package #1 - Rough Grade / Mass Exc / Finigh Grading / Utilities	0		19-Dec-17 A	
Permit Package #2 - Foundations / Deep UG MEP					
SE80-3E10	Permit Submission/Review (Initial) - Package #2 - Foundations / Deep UG MEP (To Top of Pile Cap/Footings)	20	09-Jan-18 A	30-Jan-18 A	
SE81-3E10	Permit Approval/Receipt - Package #2 - Foundations / Deep UG MEP (To Top of Pile Cap/Footings)	0		19-Feb-18 A	
SE80-3E20	Permit Submission/Review (Final) - Package #2 - Foundations / Deep UG MEP (To Top of Pile Cap/Footings)	10	05-Feb-18 A	19-Feb-18 A	
Cable Truss Analysis Review					
TE80-3E30	Cable Truss Analysis Review - Initial - (Clark County/Peer Review)	10	05-Mar-18	16-Mar-18	29
TE81-3E20	Completion of Review - Cable Truss	0		23-Mar-18	29
TE80-3E40	Cable Truss Analysis Review (Final Approval of Cable Truss Peer Review)	5	19-Mar-18	23-Mar-18	29
Permit Package #3a - Concrete Structure					
SE90-3E30	Permit Submission/Review (Initial) - Package #3a - Concrete Structure 1st Lift Walls/Columns Area AFBE	10	06-Mar-18*	19-Mar-18	4
SE91-3E20	Permit Approval/Receipt - Package #3a - Concrete Structure 1st Lift Walls/Columns Area AFBE	0		26-Mar-18	4
SE90-3E40	Permit Submission/Review (Final) - Package #3a - Concrete Structure 1st Lift Walls/Columns Area AFBE	5	20-Mar-18	26-Mar-18	4
Permit Package #3b - Concrete Structure					
TE90-3E50	Permit Submission/Review (Initial) - Package #3b - Concrete Area AFBE to Lvl 100	30	12-Mar-18*	20-Apr-18	0
TE91-3E30	Permit Approval/Receipt - Package #3b - Concrete Area AFBE to Lvl 100	0		11-May-18	0
TE90-3E60	Permit Submission/Review (Final) - Package #3b - Concrete Area AFBE to Lvl 100	15	23-Apr-18	11-May-18	0
Permit Package #4 - Concrete Structure & Structural Steel					
SE90-3E10	Permit Submission/Review (Initial) - Package #4 - Balance of Concrete & Structural Steel	30	03-Apr-18	14-May-18	23
SE91-3E10	Permit Approval/Receipt - Package #4 - Balance of Concrete & Structural Steel	0		05-Jun-18	23
SE90-3E20	Permit Submission/Review (Final) - Package #4 - Balance of Concrete & Structural Steel	15	15-May-18	05-Jun-18	23
Permit Package #5 - General Building					
SE100-3E10	Permit Submission/Review (Initial) - Package #5 - General Building	30	09-Jul-18	17-Aug-18	1
SE101-3E10	Permit Approval/Receipt - Package #5 - General Building	0		10-Sep-18	1
SE100-3E20	Permit Submission/Review (Final) - Package #5 - General Building	15	20-Aug-18	10-Sep-18	1
Assemble Construction Team					
Solicit Bids					
Pre-Meeting					

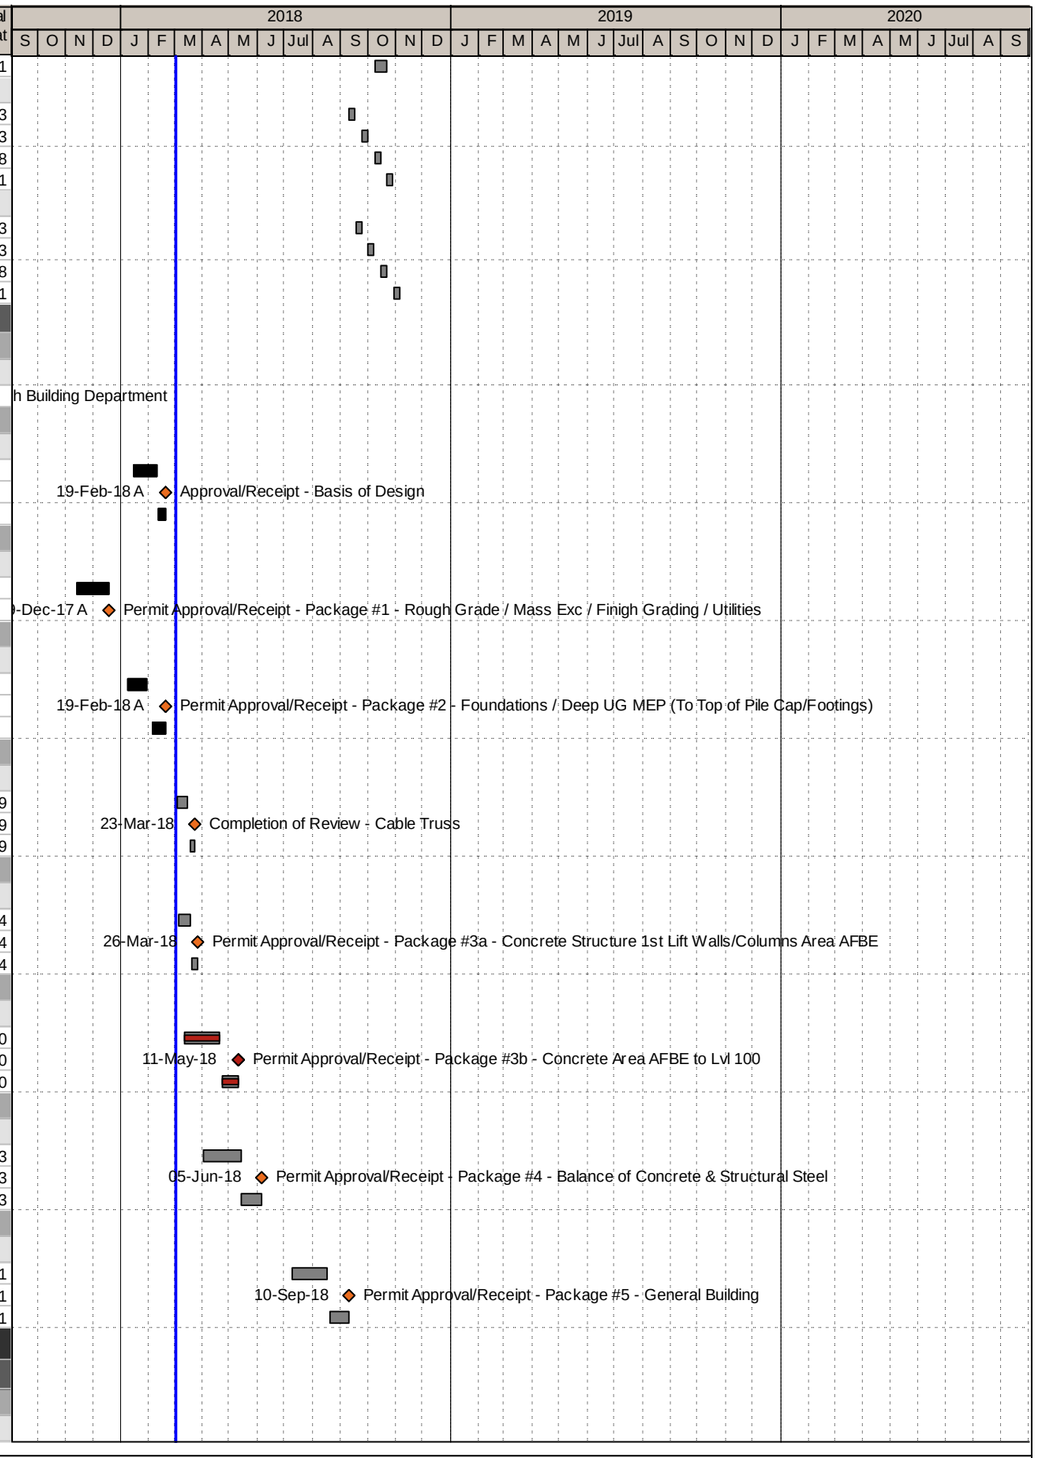

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
SEA0-4H33	Initial Outreach Meeting	1	15-Jun-17 A	15-Jun-17 A	
Bid Package 1a					
SEA0-4H05	Issue Bid Package - Bid Pak 1a (Steel/Cable Net Roof/ETFE)	0	05-Jul-17 A		
SEA0-4H15	Pre-Bid Meeting - Bid Pak 1a (Steel/Cable Net Roof/ETFE)	1	12-Jul-17 A	12-Jul-17 A	
SEA0-4H20	Solicit Bids - Bid Pak 1a (Steel/Cable Net Roof/ETFE)	20	05-Jul-17 A	31-Jul-17 A	
SEA0-4H34	Issue Bid Package - Bid Pak (Steel)	0	02-Jan-18 A		
SEA0-4H35	Solicit Bids - Bid Pak (Steel)	15	02-Jan-18 A	19-Jan-18 A	
Bid Package 1b					
SEB0-4H05	Issue Bid Package - Bid Pak 1b (Precast/MEP/Vertical Transportation/Enclosure)	0	05-Jul-17 A		
SEB0-4H15	Pre-Bid Meeting - Bid Pak 1b (Precast/MEP/Vertical Transportation/Enclosure)	1	12-Jul-17 A	12-Jul-17 A	
SEB0-4H20	Solicit Bids - Bid Pak 1b (Precast/MEP/Vertical Transportation/Enclosure)	20	05-Jul-17 A	31-Jul-17 A	
Bid Package 2a					
SEC0-4H05	Issue Bid Package - Bid Pak 2a (Box-Culvert)	0	05-Sep-17 A		
SEC0-4H20	Solicit Bids - Bid Pak 2a (Box-Culvert)	15	05-Sep-17 A	25-Sep-17 A	
Bid Package 2b					
SED0-4H05	Issue Bid Package - Bid Pak 2b (Demo/Site Clearing/Mass Excavation)	0	10-Oct-17 A		
SED0-4H20	Solicit Bids - Bid Pak 2b (Demo/Site Clearing/Mass Excavation)	15	10-Oct-17 A	31-Oct-17 A	
Bid Package 2c					
SEE0-4H05	Issue Bid Package - Bid Pak 2c (Deep Foundations)	0	10-Oct-17 A		
SEE0-4H20	Solicit Bids - Bid Pak 2c (Deep Foundations)	15	10-Oct-17 A	31-Oct-17 A	
Bid Package 2d					
SEI0-4H05	Issue Bid Package - Bid Pak 2d (Box-Culvert Concrete)	0	23-Oct-17 A		
SEI0-4H20	Solicit Bids - Bid Pak 2d (Box-Culvert Concrete)	15	23-Oct-17 A	13-Nov-17 A	
Bid Package - DAS					
SEE0-4H24	Issue Bid Package - Bid Pak (DAS)	0	10-Oct-17 A		
SEE0-4H25	Solicit Bids - Bid Pak (DAS)	15	10-Oct-17 A	20-Nov-17 A	
Bid Package 3a					
SEF0-4H05	Issue Bid Package - Bid Pak 3a (Structural Ex, Seating, Site Security/Access)	0	29-Nov-17 A		
SEF0-4H20	Solicit Bids - Bid Pak 3a (Structural Ex, Seating, Site Security/Access)	16	29-Nov-17 A	20-Dec-17 A	
Bid Package 3b					
SEF0-4H22	Issue Bid Package - Bid Pak 3b RFQ (Signature Tower)	0	29-Nov-17 A		
SEF0-4H23	Solicit Bids - Bid Pak 3b RFQ (Signature Tower)	16	29-Nov-17 A	20-Dec-17 A	
SEF0-4H25	Solicit Bids - Bid Pak 3b RFP (Signature Tower)	14	22-Dec-17 A	23-Feb-18 A	
Bid Package 3c					
SEF2-4H05	Issue Bid Package - Bid Pak 3c (Ext Studs/Air Barrier, Roofing, Railings, Etc.)	0	02-Jan-18 A		
SEF2-4H20	Solicit Bids - Bid Pak 3c (Ext Studs/Air Barrier, Roofing, Railings, Etc.)	15	02-Jan-18 A	22-Jan-18 A	
Bid Package 4					
SEG0-4H05	Issue Bid Package - Bid Pak 4 (Framing/Drywall/Masonry/Doors & Frames)	0	09-Jul-18		49
SEG0-4H20	Solicit Bids - Bid Pak 4 (Framing/Drywall/Masonry/Doors & Frames)	30	09-Jul-18	17-Aug-18	49
Bid Package 5					
SEH0-4H05	Issue Bid Package - Bid Pak 5 (Specialties/Finishes)	0	22-Oct-18		10
SEH0-4H20	Solicit Bids - Bid Pak 5 (Specialties/Finishes)	30	22-Oct-18	04-Dec-18	10
Evaluate Bids & Award Contracts					
Bid Package 1a					
SEA0-4H21	Evaluate Bids & Award Contracts - Bid Pak 1a (Structure/Cable Net Roof/ETFE)	20	01-Aug-17 A	25-Aug-17 A	

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
SEA0-4H36	Evaluate Bids & Award Contracts - Bid Pak (Steel)	5	22-Jan-18 A	26-Jan-18 A	
SEA0-4H23	Award - Bid Pak 1a (Steel)	0	25-Aug-17 A		
SEA1-4H23	Award - Bid Pak 1a (Cable Net/ETFE)	0	25-Aug-17 A		
SEA0-4H37	Award - Bid Pak (Steel)	0	29-Jan-18 A		
Bid Package 1b					
SEB0-4H21	Evaluate Bids & Award Contracts - Bid Pak 1b (MEP/Vertical Transportation)	20	01-Aug-17 A	25-Aug-17 A	
SEB1-4H21	Evaluate Bids & Award Contracts - Bid Pak 1b (Precast)	30	01-Aug-17 A	12-Sep-17 A	
SEB2-4H21	Evaluate Bids & Award Contracts - Bid Pak 1b (Enclosure)	30	01-Aug-17 A	12-Sep-17 A	
SEB0-4H23	Award - Bid Pak 1b (HVAC/Controls)	0	25-Aug-17 A		
SEB1-4H23	Award - Bid Pak 1b (Plumbing)	0	25-Aug-17 A		
SEB2-4H23	Award - Bid Pak 1b (Electrical)	0	25-Aug-17 A		
SEB3-4H23	Award - Bid Pak 1b (Fire Protection)	0	25-Aug-17 A		
SEB8-4H23	Award - Bid Pak 1b (Elevators & Lifts)	0	25-Aug-17 A		
SEB9-4H23	Award - Bid Pak 1b (Escalators)	0	25-Aug-17 A		
SEB4-4H23	Award - Bid Pak 1b (Structural Precast)	0	13-Sep-17 A		
SEB5-4H23	Award - Bid Pak 1b (Exterior Curtainwall & Glazing)	0	13-Sep-17 A		
SEB6-4H23	Award - Bid Pak 1b (Metal Panels)	0	13-Sep-17 A		
SEF8-4H23	Award - Bid Pak 1b (Operable Wall)	0	13-Sep-17 A		
Bid Package 2a					
SEC0-4H21	Evaluate Bids & Make Recommendations - Bid Pak 2a (Box-Culvert)	10	26-Sep-17 A	27-Oct-17 A	
SEC0-4H22	Raiders Approve Recommendations - Bid Pak 2a (Box-Culvert)	5	30-Oct-17 A	17-Nov-17 A	
SEC0-4H23	Award - Bid Pak 2a (Box-Culvert)	0	29-Nov-17 A		
Bid Package 2b					
SED0-4H21	Evaluate Bids & Make Recommendations - Bid Pak 2b (Demo/Site Clearing/Mass Excavation)	17	01-Nov-17 A	17-Nov-17 A	
SED0-4H22	Raiders Approve Recommendations - Bid Pak 2b (Demo/Site Clearing/Mass Excavation)	2	20-Nov-17 A	27-Nov-17 A	
SED0-4H23	Award - Bid Pak 2b (Earthwork)	0	30-Nov-17 A		
SED1-4H23	Award - Bid Pak 2b (Site Utilities)	0	30-Nov-17 A		
Bid Package 2c					
SEE0-4H21	Evaluate Bids & Make Recommendations - Bid Pak 2c (Deep Foundations)	21	01-Nov-17 A	08-Dec-17 A	
SEE0-4H22	Raiders Approve Recommendations - Bid Pak 2c (Deep Foundations)	2	11-Dec-17 A	12-Dec-17 A	
SEE0-4H23	Award - Bid Pak 2c (Deep Foundations)	0	13-Dec-17 A		
Bid Package 2d					
SEI0-4H21	Evaluate Bids & Make Recommendations - Bid Pak 2d (Box-Culvert Concrete)	8	14-Nov-17 A	08-Dec-17 A	
SEI0-4H22	Raiders Approve Recommendations - Bid Pak 2d (Box-Culvert Concrete)	1	11-Dec-17 A	12-Dec-17 A	
SEI0-4H23	Award - Bid Pak 2d (Box-Culvert Concrete)	0	13-Dec-17 A		
Bid Package - DAS					
SEE0-4H26	Evaluate Bids & Make Recommendations - Bid Pak (DAS)	40	21-Nov-17 A	05-Mar-18	52
SEE0-4H27	Raiders Approve Recommendations - Bid Pak (DAS)	5	06-Mar-18	12-Mar-18	52
SEF10-4H23	Award - Bid Pak (DAS)	0	13-Mar-18		52
Bid Package 3a					

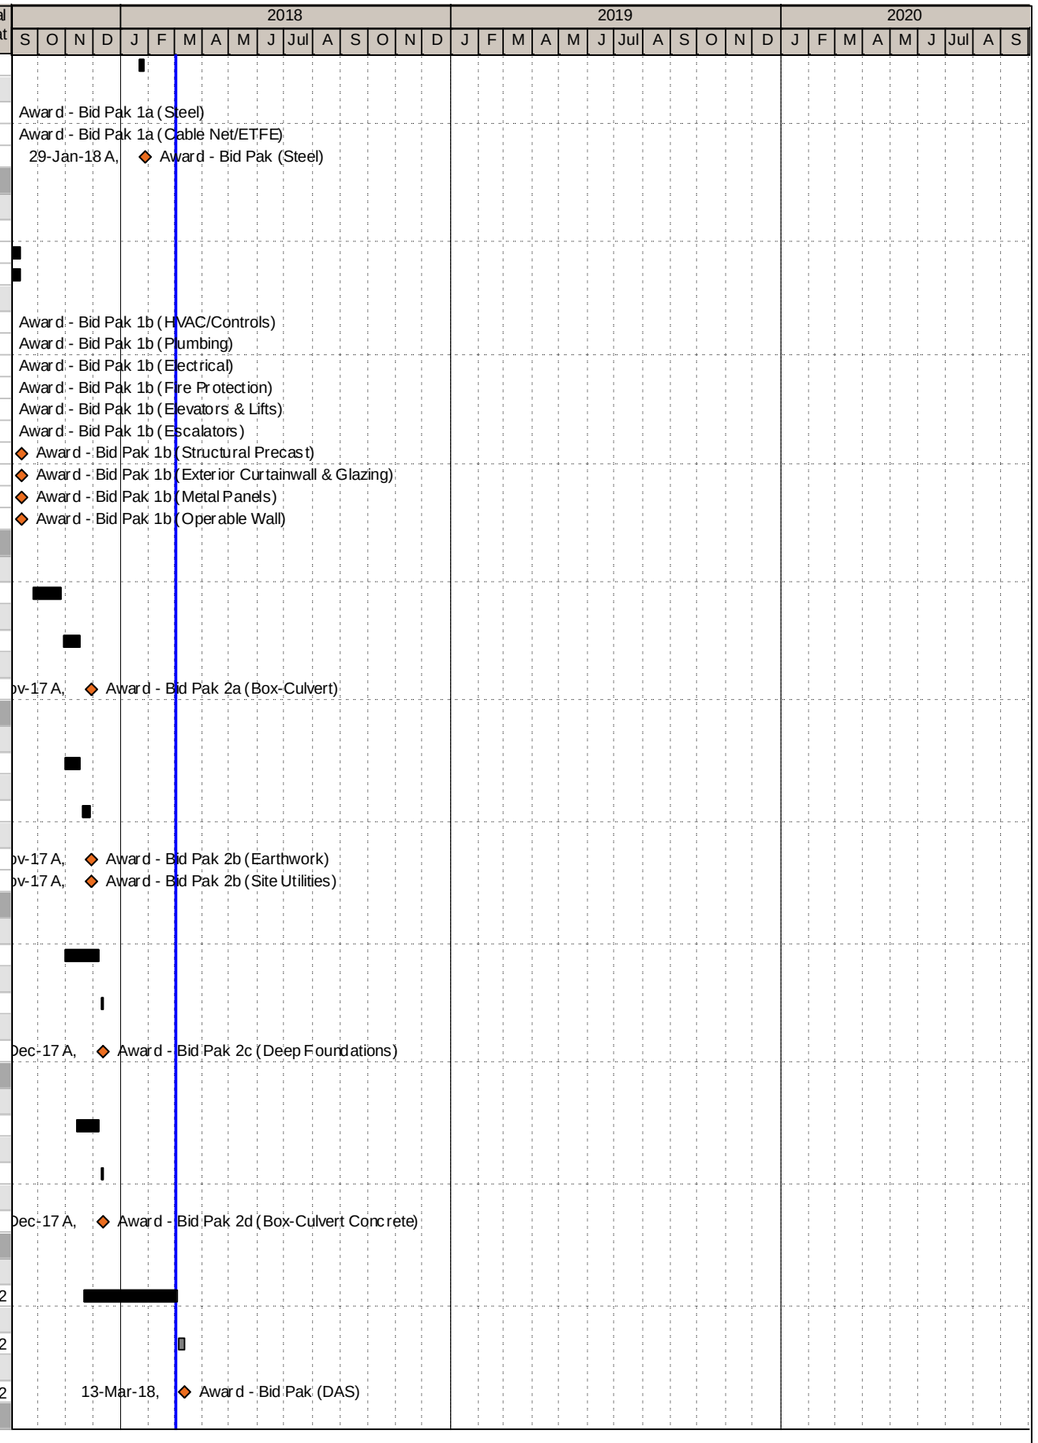

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
SEF0-4H21	Evaluate Bids & Award Contracts - Bid Pak 3a (Structural Ex, Seating, Site Security/Access)	25	21-Dec-17 A	30-Mar-18	3
SEE2-4H23	Award - Bid Pak 3a (Structural Excavation/Backfill/Subdrainage)	0	05-Mar-18		3
SEF3-4H23	Award - Bid Pak 3a (Fixed Seating)	0	02-Apr-18		130
SEF4-4H23	Award - Bid Pak 3a (Retractable Seating)	0	02-Apr-18		219
Bid Package 3b					
SEF0-4H24	Evaluate Bids & Make Recommendations - Bid Pak 3b RFP (Signature Tower)	20	26-Feb-18 A	23-Mar-18	226
SEF0-4H26	Raiders Approve Recommendations - Bid Pak 3b (Signature Tower)	5	26-Mar-18	30-Mar-18	226
SEF7-4H23	Award - Bid Pak 3b (Signature Tower)	0	02-Apr-18		226
Bid Package 3c					
SEF5-4H21	Evaluate Bids & Award Contracts - Bid Pak 3c (Ext Studs/Air Barrier, Roofing, Railings, Etc.)	5	23-Jan-18 A	08-Mar-18	4
SEF12-4H23	Award - Bid Pak 3c (Concrete Deck Formwork)	0	09-Feb-18 A		
SEF13-4H23	Award - Bid Pak 3c (Rebar - Superstructure)	0	16-Feb-18 A		
SEF5-4H23	Award - Bid Pak 3c (Roofing/Roof Systems)	0	21-Feb-18 A		
SEF11-4H23	Award - Bid Pak 3c (Waterproofing/Dampproofing)	0	21-Feb-18 A		
SEF6-4H23	Award - Bid Pak 3c (Misc Metals)	0	09-Mar-18		16
SEB7-4H23	Award - Bid Pak 3c (Exterior Framing/Sheathing/Air Barrier)	0	06-Apr-18		18
SEF9-4H23	Award - Bid Pak 3c (Operable Field Mechanization)	0	06-Apr-18		43
SEG4-4H23	Award - Bid Pak 3c (Stadium Railings)	0	06-Apr-18		143
Bid Package 4					
SEG0-4H21	Evaluate Bids & Award Contracts - Bid Pak 4 (Framing/Drywall/Masonry/Doors & Frames)	30	20-Aug-18	01-Oct-18	49
SEG0-4H23	Award - Bid Pak 4 (Interior Framing/Drywall)	0	02-Oct-18		49
SEG1-4H23	Award - Bid Pak 4 (Masonry/Stone/Brick)	0	02-Oct-18		49
SEG2-4H23	Award - Bid Pak 4 (Doors/Frames/Hardware)	0	02-Oct-18		49
SEG3-4H23	Award - Bid Pak 4 (Interior Storefront/Glazing)	0	02-Oct-18		49
SEG5-4H23	Award - Bid Pak 4 (Misc Metals)	0	02-Oct-18		49
SEG6-4H23	Award - Bid Pak 4 (Expansion Control)	0	02-Oct-18		49
SEG7-4H23	Award - Bid Pak 4 (Low Voltage)	0	02-Oct-18		49
SEG8-4H23	Award - Bid Pak 4 (Bituminous Pavement)	0	02-Oct-18		49
SEG9-4H23	Award - Bid Pak 4 (Site Concrete)	0	02-Oct-18		49
SEG10-4H23	Award - Bid Pak 4 (Landscape/Irrigation)	0	02-Oct-18		49
SEG11-4H23	Award - Bid Pak 4 (Fireproofing)	0	02-Oct-18		49
Bid Package 5					
SEH0-4H21	Evaluate Bids & Award Contracts - Bid Pak 5 (Specialties/Finishes)	60	05-Dec-18	28-Feb-19	10
SEH0-4H23	Award - Bid Pak 5 (Acoustical Ceilings/Walls)	0	01-Mar-19		34
SEH1-4H23	Award - Bid Pak 5 (Ceramic Tile)	0	01-Mar-19		34
SEH2-4H23	Award - Bid Pak 5 (Carpet/Resilient/Wood Flooring)	0	01-Mar-19		34
SEH3-4H23	Award - Bid Pak 5 (Floor Coatings)	0	01-Mar-19		34
SEH4-4H23	Award - Bid Pak 5 (Wall Finishes/Painting)	0	01-Mar-19		34
SEH5-4H23	Award - Bid Pak 5 (Concrete Sealer)	0	01-Mar-19		34
SEH6-4H23	Award - Bid Pak 5 (Toilet Compartments)	0	01-Mar-19		34
SEH7-4H23	Award - Bid Pak 5 (Toilet Accessories)	0	01-Mar-19		34
SEH8-4H23	Award - Bid Pak 5 (Site Furnishings)	0	01-Mar-19		34
SEH9-4H23	Award - Bid Pak 5 (Signage - Exterior/Interior)	0	01-Mar-19		34
SEH10-4H23	Award - Bid Pak 5 (Overhead Doors)	0	01-Mar-19		34
SEH11-4H23	Award - Bid Pak 5 (Vomitory/Stadium Curtains)	0	01-Mar-19		34
SEH12-4H23	Award - Bid Pak 5 (Fences/Gates)	0	01-Mar-19		34
SEH13-4H23	Award - Bid Pak 5 (Millwork/Casework/Wood Lockers)	0	01-Mar-19		34
SEH14-4H23	Award - Bid Pak 5 (Misc Metals)	0	01-Mar-19		34
SEH15-4H23	Award - Bid Pak 5 (Grass Field)	0	01-Mar-19		34
SEH16-4H23	Award - Bid Pak 5 (Interior Sealants/Firesafing)	0	01-Mar-19		34

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
SEH17-4H23	Award - Bid Pak 5 (Bowl Acoustical Treatment)	0	01-Mar-19		34
SEH18-4H23	Award - Bid Pak 5 (Loading Dock Equipment)	0	01-Mar-19		34
SEH19-4H23	Award - Bid Pak 5 (Residential Appliances)	0	01-Mar-19		34
SEH20-4H23	Award - Bid Pak 5 (Food Service Equipment)	0	01-Mar-19		34
SEH21-4H23	Award - Bid Pak 5 (Misc Specialties)	0	01-Mar-19		34
SEH22-4H23	Award - Bid Pak 5 (Sports Equipment)	0	01-Mar-19		34
SEH23-4H23	Award - Bid Pak 5 (Window Treatments)	0	01-Mar-19		34
Procurement					
Excavation					
S00-5M4R	Submit/Approve/Procure - Demo and Site Preparation	10	07-Dec-17 A	22-Dec-17 A	
Blasting & Misc Permits					
S000-5M40	Submit for Blasting Permit - Mass Excavation	10	07-Dec-17 A	21-Dec-17 A	
S001-5M40	Receive Blasting Permit - Mass Excavation	0		21-Dec-17 A	
Foundations					
S00-5N1P30	Submit - Box-Culvert Reinforcing	10	06-Nov-17 A	16-Nov-17 A	
S00-5N1P20	Approve - Box-Culvert Reinforcing	5	17-Nov-17 A	06-Dec-17 A	
S00-5N1P10	Procure - Box-Culvert Reinforcing	6	05-Dec-17 A	19-Dec-17 A	
Deep Foundations					
000 Event Level					
Submit					
SEA0-5N1S	Deep Foundations - Subcontractor Develop/Submit Shop Drawings - Area A	12	18-Dec-17 A	12-Jan-18 A	
SEF0-5N1S	Deep Foundations - Subcontractor Develop/Submit Shop Drawings - Area F	10	12-Jan-18 A	23-Jan-18 A	
SEB0-5N1S	Deep Foundations - Subcontractor Develop/Submit Shop Drawings - Area B	10	19-Jan-18 A	30-Jan-18 A	
SEC0-5N1S	Deep Foundations - Subcontractor Develop/Submit Shop Drawings - Area C	10	26-Jan-18 A	30-Jan-18 A	
SEE0-5N1S	Deep Foundations - Subcontractor Develop/Submit Shop Drawings - Area E	10	26-Jan-18 A	30-Jan-18 A	
SED0-5N1S	Deep Foundations - Subcontractor Develop/Submit Shop Drawings - Area D	10	26-Jan-18 A	30-Jan-18 A	
Approve					
SEA0-5N1A	Deep Foundations - Design Team Review/Approve Shop Drawings - Area A	10	22-Jan-18 A	26-Jan-18 A	
SEB0-5N1A	Deep Foundations - Design Team Review/Approve Shop Drawings - Area B	10	01-Feb-18 A	06-Feb-18 A	
SEF0-5N1A	Deep Foundations - Design Team Review/Approve Shop Drawings - Area F	10	01-Feb-18 A	06-Feb-18 A	
SEC0-5N1A	Deep Foundations - Design Team Review/Approve Shop Drawings - Area C	10	01-Feb-18 A	06-Feb-18 A	
SEE0-5N1A	Deep Foundations - Design Team Review/Approve Shop Drawings - Area E	10	01-Feb-18 A	06-Feb-18 A	
SED0-5N1A	Deep Foundations - Design Team Review/Approve Shop Drawings - Area D	10	01-Feb-18 A	06-Feb-18 A	
Fabricate					
SEA0-5N1F	Deep Foundations - Fabricate - Area A	10	29-Jan-18 A	16-Feb-18 A	
SEF0-5N1F	Deep Foundations - Fabricate - Area F	10	08-Feb-18 A	26-Feb-18 A	
SEB0-5N1F	Deep Foundations - Fabricate - Area B	10	19-Feb-18 A	05-Mar-18	14
SEC0-5N1F	Deep Foundations - Fabricate - Area C	10	26-Feb-18 A	09-Mar-18	17
SEE0-5N1F	Deep Foundations - Fabricate - Area E	10	05-Mar-18	16-Mar-18	17
SED0-5N1F	Deep Foundations - Fabricate - Area D	10	12-Mar-18	23-Mar-18	60
FRP Mat Foundations					
000 Event Level					
Submit					
SEA0-5NBS	Rebar Mat Foundations - Subcontractor Develop/Submit Shop Drawings - Area A	10	26-Dec-17 A	29-Jan-18 A	
SEF0-5NBS	Rebar Mat Foundations - Subcontractor Develop/Submit Shop Drawings - Area F	10	25-Jan-18 A	06-Feb-18 A	
SEB0-5NBS	Rebar Mat Foundations - Subcontractor Develop/Submit Shop Drawings - Area B	13	07-Feb-18 A	26-Feb-18 A	
SEE0-5NBS	Rebar Mat Foundations - Subcontractor Develop/Submit Shop Drawings - Area E	10	19-Feb-18 A	12-Mar-18	15
SEC0-5NBS	Rebar Mat Foundations - Subcontractor Develop/Submit Shop Drawings - Area C	10	06-Mar-18	19-Mar-18	51
SED0-5NBS	Rebar Mat Foundations - Subcontractor Develop/Submit Shop Drawings - Area D	10	13-Mar-18	26-Mar-18	51
Mortenson Review					
SEA0-5NBS1	Rebar Mat Foundations - MMCJV Review Shop Drawings - Area A	2	30-Jan-18 A	01-Feb-18 A	
SEF0-5NBS1	Rebar Mat Foundations - MMCJV Review Shop Drawings - Area F	2	07-Feb-18 A	08-Feb-18 A	
SEB0-5NBS1	Rebar Mat Foundations - MMCJV Review Shop Drawings - Area B	2	27-Feb-18 A	28-Feb-18 A	
SEE0-5NBS1	Rebar Mat Foundations - MMCJV Review Shop Drawings - Area E	2	13-Mar-18	14-Mar-18	15

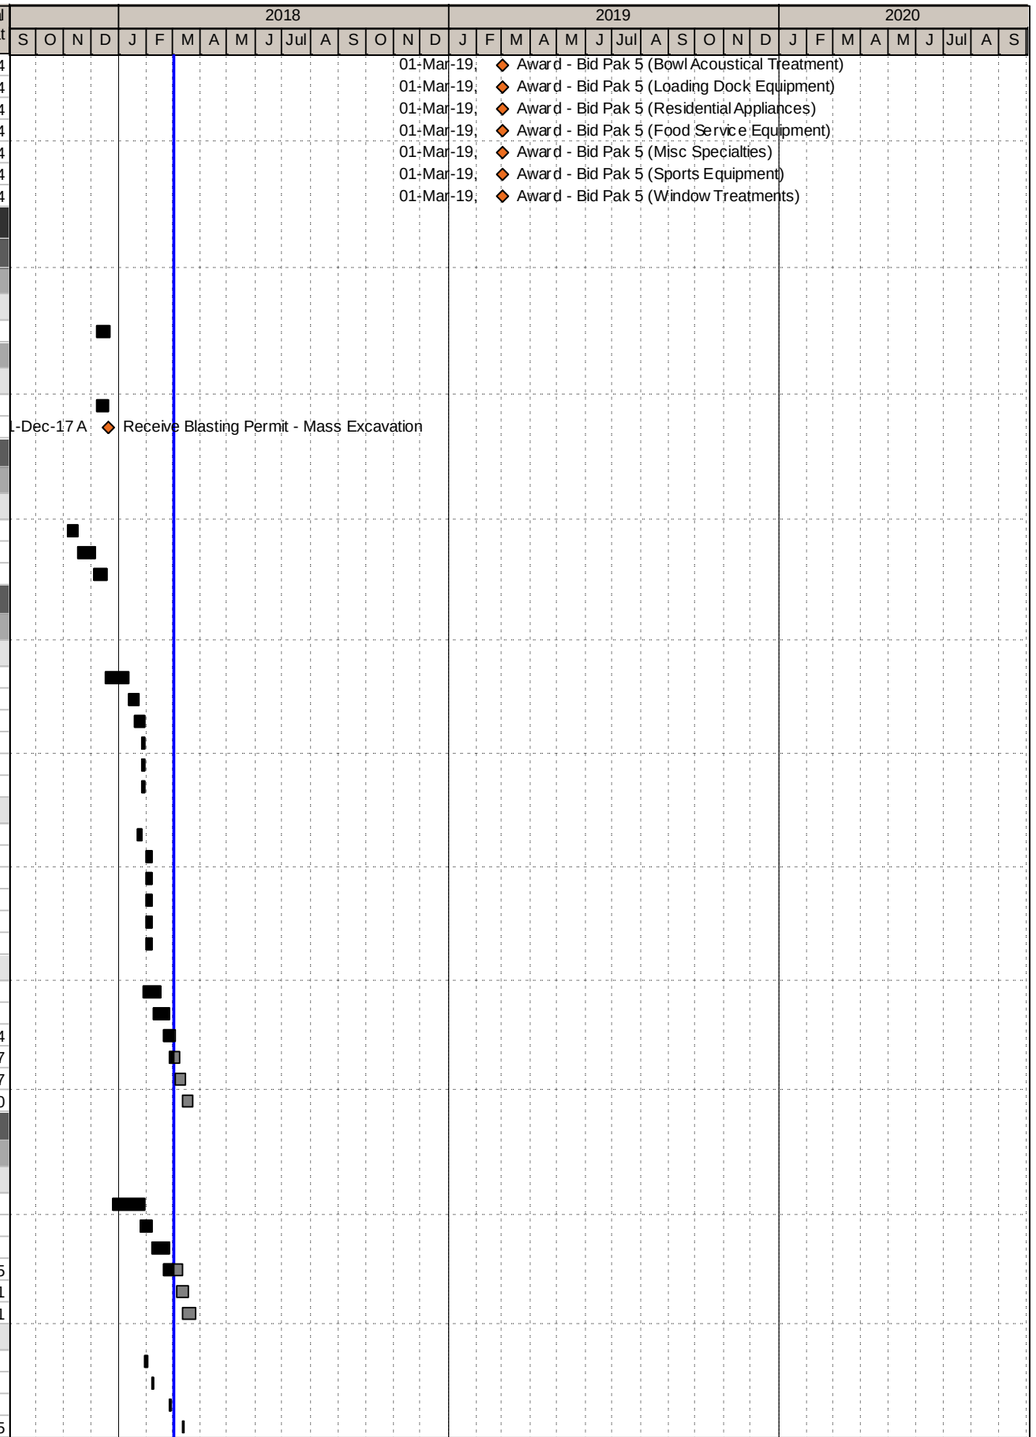

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
SEC0-5NBS1	Rebar Mat Foundations - MMCJV Review Shop Drawings - Area C	2	20-Mar-18	21-Mar-18	52
SED0-5NBS1	Rebar Mat Foundations - MMCJV Review Shop Drawings - Area D	2	27-Mar-18	28-Mar-18	51
Approve					
SEA0-5NBA	Rebar Mat Foundations - Design Team Review/Approve Shop Drawings - Area A	10	02-Feb-18 A	12-Feb-18 A	
SEF0-5NBA	Rebar Mat Foundations - Design Team Review/Approve Shop Drawings - Area F	10	09-Feb-18 A	28-Feb-18 A	
SEB0-5NBA	Rebar Mat Foundations - Design Team Review/Approve Shop Drawings - Area B	10	01-Mar-18 A	16-Mar-18	19
SEE0-5NBA	Rebar Mat Foundations - Design Team Review/Approve Shop Drawings - Area E	10	15-Mar-18	28-Mar-18	15
SEC0-5NBA	Rebar Mat Foundations - Design Team Review/Approve Shop Drawings - Area C	10	22-Mar-18	04-Apr-18	52
SED0-5NBA	Rebar Mat Foundations - Design Team Review/Approve Shop Drawings - Area D	10	29-Mar-18	11-Apr-18	51
Fabricate					
SEA3-5NBF	Rebar Mat Foundations - Fabricate - Area A3	5	06-Mar-18	12-Mar-18	3
SEF3-5NBF	Rebar Mat Foundations - Fabricate - Area F3	5	08-Mar-18	14-Mar-18	3
SEA1-5NBF	Rebar Mat Foundations - Fabricate - Area A1	5	09-Mar-18	15-Mar-18	3
SEF1-5NBF	Rebar Mat Foundations - Fabricate - Area F1	5	13-Mar-18	19-Mar-18	3
SEA2-5NBF	Rebar Mat Foundations - Fabricate - Area A2	5	14-Mar-18	20-Mar-18	4
SEF2-5NBF	Rebar Mat Foundations - Fabricate - Area F2	5	16-Mar-18	22-Mar-18	4
SEA4-5NBF	Rebar Mat Foundations - Fabricate - Area A4	5	19-Mar-18	23-Mar-18	14
SEF4-5NBF	Rebar Mat Foundations - Fabricate - Area F4	5	21-Mar-18	27-Mar-18	11
SEB2-5NBF	Rebar Mat Foundations - Fabricate - Area B2	5	22-Mar-18	28-Mar-18	16
SEB1-5NBF	Rebar Mat Foundations - Fabricate - Area B1	5	27-Mar-18	02-Apr-18	16
SEB3-5NBF	Rebar Mat Foundations - Fabricate - Area B3	5	30-Mar-18	05-Apr-18	20
SEE2-5NBF	Rebar Mat Foundations - Fabricate - Area E2	5	02-Apr-18	06-Apr-18	13
SEB5-5NBF	Rebar Mat Foundations - Fabricate - Area B5	5	04-Apr-18	10-Apr-18	28
SEE1-5NBF	Rebar Mat Foundations - Fabricate - Area E1	5	05-Apr-18	11-Apr-18	13
SEB4-5NBF	Rebar Mat Foundations - Fabricate - Area B4	5	09-Apr-18	13-Apr-18	28
SEB6-5NBF	Rebar Mat Foundations - Fabricate - Area B6	5	12-Apr-18	18-Apr-18	43
SEE3-5NBF	Rebar Mat Foundations - Fabricate - Area E3	5	13-Apr-18	19-Apr-18	14
SEC1-5NBF	Rebar Mat Foundations - Fabricate - Area C1	5	17-Apr-18	23-Apr-18	44
SEE5-5NBF	Rebar Mat Foundations - Fabricate - Area E5	5	18-Apr-18	24-Apr-18	16
SEC2-5NBF	Rebar Mat Foundations - Fabricate - Area C2	5	20-Apr-18	26-Apr-18	48
SEE4-5NBF	Rebar Mat Foundations - Fabricate - Area E4	5	23-Apr-18	27-Apr-18	16
SEC3-5NBF	Rebar Mat Foundations - Fabricate - Area C3	5	25-Apr-18	01-May-18	48
SEE6-5NBF	Rebar Mat Foundations - Fabricate - Area E6	5	26-Apr-18	02-May-18	31
SEC4-5NBF	Rebar Mat Foundations - Fabricate - Area C4	5	30-Apr-18	04-May-18	48
SED1-5NBF	Rebar Mat Foundations - Fabricate - Area D1	5	01-May-18	07-May-18	38
SED2-5NBF	Rebar Mat Foundations - Fabricate - Area D2	5	04-May-18	10-May-18	43
SED3-5NBF	Rebar Mat Foundations - Fabricate - Area D3	5	09-May-18	15-May-18	43
SED4-5NBF	Rebar Mat Foundations - Fabricate - Area D4	5	14-May-18	18-May-18	43
FRP Spread Footings					
000 Event Level					
Submit					
SEA0-5NCS	Rebar Spread Footings - Subcontractor Develop/Submit Shop Drawings - Area A	20	02-Jan-18 A	29-Jan-18 A	
SEF0-5NCS	Rebar Spread Footings - Subcontractor Develop/Submit Shop Drawings - Area F	10	25-Jan-18 A	06-Feb-18 A	
SEB0-5NCS	Rebar Spread Footings - Subcontractor Develop/Submit Shop Drawings - Area B	13	07-Feb-18 A	26-Feb-18 A	
SEE0-5NCS	Rebar Spread Footings - Subcontractor Develop/Submit Shop Drawings - Area E	10	19-Feb-18 A	12-Mar-18	18
SEC0-5NCS	Rebar Spread Footings - Subcontractor Develop/Submit Shop Drawings - Area C	10	06-Mar-18	19-Mar-18	54
SED0-5NCS	Rebar Spread Footings - Subcontractor Develop/Submit Shop Drawings - Area D	10	13-Mar-18	26-Mar-18	54
Mortenson Review					
SEA0-5NCS1	Rebar Spread Footings - MMCJV Review Shop Drawings - Area A	2	30-Jan-18 A	31-Jan-18 A	
SEF0-5NCS1	Rebar Spread Footings - MMCJV Review Shop Drawings - Area F	2	07-Feb-18 A	08-Feb-18 A	
SEB0-5NCS1	Rebar Spread Footings - MMCJV Review Shop Drawings - Area B	2	27-Feb-18 A	01-Mar-18 A	
SEE0-5NCS1	Rebar Spread Footings - MMCJV Review Shop Drawings - Area E	2	13-Mar-18	14-Mar-18	18
SEC0-5NCS1	Rebar Spread Footings - MMCJV Review Shop Drawings - Area C	2	20-Mar-18	21-Mar-18	57
SED0-5NCS1	Rebar Spread Footings - MMCJV Review Shop Drawings - Area D	2	27-Mar-18	28-Mar-18	54
Approve					
SEA0-5NCA	Rebar Spread Footings - Design Team Review/Approve Shop Drawings - Area A	10	02-Feb-18 A	12-Feb-18 A	
SEF0-5NCA	Rebar Spread Footings - Design Team Review/Approve Shop Drawings - Area F	10	09-Feb-18 A	28-Feb-18 A	
SEB0-5NCA	Rebar Spread Footings - Design Team Review/Approve Shop Drawings - Area B	10	02-Mar-18 A	15-Mar-18	22
SEE0-5NCA	Rebar Spread Footings - Design Team Review/Approve Shop Drawings - Area E	10	15-Mar-18	28-Mar-18	18
SEC0-5NCA	Rebar Spread Footings - Design Team Review/Approve Shop Drawings - Area C	10	22-Mar-18	04-Apr-18	57
SED0-5NCA	Rebar Spread Footings - Design Team Review/Approve Shop Drawings - Area D	10	29-Mar-18	11-Apr-18	54
Fabricate					

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
SEA0-5NCF	Rebar Spread Footings - Fabricate - Area A1	5	12-Mar-18	16-Mar-18	4
SEF0-5NCF	Rebar Spread Footings - Fabricate - Area F1	5	12-Mar-18	16-Mar-18	4
SEA0-5NCF1	Rebar Spread Footings - Fabricate - Area A2	5	19-Mar-18	23-Mar-18	11
SEF0-5NCF1	Rebar Spread Footings - Fabricate - Area F2	5	20-Mar-18	26-Mar-18	11
SEA0-5NCF2	Rebar Spread Footings - Fabricate - Area A3	5	26-Mar-18	30-Mar-18	11
SEF0-5NCF2	Rebar Spread Footings - Fabricate - Area F3	5	27-Mar-18	02-Apr-18	12
SEB0-5NCF	Rebar Spread Footings - Fabricate - Area B1	5	02-Apr-18	06-Apr-18	11
SEF0-5NCF3	Rebar Spread Footings - Fabricate - Area F4	5	02-Apr-18	06-Apr-18	12
SEE0-5NCF	Rebar Spread Footings - Fabricate - Area E1	5	06-Apr-18	12-Apr-18	12
SEB0-5NCF1	Rebar Spread Footings - Fabricate - Area B2	5	09-Apr-18	13-Apr-18	22
SEE0-5NCF1	Rebar Spread Footings - Fabricate - Area E2	5	13-Apr-18	19-Apr-18	24
SEB0-5NCF2	Rebar Spread Footings - Fabricate - Area B3	5	17-Apr-18	23-Apr-18	34
SEE0-5NCF2	Rebar Spread Footings - Fabricate - Area E3	5	20-Apr-18	26-Apr-18	27
SEB0-5NCF3	Rebar Spread Footings - Fabricate - Area B4	5	23-Apr-18	27-Apr-18	34
SEE0-5NCF3	Rebar Spread Footings - Fabricate - Area E4	5	27-Apr-18	03-May-18	32
SEB0-5NCF4	Rebar Spread Footings - Fabricate - Area B5	5	01-May-18	07-May-18	34
SEE0-5NCF4	Rebar Spread Footings - Fabricate - Area E5	5	07-May-18	11-May-18	32
SEC0-5NCF	Rebar Spread Footings - Fabricate - Area C1	5	08-May-18	14-May-18	34
SED0-5NCF	Rebar Spread Footings - Fabricate - Area D1	5	14-May-18	18-May-18	32
SEC0-5NCF1	Rebar Spread Footings - Fabricate - Area C2	5	17-May-18	23-May-18	34
SED0-5NCF1	Rebar Spread Footings - Fabricate - Area D2	5	23-May-18	30-May-18	34
SEC0-5NCF2	Rebar Spread Footings - Fabricate - Area C3	5	25-May-18	01-Jun-18	34
SED0-5NCF2	Rebar Spread Footings - Fabricate - Area D3	5	01-Jun-18	07-Jun-18	34
Foundation Walls					
000 Event Level					
Submit					
SEA0-5N3S	Rebar Foundation Walls - Subcontractor Develop/Submit Shop Drawings - Area A	10	16-Feb-18 A	12-Mar-18	4
SEF0-5N3S	Rebar Foundation Walls - Subcontractor Develop/Submit Shop Drawings - Area F	10	22-Feb-18 A	14-Mar-18	4
SEB0-5N3S	Rebar Foundation Walls - Subcontractor Develop/Submit Shop Drawings - Area B	10	13-Mar-18	26-Mar-18	10
SEE0-5N3S	Rebar Foundation Walls - Subcontractor Develop/Submit Shop Drawings - Area E	10	21-Mar-18	03-Apr-18	10
SEC0-5N3S	Rebar Foundation Walls - Subcontractor Develop/Submit Shop Drawings - Area C	10	04-Apr-18	17-Apr-18	34
SED0-5N3S	Rebar Foundation Walls - Subcontractor Develop/Submit Shop Drawings - Area D	10	18-Apr-18	01-May-18	34
Mortenson Review					
SEA0-5N3S1	Rebar Foundation Walls - MMCJV Review Shop Drawings - Area A	1	13-Mar-18	13-Mar-18	4
SEF0-5N3S1	Rebar Foundation Walls - MMCJV Review Shop Drawings - Area F	1	15-Mar-18	15-Mar-18	4
SEB0-5N3S1	Rebar Foundation Walls - MMCJV Review Shop Drawings - Area B	2	27-Mar-18	28-Mar-18	12
SEE0-5N3S1	Rebar Foundation Walls - MMCJV Review Shop Drawings - Area E	2	04-Apr-18	05-Apr-18	10
SEC0-5N3S1	Rebar Foundation Walls - MMCJV Review Shop Drawings - Area C	2	18-Apr-18	19-Apr-18	40
SED0-5N3S1	Rebar Foundation Walls - MMCJV Review Shop Drawings - Area D	2	02-May-18	03-May-18	34
Approve					
SEA0-5N3A	Rebar Foundation Walls - Design Team Review/Approve Shop Drawings - Area A	5	14-Mar-18	20-Mar-18	4
SEF0-5N3A	Rebar Foundation Walls - Design Team Review/Approve Shop Drawings - Area F	5	16-Mar-18	22-Mar-18	4
SEB0-5N3A	Rebar Foundation Walls - Design Team Review/Approve Shop Drawings - Area B	10	29-Mar-18	11-Apr-18	12
SEE0-5N3A	Rebar Foundation Walls - Design Team Review/Approve Shop Drawings - Area E	10	06-Apr-18	19-Apr-18	10
SEC0-5N3A	Rebar Foundation Walls - Design Team Review/Approve Shop Drawings - Area C	10	20-Apr-18	03-May-18	40
SED0-5N3A	Rebar Foundation Walls - Design Team Review/Approve Shop Drawings - Area D	10	04-May-18	17-May-18	34
Fabricate					
SEA0-5N3F	Rebar Foundation Walls - Fabricate - Area A1	5	22-Mar-18	28-Mar-18	3
SEF0-5N3F	Rebar Foundation Walls - Fabricate - Area F1	5	26-Mar-18	30-Mar-18	3
SEA0-5N3F1	Rebar Foundation Walls - Fabricate - Area A2	5	26-Mar-18	30-Mar-18	4
SEF0-5N3F1	Rebar Foundation Walls - Fabricate - Area F2	5	28-Mar-18	03-Apr-18	4
SEA0-5N3F2	Rebar Foundation Walls - Fabricate - Area A3	5	03-Apr-18	09-Apr-18	6
SEF0-5N3F2	Rebar Foundation Walls - Fabricate - Area F3	5	05-Apr-18	11-Apr-18	5
SEA0-5N3F3	Rebar Foundation Walls - Fabricate - Area A4	5	09-Apr-18	13-Apr-18	7
SEF0-5N3F3	Rebar Foundation Walls - Fabricate - Area F4	5	10-Apr-18	16-Apr-18	5
SEA0-5N3F4	Rebar Foundation Walls - Fabricate - Area A5	5	16-Apr-18	20-Apr-18	5
SEF0-5N3F4	Rebar Foundation Walls - Fabricate - Area F5	5	17-Apr-18	23-Apr-18	8
SEB0-5N3F	Rebar Foundation Walls - Fabricate - Area B1	5	23-Apr-18	27-Apr-18	5
SEE0-5N3F	Rebar Foundation Walls - Fabricate - Area E1	5	23-Apr-18	27-Apr-18	9
SEB0-5N3F1	Rebar Foundation Walls - Fabricate - Area B2	5	27-Apr-18	03-May-18	4
SEE0-5N3F1	Rebar Foundation Walls - Fabricate - Area E2	5	30-Apr-18	04-May-18	7
SEB0-5N3F2	Rebar Foundation Walls - Fabricate - Area B3	5	03-May-18	09-May-18	5

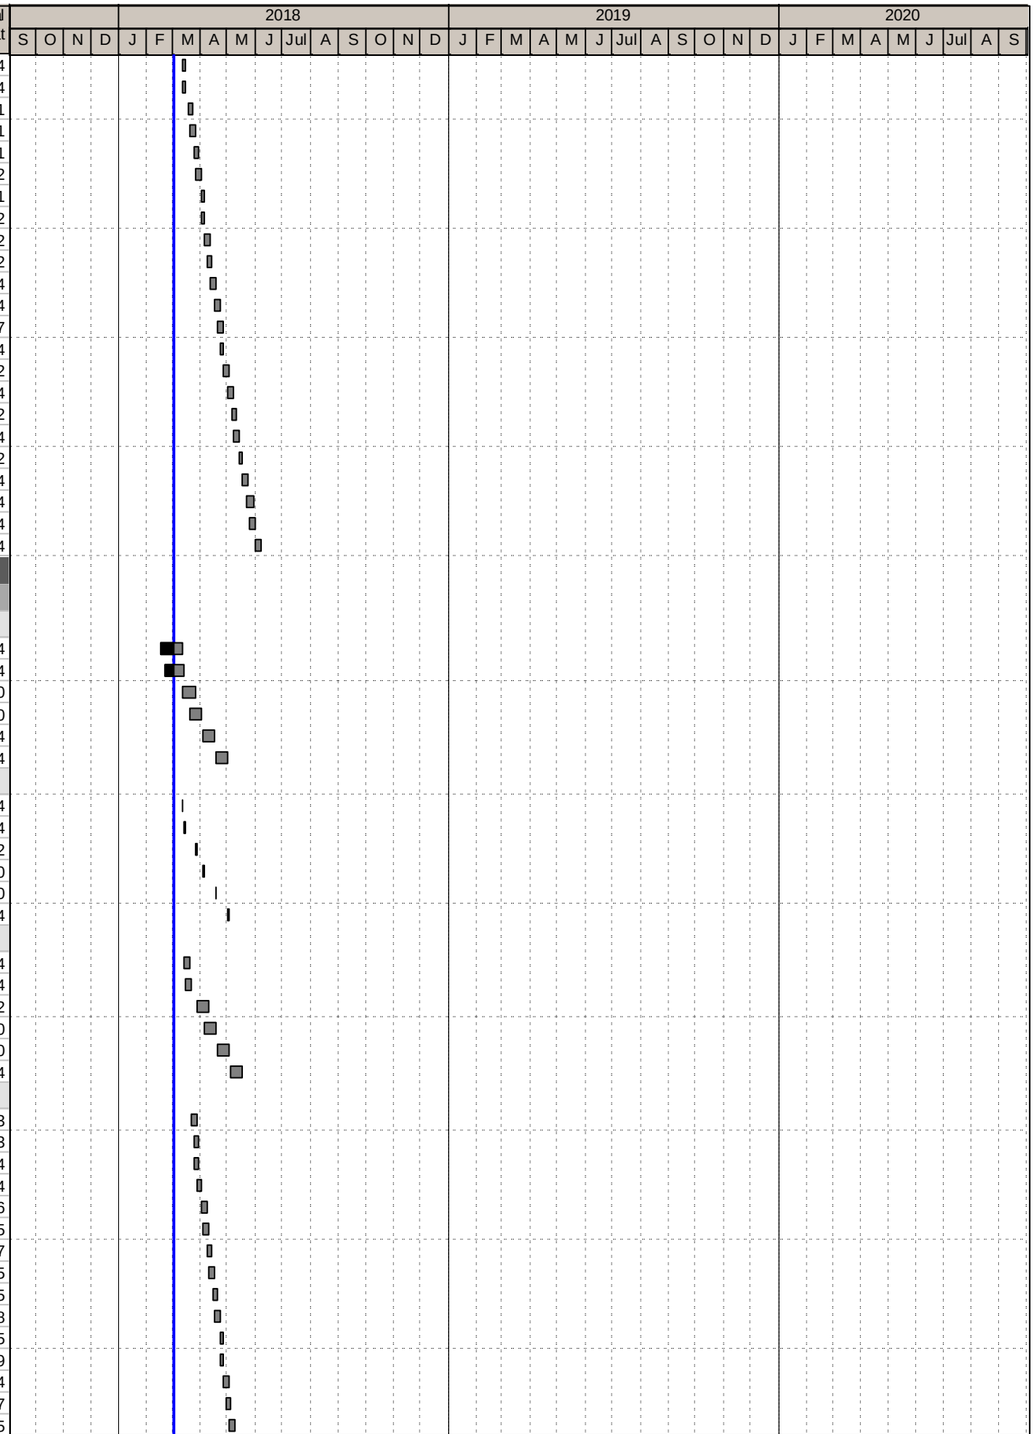

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
SEE0-5N3F2	Rebar Foundation Walls - Fabricate - Area E3	5	07-May-18	11-May-18	7
SEB0-5N3F3	Rebar Foundation Walls - Fabricate - Area B4	5	09-May-18	15-May-18	12
SEE0-5N3F3	Rebar Foundation Walls - Fabricate - Area E4	5	11-May-18	17-May-18	11
SEB0-5N3F4	Rebar Foundation Walls - Fabricate - Area B5	5	15-May-18	21-May-18	11
SEE0-5N3F4	Rebar Foundation Walls - Fabricate - Area E5	5	17-May-18	23-May-18	10
SEB0-5N3F5	Rebar Foundation Walls - Fabricate - Area B6	5	21-May-18	25-May-18	16
SEE0-5N3F5	Rebar Foundation Walls - Fabricate - Area E6	5	23-May-18	30-May-18	15
SEB0-5N3F6	Rebar Foundation Walls - Fabricate - Area B7	5	25-May-18	01-Jun-18	17
SEE0-5N3F6	Rebar Foundation Walls - Fabricate - Area E7	5	30-May-18	05-Jun-18	16
SEB0-5N3F7	Rebar Foundation Walls - Fabricate - Area B8	5	01-Jun-18	07-Jun-18	16
SEE0-5N3F7	Rebar Foundation Walls - Fabricate - Area E8	5	05-Jun-18	11-Jun-18	15
SEC0-5N3F	Rebar Foundation Walls - Fabricate - Area C1	5	07-Jun-18	13-Jun-18	17
SED0-5N3F	Rebar Foundation Walls - Fabricate - Area D1	5	11-Jun-18	15-Jun-18	19
SEC0-5N3F1	Rebar Foundation Walls - Fabricate - Area C2	5	13-Jun-18	19-Jun-18	18
SED0-5N3F1	Rebar Foundation Walls - Fabricate - Area D2	5	15-Jun-18	21-Jun-18	20
SEC0-5N3F2	Rebar Foundation Walls - Fabricate - Area C3	5	19-Jun-18	25-Jun-18	17
SED0-5N3F2	Rebar Foundation Walls - Fabricate - Area D3	5	21-Jun-18	27-Jun-18	19
SEC0-5N3F3	Rebar Foundation Walls - Fabricate - Area C4	5	25-Jun-18	29-Jun-18	58
SED0-5N3F3	Rebar Foundation Walls - Fabricate - Area D4	5	27-Jun-18	03-Jul-18	54
SEC0-5N3F4	Rebar Foundation Walls - Fabricate - Area C5	5	29-Jun-18	06-Jul-18	57
SED0-5N3F4	Rebar Foundation Walls - Fabricate - Area D5	5	03-Jul-18	10-Jul-18	53
SEC0-5N3F5	Rebar Foundation Walls - Fabricate - Area C6	5	06-Jul-18	12-Jul-18	58
SED0-5N3F5	Rebar Foundation Walls - Fabricate - Area D6	5	10-Jul-18	16-Jul-18	54
SEC0-5N3F6	Rebar Foundation Walls - Fabricate - Area C7	5	12-Jul-18	18-Jul-18	57
SED0-5N3F6	Rebar Foundation Walls - Fabricate - Area D7	5	16-Jul-18	20-Jul-18	53
Elevator Pits					
000 Event Level					
Submit					
SEA0-5P1S1	Rebar Pits - Subcontractor Develop/Submit Shop Drawings - Area A	15	05-Jan-18 A	26-Feb-18 A	
SEB0-5P1S1	Rebar Pits - Subcontractor Develop/Submit Shop Drawings - Area B	10	07-Feb-18 A	26-Feb-18 A	
SEF0-5P1S1	Rebar Pits - Subcontractor Develop/Submit Shop Drawings - Area F	10	25-Jan-18 A	26-Feb-18 A	
SEE0-5P1S1	Rebar Pits - Subcontractor Develop/Submit Shop Drawings - Area E	10	05-Mar-18	16-Mar-18	26
SEC0-5P1S1	Rebar Pits - Subcontractor Develop/Submit Shop Drawings - Area C	10	12-Mar-18	23-Mar-18	51
SED0-5P1S1	Rebar Pits - Subcontractor Develop/Submit Shop Drawings - Area D	10	19-Mar-18	30-Mar-18	51
Mortenson Review					
SEA0-5P1S2	Rebar Pits - MMCJV Review Shop Drawings - Area A	2	27-Feb-18 A	01-Mar-18 A	
SEB0-5P1S2	Rebar Pits - MMCJV Review Shop Drawings - Area B	2	27-Feb-18 A	01-Mar-18 A	
SEF0-5P1S2	Rebar Pits - MMCJV Review Shop Drawings - Area F	1	27-Feb-18 A	01-Mar-18 A	
SEE0-5P1S2	Rebar Pits - MMCJV Review Shop Drawings - Area E	2	19-Mar-18	20-Mar-18	26
SEC0-5P1S2	Rebar Pits - MMCJV Review Shop Drawings - Area C	2	26-Mar-18	27-Mar-18	56
SED0-5P1S2	Rebar Pits - MMCJV Review Shop Drawings - Area D	2	02-Apr-18	03-Apr-18	51
Approve					
SEA0-5P1A1	Rebar Pits - Design Team Review/Approve Shop Drawings - Area A	10	02-Mar-18 A	12-Mar-18	16
SEF0-5P1A1	Rebar Pits - Design Team Review/Approve Shop Drawings - Area F	10	02-Mar-18 A	13-Mar-18	17
SEB0-5P1A1	Rebar Pits - Design Team Review/Approve Shop Drawings - Area B	10	02-Mar-18 A	15-Mar-18	27
SEE0-5P1A1	Rebar Pits - Design Team Review/Approve Shop Drawings - Area E	10	21-Mar-18	03-Apr-18	26
SEC0-5P1A1	Rebar Pits - Design Team Review/Approve Shop Drawings - Area C	10	28-Mar-18	10-Apr-18	56
SED0-5P1A1	Rebar Pits - Design Team Review/Approve Shop Drawings - Area D	10	04-Apr-18	17-Apr-18	51
Fabricate					
SEA0-5P1F1	Rebar Pits - Fabricate - Area A1	8	14-Mar-18	23-Mar-18	15
SEF0-5P1F1	Rebar Pits - Fabricate - Area F1	8	15-Mar-18	26-Mar-18	16
SEB0-5P1F1	Rebar Pits - Fabricate - Area B1	8	04-Apr-18	13-Apr-18	14
SEB2-5P1F1	Rebar Pits - Fabricate - Area B5	10	03-Apr-18	16-Apr-18	74
SEB1-5P1F1	Rebar Pits - Fabricate - Area B2	10	06-Apr-18	19-Apr-18	25
SEE0-5P1F1	Rebar Pits - Fabricate - Area E2	10	11-Apr-18	24-Apr-18	21
SEE1-5P1F1	Rebar Pits - Fabricate - Area E3	10	17-Apr-18	30-Apr-18	34
SEC0-5P1F1	Rebar Pits - Fabricate - Area C	10	19-Apr-18	02-May-18	50
SED0-5P1F1	Rebar Pits - Fabricate - Area D1	10	19-Apr-18	02-May-18	50
SEE2-5P1F1	Rebar Pits - Fabricate - Area E5	10	19-Apr-18	02-May-18	61
FRP Slab on Grade					
000 Event Level					
Submit					

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
SEA0-5P1S	Rebar Slab on Grade - Subcontractor Develop/Submit Shop Drawings - Area A	20	24-Apr-18	21-May-18	57
SEF0-5P1S	Rebar Slab on Grade - Subcontractor Develop/Submit Shop Drawings - Area F	15	22-May-18	12-Jun-18	57
SEB0-5P1S	Rebar Slab on Grade - Subcontractor Develop/Submit Shop Drawings - Area B	15	13-Jun-18	03-Jul-18	57
SEE0-5P1S	Rebar Slab on Grade - Subcontractor Develop/Submit Shop Drawings - Area E	15	05-Jul-18	25-Jul-18	73
SEC0-5P1S	Rebar Slab on Grade - Subcontractor Develop/Submit Shop Drawings - Area C	15	26-Jul-18	15-Aug-18	88
SED0-5P1S	Rebar Slab on Grade - Subcontractor Develop/Submit Shop Drawings - Area D	15	16-Aug-18	06-Sep-18	104
Approve					
SEA0-5P1A	Rebar Slab on Grade - Design Team Review/Approve Shop Drawings - Area A	10	22-May-18	05-Jun-18	57
SEF0-5P1A	Rebar Slab on Grade - Design Team Review/Approve Shop Drawings - Area F	10	13-Jun-18	26-Jun-18	62
SEB0-5P1A	Rebar Slab on Grade - Design Team Review/Approve Shop Drawings - Area B	10	05-Jul-18	18-Jul-18	57
SEE0-5P1A	Rebar Slab on Grade - Design Team Review/Approve Shop Drawings - Area E	10	26-Jul-18	08-Aug-18	73
SEC0-5P1A	Rebar Slab on Grade - Design Team Review/Approve Shop Drawings - Area C	10	16-Aug-18	29-Aug-18	88
SED0-5P1A	Rebar Slab on Grade - Design Team Review/Approve Shop Drawings - Area D	10	07-Sep-18	20-Sep-18	104
Fabricate					
SEA0-5P1F	Rebar Slab on Grade - Fabricate - Area A	10	06-Jun-18	19-Jun-18	57
SEF0-5P1F	Rebar Slab on Grade - Fabricate - Area F	10	27-Jun-18	11-Jul-18	62
SEB0-5P1F	Rebar Slab on Grade - Fabricate - Area B	10	19-Jul-18	01-Aug-18	57
SEE0-5P1F	Rebar Slab on Grade - Fabricate - Area E	10	09-Aug-18	22-Aug-18	73
SEC0-5P1F	Rebar Slab on Grade - Fabricate - Area C	10	30-Aug-18	13-Sep-18	88
SED0-5P1F	Rebar Slab on Grade - Fabricate - Area D	10	21-Sep-18	04-Oct-18	104
FRP Concrete Walls					
000 Event Level					
Submit					
SEA0-5P2BS	Rebar Concrete Core Walls - Subcontractor Develop/Submit Shop Drawings - Core 3 Event to Mezz	10	19-Feb-18 A	09-Mar-18	16
SEF0-5P2BS	Rebar Concrete Core Walls - Subcontractor Develop/Submit Shop Drawings - Core 2 Event to Mezz	10	19-Feb-18 A	14-Mar-18	14
SEB0-5P2BS	Rebar Concrete Core Walls - Subcontractor Develop/Submit Shop Drawings - Core 4 Event to Mezz	10	13-Mar-18	26-Mar-18	22
SEB1-5P2BS	Rebar Concrete Core Walls - Subcontractor Develop/Submit Shop Drawings - Core 5 Event to Mezz	10	20-Mar-18	02-Apr-18	33
SEE1-5P2BS	Rebar Concrete Core Walls - Subcontractor Develop/Submit Shop Drawings - Core 1 Event to Mezz	10	20-Mar-18	02-Apr-18	22
SEE0-5P2BS	Rebar Concrete Core Walls - Subcontractor Develop/Submit Shop Drawings - Core 8 Event to Mezz	10	28-Mar-18	10-Apr-18	33
SEC0-5P2BS	Rebar Concrete Core Walls - Subcontractor Develop/Submit Shop Drawings - Core 6 Event to Mezz	10	10-Apr-18	23-Apr-18	49
SED0-5P2BS	Rebar Concrete Core Walls - Subcontractor Develop/Submit Shop Drawings - Core 7 Event to Mezz	10	17-Apr-18	30-Apr-18	49
Mortenson Review					
SEA0-5P2BS1	Rebar Concrete Core Walls - MMCJV Review Shop Drawings - Core 3 Event to Mezz	1	12-Mar-18	12-Mar-18	16
SEF0-5P2BS1	Rebar Concrete Core Walls - MMCJV Review Shop Drawings - Core 2 Event to Mezz	1	15-Mar-18	15-Mar-18	14
SEB0-5P2BS1	Rebar Concrete Core Walls - MMCJV Review Shop Drawings - Core 4 Event to Mezz	1	27-Mar-18	27-Mar-18	23
SEE1-5P2BS1	Rebar Concrete Core Walls - MMCJV Review Shop Drawings - Core 1 Event to Mezz	1	03-Apr-18	03-Apr-18	22
SEB1-5P2BS1	Rebar Concrete Core Walls - MMCJV Review Shop Drawings - Core 5 Event to Mezz	2	03-Apr-18	04-Apr-18	35
SEE0-5P2BS1	Rebar Concrete Core Walls - MMCJV Review Shop Drawings - Core 8 Event to Mezz	2	11-Apr-18	12-Apr-18	33
SEC0-5P2BS1	Rebar Concrete Core Walls - MMCJV Review Shop Drawings - Core 6 Event to Mezz	2	24-Apr-18	25-Apr-18	49
SED0-5P2BS1	Rebar Concrete Core Walls - MMCJV Review Shop Drawings - Core 7 Event to Mezz	2	01-May-18	02-May-18	49
Approve					
SEA0-5P2BA	Rebar Concrete Core Walls - Design Team Review/Approve Shop Drawings - Core 3 Event to Mezz	5	13-Mar-18	19-Mar-18	16
SEF0-5P2BA	Rebar Concrete Core Walls - Design Team Review/Approve Shop Drawings - Core 2 Event to Mezz	5	16-Mar-18	22-Mar-18	14
SEB0-5P2BA	Rebar Concrete Core Walls - Design Team Review/Approve Shop Drawings - Core 4 Event to Mezz	5	28-Mar-18	03-Apr-18	23
SEE1-5P2BA	Rebar Concrete Core Walls - Design Team Review/Approve Shop Drawings - Core 1 Event to Mezz	5	04-Apr-18	10-Apr-18	22
SEB1-5P2BA	Rebar Concrete Core Walls - Design Team Review/Approve Shop Drawings - Core 5 Event to Mezz	10	05-Apr-18	18-Apr-18	35
SEE0-5P2BA	Rebar Concrete Core Walls - Design Team Review/Approve Shop Drawings - Core 8 Event to Mezz	10	13-Apr-18	26-Apr-18	33
SEC0-5P2BA	Rebar Concrete Core Walls - Design Team Review/Approve Shop Drawings - Core 6 Event to Mezz	10	26-Apr-18	09-May-18	49
SED0-5P2BA	Rebar Concrete Core Walls - Design Team Review/Approve Shop Drawings - Core 7 Event to Mezz	10	03-May-18	16-May-18	49
Fabricate					
SEA0-5P2BF	Rebar Concrete Core Walls - Fabricate - Core 3 Event to Mezz	5	21-Mar-18	27-Mar-18	15
SEF0-5P2BF	Rebar Concrete Core Walls - Fabricate - Core 2 Event to Mezz	5	26-Mar-18	30-Mar-18	13
SEB0-5P2BF	Rebar Concrete Core Walls - Fabricate - Core 4 Event to Mezz	5	10-Apr-18	16-Apr-18	19
SEE1-5P2BF	Rebar Concrete Core Walls - Fabricate - Core 1 Event to Mezz	5	13-Apr-18	19-Apr-18	20
SEB1-5P2BF	Rebar Concrete Core Walls - Fabricate - Core 5 Event to Mezz	5	24-Apr-18	30-Apr-18	32
SEE0-5P2BF	Rebar Concrete Core Walls - Fabricate - Core 8 Event to Mezz	5	01-May-18	07-May-18	31
SEC0-5P2BF	Rebar Concrete Core Walls - Fabricate - Core 6 Event to Mezz	5	11-May-18	17-May-18	48
SED0-5P2BF	Rebar Concrete Core Walls - Fabricate - Core 7 Event to Mezz	5	25-May-18	01-Jun-18	43
050 Lower Mezz Level					
Submit					
S2A0-5P2BS	Rebar Concrete Core Walls - Subcontractor Develop/Submit Shop Drawings - Core 3 Mezz to Main	20	09-Mar-18	05-Apr-18	16

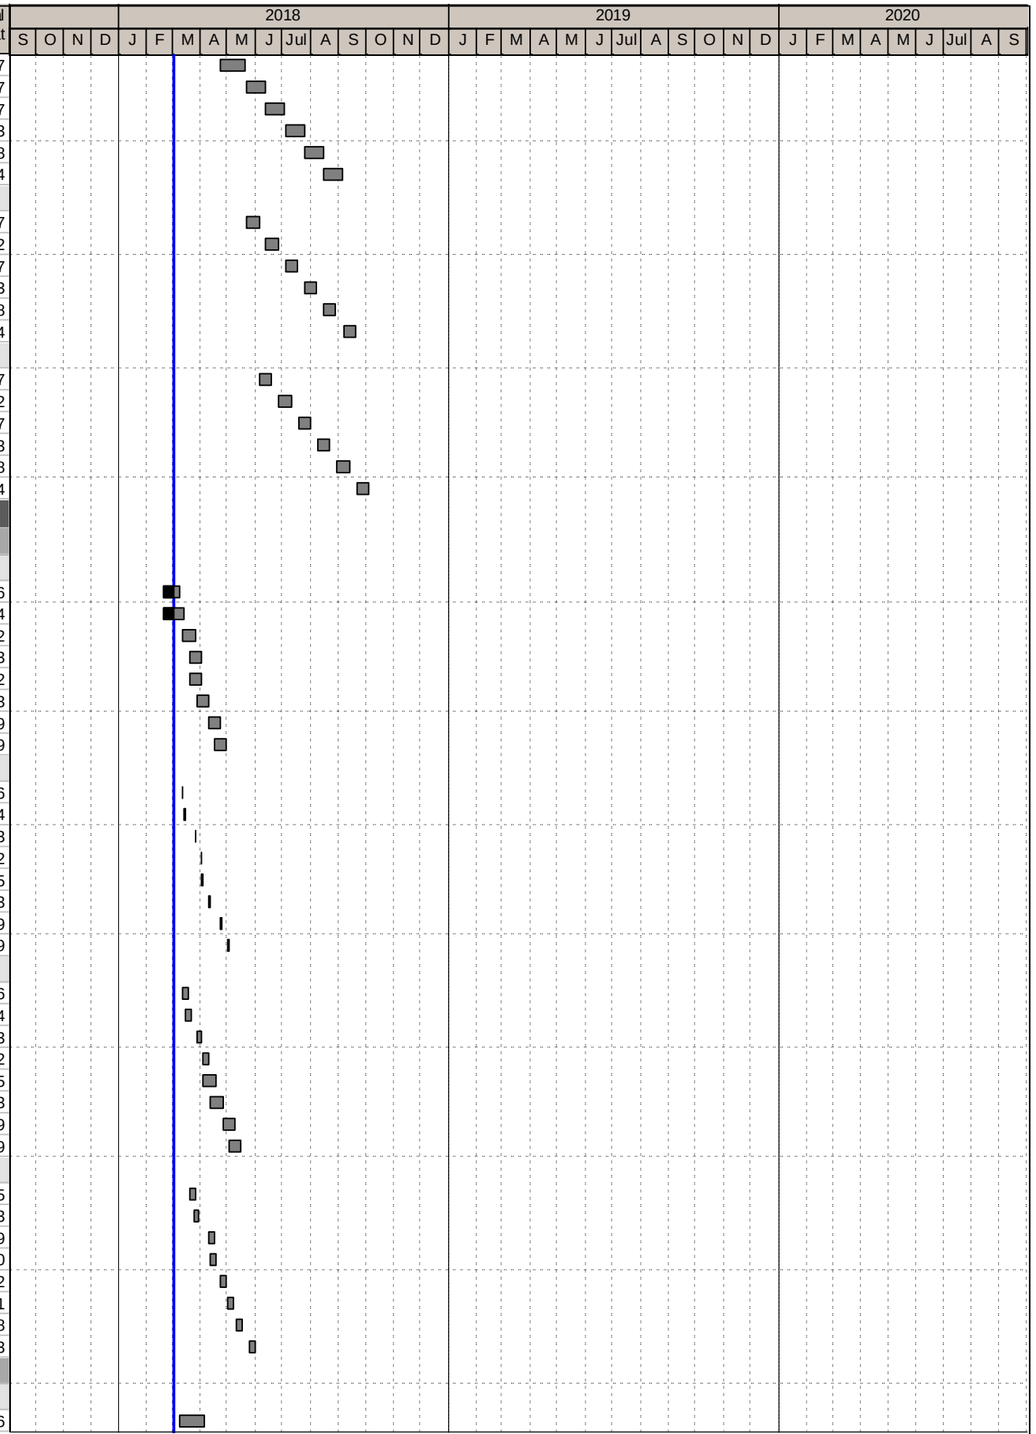

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S2F0-5P2BS	Rebar Concrete Core Walls - Subcontractor Develop/Submit Shop Drawings - Core 2 Mezz to Main	10	30-Mar-18	12-Apr-18	16
S2B0-5P2BS	Rebar Concrete Core Walls - Subcontractor Develop/Submit Shop Drawings - Core 4 Mezz to Main	10	13-Apr-18	26-Apr-18	20
S2E1-5P2BS	Rebar Concrete Core Walls - Subcontractor Develop/Submit Shop Drawings - Core 1 Mezz to Main	10	20-Apr-18	03-May-18	20
S2B1-5P2BS	Rebar Concrete Core Walls - Subcontractor Develop/Submit Shop Drawings - Core 5 Mezz to Main	10	04-May-18	17-May-18	32
S2E0-5P2BS	Rebar Concrete Core Walls - Subcontractor Develop/Submit Shop Drawings - Core 8 Mezz to Main	10	11-May-18	24-May-18	32
S2C0-5P2BS	Rebar Concrete Core Walls - Subcontractor Develop/Submit Shop Drawings - Core 6 Mezz to Main	10	25-May-18	08-Jun-18	43
S2D0-5P2BS	Rebar Concrete Core Walls - Subcontractor Develop/Submit Shop Drawings - Core 7 Mezz to Main	10	04-Jun-18	15-Jun-18	43
Mortenson Review					
S2A0-5P2BS1	Rebar Concrete Core Walls - MMCJV Review Shop Drawings - Core 3 Mezz to Main	2	06-Apr-18	09-Apr-18	19
S2F0-5P2BS1	Rebar Concrete Core Walls - MMCJV Review Shop Drawings - Core 2 Mezz to Main	2	13-Apr-18	16-Apr-18	16
S2B0-5P2BS1	Rebar Concrete Core Walls - MMCJV Review Shop Drawings - Core 4 Mezz to Main	2	27-Apr-18	30-Apr-18	21
S2E1-5P2BS1	Rebar Concrete Core Walls - MMCJV Review Shop Drawings - Core 1 Mezz to Main	2	04-May-18	07-May-18	20
S2B1-5P2BS1	Rebar Concrete Core Walls - MMCJV Review Shop Drawings - Core 5 Mezz to Main	2	18-May-18	21-May-18	37
S2E0-5P2BS1	Rebar Concrete Core Walls - MMCJV Review Shop Drawings - Core 8 Mezz to Main	2	25-May-18	29-May-18	32
S2C0-5P2BS1	Rebar Concrete Core Walls - MMCJV Review Shop Drawings - Core 6 Mezz to Main	2	11-Jun-18	12-Jun-18	44
S2D0-5P2BS1	Rebar Concrete Core Walls - MMCJV Review Shop Drawings - Core 7 Mezz to Main	2	18-Jun-18	19-Jun-18	43
Approve					
S2A0-5P2BA	Rebar Concrete Core Walls - Design Team Review/Approve Shop Drawings - Core 3 Mezz to Main	10	10-Apr-18	23-Apr-18	19
S2F0-5P2BA	Rebar Concrete Core Walls - Design Team Review/Approve Shop Drawings - Core 2 Mezz to Main	10	17-Apr-18	30-Apr-18	16
S2B0-5P2BA	Rebar Concrete Core Walls - Design Team Review/Approve Shop Drawings - Core 4 Mezz to Main	10	01-May-18	14-May-18	21
S2E1-5P2BA	Rebar Concrete Core Walls - Design Team Review/Approve Shop Drawings - Core 1 Mezz to Main	10	08-May-18	21-May-18	20
S2B1-5P2BA	Rebar Concrete Core Walls - Design Team Review/Approve Shop Drawings - Core 5 Mezz to Main	10	22-May-18	05-Jun-18	37
S2E0-5P2BA	Rebar Concrete Core Walls - Design Team Review/Approve Shop Drawings - Core 8 Mezz to Main	10	30-May-18	12-Jun-18	32
S2C0-5P2BA	Rebar Concrete Core Walls - Design Team Review/Approve Shop Drawings - Core 6 Mezz to Main	10	13-Jun-18	26-Jun-18	44
S2D0-5P2BA	Rebar Concrete Core Walls - Design Team Review/Approve Shop Drawings - Core 7 Mezz to Main	10	20-Jun-18	03-Jul-18	43
Fabricate					
S2A0-5P2BF	Rebar Concrete Core Walls - Fabricate - Core 3 Mezz to Main	5	14-May-18	18-May-18	5
S2F0-5P2BF	Rebar Concrete Core Walls - Fabricate - Core 2 Mezz to Main	5	17-May-18	23-May-18	4
S2B0-5P2BF	Rebar Concrete Core Walls - Fabricate - Core 4 Mezz to Main	5	08-Jun-18	14-Jun-18	4
S2E1-5P2BF	Rebar Concrete Core Walls - Fabricate - Core 1 Mezz to Main	5	08-Jun-18	14-Jun-18	8
S2B1-5P2BF	Rebar Concrete Core Walls - Fabricate - Core 5 Mezz to Main	5	06-Jul-18	12-Jul-18	16
S2E0-5P2BF	Rebar Concrete Core Walls - Fabricate - Core 8 Mezz to Main	5	09-Jul-18	13-Jul-18	15
S2C0-5P2BF	Rebar Concrete Core Walls - Fabricate - Core 6 Mezz to Main	5	01-Aug-18	07-Aug-18	20
S2D0-5P2BF	Rebar Concrete Core Walls - Fabricate - Core 7 Mezz to Main	5	02-Aug-18	08-Aug-18	23
100 Main Concourse					
Submit					
S3A0-5P2BS	Rebar Concrete Core Walls - Subcontractor Develop/Submit Shop Drawings - Core 3 Main to TOC	20	06-Apr-18	03-May-18	32
S3F0-5P2BS	Rebar Concrete Core Walls - Subcontractor Develop/Submit Shop Drawings - Core 2 Main to TOC	10	27-Apr-18	10-May-18	33
S3B0-5P2BS	Rebar Concrete Core Walls - Subcontractor Develop/Submit Shop Drawings - Core 4 Main to TOC	10	11-May-18	24-May-18	33
S3E1-5P2BS	Rebar Concrete Core Walls - Subcontractor Develop/Submit Shop Drawings - Core 1 Main to TOC	10	18-May-18	01-Jun-18	33
S3B1-5P2BS	Rebar Concrete Core Walls - Subcontractor Develop/Submit Shop Drawings - Core 5 Main to TOC	10	04-Jun-18	15-Jun-18	50
S3E0-5P2BS	Rebar Concrete Core Walls - Subcontractor Develop/Submit Shop Drawings - Core 8 Main to TOC	10	11-Jun-18	22-Jun-18	50
S3C0-5P2BS	Rebar Concrete Core Walls - Subcontractor Develop/Submit Shop Drawings - Core 6 Main to TOC	10	25-Jun-18	09-Jul-18	51
S3D0-5P2BS	Rebar Concrete Core Walls - Subcontractor Develop/Submit Shop Drawings - Core 7 Main to TOC	10	02-Jul-18	16-Jul-18	60
Mortenson Review					
S3A0-5P2BS1	Rebar Concrete Core Walls - MMCJV Review Shop Drawings - Core 3 Main to TOC	2	04-May-18	07-May-18	32
S3F0-5P2BS1	Rebar Concrete Core Walls - MMCJV Review Shop Drawings - Core 2 Main to TOC	2	11-May-18	14-May-18	42
S3B0-5P2BS1	Rebar Concrete Core Walls - MMCJV Review Shop Drawings - Core 4 Main to TOC	2	25-May-18	29-May-18	39
S3E1-5P2BS1	Rebar Concrete Core Walls - MMCJV Review Shop Drawings - Core 1 Main to TOC	2	04-Jun-18	05-Jun-18	33
S3B1-5P2BS1	Rebar Concrete Core Walls - MMCJV Review Shop Drawings - Core 5 Main to TOC	2	18-Jun-18	19-Jun-18	53
S3E0-5P2BS1	Rebar Concrete Core Walls - MMCJV Review Shop Drawings - Core 8 Main to TOC	2	25-Jun-18	26-Jun-18	50
S3C0-5P2BS1	Rebar Concrete Core Walls - MMCJV Review Shop Drawings - Core 6 Main to TOC	2	10-Jul-18	11-Jul-18	51
S3D0-5P2BS1	Rebar Concrete Core Walls - MMCJV Review Shop Drawings - Core 7 Main to TOC	2	17-Jul-18	18-Jul-18	60
Approve					
S3A0-5P2BA	Rebar Concrete Core Walls - Design Team Review/Approve Shop Drawings - Core 3 Main to TOC	10	08-May-18	21-May-18	32
S3F0-5P2BA	Rebar Concrete Core Walls - Design Team Review/Approve Shop Drawings - Core 2 Main to TOC	10	15-May-18	29-May-18	42
S3B0-5P2BA	Rebar Concrete Core Walls - Design Team Review/Approve Shop Drawings - Core 4 Main to TOC	10	30-May-18	12-Jun-18	39
S3E1-5P2BA	Rebar Concrete Core Walls - Design Team Review/Approve Shop Drawings - Core 1 Main to TOC	10	06-Jun-18	19-Jun-18	33
S3B1-5P2BA	Rebar Concrete Core Walls - Design Team Review/Approve Shop Drawings - Core 5 Main to TOC	10	20-Jun-18	03-Jul-18	53
S3E0-5P2BA	Rebar Concrete Core Walls - Design Team Review/Approve Shop Drawings - Core 8 Main to TOC	10	27-Jun-18	11-Jul-18	50
S3C0-5P2BA	Rebar Concrete Core Walls - Design Team Review/Approve Shop Drawings - Core 6 Main to TOC	10	12-Jul-18	25-Jul-18	51
S3D0-5P2BA	Rebar Concrete Core Walls - Design Team Review/Approve Shop Drawings - Core 7 Main to TOC	10	19-Jul-18	01-Aug-18	60

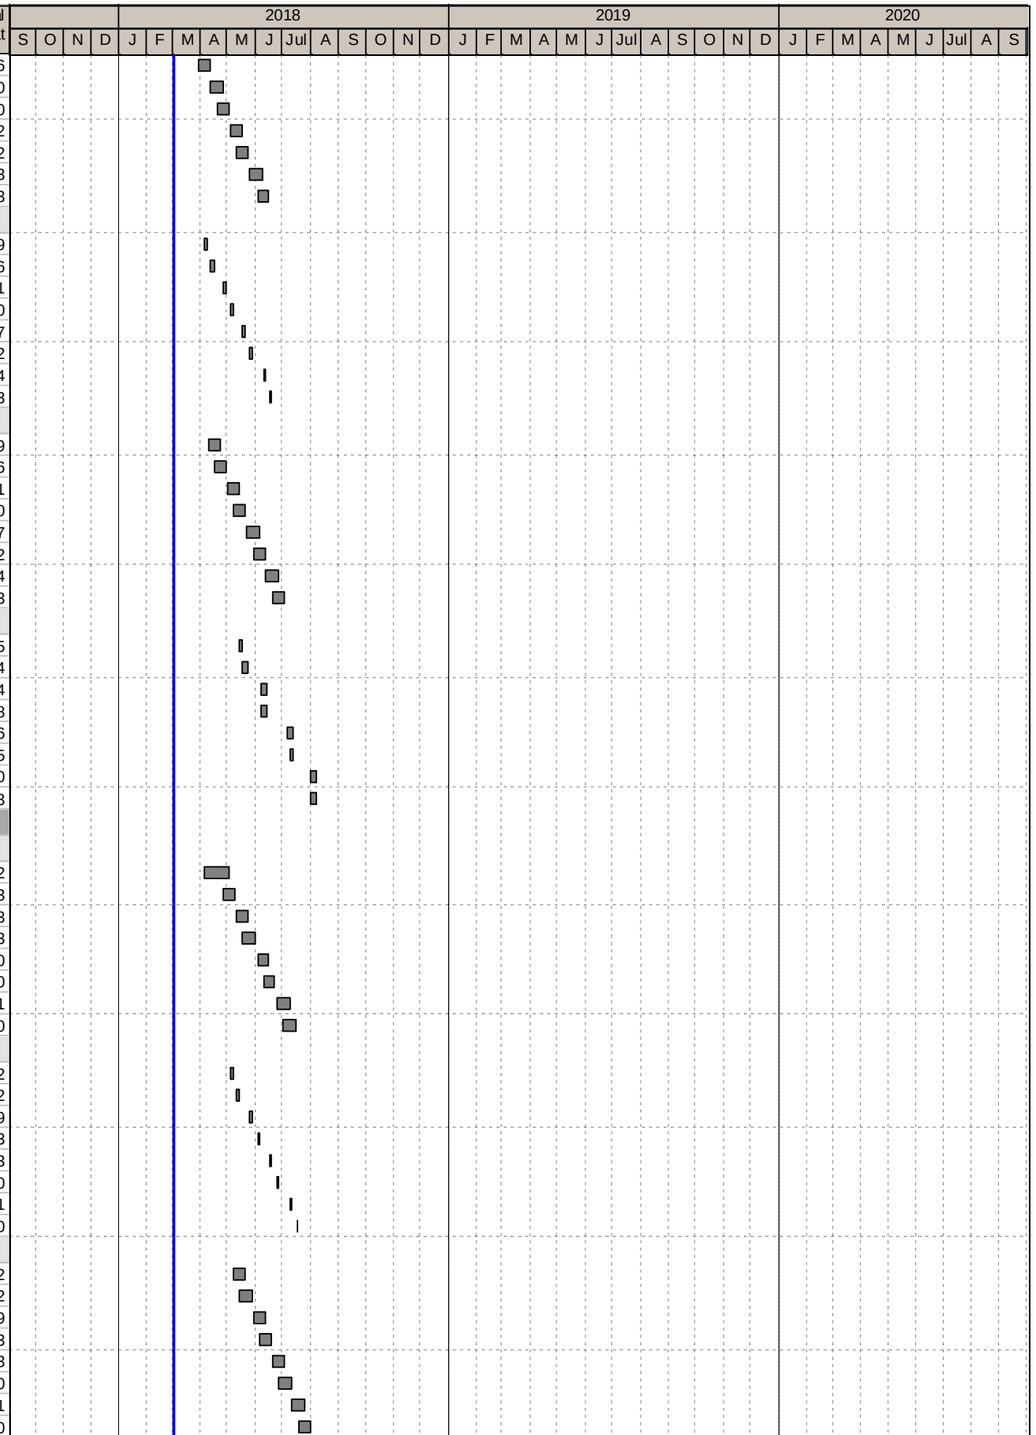

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
Fabricate					
S3F0-5P2BF	Rebar Concrete Core Walls - Fabricate - Core 2 Main to TOC	5	25-Jun-18	29-Jun-18	24
S3A0-5P2BF	Rebar Concrete Core Walls - Fabricate - Core 3 Main to TOC	5	27-Jun-18	03-Jul-18	7
S3E1-5P2BF	Rebar Concrete Core Walls - Fabricate - Core 1 Main to TOC	5	23-Jul-18	27-Jul-18	11
S3B0-5P2BF	Rebar Concrete Core Walls - Fabricate - Core 4 Main to TOC	5	25-Jul-18	31-Jul-18	10
S3E0-5P2BF	Rebar Concrete Core Walls - Fabricate - Core 8 Main to TOC	5	10-Sep-18	14-Sep-18	9
S3B1-5P2BF	Rebar Concrete Core Walls - Fabricate - Core 5 Main to TOC	5	10-Sep-18	14-Sep-18	7
S3C0-5P2BF	Rebar Concrete Core Walls - Fabricate - Core 6 Main to TOC	5	01-Oct-18	05-Oct-18	5
S3D0-5P2BF	Rebar Concrete Core Walls - Fabricate - Core 7 Main to TOC	5	01-Oct-18	05-Oct-18	19
FRP Columns					
000 Event Level					
Submit					
S1A0-5P2CS	Rebar Columns - Subcontractor Develop/Submit Shop Drawings - Event Area A	10	19-Feb-18 A	09-Mar-18	5
S1F0-5P2CS	Rebar Columns - Subcontractor Develop/Submit Shop Drawings - Event Area F	10	19-Feb-18 A	12-Mar-18	5
S1B0-5P2CS	Rebar Columns - Subcontractor Develop/Submit Shop Drawings - Event Area B	10	05-Mar-18	16-Mar-18	15
S1E0-5P2CS	Rebar Columns - Subcontractor Develop/Submit Shop Drawings - Event Area E	10	12-Mar-18	23-Mar-18	15
S1C0-5P2CS	Rebar Columns - Subcontractor Develop/Submit Shop Drawings - Event Area C	10	26-Mar-18	06-Apr-18	48
S1D0-5P2CS	Rebar Columns - Subcontractor Develop/Submit Shop Drawings - Event Area D	10	02-Apr-18	13-Apr-18	48
Mortenson Review					
S1A0-5P2CS1	Rebar Columns - MMCJV Review Shop Drawings - Event Area A	1	12-Mar-18	12-Mar-18	5
S1F0-5P2CS1	Rebar Columns - MMCJV Review Shop Drawings - Event Area F	1	13-Mar-18	13-Mar-18	5
S1B0-5P2CS1	Rebar Columns - MMCJV Review Shop Drawings - Event Area B	2	19-Mar-18	20-Mar-18	15
S1E0-5P2CS1	Rebar Columns - MMCJV Review Shop Drawings - Event Area E	2	26-Mar-18	27-Mar-18	15
S1C0-5P2CS1	Rebar Columns - MMCJV Review Shop Drawings - Event Area C	2	09-Apr-18	10-Apr-18	51
S1D0-5P2CS1	Rebar Columns - MMCJV Review Shop Drawings - Event Area D	2	16-Apr-18	17-Apr-18	48
Approve					
S1A0-5P2CA	Rebar Columns - Design Team Review/Approve Shop Drawings - Event Area A	5	12-Mar-18	16-Mar-18	5
S1F0-5P2CA	Rebar Columns - Design Team Review/Approve Shop Drawings - Event Area F	5	13-Mar-18	19-Mar-18	5
S1B0-5P2CA	Rebar Columns - Design Team Review/Approve Shop Drawings - Event Area B	10	21-Mar-18	03-Apr-18	15
S1E0-5P2CA	Rebar Columns - Design Team Review/Approve Shop Drawings - Event Area E	10	28-Mar-18	10-Apr-18	15
S1C0-5P2CA	Rebar Columns - Design Team Review/Approve Shop Drawings - Event Area C	10	11-Apr-18	24-Apr-18	51
S1D0-5P2CA	Rebar Columns - Design Team Review/Approve Shop Drawings - Event Area D	10	18-Apr-18	01-May-18	48
Fabricate					
S1A0-5P2CF	Rebar Columns - Fabricate - Event Area A1	5	20-Mar-18	26-Mar-18	4
S1F0-5P2CF	Rebar Columns - Fabricate - Event Area F1	5	21-Mar-18	27-Mar-18	4
S1A2-5P2CF	Rebar Columns - Fabricate - Event Area A2	5	28-Mar-18	03-Apr-18	10
S1F2-5P2CF	Rebar Columns - Fabricate - Event Area F2	5	29-Mar-18	04-Apr-18	10
S1B0-5P2CF	Rebar Columns - Fabricate - Event Area B1	5	10-Apr-18	16-Apr-18	11
S1E0-5P2CF	Rebar Columns - Fabricate - Event Area E1	5	16-Apr-18	20-Apr-18	12
S1B2-5P2CF	Rebar Columns - Fabricate - Event Area B2	5	18-Apr-18	24-Apr-18	22
S1E2-5P2CF	Rebar Columns - Fabricate - Event Area E2	5	23-Apr-18	27-Apr-18	24
S1B3-5P2CF	Rebar Columns - Fabricate - Event Area B3	5	27-Apr-18	03-May-18	36
S1E3-5P2CF	Rebar Columns - Fabricate - Event Area E3	5	01-May-18	07-May-18	26
S1C0-5P2CF	Rebar Columns - Fabricate - Event Area C1	5	18-May-18	24-May-18	34
S1D0-5P2CF	Rebar Columns - Fabricate - Event Area D1	5	24-May-18	31-May-18	32
S1C2-5P2CF	Rebar Columns - Fabricate - Event Area C2	5	29-May-18	04-Jun-18	62
S1D2-5P2CF	Rebar Columns - Fabricate - Event Area D2	5	04-Jun-18	08-Jun-18	63
050 Lower Mezz Level					
Submit					
S2A0-5P2CS	Rebar Columns - Subcontractor Develop/Submit Shop Drawings - Mezz Level Area A	10	20-Mar-18	02-Apr-18	9
S2F0-5P2CS	Rebar Columns - Subcontractor Develop/Submit Shop Drawings - Mezz Level Area F	10	27-Mar-18	09-Apr-18	9
S2B0-5P2CS	Rebar Columns - Subcontractor Develop/Submit Shop Drawings - Mezz Level Area B	10	10-Apr-18	23-Apr-18	24
S2E0-5P2CS	Rebar Columns - Subcontractor Develop/Submit Shop Drawings - Mezz Level Area E	10	17-Apr-18	30-Apr-18	24
S2C0-5P2CS	Rebar Columns - Subcontractor Develop/Submit Shop Drawings - Mezz Level Area C	10	01-May-18	14-May-18	51
S2D0-5P2CS	Rebar Columns - Subcontractor Develop/Submit Shop Drawings - Mezz Level Area D	10	08-May-18	21-May-18	51
Mortenson Review					
S2A0-5P2CS1	Rebar Columns - MMCJV Review Shop Drawings - Mezz Level Area A	1	03-Apr-18	03-Apr-18	14
S2F0-5P2CS1	Rebar Columns - MMCJV Review Shop Drawings - Mezz Level Area F	1	10-Apr-18	10-Apr-18	9
S2B0-5P2CS1	Rebar Columns - MMCJV Review Shop Drawings - Mezz Level Area B	1	24-Apr-18	24-Apr-18	25
S2E0-5P2CS1	Rebar Columns - MMCJV Review Shop Drawings - Mezz Level Area E	1	01-May-18	01-May-18	24
S2C0-5P2CS1	Rebar Columns - MMCJV Review Shop Drawings - Mezz Level Area C	2	15-May-18	16-May-18	53

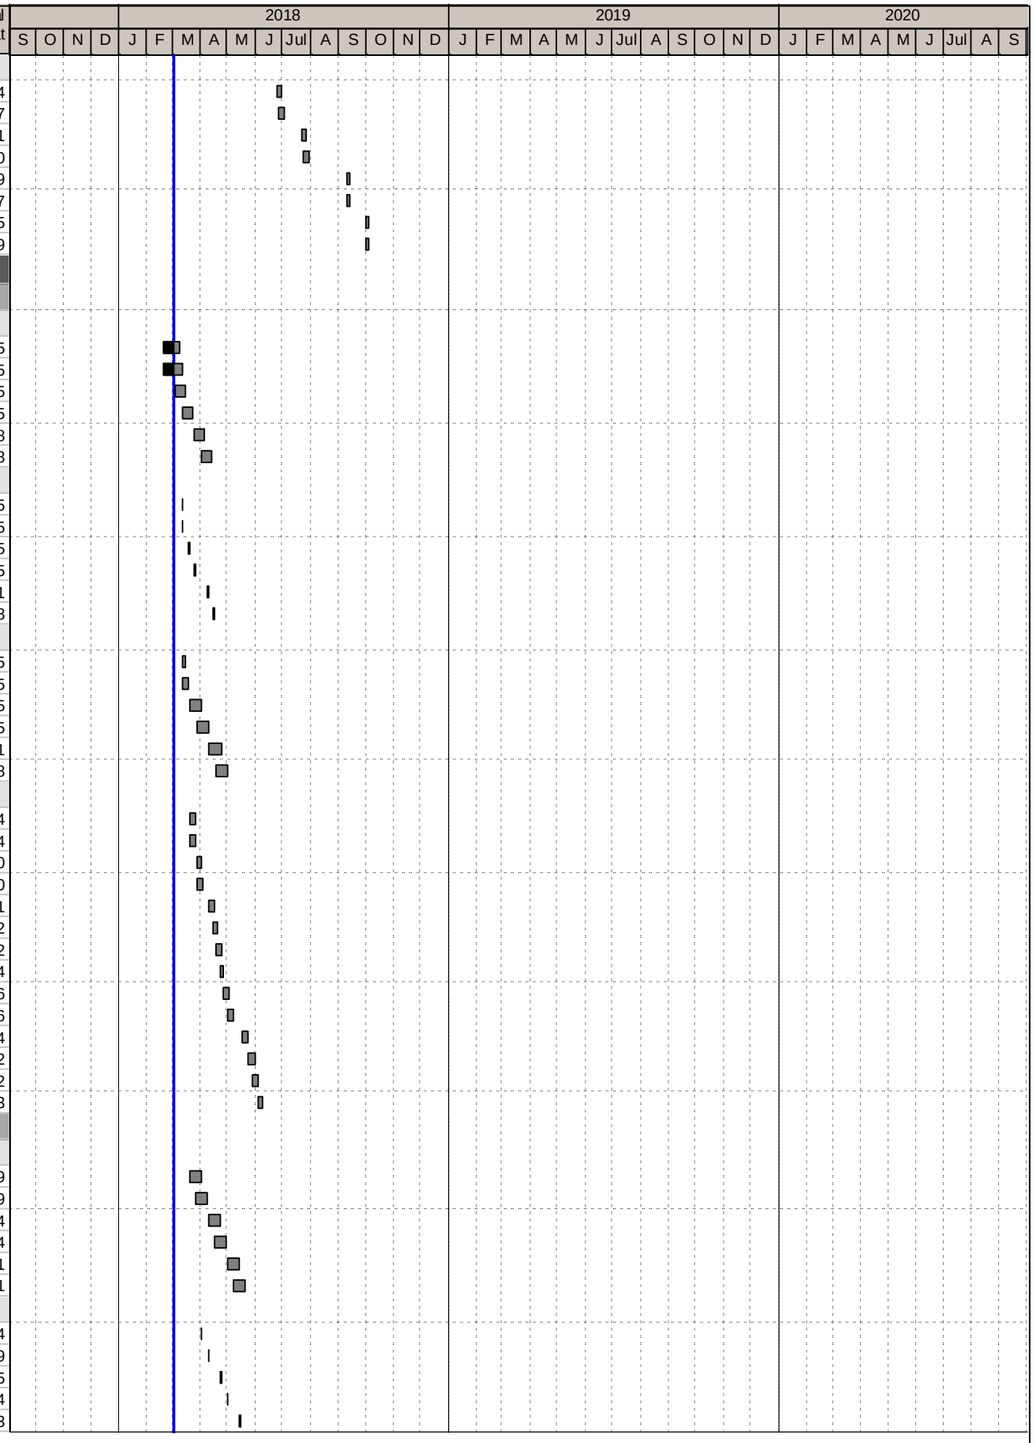

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S2D0-5P2CS1	Rebar Columns - MMCJV Review Shop Drawings - Mezz Level Area D	2	22-May-18	23-May-18	51
Approve					
S2A0-5P2CA	Rebar Columns - Design Team Review/Approve Shop Drawings - Mezz Level Area A	10	04-Apr-18	17-Apr-18	14
S2F0-5P2CA	Rebar Columns - Design Team Review/Approve Shop Drawings - Mezz Level Area F	10	11-Apr-18	24-Apr-18	9
S2B0-5P2CA	Rebar Columns - Design Team Review/Approve Shop Drawings - Mezz Level Area B	10	25-Apr-18	08-May-18	25
S2E0-5P2CA	Rebar Columns - Design Team Review/Approve Shop Drawings - Mezz Level Area E	10	02-May-18	15-May-18	24
S2C0-5P2CA	Rebar Columns - Design Team Review/Approve Shop Drawings - Mezz Level Area C	10	17-May-18	31-May-18	53
S2D0-5P2CA	Rebar Columns - Design Team Review/Approve Shop Drawings - Mezz Level Area D	10	24-May-18	07-Jun-18	51
Fabricate					
S2A0-5P2CF	Rebar Columns - Fabricate - Mezz Level Area A1	5	08-May-18	14-May-18	0
S2F0-5P2CF	Rebar Columns - Fabricate - Mezz Level Area F1	5	08-May-18	14-May-18	0
S2A2-5P2CF	Rebar Columns - Fabricate - Mezz Level Area A2	5	14-May-18	18-May-18	5
S2F2-5P2CF	Rebar Columns - Fabricate - Mezz Level Area F2	5	16-May-18	22-May-18	5
S2A3-5P2CF	Rebar Columns - Fabricate - Mezz Level Area A3	5	21-May-18	25-May-18	11
S2F3-5P2CF	Rebar Columns - Fabricate - Mezz Level Area F3	5	23-May-18	30-May-18	13
S2B0-5P2CF	Rebar Columns - Fabricate - Mezz Level Area B1	5	31-May-18	06-Jun-18	10
S2E0-5P2CF	Rebar Columns - Fabricate - Mezz Level Area E1	5	01-Jun-18	07-Jun-18	13
S2B2-5P2CF	Rebar Columns - Fabricate - Mezz Level Area B2	5	08-Jun-18	14-Jun-18	10
S2E2-5P2CF	Rebar Columns - Fabricate - Mezz Level Area E2	5	08-Jun-18	14-Jun-18	15
S2B3-5P2CF	Rebar Columns - Fabricate - Mezz Level Area B3	5	18-Jun-18	22-Jun-18	11
S2E3-5P2CF	Rebar Columns - Fabricate - Mezz Level Area E3	5	21-Jun-18	27-Jun-18	10
S2B4-5P2CF	Rebar Columns - Fabricate - Mezz Level Area B4	5	25-Jun-18	29-Jun-18	15
S2E4-5P2CF	Rebar Columns - Fabricate - Mezz Level Area E4	5	29-Jun-18	06-Jul-18	15
S2B5-5P2CF	Rebar Columns - Fabricate - Mezz Level Area B5	5	06-Jul-18	12-Jul-18	21
S2E5-5P2CF	Rebar Columns - Fabricate - Mezz Level Area E5	5	09-Jul-18	13-Jul-18	20
S2C0-5P2CF	Rebar Columns - Fabricate - Mezz Level Area C1	5	24-Jul-18	30-Jul-18	17
S2D0-5P2CF	Rebar Columns - Fabricate - Mezz Level Area D1	5	25-Jul-18	31-Jul-18	19
S2C2-5P2CF	Rebar Columns - Fabricate - Mezz Level Area C2	5	31-Jul-18	06-Aug-18	26
S2D2-5P2CF	Rebar Columns - Fabricate - Mezz Level Area D2	5	01-Aug-18	07-Aug-18	29
FRP Pan & Joist Deck					
050 Lower Mezz Level					
Submit					
S2A0-5P2GS	Rebar Pan & Joist Deck - Subcontractor Develop/Submit Shop Drawings - Area A Mezz Lvl A1	15	08-Mar-18	28-Mar-18	3
S2F0-5P2GS	Rebar Pan & Joist Deck - Subcontractor Develop/Submit Shop Drawings - Area F Mezz Lvl F1	15	08-Mar-18	28-Mar-18	4
S2A2-5P2GS	Rebar Pan & Joist Deck - Subcontractor Develop/Submit Shop Drawings - Area A Mezz Lvl A2	10	15-Mar-18	28-Mar-18	13
S2F2-5P2GS	Rebar Pan & Joist Deck - Subcontractor Develop/Submit Shop Drawings - Area F Mezz Lvl F2	10	15-Mar-18	28-Mar-18	15
S2A3-5P2GS	Rebar Pan & Joist Deck - Subcontractor Develop/Submit Shop Drawings - Area A Mezz Lvl A3	10	20-Mar-18	02-Apr-18	13
S2F3-5P2GS	Rebar Pan & Joist Deck - Subcontractor Develop/Submit Shop Drawings - Area F Mezz Lvl F3	10	20-Mar-18	02-Apr-18	18
S2B0-5P2GS	Rebar Pan & Joist Deck - Subcontractor Develop/Submit Shop Drawings - Area B Mezz Lvl B1 / B2	10	03-Apr-18	16-Apr-18	13
S2B3-5P2GS	Rebar Pan & Joist Deck - Subcontractor Develop/Submit Shop Drawings - Area B Mezz Lvl B3 / B4 / B5	10	03-Apr-18	16-Apr-18	32
S2E0-5P2GS	Rebar Pan & Joist Deck - Subcontractor Develop/Submit Shop Drawings - Area E Mezz Lvl E1 / E2	10	10-Apr-18	23-Apr-18	13
S2E3-5P2GS	Rebar Pan & Joist Deck - Subcontractor Develop/Submit Shop Drawings - Area E Mezz Lvl E3 / E4 / E5	10	10-Apr-18	23-Apr-18	28
S2C0-5P2GS	Rebar Pan & Joist Deck - Subcontractor Develop/Submit Shop Drawings - Area C Mezz Lvl	10	24-Apr-18	07-May-18	45
S2D0-5P2GS	Rebar Pan & Joist Deck - Subcontractor Develop/Submit Shop Drawings - Area D Mezz Lvl	10	24-Apr-18	07-May-18	50
Mortenson Review					
S2A0-5P2GS1	Rebar Pan & Joist Deck - MMCJV Review Shop Drawings - Area A Mezz Lvl A1	2	29-Mar-18	30-Mar-18	3
S2F0-5P2GS1	Rebar Pan & Joist Deck - MMCJV Review Shop Drawings - Area F Mezz Lvl F1	2	29-Mar-18	30-Mar-18	4
S2A2-5P2GS1	Rebar Pan & Joist Deck - MMCJV Review Shop Drawings - Area A Mezz Lvl A2	2	29-Mar-18	30-Mar-18	13
S2F2-5P2GS1	Rebar Pan & Joist Deck - MMCJV Review Shop Drawings - Area F Mezz Lvl F2	2	29-Mar-18	30-Mar-18	15
S2A3-5P2GS1	Rebar Pan & Joist Deck - MMCJV Review Shop Drawings - Area A Mezz Lvl A3	2	03-Apr-18	04-Apr-18	21
S2F3-5P2GS1	Rebar Pan & Joist Deck - MMCJV Review Shop Drawings - Area F Mezz Lvl F3	2	03-Apr-18	04-Apr-18	25
S2B0-5P2GS1	Rebar Pan & Joist Deck - MMCJV Review Shop Drawings - Area B Mezz Lvl B1 / B2	2	17-Apr-18	18-Apr-18	13
S2B3-5P2GS1	Rebar Pan & Joist Deck - MMCJV Review Shop Drawings - Area B Mezz Lvl B3 / B4 / B5	2	17-Apr-18	18-Apr-18	32
S2E0-5P2GS1	Rebar Pan & Joist Deck - MMCJV Review Shop Drawings - Area E Mezz Lvl E1 / E2	2	24-Apr-18	25-Apr-18	13
S2E3-5P2GS1	Rebar Pan & Joist Deck - MMCJV Review Shop Drawings - Area E Mezz Lvl E3 / E4 / E5	2	24-Apr-18	25-Apr-18	28
S2C0-5P2GS1	Rebar Pan & Joist Deck - MMCJV Review Shop Drawings - Area C Mezz Lvl	2	08-May-18	09-May-18	45
S2D0-5P2GS1	Rebar Pan & Joist Deck - MMCJV Review Shop Drawings - Area D Mezz Lvl	2	08-May-18	09-May-18	50
Approve					
S2A0-5P2GA	Rebar Pan & Joist Deck - Design Team Review/Approve Shop Drawings - Area A Mezz Lvl A1	10	02-Apr-18	13-Apr-18	3
S2F0-5P2GA	Rebar Pan & Joist Deck - Design Team Review/Approve Shop Drawings - Area F Mezz Lvl F1	10	02-Apr-18	13-Apr-18	4
S2A2-5P2GA	Rebar Pan & Joist Deck - Design Team Review/Approve Shop Drawings - Area A Mezz Lvl A2	10	02-Apr-18	13-Apr-18	13
S2F2-5P2GA	Rebar Pan & Joist Deck - Design Team Review/Approve Shop Drawings - Area F Mezz Lvl F2	10	02-Apr-18	13-Apr-18	15

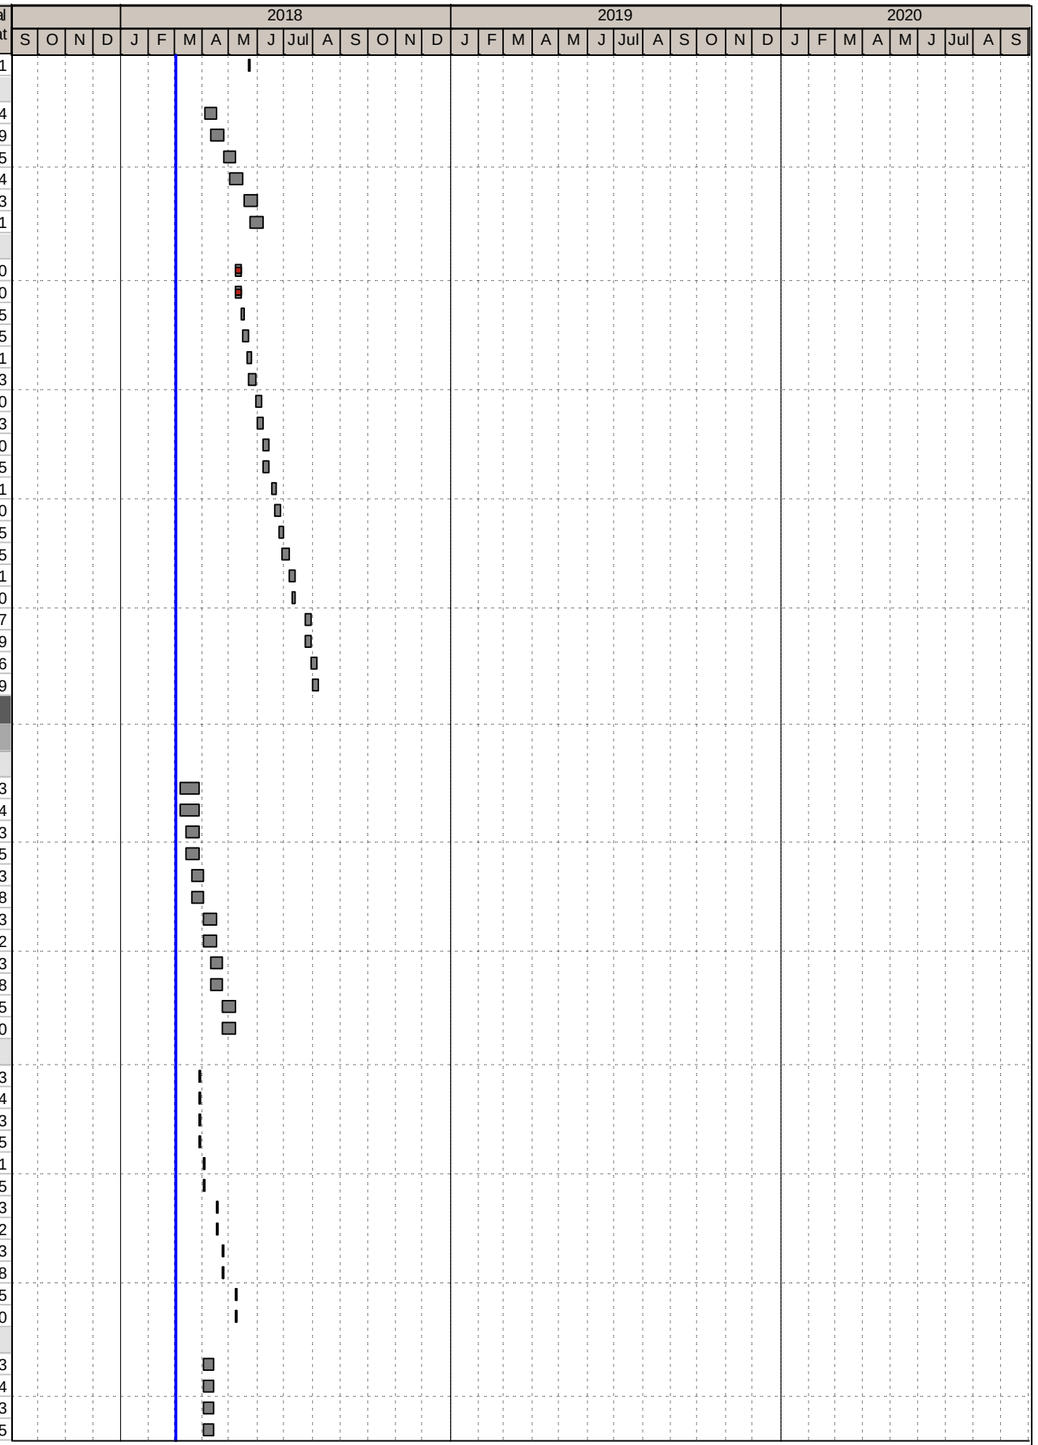

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S2A3-5P2GA	Rebar Pan & Joist Deck - Design Team Review/Approve Shop Drawings - Area A Mezz Lvl A3	10	05-Apr-18	18-Apr-18	21
S2F3-5P2GA	Rebar Pan & Joist Deck - Design Team Review/Approve Shop Drawings - Area F Mezz Lvl F3	10	05-Apr-18	18-Apr-18	25
S2B0-5P2GA	Rebar Pan & Joist Deck - Design Team Review/Approve Shop Drawings - Area B Mezz Lvl B1 / B2	10	19-Apr-18	02-May-18	13
S2B3-5P2GA	Rebar Pan & Joist Deck - Design Team Review/Approve Shop Drawings - Area B Mezz Lvl B3 / B4 / B5	10	19-Apr-18	02-May-18	32
S2E0-5P2GA	Rebar Pan & Joist Deck - Design Team Review/Approve Shop Drawings - Area E Mezz Lvl E1 / E2	10	26-Apr-18	09-May-18	13
S2E3-5P2GA	Rebar Pan & Joist Deck - Design Team Review/Approve Shop Drawings - Area E Mezz Lvl E3 / E4 / E5	10	26-Apr-18	09-May-18	28
S2C0-5P2GA	Rebar Pan & Joist Deck - Design Team Review/Approve Shop Drawings - Area C Mezz Lvl	10	10-May-18	23-May-18	45
S2D0-5P2GA	Rebar Pan & Joist Deck - Design Team Review/Approve Shop Drawings - Area D Mezz Lvl	10	10-May-18	23-May-18	50
Fabricate					
S2A0-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area A Mezz Lvl A1	5	17-Apr-18	23-Apr-18	2
S2F0-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area F Mezz Lvl F1	5	17-Apr-18	23-Apr-18	3
S2A2-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area A Mezz Lvl A2	5	26-Apr-18	02-May-18	5
S2F2-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area F Mezz Lvl F2	5	30-Apr-18	04-May-18	5
S2A3-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area A Mezz Lvl A3	5	07-May-18	11-May-18	9
S2F3-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area F Mezz Lvl F3	5	08-May-18	14-May-18	12
S2B0-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area B Mezz Lvl B1	5	14-May-18	18-May-18	6
S2E0-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area E Mezz Lvl E1	5	16-May-18	22-May-18	9
S2B2-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area B Mezz Lvl B2	5	23-May-18	30-May-18	4
S2E2-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area E Mezz Lvl E2	5	23-May-18	30-May-18	7
S2B3-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area B Mezz Lvl B3	5	04-Jun-18	08-Jun-18	11
S2E3-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area E Mezz Lvl E3	5	06-Jun-18	12-Jun-18	10
S2B4-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area B Mezz Lvl B4	5	08-Jun-18	14-Jun-18	15
S2E4-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area E Mezz Lvl E4	5	14-Jun-18	20-Jun-18	15
S2B5-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area B Mezz Lvl B5	5	19-Jun-18	25-Jun-18	16
S2E5-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area E Mezz Lvl E5	5	20-Jun-18	26-Jun-18	15
S2C0-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area C Mezz Lvl C1	5	05-Jul-18	11-Jul-18	17
S2D0-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area D Mezz Lvl D1	5	10-Jul-18	16-Jul-18	19
S2C2-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area C Mezz Lvl C2	5	13-Jul-18	19-Jul-18	20
S2D2-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area D Mezz Lvl D2	5	17-Jul-18	23-Jul-18	23
100 Main Concourse					
Submit					
S3A0-5P2GS	Rebar Pan & Joist Deck - Subcontractor Develop/Submit Shop Drawings - Area A Main Conc A1	10	20-Mar-18	02-Apr-18	23
S3F0-5P2GS	Rebar Pan & Joist Deck - Subcontractor Develop/Submit Shop Drawings - Area F Main Conc F1	10	27-Mar-18	09-Apr-18	29
S3A2-5P2GS	Rebar Pan & Joist Deck - Subcontractor Develop/Submit Shop Drawings - Area A Main Conc A2	10	27-Mar-18	09-Apr-18	23
S3A3-5P2GS	Rebar Pan & Joist Deck - Subcontractor Develop/Submit Shop Drawings - Area A Main Conc A3	10	03-Apr-18	16-Apr-18	23
S3F2-5P2GS	Rebar Pan & Joist Deck - Subcontractor Develop/Submit Shop Drawings - Area F Main Conc F2	10	03-Apr-18	16-Apr-18	29
S3A4-5P2GS	Rebar Pan & Joist Deck - Subcontractor Develop/Submit Shop Drawings - Area A Main Conc A4	10	10-Apr-18	23-Apr-18	23
S3F3-5P2GS	Rebar Pan & Joist Deck - Subcontractor Develop/Submit Shop Drawings - Area F Main Conc F3	10	10-Apr-18	23-Apr-18	29
S3B0-5P2GS	Rebar Pan & Joist Deck - Subcontractor Develop/Submit Shop Drawings - Area B Main Conc B1 / B2 / B3	15	24-Apr-18	14-May-18	23
S3E0-5P2GS	Rebar Pan & Joist Deck - Subcontractor Develop/Submit Shop Drawings - Area E Main Conc E1 / E2 / E3	15	24-Apr-18	14-May-18	29
S3B3-5P2GS	Rebar Pan & Joist Deck - Subcontractor Develop/Submit Shop Drawings - Area B Main Conc B4 / B5 / B6	15	15-May-18	05-Jun-18	28
S3E3-5P2GS	Rebar Pan & Joist Deck - Subcontractor Develop/Submit Shop Drawings - Area E Main Conc E4 / E5 / E6	15	15-May-18	05-Jun-18	33
S3C0-5P2GS	Rebar Pan & Joist Deck - Subcontractor Develop/Submit Shop Drawings - Area C Main Conc	15	06-Jun-18	26-Jun-18	43
S3D0-5P2GS	Rebar Pan & Joist Deck - Subcontractor Develop/Submit Shop Drawings - Area D Main Conc	15	06-Jun-18	26-Jun-18	42
Mortenson Review					
S3A0-5P2GS1	Rebar Pan & Joist Deck - MMCJV Review Shop Drawings - Area A Main Conc A1	2	03-Apr-18	04-Apr-18	25
S3F0-5P2GS1	Rebar Pan & Joist Deck - MMCJV Review Shop Drawings - Area F Main Conc F1	2	10-Apr-18	11-Apr-18	35
S3A2-5P2GS1	Rebar Pan & Joist Deck - MMCJV Review Shop Drawings - Area A Main Conc A2	2	10-Apr-18	11-Apr-18	30
S3A3-5P2GS1	Rebar Pan & Joist Deck - MMCJV Review Shop Drawings - Area A Main Conc A3	2	17-Apr-18	18-Apr-18	33
S3F2-5P2GS1	Rebar Pan & Joist Deck - MMCJV Review Shop Drawings - Area F Main Conc F2	2	17-Apr-18	18-Apr-18	39
S3A4-5P2GS1	Rebar Pan & Joist Deck - MMCJV Review Shop Drawings - Area A Main Conc A4	2	24-Apr-18	25-Apr-18	35
S3F3-5P2GS1	Rebar Pan & Joist Deck - MMCJV Review Shop Drawings - Area F Main Conc F3	2	24-Apr-18	25-Apr-18	39
S3B0-5P2GS1	Rebar Pan & Joist Deck - MMCJV Review Shop Drawings - Area B Main Conc B1 / B2 / B3	2	15-May-18	16-May-18	23
S3E0-5P2GS1	Rebar Pan & Joist Deck - MMCJV Review Shop Drawings - Area E Main Conc E1 / E2 / E3	2	15-May-18	16-May-18	29
S3B3-5P2GS1	Rebar Pan & Joist Deck - MMCJV Review Shop Drawings - Area B Main Conc B4 / B5 / B6	2	06-Jun-18	07-Jun-18	28
S3E3-5P2GS1	Rebar Pan & Joist Deck - MMCJV Review Shop Drawings - Area E Main Conc E4 / E5 / E6	2	06-Jun-18	07-Jun-18	33
S3C0-5P2GS1	Rebar Pan & Joist Deck - MMCJV Review Shop Drawings - Area C Main Conc	2	27-Jun-18	28-Jun-18	43
S3D0-5P2GS1	Rebar Pan & Joist Deck - MMCJV Review Shop Drawings - Area D Main Conc	2	27-Jun-18	28-Jun-18	42
Approve					
S3A0-5P2GA	Rebar Pan & Joist Deck - Design Team Review/Approve Shop Drawings - Area A Main Conc A1	10	05-Apr-18	18-Apr-18	25
S3F0-5P2GA	Rebar Pan & Joist Deck - Design Team Review/Approve Shop Drawings - Area F Main Conc F1	10	12-Apr-18	25-Apr-18	35
S3A2-5P2GA	Rebar Pan & Joist Deck - Design Team Review/Approve Shop Drawings - Area A Main Conc A2	10	12-Apr-18	25-Apr-18	30
S3A3-5P2GA	Rebar Pan & Joist Deck - Design Team Review/Approve Shop Drawings - Area A Main Conc A3	10	19-Apr-18	02-May-18	33

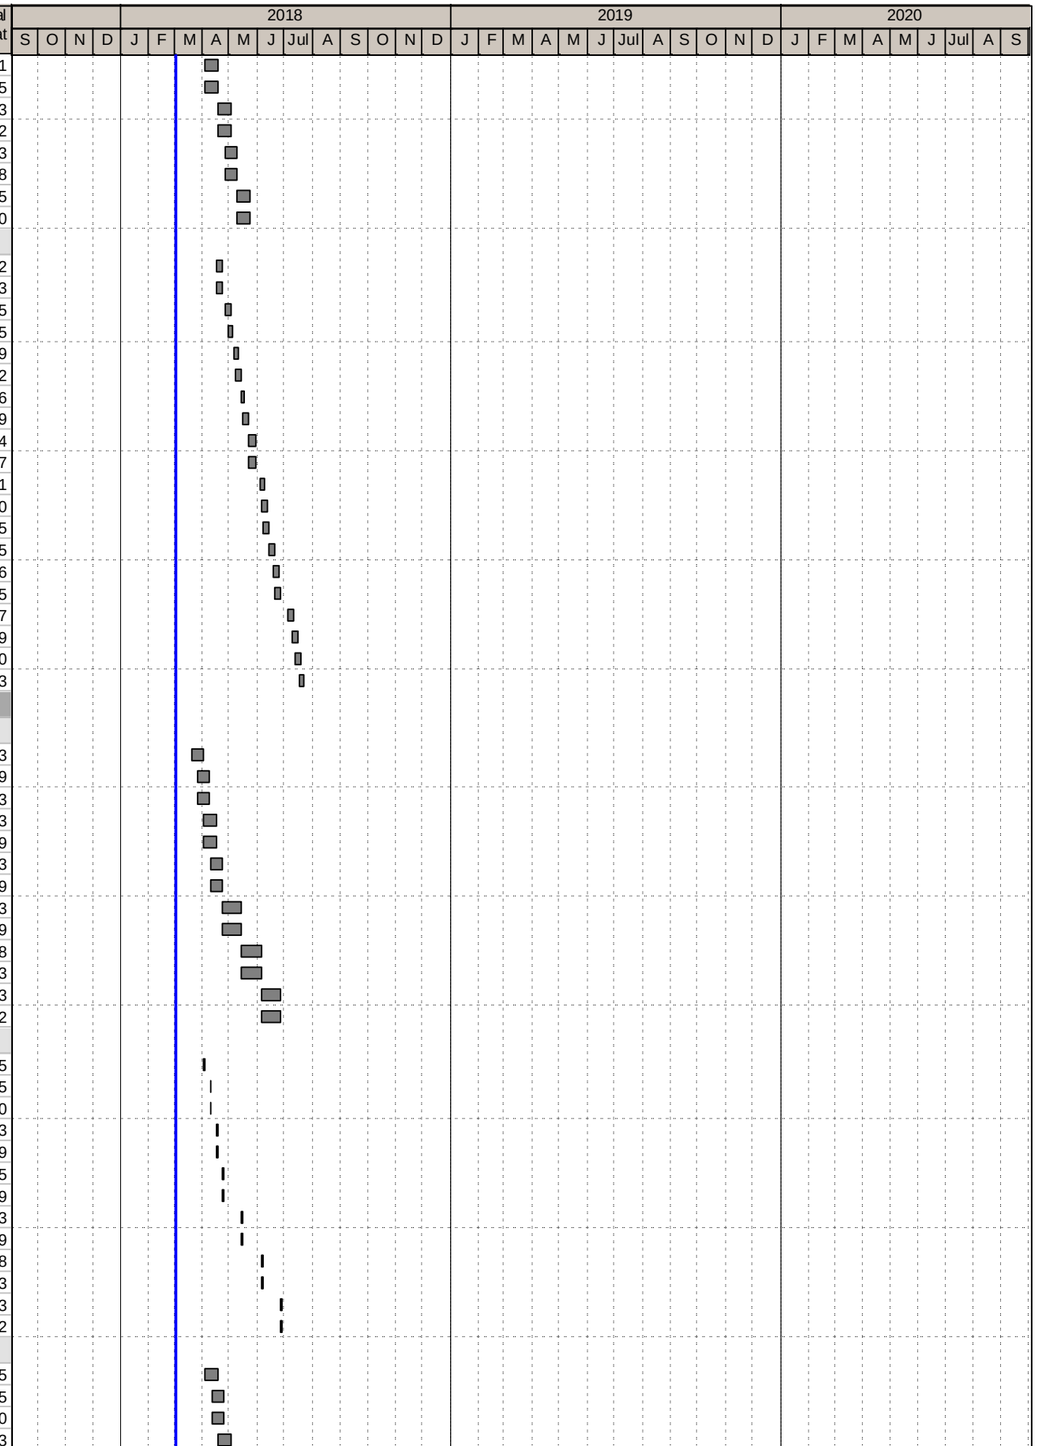

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S3F2-5P2GA	Rebar Pan & Joist Deck - Design Team Review/Approve Shop Drawings - Area F Main Conc F2	10	19-Apr-18	02-May-18	39
S3A4-5P2GA	Rebar Pan & Joist Deck - Design Team Review/Approve Shop Drawings - Area A Main Conc A4	10	26-Apr-18	09-May-18	35
S3F3-5P2GA	Rebar Pan & Joist Deck - Design Team Review/Approve Shop Drawings - Area F Main Conc F3	10	26-Apr-18	09-May-18	39
S3B0-5P2GA	Rebar Pan & Joist Deck - Design Team Review/Approve Shop Drawings - Area B Main Conc B1 / B2 / B3	10	17-May-18	31-May-18	23
S3E0-5P2GA	Rebar Pan & Joist Deck - Design Team Review/Approve Shop Drawings - Area E Main Conc E1 / E2 / E3	10	17-May-18	31-May-18	29
S3B3-5P2GA	Rebar Pan & Joist Deck - Design Team Review/Approve Shop Drawings - Area B Main Conc B4 / B5 / B6	10	08-Jun-18	21-Jun-18	28
S3E3-5P2GA	Rebar Pan & Joist Deck - Design Team Review/Approve Shop Drawings - Area E Main Conc E4 / E5 / E6	10	08-Jun-18	21-Jun-18	33
S3C0-5P2GA	Rebar Pan & Joist Deck - Design Team Review/Approve Shop Drawings - Area C Main Conc	10	29-Jun-18	13-Jul-18	43
S3D0-5P2GA	Rebar Pan & Joist Deck - Design Team Review/Approve Shop Drawings - Area D Main Conc	10	29-Jun-18	13-Jul-18	42
Fabricate					
S3A0-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area A Main Conc A1	5	21-May-18	25-May-18	3
S3F0-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area F Main Conc F1	5	30-May-18	05-Jun-18	12
S3A2-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area A Main Conc A2	5	01-Jun-18	07-Jun-18	5
S3F2-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area F Main Conc F2	5	08-Jun-18	14-Jun-18	14
S3A3-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area A Main Conc A3	5	11-Jun-18	15-Jun-18	7
S3F3-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area F Main Conc F3	5	18-Jun-18	22-Jun-18	13
S3A4-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area A Main Conc A4	5	20-Jun-18	26-Jun-18	7
S3E0-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area E Main Conc E1	5	25-Jun-18	29-Jun-18	13
S3B0-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area B Main Conc B1	5	26-Jun-18	02-Jul-18	6
S3E2-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area E Main Conc E2	5	05-Jul-18	11-Jul-18	10
S3B2-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area B Main Conc B2	5	09-Jul-18	13-Jul-18	4
S3E3-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area E Main Conc E3	5	19-Jul-18	25-Jul-18	6
S3B3-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area B Main Conc B3	5	20-Jul-18	26-Jul-18	0
S3E4-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area E Main Conc E4	5	01-Aug-18	07-Aug-18	6
S3B4-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area B Main Conc B4	5	02-Aug-18	08-Aug-18	0
S3B5-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area B Main Conc B5	5	13-Aug-18	17-Aug-18	10
S3E5-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area E Main Conc E5	5	13-Aug-18	17-Aug-18	8
S3E6-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area E Main Conc E6	5	22-Aug-18	28-Aug-18	5
S3B6-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area B Main Conc B6	5	23-Aug-18	29-Aug-18	6
S3C0-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area C Main Conc C1	5	31-Aug-18	07-Sep-18	9
S3D0-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area D Main Conc D1	5	31-Aug-18	07-Sep-18	8
S3C2-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area C Main Conc C2	5	13-Sep-18	19-Sep-18	5
S3D2-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area D Main Conc D2	5	14-Sep-18	20-Sep-18	10
S3C3-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area C Main Conc C3	5	25-Sep-18	01-Oct-18	12
S3D3-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area D Main Conc D3	5	25-Sep-18	01-Oct-18	9
S3C4-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area C Main Conc C4	5	03-Oct-18	09-Oct-18	12
S3D4-5P2GF	Rebar Pan & Joist Deck - Fabricate - Area D Main Conc D4	5	03-Oct-18	09-Oct-18	10
Steel Structure					
Procure					
S00-5P5A100	Prepare ABM - Steel Structural Frame	10	03-Apr-18	17-Apr-18	12
200/250 Lower Suite & Upper Suite Lvl					
Submit					
S4A0-5P4S	Bowl Steel - Develop/Submit Shop Dwgs - Area A Lower & Upper Suite Lvl (Seq 1108)	20	09-Apr-18	04-May-18	12
S4F0-5P4S	Bowl Steel - Develop/Submit Shop Dwgs - Area F Lower & Upper Suite Lvl (Seq 1107)	20	16-Apr-18	11-May-18	12
S4A1-5P4S	Bowl Steel - Develop/Submit Shop Dwgs - Area A Lower & Upper Suite Lvl (Seq 1109)	20	23-Apr-18	18-May-18	12
S4B0-5P4S	Bowl Steel - Develop/Submit Shop Dwgs - Area B Lower & Upper Suite Lvl (Seq 1111)	20	30-Apr-18	25-May-18	12
S4F1-5P4S	Bowl Steel - Develop/Submit Shop Dwgs - Area F Lower & Upper Suite Lvl (Seq 1106)	20	04-May-18	01-Jun-18	12
S4A2-5P4S	Bowl Steel - Develop/Submit Shop Dwgs - Area A Lower & Upper Suite Lvl (Seq 1110)	20	11-May-18	08-Jun-18	12
S4E0-5P4S	Bowl Steel - Develop/Submit Shop Dwgs - Area E Lower & Upper Suite Lvl (Seq 1103)	20	18-May-18	15-Jun-18	12
S4B0-5P4S10	Bowl Steel - Develop/Submit Shop Dwgs - Area B Lower & Upper Suite Lvl (Seq 1112)	20	18-May-18	15-Jun-18	12
S4F2-5P4S	Bowl Steel - Develop/Submit Shop Dwgs - Area F Lower & Upper Suite Lvl (Seq 1105)	20	18-May-18	15-Jun-18	12
S4E0-5P4S10	Bowl Steel - Develop/Submit Shop Dwgs - Area E Lower & Upper Suite Lvl (Seq 1104)	20	25-May-18	22-Jun-18	12
S4E0-5P4S20	Bowl Steel - Develop/Submit Shop Dwgs - Area E Lower & Upper Suite Lvl (Seq 1102)	20	25-May-18	22-Jun-18	12
S4E3-5P4S20	Bowl Steel - Develop/Submit Shop Dwgs - Area E Lower & Upper Suite Lvl (Seq 1101)	20	25-May-18	22-Jun-18	12
S4B0-5P4S20	Bowl Steel - Develop/Submit Shop Dwgs - Area B Lower & Upper Suite Lvl (Seq 1113)	20	15-Jun-18	13-Jul-18	14
S4B3-5P4S20	Bowl Steel - Develop/Submit Shop Dwgs - Area B Lower & Upper Suite Lvl (Seq 1114)	20	15-Jun-18	13-Jul-18	14
S4B4-5P4S20	Bowl Steel - Develop/Submit Shop Dwgs - Area B Lower & Upper Suite Lvl (Seq 1115)	20	22-Jun-18	20-Jul-18	16
S4C0-5P4S	Bowl Steel - Develop/Submit Shop Dwgs - Area C Lower & Upper Suite Lvl (Seq 1117)	20	09-Jul-18	03-Aug-18	19
S4E4-5P4S20	Bowl Steel - Develop/Submit Shop Dwgs - Area E Lower & Upper Suite Lvl (Seq 1125)	20	09-Jul-18	03-Aug-18	19
S4B5-5P4S20	Bowl Steel - Develop/Submit Shop Dwgs - Area B Lower & Upper Suite Lvl (Seq 1116)	20	09-Jul-18	03-Aug-18	19
S4E5-5P4S20	Bowl Steel - Develop/Submit Shop Dwgs - Area E Lower & Upper Suite Lvl (Seq 1124)	20	16-Jul-18	10-Aug-18	19

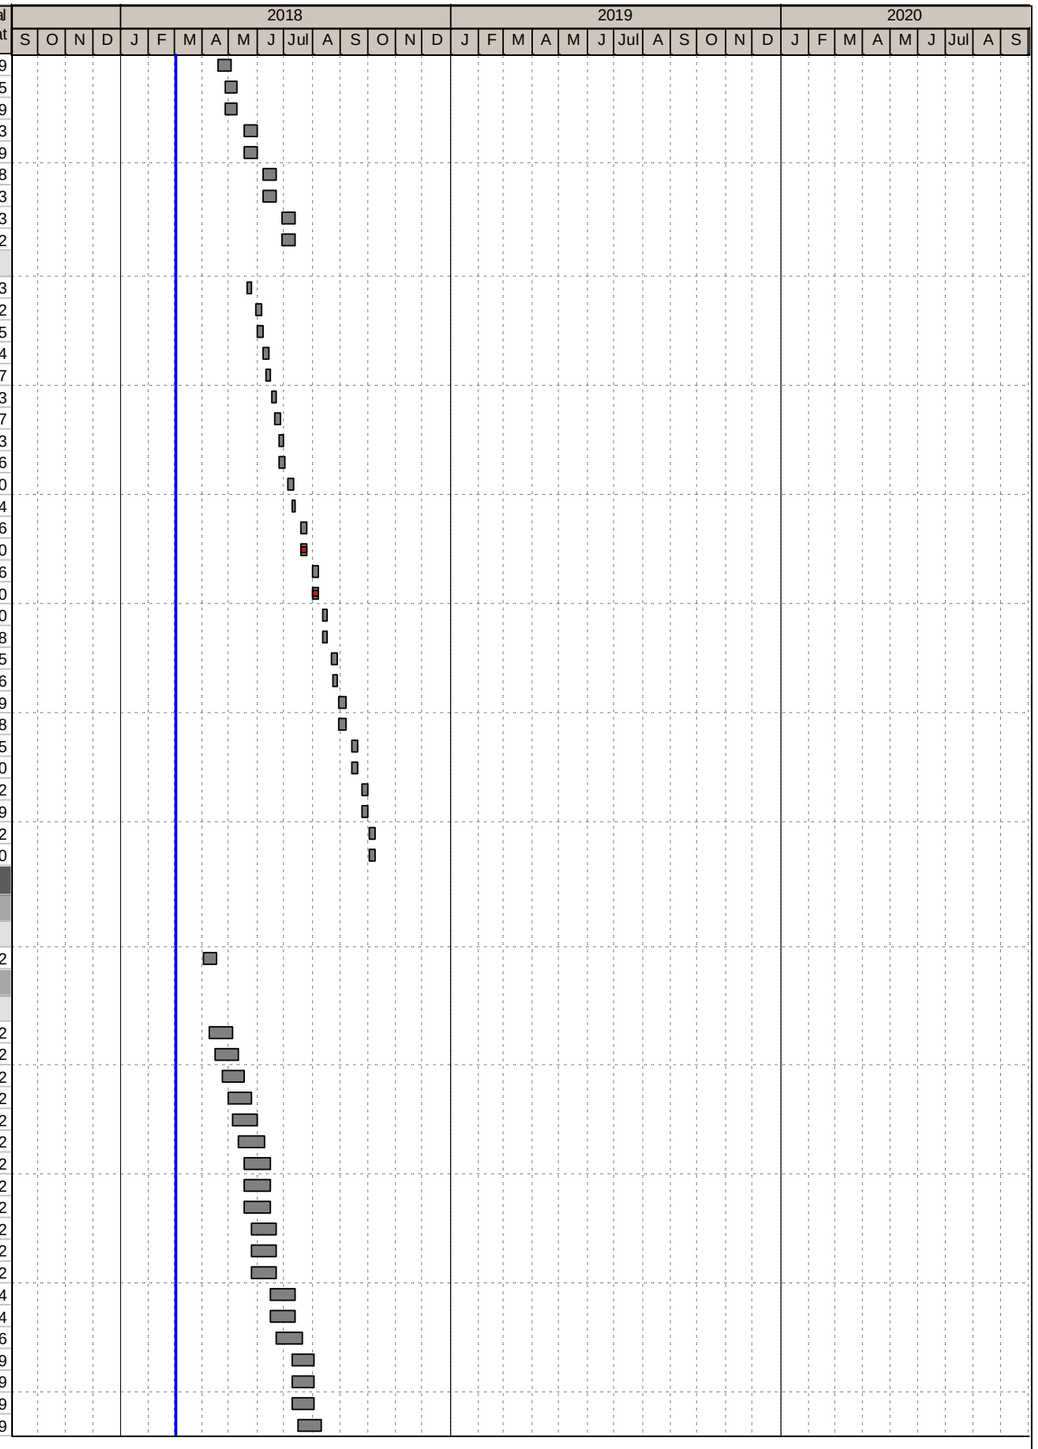

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S4E6-5P4S20	Bowl Steel - Develop/Submit Shop Dwgs - Area E Lower & Upper Suite Lvl (Seq 1123)	20	16-Jul-18	10-Aug-18	22
S4C0-5P4S10	Bowl Steel - Develop/Submit Shop Dwgs - Area C Lower & Upper Suite Lvl (Seq 1118)	20	23-Jul-18	17-Aug-18	22
S4D0-5P4S	Bowl Steel - Develop/Submit Shop Dwgs - Area D Lower & Upper Suite Lvl (Seq 1122)	20	30-Jul-18	24-Aug-18	30
S4D0-5P4S10	Bowl Steel - Develop/Submit Shop Dwgs - Area D Lower & Upper Suite Lvl (Seq 1121)	20	06-Aug-18	31-Aug-18	37
S4C2-5P4S10	Bowl Steel - Develop/Submit Shop Dwgs - Area C Lower & Upper Suite Lvl (Seq 1119)	20	06-Aug-18	31-Aug-18	43
S4C3-5P4S10	Bowl Steel - Develop/Submit Shop Dwgs - Area C Lower & Upper Suite Lvl (Seq 1126)	20	06-Aug-18	31-Aug-18	37
S4C5-5P4S10	Bowl Steel - Develop/Submit Shop Dwgs - Area C Lower & Upper Suite Lvl (Seq 1120)	20	06-Aug-18	31-Aug-18	41
S4C4-5P4S10	Bowl Steel - Develop/Submit Shop Dwgs - Area C Lower & Upper Suite Lvl (Seq 1127)	20	20-Aug-18	17-Sep-18	57
Mortenson Review					
S4A0-5P4R	Bowl Steel - MMCJV Review Shop Drawings - Area A Lower & Upper Suite Lvl (Seq 1108)	2	07-May-18	08-May-18	41
S4F0-5P4R	Bowl Steel - MMCJV Review Shop Drawings - Area F Lower & Upper Suite Lvl (Seq 1107)	2	14-May-18	15-May-18	41
S4A1-5P4R	Bowl Steel - MMCJV Review Shop Drawings - Area A Lower & Upper Suite Lvl (Seq 1109)	2	21-May-18	22-May-18	36
S4B0-5P4R	Bowl Steel - MMCJV Review Shop Drawings - Area B Lower & Upper Suite Lvl (Seq 1111)	2	29-May-18	30-May-18	28
S4F1-5P4R	Bowl Steel - MMCJV Review Shop Drawings - Area F Lower & Upper Suite Lvl (Seq 1106)	2	04-Jun-18	05-Jun-18	32
S4A2-5P4R	Bowl Steel - MMCJV Review Shop Drawings - Area A Lower & Upper Suite Lvl (Seq 1110)	2	11-Jun-18	12-Jun-18	27
S4E0-5P4R	Bowl Steel - MMCJV Review Shop Drawings - Area E Lower & Upper Suite Lvl (Seq 1103)	2	18-Jun-18	19-Jun-18	26
S4B0-5P4R10	Bowl Steel - MMCJV Review Shop Drawings - Area B Lower & Upper Suite Lvl (Seq 1112)	2	18-Jun-18	19-Jun-18	20
S4F2-5P4R	Bowl Steel - MMCJV Review Shop Drawings - Area F Lower & Upper Suite Lvl (Seq 1105)	2	18-Jun-18	19-Jun-18	27
S4E0-5P4R10	Bowl Steel - MMCJV Review Shop Drawings - Area E Lower & Upper Suite Lvl (Seq 1104)	2	25-Jun-18	26-Jun-18	27
S4E0-5P4R20	Bowl Steel - MMCJV Review Shop Drawings - Area E Lower & Upper Suite Lvl (Seq 1102)	2	25-Jun-18	26-Jun-18	26
S4E3-5P4R20	Bowl Steel - MMCJV Review Shop Drawings - Area E Lower & Upper Suite Lvl (Seq 1101)	2	25-Jun-18	26-Jun-18	29
S4B0-5P4R20	Bowl Steel - MMCJV Review Shop Drawings - Area B Lower & Upper Suite Lvl (Seq 1113)	2	16-Jul-18	17-Jul-18	19
S4B3-5P4R20	Bowl Steel - MMCJV Review Shop Drawings - Area B Lower & Upper Suite Lvl (Seq 1114)	2	16-Jul-18	17-Jul-18	22
S4B4-5P4R20	Bowl Steel - MMCJV Review Shop Drawings - Area B Lower & Upper Suite Lvl (Seq 1115)	2	23-Jul-18	24-Jul-18	22
S4C0-5P4R	Bowl Steel - MMCJV Review Shop Drawings - Area C Lower & Upper Suite Lvl (Seq 1117)	2	06-Aug-18	07-Aug-18	26
S4E4-5P4R20	Bowl Steel - MMCJV Review Shop Drawings - Area E Lower & Upper Suite Lvl (Seq 1125)	2	06-Aug-18	07-Aug-18	20
S4B5-5P4R20	Bowl Steel - MMCJV Review Shop Drawings - Area B Lower & Upper Suite Lvl (Seq 1116)	2	06-Aug-18	07-Aug-18	21
S4E5-5P4R20	Bowl Steel - MMCJV Review Shop Drawings - Area E Lower & Upper Suite Lvl (Seq 1124)	2	13-Aug-18	14-Aug-18	19
S4E6-5P4R20	Bowl Steel - MMCJV Review Shop Drawings - Area E Lower & Upper Suite Lvl (Seq 1123)	2	13-Aug-18	14-Aug-18	26
S4C0-5P4R10	Bowl Steel - MMCJV Review Shop Drawings - Area C Lower & Upper Suite Lvl (Seq 1118)	2	20-Aug-18	21-Aug-18	22
S4D0-5P4R	Bowl Steel - MMCJV Review Shop Drawings - Area D Lower & Upper Suite Lvl (Seq 1122)	2	27-Aug-18	28-Aug-18	37
S4D0-5P4R10	Bowl Steel - MMCJV Review Shop Drawings - Area D Lower & Upper Suite Lvl (Seq 1121)	2	04-Sep-18	05-Sep-18	37
S4C2-5P4R10	Bowl Steel - MMCJV Review Shop Drawings - Area C Lower & Upper Suite Lvl (Seq 1119)	2	04-Sep-18	05-Sep-18	44
S4C3-5P4R10	Bowl Steel - MMCJV Review Shop Drawings - Area C Lower & Upper Suite Lvl (Seq 1126)	2	04-Sep-18	05-Sep-18	37
S4C5-5P4R10	Bowl Steel - MMCJV Review Shop Drawings - Area C Lower & Upper Suite Lvl (Seq 1120)	2	04-Sep-18	05-Sep-18	41
S4C4-5P4R10	Bowl Steel - MMCJV Review Shop Drawings - Area C Lower & Upper Suite Lvl (Seq 1127)	2	18-Sep-18	19-Sep-18	57
Approve					
S4A0-5P4A	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area A Lower & Upper Suite Lvl (Seq 1108)	10	09-May-18	22-May-18	41
S4F0-5P4A	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area F Lower & Upper Suite Lvl (Seq 1107)	10	16-May-18	30-May-18	41
S4A1-5P4A	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area A Lower & Upper Suite Lvl (Seq 1109)	10	23-May-18	06-Jun-18	36
S4B0-5P4A	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area B Lower & Upper Suite Lvl (Seq 1111)	10	31-May-18	13-Jun-18	28
S4F1-5P4A	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area F Lower & Upper Suite Lvl (Seq 1106)	10	06-Jun-18	19-Jun-18	32
S4A2-5P4A	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area A Lower & Upper Suite Lvl (Seq 1110)	10	13-Jun-18	26-Jun-18	27
S4E0-5P4A	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area E Lower & Upper Suite Lvl (Seq 1103)	10	20-Jun-18	03-Jul-18	26
S4B0-5P4A10	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area B Lower & Upper Suite Lvl (Seq 1112)	10	20-Jun-18	03-Jul-18	20
S4F2-5P4A	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area F Lower & Upper Suite Lvl (Seq 1105)	10	20-Jun-18	03-Jul-18	27
S4E0-5P4A10	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area E Lower & Upper Suite Lvl (Seq 1104)	10	27-Jun-18	11-Jul-18	27
S4E0-5P4A20	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area E Lower & Upper Suite Lvl (Seq 1102)	10	27-Jun-18	11-Jul-18	26
S4E3-5P4A20	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area E Lower & Upper Suite Lvl (Seq 1101)	10	27-Jun-18	11-Jul-18	29
S4B0-5P4A20	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area B Lower & Upper Suite Lvl (Seq 1113)	10	18-Jul-18	31-Jul-18	19
S4B3-5P4A20	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area B Lower & Upper Suite Lvl (Seq 1114)	10	18-Jul-18	31-Jul-18	22
S4B4-5P4A20	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area B Lower & Upper Suite Lvl (Seq 1115)	10	25-Jul-18	07-Aug-18	22
S4C0-5P4A	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area C Lower & Upper Suite Lvl (Seq 1117)	10	08-Aug-18	21-Aug-18	26
S4E4-5P4A20	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area E Lower & Upper Suite Lvl (Seq 1125)	10	08-Aug-18	21-Aug-18	20
S4B5-5P4A20	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area B Lower & Upper Suite Lvl (Seq 1116)	10	08-Aug-18	21-Aug-18	21
S4E5-5P4A20	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area E Lower & Upper Suite Lvl (Seq 1124)	10	15-Aug-18	28-Aug-18	19
S4E6-5P4A20	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area E Lower & Upper Suite Lvl (Seq 1123)	10	15-Aug-18	28-Aug-18	26
S4C0-5P4A10	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area C Lower & Upper Suite Lvl (Seq 1118)	10	22-Aug-18	05-Sep-18	22
S4D0-5P4A	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area D Lower & Upper Suite Lvl (Seq 1122)	10	29-Aug-18	12-Sep-18	37
S4D0-5P4A10	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area D Lower & Upper Suite Lvl (Seq 1121)	10	06-Sep-18	19-Sep-18	37
S4C2-5P4A10	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area C Lower & Upper Suite Lvl (Seq 1119)	10	06-Sep-18	19-Sep-18	44
S4C3-5P4A10	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area C Lower & Upper Suite Lvl (Seq 1126)	10	06-Sep-18	19-Sep-18	37
S4C5-5P4A10	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area C Lower & Upper Suite Lvl (Seq 1120)	10	06-Sep-18	19-Sep-18	41

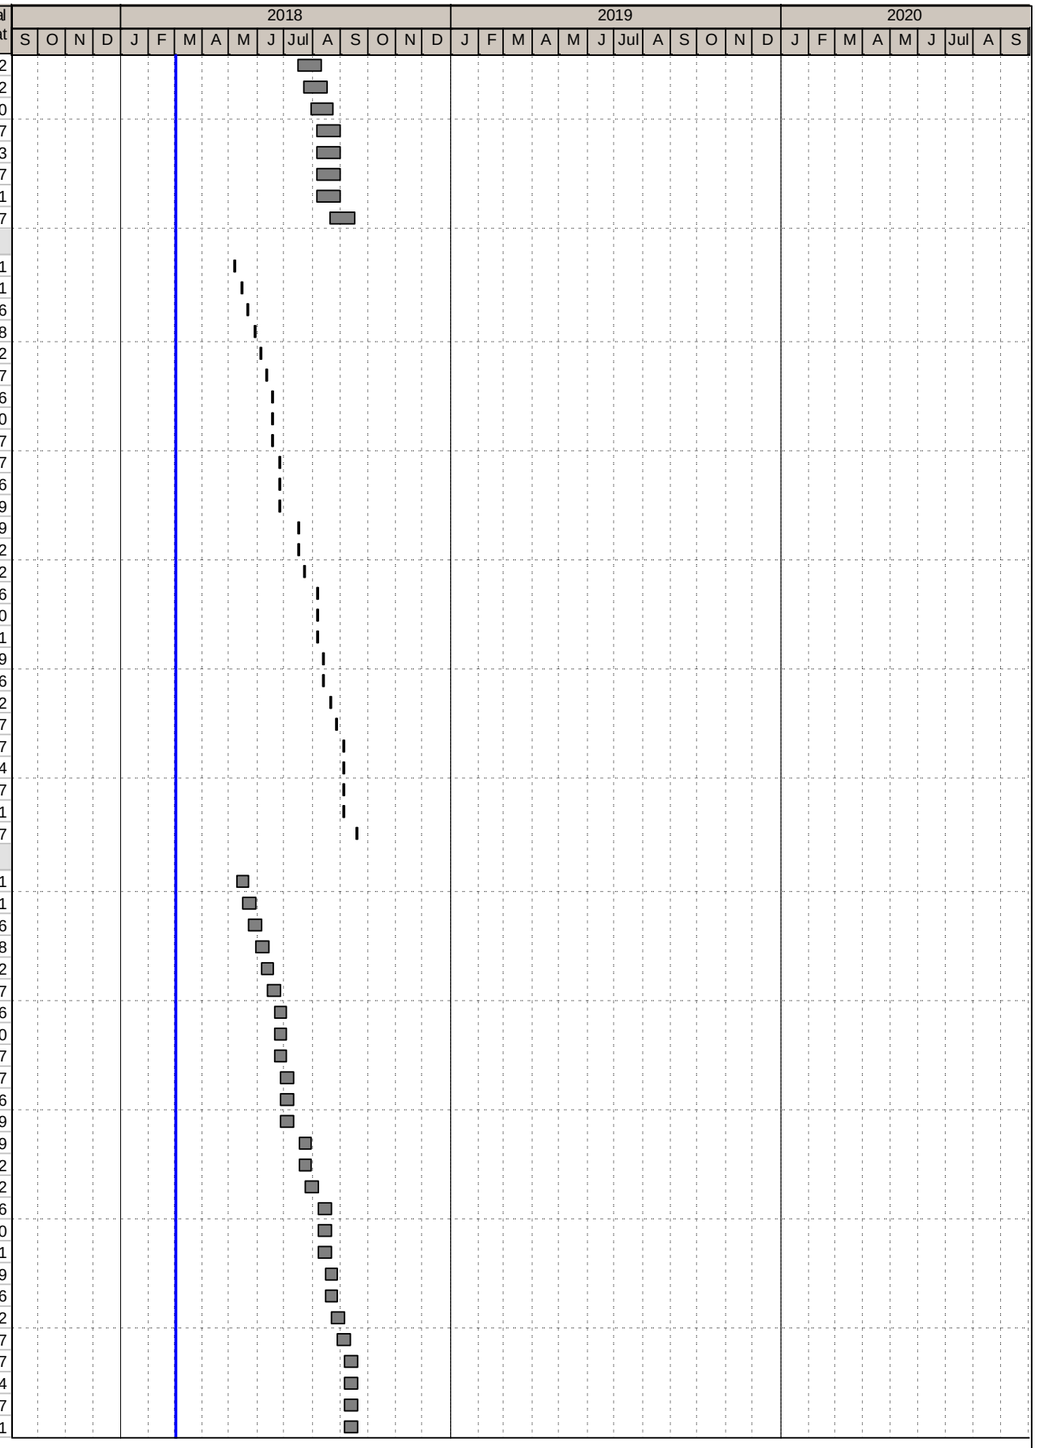

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S4C4-5P4A10	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area C Lower & Upper Suite Lvl (Seq 1127)	10	20-Sep-18	03-Oct-18	57
S4A0-5P4J	Bowl Steel - Scrub/Prepare Fab Sheets - Area A Lower & Upper Suite Lvl (Seq 1108)	5	23-May-18	30-May-18	41
S4F0-5P4J	Bowl Steel - Scrub/Prepare Fab Sheets - Area F Lower & Upper Suite Lvl (Seq 1107)	5	31-May-18	06-Jun-18	41
S4A1-5P4J	Bowl Steel - Scrub/Prepare Fab Sheets - Area A Lower & Upper Suite Lvl (Seq 1109)	5	07-Jun-18	13-Jun-18	36
S4B0-5P4J	Bowl Steel - Scrub/Prepare Fab Sheets - Area B Lower & Upper Suite Lvl (Seq 1111)	5	14-Jun-18	20-Jun-18	28
S4F1-5P4J	Bowl Steel - Scrub/Prepare Fab Sheets - Area F Lower & Upper Suite Lvl (Seq 1106)	5	20-Jun-18	26-Jun-18	32
S4A2-5P4J	Bowl Steel - Scrub/Prepare Fab Sheets - Area A Lower & Upper Suite Lvl (Seq 1110)	5	27-Jun-18	03-Jul-18	27
S4E0-5P4J	Bowl Steel - Scrub/Prepare Fab Sheets - Area E Lower & Upper Suite Lvl (Seq 1103)	5	05-Jul-18	11-Jul-18	26
S4B0-5P4J10	Bowl Steel - Scrub/Prepare Fab Sheets - Area B Lower & Upper Suite Lvl (Seq 1112)	5	05-Jul-18	11-Jul-18	20
S4F2-5P4J	Bowl Steel - Scrub/Prepare Fab Sheets - Area F Lower & Upper Suite Lvl (Seq 1105)	5	05-Jul-18	11-Jul-18	27
S4E0-5P4J10	Bowl Steel - Scrub/Prepare Fab Sheets - Area E Lower & Upper Suite Lvl (Seq 1104)	5	12-Jul-18	18-Jul-18	27
S4E0-5P4J20	Bowl Steel - Scrub/Prepare Fab Sheets - Area E Lower & Upper Suite Lvl (Seq 1102)	5	12-Jul-18	18-Jul-18	26
S4E3-5P4J20	Bowl Steel - Scrub/Prepare Fab Sheets - Area E Lower & Upper Suite Lvl (Seq 1101)	5	12-Jul-18	18-Jul-18	29
S4B0-5P4J20	Bowl Steel - Scrub/Prepare Fab Sheets - Area B Lower & Upper Suite Lvl (Seq 1113)	5	01-Aug-18	07-Aug-18	19
S4B3-5P4J20	Bowl Steel - Scrub/Prepare Fab Sheets - Area B Lower & Upper Suite Lvl (Seq 1114)	5	01-Aug-18	07-Aug-18	22
S4B4-5P4J20	Bowl Steel - Scrub/Prepare Fab Sheets - Area B Lower & Upper Suite Lvl (Seq 1115)	5	08-Aug-18	14-Aug-18	22
S4C0-5P4J	Bowl Steel - Scrub/Prepare Fab Sheets - Area C Lower & Upper Suite Lvl (Seq 1117)	5	22-Aug-18	28-Aug-18	26
S4E4-5P4J20	Bowl Steel - Scrub/Prepare Fab Sheets - Area E Lower & Upper Suite Lvl (Seq 1125)	5	22-Aug-18	28-Aug-18	20
S4B5-5P4J20	Bowl Steel - Scrub/Prepare Fab Sheets - Area B Lower & Upper Suite Lvl (Seq 1116)	5	22-Aug-18	28-Aug-18	21
S4E5-5P4J20	Bowl Steel - Scrub/Prepare Fab Sheets - Area E Lower & Upper Suite Lvl (Seq 1124)	5	29-Aug-18	05-Sep-18	19
S4E6-5P4J20	Bowl Steel - Scrub/Prepare Fab Sheets - Area E Lower & Upper Suite Lvl (Seq 1123)	5	29-Aug-18	05-Sep-18	26
S4C0-5P4J10	Bowl Steel - Scrub/Prepare Fab Sheets - Area C Lower & Upper Suite Lvl (Seq 1118)	5	06-Sep-18	12-Sep-18	22
S4D0-5P4J	Bowl Steel - Scrub/Prepare Fab Sheets - Area D Lower & Upper Suite Lvl (Seq 1122)	5	13-Sep-18	19-Sep-18	37
S4D0-5P4J10	Bowl Steel - Scrub/Prepare Fab Sheets - Area D Lower & Upper Suite Lvl (Seq 1121)	5	20-Sep-18	26-Sep-18	37
S4C2-5P4J10	Bowl Steel - Scrub/Prepare Fab Sheets - Area C Lower & Upper Suite Lvl (Seq 1119)	5	20-Sep-18	26-Sep-18	44
S4C3-5P4J10	Bowl Steel - Scrub/Prepare Fab Sheets - Area C Lower & Upper Suite Lvl (Seq 1126)	5	20-Sep-18	26-Sep-18	37
S4C5-5P4J10	Bowl Steel - Scrub/Prepare Fab Sheets - Area C Lower & Upper Suite Lvl (Seq 1120)	5	20-Sep-18	26-Sep-18	41
S4C4-5P4J10	Bowl Steel - Scrub/Prepare Fab Sheets - Area C Lower & Upper Suite Lvl (Seq 1127)	5	04-Oct-18	10-Oct-18	57
S4F0-5P4F	Bowl Steel - Subcontractor Fabricate & Paint - Area F Lower & Upper Suite Lvl (Seq 1107)	40	07-Jun-18	02-Aug-18	41
S4A0-5P4F	Bowl Steel - Subcontractor Fabricate & Paint - Area A Lower & Upper Suite Lvl (Seq 1108)	40	13-Jun-18	08-Aug-18	32
S4A1-5P4F	Bowl Steel - Subcontractor Fabricate & Paint - Area A Lower & Upper Suite Lvl (Seq 1109)	40	14-Jun-18	09-Aug-18	36
S4B0-5P4F	Bowl Steel - Subcontractor Fabricate & Paint - Area B Lower & Upper Suite Lvl (Seq 1111)	40	21-Jun-18	16-Aug-18	28
S4F1-5P4F	Bowl Steel - Subcontractor Fabricate & Paint - Area F Lower & Upper Suite Lvl (Seq 1106)	40	27-Jun-18	22-Aug-18	32
S4A2-5P4F	Bowl Steel - Subcontractor Fabricate & Paint - Area A Lower & Upper Suite Lvl (Seq 1110)	40	05-Jul-18	29-Aug-18	27
S4E0-5P4F	Bowl Steel - Subcontractor Fabricate & Paint - Area E Lower & Upper Suite Lvl (Seq 1103)	40	12-Jul-18	06-Sep-18	26
S4B0-5P4F10	Bowl Steel - Subcontractor Fabricate & Paint - Area B Lower & Upper Suite Lvl (Seq 1112)	40	12-Jul-18	06-Sep-18	20
S4F2-5P4F	Bowl Steel - Subcontractor Fabricate & Paint - Area F Lower & Upper Suite Lvl (Seq 1105)	40	12-Jul-18	06-Sep-18	27
S4E0-5P4F10	Bowl Steel - Subcontractor Fabricate & Paint - Area E Lower & Upper Suite Lvl (Seq 1104)	40	19-Jul-18	13-Sep-18	27
S4E0-5P4F20	Bowl Steel - Subcontractor Fabricate & Paint - Area E Lower & Upper Suite Lvl (Seq 1102)	40	19-Jul-18	13-Sep-18	26
S4E3-5P4F20	Bowl Steel - Subcontractor Fabricate & Paint - Area E Lower & Upper Suite Lvl (Seq 1101)	40	19-Jul-18	13-Sep-18	29
S4B0-5P4F20	Bowl Steel - Subcontractor Fabricate & Paint - Area B Lower & Upper Suite Lvl (Seq 1113)	40	08-Aug-18	03-Oct-18	19
S4B3-5P4F20	Bowl Steel - Subcontractor Fabricate & Paint - Area B Lower & Upper Suite Lvl (Seq 1114)	40	08-Aug-18	03-Oct-18	22
S4B4-5P4F20	Bowl Steel - Subcontractor Fabricate & Paint - Area B Lower & Upper Suite Lvl (Seq 1115)	40	15-Aug-18	10-Oct-18	22
S4C0-5P4F	Bowl Steel - Subcontractor Fabricate & Paint - Area C Lower & Upper Suite Lvl (Seq 1117)	40	29-Aug-18	24-Oct-18	26
S4E4-5P4F20	Bowl Steel - Subcontractor Fabricate & Paint - Area E Lower & Upper Suite Lvl (Seq 1125)	40	29-Aug-18	24-Oct-18	20
S4B5-5P4F20	Bowl Steel - Subcontractor Fabricate & Paint - Area B Lower & Upper Suite Lvl (Seq 1116)	40	29-Aug-18	24-Oct-18	21
S4E5-5P4F20	Bowl Steel - Subcontractor Fabricate & Paint - Area E Lower & Upper Suite Lvl (Seq 1124)	40	06-Sep-18	31-Oct-18	19
S4E6-5P4F20	Bowl Steel - Subcontractor Fabricate & Paint - Area E Lower & Upper Suite Lvl (Seq 1123)	40	06-Sep-18	31-Oct-18	26
S4C0-5P4F10	Bowl Steel - Subcontractor Fabricate & Paint - Area C Lower & Upper Suite Lvl (Seq 1118)	40	13-Sep-18	07-Nov-18	22
S4D0-5P4F	Bowl Steel - Subcontractor Fabricate & Paint - Area D Lower & Upper Suite Lvl (Seq 1122)	40	20-Sep-18	14-Nov-18	37
S4D0-5P4F10	Bowl Steel - Subcontractor Fabricate & Paint - Area D Lower & Upper Suite Lvl (Seq 1121)	40	27-Sep-18	21-Nov-18	37
S4C2-5P4F10	Bowl Steel - Subcontractor Fabricate & Paint - Area C Lower & Upper Suite Lvl (Seq 1119)	40	27-Sep-18	21-Nov-18	44
S4C3-5P4F10	Bowl Steel - Subcontractor Fabricate & Paint - Area C Lower & Upper Suite Lvl (Seq 1126)	40	27-Sep-18	21-Nov-18	37
S4C5-5P4F10	Bowl Steel - Subcontractor Fabricate & Paint - Area C Lower & Upper Suite Lvl (Seq 1120)	40	27-Sep-18	21-Nov-18	41
S4C4-5P4F10	Bowl Steel - Subcontractor Fabricate & Paint - Area C Lower & Upper Suite Lvl (Seq 1127)	40	11-Oct-18	07-Dec-18	57
S4A0-5P4F1	Bowl Steel - Subcontractor Deliver - Area A Lower & Upper Suite Lvl (Seq 1108)	3	24-Sep-18	26-Sep-18	1
S4F0-5P4F1	Bowl Steel - Subcontractor Deliver - Area F Lower & Upper Suite Lvl (Seq 1107)	3	24-Sep-18	26-Sep-18	6
S4B0-5P4F21	Bowl Steel - Subcontractor Deliver - Area B Lower & Upper Suite Lvl (Seq 1111)	3	27-Sep-18	01-Oct-18	0
S4A1-5P4F1	Bowl Steel - Subcontractor Deliver - Area A Lower & Upper Suite Lvl (Seq 1109)	3	01-Oct-18	03-Oct-18	1
S4F1-5P4F1	Bowl Steel - Subcontractor Deliver - Area F Lower & Upper Suite Lvl (Seq 1106)	3	01-Oct-18	03-Oct-18	6

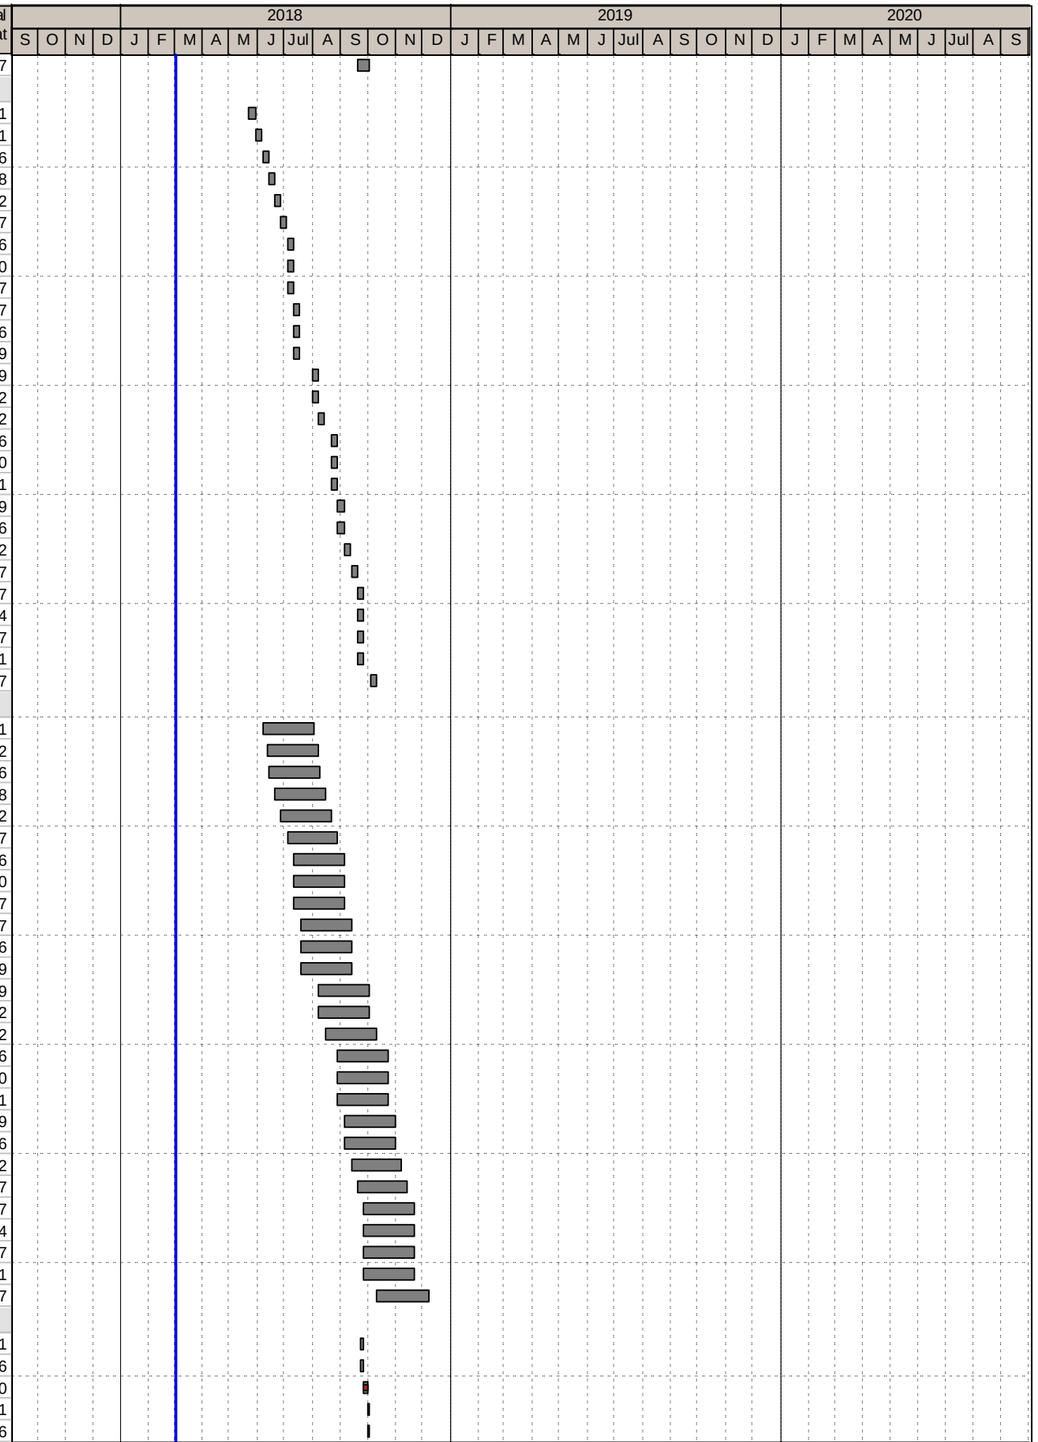

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S4B0-5P4F22	Bowl Steel - Subcontractor Deliver - Area B Lower & Upper Suite Lvl (Seq 1112)	3	05-Oct-18	09-Oct-18	0
S4A2-5P4F1	Bowl Steel - Subcontractor Deliver - Area A Lower & Upper Suite Lvl (Seq 1110)	3	08-Oct-18	10-Oct-18	1
S4F2-5P4F1	Bowl Steel - Subcontractor Deliver - Area F Lower & Upper Suite Lvl (Seq 1105)	3	08-Oct-18	10-Oct-18	6
S4E0-5P4F21	Bowl Steel - Subcontractor Deliver - Area E Lower & Upper Suite Lvl (Seq 1103)	3	12-Oct-18	16-Oct-18	1
S4E0-5P4F22	Bowl Steel - Subcontractor Deliver - Area E Lower & Upper Suite Lvl (Seq 1104)	3	15-Oct-18	17-Oct-18	6
S4E0-5P4F23	Bowl Steel - Subcontractor Deliver - Area E Lower & Upper Suite Lvl (Seq 1102)	3	19-Oct-18	23-Oct-18	1
S4E3-5P4F23	Bowl Steel - Subcontractor Deliver - Area E Lower & Upper Suite Lvl (Seq 1101)	3	24-Oct-18	26-Oct-18	1
S4B0-5P4F23	Bowl Steel - Subcontractor Deliver - Area B Lower & Upper Suite Lvl (Seq 1113)	3	30-Oct-18	01-Nov-18	1
S4B3-5P4F23	Bowl Steel - Subcontractor Deliver - Area B Lower & Upper Suite Lvl (Seq 1114)	3	02-Nov-18	06-Nov-18	1
S4B4-5P4F23	Bowl Steel - Subcontractor Deliver - Area B Lower & Upper Suite Lvl (Seq 1115)	3	09-Nov-18	13-Nov-18	1
S4B5-5P4F23	Bowl Steel - Subcontractor Deliver - Area B Lower & Upper Suite Lvl (Seq 1116)	3	21-Nov-18	27-Nov-18	2
S4E4-5P4F23	Bowl Steel - Subcontractor Deliver - Area E Lower & Upper Suite Lvl (Seq 1125)	3	26-Nov-18	28-Nov-18	0
S4E5-5P4F23	Bowl Steel - Subcontractor Deliver - Area E Lower & Upper Suite Lvl (Seq 1124)	3	30-Nov-18	04-Dec-18	0
S4C0-5P4F11	Bowl Steel - Subcontractor Deliver - Area C Lower & Upper Suite Lvl (Seq 1117)	3	03-Dec-18	05-Dec-18	1
S4E6-5P4F23	Bowl Steel - Subcontractor Deliver - Area E Lower & Upper Suite Lvl (Seq 1123)	3	05-Dec-18	07-Dec-18	4
S4C0-5P4F12	Bowl Steel - Subcontractor Deliver - Area C Lower & Upper Suite Lvl (Seq 1118)	3	11-Dec-18	13-Dec-18	1
S4D0-5P4F11	Bowl Steel - Subcontractor Deliver - Area D Lower & Upper Suite Lvl (Seq 1122)	3	27-Dec-18	31-Dec-18	10
S4D0-5P4F12	Bowl Steel - Subcontractor Deliver - Area D Lower & Upper Suite Lvl (Seq 1121)	3	07-Jan-19	09-Jan-19	9
S4C3-5P4F12	Bowl Steel - Subcontractor Deliver - Area C Lower & Upper Suite Lvl (Seq 1126)	3	07-Jan-19	09-Jan-19	9
S4C5-5P4F12	Bowl Steel - Subcontractor Deliver - Area C Lower & Upper Suite Lvl (Seq 1120)	3	11-Jan-19	15-Jan-19	9
S4C2-5P4F12	Bowl Steel - Subcontractor Deliver - Area C Lower & Upper Suite Lvl (Seq 1119)	3	16-Jan-19	18-Jan-19	9
S4C4-5P4F12	Bowl Steel - Subcontractor Deliver - Area C Lower & Upper Suite Lvl (Seq 1127)	3	28-Jan-19	30-Jan-19	24
250/300 Upper Mezz & Upper Conc					
Submit					
S6A0-5P4S	Bowl Steel - Develop/Submit Shop Dwgs - Area A Upper Mezz & Upper Conc (Seq 2209)	20	18-May-18	15-Jun-18	12
S6F0-5P4S	Bowl Steel - Develop/Submit Shop Dwgs - Area F Upper Mezz & Upper Conc (Seq 2205)	20	25-May-18	22-Jun-18	12
S6A1-5P4S	Bowl Steel - Develop/Submit Shop Dwgs - Area A Upper Mezz & Upper Conc (Seq 2210)	20	25-May-18	22-Jun-18	12
S6B0-5P4S	Bowl Steel - Develop/Submit Shop Dwgs - Area B Upper Mezz & Upper Conc (Seq 2211)	20	15-Jun-18	13-Jul-18	12
S6B0-5P4S10	Bowl Steel - Develop/Submit Shop Dwgs - Area B Upper Mezz & Upper Conc (Seq 2212)	20	15-Jun-18	13-Jul-18	14
S6F1-5P4S	Bowl Steel - Develop/Submit Shop Dwgs - Area F Upper Mezz & Upper Conc (Seq 2204)	20	15-Jun-18	13-Jul-18	14
S6E0-5P4S	Bowl Steel - Develop/Submit Shop Dwgs - Area E Upper Mezz & Upper Conc (Seq 2203)	20	22-Jun-18	20-Jul-18	16
S6B0-5P4S20	Bowl Steel - Develop/Submit Shop Dwgs - Area B Upper Mezz & Upper Conc (Seq 2213)	20	22-Jun-18	20-Jul-18	16
S6E0-5P4S10	Bowl Steel - Develop/Submit Shop Dwgs - Area E Upper Mezz & Upper Conc (Seq 2202)	20	29-Jun-18	27-Jul-18	19
S6B3-5P4S20	Bowl Steel - Develop/Submit Shop Dwgs - Area B Upper Mezz & Upper Conc (Seq 2214)	20	29-Jun-18	27-Jul-18	16
S6B4-5P4S20	Bowl Steel - Develop/Submit Shop Dwgs - Area B Upper Mezz & Upper Conc (Seq 2215)	20	29-Jun-18	27-Jul-18	19
S6E0-5P4S20	Bowl Steel - Develop/Submit Shop Dwgs - Area E Upper Mezz & Upper Conc (Seq 2201)	20	09-Jul-18	03-Aug-18	19
S6B5-5P4S20	Bowl Steel - Develop/Submit Shop Dwgs - Area B Upper Mezz & Upper Conc (Seq 2216)	20	23-Jul-18	17-Aug-18	27
S6E3-5P4S20	Bowl Steel - Develop/Submit Shop Dwgs - Area E Upper Mezz & Upper Conc (Seq 2225)	20	23-Jul-18	17-Aug-18	27
S6E4-5P4S20	Bowl Steel - Develop/Submit Shop Dwgs - Area E Upper Mezz & Upper Conc (Seq 2224)	20	23-Jul-18	17-Aug-18	27
S6C0-5P4S	Bowl Steel - Develop/Submit Shop Dwgs - Area C Upper Mezz & Upper Conc (Seq 2217)	20	06-Aug-18	31-Aug-18	43
S6D0-5P4S	Bowl Steel - Develop/Submit Shop Dwgs - Area D Upper Mezz & Upper Conc (Seq 2223)	20	13-Aug-18	10-Sep-18	43
S6C0-5P4S10	Bowl Steel - Develop/Submit Shop Dwgs - Area C Upper Mezz & Upper Conc (Seq 2218)	20	13-Aug-18	10-Sep-18	43
S6D0-5P4S10	Bowl Steel - Develop/Submit Shop Dwgs - Area D Upper Mezz & Upper Conc (Seq 2222)	20	13-Aug-18	10-Sep-18	47
S6C2-5P4S10	Bowl Steel - Develop/Submit Shop Dwgs - Area C Upper Mezz & Upper Conc (Seq 2227)	20	13-Aug-18	10-Sep-18	43
S6C3-5P4S10	Bowl Steel - Develop/Submit Shop Dwgs - Area C Upper Mezz & Upper Conc (Seq 2219)	20	13-Aug-18	10-Sep-18	47
S6C4-5P4S10	Bowl Steel - Develop/Submit Shop Dwgs - Area C Upper Mezz & Upper Conc (Seq 2226)	20	13-Aug-18	10-Sep-18	49
S5D82-5P4S10	Bowl Steel - Develop/Submit Shop Dwgs - Area C/D Scoreboard Steel (Seq 3311)	20	20-Aug-18	17-Sep-18	57
S6D2-5P4S10	Bowl Steel - Develop/Submit Shop Dwgs - Area D Upper Mezz & Upper Conc (Seq 2221)	20	20-Aug-18	17-Sep-18	52
S6C5-5P4S10	Bowl Steel - Develop/Submit Shop Dwgs - Area C Upper Mezz & Upper Conc (Seq 2220)	20	20-Aug-18	17-Sep-18	54
Mortenson Review					
S6A0-5P4R	Bowl Steel - MMCJV Review Shop Drawings - Area A Upper Mezz & Upper Conc (Seq 2209)	2	18-Jun-18	19-Jun-18	24
S6F0-5P4R	Bowl Steel - MMCJV Review Shop Drawings - Area F Upper Mezz & Upper Conc (Seq 2205)	2	25-Jun-18	26-Jun-18	32
S6A1-5P4R	Bowl Steel - MMCJV Review Shop Drawings - Area A Upper Mezz & Upper Conc (Seq 2210)	2	25-Jun-18	26-Jun-18	23
S6B0-5P4R	Bowl Steel - MMCJV Review Shop Drawings - Area B Upper Mezz & Upper Conc (Seq 2211)	2	16-Jul-18	17-Jul-18	12
S6B0-5P4R10	Bowl Steel - MMCJV Review Shop Drawings - Area B Upper Mezz & Upper Conc (Seq 2212)	2	16-Jul-18	17-Jul-18	16
S6F1-5P4R	Bowl Steel - MMCJV Review Shop Drawings - Area F Upper Mezz & Upper Conc (Seq 2204)	2	16-Jul-18	17-Jul-18	23
S6E0-5P4R	Bowl Steel - MMCJV Review Shop Drawings - Area E Upper Mezz & Upper Conc (Seq 2203)	2	23-Jul-18	24-Jul-18	26
S6B0-5P4R20	Bowl Steel - MMCJV Review Shop Drawings - Area B Upper Mezz & Upper Conc (Seq 2213)	2	23-Jul-18	24-Jul-18	18
S6E0-5P4R10	Bowl Steel - MMCJV Review Shop Drawings - Area E Upper Mezz & Upper Conc (Seq 2202)	2	30-Jul-18	31-Jul-18	26
S6B3-5P4R20	Bowl Steel - MMCJV Review Shop Drawings - Area B Upper Mezz & Upper Conc (Seq 2214)	2	30-Jul-18	31-Jul-18	20
S6B4-5P4R20	Bowl Steel - MMCJV Review Shop Drawings - Area B Upper Mezz & Upper Conc (Seq 2215)	2	30-Jul-18	31-Jul-18	23
S6E0-5P4R20	Bowl Steel - MMCJV Review Shop Drawings - Area E Upper Mezz & Upper Conc (Seq 2201)	2	06-Aug-18	07-Aug-18	23
S6B5-5P4R20	Bowl Steel - MMCJV Review Shop Drawings - Area B Upper Mezz & Upper Conc (Seq 2216)	2	20-Aug-18	21-Aug-18	27

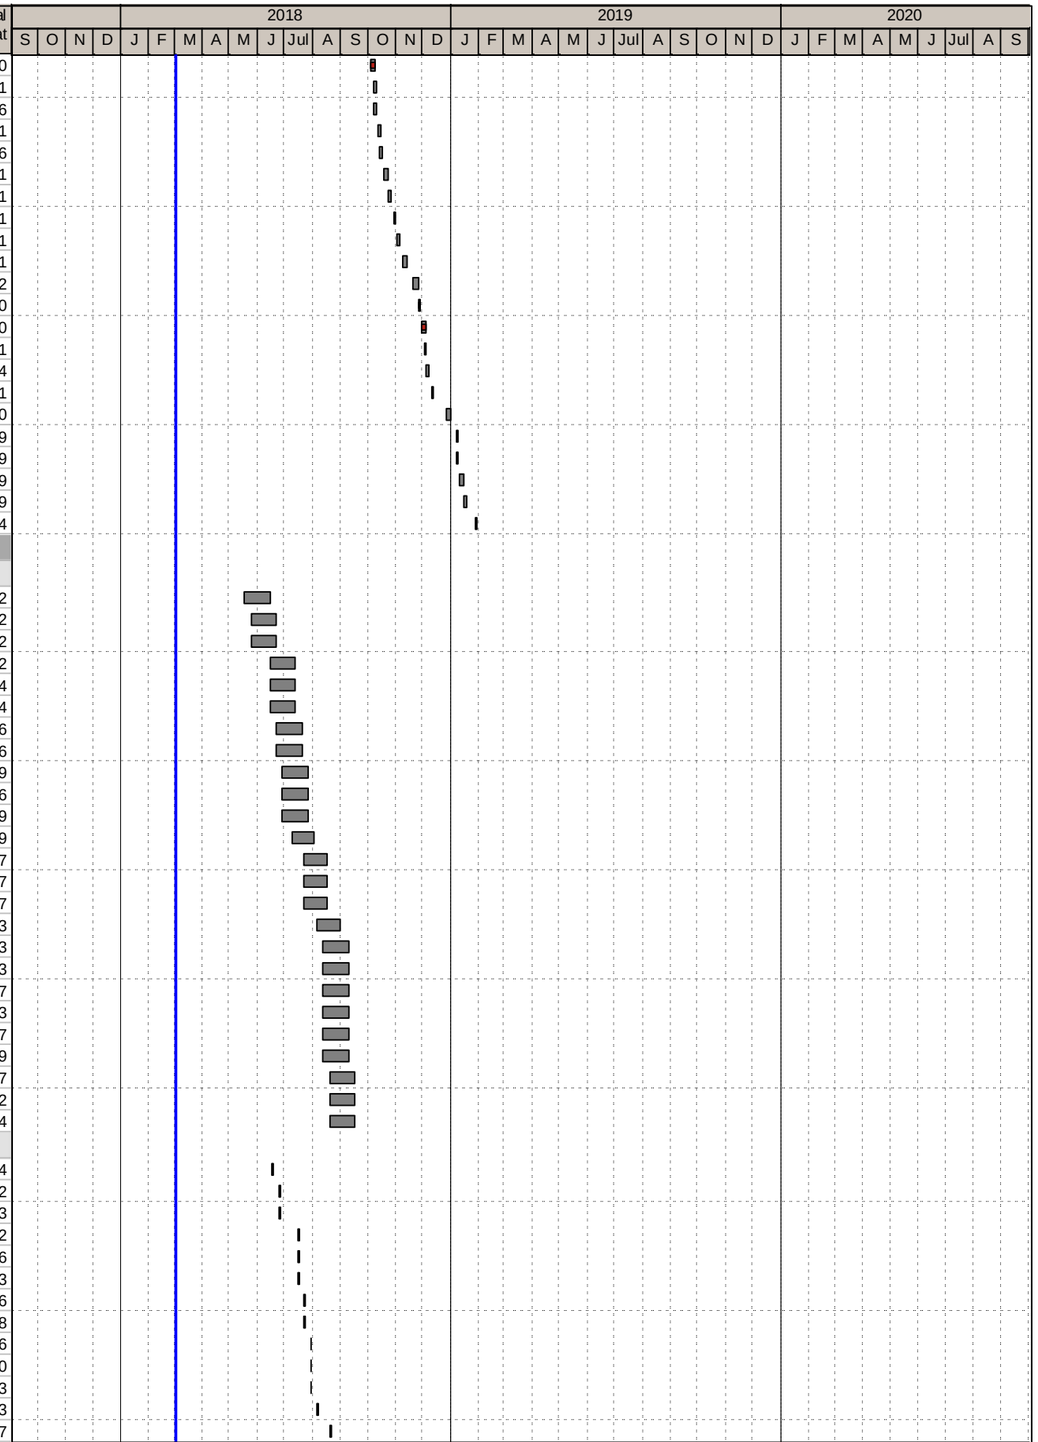

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S6E3-5P4R20	Bowl Steel - MMCJV Review Shop Drawings - Area E Upper Mezz & Upper Conc (Seq 2225)	2	20-Aug-18	21-Aug-18	27
S6E4-5P4R20	Bowl Steel - MMCJV Review Shop Drawings - Area E Upper Mezz & Upper Conc (Seq 2224)	2	20-Aug-18	21-Aug-18	30
S6C0-5P4R	Bowl Steel - MMCJV Review Shop Drawings - Area C Upper Mezz & Upper Conc (Seq 2217)	2	04-Sep-18	05-Sep-18	48
S6D0-5P4R	Bowl Steel - MMCJV Review Shop Drawings - Area D Upper Mezz & Upper Conc (Seq 2223)	2	11-Sep-18	12-Sep-18	43
S6C0-5P4R10	Bowl Steel - MMCJV Review Shop Drawings - Area C Upper Mezz & Upper Conc (Seq 2218)	2	11-Sep-18	12-Sep-18	49
S6D0-5P4R10	Bowl Steel - MMCJV Review Shop Drawings - Area D Upper Mezz & Upper Conc (Seq 2222)	2	11-Sep-18	12-Sep-18	47
S6C2-5P4R10	Bowl Steel - MMCJV Review Shop Drawings - Area C Upper Mezz & Upper Conc (Seq 2227)	2	11-Sep-18	12-Sep-18	62
S6C3-5P4R10	Bowl Steel - MMCJV Review Shop Drawings - Area C Upper Mezz & Upper Conc (Seq 2219)	2	11-Sep-18	12-Sep-18	54
S6C4-5P4R10	Bowl Steel - MMCJV Review Shop Drawings - Area C Upper Mezz & Upper Conc (Seq 2226)	2	11-Sep-18	12-Sep-18	56
S5D82-5P4R10	Bowl Steel - MMCJV Review Shop Drawings - Area C/D Scoreboard Steel (Seq 3311)	2	18-Sep-18	19-Sep-18	64
S6D2-5P4R10	Bowl Steel - MMCJV Review Shop Drawings - Area D Upper Mezz & Upper Conc (Seq 2221)	2	18-Sep-18	19-Sep-18	52
S6C5-5P4R10	Bowl Steel - MMCJV Review Shop Drawings - Area C Upper Mezz & Upper Conc (Seq 2220)	2	18-Sep-18	19-Sep-18	54
Approve					
S6A0-5P4A	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area A Upper Mezz & Upper Conc (Seq 2209)	10	20-Jun-18	03-Jul-18	24
S6F0-5P4A	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area F Upper Mezz & Upper Conc (Seq 2205)	10	27-Jun-18	11-Jul-18	32
S6A1-5P4A	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area A Upper Mezz & Upper Conc (Seq 2210)	10	27-Jun-18	11-Jul-18	23
S6B0-5P4A	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area B Upper Mezz & Upper Conc (Seq 2211)	10	18-Jul-18	31-Jul-18	12
S6B0-5P4A10	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area B Upper Mezz & Upper Conc (Seq 2212)	10	18-Jul-18	31-Jul-18	16
S6F1-5P4A	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area F Upper Mezz & Upper Conc (Seq 2204)	10	18-Jul-18	31-Jul-18	23
S6E0-5P4A	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area E Upper Mezz & Upper Conc (Seq 2203)	10	25-Jul-18	07-Aug-18	26
S6B0-5P4A20	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area B Upper Mezz & Upper Conc (Seq 2213)	10	25-Jul-18	07-Aug-18	18
S6E0-5P4A10	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area E Upper Mezz & Upper Conc (Seq 2202)	10	01-Aug-18	14-Aug-18	26
S6B3-5P4A20	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area B Upper Mezz & Upper Conc (Seq 2214)	10	01-Aug-18	14-Aug-18	20
S6B4-5P4A20	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area B Upper Mezz & Upper Conc (Seq 2215)	10	01-Aug-18	14-Aug-18	23
S6E0-5P4A20	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area E Upper Mezz & Upper Conc (Seq 2201)	10	08-Aug-18	21-Aug-18	23
S6B5-5P4A20	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area B Upper Mezz & Upper Conc (Seq 2216)	10	22-Aug-18	05-Sep-18	27
S6E3-5P4A20	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area E Upper Mezz & Upper Conc (Seq 2225)	10	22-Aug-18	05-Sep-18	27
S6E4-5P4A20	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area E Upper Mezz & Upper Conc (Seq 2224)	10	22-Aug-18	05-Sep-18	30
S6C0-5P4A	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area C Upper Mezz & Upper Conc (Seq 2217)	10	06-Sep-18	19-Sep-18	48
S6D0-5P4A	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area D Upper Mezz & Upper Conc (Seq 2223)	10	13-Sep-18	26-Sep-18	43
S6C0-5P4A10	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area C Upper Mezz & Upper Conc (Seq 2218)	10	13-Sep-18	26-Sep-18	49
S6D0-5P4A10	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area D Upper Mezz & Upper Conc (Seq 2222)	10	13-Sep-18	26-Sep-18	47
S6C2-5P4A10	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area C Upper Mezz & Upper Conc (Seq 2227)	10	13-Sep-18	26-Sep-18	62
S6C3-5P4A10	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area C Upper Mezz & Upper Conc (Seq 2219)	10	13-Sep-18	26-Sep-18	54
S6C4-5P4A10	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area C Upper Mezz & Upper Conc (Seq 2226)	10	13-Sep-18	26-Sep-18	56
S5D82-5P4A10	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area C/D Scoreboard Steel (Seq 3311)	10	20-Sep-18	03-Oct-18	64
S6D2-5P4A10	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area D Upper Mezz & Upper Conc (Seq 2221)	10	20-Sep-18	03-Oct-18	52
S6C5-5P4A10	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area C Upper Mezz & Upper Conc (Seq 2220)	10	20-Sep-18	03-Oct-18	54
S6A0-5P4J	Bowl Steel - Scrub/Prepare Fab Sheets - Area A Upper Mezz & Upper Conc (Seq 2209)	5	05-Jul-18	11-Jul-18	24
S6F0-5P4J	Bowl Steel - Scrub/Prepare Fab Sheets - Area F Upper Mezz & Upper Conc (Seq 2205)	5	12-Jul-18	18-Jul-18	32
S6A1-5P4J	Bowl Steel - Scrub/Prepare Fab Sheets - Area A Upper Mezz & Upper Conc (Seq 2210)	5	12-Jul-18	18-Jul-18	23
S6B0-5P4J	Bowl Steel - Scrub/Prepare Fab Sheets - Area B Upper Mezz & Upper Conc (Seq 2211)	5	01-Aug-18	07-Aug-18	12
S6B0-5P4J10	Bowl Steel - Scrub/Prepare Fab Sheets - Area B Upper Mezz & Upper Conc (Seq 2212)	5	01-Aug-18	07-Aug-18	16
S6F1-5P4J	Bowl Steel - Scrub/Prepare Fab Sheets - Area F Upper Mezz & Upper Conc (Seq 2204)	5	01-Aug-18	07-Aug-18	23
S6E0-5P4J	Bowl Steel - Scrub/Prepare Fab Sheets - Area E Upper Mezz & Upper Conc (Seq 2203)	5	08-Aug-18	14-Aug-18	26
S6B0-5P4J20	Bowl Steel - Scrub/Prepare Fab Sheets - Area B Upper Mezz & Upper Conc (Seq 2213)	5	08-Aug-18	14-Aug-18	18
S6E0-5P4J10	Bowl Steel - Scrub/Prepare Fab Sheets - Area E Upper Mezz & Upper Conc (Seq 2202)	5	15-Aug-18	21-Aug-18	26
S6B3-5P4J20	Bowl Steel - Scrub/Prepare Fab Sheets - Area B Upper Mezz & Upper Conc (Seq 2214)	5	15-Aug-18	21-Aug-18	20
S6B4-5P4J20	Bowl Steel - Scrub/Prepare Fab Sheets - Area B Upper Mezz & Upper Conc (Seq 2215)	5	15-Aug-18	21-Aug-18	23
S6E0-5P4J20	Bowl Steel - Scrub/Prepare Fab Sheets - Area E Upper Mezz & Upper Conc (Seq 2201)	5	22-Aug-18	28-Aug-18	23
S6B5-5P4J20	Bowl Steel - Scrub/Prepare Fab Sheets - Area B Upper Mezz & Upper Conc (Seq 2216)	5	06-Sep-18	12-Sep-18	27
S6E3-5P4J20	Bowl Steel - Scrub/Prepare Fab Sheets - Area E Upper Mezz & Upper Conc (Seq 2225)	5	06-Sep-18	12-Sep-18	27
S6E4-5P4J20	Bowl Steel - Scrub/Prepare Fab Sheets - Area E Upper Mezz & Upper Conc (Seq 2224)	5	06-Sep-18	12-Sep-18	30
S6C0-5P4J	Bowl Steel - Scrub/Prepare Fab Sheets - Area C Upper Mezz & Upper Conc (Seq 2217)	5	20-Sep-18	26-Sep-18	48
S6D0-5P4J	Bowl Steel - Scrub/Prepare Fab Sheets - Area D Upper Mezz & Upper Conc (Seq 2223)	5	27-Sep-18	03-Oct-18	43
S6C0-5P4J10	Bowl Steel - Scrub/Prepare Fab Sheets - Area C Upper Mezz & Upper Conc (Seq 2218)	5	27-Sep-18	03-Oct-18	49
S6D0-5P4J10	Bowl Steel - Scrub/Prepare Fab Sheets - Area D Upper Mezz & Upper Conc (Seq 2222)	5	27-Sep-18	03-Oct-18	47
S6C2-5P4J10	Bowl Steel - Scrub/Prepare Fab Sheets - Area C Upper Mezz & Upper Conc (Seq 2227)	5	27-Sep-18	03-Oct-18	62
S6C3-5P4J10	Bowl Steel - Scrub/Prepare Fab Sheets - Area C Upper Mezz & Upper Conc (Seq 2219)	5	27-Sep-18	03-Oct-18	54
S6C4-5P4J10	Bowl Steel - Scrub/Prepare Fab Sheets - Area C Upper Mezz & Upper Conc (Seq 2226)	5	27-Sep-18	03-Oct-18	56
S5D82-5P4J10	Bowl Steel - Scrub/Prepare Fab Sheets - Area C/D Scoreboard Steel (Seq 3311)	5	04-Oct-18	10-Oct-18	64
S6D2-5P4J10	Bowl Steel - Scrub/Prepare Fab Sheets - Area D Upper Mezz & Upper Conc (Seq 2221)	5	04-Oct-18	10-Oct-18	52

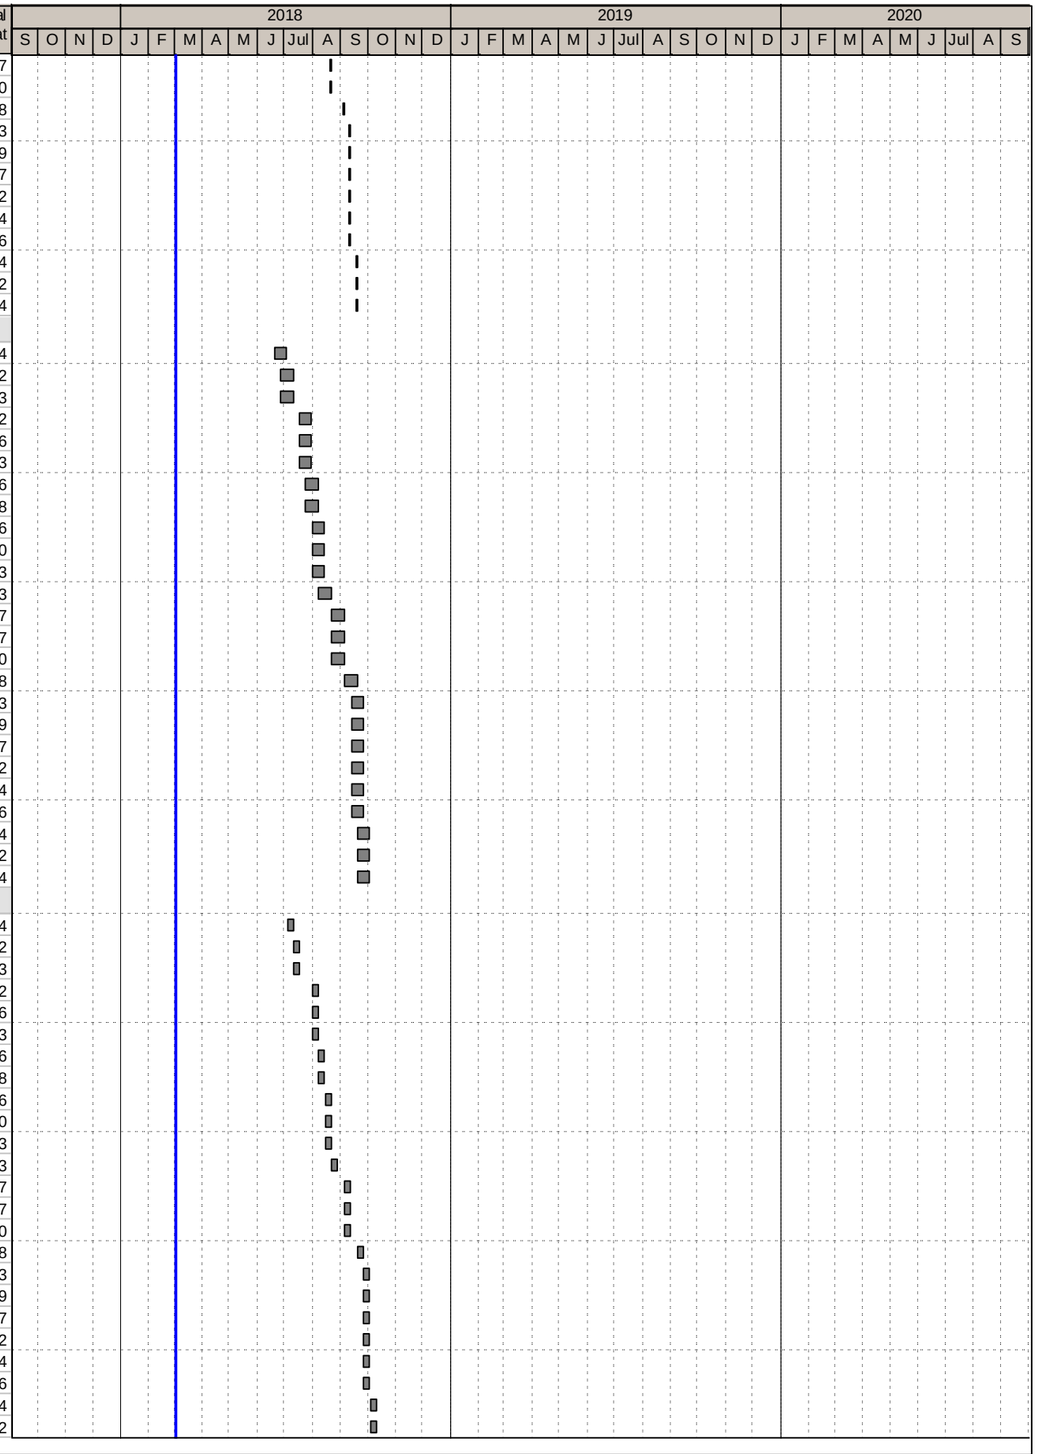

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S6C5-5P4J10	Bowl Steel - Scrub/Prepare Fab Sheets - Area C Upper Mezz & Upper Conc (Seq 2220)	5	04-Oct-18	10-Oct-18	54
S6A0-5P4F	Bowl Steel - Subcontractor Fabricate & Paint - Area A Upper Mezz & Upper Conc (Seq 2209)	40	12-Jul-18	06-Sep-18	24
S6F0-5P4F	Bowl Steel - Subcontractor Fabricate & Paint - Area F Upper Mezz & Upper Conc (Seq 2205)	40	19-Jul-18	13-Sep-18	32
S6A1-5P4F	Bowl Steel - Subcontractor Fabricate & Paint - Area A Upper Mezz & Upper Conc (Seq 2210)	40	19-Jul-18	13-Sep-18	23
S6B0-5P4F	Bowl Steel - Subcontractor Fabricate & Paint - Area B Upper Mezz & Upper Conc (Seq 2211)	40	08-Aug-18	03-Oct-18	12
S6B0-5P4F10	Bowl Steel - Subcontractor Fabricate & Paint - Area B Upper Mezz & Upper Conc (Seq 2212)	40	08-Aug-18	03-Oct-18	16
S6F1-5P4F	Bowl Steel - Subcontractor Fabricate & Paint - Area F Upper Mezz & Upper Conc (Seq 2204)	40	08-Aug-18	03-Oct-18	23
S6E0-5P4F	Bowl Steel - Subcontractor Fabricate & Paint - Area E Upper Mezz & Upper Conc (Seq 2203)	40	15-Aug-18	10-Oct-18	26
S6B0-5P4F20	Bowl Steel - Subcontractor Fabricate & Paint - Area B Upper Mezz & Upper Conc (Seq 2213)	40	15-Aug-18	10-Oct-18	18
S6E0-5P4F10	Bowl Steel - Subcontractor Fabricate & Paint - Area E Upper Mezz & Upper Conc (Seq 2202)	40	22-Aug-18	17-Oct-18	26
S6B3-5P4F20	Bowl Steel - Subcontractor Fabricate & Paint - Area B Upper Mezz & Upper Conc (Seq 2214)	40	22-Aug-18	17-Oct-18	20
S6B4-5P4F20	Bowl Steel - Subcontractor Fabricate & Paint - Area B Upper Mezz & Upper Conc (Seq 2215)	40	22-Aug-18	17-Oct-18	23
S6E0-5P4F20	Bowl Steel - Subcontractor Fabricate & Paint - Area E Upper Mezz & Upper Conc (Seq 2201)	40	29-Aug-18	24-Oct-18	23
S6B5-5P4F20	Bowl Steel - Subcontractor Fabricate & Paint - Area B Upper Mezz & Upper Conc (Seq 2216)	40	13-Sep-18	07-Nov-18	27
S6E3-5P4F20	Bowl Steel - Subcontractor Fabricate & Paint - Area E Upper Mezz & Upper Conc (Seq 2225)	40	13-Sep-18	07-Nov-18	27
S6E4-5P4F20	Bowl Steel - Subcontractor Fabricate & Paint - Area E Upper Mezz & Upper Conc (Seq 2224)	40	13-Sep-18	07-Nov-18	30
S6C0-5P4F	Bowl Steel - Subcontractor Fabricate & Paint - Area C Upper Mezz & Upper Conc (Seq 2217)	40	27-Sep-18	21-Nov-18	48
S6D0-5P4F	Bowl Steel - Subcontractor Fabricate & Paint - Area D Upper Mezz & Upper Conc (Seq 2223)	40	04-Oct-18	30-Nov-18	43
S6C0-5P4F10	Bowl Steel - Subcontractor Fabricate & Paint - Area C Upper Mezz & Upper Conc (Seq 2218)	40	04-Oct-18	30-Nov-18	49
S6D0-5P4F10	Bowl Steel - Subcontractor Fabricate & Paint - Area D Upper Mezz & Upper Conc (Seq 2222)	40	04-Oct-18	30-Nov-18	47
S6C2-5P4F10	Bowl Steel - Subcontractor Fabricate & Paint - Area C Upper Mezz & Upper Conc (Seq 2227)	40	04-Oct-18	30-Nov-18	62
S6C3-5P4F10	Bowl Steel - Subcontractor Fabricate & Paint - Area C Upper Mezz & Upper Conc (Seq 2219)	40	04-Oct-18	30-Nov-18	54
S6C4-5P4F10	Bowl Steel - Subcontractor Fabricate & Paint - Area C Upper Mezz & Upper Conc (Seq 2226)	40	04-Oct-18	30-Nov-18	56
S5D82-5P4F10	Bowl Steel - Subcontractor Fabricate & Paint - Area C/D Scoreboard Steel (Seq 3311)	40	11-Oct-18	07-Dec-18	64
S6D2-5P4F10	Bowl Steel - Subcontractor Fabricate & Paint - Area D Upper Mezz & Upper Conc (Seq 2221)	40	11-Oct-18	07-Dec-18	52
S6C5-5P4F10	Bowl Steel - Subcontractor Fabricate & Paint - Area C Upper Mezz & Upper Conc (Seq 2220)	40	11-Oct-18	07-Dec-18	54
S6A0-5P4F1	Bowl Steel - Subcontractor Deliver - Area A Upper Mezz & Upper Conc (Seq 2209)	3	11-Oct-18	15-Oct-18	0
S6A1-5P4F1	Bowl Steel - Subcontractor Deliver - Area A Upper Mezz & Upper Conc (Seq 2210)	3	17-Oct-18	19-Oct-18	0
S6F0-5P4F1	Bowl Steel - Subcontractor Deliver - Area F Upper Mezz & Upper Conc (Seq 2205)	3	22-Oct-18	24-Oct-18	6
S6B0-5P4F21	Bowl Steel - Subcontractor Deliver - Area B Upper Mezz & Upper Conc (Seq 2211)	3	22-Oct-18	24-Oct-18	0
S6B0-5P4F22	Bowl Steel - Subcontractor Deliver - Area B Upper Mezz & Upper Conc (Seq 2212)	3	26-Oct-18	30-Oct-18	0
S6F1-5P4F1	Bowl Steel - Subcontractor Deliver - Area F Upper Mezz & Upper Conc (Seq 2204)	3	29-Oct-18	31-Oct-18	6
S6B0-5P4F23	Bowl Steel - Subcontractor Deliver - Area B Upper Mezz & Upper Conc (Seq 2213)	3	06-Nov-18	08-Nov-18	0
S6E0-5P4F21	Bowl Steel - Subcontractor Deliver - Area E Upper Mezz & Upper Conc (Seq 2203)	3	08-Nov-18	12-Nov-18	6
S6B3-5P4F23	Bowl Steel - Subcontractor Deliver - Area B Upper Mezz & Upper Conc (Seq 2214)	3	14-Nov-18	16-Nov-18	1
S6E0-5P4F22	Bowl Steel - Subcontractor Deliver - Area E Upper Mezz & Upper Conc (Seq 2202)	3	15-Nov-18	19-Nov-18	6
S6E0-5P4F23	Bowl Steel - Subcontractor Deliver - Area E Upper Mezz & Upper Conc (Seq 2201)	3	19-Nov-18	21-Nov-18	6
S6B4-5P4F23	Bowl Steel - Subcontractor Deliver - Area B Upper Mezz & Upper Conc (Seq 2215)	3	19-Nov-18	21-Nov-18	1
S6E3-5P4F23	Bowl Steel - Subcontractor Deliver - Area E Upper Mezz & Upper Conc (Seq 2225)	3	13-Dec-18	17-Dec-18	4
S6B5-5P4F23	Bowl Steel - Subcontractor Deliver - Area B Upper Mezz & Upper Conc (Seq 2216)	3	18-Dec-18	20-Dec-18	1
S6E4-5P4F23	Bowl Steel - Subcontractor Deliver - Area E Upper Mezz & Upper Conc (Seq 2224)	3	18-Dec-18	20-Dec-18	4
S6C0-5P4F11	Bowl Steel - Subcontractor Deliver - Area C Upper Mezz & Upper Conc (Seq 2217)	3	07-Jan-19	09-Jan-19	20
S6C0-5P4F12	Bowl Steel - Subcontractor Deliver - Area C Upper Mezz & Upper Conc (Seq 2218)	3	15-Jan-19	17-Jan-19	20
S6C3-5P4F12	Bowl Steel - Subcontractor Deliver - Area C Upper Mezz & Upper Conc (Seq 2219)	3	21-Jan-19	23-Jan-19	21
S6D0-5P4F11	Bowl Steel - Subcontractor Deliver - Area D Upper Mezz & Upper Conc (Seq 2223)	3	22-Jan-19	24-Jan-19	9
S6C4-5P4F12	Bowl Steel - Subcontractor Deliver - Area C Upper Mezz & Upper Conc (Seq 2226)	3	23-Jan-19	25-Jan-19	21
S6D0-5P4F12	Bowl Steel - Subcontractor Deliver - Area D Upper Mezz & Upper Conc (Seq 2222)	3	28-Jan-19	30-Jan-19	9
S6C2-5P4F12	Bowl Steel - Subcontractor Deliver - Area C Upper Mezz & Upper Conc (Seq 2227)	3	28-Jan-19	30-Jan-19	24
S6D2-5P4F12	Bowl Steel - Subcontractor Deliver - Area D Upper Mezz & Upper Conc (Seq 2221)	3	08-Feb-19	12-Feb-19	10
S6C5-5P4F12	Bowl Steel - Subcontractor Deliver - Area C Upper Mezz & Upper Conc (Seq 2220)	3	12-Feb-19	14-Feb-19	10
S5D82-5P4F12	Bowl Steel - Subcontractor Deliver - Area C/D Scoreboard Steel (Seq 3311)	3	27-Feb-19	01-Mar-19	9
310 Upper Stadia Support					
Submit					
S8A0-5P4S	Bowl Steel - Develop/Submit Shop Dwgs - Area A Upper Stadia Support & Press Lvl (Seq 3303)	20	22-Jun-18	20-Jul-18	14
S8F0-5P4S	Bowl Steel - Develop/Submit Shop Dwgs - Area F Upper Stadia Support & Press Lvl (Seq 3302)	20	22-Jun-18	20-Jul-18	16
S8B0-5P4S	Bowl Steel - Develop/Submit Shop Dwgs - Area B Upper Stadia Support & Press Lvl (Seq 3304)	20	29-Jun-18	27-Jul-18	19
S8A1-5P4S	Bowl Steel - Develop/Submit Shop Dwgs - Area A Upper Stadia Support & Press Lvl (Seq 3312)	20	29-Jun-18	27-Jul-18	16
S8F1-5P4S	Bowl Steel - Develop/Submit Shop Dwgs - Area F Upper Stadia Support & Press Lvl (Seq 3313)	20	09-Jul-18	03-Aug-18	19
S8E0-5P4S	Bowl Steel - Develop/Submit Shop Dwgs - Area E Upper Stadia Support & Press Lvl (Seq 3301)	20	16-Jul-18	10-Aug-18	19
S8B0-5P4S10	Bowl Steel - Develop/Submit Shop Dwgs - Area B Upper Stadia Support & Press Lvl (Seq 3305)	20	30-Jul-18	24-Aug-18	27
S8E0-5P4S10	Bowl Steel - Develop/Submit Shop Dwgs - Area E Upper Stadia Support & Press Lvl (Seq 3310)	20	30-Jul-18	24-Aug-18	30

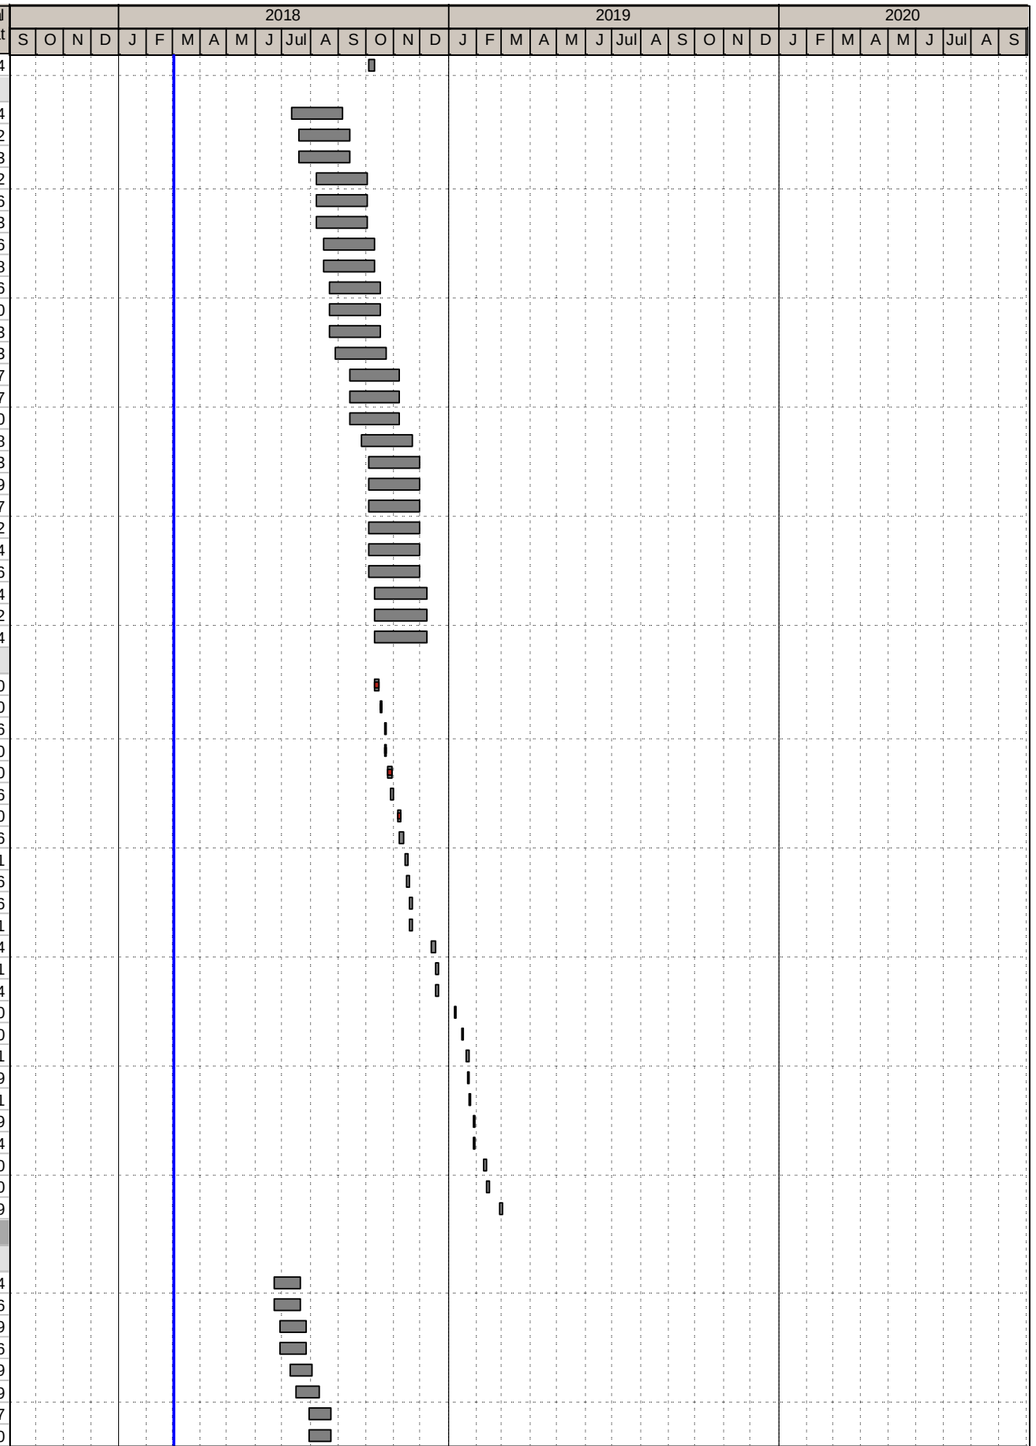

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S8C0-5P4S	Bowl Steel - Develop/Submit Shop Dwgs - Area C Upper Stadia Support & Press Lvl (Seq 3306)	20	13-Aug-18	10-Sep-18	49
S8C1-5P4S	Bowl Steel - Develop/Submit Shop Dwgs - Area C Upper Stadia Support & Press Lvl (Seq 3307)	20	20-Aug-18	17-Sep-18	57
S8C2-5P4S	Bowl Steel - Develop/Submit Shop Dwgs - Area C Upper Stadia Support & Press Lvl (Seq 3314)	20	20-Aug-18	17-Sep-18	57
S8D0-5P4S	Bowl Steel - Develop/Submit Shop Dwgs - Area D Upper Stadia Support & Press Lvl (Seq 3309)	20	20-Aug-18	17-Sep-18	49
S8D1-5P4S	Bowl Steel - Develop/Submit Shop Dwgs - Area D Upper Stadia Support & Press Lvl (Seq 3308)	20	20-Aug-18	17-Sep-18	57
Mortenson Review					
S8A0-5P4R	Bowl Steel - MMCJV Review Shop Drawings - Area A Upper Stadia Support & Press Lvl (Seq 3303)	2	23-Jul-18	24-Jul-18	14
S8F0-5P4R	Bowl Steel - MMCJV Review Shop Drawings - Area F Upper Stadia Support & Press Lvl (Seq 3302)	2	23-Jul-18	24-Jul-18	22
S8B0-5P4R	Bowl Steel - MMCJV Review Shop Drawings - Area B Upper Stadia Support & Press Lvl (Seq 3304)	2	30-Jul-18	31-Jul-18	20
S8A1-5P4R	Bowl Steel - MMCJV Review Shop Drawings - Area A Upper Stadia Support & Press Lvl (Seq 3312)	2	30-Jul-18	31-Jul-18	16
S8F1-5P4R	Bowl Steel - MMCJV Review Shop Drawings - Area F Upper Stadia Support & Press Lvl (Seq 3313)	2	06-Aug-18	07-Aug-18	26
S8E0-5P4R	Bowl Steel - MMCJV Review Shop Drawings - Area E Upper Stadia Support & Press Lvl (Seq 3301)	2	13-Aug-18	14-Aug-18	25
S8B0-5P4R10	Bowl Steel - MMCJV Review Shop Drawings - Area B Upper Stadia Support & Press Lvl (Seq 3305)	2	27-Aug-18	28-Aug-18	27
S8E0-5P4R10	Bowl Steel - MMCJV Review Shop Drawings - Area E Upper Stadia Support & Press Lvl (Seq 3310)	2	27-Aug-18	28-Aug-18	30
S8C0-5P4R	Bowl Steel - MMCJV Review Shop Drawings - Area C Upper Stadia Support & Press Lvl (Seq 3306)	2	11-Sep-18	12-Sep-18	61
S8C1-5P4R	Bowl Steel - MMCJV Review Shop Drawings - Area C Upper Stadia Support & Press Lvl (Seq 3307)	2	18-Sep-18	19-Sep-18	61
S8C2-5P4R	Bowl Steel - MMCJV Review Shop Drawings - Area C Upper Stadia Support & Press Lvl (Seq 3314)	2	18-Sep-18	19-Sep-18	62
S8D0-5P4R	Bowl Steel - MMCJV Review Shop Drawings - Area D Upper Stadia Support & Press Lvl (Seq 3309)	2	18-Sep-18	19-Sep-18	49
S8D1-5P4R	Bowl Steel - MMCJV Review Shop Drawings - Area D Upper Stadia Support & Press Lvl (Seq 3308)	2	18-Sep-18	19-Sep-18	59
Approve					
S8A0-5P4A	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area A Upper Stadia Support & Press Lvl (Seq 3303)	10	25-Jul-18	07-Aug-18	14
S8F0-5P4A	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area F Upper Stadia Support & Press Lvl (Seq 3302)	10	25-Jul-18	07-Aug-18	22
S8B0-5P4A	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area B Upper Stadia Support & Press Lvl (Seq 3304)	10	01-Aug-18	14-Aug-18	20
S8A1-5P4A	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area A Upper Stadia Support & Press Lvl (Seq 3312)	10	01-Aug-18	14-Aug-18	16
S8F1-5P4A	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area F Upper Stadia Support & Press Lvl (Seq 3313)	10	08-Aug-18	21-Aug-18	26
S8E0-5P4A	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area E Upper Stadia Support & Press Lvl (Seq 3301)	10	15-Aug-18	28-Aug-18	25
S8B0-5P4A10	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area B Upper Stadia Support & Press Lvl (Seq 3305)	10	29-Aug-18	12-Sep-18	27
S8E0-5P4A10	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area E Upper Stadia Support & Press Lvl (Seq 3310)	10	29-Aug-18	12-Sep-18	30
S8C0-5P4A	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area C Upper Stadia Support & Press Lvl (Seq 3306)	10	13-Sep-18	26-Sep-18	61
S8C1-5P4A	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area C Upper Stadia Support & Press Lvl (Seq 3307)	10	20-Sep-18	03-Oct-18	61
S8C2-5P4A	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area C Upper Stadia Support & Press Lvl (Seq 3314)	10	20-Sep-18	03-Oct-18	62
S8D0-5P4A	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area D Upper Stadia Support & Press Lvl (Seq 3309)	10	20-Sep-18	03-Oct-18	49
S8D1-5P4A	Bowl Steel - Design Team Review/Approve Shop Dwgs - Area D Upper Stadia Support & Press Lvl (Seq 3308)	10	20-Sep-18	03-Oct-18	59
S8A0-5P4J	Bowl Steel - Scrub/Prepare Fab Sheets - Area A Upper Stadia Support & Press Lvl (Seq 3303)	5	08-Aug-18	14-Aug-18	14
S8F0-5P4J	Bowl Steel - Scrub/Prepare Fab Sheets - Area F Upper Stadia Support & Press Lvl (Seq 3302)	5	08-Aug-18	14-Aug-18	22
S8B0-5P4J	Bowl Steel - Scrub/Prepare Fab Sheets - Area B Upper Stadia Support & Press Lvl (Seq 3304)	5	15-Aug-18	21-Aug-18	20
S8A1-5P4J	Bowl Steel - Scrub/Prepare Fab Sheets - Area A Upper Stadia Support & Press Lvl (Seq 3312)	5	15-Aug-18	21-Aug-18	16
S8F1-5P4J	Bowl Steel - Scrub/Prepare Fab Sheets - Area F Upper Stadia Support & Press Lvl (Seq 3313)	5	22-Aug-18	28-Aug-18	26
S8E0-5P4J	Bowl Steel - Scrub/Prepare Fab Sheets - Area E Upper Stadia Support & Press Lvl (Seq 3301)	5	29-Aug-18	05-Sep-18	25
S8B0-5P4J10	Bowl Steel - Scrub/Prepare Fab Sheets - Area B Upper Stadia Support & Press Lvl (Seq 3305)	5	13-Sep-18	19-Sep-18	27
S8E0-5P4J10	Bowl Steel - Scrub/Prepare Fab Sheets - Area E Upper Stadia Support & Press Lvl (Seq 3310)	5	13-Sep-18	19-Sep-18	30
S8C0-5P4J	Bowl Steel - Scrub/Prepare Fab Sheets - Area C Upper Stadia Support & Press Lvl (Seq 3306)	5	27-Sep-18	03-Oct-18	61
S8C1-5P4J	Bowl Steel - Scrub/Prepare Fab Sheets - Area C Upper Stadia Support & Press Lvl (Seq 3307)	5	04-Oct-18	10-Oct-18	61
S8C2-5P4J	Bowl Steel - Scrub/Prepare Fab Sheets - Area C Upper Stadia Support & Press Lvl (Seq 3314)	5	04-Oct-18	10-Oct-18	62
S8D0-5P4J	Bowl Steel - Scrub/Prepare Fab Sheets - Area D Upper Stadia Support & Press Lvl (Seq 3309)	5	04-Oct-18	10-Oct-18	49
S8D1-5P4J	Bowl Steel - Scrub/Prepare Fab Sheets - Area D Upper Stadia Support & Press Lvl (Seq 3308)	5	04-Oct-18	10-Oct-18	59
S8A0-5P4F	Bowl Steel - Subcontractor Fabricate & Paint - Area A Upper Stadia Support & Press Lvl (Seq 3303)	40	15-Aug-18	10-Oct-18	14
S8F0-5P4F	Bowl Steel - Subcontractor Fabricate & Paint - Area F Upper Stadia Support & Press Lvl (Seq 3302)	40	15-Aug-18	10-Oct-18	22
S8B0-5P4F	Bowl Steel - Subcontractor Fabricate & Paint - Area B Upper Stadia Support & Press Lvl (Seq 3304)	40	22-Aug-18	17-Oct-18	20
S8A1-5P4F	Bowl Steel - Subcontractor Fabricate & Paint - Area A Upper Stadia Support & Press Lvl (Seq 3312)	40	22-Aug-18	17-Oct-18	16
S8F1-5P4F	Bowl Steel - Subcontractor Fabricate & Paint - Area F Upper Stadia Support & Press Lvl (Seq 3313)	40	29-Aug-18	24-Oct-18	26
S8E0-5P4F	Bowl Steel - Subcontractor Fabricate & Paint - Area E Upper Stadia Support & Press Lvl (Seq 3301)	40	06-Sep-18	31-Oct-18	25
S8B0-5P4F10	Bowl Steel - Subcontractor Fabricate & Paint - Area B Upper Stadia Support & Press Lvl (Seq 3305)	40	20-Sep-18	14-Nov-18	27
S8E0-5P4F10	Bowl Steel - Subcontractor Fabricate & Paint - Area E Upper Stadia Support & Press Lvl (Seq 3310)	40	20-Sep-18	14-Nov-18	30
S8C0-5P4F	Bowl Steel - Subcontractor Fabricate & Paint - Area C Upper Stadia Support & Press Lvl (Seq 3306)	40	04-Oct-18	30-Nov-18	61
S8C1-5P4F	Bowl Steel - Subcontractor Fabricate & Paint - Area C Upper Stadia Support & Press Lvl (Seq 3307)	40	11-Oct-18	07-Dec-18	61
S8C2-5P4F	Bowl Steel - Subcontractor Fabricate & Paint - Area C Upper Stadia Support & Press Lvl (Seq 3314)	40	11-Oct-18	07-Dec-18	62
S8D0-5P4F	Bowl Steel - Subcontractor Fabricate & Paint - Area D Upper Stadia Support & Press Lvl (Seq 3309)	40	11-Oct-18	07-Dec-18	49
S8D1-5P4F	Bowl Steel - Subcontractor Fabricate & Paint - Area D Upper Stadia Support & Press Lvl (Seq 3308)	40	11-Oct-18	07-Dec-18	59
S8A0-5P4F2	Bowl Steel - Subcontractor Deliver - Area A Upper Stadia Support & Press Lvl (Seq 3303)	3	31-Oct-18	02-Nov-18	0

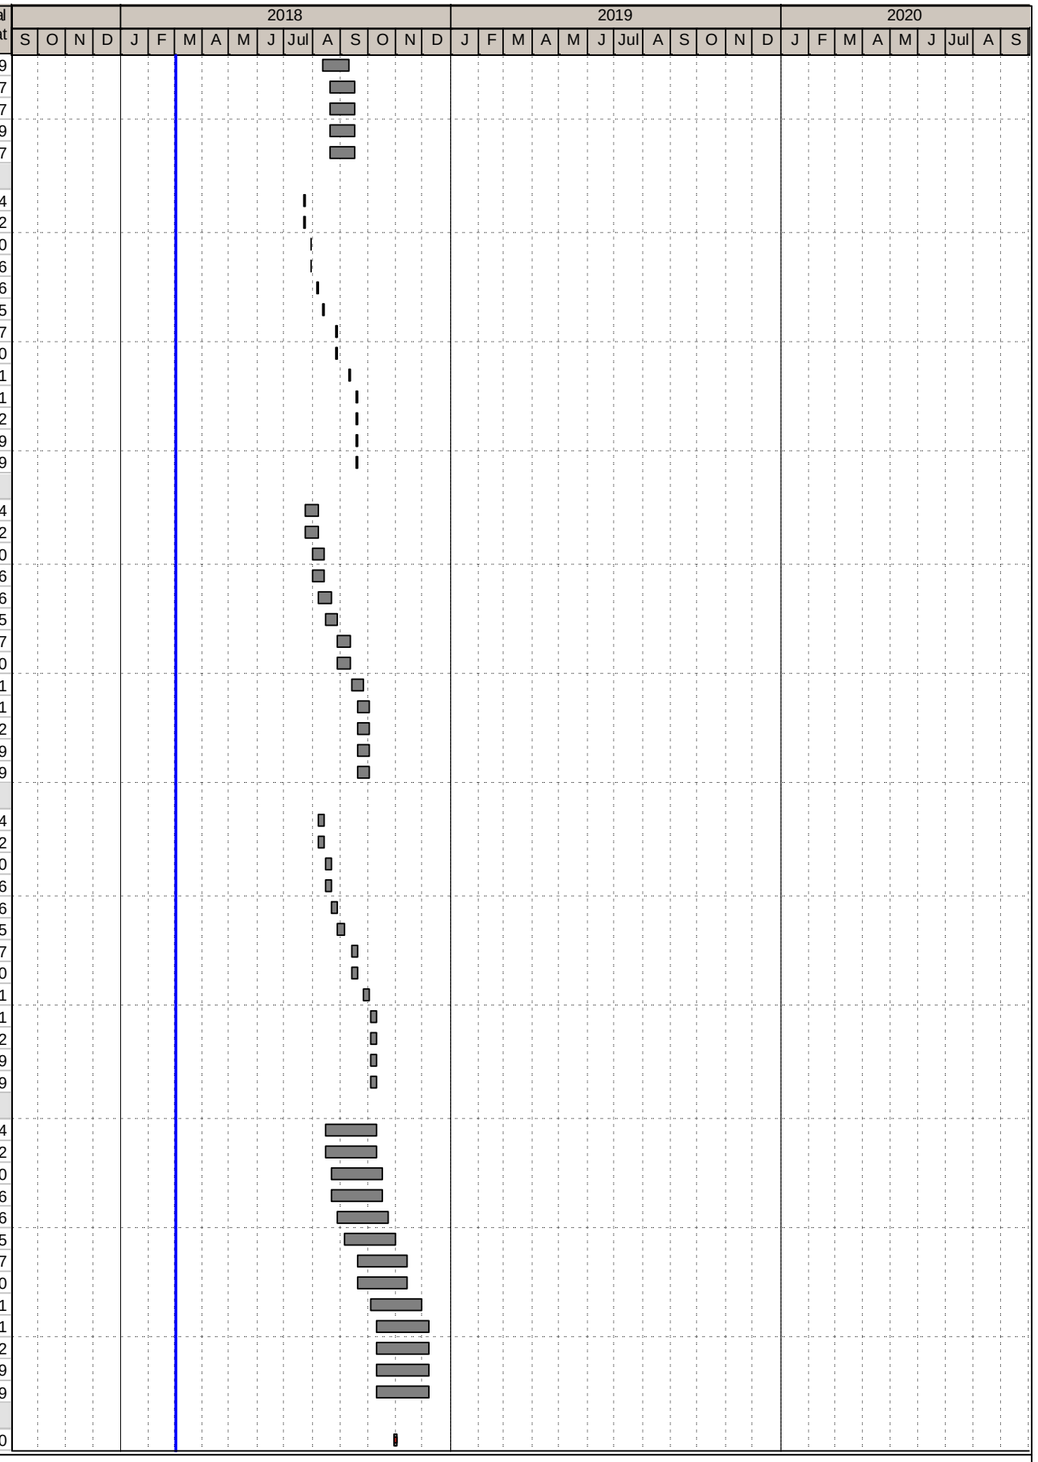

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S8F0-5P4F2	Bowl Steel - Subcontractor Deliver - Area F Upper Stadia Support & Press Lvl (Seq 3302)	3	01-Nov-18	05-Nov-18	7
S8A1-5P4F2	Bowl Steel - Subcontractor Deliver - Area A Upper Stadia Support & Press Lvl (Seq 3312)	3	09-Nov-18	13-Nov-18	0
S8B0-5P4F21	Bowl Steel - Subcontractor Deliver - Area B Upper Stadia Support & Press Lvl (Seq 3304)	3	15-Nov-18	19-Nov-18	0
S8F1-5P4F2	Bowl Steel - Subcontractor Deliver - Area F Upper Stadia Support & Press Lvl (Seq 3313)	3	26-Nov-18	28-Nov-18	6
S8E0-5P4F21	Bowl Steel - Subcontractor Deliver - Area E Upper Stadia Support & Press Lvl (Seq 3301)	3	30-Nov-18	04-Dec-18	6
S8E0-5P4F22	Bowl Steel - Subcontractor Deliver - Area E Upper Stadia Support & Press Lvl (Seq 3310)	3	26-Dec-18	28-Dec-18	4
S8B0-5P4F22	Bowl Steel - Subcontractor Deliver - Area B Upper Stadia Support & Press Lvl (Seq 3305)	3	26-Dec-18	28-Dec-18	1
S8C0-5P4F2	Bowl Steel - Subcontractor Deliver - Area C Upper Stadia Support & Press Lvl (Seq 3306)	3	23-Jan-19	25-Jan-19	26
S8D0-5P4F2	Bowl Steel - Subcontractor Deliver - Area D Upper Stadia Support & Press Lvl (Seq 3309)	3	05-Feb-19	07-Feb-19	10
S8C1-5P4F2	Bowl Steel - Subcontractor Deliver - Area C Upper Stadia Support & Press Lvl (Seq 3307)	3	15-Feb-19	19-Feb-19	14
S8C2-5P4F2	Bowl Steel - Subcontractor Deliver - Area C Upper Stadia Support & Press Lvl (Seq 3314)	3	15-Feb-19	19-Feb-19	15
S8D1-5P4F2	Bowl Steel - Subcontractor Deliver - Area D Upper Stadia Support & Press Lvl (Seq 3308)	3	20-Feb-19	22-Feb-19	9
Erect Structural Steel/Metal Deck					
100 Main Concourse					
Submit					
S3A0-5P4S	Long Span at Field - Subcontractor Develop/Submit Shop Dwgs - Left (Seq 0011 to 0091)	20	04-Jun-18	29-Jun-18	23
S3A0-5P4S10	Long Span at Field - Subcontractor Develop/Submit Shop Dwgs - Right (Seq 0012 to 0092)	20	11-Jun-18	09-Jul-18	36
Mortenson Review					
S3A0-5P4R	Long Span at Field - MMCJV Review Shop Drawings - Left (Seq 0011 to 0091)	2	02-Jul-18	03-Jul-18	23
S3A0-5P4R10	Long Span at Field - MMCJV Review Shop Drawings - Right (Seq 0012 to 0092)	2	10-Jul-18	11-Jul-18	36
Approve					
S3AL-5P4A	Long Span at Field - Design Team Review/Approve Shop Drawings - Left (Seq 0011 to 0091)	10	05-Jul-18	18-Jul-18	23
S3AR-5P4A	Long Span at Field - Design Team Review/Approve Shop Drawings - Right (Seq 0012 to 0092)	10	12-Jul-18	25-Jul-18	36
S3AL-5P4J	Long Span at Field - Subcontractor Scrub/Prepare Fab Sheets - Left (Seq 0011 to 0091)	5	19-Jul-18	25-Jul-18	23
S3AR-5P4J	Long Span at Field - Subcontractor Scrub/Prepare Fab Sheets - Right (Seq 0012 to 0092)	5	26-Jul-18	01-Aug-18	36
S3AL3-5P46	Long Span at Field - Fabricate & Paint - Left (0031)	40	26-Jul-18	20-Sep-18	23
S3AL4-5P46	Long Span at Field - Fabricate & Paint - Left (0041)	40	31-Jul-18	25-Sep-18	23
S3AL5-5P46	Long Span at Field - Fabricate & Paint - Left (0051)	40	03-Aug-18	28-Sep-18	23
S3AL6-5P46	Long Span at Field - Fabricate & Paint - Left (0061)	40	08-Aug-18	03-Oct-18	23
S3AL7-5P46	Long Span at Field - Fabricate & Paint - Left (0071)	40	13-Aug-18	08-Oct-18	23
S3AL8-5P46	Long Span at Field - Fabricate & Paint - Left (0081)	40	16-Aug-18	11-Oct-18	23
S3AL9-5P46	Long Span at Field - Fabricate & Paint - Left (0091)	40	21-Aug-18	16-Oct-18	23
S3AL1-5P46	Long Span at Field - Fabricate & Paint - Left (0011)	40	24-Aug-18	19-Oct-18	35
S3AL2-5P46	Long Span at Field - Fabricate & Paint - Left (0021)	40	29-Aug-18	24-Oct-18	35
S3AR3-5P46	Long Span at Field - Fabricate & Paint - Right (0032)	40	02-Aug-18	27-Sep-18	36
S3AR4-5P46	Long Span at Field - Fabricate & Paint - Right (0042)	40	07-Aug-18	02-Oct-18	36
S3AR5-5P46	Long Span at Field - Fabricate & Paint - Right (0052)	40	10-Aug-18	05-Oct-18	36
S3AR6-5P46	Long Span at Field - Fabricate & Paint - Right (0062)	40	15-Aug-18	10-Oct-18	36
S3AR7-5P46	Long Span at Field - Fabricate & Paint - Right (0072)	40	20-Aug-18	15-Oct-18	36
S3AR8-5P46	Long Span at Field - Fabricate & Paint - Right (0082)	40	23-Aug-18	18-Oct-18	36
S3AR9-5P46	Long Span at Field - Fabricate & Paint - Right (0092)	40	28-Aug-18	23-Oct-18	36
S3AR1-5P46	Long Span at Field - Fabricate & Paint - Right (0012)	40	31-Aug-18	26-Oct-18	36
S3AR2-5P46	Long Span at Field - Fabricate & Paint - Right (0022)	40	06-Sep-18	31-Oct-18	36
S3AL3-5P45	Long Span at Field - Deliver - Left (0031)	3	11-Oct-18	15-Oct-18	9
S3AL4-5P45	Long Span at Field - Deliver - Left (0041)	3	16-Oct-18	18-Oct-18	9
S3AL5-5P45	Long Span at Field - Deliver - Left (0051)	3	19-Oct-18	23-Oct-18	9
S3AL6-5P45	Long Span at Field - Deliver - Left (0061)	3	24-Oct-18	26-Oct-18	9
S3AL7-5P45	Long Span at Field - Deliver - Left (0071)	3	29-Oct-18	31-Oct-18	9
S3AL8-5P45	Long Span at Field - Deliver - Left (0081)	3	01-Nov-18	05-Nov-18	9
S3AL9-5P45	Long Span at Field - Deliver - Left (0091)	3	06-Nov-18	08-Nov-18	9
S3AR3-5P45	Long Span at Field - Deliver - Right (0032)	3	09-Nov-18	14-Nov-18	9
S3AR4-5P45	Long Span at Field - Deliver - Right (0042)	3	15-Nov-18	19-Nov-18	9
S3AR5-5P45	Long Span at Field - Deliver - Right (0052)	3	20-Nov-18	26-Nov-18	9
S3AR6-5P45	Long Span at Field - Deliver - Right (0062)	3	27-Nov-18	29-Nov-18	9
S3AR7-5P45	Long Span at Field - Deliver - Right (0072)	3	30-Nov-18	04-Dec-18	9
S3AL1-5P45	Long Span at Field - Deliver - Left (0011)	3	30-Nov-18	04-Dec-18	9
S3AL2-5P45	Long Span at Field - Deliver - Left (0021)	3	05-Dec-18	07-Dec-18	9
S3AR8-5P45	Long Span at Field - Deliver - Right (0082)	3	05-Dec-18	07-Dec-18	9

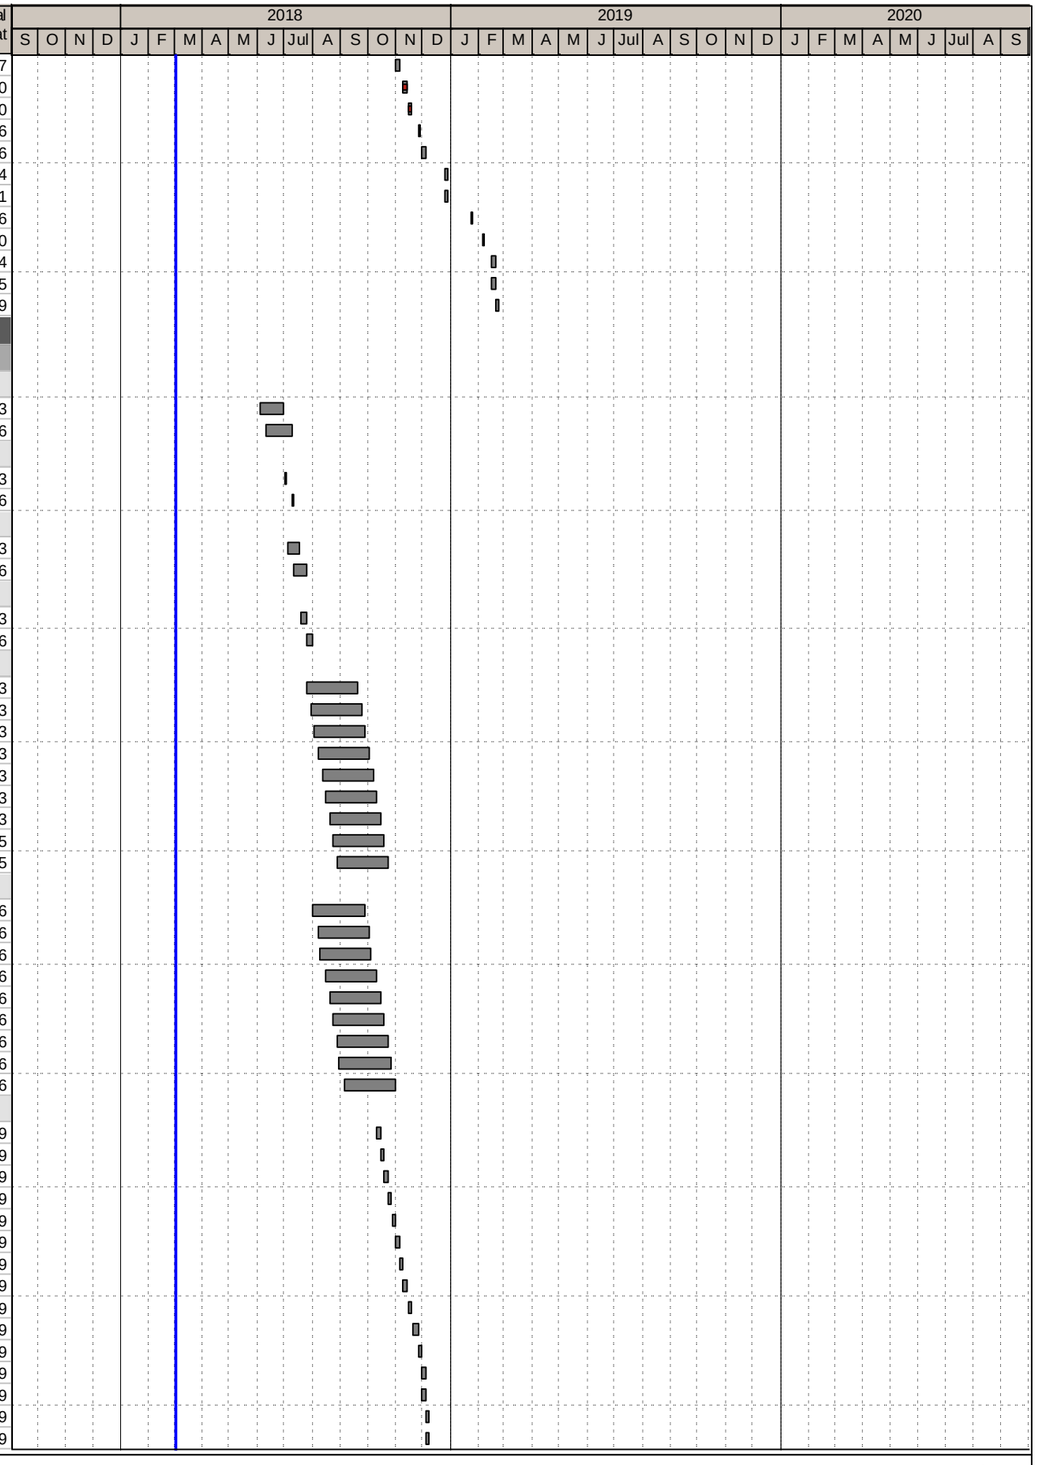

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S3AR9-5P45	Long Span at Field - Deliver - Right (0092)	3	10-Dec-18	12-Dec-18	9
S3AR1-5P45	Long Span at Field - Deliver - Right (0012)	3	10-Dec-18	12-Dec-18	9
S3AR2-5P45	Long Span at Field - Deliver - Right (0022)	3	13-Dec-18	17-Dec-18	9
Steel Roof Trusses					
Procure					
S00-5P5P170	Geometry Fixed - Cable Net Roof System	0	14-Mar-18		57
S00-5P5A130	Prepare ABM - Steel Truss Columns	10	08-Feb-18 A	21-Feb-18 A	
S00-5P5A311	Prepare/Engineer Staged Construction Analysis	20	13-Feb-18 A	27-Feb-18 A	
S00-5P5A312	Design Review and Revised Member Sizing - Staged Construction Analysis	10	28-Feb-18 A	13-Mar-18	16
S00-5P5A313	Staged Construction Analysis Review of Revised Members	10	14-Mar-18	27-Mar-18	16
S00-5P5A90	Prepare ABM - Steel Roof Canopy	10	03-Apr-18	17-Apr-18	81
S90-5P5A120	Roll/Deliver Mill Order - Steel Truss Columns	60	22-Feb-18 A	23-May-18	19
S00-5P5A120	Roll/Deliver Mill Order - Steel Roof	80	17-Apr-18	08-Aug-18	81
S00-5P5A160	Steel Truss Column Design - Package #1 Issued	1	07-Feb-18 A	07-Feb-18 A	
S00-5P5A190	Steel Truss Column Design - Package #5 Issued	1	07-Feb-18 A	07-Feb-18 A	
S00-5P5A170	Steel Truss Column Design - Package #2 Issued	1	13-Mar-18	13-Mar-18	9
S00-5P5A200	Steel Truss Column Design - Package #6 Issued	1	13-Mar-18	13-Mar-18	12
S00-5P5A180	Steel Truss Column Design - Package #3 Issued	1	03-Apr-18	03-Apr-18	21
S00-5P5A210	Steel Truss Column Design - Package #7 Issued	1	03-Apr-18	03-Apr-18	25
S00-5P5A300	Steel Truss Column Design - Package #4 Issued	1	03-Apr-18	03-Apr-18	24
S00-5P5A310	Steel Truss Column Design - Package #8 Issued	1	03-Apr-18	03-Apr-18	24
S00-5P5A230	Steel Roof Canopy Design - Issued	1	03-Apr-18	03-Apr-18	14
410 Canopy Roof Support					
Submit					
SR2A419-5P4S	Steel Truss Col - Subcontractor Detail/Submit Shop Drawings - Area A Truss Column (Seq 419)	20	08-Feb-18 A	07-Mar-18	32
SR2A420-5P4S	Steel Truss Col - Subcontractor Detail/Submit Shop Drawings - Area A Truss Column (Seq 420)	20	08-Feb-18 A	07-Mar-18	34
SR2A418-5P4S	Steel Truss Col - Subcontractor Detail/Submit Shop Drawings - Area A Truss Column (Seq 418)	20	08-Feb-18 A	07-Mar-18	38
SR2A417-5P4S	Steel Truss Col - Subcontractor Detail/Submit Shop Drawings - Area A Truss Column (Seq 417)	20	08-Feb-18 A	07-Mar-18	40
SR2F408-5P4S	Steel Truss Col - Subcontractor Detail/Submit Shop Drawings - Area F Truss Column (Seq 408)	20	15-Feb-18 A	14-Mar-18	31
SR2F407-5P4S	Steel Truss Col - Subcontractor Detail/Submit Shop Drawings - Area F Truss Column (Seq 407)	20	15-Feb-18 A	14-Mar-18	31
SR2F409-5P4S	Steel Truss Col - Subcontractor Detail/Submit Shop Drawings - Area F Truss Column (Seq 409)	20	15-Feb-18 A	14-Mar-18	31
SR2F410-5P4S	Steel Truss Col - Subcontractor Detail/Submit Shop Drawings - Area F Truss Column (Seq 410)	20	15-Feb-18 A	14-Mar-18	31
SR2B424-5P4S	Steel Truss Col - Subcontractor Detail/Submit Shop Drawings - Area B Truss Column (Seq 424)	20	26-Mar-18	20-Apr-18	29
SR2B421-5P4S	Steel Truss Col - Subcontractor Detail/Submit Shop Drawings - Area B Truss Column (Seq 421)	20	26-Mar-18	20-Apr-18	24
SR2B422-5P4S	Steel Truss Col - Subcontractor Detail/Submit Shop Drawings - Area B Truss Column (Seq 422)	20	26-Mar-18	20-Apr-18	29
SR2B423-5P4S	Steel Truss Col - Subcontractor Detail/Submit Shop Drawings - Area B Truss Column (Seq 423)	20	26-Mar-18	20-Apr-18	29
SR2E403-5P4S	Steel Truss Col - Subcontractor Detail/Submit Shop Drawings - Area E Truss Column (Seq 403)	20	02-Apr-18	27-Apr-18	29
SR2E406-5P4S	Steel Truss Col - Subcontractor Detail/Submit Shop Drawings - Area E Truss Column (Seq 406)	20	02-Apr-18	27-Apr-18	29
SR2E405-5P4S	Steel Truss Col - Subcontractor Detail/Submit Shop Drawings - Area E Truss Column (Seq 405)	20	02-Apr-18	27-Apr-18	29
SR2E404-5P4S	Steel Truss Col - Subcontractor Detail/Submit Shop Drawings - Area E Truss Column (Seq 404)	20	02-Apr-18	27-Apr-18	29
SR2B425-5P4S	Steel Truss Col - Subcontractor Detail/Submit Shop Drawings - Area B Truss Column (Seq 425)	20	09-Apr-18	04-May-18	29
SR2B426-5P4S	Steel Truss Col - Subcontractor Detail/Submit Shop Drawings - Area B Truss Column (Seq 426)	20	09-Apr-18	04-May-18	31
SR2B427-5P4S	Steel Truss Col - Subcontractor Detail/Submit Shop Drawings - Area B Truss Column (Seq 427)	20	09-Apr-18	04-May-18	31
SR2B428-5P4S	Steel Truss Col - Subcontractor Detail/Submit Shop Drawings - Area B Truss Column (Seq 428)	20	09-Apr-18	04-May-18	31
SR2E402-5P4S	Steel Truss Col - Subcontractor Detail/Submit Shop Drawings - Area E Truss Column (Seq 402)	20	16-Apr-18	11-May-18	31
SR2E401-5P4S	Steel Truss Col - Subcontractor Detail/Submit Shop Drawings - Area E Truss Column (Seq 401)	20	16-Apr-18	11-May-18	33
SR2E450-5P4S	Steel Truss Col - Subcontractor Detail/Submit Shop Drawings - Area E Truss Column (Seq 450)	20	16-Apr-18	11-May-18	41
SR2E449-5P4S	Steel Truss Col - Subcontractor Detail/Submit Shop Drawings - Area E Truss Column (Seq 449)	20	16-Apr-18	11-May-18	41
SR2B429-5P4S	Steel Truss Col - Subcontractor Detail/Submit Shop Drawings - Area B Truss Column (Seq 429)	20	23-Apr-18	18-May-18	41
SR2B430-5P4S	Steel Truss Col - Subcontractor Detail/Submit Shop Drawings - Area B Truss Column (Seq 430)	20	23-Apr-18	18-May-18	43
SR2B431-5P4S	Steel Truss Col - Subcontractor Detail/Submit Shop Drawings - Area B Truss Column (Seq 431)	20	23-Apr-18	18-May-18	45
SR2B432-5P4S	Steel Truss Col - Subcontractor Detail/Submit Shop Drawings - Area B Truss Column (Seq 432)	20	23-Apr-18	18-May-18	46
SR2E448-5P4S	Steel Truss Col - Subcontractor Detail/Submit Shop Drawings - Area E Truss Column (Seq 448)	20	30-Apr-18	25-May-18	46
SR2E447-5P4S	Steel Truss Col - Subcontractor Detail/Submit Shop Drawings - Area E Truss Column (Seq 447)	20	30-Apr-18	25-May-18	46
SR2E446-5P4S	Steel Truss Col - Subcontractor Detail/Submit Shop Drawings - Area E Truss Column (Seq 446)	20	30-Apr-18	25-May-18	46
SR2E445-5P4S	Steel Truss Col - Subcontractor Detail/Submit Shop Drawings - Area E Truss Column (Seq 445)	20	30-Apr-18	25-May-18	46
SR2C433-5P4S	Steel Truss Col - Subcontractor Detail/Submit Shop Drawings - Area C Truss Column (Seq 433)	20	04-May-18	01-Jun-18	46
SR2C434-5P4S	Steel Truss Col - Subcontractor Detail/Submit Shop Drawings - Area C Truss Column (Seq 434)	20	04-May-18	01-Jun-18	48

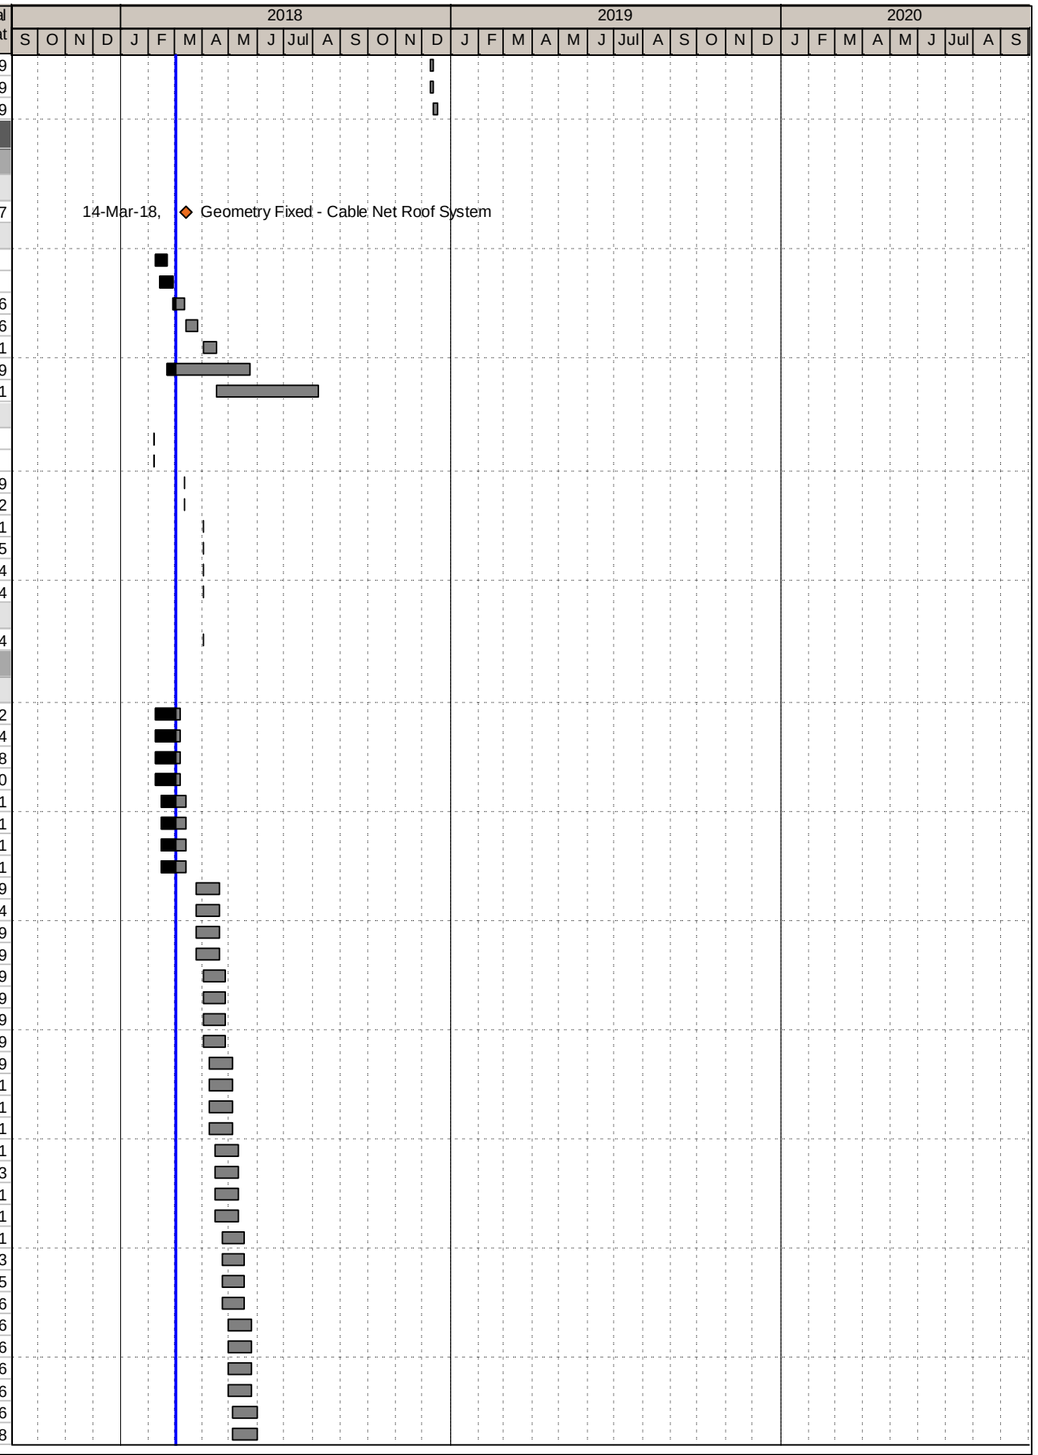

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
SR2C534-5P4S	Steel Truss Col - Subcontractor Detail/Submit Shop Drawings - Area C Truss Column (Seq 435)	20	04-May-18	01-Jun-18	50
SR2C436-5P4S	Steel Truss Col - Subcontractor Detail/Submit Shop Drawings - Area C Truss Column (Seq 436)	20	04-May-18	01-Jun-18	53
SR2D444-5P4S	Steel Truss Col - Subcontractor Detail/Submit Shop Drawings - Area D Truss Column (Seq 444)	20	11-May-18	08-Jun-18	55
SR2D443-5P4S	Steel Truss Col - Subcontractor Detail/Submit Shop Drawings - Area D Truss Column (Seq 443)	20	11-May-18	08-Jun-18	57
SR2D442-5P4S	Steel Truss Col - Subcontractor Detail/Submit Shop Drawings - Area D Truss Column (Seq 442)	20	11-May-18	08-Jun-18	59
SR2D441-5P4S	Steel Truss Col - Subcontractor Detail/Submit Shop Drawings - Area D Truss Column (Seq 441)	20	11-May-18	08-Jun-18	61
Mortenson Review					
SR2A419-5P4R	Steel Truss Col - MMCJVLV Review Shop Drawings - Area A Truss Column (Seq 419)	2	08-Mar-18	09-Mar-18	32
SR2A420-5P4R	Steel Truss Col - MMCJVLV Review Shop Drawings - Area A Truss Column (Seq 420)	2	08-Mar-18	09-Mar-18	34
SR2A418-5P4R	Steel Truss Col - MMCJVLV Review Shop Drawings - Area A Truss Column (Seq 418)	2	08-Mar-18	09-Mar-18	38
SR2A417-5P4R	Steel Truss Col - MMCJVLV Review Shop Drawings - Area A Truss Column (Seq 417)	2	08-Mar-18	09-Mar-18	40
SR2F408-5P4R	Steel Truss Col - MMCJVLV Review Shop Drawings - Area F Truss Column (Seq 408)	2	15-Mar-18	16-Mar-18	47
SR2F407-5P4R	Steel Truss Col - MMCJVLV Review Shop Drawings - Area F Truss Column (Seq 407)	2	15-Mar-18	16-Mar-18	49
SR2F409-5P4R	Steel Truss Col - MMCJVLV Review Shop Drawings - Area F Truss Column (Seq 409)	2	15-Mar-18	16-Mar-18	53
SR2F410-5P4R	Steel Truss Col - MMCJVLV Review Shop Drawings - Area F Truss Column (Seq 410)	2	15-Mar-18	16-Mar-18	55
SR2B424-5P4R	Steel Truss Col - MMCJVLV Review Shop Drawings - Area B Truss Column (Seq 424)	2	23-Apr-18	24-Apr-18	37
SR2B421-5P4R	Steel Truss Col - MMCJVLV Review Shop Drawings - Area B Truss Column (Seq 421)	2	23-Apr-18	24-Apr-18	24
SR2B422-5P4R	Steel Truss Col - MMCJVLV Review Shop Drawings - Area B Truss Column (Seq 422)	2	23-Apr-18	24-Apr-18	33
SR2B423-5P4R	Steel Truss Col - MMCJVLV Review Shop Drawings - Area B Truss Column (Seq 423)	2	23-Apr-18	24-Apr-18	35
SR2E403-5P4R	Steel Truss Col - MMCJVLV Review Shop Drawings - Area E Truss Column (Seq 403)	2	30-Apr-18	01-May-18	39
SR2E406-5P4R	Steel Truss Col - MMCJVLV Review Shop Drawings - Area E Truss Column (Seq 406)	2	30-Apr-18	01-May-18	29
SR2E405-5P4R	Steel Truss Col - MMCJVLV Review Shop Drawings - Area E Truss Column (Seq 405)	2	30-Apr-18	01-May-18	35
SR2E404-5P4R	Steel Truss Col - MMCJVLV Review Shop Drawings - Area E Truss Column (Seq 404)	2	30-Apr-18	01-May-18	37
SR2B425-5P4R	Steel Truss Col - MMCJVLV Review Shop Drawings - Area B Truss Column (Seq 425)	2	07-May-18	08-May-18	29
SR2B426-5P4R	Steel Truss Col - MMCJVLV Review Shop Drawings - Area B Truss Column (Seq 426)	2	07-May-18	08-May-18	39
SR2B427-5P4R	Steel Truss Col - MMCJVLV Review Shop Drawings - Area B Truss Column (Seq 427)	2	07-May-18	08-May-18	41
SR2B428-5P4R	Steel Truss Col - MMCJVLV Review Shop Drawings - Area B Truss Column (Seq 428)	2	07-May-18	08-May-18	43
SR2E402-5P4R	Steel Truss Col - MMCJVLV Review Shop Drawings - Area E Truss Column (Seq 402)	2	14-May-18	15-May-18	31
SR2E401-5P4R	Steel Truss Col - MMCJVLV Review Shop Drawings - Area E Truss Column (Seq 401)	2	14-May-18	15-May-18	33
SR2E450-5P4R	Steel Truss Col - MMCJVLV Review Shop Drawings - Area E Truss Column (Seq 450)	2	14-May-18	15-May-18	45
SR2E449-5P4R	Steel Truss Col - MMCJVLV Review Shop Drawings - Area E Truss Column (Seq 449)	2	14-May-18	15-May-18	47
SR2B429-5P4R	Steel Truss Col - MMCJVLV Review Shop Drawings - Area B Truss Column (Seq 429)	2	21-May-18	22-May-18	41
SR2B430-5P4R	Steel Truss Col - MMCJVLV Review Shop Drawings - Area B Truss Column (Seq 430)	2	21-May-18	22-May-18	43
SR2B431-5P4R	Steel Truss Col - MMCJVLV Review Shop Drawings - Area B Truss Column (Seq 431)	2	21-May-18	22-May-18	45
SR2B432-5P4R	Steel Truss Col - MMCJVLV Review Shop Drawings - Area B Truss Column (Seq 432)	2	21-May-18	22-May-18	53
SR2E448-5P4R	Steel Truss Col - MMCJVLV Review Shop Drawings - Area E Truss Column (Seq 448)	2	29-May-18	30-May-18	47
SR2E447-5P4R	Steel Truss Col - MMCJVLV Review Shop Drawings - Area E Truss Column (Seq 447)	2	29-May-18	30-May-18	49
SR2E446-5P4R	Steel Truss Col - MMCJVLV Review Shop Drawings - Area E Truss Column (Seq 446)	2	29-May-18	30-May-18	51
SR2E445-5P4R	Steel Truss Col - MMCJVLV Review Shop Drawings - Area E Truss Column (Seq 445)	2	29-May-18	30-May-18	53
SR2C433-5P4R	Steel Truss Col - MMCJVLV Review Shop Drawings - Area C Truss Column (Seq 433)	2	04-Jun-18	05-Jun-18	46
SR2C434-5P4R	Steel Truss Col - MMCJVLV Review Shop Drawings - Area C Truss Column (Seq 434)	2	04-Jun-18	05-Jun-18	48
SR2C435-5P4R	Steel Truss Col - MMCJVLV Review Shop Drawings - Area C Truss Column (Seq 435)	2	04-Jun-18	05-Jun-18	50
SR2C436-5P4R	Steel Truss Col - MMCJVLV Review Shop Drawings - Area C Truss Column (Seq 436)	2	04-Jun-18	05-Jun-18	53
SR2D444-5P4R	Steel Truss Col - MMCJVLV Review Shop Drawings - Area D Truss Column (Seq 444)	2	11-Jun-18	12-Jun-18	55
SR2D443-5P4R	Steel Truss Col - MMCJVLV Review Shop Drawings - Area D Truss Column (Seq 443)	2	11-Jun-18	12-Jun-18	57
SR2D442-5P4R	Steel Truss Col - MMCJVLV Review Shop Drawings - Area D Truss Column (Seq 442)	2	11-Jun-18	12-Jun-18	59
SR2D441-5P4R	Steel Truss Col - MMCJVLV Review Shop Drawings - Area D Truss Column (Seq 441)	2	11-Jun-18	12-Jun-18	61
Approve					
SR2A419-5P4A	Steel Truss Col - Design Team Review/ Approve Shop Drawings - Area A Truss Column (Seq 419)	10	12-Mar-18	23-Mar-18	32
SR2A420-5P4A	Steel Truss Col - Design Team Review/ Approve Shop Drawings - Area A Truss Column (Seq 420)	10	12-Mar-18	23-Mar-18	34
SR2A418-5P4A	Steel Truss Col - Design Team Review/ Approve Shop Drawings - Area A Truss Column (Seq 418)	10	12-Mar-18	23-Mar-18	38
SR2A417-5P4A	Steel Truss Col - Design Team Review/ Approve Shop Drawings - Area A Truss Column (Seq 417)	10	12-Mar-18	23-Mar-18	40
SR2F408-5P4A	Steel Truss Col - Design Team Review/ Approve Shop Drawings - Area F Truss Column (Seq 408)	10	19-Mar-18	30-Mar-18	47
SR2F407-5P4A	Steel Truss Col - Design Team Review/ Approve Shop Drawings - Area F Truss Column (Seq 407)	10	19-Mar-18	30-Mar-18	49
SR2F409-5P4A	Steel Truss Col - Design Team Review/ Approve Shop Drawings - Area F Truss Column (Seq 409)	10	19-Mar-18	30-Mar-18	53
SR2F410-5P4A	Steel Truss Col - Design Team Review/ Approve Shop Drawings - Area F Truss Column (Seq 410)	10	19-Mar-18	30-Mar-18	55
SR2B424-5P4A	Steel Truss Col - Design Team Review/ Approve Shop Drawings - Area B Truss Column (Seq 424)	10	25-Apr-18	08-May-18	37
SR2B421-5P4A	Steel Truss Col - Design Team Review/ Approve Shop Drawings - Area B Truss Column (Seq 421)	10	25-Apr-18	08-May-18	24
SR2B422-5P4A	Steel Truss Col - Design Team Review/ Approve Shop Drawings - Area B Truss Column (Seq 422)	10	25-Apr-18	08-May-18	33
SR2B423-5P4A	Steel Truss Col - Design Team Review/ Approve Shop Drawings - Area B Truss Column (Seq 423)	10	25-Apr-18	08-May-18	35
SR2E403-5P4A	Steel Truss Col - Design Team Review/ Approve Shop Drawings - Area E Truss Column (Seq 403)	10	02-May-18	15-May-18	39
SR2E406-5P4A	Steel Truss Col - Design Team Review/ Approve Shop Drawings - Area E Truss Column (Seq 406)	10	02-May-18	15-May-18	29
SR2E405-5P4A	Steel Truss Col - Design Team Review/ Approve Shop Drawings - Area E Truss Column (Seq 405)	10	02-May-18	15-May-18	35

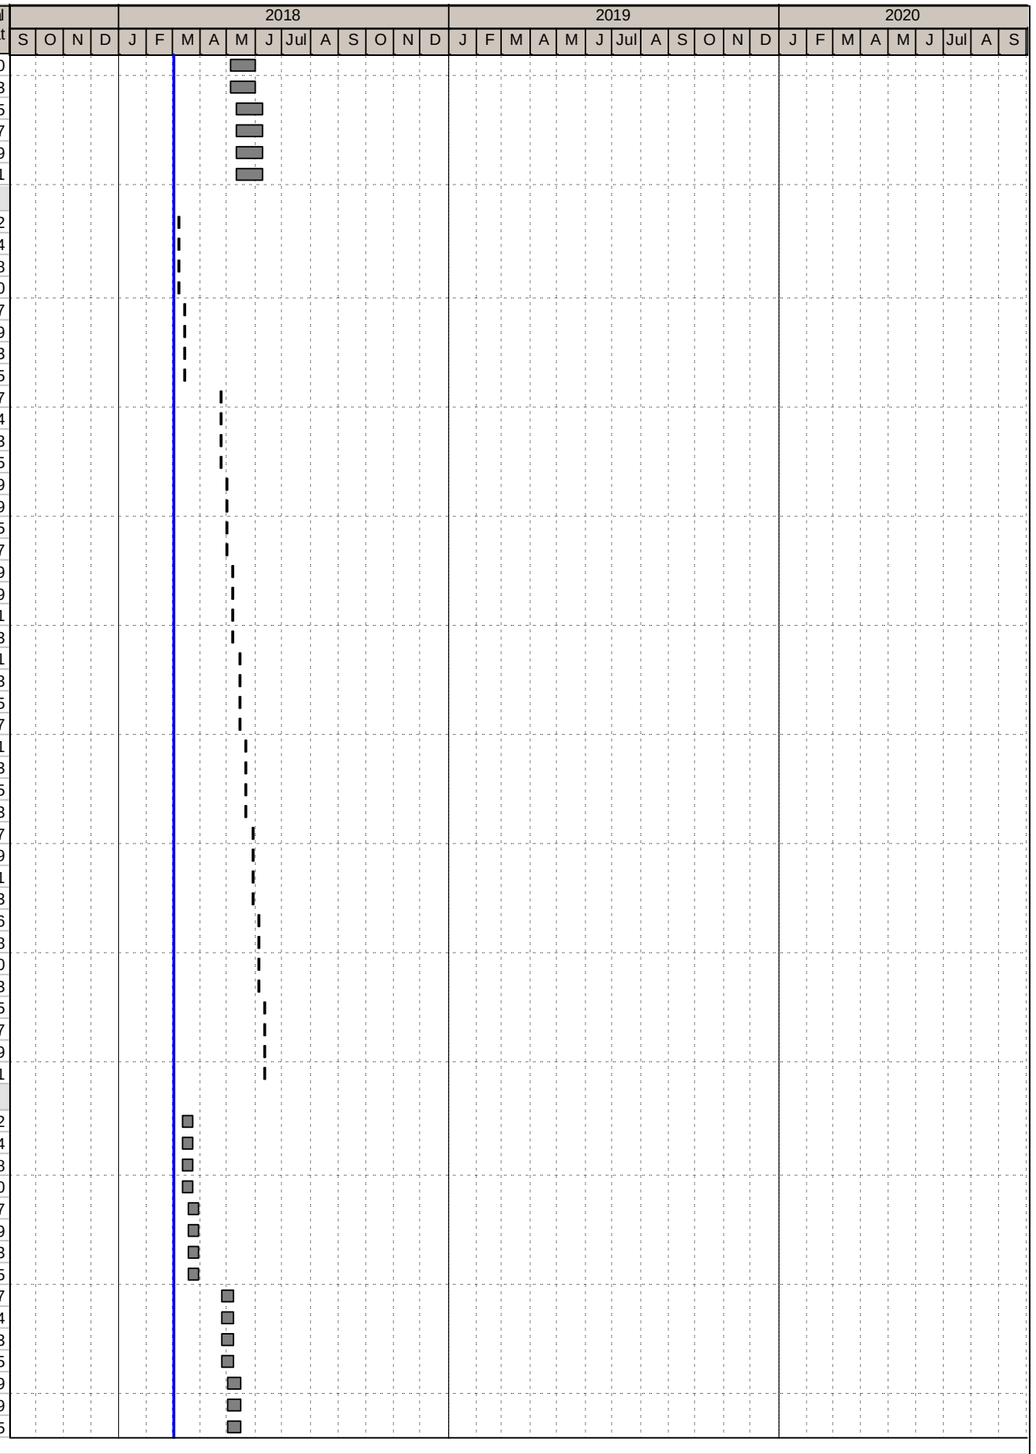

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
SR2E404-5P4A	Steel Truss Col - Design Team Review/ Approve Shop Drawings - Area E Truss Column (Seq 404)	10	02-May-18	15-May-18	37
SR2B425-5P4A	Steel Truss Col - Design Team Review/ Approve Shop Drawings - Area B Truss Column (Seq 425)	10	09-May-18	22-May-18	29
SR2B426-5P4A	Steel Truss Col - Design Team Review/ Approve Shop Drawings - Area B Truss Column (Seq 426)	10	09-May-18	22-May-18	39
SR2B427-5P4A	Steel Truss Col - Design Team Review/ Approve Shop Drawings - Area B Truss Column (Seq 427)	10	09-May-18	22-May-18	41
SR2B428-5P4A	Steel Truss Col - Design Team Review/ Approve Shop Drawings - Area B Truss Column (Seq 428)	10	09-May-18	22-May-18	43
SR2E402-5P4A	Steel Truss Col - Design Team Review/ Approve Shop Drawings - Area E Truss Column (Seq 402)	10	16-May-18	30-May-18	31
SR2E401-5P4A	Steel Truss Col - Design Team Review/ Approve Shop Drawings - Area E Truss Column (Seq 401)	10	16-May-18	30-May-18	33
SR2E450-5P4A	Steel Truss Col - Design Team Review/ Approve Shop Drawings - Area E Truss Column (Seq 450)	10	16-May-18	30-May-18	45
SR2E449-5P4A	Steel Truss Col - Design Team Review/ Approve Shop Drawings - Area E Truss Column (Seq 449)	10	16-May-18	30-May-18	47
SR2B429-5P4A	Steel Truss Col - Design Team Review/ Approve Shop Drawings - Area B Truss Column (Seq 429)	10	23-May-18	06-Jun-18	41
SR2B430-5P4A	Steel Truss Col - Design Team Review/ Approve Shop Drawings - Area B Truss Column (Seq 430)	10	23-May-18	06-Jun-18	43
SR2B431-5P4A	Steel Truss Col - Design Team Review/ Approve Shop Drawings - Area B Truss Column (Seq 431)	10	23-May-18	06-Jun-18	45
SR2B432-5P4A	Steel Truss Col - Design Team Review/ Approve Shop Drawings - Area B Truss Column (Seq 432)	10	23-May-18	06-Jun-18	53
SR2E448-5P4A	Steel Truss Col - Design Team Review/ Approve Shop Drawings - Area E Truss Column (Seq 448)	10	31-May-18	13-Jun-18	47
SR2E447-5P4A	Steel Truss Col - Design Team Review/ Approve Shop Drawings - Area E Truss Column (Seq 447)	10	31-May-18	13-Jun-18	49
SR2E446-5P4A	Steel Truss Col - Design Team Review/ Approve Shop Drawings - Area E Truss Column (Seq 446)	10	31-May-18	13-Jun-18	51
SR2E445-5P4A	Steel Truss Col - Design Team Review/ Approve Shop Drawings - Area E Truss Column (Seq 445)	10	31-May-18	13-Jun-18	53
SR2C433-5P4A	Steel Truss Col - Design Team Review/ Approve Shop Drawings - Area C Truss Column (Seq 433)	10	06-Jun-18	19-Jun-18	46
SR2C434-5P4A	Steel Truss Col - Design Team Review/ Approve Shop Drawings - Area C Truss Column (Seq 434)	10	06-Jun-18	19-Jun-18	48
SR2C435-5P4A	Steel Truss Col - Design Team Review/ Approve Shop Drawings - Area C Truss Column (Seq 435)	10	06-Jun-18	19-Jun-18	50
SR2C436-5P4A	Steel Truss Col - Design Team Review/ Approve Shop Drawings - Area C Truss Column (Seq 436)	10	06-Jun-18	19-Jun-18	53
SR2D444-5P4A	Steel Truss Col - Design Team Review/ Approve Shop Drawings - Area D Truss Column (Seq 444)	10	13-Jun-18	26-Jun-18	55
SR2D443-5P4A	Steel Truss Col - Design Team Review/ Approve Shop Drawings - Area D Truss Column (Seq 443)	10	13-Jun-18	26-Jun-18	57
SR2D442-5P4A	Steel Truss Col - Design Team Review/ Approve Shop Drawings - Area D Truss Column (Seq 442)	10	13-Jun-18	26-Jun-18	59
SR2D441-5P4A	Steel Truss Col - Design Team Review/ Approve Shop Drawings - Area D Truss Column (Seq 441)	10	13-Jun-18	26-Jun-18	61
SR2A419-5P4J	Steel Truss Col - Subcontractor Scrub/Prepare Fab Sheets - Area A Truss Column (Seq 419)	5	26-Mar-18	30-Mar-18	32
SR2A420-5P4J	Steel Truss Col - Subcontractor Scrub/Prepare Fab Sheets - Area A Truss Column (Seq 420)	5	26-Mar-18	30-Mar-18	34
SR2A418-5P4J	Steel Truss Col - Subcontractor Scrub/Prepare Fab Sheets - Area A Truss Column (Seq 418)	5	26-Mar-18	30-Mar-18	38
SR2A417-5P4J	Steel Truss Col - Subcontractor Scrub/Prepare Fab Sheets - Area A Truss Column (Seq 417)	5	26-Mar-18	30-Mar-18	40
SR2F408-5P4J	Steel Truss Col - Subcontractor Scrub/Prepare Fab Sheets - Area F Truss Column (Seq 408)	5	02-Apr-18	06-Apr-18	47
SR2F407-5P4J	Steel Truss Col - Subcontractor Scrub/Prepare Fab Sheets - Area F Truss Column (Seq 407)	5	02-Apr-18	06-Apr-18	49
SR2F409-5P4J	Steel Truss Col - Subcontractor Scrub/Prepare Fab Sheets - Area F Truss Column (Seq 409)	5	02-Apr-18	06-Apr-18	53
SR2F410-5P4J	Steel Truss Col - Subcontractor Scrub/Prepare Fab Sheets - Area F Truss Column (Seq 410)	5	02-Apr-18	06-Apr-18	55
SR2B424-5P4J	Steel Truss Col - Subcontractor Scrub/Prepare Fab Sheets - Area B Truss Column (Seq 424)	5	09-May-18	15-May-18	37
SR2B421-5P4J	Steel Truss Col - Subcontractor Scrub/Prepare Fab Sheets - Area B Truss Column (Seq 421)	5	09-May-18	15-May-18	24
SR2B422-5P4J	Steel Truss Col - Subcontractor Scrub/Prepare Fab Sheets - Area B Truss Column (Seq 422)	5	09-May-18	15-May-18	33
SR2B423-5P4J	Steel Truss Col - Subcontractor Scrub/Prepare Fab Sheets - Area B Truss Column (Seq 423)	5	09-May-18	15-May-18	35
SR2E403-5P4J	Steel Truss Col - Subcontractor Scrub/Prepare Fab Sheets - Area E Truss Column (Seq 403)	5	16-May-18	22-May-18	39
SR2E406-5P4J	Steel Truss Col - Subcontractor Scrub/Prepare Fab Sheets - Area E Truss Column (Seq 406)	5	16-May-18	22-May-18	29
SR2E405-5P4J	Steel Truss Col - Subcontractor Scrub/Prepare Fab Sheets - Area E Truss Column (Seq 405)	5	16-May-18	22-May-18	35
SR2E404-5P4J	Steel Truss Col - Subcontractor Scrub/Prepare Fab Sheets - Area E Truss Column (Seq 404)	5	16-May-18	22-May-18	37
SR2B425-5P4J	Steel Truss Col - Subcontractor Scrub/Prepare Fab Sheets - Area B Truss Column (Seq 425)	5	23-May-18	30-May-18	29
SR2B426-5P4J	Steel Truss Col - Subcontractor Scrub/Prepare Fab Sheets - Area B Truss Column (Seq 426)	5	23-May-18	30-May-18	39
SR2B427-5P4J	Steel Truss Col - Subcontractor Scrub/Prepare Fab Sheets - Area B Truss Column (Seq 427)	5	23-May-18	30-May-18	41
SR2B428-5P4J	Steel Truss Col - Subcontractor Scrub/Prepare Fab Sheets - Area B Truss Column (Seq 428)	5	23-May-18	30-May-18	43
SR2E402-5P4J	Steel Truss Col - Subcontractor Scrub/Prepare Fab Sheets - Area E Truss Column (Seq 402)	5	31-May-18	06-Jun-18	31
SR2E401-5P4J	Steel Truss Col - Subcontractor Scrub/Prepare Fab Sheets - Area E Truss Column (Seq 401)	5	31-May-18	06-Jun-18	33
SR2E450-5P4J	Steel Truss Col - Subcontractor Scrub/Prepare Fab Sheets - Area E Truss Column (Seq 450)	5	31-May-18	06-Jun-18	45
SR2E449-5P4J	Steel Truss Col - Subcontractor Scrub/Prepare Fab Sheets - Area E Truss Column (Seq 449)	5	31-May-18	06-Jun-18	47
SR2B429-5P4J	Steel Truss Col - Subcontractor Scrub/Prepare Fab Sheets - Area B Truss Column (Seq 429)	5	07-Jun-18	13-Jun-18	41
SR2B430-5P4J	Steel Truss Col - Subcontractor Scrub/Prepare Fab Sheets - Area B Truss Column (Seq 430)	5	07-Jun-18	13-Jun-18	43
SR2B431-5P4J	Steel Truss Col - Subcontractor Scrub/Prepare Fab Sheets - Area B Truss Column (Seq 431)	5	07-Jun-18	13-Jun-18	45
SR2B432-5P4J	Steel Truss Col - Subcontractor Scrub/Prepare Fab Sheets - Area B Truss Column (Seq 432)	5	07-Jun-18	13-Jun-18	53
SR2E448-5P4J	Steel Truss Col - Subcontractor Scrub/Prepare Fab Sheets - Area E Truss Column (Seq 448)	5	14-Jun-18	20-Jun-18	47
SR2E447-5P4J	Steel Truss Col - Subcontractor Scrub/Prepare Fab Sheets - Area E Truss Column (Seq 447)	5	14-Jun-18	20-Jun-18	49
SR2E446-5P4J	Steel Truss Col - Subcontractor Scrub/Prepare Fab Sheets - Area E Truss Column (Seq 446)	5	14-Jun-18	20-Jun-18	51
SR2E445-5P4J	Steel Truss Col - Subcontractor Scrub/Prepare Fab Sheets - Area E Truss Column (Seq 445)	5	14-Jun-18	20-Jun-18	53
SR2C433-5P4J	Steel Truss Col - Subcontractor Scrub/Prepare Fab Sheets - Area C Truss Column (Seq 433)	5	20-Jun-18	26-Jun-18	46
SR2C434-5P4J	Steel Truss Col - Subcontractor Scrub/Prepare Fab Sheets - Area C Truss Column (Seq 434)	5	20-Jun-18	26-Jun-18	48
SR2C435-5P4J	Steel Truss Col - Subcontractor Scrub/Prepare Fab Sheets - Area C Truss Column (Seq 435)	5	20-Jun-18	26-Jun-18	50
SR2C436-5P4J	Steel Truss Col - Subcontractor Scrub/Prepare Fab Sheets - Area C Truss Column (Seq 436)	5	20-Jun-18	26-Jun-18	53
SR2D444-5P4J	Steel Truss Col - Subcontractor Scrub/Prepare Fab Sheets - Area D Truss Column (Seq 444)	5	27-Jun-18	03-Jul-18	55

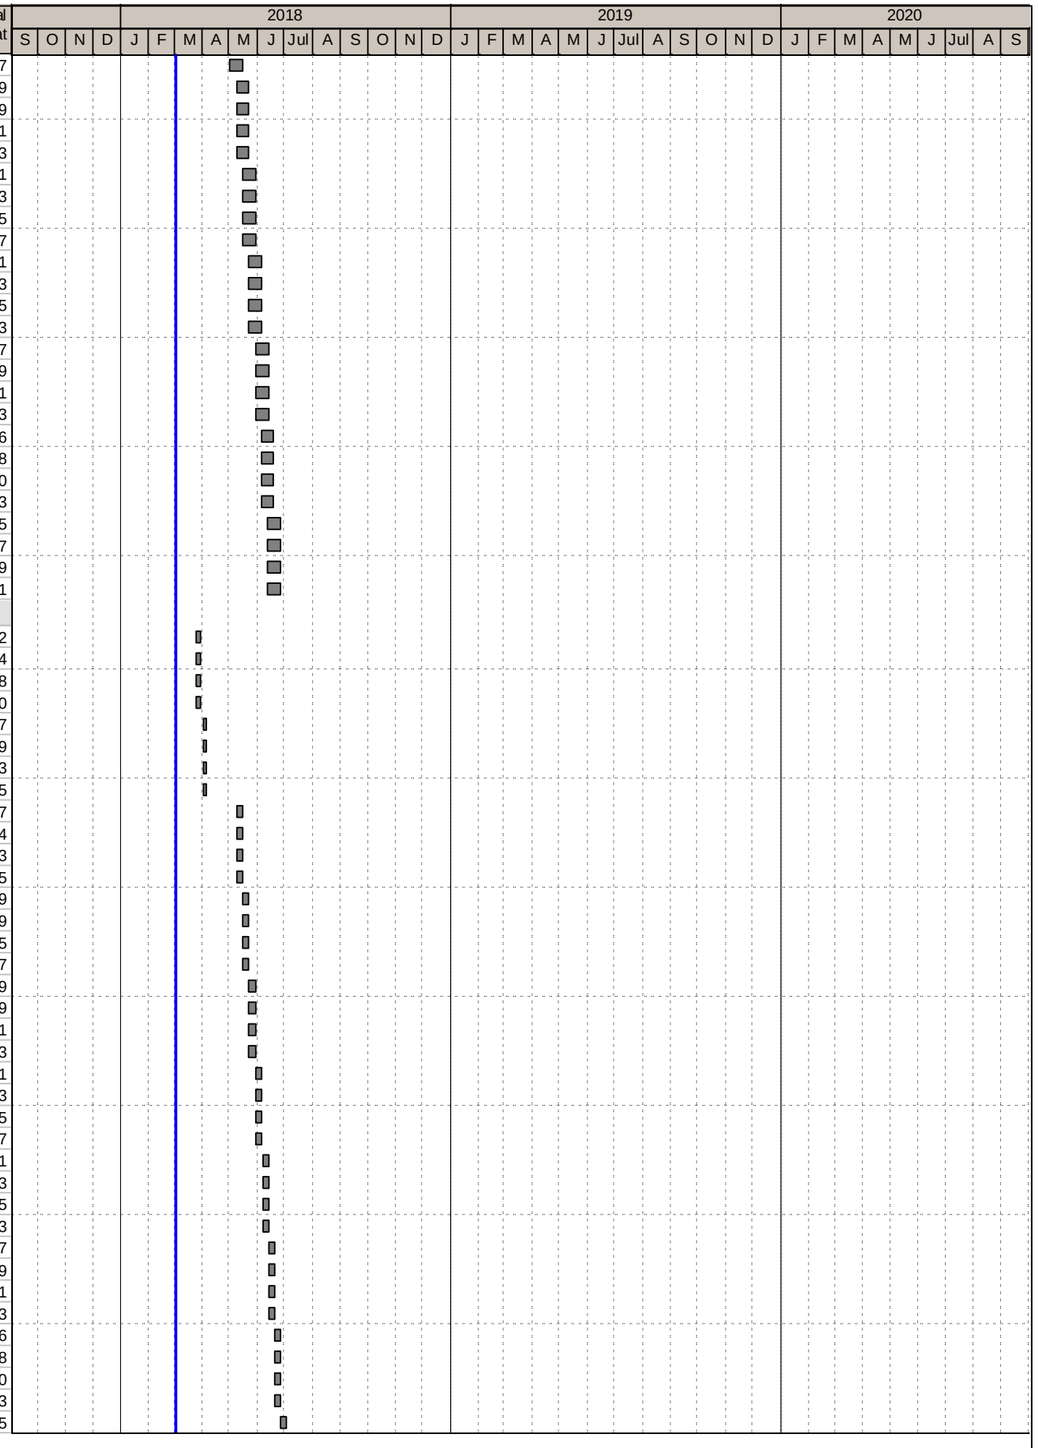

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
SR2D443-5P4J	Steel Truss Col - Subcontractor Scrub/Prepare Fab Sheets - Area D Truss Column (Seq 443)	5	27-Jun-18	03-Jul-18	57
SR2D442-5P4J	Steel Truss Col - Subcontractor Scrub/Prepare Fab Sheets - Area D Truss Column (Seq 442)	5	27-Jun-18	03-Jul-18	59
SR2D441-5P4J	Steel Truss Col - Subcontractor Scrub/Prepare Fab Sheets - Area D Truss Column (Seq 441)	5	27-Jun-18	03-Jul-18	61
SR2A419-5P4F	Steel Truss Col - Subcontractor Fabricate - Area A Truss Column (Seq 419)	45	19-Apr-18	21-Jun-18	19
SR2A420-5P4F	Steel Truss Col - Subcontractor Fabricate - Area A Truss Column (Seq 420)	45	19-Apr-18	21-Jun-18	21
SR2B421-5P4F	Steel Truss Col - Subcontractor Fabricate - Area B Truss Column (Seq 421)	25	17-May-18	21-Jun-18	23
SR2A418-5P4F	Steel Truss Col - Subcontractor Fabricate - Area A Truss Column (Seq 418)	45	19-Apr-18	21-Jun-18	25
SR2A417-5P4F	Steel Truss Col - Subcontractor Fabricate - Area A Truss Column (Seq 417)	45	19-Apr-18	21-Jun-18	27
SR2F408-5P4F	Steel Truss Col - Subcontractor Fabricate - Area F Truss Column (Seq 408)	45	17-May-18	20-Jul-18	19
SR2F407-5P4F	Steel Truss Col - Subcontractor Fabricate - Area F Truss Column (Seq 407)	45	17-May-18	20-Jul-18	21
SR2E406-5P4F	Steel Truss Col - Subcontractor Fabricate - Area E Truss Column (Seq 406)	35	01-Jun-18	20-Jul-18	23
SR2F409-5P4F	Steel Truss Col - Subcontractor Fabricate - Area F Truss Column (Seq 409)	45	17-May-18	20-Jul-18	25
SR2F410-5P4F	Steel Truss Col - Subcontractor Fabricate - Area F Truss Column (Seq 410)	45	17-May-18	20-Jul-18	27
SR2B424-5P4F	Steel Truss Col - Subcontractor Fabricate - Area B Truss Column (Seq 424)	45	24-May-18	27-Jul-18	31
SR2E403-5P4F	Steel Truss Col - Subcontractor Fabricate - Area E Truss Column (Seq 403)	45	24-May-18	27-Jul-18	38
SR2B422-5P4F	Steel Truss Col - Subcontractor Fabricate - Area B Truss Column (Seq 422)	45	24-May-18	27-Jul-18	27
SR2B423-5P4F	Steel Truss Col - Subcontractor Fabricate - Area B Truss Column (Seq 423)	45	24-May-18	27-Jul-18	29
SR2E405-5P4F	Steel Truss Col - Subcontractor Fabricate - Area E Truss Column (Seq 405)	45	24-May-18	27-Jul-18	34
SR2E404-5P4F	Steel Truss Col - Subcontractor Fabricate - Area E Truss Column (Seq 404)	45	24-May-18	27-Jul-18	36
SR2B425-5P4F	Steel Truss Col - Subcontractor Fabricate - Area B Truss Column (Seq 425)	45	31-May-18	02-Aug-18	29
SR2B426-5P4F	Steel Truss Col - Subcontractor Fabricate - Area B Truss Column (Seq 426)	45	31-May-18	02-Aug-18	39
SR2B427-5P4F	Steel Truss Col - Subcontractor Fabricate - Area B Truss Column (Seq 427)	45	31-May-18	02-Aug-18	41
SR2B428-5P4F	Steel Truss Col - Subcontractor Fabricate - Area B Truss Column (Seq 428)	45	31-May-18	02-Aug-18	43
SR2E402-5P4F	Steel Truss Col - Subcontractor Fabricate - Area E Truss Column (Seq 402)	45	07-Jun-18	09-Aug-18	31
SR2E401-5P4F	Steel Truss Col - Subcontractor Fabricate - Area E Truss Column (Seq 401)	45	07-Jun-18	09-Aug-18	33
SR2E450-5P4F	Steel Truss Col - Subcontractor Fabricate - Area E Truss Column (Seq 450)	45	07-Jun-18	09-Aug-18	45
SR2E449-5P4F	Steel Truss Col - Subcontractor Fabricate - Area E Truss Column (Seq 449)	45	07-Jun-18	09-Aug-18	47
SR2B429-5P4F	Steel Truss Col - Subcontractor Fabricate - Area B Truss Column (Seq 429)	45	14-Jun-18	16-Aug-18	41
SR2B430-5P4F	Steel Truss Col - Subcontractor Fabricate - Area B Truss Column (Seq 430)	45	14-Jun-18	16-Aug-18	43
SR2B431-5P4F	Steel Truss Col - Subcontractor Fabricate - Area B Truss Column (Seq 431)	45	14-Jun-18	16-Aug-18	45
SR2B432-5P4F	Steel Truss Col - Subcontractor Fabricate - Area B Truss Column (Seq 432)	45	14-Jun-18	16-Aug-18	53
SR2E448-5P4F	Steel Truss Col - Subcontractor Fabricate - Area E Truss Column (Seq 448)	45	21-Jun-18	23-Aug-18	47
SR2E447-5P4F	Steel Truss Col - Subcontractor Fabricate - Area E Truss Column (Seq 447)	45	21-Jun-18	23-Aug-18	49
SR2E446-5P4F	Steel Truss Col - Subcontractor Fabricate - Area E Truss Column (Seq 446)	45	21-Jun-18	23-Aug-18	51
SR2E445-5P4F	Steel Truss Col - Subcontractor Fabricate - Area E Truss Column (Seq 445)	45	21-Jun-18	23-Aug-18	53
SR2C433-5P4F	Steel Truss Col - Subcontractor Fabricate - Area C Truss Column (Seq 433)	45	27-Jun-18	29-Aug-18	46
SR2C434-5P4F	Steel Truss Col - Subcontractor Fabricate - Area C Truss Column (Seq 434)	45	27-Jun-18	29-Aug-18	48
SR2C435-5P4F	Steel Truss Col - Subcontractor Fabricate - Area C Truss Column (Seq 435)	45	27-Jun-18	29-Aug-18	50
SR2C436-5P4F	Steel Truss Col - Subcontractor Fabricate - Area C Truss Column (Seq 436)	45	27-Jun-18	29-Aug-18	53
SR2D444-5P4F	Steel Truss Col - Subcontractor Fabricate - Area D Truss Column (Seq 444)	45	05-Jul-18	06-Sep-18	55
SR2D443-5P4F	Steel Truss Col - Subcontractor Fabricate - Area D Truss Column (Seq 443)	45	05-Jul-18	06-Sep-18	57
SR2D442-5P4F	Steel Truss Col - Subcontractor Fabricate - Area D Truss Column (Seq 442)	45	05-Jul-18	06-Sep-18	59
SR2D441-5P4F	Steel Truss Col - Subcontractor Fabricate - Area D Truss Column (Seq 441)	45	05-Jul-18	06-Sep-18	61
Truss Column Embed/Supports					
Submit					
SR2A419-5P4S1	Steel Truss Col Embed/Embed Supports - Sub Detail/Submit Shop Drawings - Area A (Seq 1)	15	26-Feb-18 A	08-Mar-18	9
SR21F0-5P4S	Steel Truss Col Embed/Embed Supports - Sub Detail/Submit Shop Drawings - Area F (Seq 5)	15	26-Feb-18 A	08-Mar-18	11
SR21E0-5P4S	Steel Truss Col Embed/Embed Supports - Sub Detail/Submit Shop Drawings - Area E (Seq 6)	15	14-Mar-18	03-Apr-18	12
SR21B0-5P4S	Steel Truss Col Embed/Embed Supports - Sub Detail/Submit Shop Drawings - Area B (Seq 2)	15	14-Mar-18	03-Apr-18	9
SR21B1-5P4S	Steel Truss Col Embed/Embed Supports - Sub Detail/Submit Shop Drawings - Area B (Seq 3)	15	28-Mar-18	17-Apr-18	21
SR21E1-5P4S	Steel Truss Col Embed/Embed Supports - Sub Detail/Submit Shop Drawings - Area E (Seq 7)	15	28-Mar-18	17-Apr-18	25
SR21D0-5P4S	Steel Truss Col Embed/Embed Supports - Sub Detail/Submit Shop Drawings - Area D (Seq 8)	15	04-Apr-18	24-Apr-18	24
SR21C0-5P4S	Steel Truss Col Embed/Embed Supports - Sub Detail/Submit Shop Drawings - Area C (Seq 4)	15	04-Apr-18	24-Apr-18	24
Mortenson Review					
SR2A419-5P4R1	Steel Truss Col Embed/Embed Supports - MMCJVLV Review Shop Drawings - Area A (Seq 1)	2	09-Mar-18	12-Mar-18	9
SR21F0-5P4R	Steel Truss Col Embed/Embed Supports - MMCJVLV Review Shop Drawings - Area F (Seq 5)	2	09-Mar-18	12-Mar-18	11
SR21E0-5P4R	Steel Truss Col Embed/Embed Supports - MMCJVLV Review Shop Drawings - Area E (Seq 6)	2	04-Apr-18	05-Apr-18	12
SR21B0-5P4R	Steel Truss Col Embed/Embed Supports - MMCJVLV Review Shop Drawings - Area B (Seq 2)	2	04-Apr-18	05-Apr-18	9
SR21B1-5P4R	Steel Truss Col Embed/Embed Supports - MMCJVLV Review Shop Drawings - Area B (Seq 3)	2	18-Apr-18	19-Apr-18	21
SR21E1-5P4R	Steel Truss Col Embed/Embed Supports - MMCJVLV Review Shop Drawings - Area E (Seq 7)	2	18-Apr-18	19-Apr-18	25
SR21D0-5P4R	Steel Truss Col Embed/Embed Supports - MMCJVLV Review Shop Drawings - Area D (Seq 8)	2	25-Apr-18	26-Apr-18	24
SR21C0-5P4R	Steel Truss Col Embed/Embed Supports - MMCJVLV Review Shop Drawings - Area C (Seq 4)	2	25-Apr-18	26-Apr-18	24

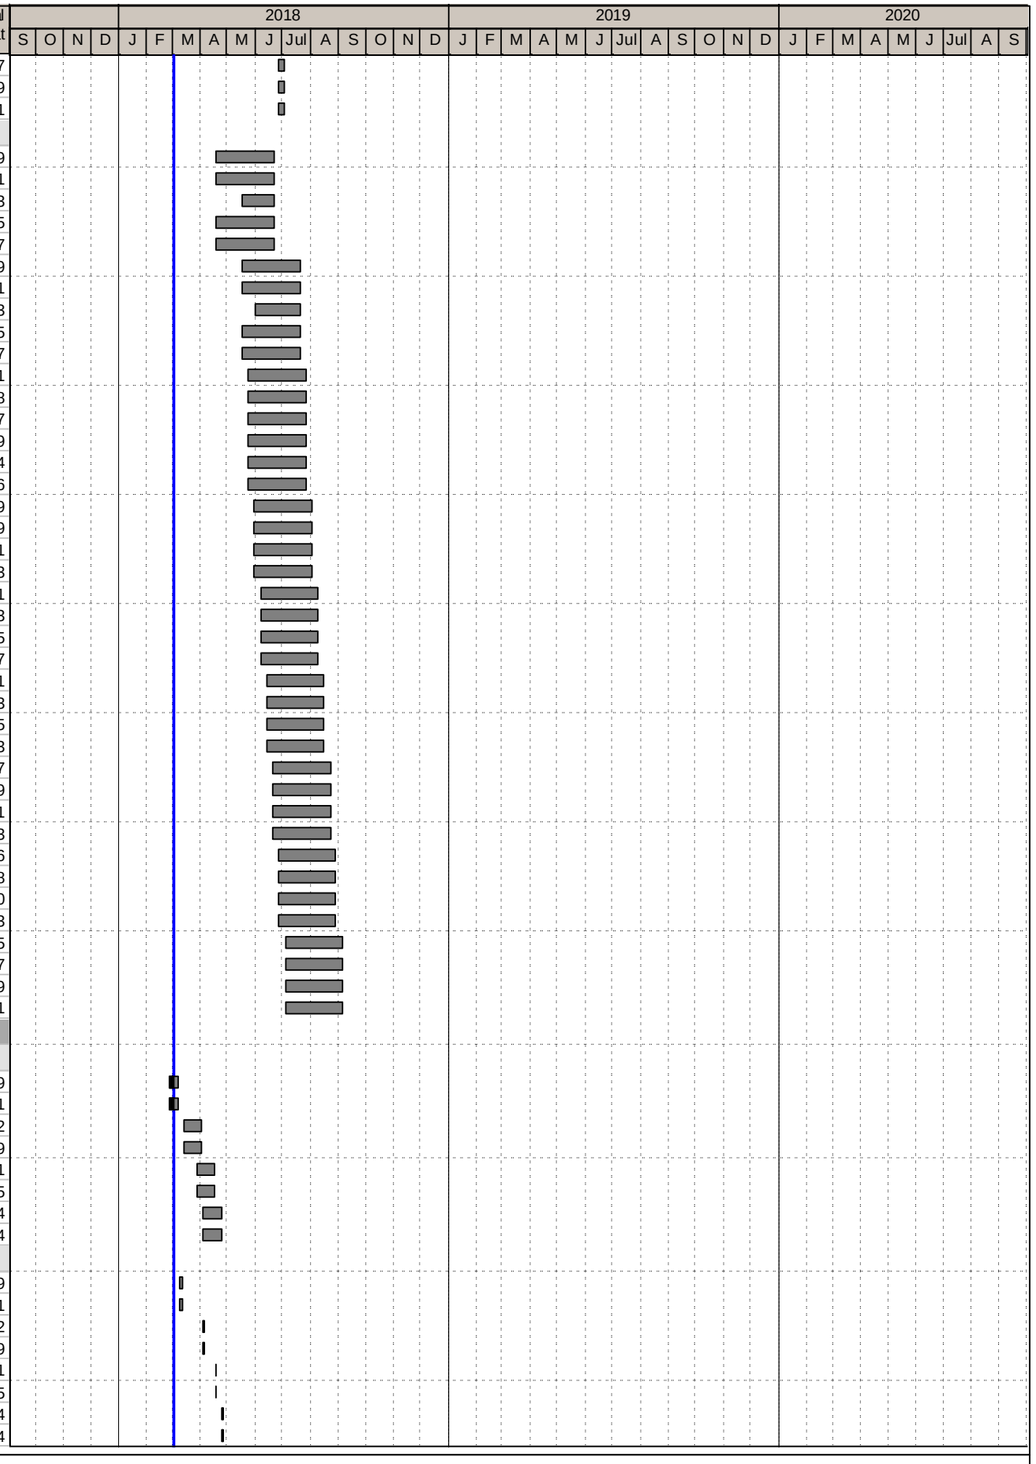

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
Approve					
SR2A419-5P4A1	Steel Truss Col Embed/Embed Supports - Design Team Review/Approve Shop Drawings - Area A (Seq 1)	10	13-Mar-18	26-Mar-18	9
SR21F0-5P4A	Steel Truss Col Embed/Embed Supports - Design Team Review/Approve Shop Drawings - Area F (Seq 5)	10	13-Mar-18	26-Mar-18	11
SR21E0-5P4A	Steel Truss Col Embed/Embed Supports - Design Team Review/Approve Shop Drawings - Area E (Seq 6)	10	06-Apr-18	19-Apr-18	12
SR21B0-5P4A	Steel Truss Col Embed/Embed Supports - Design Team Review/Approve Shop Drawings - Area B (Seq 2)	10	06-Apr-18	19-Apr-18	9
SR21B1-5P4A	Steel Truss Col Embed/Embed Supports - Design Team Review/Approve Shop Drawings - Area B (Seq 3)	10	20-Apr-18	03-May-18	21
SR21E1-5P4A	Steel Truss Col Embed/Embed Supports - Design Team Review/Approve Shop Drawings - Area E (Seq 7)	10	20-Apr-18	03-May-18	25
SR21D0-5P4A	Steel Truss Col Embed/Embed Supports - Design Team Review/Approve Shop Drawings - Area D (Seq 8)	10	27-Apr-18	10-May-18	24
SR21C0-5P4A	Steel Truss Col Embed/Embed Supports - Design Team Review/Approve Shop Drawings - Area C (Seq 4)	10	27-Apr-18	10-May-18	24
SR2A419-5P4J1	Steel Truss Col Embed/Embed Supports - Sub Scrub/Prepare Fab Sheets - Area A (Seq 1)	5	27-Mar-18	02-Apr-18	9
SR21F0-5P4J	Steel Truss Col Embed/Embed Supports - Sub Scrub/Prepare Fab Sheets - Area F (Seq 5)	5	27-Mar-18	02-Apr-18	11
SR21E0-5P4J	Steel Truss Col Embed/Embed Supports - Sub Scrub/Prepare Fab Sheets - Area E (Seq 6)	5	20-Apr-18	26-Apr-18	12
SR21B0-5P4J	Steel Truss Col Embed/Embed Supports - Sub Scrub/Prepare Fab Sheets - Area B (Seq 2)	5	20-Apr-18	26-Apr-18	9
SR21B1-5P4J	Steel Truss Col Embed/Embed Supports - Sub Scrub/Prepare Fab Sheets - Area B (Seq 3)	5	04-May-18	10-May-18	21
SR21E1-5P4J	Steel Truss Col Embed/Embed Supports - Sub Scrub/Prepare Fab Sheets - Area E (Seq 7)	5	04-May-18	10-May-18	25
SR21D0-5P4J	Steel Truss Col Embed/Embed Supports - Sub Scrub/Prepare Fab Sheets - Area D (Seq 8)	5	11-May-18	17-May-18	24
SR21C0-5P4J	Steel Truss Col Embed/Embed Supports - Sub Scrub/Prepare Fab Sheets - Area C (Seq 4)	5	11-May-18	17-May-18	24
SR21A0-5P4F	Steel Truss Col Embed/Embed Supports - Sub Fabricate Embed Support - Area A (Seq 1)	15	03-Apr-18	23-Apr-18	14
SR21F0-5P4F	Steel Truss Col Embed/Embed Supports - Sub Fabricate Embed Support - Area F (Seq 5)	15	03-Apr-18	23-Apr-18	16
SR21A0-5P4F1	Steel Truss Col Embed/Embed Supports - Sub Fabricate Embed - Area A (Seq 1)	20	03-Apr-18	30-Apr-18	9
SR21F0-5P4F1	Steel Truss Col Embed/Embed Supports - Sub Fabricate Embed - Area F (Seq 5)	20	03-Apr-18	30-Apr-18	11
SR21E0-5P4F	Steel Truss Col Embed/Embed Supports - Sub Fabricate Embed Support - Area E (Seq 6)	15	27-Apr-18	17-May-18	17
SR21B0-5P4F	Steel Truss Col Embed/Embed Supports - Sub Fabricate Embed Support - Area B (Seq 2)	15	27-Apr-18	17-May-18	14
SR21E0-5P4F1	Steel Truss Col Embed/Embed Supports - Sub Fabricate Embed - Area E (Seq 6)	20	27-Apr-18	24-May-18	12
SR21B0-5P4F1	Steel Truss Col Embed/Embed Supports - Sub Fabricate Embed - Area B (Seq 2)	20	27-Apr-18	24-May-18	9
SR21B1-5P4F	Steel Truss Col Embed/Embed Supports - Sub Fabricate Embed Support - Area B (Seq 3)	15	11-May-18	01-Jun-18	26
SR21E1-5P4F	Steel Truss Col Embed/Embed Supports - Sub Fabricate Embed Support - Area E (Seq 7)	15	11-May-18	01-Jun-18	30
SR21D0-5P4F	Steel Truss Col Embed/Embed Supports - Sub Fabricate Embed Support - Area D (Seq 8)	15	18-May-18	08-Jun-18	29
SR21C0-5P4F	Steel Truss Col Embed/Embed Supports - Sub Fabricate Embed Support - Area C (Seq 4)	15	18-May-18	08-Jun-18	29
SR21B1-5P4F1	Steel Truss Col Embed/Embed Supports - Sub Fabricate Embed - Area B (Seq 3)	20	11-May-18	08-Jun-18	21
SR21E1-5P4F1	Steel Truss Col Embed/Embed Supports - Sub Fabricate Embed - Area E (Seq 7)	20	11-May-18	08-Jun-18	25
SR21D0-5P4F1	Steel Truss Col Embed/Embed Supports - Sub Fabricate Embed - Area D (Seq 8)	20	18-May-18	15-Jun-18	24
SR21C0-5P4F1	Steel Truss Col Embed/Embed Supports - Sub Fabricate Embed - Area C (Seq 4)	20	18-May-18	15-Jun-18	24
400 Canopy Roof Lvl					
Submit					
SRA501-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area A (Seq 5190)	25	17-Aug-18	21-Sep-18	14
SRB504-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area B (Seq 5180)	25	17-Aug-18	21-Sep-18	14
SRB505-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area A (Seq 5160)	25	17-Aug-18	21-Sep-18	14
SRA521-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area A (Seq 5170)	25	17-Aug-18	21-Sep-18	14
SRA511-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area F (Seq 5070)	25	24-Aug-18	28-Sep-18	14
SRB502-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area F (Seq 5090)	25	24-Aug-18	28-Sep-18	14
SRB503-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area F (Seq 5080)	25	24-Aug-18	28-Sep-18	14
SRC506-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area F (Seq 5100)	25	24-Aug-18	28-Sep-18	14
SRF513-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area B (Seq 5220)	25	31-Aug-18	05-Oct-18	28
SRF515-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area B (Seq 5200)	25	31-Aug-18	05-Oct-18	28
SRC522-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area B (Seq 5210)	25	31-Aug-18	05-Oct-18	28
SRC525-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area B (Seq 5230)	25	31-Aug-18	05-Oct-18	28
SRE518-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area B (Seq 5240)	25	10-Sep-18	12-Oct-18	28
SRE519-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area E (Seq 5060)	25	10-Sep-18	12-Oct-18	28
SRC526-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area E (Seq 5050)	25	10-Sep-18	12-Oct-18	28
SRC527-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area B (Seq 5250)	25	10-Sep-18	12-Oct-18	28
SRC507-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area E (Seq 5040)	25	17-Sep-18	19-Oct-18	28
SRF516-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area E (Seq 5030)	25	17-Sep-18	19-Oct-18	28
SRF523-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area B (Seq 5270)	25	17-Sep-18	19-Oct-18	28
SRD524-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area B (Seq 5260)	25	17-Sep-18	19-Oct-18	28
SRA512-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area E (Seq 5010)	25	24-Sep-18	26-Oct-18	28
SRF514-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area B (Seq 5290)	25	24-Sep-18	26-Oct-18	28
SRE520-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area B (Seq 5310)	25	24-Sep-18	26-Oct-18	29
SRD508-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area B (Seq 5280)	25	24-Sep-18	26-Oct-18	28
SRE502-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area E (Seq 5020)	25	24-Sep-18	26-Oct-18	29
SRE531-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area B (Seq 5300)	25	24-Sep-18	26-Oct-18	29

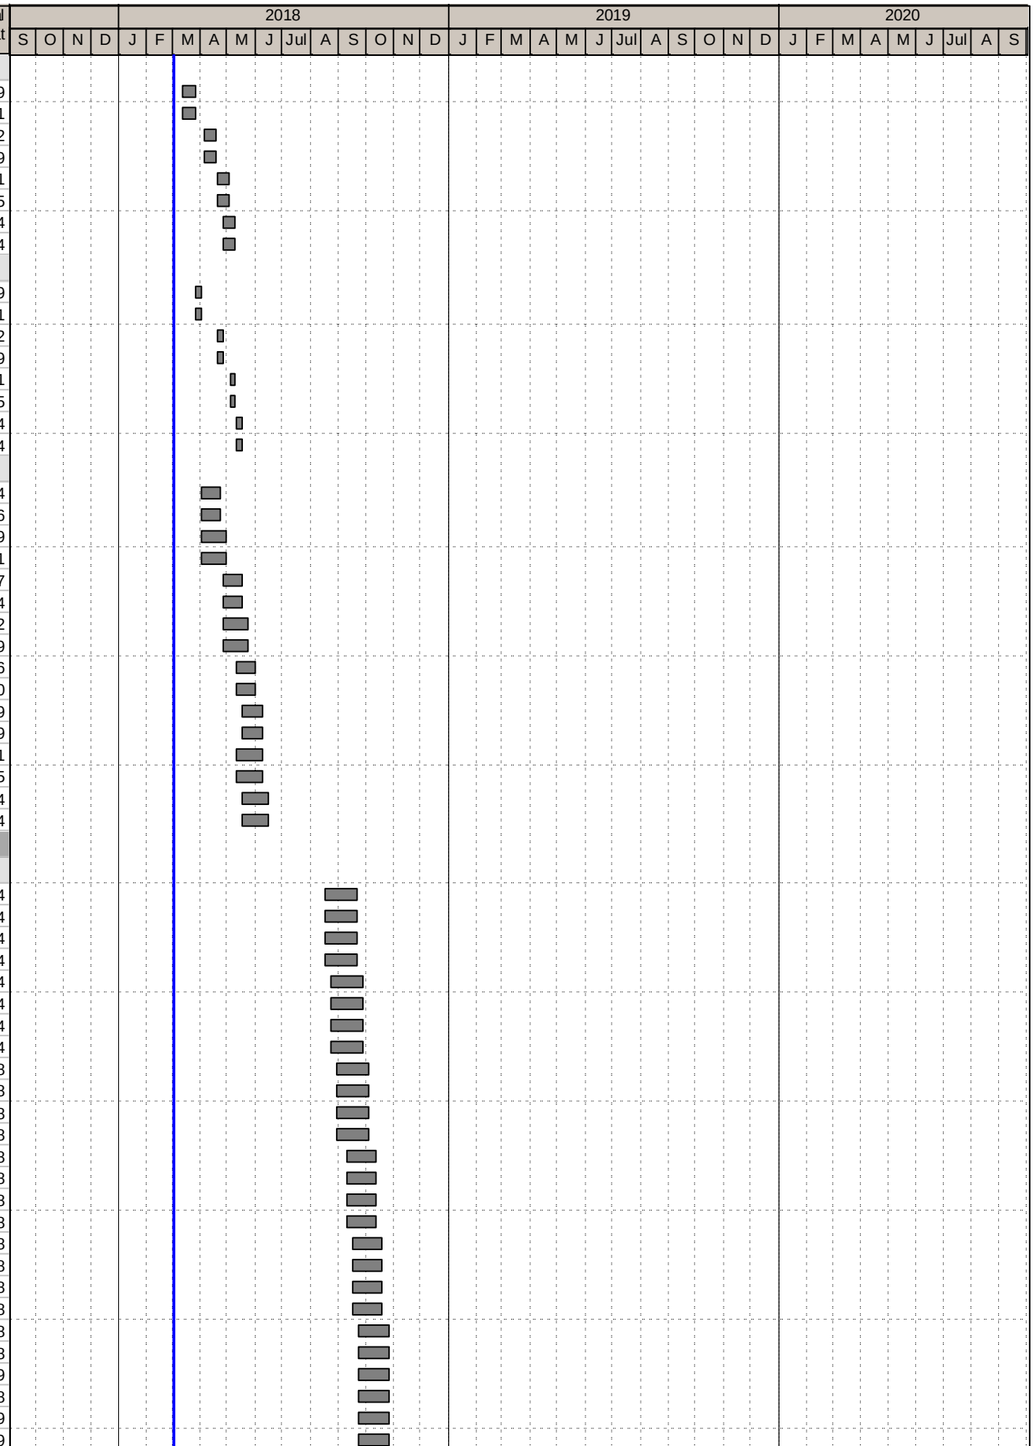

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
SRE517-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area A (Seq 5140)	25	01-Oct-18	02-Nov-18	29
SRD510-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area F (Seq 5120)	25	01-Oct-18	02-Nov-18	34
SRE513-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area A (Seq 5132)	25	01-Oct-18	02-Nov-18	38
SRE5131-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area A (Seq 5131)	25	01-Oct-18	02-Nov-18	38
SRF511-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area F (Seq 5112)	25	01-Oct-18	02-Nov-18	38
SRF51-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area F (Seq 5111)	25	01-Oct-18	02-Nov-18	38
SRD509-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area E (Seq 5490)	25	08-Oct-18	09-Nov-18	38
SRE550-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area E (Seq 5500)	25	08-Oct-18	09-Nov-18	41
SRE547-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area E (Seq 5470)	25	08-Oct-18	09-Nov-18	41
SRE548-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area E (Seq 5480)	25	08-Oct-18	09-Nov-18	41
SRE545-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area E (Seq 5450)	25	15-Oct-18	16-Nov-18	41
SRE546-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area E (Seq 5460)	25	15-Oct-18	16-Nov-18	41
SRD543-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area D (Seq 5430)	25	15-Oct-18	16-Nov-18	41
SRD544-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area D (Seq 5440)	25	15-Oct-18	16-Nov-18	41
SRC533-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area C (Seq 5330)	25	19-Oct-18	26-Nov-18	41
SRC532-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area C (Seq 5320)	25	19-Oct-18	26-Nov-18	45
SRC534-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area C (Seq 5340)	25	19-Oct-18	26-Nov-18	45
SRC5331-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area C (Seq 5331)	25	19-Oct-18	26-Nov-18	45
SRD542-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area D (Seq 5420)	25	25-Oct-18	30-Nov-18	45
SRD5421-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area D (Seq 5421)	25	25-Oct-18	30-Nov-18	47
SRD540-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area D (Seq 5400)	25	25-Oct-18	30-Nov-18	52
SRC536-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area C (Seq 5360)	25	25-Oct-18	30-Nov-18	47
SRD5412-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area D (Seq 5412)	25	01-Nov-18	07-Dec-18	58
SRD5411-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area D (Seq 5411)	25	01-Nov-18	07-Dec-18	62
SRD5371-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area D (Seq 5371)	25	01-Nov-18	07-Dec-18	65
SRC537-5P4S	Steel Roof Canopy - Detail/Submit Shop Drawings - Area C (Seq 5372)	25	01-Nov-18	07-Dec-18	61
Mortenson Review					
SRA501-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area A (Seq 5190)	2	24-Sep-18	25-Sep-18	23
SRB504-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area B (Seq 5180)	2	24-Sep-18	25-Sep-18	42
SRB505-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area B (Seq 5160)	2	24-Sep-18	25-Sep-18	33
SRA521-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area A (Seq 5170)	2	24-Sep-18	25-Sep-18	28
SRA511-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area A (Seq 5070)	2	01-Oct-18	02-Oct-18	23
SRB502-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area B (Seq 5090)	2	01-Oct-18	02-Oct-18	28
SRB503-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area B (Seq 5080)	2	01-Oct-18	02-Oct-18	45
SRC506-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area C (Seq 5100)	2	01-Oct-18	02-Oct-18	33
SRF513-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area F (Seq 5220)	2	08-Oct-18	09-Oct-18	51
SRF515-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area F (Seq 5200)	2	08-Oct-18	09-Oct-18	44
SRC522-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area C (Seq 5210)	2	08-Oct-18	09-Oct-18	34
SRC525-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area C (Seq 5230)	2	08-Oct-18	09-Oct-18	40
SRE518-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area E (Seq 5240)	2	15-Oct-18	16-Oct-18	52
SRE519-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area E (Seq 5060)	2	15-Oct-18	16-Oct-18	44
SRC526-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area C (Seq 5050)	2	15-Oct-18	16-Oct-18	28
SRC527-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area C (Seq 5250)	2	15-Oct-18	16-Oct-18	42
SRC507-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area C (Seq 5040)	2	22-Oct-18	23-Oct-18	43
SRF516-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area F (Seq 5030)	2	22-Oct-18	23-Oct-18	28
SRF523-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area F (Seq 5270)	2	22-Oct-18	23-Oct-18	43
SRD524-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area D (Seq 5260)	2	22-Oct-18	23-Oct-18	53
SRA512-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area A (Seq 5010)	2	29-Oct-18	30-Oct-18	28
SRF514-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area F (Seq 5290)	2	29-Oct-18	30-Oct-18	44
SRE520-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area E (Seq 5310)	2	29-Oct-18	30-Oct-18	50
SRD508-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area D (Seq 5280)	2	29-Oct-18	30-Oct-18	54
SRE502-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area E (Seq 5020)	2	29-Oct-18	30-Oct-18	42
SRE531-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area B (Seq 5300)	2	29-Oct-18	30-Oct-18	60
SRE517-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area E (Seq 5140)	2	05-Nov-18	06-Nov-18	29
SRD510-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area D (Seq 5120)	2	05-Nov-18	06-Nov-18	34
SRE513-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area A (Seq 5132)	2	05-Nov-18	06-Nov-18	45
SRE5131-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area A (Seq 5131)	2	05-Nov-18	06-Nov-18	60
SRF511-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area F (Seq 5112)	2	05-Nov-18	06-Nov-18	45
SRF51-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area F (Seq 5111)	2	05-Nov-18	06-Nov-18	57
SRD509-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area D (Seq 5490)	2	12-Nov-18	13-Nov-18	38
SRE550-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area E (Seq 5500)	2	12-Nov-18	13-Nov-18	51
SRE547-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area E (Seq 5470)	2	12-Nov-18	13-Nov-18	43
SRE548-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area E (Seq 5480)	2	12-Nov-18	13-Nov-18	56

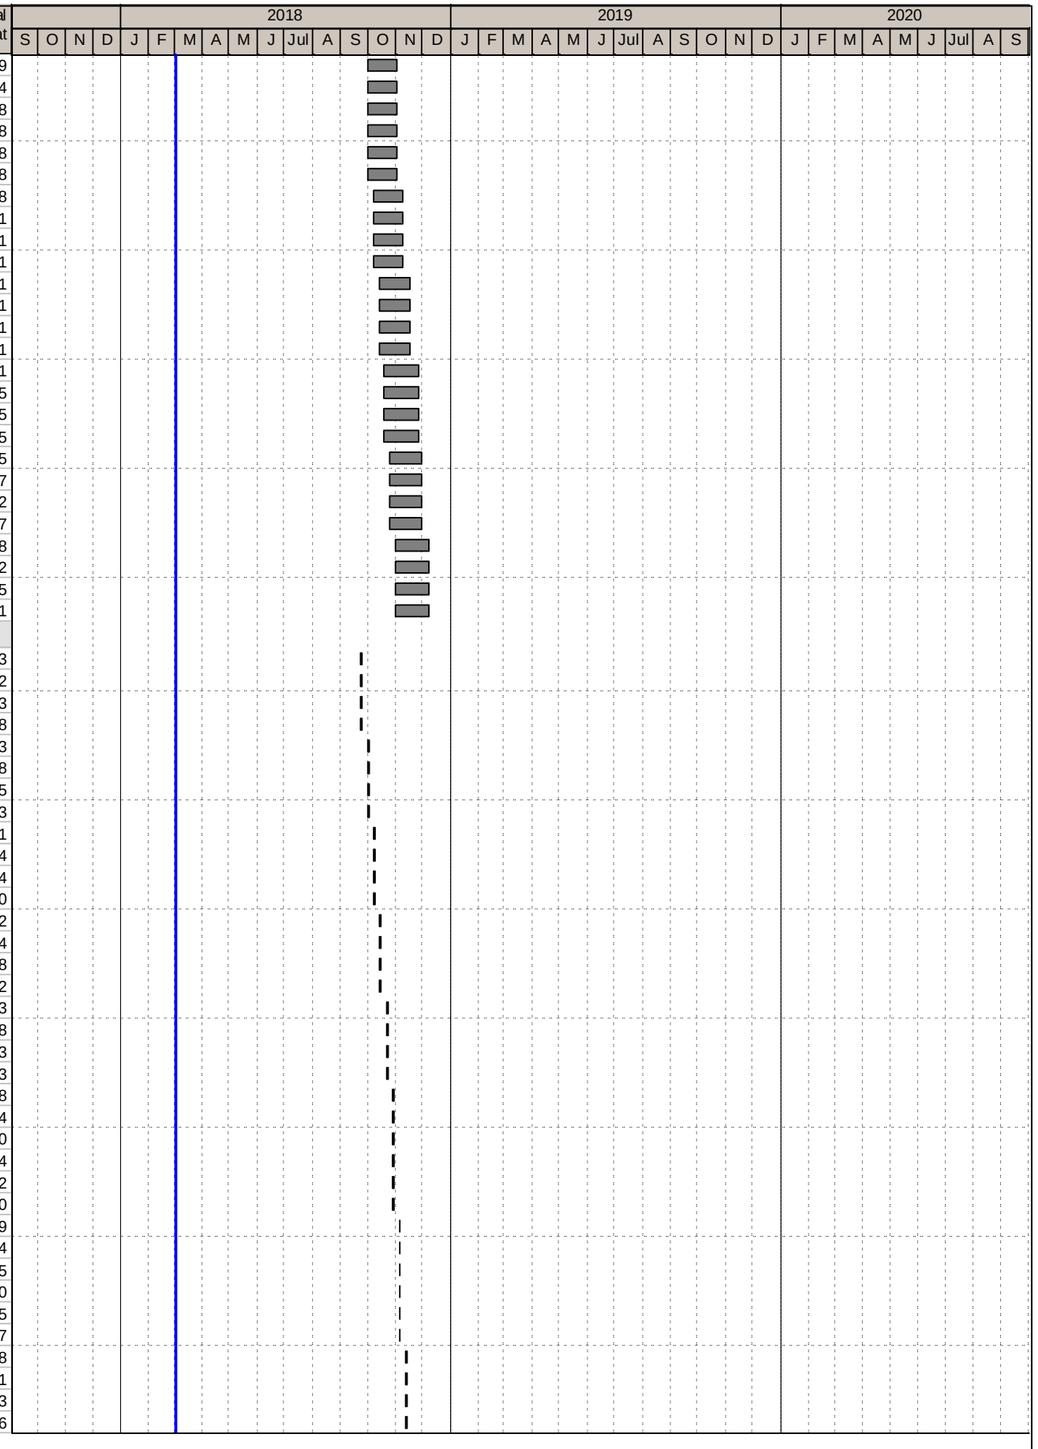

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
SRE545-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area E (Seq 5450)	2	19-Nov-18	20-Nov-18	43
SRE546-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area E (Seq 5460)	2	19-Nov-18	20-Nov-18	55
SRD543-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area D (Seq 5430)	2	19-Nov-18	20-Nov-18	48
SRD544-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area D (Seq 5440)	2	19-Nov-18	20-Nov-18	59
SRC533-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area C (Seq 5330)	2	27-Nov-18	28-Nov-18	41
SRC532-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area C (Seq 5320)	2	27-Nov-18	28-Nov-18	55
SRC534-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area C (Seq 5340)	2	27-Nov-18	28-Nov-18	46
SRC5331-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area C (Seq 5331)	2	27-Nov-18	28-Nov-18	59
SRD542-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area D (Seq 5420)	2	03-Dec-18	04-Dec-18	45
SRD5421-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area D (Seq 5421)	2	03-Dec-18	04-Dec-18	55
SRD540-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area D (Seq 5400)	2	03-Dec-18	04-Dec-18	52
SRC536-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area C (Seq 5360)	2	03-Dec-18	04-Dec-18	47
SRD5412-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area D (Seq 5412)	2	10-Dec-18	11-Dec-18	58
SRD5411-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area D (Seq 5411)	2	10-Dec-18	11-Dec-18	62
SRD5371-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area D (Seq 5371)	2	10-Dec-18	11-Dec-18	65
SRC537-5P4R	Steel Roof Canopy - MMCJVLV Review Shop Drawings - Area C (Seq 5372)	2	10-Dec-18	11-Dec-18	61
Approve					
SRA501-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area A (Seq 5190)	10	26-Sep-18	09-Oct-18	23
SRB504-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area B (Seq 5180)	10	26-Sep-18	09-Oct-18	42
SRB505-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area B (Seq 5160)	10	26-Sep-18	09-Oct-18	33
SRA521-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area A (Seq 5170)	10	26-Sep-18	09-Oct-18	28
SRA511-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area A (Seq 5070)	10	03-Oct-18	16-Oct-18	23
SRB502-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area B (Seq 5090)	10	03-Oct-18	16-Oct-18	28
SRB503-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area B (Seq 5080)	10	03-Oct-18	16-Oct-18	45
SRC506-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area C (Seq 5100)	10	03-Oct-18	16-Oct-18	33
SRF513-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area F (Seq 5220)	10	10-Oct-18	23-Oct-18	51
SRF515-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area F (Seq 5200)	10	10-Oct-18	23-Oct-18	44
SRC522-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area C (Seq 5210)	10	10-Oct-18	23-Oct-18	34
SRC525-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area C (Seq 5230)	10	10-Oct-18	23-Oct-18	40
SRE518-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area E (Seq 5240)	10	17-Oct-18	30-Oct-18	52
SRE519-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area E (Seq 5060)	10	17-Oct-18	30-Oct-18	44
SRC526-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area C (Seq 5050)	10	17-Oct-18	30-Oct-18	28
SRC527-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area C (Seq 5250)	10	17-Oct-18	30-Oct-18	42
SRC507-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area C (Seq 5040)	10	24-Oct-18	06-Nov-18	43
SRF516-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area F (Seq 5030)	10	24-Oct-18	06-Nov-18	28
SRF523-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area F (Seq 5270)	10	24-Oct-18	06-Nov-18	43
SRD524-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area D (Seq 5260)	10	24-Oct-18	06-Nov-18	53
SRA512-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area A (Seq 5010)	10	31-Oct-18	13-Nov-18	28
SRF514-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area F (Seq 5290)	10	31-Oct-18	13-Nov-18	44
SRE520-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area E (Seq 5310)	10	31-Oct-18	13-Nov-18	50
SRD508-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area D (Seq 5280)	10	31-Oct-18	13-Nov-18	54
SRE502-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area E (Seq 5020)	10	31-Oct-18	13-Nov-18	42
SRE531-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area B (Seq 5300)	10	31-Oct-18	13-Nov-18	60
SRE517-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area E (Seq 5140)	10	07-Nov-18	20-Nov-18	29
SRD510-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area D (Seq 5120)	10	07-Nov-18	20-Nov-18	34
SRE513-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area A (Seq 5132)	10	07-Nov-18	20-Nov-18	45
SRE5131-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area A (Seq 5131)	10	07-Nov-18	20-Nov-18	60
SRF511-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area F (Seq 5112)	10	07-Nov-18	20-Nov-18	45
SRF51-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area F (Seq 5111)	10	07-Nov-18	20-Nov-18	57
SRD509-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area D (Seq 5490)	10	14-Nov-18	29-Nov-18	38
SRE550-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area E (Seq 5500)	10	14-Nov-18	29-Nov-18	51
SRE547-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area E (Seq 5470)	10	14-Nov-18	29-Nov-18	43
SRE548-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area E (Seq 5480)	10	14-Nov-18	29-Nov-18	56
SRE545-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area E (Seq 5450)	10	21-Nov-18	06-Dec-18	43
SRE546-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area E (Seq 5460)	10	21-Nov-18	06-Dec-18	55
SRD543-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area D (Seq 5430)	10	21-Nov-18	06-Dec-18	48
SRD544-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area D (Seq 5440)	10	21-Nov-18	06-Dec-18	59
SRC533-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area C (Seq 5330)	10	29-Nov-18	12-Dec-18	41
SRC532-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area C (Seq 5320)	10	29-Nov-18	12-Dec-18	55
SRC534-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area C (Seq 5340)	10	29-Nov-18	12-Dec-18	46
SRC5331-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area C (Seq 5331)	10	29-Nov-18	12-Dec-18	59
SRD542-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area D (Seq 5420)	10	05-Dec-18	18-Dec-18	45
SRD5421-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area D (Seq 5421)	10	05-Dec-18	18-Dec-18	55

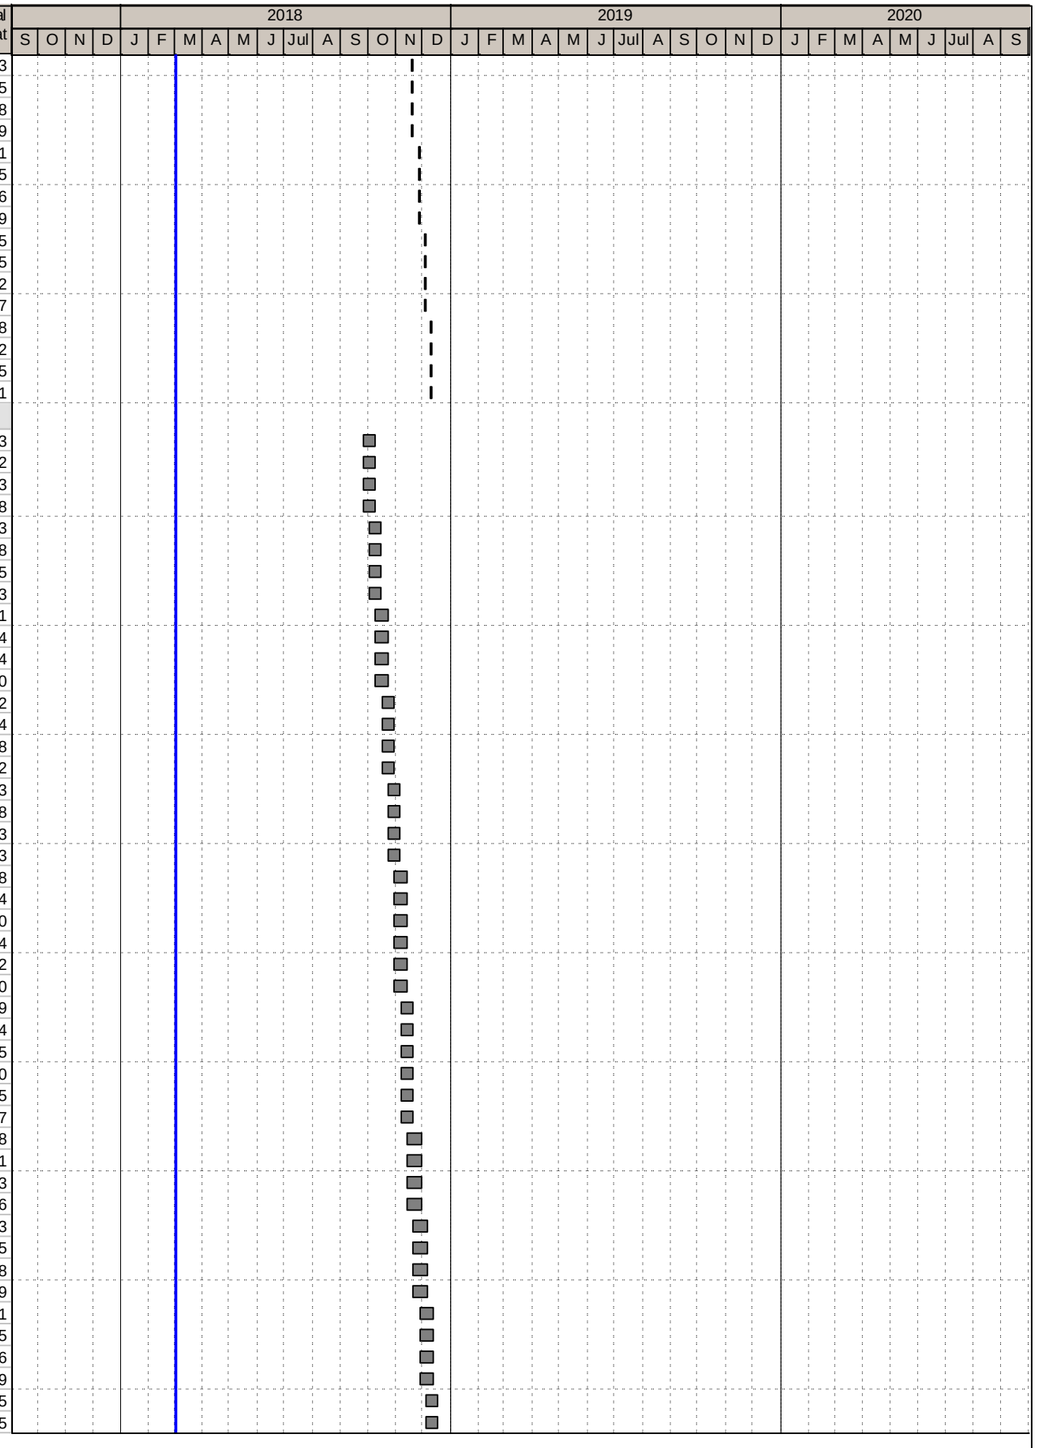

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
SRD540-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area D (Seq 5400)	10	05-Dec-18	18-Dec-18	52
SRC536-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area C (Seq 5360)	10	05-Dec-18	18-Dec-18	47
SRD5412-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area D (Seq 5412)	10	12-Dec-18	26-Dec-18	58
SRD5411-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area D (Seq 5411)	10	12-Dec-18	26-Dec-18	62
SRD5371-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area D (Seq 5371)	10	12-Dec-18	26-Dec-18	65
SRC537-5P4A	Steel Roof Canopy - Design Team Review/Approve Shop Drawings - Area C (Seq 5372)	10	12-Dec-18	26-Dec-18	61
SRA501-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area A (Seq 5190)	5	10-Oct-18	16-Oct-18	23
SRB504-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area B (Seq 5180)	5	10-Oct-18	16-Oct-18	42
SRB505-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area B (Seq 5160)	5	10-Oct-18	16-Oct-18	33
SRA521-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area A (Seq 5170)	5	10-Oct-18	16-Oct-18	28
SRA511-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area A (Seq 5070)	5	17-Oct-18	23-Oct-18	23
SRB502-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area B (Seq 5090)	5	17-Oct-18	23-Oct-18	28
SRB503-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area B (Seq 5080)	5	17-Oct-18	23-Oct-18	45
SRC506-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area C (Seq 5100)	5	17-Oct-18	23-Oct-18	33
SRF513-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area F (Seq 5220)	5	24-Oct-18	30-Oct-18	51
SRF515-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area F (Seq 5200)	5	24-Oct-18	30-Oct-18	44
SRC522-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area C (Seq 5210)	5	24-Oct-18	30-Oct-18	34
SRC525-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area C (Seq 5230)	5	24-Oct-18	30-Oct-18	40
SRE518-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area E (Seq 5240)	5	31-Oct-18	06-Nov-18	52
SRE519-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area E (Seq 5060)	5	31-Oct-18	06-Nov-18	44
SRC526-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area C (Seq 5050)	5	31-Oct-18	06-Nov-18	28
SRC527-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area C (Seq 5250)	5	31-Oct-18	06-Nov-18	42
SRC507-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area C (Seq 5040)	5	07-Nov-18	13-Nov-18	43
SRF516-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area F (Seq 5030)	5	07-Nov-18	13-Nov-18	28
SRF523-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area F (Seq 5270)	5	07-Nov-18	13-Nov-18	43
SRD524-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area D (Seq 5260)	5	07-Nov-18	13-Nov-18	53
SRA512-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area A (Seq 5010)	5	14-Nov-18	20-Nov-18	28
SRF514-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area F (Seq 5290)	5	14-Nov-18	20-Nov-18	44
SRE520-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area E (Seq 5310)	5	14-Nov-18	20-Nov-18	50
SRD508-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area D (Seq 5280)	5	14-Nov-18	20-Nov-18	54
SRE502-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area E (Seq 5020)	5	14-Nov-18	20-Nov-18	42
SRE531-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area B (Seq 5300)	5	14-Nov-18	20-Nov-18	60
SRE517-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area E (Seq 5140)	5	21-Nov-18	29-Nov-18	29
SRD510-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area D (Seq 5120)	5	21-Nov-18	29-Nov-18	34
SRE513-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area A (Seq 5132)	5	21-Nov-18	29-Nov-18	45
SRE5131-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area A (Seq 5131)	5	21-Nov-18	29-Nov-18	60
SRF511-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area F (Seq 5112)	5	21-Nov-18	29-Nov-18	45
SRF51-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area F (Seq 5111)	5	21-Nov-18	29-Nov-18	57
SRD509-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area D (Seq 5490)	5	30-Nov-18	06-Dec-18	38
SRE550-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area E (Seq 5500)	5	30-Nov-18	06-Dec-18	51
SRE547-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area E (Seq 5470)	5	30-Nov-18	06-Dec-18	43
SRE548-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area E (Seq 5480)	5	30-Nov-18	06-Dec-18	56
SRE545-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area E (Seq 5450)	5	07-Dec-18	13-Dec-18	43
SRE546-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area E (Seq 5460)	5	07-Dec-18	13-Dec-18	55
SRD543-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area D (Seq 5430)	5	07-Dec-18	13-Dec-18	48
SRD544-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area D (Seq 5440)	5	07-Dec-18	13-Dec-18	59
SRC533-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area C (Seq 5330)	5	13-Dec-18	19-Dec-18	41
SRC532-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area C (Seq 5320)	5	13-Dec-18	19-Dec-18	55
SRC534-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area C (Seq 5340)	5	13-Dec-18	19-Dec-18	46
SRC5331-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area C (Seq 5331)	5	13-Dec-18	19-Dec-18	59
SRD542-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area D (Seq 5420)	5	19-Dec-18	26-Dec-18	45
SRD5421-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area D (Seq 5421)	5	19-Dec-18	26-Dec-18	55
SRD540-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area D (Seq 5400)	5	19-Dec-18	26-Dec-18	52
SRC536-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area C (Seq 5360)	5	19-Dec-18	26-Dec-18	47
SRD5412-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area D (Seq 5412)	5	27-Dec-18	03-Jan-19	58
SRD5411-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area D (Seq 5411)	5	27-Dec-18	03-Jan-19	62
SRD5371-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area D (Seq 5371)	5	27-Dec-18	03-Jan-19	65
SRC537-5P4J	Steel Roof Canopy - Subcontractor Scrub/Prepare Fab Sheets - Area C (Seq 5372)	5	27-Dec-18	03-Jan-19	61
SRA501-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area A (Seq 5190)	25	17-Oct-18	20-Nov-18	23
SRB504-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area B (Seq 5180)	25	17-Oct-18	20-Nov-18	42
SRB505-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area B (Seq 5160)	25	17-Oct-18	20-Nov-18	33

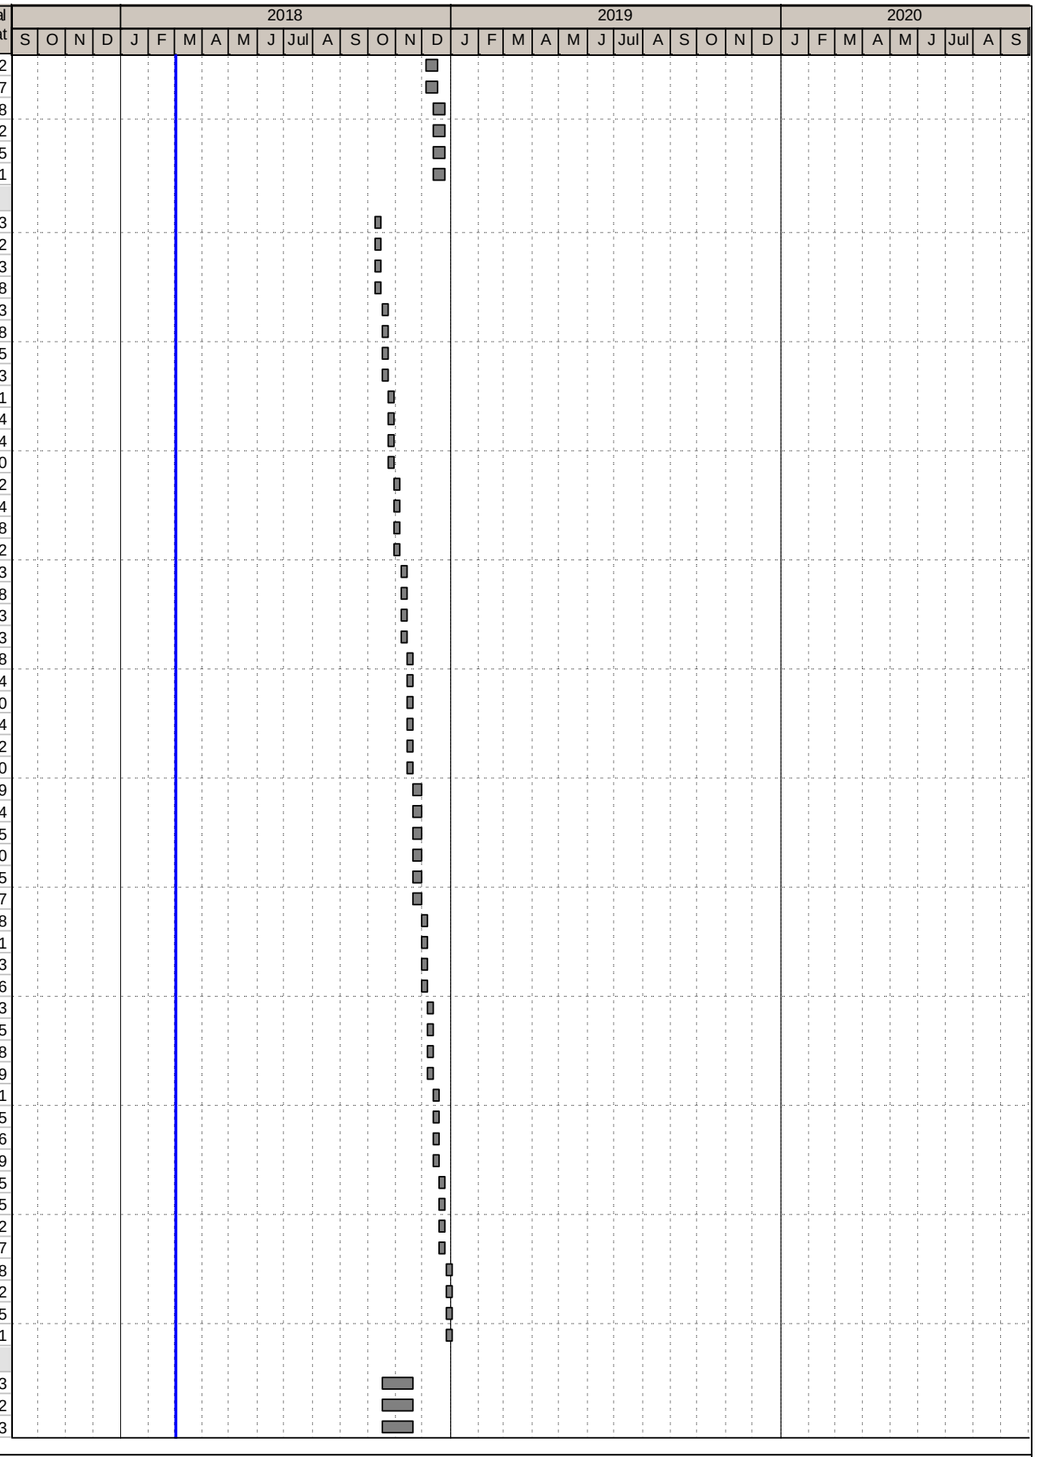

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
SRA521-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area A (Seq 5170)	25	17-Oct-18	20-Nov-18	28
SRA511-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area A (Seq 5070)	25	24-Oct-18	29-Nov-18	23
SRB502-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area B (Seq 5090)	25	24-Oct-18	29-Nov-18	28
SRB503-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area B (Seq 5080)	25	24-Oct-18	29-Nov-18	45
SRC506-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area C (Seq 5100)	25	24-Oct-18	29-Nov-18	33
SRF513-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area F (Seq 5220)	25	31-Oct-18	06-Dec-18	51
SRF515-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area F (Seq 5200)	25	31-Oct-18	06-Dec-18	44
SRC522-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area C (Seq 5210)	25	31-Oct-18	06-Dec-18	34
SRC525-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area C (Seq 5230)	25	31-Oct-18	06-Dec-18	40
SRE518-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area E (Seq 5240)	25	07-Nov-18	13-Dec-18	52
SRE519-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area E (Seq 5060)	25	07-Nov-18	13-Dec-18	44
SRC526-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area C (Seq 5050)	25	07-Nov-18	13-Dec-18	28
SRC527-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area C (Seq 5250)	25	07-Nov-18	13-Dec-18	42
SRC507-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area C (Seq 5040)	25	14-Nov-18	20-Dec-18	43
SRF516-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area F (Seq 5030)	25	14-Nov-18	20-Dec-18	28
SRF523-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area F (Seq 5270)	25	14-Nov-18	20-Dec-18	43
SRD524-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area D (Seq 5260)	25	14-Nov-18	20-Dec-18	53
SRA512-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area A (Seq 5010)	25	21-Nov-18	28-Dec-18	28
SRF514-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area F (Seq 5290)	25	21-Nov-18	28-Dec-18	44
SRE520-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area E (Seq 5310)	25	21-Nov-18	28-Dec-18	50
SRD508-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area D (Seq 5280)	25	21-Nov-18	28-Dec-18	54
SRE502-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area E (Seq 5020)	25	21-Nov-18	28-Dec-18	42
SRE531-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area B (Seq 5300)	25	21-Nov-18	28-Dec-18	60
SRE517-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area E (Seq 5140)	25	30-Nov-18	07-Jan-19	29
SRD510-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area D (Seq 5120)	25	30-Nov-18	07-Jan-19	34
SRE513-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area A (Seq 5132)	25	30-Nov-18	07-Jan-19	45
SRE5131-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area A (Seq 5131)	25	30-Nov-18	07-Jan-19	60
SRF511-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area F (Seq 5112)	25	30-Nov-18	07-Jan-19	45
SRF51-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area F (Seq 5111)	25	30-Nov-18	07-Jan-19	57
SRD509-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area D (Seq 5490)	25	07-Dec-18	14-Jan-19	38
SRE550-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area E (Seq 5500)	25	07-Dec-18	14-Jan-19	51
SRE547-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area E (Seq 5470)	25	07-Dec-18	14-Jan-19	43
SRE548-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area E (Seq 5480)	25	07-Dec-18	14-Jan-19	56
SRE545-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area E (Seq 5450)	25	14-Dec-18	21-Jan-19	43
SRE546-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area E (Seq 5460)	25	14-Dec-18	21-Jan-19	55
SRD543-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area D (Seq 5430)	25	14-Dec-18	21-Jan-19	48
SRD544-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area D (Seq 5440)	25	14-Dec-18	21-Jan-19	59
SRC533-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area C (Seq 5330)	25	20-Dec-18	25-Jan-19	41
SRC532-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area C (Seq 5320)	25	20-Dec-18	25-Jan-19	55
SRC534-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area C (Seq 5340)	25	20-Dec-18	25-Jan-19	46
SRC5331-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area C (Seq 5331)	25	20-Dec-18	25-Jan-19	59
SRD542-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area D (Seq 5420)	25	27-Dec-18	31-Jan-19	45
SRD5421-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area D (Seq 5421)	25	27-Dec-18	31-Jan-19	55
SRD540-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area D (Seq 5400)	25	27-Dec-18	31-Jan-19	52
SRC536-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area C (Seq 5360)	25	27-Dec-18	31-Jan-19	47
SRD5412-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area D (Seq 5412)	25	04-Jan-19	07-Feb-19	58
SRD5411-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area D (Seq 5411)	25	04-Jan-19	07-Feb-19	62
SRD5371-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area D (Seq 5371)	25	04-Jan-19	07-Feb-19	65
SRC537-5P4F	Steel Roof Canopy - Subcontractor Fabricate & Paint - Area C (Seq 5372)	25	04-Jan-19	07-Feb-19	61
SRA501-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area A (Seq 5190)	3	06-Dec-18	10-Dec-18	14
SRA511-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area A (Seq 5070)	3	10-Dec-18	12-Dec-18	17
SRA521-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area A (Seq 5170)	3	13-Dec-18	17-Dec-18	14
SRB502-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area B (Seq 5090)	3	17-Dec-18	19-Dec-18	17
SRB505-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area B (Seq 5160)	3	20-Dec-18	24-Dec-18	14
SRC506-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area C (Seq 5100)	3	24-Dec-18	27-Dec-18	17
SRB503-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area B (Seq 5080)	3	03-Jan-19	07-Jan-19	23
SRB504-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area B (Seq 5180)	3	03-Jan-19	07-Jan-19	15
SRC522-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area C (Seq 5210)	3	11-Jan-19	15-Jan-19	11
SRC526-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area C (Seq 5050)	3	16-Jan-19	18-Jan-19	7
SRC525-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area C (Seq 5230)	3	18-Jan-19	22-Jan-19	12
SRF516-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area F (Seq 5030)	3	23-Jan-19	25-Jan-19	7
SRC527-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area C (Seq 5250)	3	25-Jan-19	29-Jan-19	14

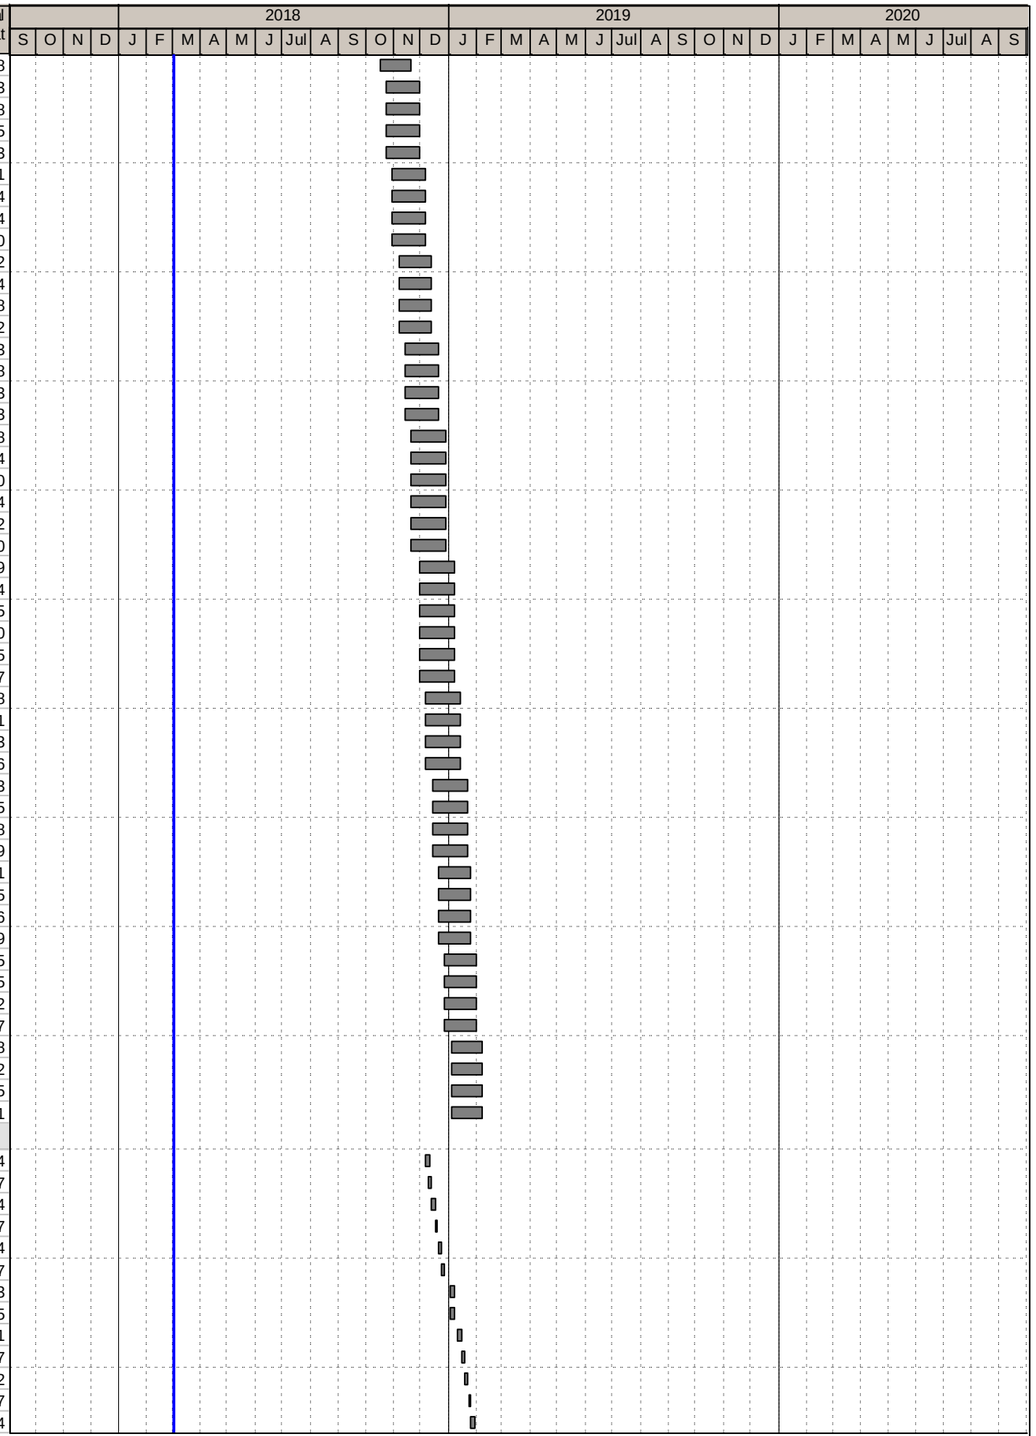

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
SRA512-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area A (Seq 5010)	3	30-Jan-19	01-Feb-19	7
SRF515-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area F (Seq 5200)	3	01-Feb-19	05-Feb-19	6
SRF523-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area F (Seq 5270)	3	01-Feb-19	05-Feb-19	15
SRE517-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area E (Seq 5140)	3	06-Feb-19	08-Feb-19	8
SRF513-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area F (Seq 5220)	3	07-Feb-19	11-Feb-19	9
SRE519-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area E (Seq 5060)	3	07-Feb-19	11-Feb-19	7
SRF514-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area F (Seq 5290)	3	08-Feb-19	12-Feb-19	16
SRC507-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area C (Seq 5040)	3	14-Feb-19	18-Feb-19	6
SRE518-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area E (Seq 5240)	3	14-Feb-19	18-Feb-19	10
SRD510-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area D (Seq 5120)	3	14-Feb-19	18-Feb-19	7
SRE520-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area E (Seq 5310)	3	18-Feb-19	20-Feb-19	16
SRD524-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area D (Seq 5260)	3	20-Feb-19	22-Feb-19	12
SRE502-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area E (Seq 5020)	3	20-Feb-19	22-Feb-19	6
SRD509-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area D (Seq 5490)	3	21-Feb-19	25-Feb-19	11
SRD508-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area D (Seq 5280)	3	26-Feb-19	28-Feb-19	14
SRE547-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area E (Seq 5470)	3	28-Feb-19	04-Mar-19	11
SRE531-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area B (Seq 5300)	3	04-Mar-19	06-Mar-19	16
SRE513-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area A (Seq 5132)	3	04-Mar-19	06-Mar-19	6
SRF511-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area F (Seq 5112)	3	04-Mar-19	06-Mar-19	6
SRE545-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area E (Seq 5450)	3	07-Mar-19	11-Mar-19	11
SRE550-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area E (Seq 5500)	3	08-Mar-19	12-Mar-19	13
SRC533-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area C (Seq 5330)	3	13-Mar-19	15-Mar-19	9
SRE548-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area E (Seq 5480)	3	14-Mar-19	18-Mar-19	14
SRD543-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area D (Seq 5430)	3	18-Mar-19	20-Mar-19	9
SRF51-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area F (Seq 5111)	3	20-Mar-19	22-Mar-19	6
SRC534-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area C (Seq 5340)	3	20-Mar-19	22-Mar-19	9
SRE546-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area E (Seq 5460)	3	21-Mar-19	25-Mar-19	13
SRE5131-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area A (Seq 5131)	3	25-Mar-19	27-Mar-19	6
SRD542-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area D (Seq 5420)	3	25-Mar-19	27-Mar-19	9
SRC536-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area C (Seq 5360)	3	27-Mar-19	29-Mar-19	9
SRD544-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area D (Seq 5440)	3	02-Apr-19	04-Apr-19	9
SRC532-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area C (Seq 5320)	3	02-Apr-19	04-Apr-19	9
SRD540-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area D (Seq 5400)	3	03-Apr-19	05-Apr-19	9
SRD5421-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area D (Seq 5421)	3	08-Apr-19	10-Apr-19	9
SRC5331-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area C (Seq 5331)	3	08-Apr-19	10-Apr-19	9
SRD5412-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area D (Seq 5412)	3	18-Apr-19	22-Apr-19	9
SRD5411-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area D (Seq 5411)	3	23-Apr-19	25-Apr-19	10
SRC537-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area C (Seq 5372)	3	23-Apr-19	25-Apr-19	9
SRD5371-5P4F1	Steel Roof Canopy - Subcontractor Deliver - Area D (Seq 5371)	3	29-Apr-19	01-May-19	9
FRP Slab on Metal Deck					
100 Main Concourse					
Submit					
S3C1-8P4FS	Rebar SOMD - Subcontractor Develop/Submit Shop Drawings - Main Concourse C/D	10	06-Jun-18	19-Jun-18	221
Mortenson Review					
S3C1-8P4FR	Rebar SOMD - MMCJV Review Shop Drawings - Main Concourse C/D	2	20-Jun-18	21-Jun-18	221
Approve					
S3C1-8P4FA	Rebar SOMD - Design Team Review/Approve Shop Drawings - Main Concourse C/D	10	22-Jun-18	06-Jul-18	221
Fabricate					
S3C1-5P4FF	Rebar SOMD - Fabricate - Main Concourse C1	5	23-Apr-19	29-Apr-19	22
S3C2-5P4FF	Rebar SOMD - Fabricate - Main Concourse C2	5	26-Apr-19	02-May-19	22
S3D1-5P4FF	Rebar SOMD - Fabricate - Main Concourse D1	5	01-May-19	07-May-19	22
S3D2-5P4FF	Rebar SOMD - Fabricate - Main Concourse D2	5	06-May-19	10-May-19	22
150 Lower Suite Level					
Submit					
S4A1-8P4FS	Rebar SOMD - Subcontractor Develop/Submit Shop Drawings - Lower Suite A	10	08-May-18	21-May-18	107
S4FS-8P4FS	Rebar SOMD - Subcontractor Develop/Submit Shop Drawings - Lower Suite F	10	15-May-18	29-May-18	107
S4B1-8P4FS	Rebar SOMD - Subcontractor Develop/Submit Shop Drawings - Lower Suite B	10	22-May-18	05-Jun-18	121
S4E1-8P4FS	Rebar SOMD - Subcontractor Develop/Submit Shop Drawings - Lower Suite E	10	30-May-18	12-Jun-18	121
S4C1-8P4FS	Rebar SOMD - Subcontractor Develop/Submit Shop Drawings - Lower Suite C	10	06-Jun-18	19-Jun-18	171
S4D1-8P4FS	Rebar SOMD - Subcontractor Develop/Submit Shop Drawings - Lower Suite D	10	13-Jun-18	26-Jun-18	171
Mortenson Review					
S4A1-8P4FR	Rebar SOMD - MMCJV Review Shop Drawings - Lower Suite A	2	22-May-18	23-May-18	112

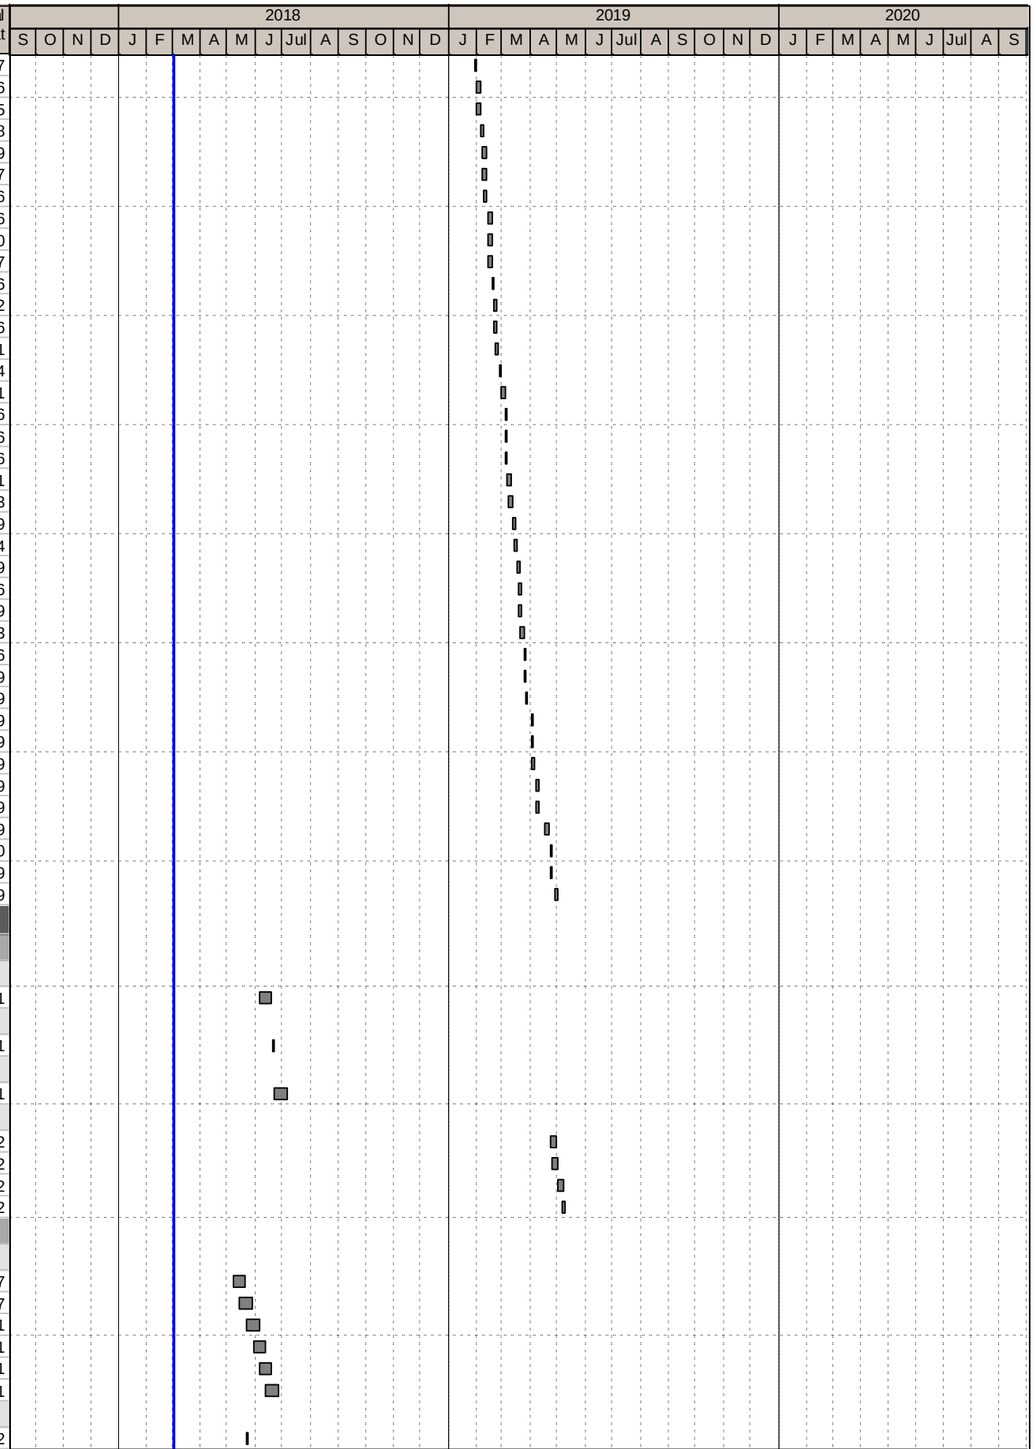

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S4FS-8P4FR	Rebar SOMD - MMCJV Review Shop Drawings - Lower Suite F	2	30-May-18	31-May-18	107
S4B1-8P4FR	Rebar SOMD - MMCJV Review Shop Drawings - Lower Suite B	2	06-Jun-18	07-Jun-18	121
S4E1-8P4FR	Rebar SOMD - MMCJV Review Shop Drawings - Lower Suite E	2	13-Jun-18	14-Jun-18	121
S4C1-8P4FR	Rebar SOMD - MMCJV Review Shop Drawings - Lower Suite C	2	20-Jun-18	21-Jun-18	223
S4D1-8P4FR	Rebar SOMD - MMCJV Review Shop Drawings - Lower Suite D	2	27-Jun-18	28-Jun-18	171
Approve					
S4A1-8P4FA	Rebar SOMD - Design Team Review/Approve Shop Drawings - Lower Suite A	10	24-May-18	07-Jun-18	112
S4FS-8P4FA	Rebar SOMD - Design Team Review/Approve Shop Drawings - Lower Suite F	10	01-Jun-18	14-Jun-18	107
S4B1-8P4FA	Rebar SOMD - Design Team Review/Approve Shop Drawings - Lower Suite B	10	08-Jun-18	21-Jun-18	121
S4E1-8P4FA	Rebar SOMD - Design Team Review/Approve Shop Drawings - Lower Suite E	10	15-Jun-18	28-Jun-18	121
S4C1-8P4FA	Rebar SOMD - Design Team Review/Approve Shop Drawings - Lower Suite C	10	22-Jun-18	06-Jul-18	223
S4D1-8P4FA	Rebar SOMD - Design Team Review/Approve Shop Drawings - Lower Suite D	10	29-Jun-18	13-Jul-18	171
Fabricate					
S4B1-5P4FF	Rebar SOMD - Fabricate - Lower Suite B1	5	17-Oct-18	23-Oct-18	40
S4A1-5P4FF	Rebar SOMD - Fabricate - Lower Suite A1	5	18-Oct-18	24-Oct-18	20
S4F1-5P4FF	Rebar SOMD - Fabricate - Lower Suite F1	5	18-Oct-18	24-Oct-18	20
S4E1-5P4FF	Rebar SOMD - Fabricate - Lower Suite E1	5	30-Oct-18	05-Nov-18	36
S4E2-5P4FF	Rebar SOMD - Fabricate - Lower Suite E2	5	08-Nov-18	15-Nov-18	31
S4B2-5P4FF	Rebar SOMD - Fabricate - Lower Suite B2	5	15-Nov-18	21-Nov-18	33
S4B3-5P4FF	Rebar SOMD - Fabricate - Lower Suite B3	5	20-Nov-18	28-Nov-18	32
S4B4-5P4FF	Rebar SOMD - Fabricate - Lower Suite B4	5	21-Nov-18	29-Nov-18	31
S4B5-5P4FF	Rebar SOMD - Fabricate - Lower Suite B5	5	10-Dec-18	14-Dec-18	22
S4E3-5P4FF	Rebar SOMD - Fabricate - Lower Suite E3	5	10-Dec-18	14-Dec-18	14
S4E4-5P4FF	Rebar SOMD - Fabricate - Lower Suite E4	5	13-Dec-18	19-Dec-18	13
S4C1-5P4FF	Rebar SOMD - Fabricate - Lower Suite C1	5	18-Dec-18	24-Dec-18	111
S4E5-5P4FF	Rebar SOMD - Fabricate - Lower Suite E5	5	20-Dec-18	27-Dec-18	10
S4D1-5P4FF	Rebar SOMD - Fabricate - Lower Suite D1	5	10-Jan-19	16-Jan-19	49
S4D2-5P4FF	Rebar SOMD - Fabricate - Lower Suite D2	5	25-Jan-19	31-Jan-19	97
S4C2-5P4FF	Rebar SOMD - Fabricate - Lower Suite C2	5	28-Jan-19	01-Feb-19	86
S4C3-5P4FF	Rebar SOMD - Fabricate - Lower Suite C3	5	30-Jan-19	05-Feb-19	99
200 Upper Suite Level					
Submit					
S5A1-8P4FS	Rebar SOMD - Subcontractor Develop/Submit Shop Drawings - Upper Suite A	10	22-May-18	05-Jun-18	102
S5F0-8P4FS	Rebar SOMD - Subcontractor Develop/Submit Shop Drawings - Upper Suite F	10	30-May-18	12-Jun-18	102
S5B1-8P4FS	Rebar SOMD - Subcontractor Develop/Submit Shop Drawings - Upper Suite B	10	06-Jun-18	19-Jun-18	111
S5E1-8P4FS	Rebar SOMD - Subcontractor Develop/Submit Shop Drawings - Upper Suite E	10	13-Jun-18	26-Jun-18	111
S5C1-8P4FS	Rebar SOMD - Subcontractor Develop/Submit Shop Drawings - Upper Suite C	10	20-Jun-18	03-Jul-18	159
S5D1-8P4FS	Rebar SOMD - Subcontractor Develop/Submit Shop Drawings - Upper Suite D	10	27-Jun-18	11-Jul-18	159
Mortenson Review					
S5A1-8P4FR	Rebar SOMD - MMCJV Review Shop Drawings - Upper Suite A	2	06-Jun-18	07-Jun-18	107
S5F0-8P4FR	Rebar SOMD - MMCJV Review Shop Drawings - Upper Suite F	2	13-Jun-18	14-Jun-18	102
S5B1-8P4FR	Rebar SOMD - MMCJV Review Shop Drawings - Upper Suite B	2	20-Jun-18	21-Jun-18	120
S5E1-8P4FR	Rebar SOMD - MMCJV Review Shop Drawings - Upper Suite E	2	27-Jun-18	28-Jun-18	111
S5C1-8P4FR	Rebar SOMD - MMCJV Review Shop Drawings - Upper Suite C	2	05-Jul-18	06-Jul-18	167
S5D1-8P4FR	Rebar SOMD - MMCJV Review Shop Drawings - Upper Suite D	2	12-Jul-18	13-Jul-18	159
Approve					
S5A1-8P4FA	Rebar SOMD - Design Team Review/Approve Shop Drawings - Upper Suite A	10	08-Jun-18	21-Jun-18	107
S5F0-8P4FA	Rebar SOMD - Design Team Review/Approve Shop Drawings - Upper Suite F	10	15-Jun-18	28-Jun-18	102
S5B1-8P4FA	Rebar SOMD - Design Team Review/Approve Shop Drawings - Upper Suite B	10	22-Jun-18	06-Jul-18	120
S5E1-8P4FA	Rebar SOMD - Design Team Review/Approve Shop Drawings - Upper Suite E	10	29-Jun-18	13-Jul-18	111
S5C1-8P4FA	Rebar SOMD - Design Team Review/Approve Shop Drawings - Upper Suite C	10	09-Jul-18	20-Jul-18	167
S5D1-8P4FA	Rebar SOMD - Design Team Review/Approve Shop Drawings - Upper Suite D	10	16-Jul-18	27-Jul-18	159
Fabricate					
S5A1-5P4FF	Rebar SOMD - Fabricate - Upper Suite A1	5	12-Oct-18	18-Oct-18	29
S5F0-5P4FF	Rebar SOMD - Fabricate - Upper Suite F1	5	16-Oct-18	22-Oct-18	27
S5A2-5P4FF	Rebar SOMD - Fabricate - Upper Suite A2	5	22-Oct-18	26-Oct-18	25
S5A3-5P4FF	Rebar SOMD - Fabricate - Upper Suite A3	5	24-Oct-18	30-Oct-18	26
S5F2-5P4FF	Rebar SOMD - Fabricate - Upper Suite F2	5	01-Nov-18	07-Nov-18	17
S5B1-5P4FF	Rebar SOMD - Fabricate - Upper Suite B1	5	02-Nov-18	08-Nov-18	37
S5F3-5P4FF	Rebar SOMD - Fabricate - Upper Suite F3	5	05-Nov-18	09-Nov-18	18
S5B2-5P4FF	Rebar SOMD - Fabricate - Upper Suite B2	5	03-Dec-18	07-Dec-18	21
S5B3-5P4FF	Rebar SOMD - Fabricate - Upper Suite B3	5	05-Dec-18	11-Dec-18	21

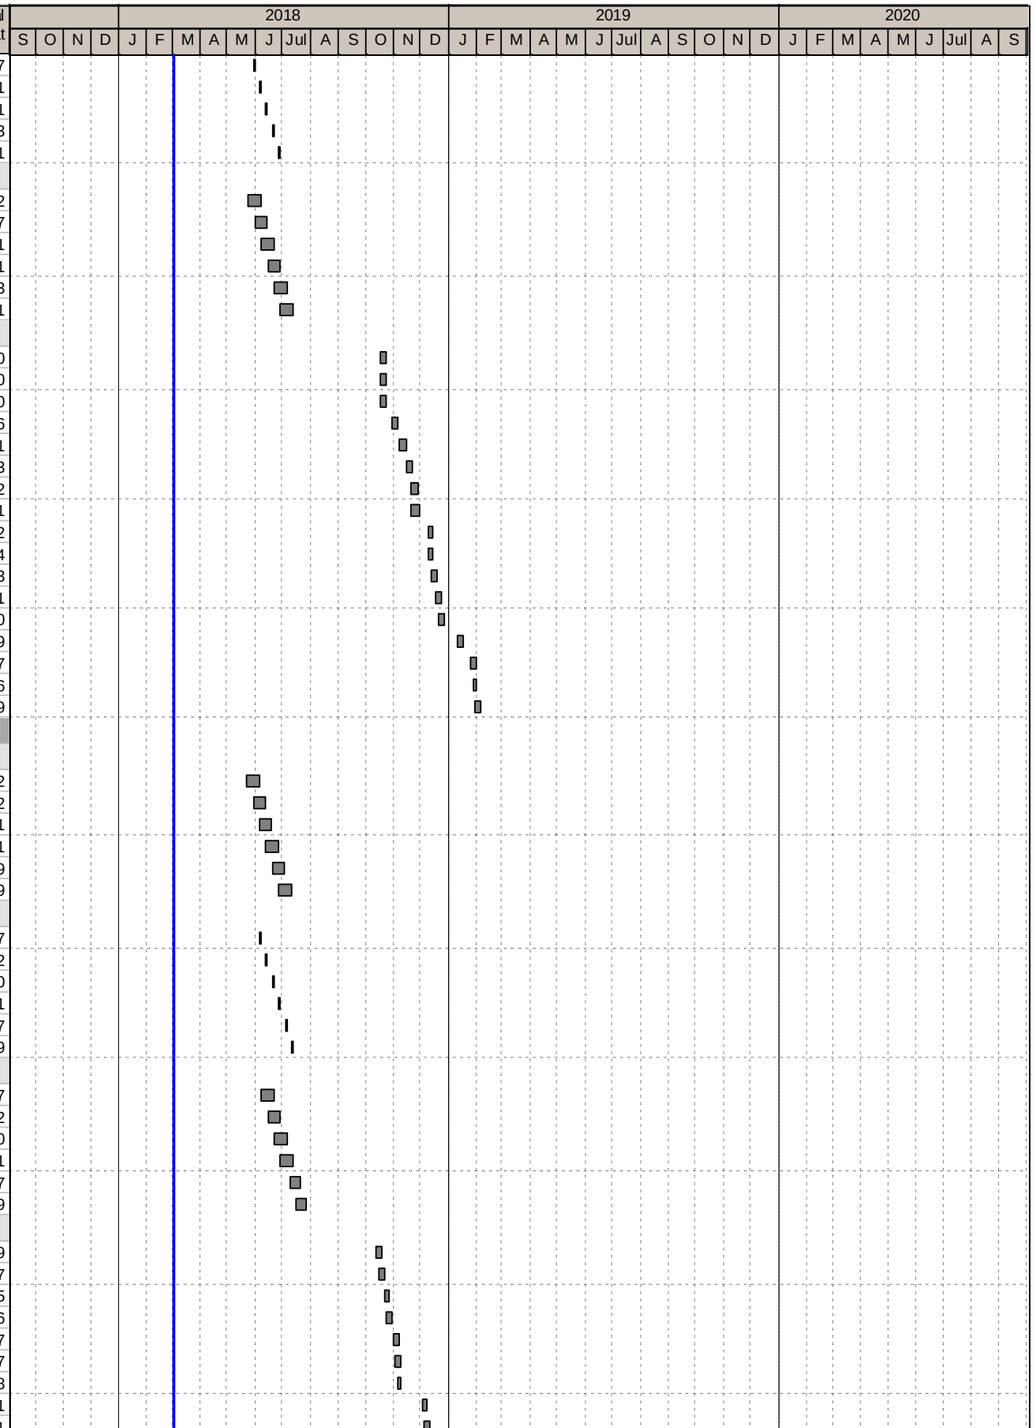

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S5B4-5P4FF	Rebar SOMD - Fabricate - Upper Suite B4	5	10-Dec-18	14-Dec-18	20
S5B5-5P4FF	Rebar SOMD - Fabricate - Upper Suite B5	5	12-Dec-18	18-Dec-18	20
S5E1-5P4FF	Rebar SOMD - Fabricate - Upper Suite E1	5	20-Dec-18	27-Dec-18	2
S5E2-5P4FF	Rebar SOMD - Fabricate - Upper Suite E2	5	27-Dec-18	03-Jan-19	0
S5E3-5P4FF	Rebar SOMD - Fabricate - Upper Suite E3	5	31-Dec-18	07-Jan-19	0
S5E4-5P4FF	Rebar SOMD - Fabricate - Upper Suite E4	5	03-Jan-19	09-Jan-19	0
S5E5-5P4FF	Rebar SOMD - Fabricate - Upper Suite E5	5	07-Jan-19	11-Jan-19	0
S5D1-5P4FF	Rebar SOMD - Fabricate - Upper Suite D1	5	01-Feb-19	07-Feb-19	31
S5C1-5P4FF	Rebar SOMD - Fabricate - Upper Suite C1	5	04-Feb-19	08-Feb-19	33
S5C2-5P4FF	Rebar SOMD - Fabricate - Upper Suite C2	5	11-Feb-19	15-Feb-19	30
S5C3-5P4FF	Rebar SOMD - Fabricate - Upper Suite C3	5	22-Feb-19	28-Feb-19	82
S5D2-5P4FF	Rebar SOMD - Fabricate - Upper Suite D2	5	22-Feb-19	28-Feb-19	19
250 Mid Bowl Mezz Level					
Submit					
S6B1-8P4FS	Rebar SOMD - Subcontractor Develop/Submit Shop Drawings - Mid Bowl Mezzanine B	10	13-Jun-18	26-Jun-18	120
S6E1-8P4FS	Rebar SOMD - Subcontractor Develop/Submit Shop Drawings - Mid Bowl Mezzanine E	10	20-Jun-18	03-Jul-18	122
S6C1-8P4FS	Rebar SOMD - Subcontractor Develop/Submit Shop Drawings - Mid Bowl Mezzanine C	10	27-Jun-18	11-Jul-18	157
S6D1-8P4FS	Rebar SOMD - Subcontractor Develop/Submit Shop Drawings - Mid Bowl Mezzanine D	10	05-Jul-18	18-Jul-18	157
Mortenson Review					
S6B1-8P4FR	Rebar SOMD - MMCJV Review Shop Drawings - Mid Bowl Mezzanine B	2	27-Jun-18	28-Jun-18	120
S6E1-8P4FR	Rebar SOMD - MMCJV Review Shop Drawings - Mid Bowl Mezzanine E	2	05-Jul-18	06-Jul-18	122
S6C1-8P4FR	Rebar SOMD - MMCJV Review Shop Drawings - Mid Bowl Mezzanine C	2	12-Jul-18	13-Jul-18	163
S6D1-8P4FR	Rebar SOMD - MMCJV Review Shop Drawings - Mid Bowl Mezzanine D	2	19-Jul-18	20-Jul-18	157
Approve					
S6B1-8P4FA	Rebar SOMD - Design Team Review/Approve Shop Drawings - Mid Bowl Mezzanine B	10	29-Jun-18	13-Jul-18	120
S6E1-8P4FA	Rebar SOMD - Design Team Review/Approve Shop Drawings - Mid Bowl Mezzanine E	10	09-Jul-18	20-Jul-18	122
S6C1-8P4FA	Rebar SOMD - Design Team Review/Approve Shop Drawings - Mid Bowl Mezzanine C	10	16-Jul-18	27-Jul-18	163
S6D1-8P4FA	Rebar SOMD - Design Team Review/Approve Shop Drawings - Mid Bowl Mezzanine D	10	23-Jul-18	03-Aug-18	157
Fabricate					
S6B1-5P4FF	Rebar SOMD - Fabricate - Mid Bowl Mezzanine B1	5	02-Nov-18	08-Nov-18	42
S6B2-5P4FF	Rebar SOMD - Fabricate - Mid Bowl Mezzanine B2	5	10-Dec-18	14-Dec-18	27
S6E1-5P4FF	Rebar SOMD - Fabricate - Mid Bowl Mezzanine E1	5	20-Dec-18	27-Dec-18	18
S6E2-5P4FF	Rebar SOMD - Fabricate - Mid Bowl Mezzanine E2	5	10-Jan-19	16-Jan-19	13
S6D1-5P4FF	Rebar SOMD - Fabricate - Mid Bowl Mezzanine D1	5	01-Feb-19	07-Feb-19	34
S6C1-5P4FF	Rebar SOMD - Fabricate - Mid Bowl Mezzanine C1	5	04-Feb-19	08-Feb-19	34
S6D2-5P4FF	Rebar SOMD - Fabricate - Mid Bowl Mezzanine D2	5	22-Feb-19	28-Feb-19	22
300 Upper Concourse					
Submit					
S7A1-8P4FS	Rebar SOMD - Subcontractor Develop/Submit Shop Drawings - Upper Concourse A	10	27-Jun-18	11-Jul-18	89
S7FS-8P4FS	Rebar SOMD - Subcontractor Develop/Submit Shop Drawings - Upper Concourse F	10	05-Jul-18	18-Jul-18	90
S7B1-8P4FS	Rebar SOMD - Subcontractor Develop/Submit Shop Drawings - Upper Concourse B	10	12-Jul-18	25-Jul-18	90
S7E1-8P4FS	Rebar SOMD - Subcontractor Develop/Submit Shop Drawings - Upper Concourse E	10	19-Jul-18	01-Aug-18	103
S7C1-8P4FS	Rebar SOMD - Subcontractor Develop/Submit Shop Drawings - Upper Concourse C	10	26-Jul-18	08-Aug-18	135
S7D1-8P4FS	Rebar SOMD - Subcontractor Develop/Submit Shop Drawings - Upper Concourse D	10	02-Aug-18	15-Aug-18	135
Mortenson Review					
S7A1-8P4FR	Rebar SOMD - MMCJV Review Shop Drawings - Upper Concourse A	2	12-Jul-18	13-Jul-18	89
S7FS-8P4FR	Rebar SOMD - MMCJV Review Shop Drawings - Upper Concourse F	2	19-Jul-18	20-Jul-18	107
S7B1-8P4FR	Rebar SOMD - MMCJV Review Shop Drawings - Upper Concourse B	2	26-Jul-18	27-Jul-18	90
S7E1-8P4FR	Rebar SOMD - MMCJV Review Shop Drawings - Upper Concourse E	2	02-Aug-18	03-Aug-18	103
S7C1-8P4FR	Rebar SOMD - MMCJV Review Shop Drawings - Upper Concourse C	2	09-Aug-18	10-Aug-18	140
S7D1-8P4FR	Rebar SOMD - MMCJV Review Shop Drawings - Upper Concourse D	2	16-Aug-18	17-Aug-18	135
Approve					
S7A1-8P4FA	Rebar SOMD - Design Team Review/Approve Shop Drawings - Upper Concourse A	10	16-Jul-18	27-Jul-18	89
S7FS-8P4FA	Rebar SOMD - Design Team Review/Approve Shop Drawings - Upper Concourse F	10	23-Jul-18	03-Aug-18	107
S7B1-8P4FA	Rebar SOMD - Design Team Review/Approve Shop Drawings - Upper Concourse B	10	30-Jul-18	10-Aug-18	90
S7E1-8P4FA	Rebar SOMD - Design Team Review/Approve Shop Drawings - Upper Concourse E	10	06-Aug-18	17-Aug-18	103
S7C1-8P4FA	Rebar SOMD - Design Team Review/Approve Shop Drawings - Upper Concourse C	10	13-Aug-18	24-Aug-18	140
S7D1-8P4FA	Rebar SOMD - Design Team Review/Approve Shop Drawings - Upper Concourse D	10	20-Aug-18	31-Aug-18	135
Fabricate					
S7A1-5P4FF	Rebar SOMD - Fabricate - Upper Concourse A1	5	29-Oct-18	02-Nov-18	25
S7B1-5P4FF	Rebar SOMD - Fabricate - Upper Concourse B1	5	29-Nov-18	05-Dec-18	16
S7B2-5P4FF	Rebar SOMD - Fabricate - Upper Concourse B2	5	03-Dec-18	07-Dec-18	16

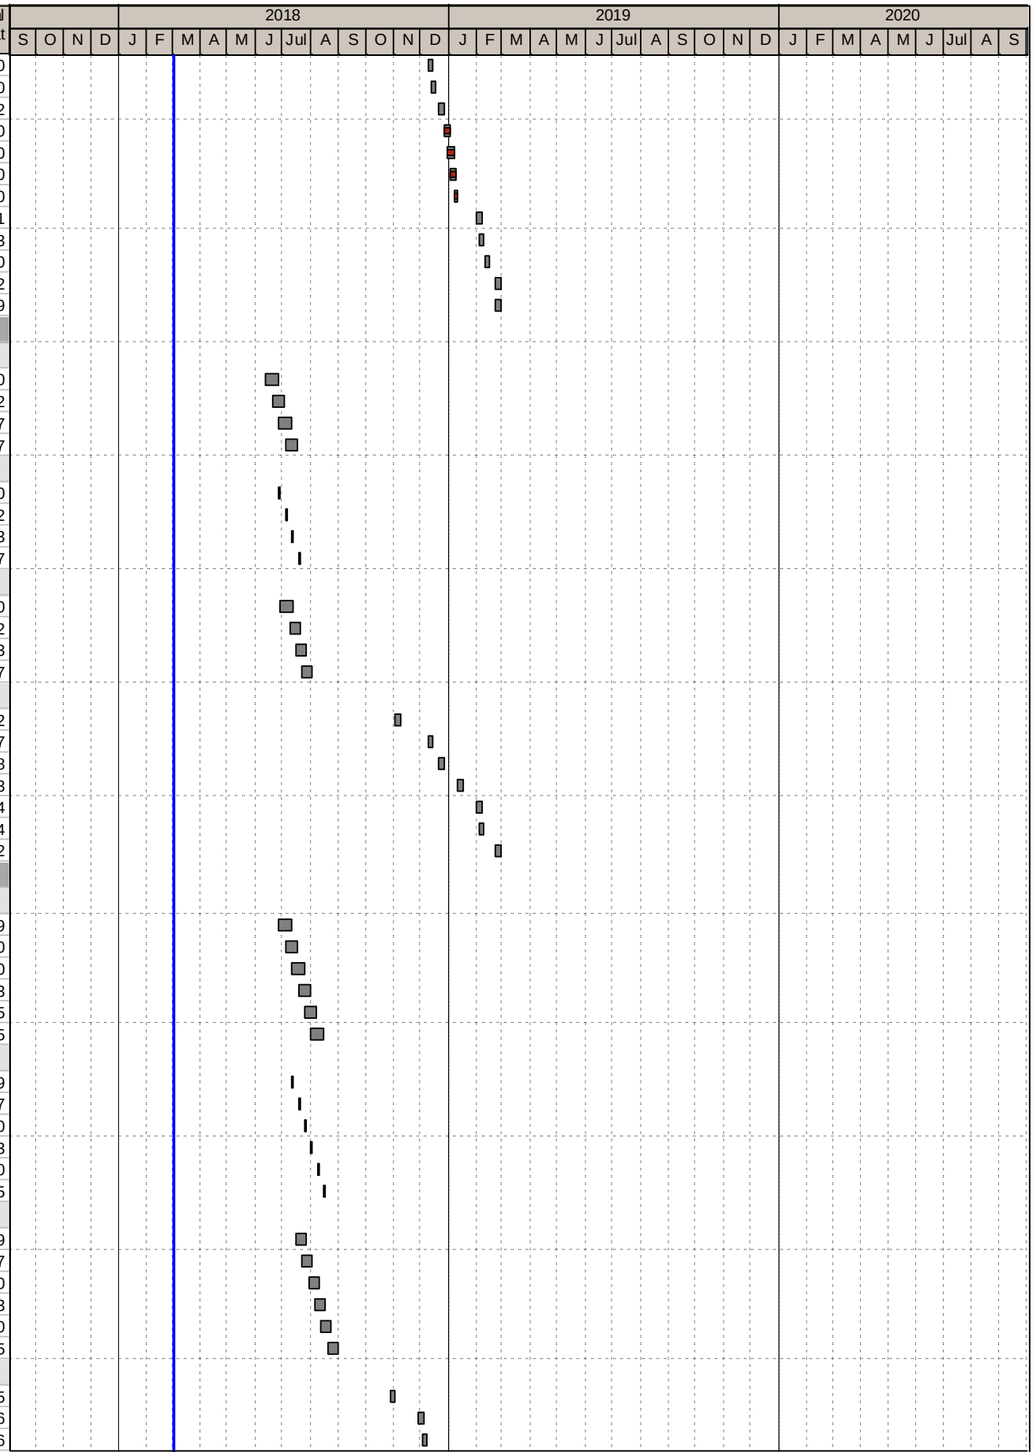

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S7F1-5P4FF	Rebar SOMD - Fabricate - Upper Concourse F1	5	06-Dec-18	12-Dec-18	23
S7B3-5P4FF	Rebar SOMD - Fabricate - Upper Concourse B3	5	08-Jan-19	14-Jan-19	3
S7E1-5P4FF	Rebar SOMD - Fabricate - Upper Concourse E1	5	10-Jan-19	16-Jan-19	6
S7B4-5P4FF	Rebar SOMD - Fabricate - Upper Concourse B4	5	14-Jan-19	18-Jan-19	1
S7E2-5P4FF	Rebar SOMD - Fabricate - Upper Concourse E2	5	14-Jan-19	18-Jan-19	6
S7B5-5P4FF	Rebar SOMD - Fabricate - Upper Concourse B5	5	16-Jan-19	22-Jan-19	1
S7E3-5P4FF	Rebar SOMD - Fabricate - Upper Concourse E3	5	18-Jan-19	24-Jan-19	4
S7E4-5P4FF	Rebar SOMD - Fabricate - Upper Concourse E4	5	22-Jan-19	28-Jan-19	4
S7C1-5P4FF	Rebar SOMD - Fabricate - Upper Concourse C1	5	05-Feb-19	11-Feb-19	30
S7D1-5P4FF	Rebar SOMD - Fabricate - Upper Concourse D1	5	13-Feb-19	20-Feb-19	24
S7C2-5P4FF	Rebar SOMD - Fabricate - Upper Concourse C2	5	11-Mar-19	15-Mar-19	9
S7D2-5P4FF	Rebar SOMD - Fabricate - Upper Concourse D2	5	11-Mar-19	15-Mar-19	9
S7C3-5P4FF	Rebar SOMD - Fabricate - Upper Concourse C3	5	13-Mar-19	19-Mar-19	11
S7D3-5P4FF	Rebar SOMD - Fabricate - Upper Concourse D3	5	13-Mar-19	19-Mar-19	11
400 Press Level					
Submit					
S9A1-8P4FS	Rebar SOMD - Subcontractor Develop/Submit Shop Drawings - Upper Mezzanine A	10	12-Jul-18	25-Jul-18	75
S9FS-8P4FS	Rebar SOMD - Subcontractor Develop/Submit Shop Drawings - Upper Mezzanine F	10	19-Jul-18	01-Aug-18	75
S9C1-8P4FS	Rebar SOMD - Subcontractor Develop/Submit Shop Drawings - Upper Mezzanine C	10	26-Jul-18	08-Aug-18	75
S9D1-8P4FS	Rebar SOMD - Subcontractor Develop/Submit Shop Drawings - Upper Mezzanine D	10	02-Aug-18	15-Aug-18	75
Mortenson Review					
S9A1-8P4FR	Rebar SOMD - MMCJV Review Shop Drawings - Upper Mezzanine A	2	26-Jul-18	27-Jul-18	94
S9FS-8P4FR	Rebar SOMD - MMCJV Review Shop Drawings - Upper Mezzanine F	2	02-Aug-18	03-Aug-18	97
S9C1-8P4FR	Rebar SOMD - MMCJV Review Shop Drawings - Upper Mezzanine C	2	09-Aug-18	10-Aug-18	147
S9D1-8P4FR	Rebar SOMD - MMCJV Review Shop Drawings - Upper Mezzanine D	2	16-Aug-18	17-Aug-18	142
Approve					
S9A1-8P4FA	Rebar SOMD - Design Team Review/Approve Shop Drawings - Upper Mezzanine A	10	30-Jul-18	10-Aug-18	94
S9FS-8P4FA	Rebar SOMD - Design Team Review/Approve Shop Drawings - Upper Mezzanine F	10	06-Aug-18	17-Aug-18	97
S9C1-8P4FA	Rebar SOMD - Design Team Review/Approve Shop Drawings - Upper Mezzanine C	10	13-Aug-18	24-Aug-18	147
S9D1-8P4FA	Rebar SOMD - Design Team Review/Approve Shop Drawings - Upper Mezzanine D	10	20-Aug-18	31-Aug-18	142
Fabricate					
S9A1-5P4FF	Rebar SOMD - Fabricate - Upper Mezzanine A1	5	21-Nov-18	29-Nov-18	24
S9F1-5P4FF	Rebar SOMD - Fabricate - Upper Mezzanine F1	5	06-Dec-18	12-Dec-18	23
S9C1-5P4FF	Rebar SOMD - Fabricate - Upper Mezzanine C1	5	28-Feb-19	06-Mar-19	21
S9D1-5P4FF	Rebar SOMD - Fabricate - Upper Mezzanine D1	5	05-Mar-19	11-Mar-19	18
350/400 Upper Stadia Support & Press Lvl					
Submit					
S95A1-8P4FS	Rebar SOMD - Subcontractor Develop/Submit Shop Drawings - Press A	10	09-Aug-18	22-Aug-18	75
S95FS-8P4FS	Rebar SOMD - Subcontractor Develop/Submit Shop Drawings - Press F	10	16-Aug-18	29-Aug-18	80
S95E1-8P4FS	Rebar SOMD - Subcontractor Develop/Submit Shop Drawings - Press E	10	23-Aug-18	06-Sep-18	80
Mortenson Review					
S95A1-8P4FR	Rebar SOMD - MMCJV Review Shop Drawings - Press A	2	23-Aug-18	24-Aug-18	75
S95FS-8P4FR	Rebar SOMD - MMCJV Review Shop Drawings - Press F	2	30-Aug-18	31-Aug-18	80
S95E1-8P4FR	Rebar SOMD - MMCJV Review Shop Drawings - Press E	2	07-Sep-18	10-Sep-18	80
Approve					
S95A1-8P4FA	Rebar SOMD - Design Team Review/Approve Shop Drawings - Press A	10	27-Aug-18	10-Sep-18	75
S95FS-8P4FA	Rebar SOMD - Design Team Review/Approve Shop Drawings - Press F	10	04-Sep-18	17-Sep-18	80
S95E1-8P4FA	Rebar SOMD - Design Team Review/Approve Shop Drawings - Press E	10	11-Sep-18	24-Sep-18	80
Fabricate					
S95A1-5P4FF	Rebar SOMD - Fabricate - Press A1	5	21-Nov-18	29-Nov-18	25
S95F1-5P4FF	Rebar SOMD - Fabricate - Press F1	5	11-Dec-18	17-Dec-18	23
S95E1-5P4FF	Rebar SOMD - Fabricate - Press E1	5	11-Jan-19	17-Jan-19	7
S95E2-5P4FF	Rebar SOMD - Fabricate - Press E2	5	17-Jan-19	23-Jan-19	6
Misc. Structural Supports					
200 Upper Suite Level					
Submit					
S510-5P4JS	Fixed Panel Operable Window - Develop/Submit Shop Dwgs - Upper Suite Grids 16 to 17	25	17-Aug-18	21-Sep-18	14
S520-5P4JS	Fixed Panel Operable Window - Develop/Submit Shop Dwgs - Upper Suite Grids 10 to 11	25	24-Aug-18	28-Sep-18	14
Mortenson Review					
S510-5P4JR	Fixed Panel Operable Window - MMCJV Review Shop Dwgs - Upper Suite Grids 16 to 17	2	24-Sep-18	25-Sep-18	14
S520-5P4JR	Fixed Panel Operable Window - MMCJV Review Shop Dwgs - Upper Suite Grids 10 to 11	2	01-Oct-18	02-Oct-18	14

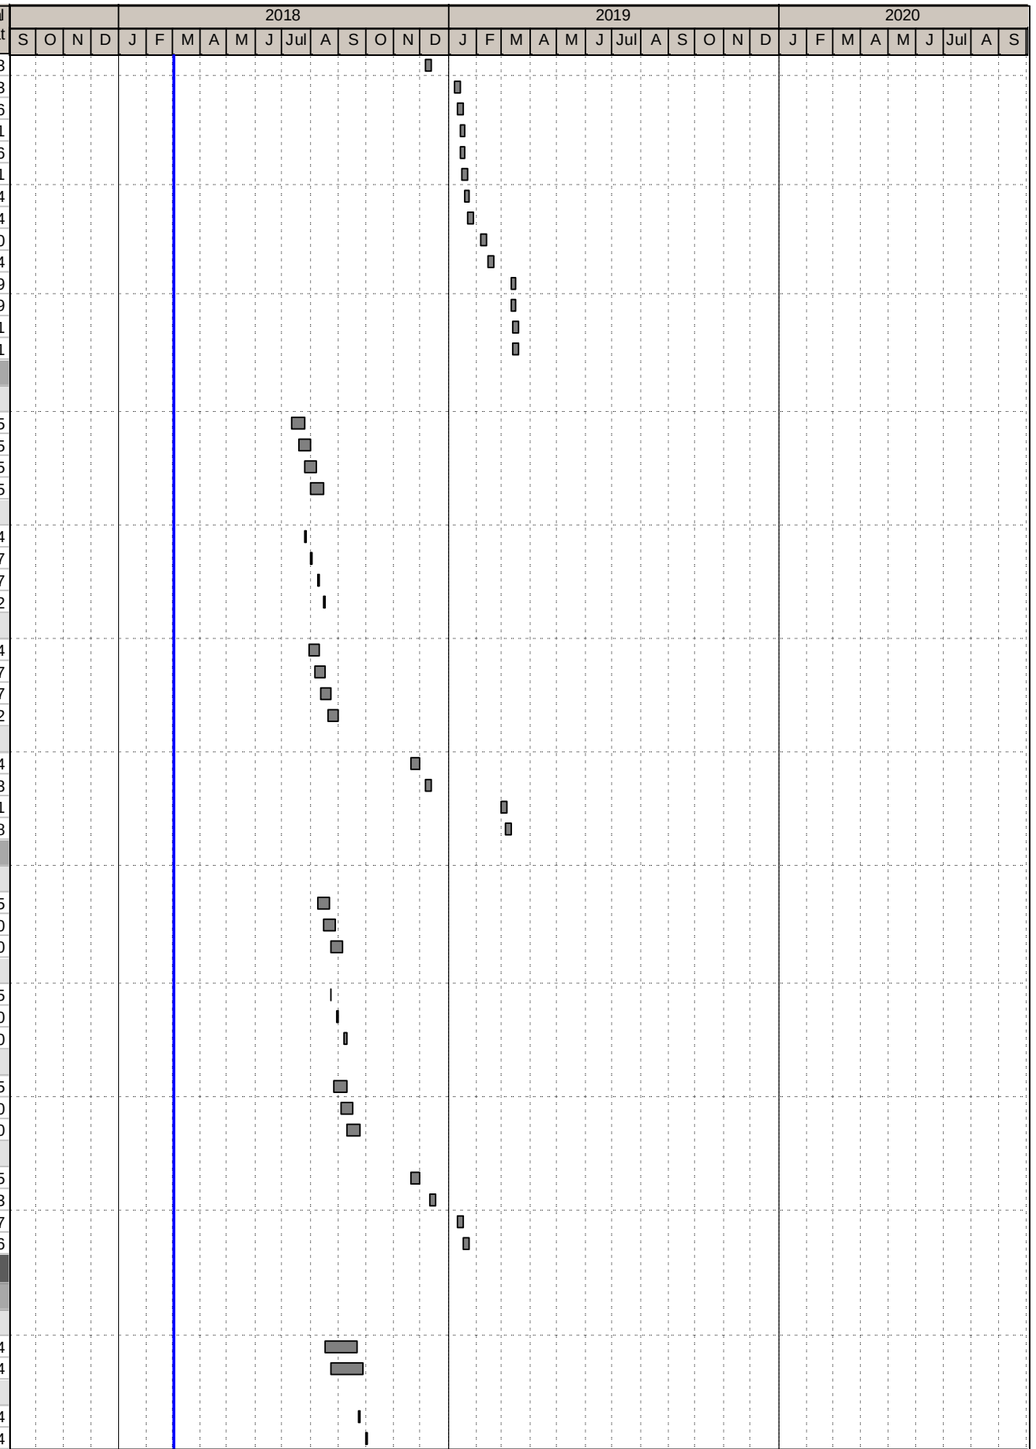

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
Approve					
S510-5P4JA	Fixed Panel Operable Window - Design Team Review/Approve Shop Dwgs - Upper Suite Grids 16 to 17	10	26-Sep-18	09-Oct-18	14
S520-5P4JA	Fixed Panel Operable Window - Design Team Review/Approve Shop Dwgs - Upper Suite Grids 10 to 11	10	03-Oct-18	16-Oct-18	14
S510-5P4J0	Fixed Panel Operable Window - Scrub/Prepare Shop Dwgs - Upper Suite Grids 16 to 17	5	10-Oct-18	16-Oct-18	14
S520-5P4J0	Fixed Panel Operable Window - Scrub/Prepare Shop Dwgs - Upper Suite Grids 10 to 11	5	17-Oct-18	23-Oct-18	14
S510-5P4JF	Fixed Panel Operable Window - Fabricate & Paint - Upper Suite Grids 16 to 17	20	17-Oct-18	14-Nov-18	14
S520-5P4JF	Fixed Panel Operable Window - Fabricate & Paint - Upper Suite Grids 10 to 11	20	24-Oct-18	21-Nov-18	14
S51A1-5P4JF1	Fixed Panel Operable Window - Deliver - Upper Suite Grids 16 to 17	3	15-Nov-18	19-Nov-18	14
S52A1-5P4JF1	Fixed Panel Operable Window - Deliver - Upper Suite Grids 10 to 11	3	26-Nov-18	28-Nov-18	14
Lower Seating Bowl Grids AA-CC					
Submit					
SS10-5P4JS	Steel Precast Bracing - Develop/Submit Shop Dwgs - Lower Bowl from AA-CC	25	08-Nov-18	17-Dec-18	176
Mortenson Review					
SS10-5P4JR	Steel Precast Bracing - MMCJV Review Shop Dwgs - Lower Bowl from AA-CC	2	18-Dec-18	19-Dec-18	176
Approve					
SS10-5P4JA	Steel Precast Bracing - Design Team Review/Approve Shop Dwgs - Lower Bowl from AA-CC	10	20-Dec-18	04-Jan-19	176
SS10-5P4J0	Steel Precast Bracing - Scrub/Prepare Shop Dwgs - Lower Bowl from AA-CC	5	07-Jan-19	11-Jan-19	176
SS10-5P4JF	Steel Precast Bracing - Fabricate & Paint - Lower Bowl from AA-CC	30	14-Jan-19	25-Feb-19	176
SS1A1-5P4JF1	Steel Precast Bracing - Deliver - Lower Bowl from AA-CC Area A1 (Seq 7080 & 7090)	3	06-Sep-19	10-Sep-19	41
SS1F1-5P4JF1	Steel Precast Bracing - Deliver - Lower Bowl from AA-CC Area F1 (Seq 7040 & 7090)	3	06-Sep-19	10-Sep-19	41
SS1E1-5P4JF1	Steel Precast Bracing - Deliver - Lower Bowl from AA-CC Area E1 (Seq 7030)	3	16-Sep-19	18-Sep-19	35
SS1B1-5P4JF1	Steel Precast Bracing - Deliver - Lower Bowl from AA-CC Area B1 (Seq 7070)	3	17-Sep-19	19-Sep-19	34
SS1E3-5P4JF1	Steel Precast Bracing - Deliver - Lower Bowl from AA-CC Area E3 (Seq 7020)	3	02-Oct-19	04-Oct-19	23
SS1B3-5P4JF1	Steel Precast Bracing - Deliver - Lower Bowl from AA-CC Area B3 (Seq 7060)	3	03-Oct-19	07-Oct-19	22
SS1D1-5P4JF1	Steel Precast Bracing - Deliver - Lower Bowl from AA-CC Area D1 (Seq 7010)	3	09-Oct-19	11-Oct-19	18
SS1C1-5P4JF1	Steel Precast Bracing - Deliver - Lower Bowl from AA-CC Area C1 (Seq 7050)	3	10-Oct-19	14-Oct-19	17
Lower Seating Bowl Grids CC-DD					
Submit					
SS40-5P4JS	Steel Precast Bracing - Develop/Submit Shop Dwgs - Lower Bowl from CC-DD	25	16-Apr-18	18-May-18	211
Mortenson Review					
SS40-5P4JR	Steel Precast Bracing - MMCJV Review Shop Dwgs - Lower Bowl from CC-DD	2	21-May-18	22-May-18	211
Approve					
SS40-5P4JA	Steel Precast Bracing - Design Team Review/Approve Shop Dwgs - Lower Bowl from CC-DD	10	23-May-18	06-Jun-18	211
SS40-5P4J0	Steel Precast Bracing - Scrub/Prepare Shop Dwgs - Lower Bowl from CC-DD	5	07-Jun-18	13-Jun-18	211
SS40-5P4JF	Steel Precast Bracing - Fabricate & Paint - Lower Bowl from CC-DD	30	14-Jun-18	26-Jul-18	211
SS4A1-5P4JF1	Steel Precast Bracing - Deliver - Lower Bowl from CC-DD Area A1 (Seq 7085 & 7095)	3	07-Sep-18	11-Sep-18	182
SS4F1-5P4JF1	Steel Precast Bracing - Deliver - Lower Bowl from CC-DD Area F1 (Seq 7045 & 7095)	3	14-Sep-18	18-Sep-18	177
SS4E1-5P4JF1	Steel Precast Bracing - Deliver - Lower Bowl from CC-DD Area E1 (Seq 7035)	3	20-Sep-18	24-Sep-18	173
SS4B1-5P4JF1	Steel Precast Bracing - Deliver - Lower Bowl from CC-DD Area B1 (Seq 7075)	3	24-Sep-18	26-Sep-18	171
SS4E3-5P4JF1	Steel Precast Bracing - Deliver - Lower Bowl from CC-DD Area E3 (Seq 7025)	3	04-Oct-18	08-Oct-18	168
SS4B3-5P4JF1	Steel Precast Bracing - Deliver - Lower Bowl from CC-DD Area B3 (Seq 7065)	3	08-Oct-18	10-Oct-18	166
SS4D1-5P4JF1	Steel Precast Bracing - Deliver - Lower Bowl from CC-DD Area D1 (Seq 7015)	3	25-Mar-19	27-Mar-19	52
SS4C1-5P4JF1	Steel Precast Bracing - Deliver - Lower Bowl from CC-DD Area C1 (Seq 7075)	3	27-Mar-19	29-Mar-19	50
Precast Structure					
Geometry Package					
S000-5P5S	Precast - Geometry Package - Subcontractor Prepare Submittal	80	04-Dec-17 A	02-Mar-18 A	
S000-5P5R	Precast - Geometry Package - MMCJV Review	2	05-Mar-18	06-Mar-18	16

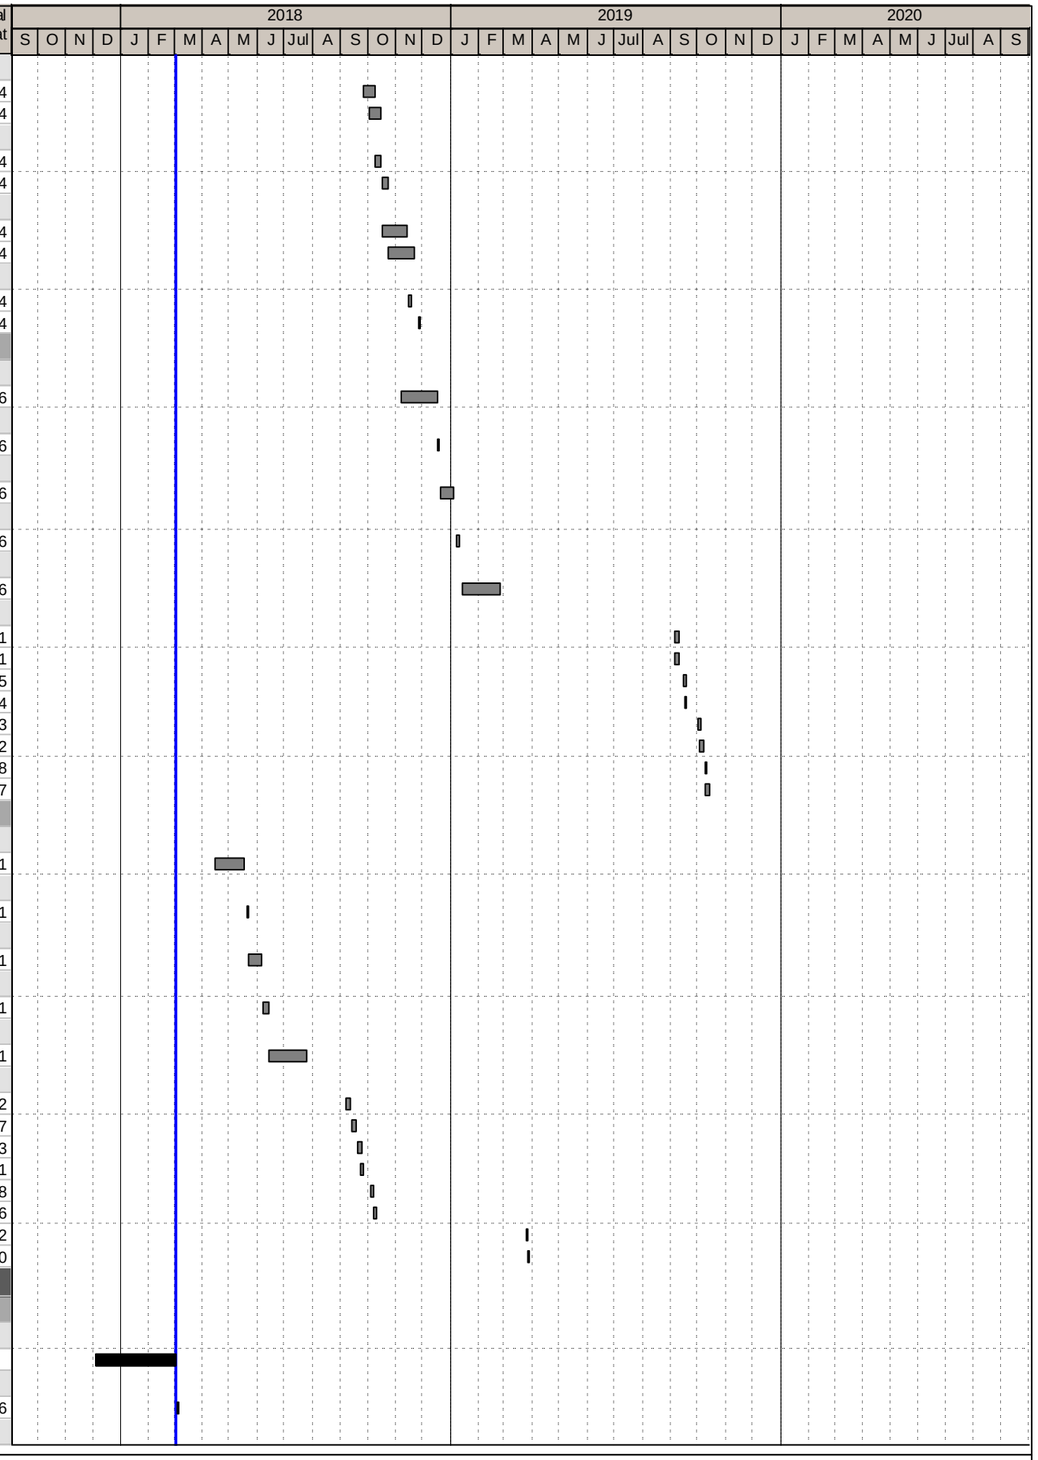

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S000-5P5A	Precast - Geometry Package - Design Team Review/Approval	10	07-Mar-18	20-Mar-18	16
S000-5P5F1	Precast - Geometry Package - Scrub Shop Drawings	2	21-Mar-18	22-Mar-18	16
S000-5P5F	Precast - Geometry Package - Procure Forms Lower Bowl CC-DD	60	23-Mar-18	15-Jun-18	16
S002-5P5F	Precast - Geometry Package - Procure Forms Upper Bowl	60	30-Mar-18	22-Jun-18	39
S001-5P5F	Precast - Geometry Package - Procure Forms Suite Level	60	06-Apr-18	29-Jun-18	68
S003-5P5F	Precast - Geometry Package - Procure Forms Lower Bowl AA-CC	60	13-Apr-18	09-Jul-18	137
Foundation Embeds					
S100-5P5S	Precast - Foundation Embeds - Subcontractor Prepare Submittal	20	02-Jan-18 A	12-Feb-18 A	
S100-5P5R	Precast - Foundation Embeds - MMCJV Review	2	13-Feb-18 A	16-Feb-18 A	
S100-5P5A	Precast - Foundation Embeds - Design Team Review/Approval	10	19-Feb-18 A	08-Mar-18	15
S100-5P5F1	Precast - Foundation Embeds - Scrub Shop Drawings	3	09-Mar-18	13-Mar-18	15
S100-5P5F	Precast - Foundation Embeds - Fabricate & Deliver Embeds/Anchor Bolts	10	14-Mar-18	27-Mar-18	15
Small Finish Mock-up					
SPC40-5P5S	Precast - Small Finish Mock-up - Subcontractor Prepare Submittal Samples	20	13-Mar-18	09-Apr-18	52
SPC40-5P5R	Precast - Small Finish Mock-up - MMCJV Review	2	10-Apr-18	11-Apr-18	52
SPC40-5P5A	Precast - Small Finish Mock-up - Design Team Review/Approval	10	12-Apr-18	25-Apr-18	52
Riser Mock-up					
SPC50-5P5S	Precast - Riser Mock-up - Subcontractor Cast First 2 Risers	2	18-Jun-18	19-Jun-18	16
SPC50-5P5R	Precast - Riser Mock-up - MMCJV Review	2	20-Jun-18	21-Jun-18	16
SPC50-5P5A	Precast - Riser Mock-up - Design Team Review/Approval	2	20-Jun-18	21-Jun-18	16
Lower Bowl Area AA-CC Precast Submittals					
SPC6A-5P5S	Precast - Subcontractor Prepare Shop Drawings - Lower Bowl AA-CC	40	30-Jul-18	24-Sep-18	46
SPC6A-5P5R	Precast - MMCJV Review - Lower Bowl AA-CC	2	25-Sep-18	26-Sep-18	46
SPC6A-5P5A	Precast - Design Team Review/Approval - Lower Bowl AA-CC	10	27-Sep-18	10-Oct-18	46
Lower Bowl Area AA-CC Deferred Precast Submittal					
SPC60-5P5S	Precast - Subcontractor Finalize & Submit Deferred Submittal - Lower Bowl AA-CC	5	11-Oct-18	17-Oct-18	46
SPC60-5P5A	Precast - Clark County Deferred Submittal Review/Approval - Lower Bowl AA-CC	20	18-Oct-18	14-Nov-18	46
SPC6A-5P5F	Precast - Fabricate & Deliver - Lower Bowl AA-CC	176	15-Nov-18	26-Jul-19	46
Lower Bowl Areas CC-DD Precast Submittals					
SPC7A-5P5S	Precast - Subcontractor Prepare Shop Drawings - Lower Bowl CC-DD Areas AFBE	17	13-Mar-18	04-Apr-18	18
SPC71-5P5S	Precast - Subcontractor Prepare Shop Drawings - Lower Bowl CC-DD Areas C & D	17	13-Mar-18	04-Apr-18	203
SPC7A-5P5R	Precast - MMCJV Review - Lower Bowl Areas CC-DD Areas AFBE	2	05-Apr-18	06-Apr-18	30
SPC71-5P5R	Precast - MMCJV Review - Lower Bowl Areas CC-DD Areas C & D	2	05-Apr-18	06-Apr-18	203
SPC7A-5P5A	Precast - Design Team Review/Approval - Lower Bowl Areas CC-DD Areas AFBE	10	09-Apr-18	20-Apr-18	30
SPC71-5P5A	Precast - Design Team Review/Approval - Lower Bowl Areas CC-DD Areas C & D	10	09-Apr-18	20-Apr-18	203
Lower Bowl Areas CC-DD Deferred Precast Submittal					

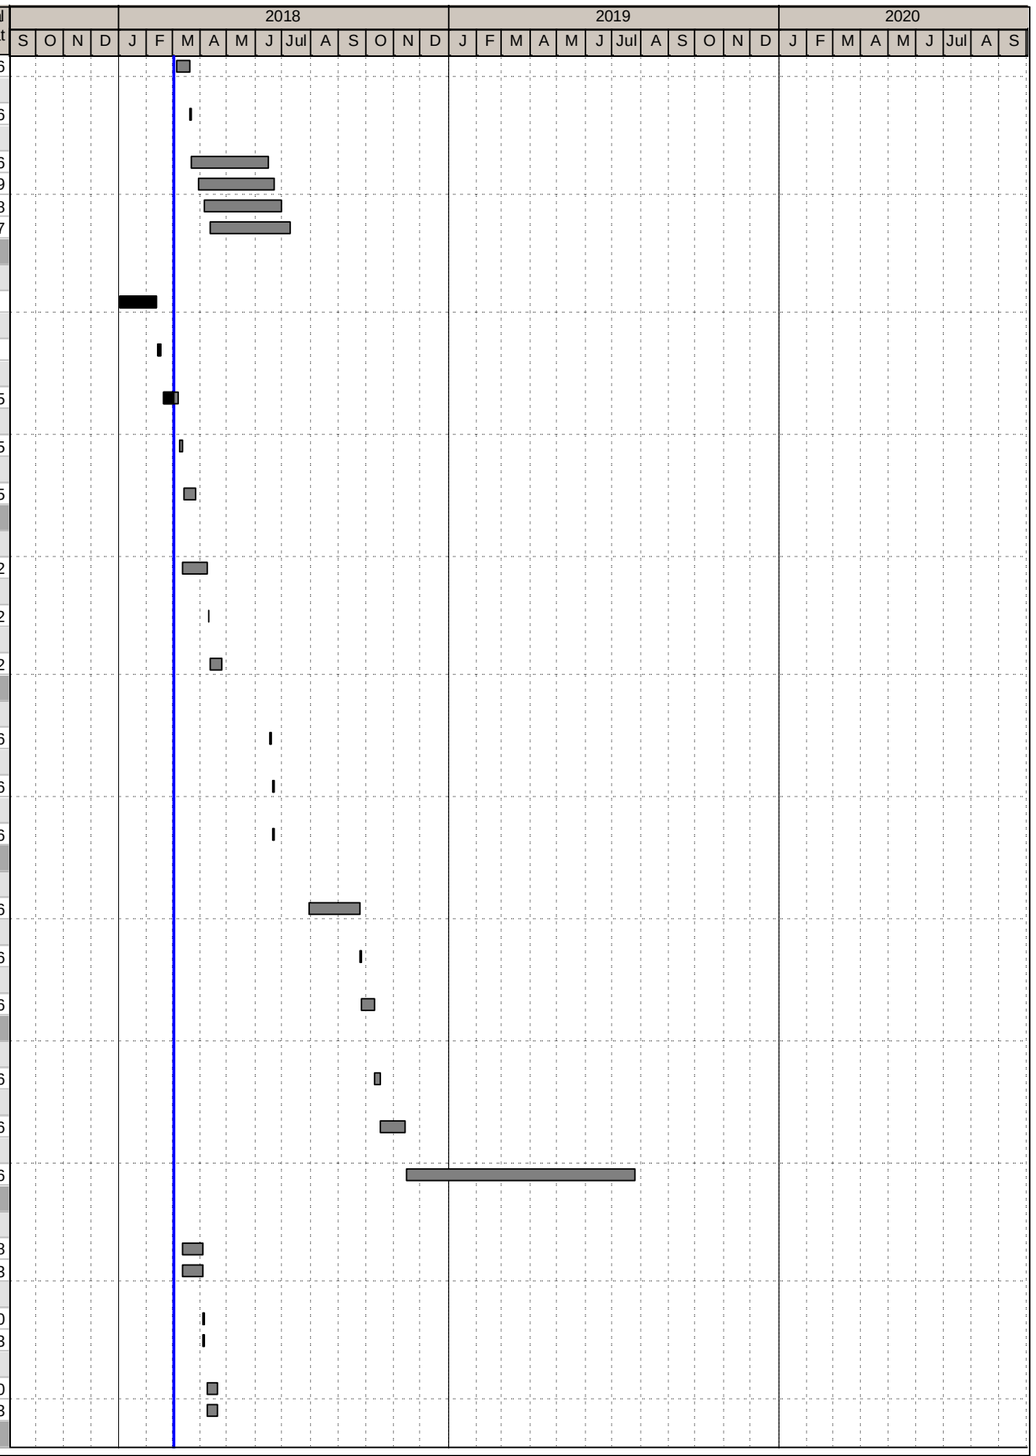

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
SPC70-5P5S	Precast - Subcontractor Finalize & Submit Deferred Submittal - Lower Bowl CC-DD Areas AFBE	5	23-Apr-18	27-Apr-18	30
SPC73-5P5S	Precast - Subcontractor Finalize & Submit Deferred Submittal - Lower Bowl CC-DD Areas C & D	5	23-Apr-18	27-Apr-18	203
SPC70-5P5A	Precast - Clark County Deferred Submittal Review/Approval - Lower Bowl CC-DD Areas AFBE	20	30-Apr-18	25-May-18	30
SPC73-5P5A	Precast - Clark County Deferred Submittal Review/Approval - Lower Bowl CC-DD Areas C & D	20	30-Apr-18	25-May-18	203
SPC7A-5P5F	Precast - Fabricate & Deliver - Lower Bowl CC-DD Area AFBE	44	22-Jun-18	23-Aug-18	16
SPC7C-5P5F	Precast - Fabricate & Deliver - Lower Bowl CC-DD Area C & D	10	24-Aug-18	07-Sep-18	141
Suite Level Precast Submittals					
SPC8A-5P5S	Precast - Subcontractor Prepare Shop Drawings - Suite Level GA Seating	15	01-Jun-18	21-Jun-18	37
SPC8B-5P5S	Precast - Subcontractor Prepare Shop Drawings - Suite Level Boxes	25	22-Jun-18	27-Jul-18	46
SPC8A-5P5R	Precast - MMCJV Review - Suite Level GA Seating	2	22-Jun-18	25-Jun-18	37
SPC8B-5P5R	Precast - MMCJV Review - Suite Level Boxes	2	30-Jul-18	31-Jul-18	58
SPC8A-5P5A	Precast - Design Team Review/Approval - Suite Level GA Seating	10	26-Jun-18	10-Jul-18	37
SPC8B-5P5A	Precast - Design Team Review/Approval - Suite Level Boxes	10	01-Aug-18	14-Aug-18	58
Suite Level Deferred Precast Submittal					
SPC80-5P5S	Precast - Subcontractor Finalize & Submit Deferred Submittal - Suite Level GA Seating	5	11-Jul-18	17-Jul-18	37
SPC81-5P5S	Precast - Subcontractor Finalize & Submit Deferred Submittal - Suite Level Boxes	5	15-Aug-18	21-Aug-18	58
SPC80-5P5A	Precast - Clark County Deferred Submittal Review/Approval - Suite Level GA Seating	20	18-Jul-18	14-Aug-18	37
SPC81-5P5A	Precast - Clark County Deferred Submittal Review/Approval - Suite Level Boxes	20	22-Aug-18	19-Sep-18	58
SPC8A-5P5F	Precast - Fabricate & Deliver - Suite Level	86	15-Aug-18	17-Dec-18	37
Upper Bowl Precast Submittals					
SPC9A-5P5S	Precast - Subcontractor Prepare Shop Drawings - Upper Bowl	40	05-Apr-18	31-May-18	18
SPC9A-5P5R	Precast - MMCJV Review - Upper Bowl	2	01-Jun-18	04-Jun-18	18
SPC9A-5P5A	Precast - Design Team Review/Approval - Upper Bowl	10	05-Jun-18	18-Jun-18	18
Upper Bowl Deferred Precast Submittal					
SPC90-5P5S	Precast - Subcontractor Finalize & Submit Deferred Submittal - Upper Bowl	5	19-Jun-18	25-Jun-18	18
SPC90-5P5A	Precast - Clark County Deferred Submittal Review/Approval - Upper Bowl	20	26-Jun-18	24-Jul-18	18
SPC9A-5P5F	Precast - Fabricate & Deliver - Upper Bowl	137	25-Jul-18	07-Feb-19	18
Wall Enclosure Systems					
S00-5P5P120	Submit/Approve - Cable Net Roof System	66	14-Mar-18	14-Jun-18	57
S00-5P5P190	Fabricate Cables & Connectors - Cable Net Roof System	110	15-Jun-18	19-Nov-18	57
S00-5P5P130	Transport & Deliver - Cable Net Roof System	55	20-Nov-18	08-Feb-19	57
S00-5P5P100	Submit/Approve/Procure - Operable Playing Field	298	06-Apr-18	07-Jun-19	43
Metal Wall Panels					
Metal Panel Ribbon Engineering					
S00-5Q3S410	Metal Panel Ribbon Engineering - Prepare Shop Drawings (North/East)	65	08-Oct-18	10-Jan-19	27
S00-5Q3S420	Metal Panel Ribbon Engineering - MMCJVLV Reivew Shop Dwgs (North/East)	3	11-Jan-19	15-Jan-19	27
S00-5Q3S430	Metal Panel Ribbon Engineering - Design Team Reivew and Approve Shop Dwgs (North/East)	10	16-Jan-19	29-Jan-19	27
S00-5Q3S440	Metal Panel Ribbon Engineering - Revise and Resubmit Shop Dwgs (North/East)	7	30-Jan-19	07-Feb-19	57
S00-5Q3S450	Metal Panel Ribbon Engineering - MMCJVLV Review Shop Dwgs (North/East)	3	08-Feb-19	12-Feb-19	57
S00-5Q3S460	Metal Panel Ribbon Engineering - Design Team Review and Approve Shop Dwgs (North/East)	10	13-Feb-19	26-Feb-19	57

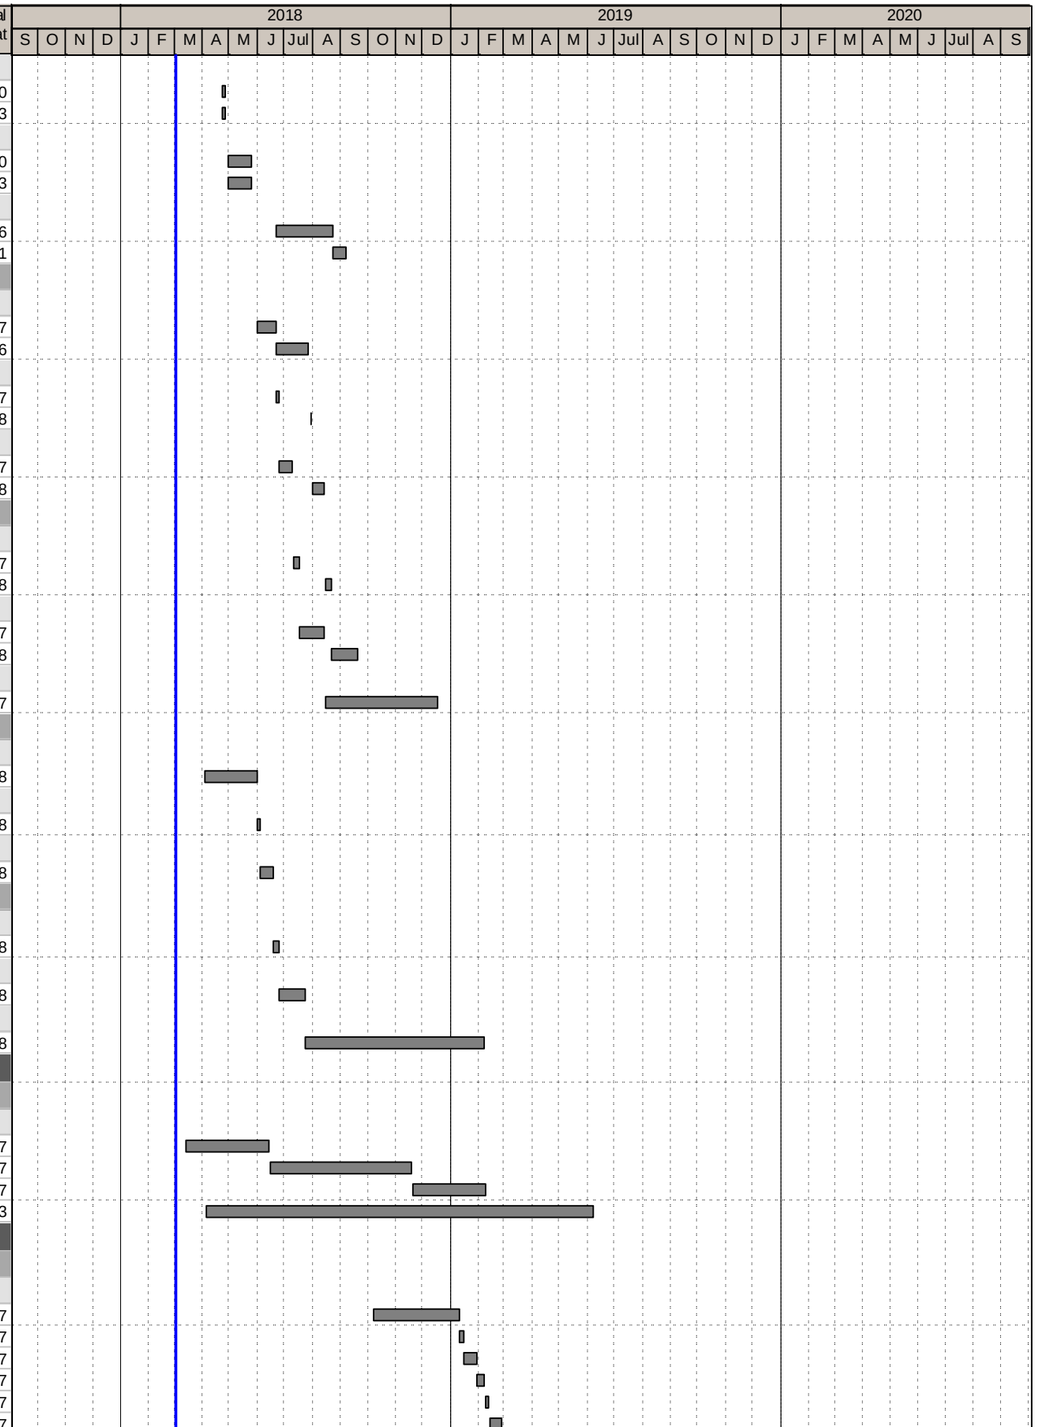

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S00-5Q3S470	Metal Panel Ribbon Engineering - Prepare Permit Package (North/East)	10	27-Feb-19	12-Mar-19	57
S00-5Q3S480	Metal Panel Ribbon Engineering - CC Approval & Permit (North/East)	30	13-Mar-19	23-Apr-19	57
S00-5Q3S490	Metal Panel Ribbon Engineering - Prepare Shop Drawings (South/West)	80	24-Dec-18	16-Apr-19	19
S00-5Q3S500	Metal Panel Ribbon Engineering - MMCJVLV Reivew Shop Dwgs (South/West)	3	17-Apr-19	19-Apr-19	19
S00-5Q3S510	Metal Panel Ribbon Engineering - Design Team Reivew and Approve Shop Dwgs (South/West)	10	22-Apr-19	03-May-19	19
S00-5Q3S550	Metal Panel Ribbon Engineering - Prepare Permit Package (South/West)	10	06-May-19	17-May-19	69
S00-5Q3S560	Metal Panel Ribbon Engineering - CC Approval & Permit (South/West)	30	20-May-19	01-Jul-19	69
Metal Panel Soffit Engineering					
S00-5Q3S650	Metal Panel Sofft Cap Engineering - Prepare Shop Dwgs	60	23-Jan-19	16-Apr-19	11
S00-5Q3S660	Metal Panel Sofft Cap Engineering - MMCJVLV Reivew Shop Dwgs	5	17-Apr-19	23-Apr-19	11
S00-5Q3S670	Metal Panel Sofft Cap Engineering - Design Team Reivew and Approve Shop Dwgs	10	24-Apr-19	07-May-19	11
S00-5Q3S710	Metal Panel Sofft Cap Engineering - Prepare CC Package	10	08-May-19	21-May-19	21
S00-5Q3S720	Metal Panel Sofft Cap Engineering - CC Deferred Submittal Review and Approval	20	22-May-19	19-Jun-19	21
Metal Panel Ribbon Production Drawings					
S00-5Q3S880	Metal Panel & Truss - Production Dwg Takeoffs (North/East)	35	30-Jan-19	19-Mar-19	27
S00-5Q3S870	Metal Panel & Truss - Production Drawings (North/East)	90	30-Jan-19	05-Jun-19	27
S00-5Q3S900	Metal Panel & Truss - Production Dwg Takeoffs (South/West)	35	06-May-19	24-Jun-19	19
S00-5Q3S890	Metal Panel & Truss - Production Drawings (South/West)	50	06-May-19	16-Jul-19	19
Metal Panel Soffit Production Drawings					
S00-5Q3S910	Metal Panel Soffit - Production Drawings	40	08-May-19	03-Jul-19	11
S00-5Q3S920	Metal Panel Soffit - Production Dwg Takeoffs	35	15-May-19	03-Jul-19	11
Metal Panel Ribbon Metal Procurement					
S00-5Q3S1830	Metal Panel Ribbon - Metal Fabrication (North/East)	70	20-Mar-19	26-Jun-19	27
S00-5Q3S1850	Metal Panel Ribbon - Metal Fabrication (South/West)	70	25-Jun-19	02-Oct-19	19
Metal Panel Ribbon Panel Procurement					
S00-5Q3S1840	Metal Panel Ribbon - Panel Fabrication (North/East)	70	20-Mar-19	26-Jun-19	27
S00-5Q3S1860	Metal Panel Ribbon - Panel Fabrication (South/West)	70	25-Jun-19	02-Oct-19	19
Metal Panel Soffit Procurement					
S00-5Q3S1900	Metal Panel Soffit - Metal Fabrication - Operable Door	80	27-Jun-19	18-Oct-19	11
S00-5Q3S1910	Metal Panel Soffit - Metal Fabrication - Operable Field	80	27-Jun-19	18-Oct-19	42
S00-5Q3S1890	Metal Panel Soffit - Metal Fabrication - Storefronts	80	05-Jul-19	25-Oct-19	37
S00-5Q3S1920	Metal Panel Soffit - Panel Fabrication - Storefronts	80	27-Jun-19	18-Oct-19	42
S00-5Q3S1930	Metal Panel Soffit - Panel Fabrication - Operable Door	80	27-Jun-19	18-Oct-19	11
S00-5Q3S1940	Metal Panel Soffit - Panel Fabrication - Operable Field	80	27-Jun-19	18-Oct-19	42
Metal Panel Ribbon Assembly					
S00-5Q3S2390	Metal Panel Ribbon - Unit Assembly (North/East)	50	27-Jun-19	06-Sep-19	27
S00-5Q3S2400	Metal Panel Ribbon - Unit Assembly (South/West)	50	19-Sep-19	27-Nov-19	19
Curtain Wall					
Material Selection Mock-up					
S00-5Q2A10	Curtainwall Material Selection Mock-up - Prepare MSMU Scope Matrix	6	04-Oct-17 A	11-Oct-17 A	
S00-5Q2A20	Curtainwall Material Selection Mock-up - Revise and Confirm MSMU Scope Matrix	15	12-Oct-17 A	01-Nov-17 A	
S00-5Q2A30	Curtainwall Material Selection Mock-up - Verbal NTP for MSMU	0	07-Nov-17 A		
S00-5Q2A40	Curtainwall Material Selection Mock-up - Prepare and Submit Mockup Dwgs	13	09-Nov-17 A	29-Nov-17 A	
S00-5Q2A50	Curtainwall Material Selection Mock-up - MMCJVLV Review Mockup Dwgs	5	30-Nov-17 A	19-Dec-17 A	
S00-5Q2A60	Curtainwall Material Selection Mock-up - Revise and Resubmit Mockup Dwgs	5	20-Dec-17 A	11-Jan-18 A	

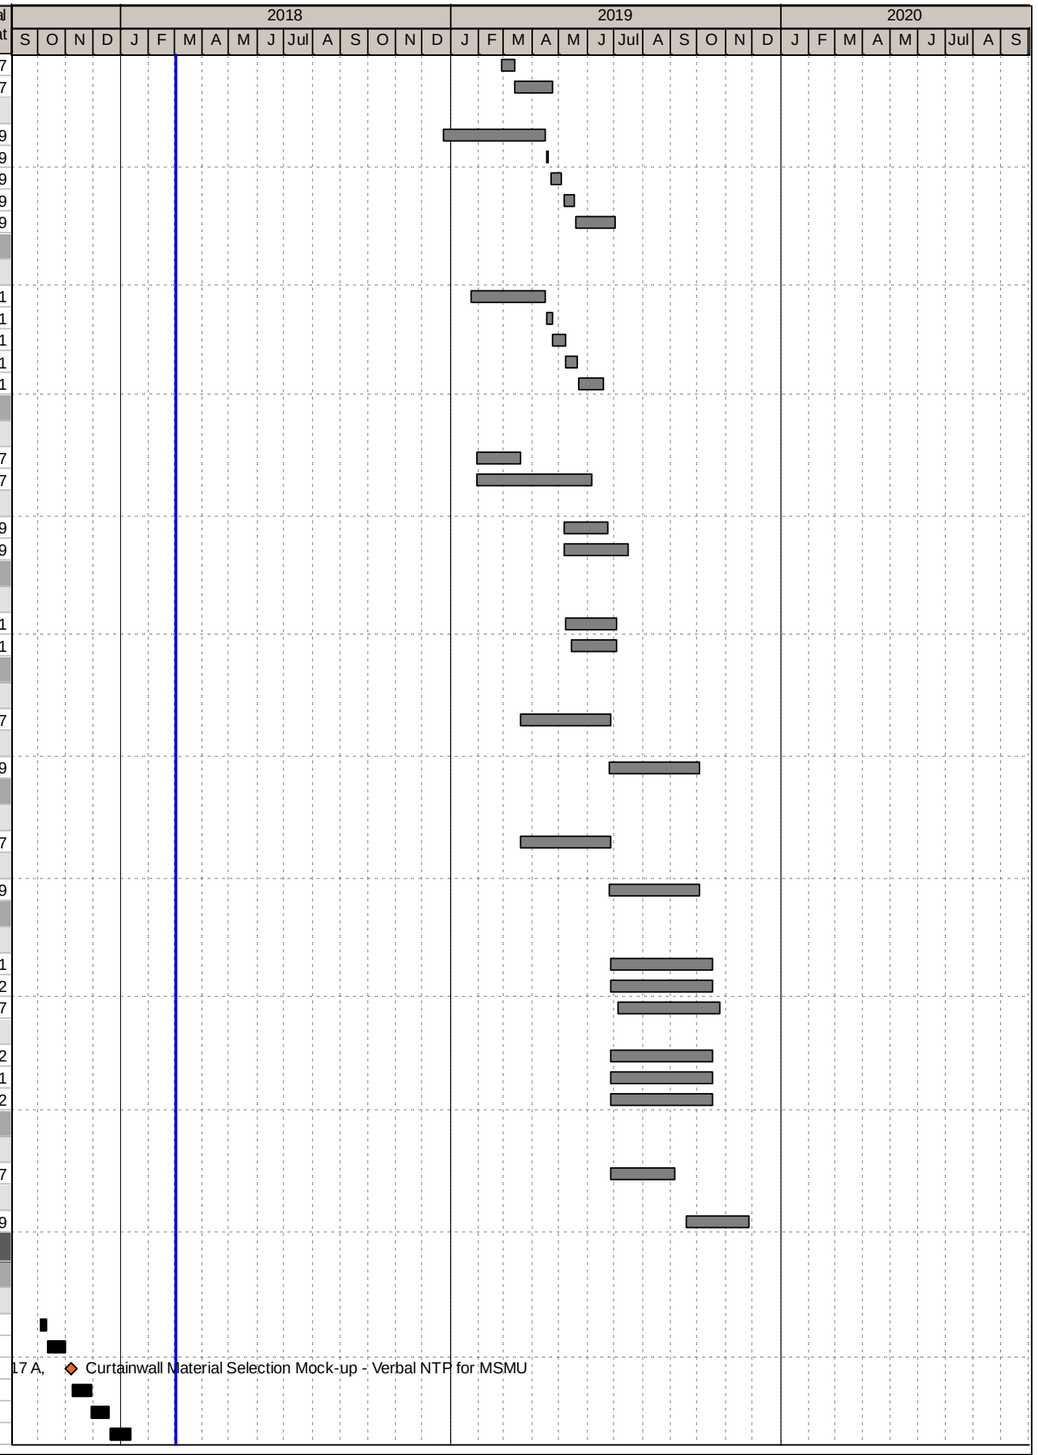

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S00-5Q2A70	Curtainwall Material Selection Mock-up - MMCJVLV Final Review Mockup Dwgs	5	12-Jan-18 A	18-Jan-18 A	
S00-5Q2A390	Curtainwall Material Selection Mock-up - Design Team Final Review and Approval Mockup Dwgs	5	15-Jan-18 A	19-Jan-18 A	
S00-5Q2A80	Curtainwall Material Selection Mock-up - Part and Unit Dwgs - MSMU	19	22-Jan-18 A	26-Jan-18 A	
S00-5Q2A90	Curtainwall Material Selection Mock-up - Procure and Fabricate MSMU Materials	30	05-Feb-18 A	16-Mar-18	67
S00-5Q2A100	Curtainwall Material Selection Mock-up - Assemble MSMU Units	5	19-Mar-18	23-Mar-18	67
S00-5Q2A110	Curtainwall Material Selection Mock-up - Erect MSMU	5	26-Mar-18	30-Mar-18	67
S00-5Q2A120	Curtainwall Material Selection Mock-up - Mockup Viewing - MSMU1	5	02-Apr-18	06-Apr-18	67
Performance Mock-up					
S00-5Q2A540	Curtainwall Performance Mockup - Prepare PMU Scope Dwgs	10	14-Nov-17 A	29-Nov-17 A	
S00-5Q2A550	Curtainwall Performance Mockup - MMCJVLV Review PMU Scope Dwgs	20	30-Nov-17 A	29-Dec-17 A	
S00-5Q2A560	Curtainwall Performance Mockup - Revise and Resubmit PMU Scope Dwgs	10	02-Jan-18 A	15-Jan-18 A	
S00-5Q2A580	Curtainwall Performance Mockup - MMCJVLV Review PMU Scope Dwgs	10	16-Jan-18 A	07-Feb-18 A	
S00-5Q2A290	Curtainwall Performance Mockup - Prepare and Submit PMU Submittal	50	08-Feb-18 A	17-Apr-18	10
S00-5Q2A300	Curtainwall Performance Mockup - MMCJVLV Review PMU Submittal	3	18-Apr-18	20-Apr-18	15
S00-5Q2A310	Curtainwall Performance Mockup - Design Team Review and Approve PMU Submittal	5	23-Apr-18	27-Apr-18	15
S00-5Q2A320	Curtainwall Performance Mockup - Revise and Resubmit PMU Submittal	10	30-Apr-18	11-May-18	15
S00-5Q2A330	Curtainwall Performance Mockup - MMCJVLV Final Review PMU Submittal	3	14-May-18	16-May-18	15
S00-5Q2A340	Curtainwall Performance Mockup - Design Team Final Review and Approval PMU Submittal	10	17-May-18	31-May-18	15
S00-5Q2A350	Curtainwall Performance Mockup - Issue Record Set of PMU Dwgs	10	01-Jun-18	14-Jun-18	15
S00-5Q2A360	Curtainwall Performance Mockup - Die Dwgs - PMU	40	01-Jun-18	27-Jul-18	15
S00-5Q2A370	Curtainwall Performance Mockup - Part and Unit Dwgs - PMU	65	01-Jun-18	31-Aug-18	26
S00-5Q2A440	Curtainwall Performance Mockup - Fabricate Dies - PMU	30	30-Jul-18	10-Sep-18	15
S00-5Q2A450	Curtainwall Performance Mockup - Extrude and Paint Metal - PMU	25	11-Sep-18	15-Oct-18	15
S00-5Q2A420	Curtainwall Performance Mockup - Procure and Fabricate Glass - PMU	40	04-Sep-18	29-Oct-18	26
S00-5Q2A460	Curtainwall Performance Mockup - Metal Fabrication - PMU	20	16-Oct-18	12-Nov-18	15
S00-5Q2A430	Curtainwall Performance Mockup - Glass Delivery - PMU	20	30-Oct-18	28-Nov-18	26
S00-5Q2A470	Curtainwall Performance Mockup - Metal Delivery - PMU	21	13-Nov-18	13-Dec-18	15
S00-5Q2A500	Curtainwall Performance Mockup - Mobilize - PMU Chamber	10	17-Dec-18	31-Dec-18	16
S00-5Q2A480	Curtainwall Performance Mockup - Shop Assembly - PMU	15	14-Dec-18	07-Jan-19	15
S00-5Q2A490	Curtainwall Performance Mockup - Shipping - PMU	1	08-Jan-19	08-Jan-19	15
S00-5Q2A510	Curtainwall Performance Mockup - Set Anchors - PMU	5	02-Jan-19	08-Jan-19	16
S00-5Q2A520	Curtainwall Performance Mockup - Installation - PMU	10	09-Jan-19	22-Jan-19	15
S00-5Q2A530	Curtainwall Performance Mockup - Test Mockup - PMU	5	23-Jan-19	29-Jan-19	15
Curtainwall & Arch Louver Engineering					
S00-5Q3S90	Curtainwall/Louver Engineering - Prepare Shop Drawings (N&E 1-5)	60	18-Apr-18	12-Jul-18	10
S00-5Q3S100	Curtainwall/Louver Engineering - MMCJVLV Reivew Shop Dwgs (N&E 1-5)	3	13-Jul-18	17-Jul-18	50
S00-5Q3S110	Curtainwall/Louver Engineering - Design Team Reivew and Approve Shop Dwgs (N&E 1-5)	10	18-Jul-18	31-Jul-18	50
S00-5Q3S120	Curtainwall/Louver Engineering - Revise and Resubmit Shop Dwgs (N&E 1-5)	10	01-Aug-18	14-Aug-18	68
S00-5Q3S130	Curtainwall/Louver Engineering - MMCJVLV Review Shop Dwgs (N&E 1-5)	2	15-Aug-18	16-Aug-18	68
S00-5Q3S140	Curtainwall/Louver Engineering - Design Team Review and Approve Shop Dwgs (N&E 1-5)	10	17-Aug-18	30-Aug-18	68
S00-5Q3S150	Curtainwall/Louver Engineering - Prepare Permit Package (N&E 1-5)	10	31-Aug-18	14-Sep-18	78
S00-5Q3S160	Curtainwall/Louver Engineering - CC Approval & Permit (N&E 1-5)	30	17-Sep-18	26-Oct-18	78
S00-5Q3S170	Curtainwall/Louver Engineering - Prepare Shop Drawings (N&E 6-9)	60	13-Jul-18	05-Oct-18	10
S00-5Q3S180	Curtainwall/Louver Engineering - MMCJVLV Reivew Shop Dwgs (N&E 6-9)	3	08-Oct-18	10-Oct-18	24
S00-5Q3S190	Curtainwall/Louver Engineering - Design Team Reivew and Approve Shop Dwgs (N&E 6-9)	10	11-Oct-18	24-Oct-18	24
S00-5Q3S230	Curtainwall/Louver Engineering - Prepare Permit Package (N&E 6-9)	10	25-Oct-18	07-Nov-18	74
S00-5Q3S240	Curtainwall/Louver Engineering - CC Approval & Permit (N&E 6-9)	30	08-Nov-18	21-Dec-18	74
S00-5Q3S250	Curtainwall/Louver Engineering - Prepare Shop Drawings (S&W 1-5)	60	08-Oct-18	03-Jan-19	10
S00-5Q3S260	Curtainwall/Louver Engineering - MMCJVLV Reivew Shop Dwgs (S&W 1-5)	3	04-Jan-19	08-Jan-19	11
S00-5Q3S270	Curtainwall/Louver Engineering - Design Team Reivew and Approve Shop Dwgs (S&W 1-5)	10	09-Jan-19	22-Jan-19	11
S00-5Q3S280	Curtainwall/Louver Engineering - Revise and Resubmit Shop Dwgs (S&W 1-5)	10	23-Jan-19	05-Feb-19	51
S00-5Q3S290	Curtainwall/Louver Engineering - MMCJVLV Review Shop Dwgs (S&W 1-5)	2	06-Feb-19	07-Feb-19	51
S00-5Q3S300	Curtainwall/Louver Engineering - Design Team Review and Approve Shop Dwgs (S&W 1-5)	10	08-Feb-19	21-Feb-19	51
S00-5Q3S310	Curtainwall/Louver Engineering - Prepare Permit Package (S&W 1-5)	10	22-Feb-19	07-Mar-19	51
S00-5Q3S320	Curtainwall/Louver Engineering - CC Approval & Permit (S&W 1-5)	30	08-Mar-19	18-Apr-19	51
S00-5Q3S330	Curtainwall/Louver Engineering - Prepare Shop Drawings (S&W 6-9)	60	04-Jan-19	28-Mar-19	10
S00-5Q3S340	Curtainwall/Louver Engineering - MMCJVLV Reivew Shop Dwgs (S&W 6-9)	3	29-Mar-19	02-Apr-19	10

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S00-5Q3S350	Curtainwall/Louver Engineering - Design Team Reivew and Approve Shop Dwgs (S&W 6-9)	10	03-Apr-19	16-Apr-19	10
S00-5Q3S390	Curtainwall/Louver Engineering - Prepare Permit Package (S&W 6-9)	10	17-Apr-19	30-Apr-19	76
S00-5Q3S400	Curtainwall/Louver Engineering - CC Approval & Permit (S&W 6-9)	30	01-May-19	12-Jun-19	76
Curtainwall Production Drawings					
S00-5Q3S760	Curtainwall - Production Dwgs Takeoffs (N&E 1-5)	60	01-Aug-18	24-Oct-18	80
S00-5Q3S750	Curtainwall - Production Drawings (N&E 1-5)	90	01-Aug-18	07-Dec-18	50
S00-5Q3S780	Curtainwall - Production Dwgs Takeoffs (N&E 6-9)	60	25-Oct-18	22-Jan-19	54
S00-5Q3S770	Curtainwall - Production Drawings (N&E 6-9)	90	25-Oct-18	05-Mar-19	24
S00-5Q3S800	Curtainwall - Production Dwgs Takeoffs (S&W 1-5)	35	23-Jan-19	12-Mar-19	46
S00-5Q3S790	Curtainwall - Production Drawings (S&W 1-5)	90	23-Jan-19	29-May-19	46
S00-5Q3S820	Curtainwall - Production Dwgs Takeoffs (S&W 6-9)	20	17-Apr-19	14-May-19	40
S00-5Q3S810	Curtainwall - Production Drawings (S&W 6-9)	90	17-Apr-19	22-Aug-19	40
Arch Louver Production Drawings					
S00-5Q3S840	Louver - Production Dwgs Takeoffs (East)	25	25-Oct-18	30-Nov-18	47
S00-5Q3S830	Louver - Production Drawings (East)	40	25-Oct-18	21-Dec-18	47
S00-5Q3S860	Louver - Production Dwgs Takeoffs (West)	25	17-Apr-19	21-May-19	10
S00-5Q3S850	Louver - Production Drawings (West)	40	17-Apr-19	12-Jun-19	10
Curtainwall Infil Procurement					
S00-5Q3S970	Curtainwall - Infill Fabrication (North Stack 1)	65	30-Jan-19	30-Apr-19	15
S00-5Q3S980	Curtainwall - Infill Fabrication (North Stack 2)	65	11-Feb-19	10-May-19	15
S00-5Q3S990	Curtainwall - Infill Fabrication (North Stack 3)	65	21-Feb-19	22-May-19	15
S00-5Q3S1000	Curtainwall - Infill Fabrication (North Stack 4)	65	05-Mar-19	04-Jun-19	15
S00-5Q3S1010	Curtainwall - Infill Fabrication (North Stack 5)	65	12-Mar-19	11-Jun-19	15
S00-5Q3S1020	Curtainwall - Infill Fabrication (North Stack 6)	65	19-Mar-19	18-Jun-19	15
S00-5Q3S1030	Curtainwall - Infill Fabrication (North Stack 7)	65	29-Mar-19	28-Jun-19	15
S00-5Q3S1040	Curtainwall - Infill Fabrication (North Stack 8)	65	10-Apr-19	11-Jul-19	15
S00-5Q3S1050	Curtainwall - Infill Fabrication (North Stack 9)	65	22-Apr-19	23-Jul-19	15
S00-5Q3S1060	Curtainwall - Infill Fabrication (East Stack 1)	65	30-Jan-19	30-Apr-19	15
S00-5Q3S1070	Curtainwall - Infill Fabrication (East Stack 2)	65	08-Feb-19	09-May-19	15
S00-5Q3S1080	Curtainwall - Infill Fabrication (East Stack 3)	65	19-Feb-19	20-May-19	15
S00-5Q3S1090	Curtainwall - Infill Fabrication (East Stack 4)	65	28-Feb-19	30-May-19	15
S00-5Q3S1100	Curtainwall - Infill Fabrication (East Stack 5)	65	11-Mar-19	10-Jun-19	15
S00-5Q3S1110	Curtainwall - Infill Fabrication (East Stack 6)	65	20-Mar-19	19-Jun-19	15
S00-5Q3S1120	Curtainwall - Infill Fabrication (East Stack 7)	65	29-Mar-19	28-Jun-19	15
S00-5Q3S1130	Curtainwall - Infill Fabrication (East Stack 8)	65	09-Apr-19	10-Jul-19	15
S00-5Q3S1140	Curtainwall - Infill Fabrication (East Stack 9)	65	18-Apr-19	19-Jul-19	15
S00-5Q3S1150	Curtainwall - Infill Fabrication (South Stack 1)	65	13-Mar-19	12-Jun-19	46
S00-5Q3S1160	Curtainwall - Infill Fabrication (South Stack 2)	65	25-Mar-19	24-Jun-19	46
S00-5Q3S1170	Curtainwall - Infill Fabrication (South Stack 3)	65	04-Apr-19	05-Jul-19	46
S00-5Q3S1180	Curtainwall - Infill Fabrication (South Stack 4)	65	16-Apr-19	17-Jul-19	46
S00-5Q3S1190	Curtainwall - Infill Fabrication (South Stack 5)	65	26-Apr-19	29-Jul-19	46
S00-5Q3S1200	Curtainwall - Infill Fabrication (South Stack 6)	65	15-May-19	15-Aug-19	41
S00-5Q3S1210	Curtainwall - Infill Fabrication (South Stack 7)	65	28-May-19	27-Aug-19	41
S00-5Q3S1220	Curtainwall - Infill Fabrication (South Stack 8)	65	07-Jun-19	09-Sep-19	42
S00-5Q3S1230	Curtainwall - Infill Fabrication (South Stack 9)	65	19-Jun-19	19-Sep-19	47
S00-5Q3S1240	Curtainwall - Infill Fabrication (West Stack 1)	65	13-Mar-19	12-Jun-19	50
S00-5Q3S1250	Curtainwall - Infill Fabrication (West Stack 2)	65	22-Mar-19	21-Jun-19	50
S00-5Q3S1260	Curtainwall - Infill Fabrication (West Stack 3)	65	02-Apr-19	02-Jul-19	50
S00-5Q3S1270	Curtainwall - Infill Fabrication (West Stack 4)	65	11-Apr-19	12-Jul-19	50
S00-5Q3S1280	Curtainwall - Infill Fabrication (West Stack 5)	65	22-Apr-19	23-Jul-19	50
S00-5Q3S1290	Curtainwall - Infill Fabrication (West Stack 6)	65	15-May-19	15-Aug-19	40

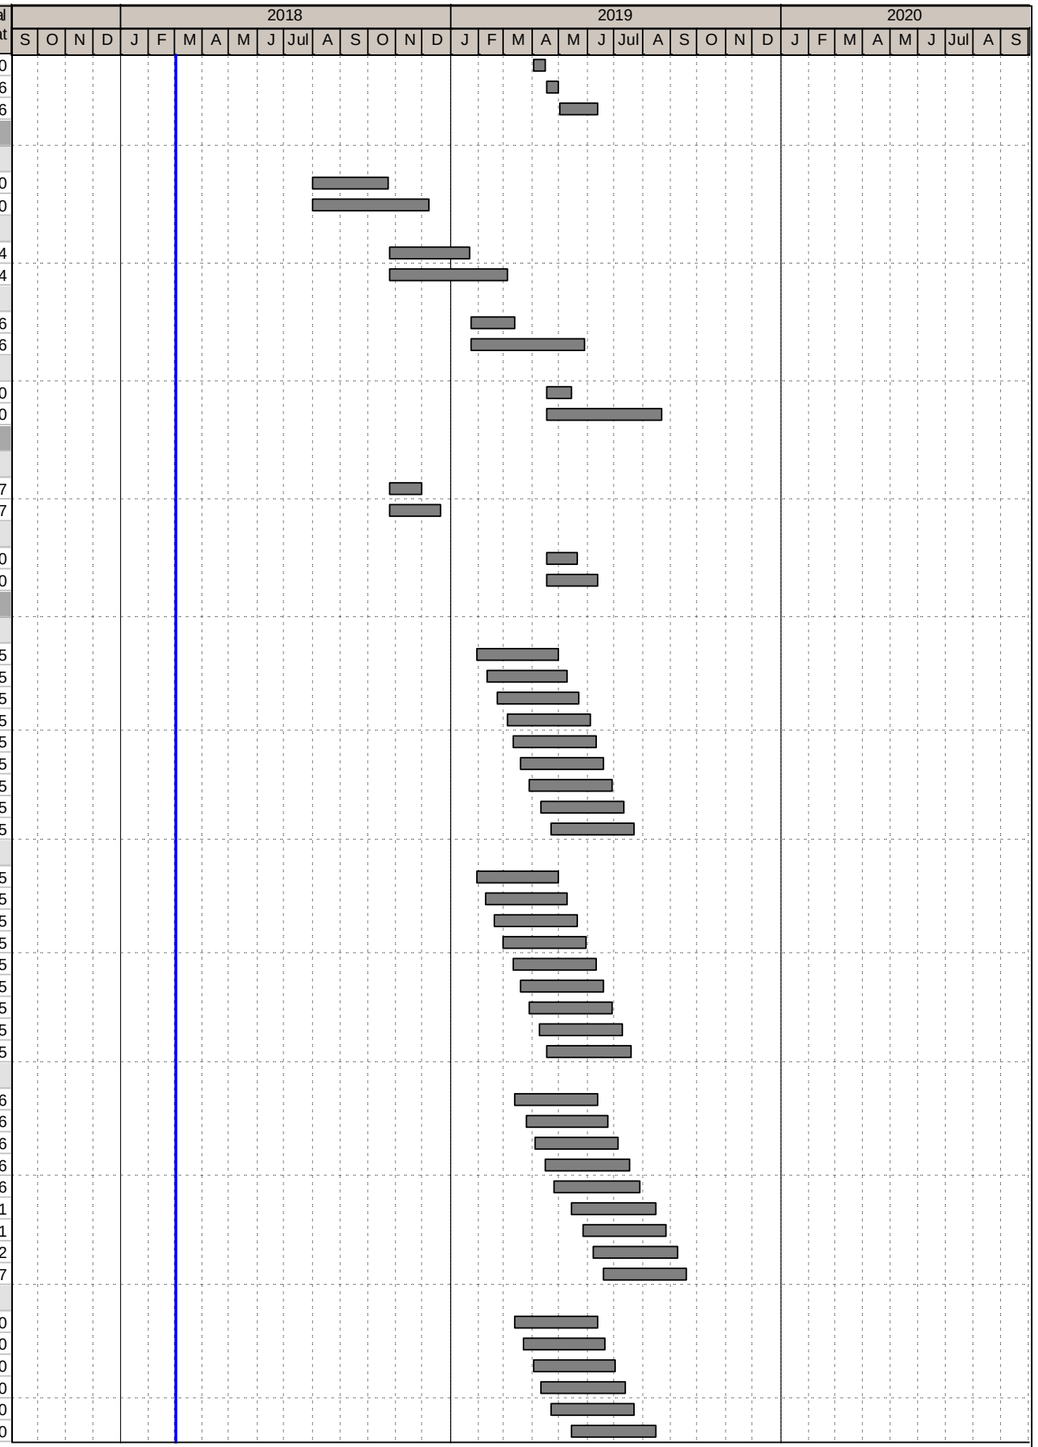

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S00-5Q3S1300	Curtainwall - Infill Fabrication (West Stack 7)	65	24-May-19	26-Aug-19	40
S00-5Q3S1310	Curtainwall - Infill Fabrication (West Stack 8)	65	05-Jun-19	05-Sep-19	41
S00-5Q3S1320	Curtainwall - Infill Fabrication (West Stack 9)	65	14-Jun-19	16-Sep-19	41
Curtainwall Metal Procurement					
S00-5Q3S1390	Curtainwall - Metal Fabrication (North Stack 1)	65	30-Jan-19	30-Apr-19	15
S00-5Q3S1400	Curtainwall - Metal Fabrication (North Stack 2)	65	11-Feb-19	10-May-19	15
S00-5Q3S1410	Curtainwall - Metal Fabrication (North Stack 3)	65	21-Feb-19	22-May-19	15
S00-5Q3S1420	Curtainwall - Metal Fabrication (North Stack 4)	65	05-Mar-19	04-Jun-19	15
S00-5Q3S1430	Curtainwall - Metal Fabrication (North Stack 5)	65	12-Mar-19	11-Jun-19	15
S00-5Q3S1440	Curtainwall - Metal Fabrication (North Stack 6)	65	19-Mar-19	18-Jun-19	15
S00-5Q3S1450	Curtainwall - Metal Fabrication (North Stack 7)	65	29-Mar-19	28-Jun-19	15
S00-5Q3S1460	Curtainwall - Metal Fabrication (North Stack 8)	65	10-Apr-19	11-Jul-19	15
S00-5Q3S1470	Curtainwall - Metal Fabrication (North Stack 9)	65	22-Apr-19	23-Jul-19	15
S00-5Q3S1480	Curtainwall - Metal Fabrication (East Stack 1)	65	30-Jan-19	30-Apr-19	15
S00-5Q3S1490	Curtainwall - Metal Fabrication (East Stack 2)	65	08-Feb-19	09-May-19	15
S00-5Q3S1500	Curtainwall - Metal Fabrication (East Stack 3)	65	19-Feb-19	20-May-19	15
S00-5Q3S1510	Curtainwall - Metal Fabrication (East Stack 4)	65	28-Feb-19	30-May-19	15
S00-5Q3S1520	Curtainwall - Metal Fabrication (East Stack 5)	65	11-Mar-19	10-Jun-19	15
S00-5Q3S1530	Curtainwall - Metal Fabrication (East Stack 6)	65	20-Mar-19	19-Jun-19	15
S00-5Q3S1540	Curtainwall - Metal Fabrication (East Stack 7)	65	29-Mar-19	28-Jun-19	15
S00-5Q3S1550	Curtainwall - Metal Fabrication (East Stack 8)	65	09-Apr-19	10-Jul-19	15
S00-5Q3S1560	Curtainwall - Metal Fabrication (East Stack 9)	65	18-Apr-19	19-Jul-19	15
S00-5Q3S1570	Curtainwall - Metal Fabrication (South Stack 1)	65	13-Mar-19	12-Jun-19	46
S00-5Q3S1580	Curtainwall - Metal Fabrication (South Stack 2)	65	25-Mar-19	24-Jun-19	46
S00-5Q3S1590	Curtainwall - Metal Fabrication (South Stack 3)	65	04-Apr-19	05-Jul-19	46
S00-5Q3S1600	Curtainwall - Metal Fabrication (South Stack 4)	65	16-Apr-19	17-Jul-19	46
S00-5Q3S1610	Curtainwall - Metal Fabrication (South Stack 5)	65	26-Apr-19	29-Jul-19	46
S00-5Q3S1620	Curtainwall - Metal Fabrication (South Stack 6)	65	15-May-19	15-Aug-19	41
S00-5Q3S1630	Curtainwall - Metal Fabrication (South Stack 7)	65	28-May-19	27-Aug-19	41
S00-5Q3S1640	Curtainwall - Metal Fabrication (South Stack 8)	65	07-Jun-19	09-Sep-19	42
S00-5Q3S1650	Curtainwall - Metal Fabrication (South Stack 9)	65	19-Jun-19	19-Sep-19	47
S00-5Q3S1660	Curtainwall - Metal Fabrication (West Stack 1)	65	13-Mar-19	12-Jun-19	50
S00-5Q3S1670	Curtainwall - Metal Fabrication (West Stack 2)	65	22-Mar-19	21-Jun-19	50
S00-5Q3S1680	Curtainwall - Metal Fabrication (West Stack 3)	65	02-Apr-19	02-Jul-19	50
S00-5Q3S1690	Curtainwall - Metal Fabrication (West Stack 4)	65	11-Apr-19	12-Jul-19	50
S00-5Q3S1700	Curtainwall - Metal Fabrication (West Stack 5)	65	22-Apr-19	23-Jul-19	50
S00-5Q3S1710	Curtainwall - Metal Fabrication (West Stack 6)	65	15-May-19	15-Aug-19	40
S00-5Q3S1720	Curtainwall - Metal Fabrication (West Stack 7)	65	24-May-19	26-Aug-19	40
S00-5Q3S1730	Curtainwall - Metal Fabrication (West Stack 8)	65	05-Jun-19	05-Sep-19	41
S00-5Q3S1740	Curtainwall - Metal Fabrication (West Stack 9)	65	14-Jun-19	16-Sep-19	41
Arch Louver Procurement					
S00-5Q3S1810	Arch Louvers - Fabrication - East	50	03-Dec-18	12-Feb-19	47
S00-5Q3S1820	Arch Louvers - Fabrication - West	50	22-May-19	01-Aug-19	10
Curtainwall Assembly					
S00-5Q3S1950	Curtainwall - Unit Assembly (North Stack 1)	8	01-May-19	10-May-19	18
S00-5Q3S1960	Curtainwall - Unit Assembly (North Stack 2)	8	13-May-19	22-May-19	18
S00-5Q3S1970	Curtainwall - Unit Assembly (North Stack 3)	8	23-May-19	04-Jun-19	18
S00-5Q3S1980	Curtainwall - Unit Assembly (North Stack 4)	5	05-Jun-19	11-Jun-19	18
S00-5Q3S1990	Curtainwall - Unit Assembly (North Stack 5)	5	12-Jun-19	18-Jun-19	18
S00-5Q3S2000	Curtainwall - Unit Assembly (North Stack 6)	5	19-Jun-19	25-Jun-19	18
S00-5Q3S2010	Curtainwall - Unit Assembly (North Stack 7)	8	01-Jul-19	11-Jul-19	15
S00-5Q3S2020	Curtainwall - Unit Assembly (North Stack 8)	8	12-Jul-19	23-Jul-19	15
S00-5Q3S2030	Curtainwall - Unit Assembly (North Stack 9)	3	24-Jul-19	26-Jul-19	15

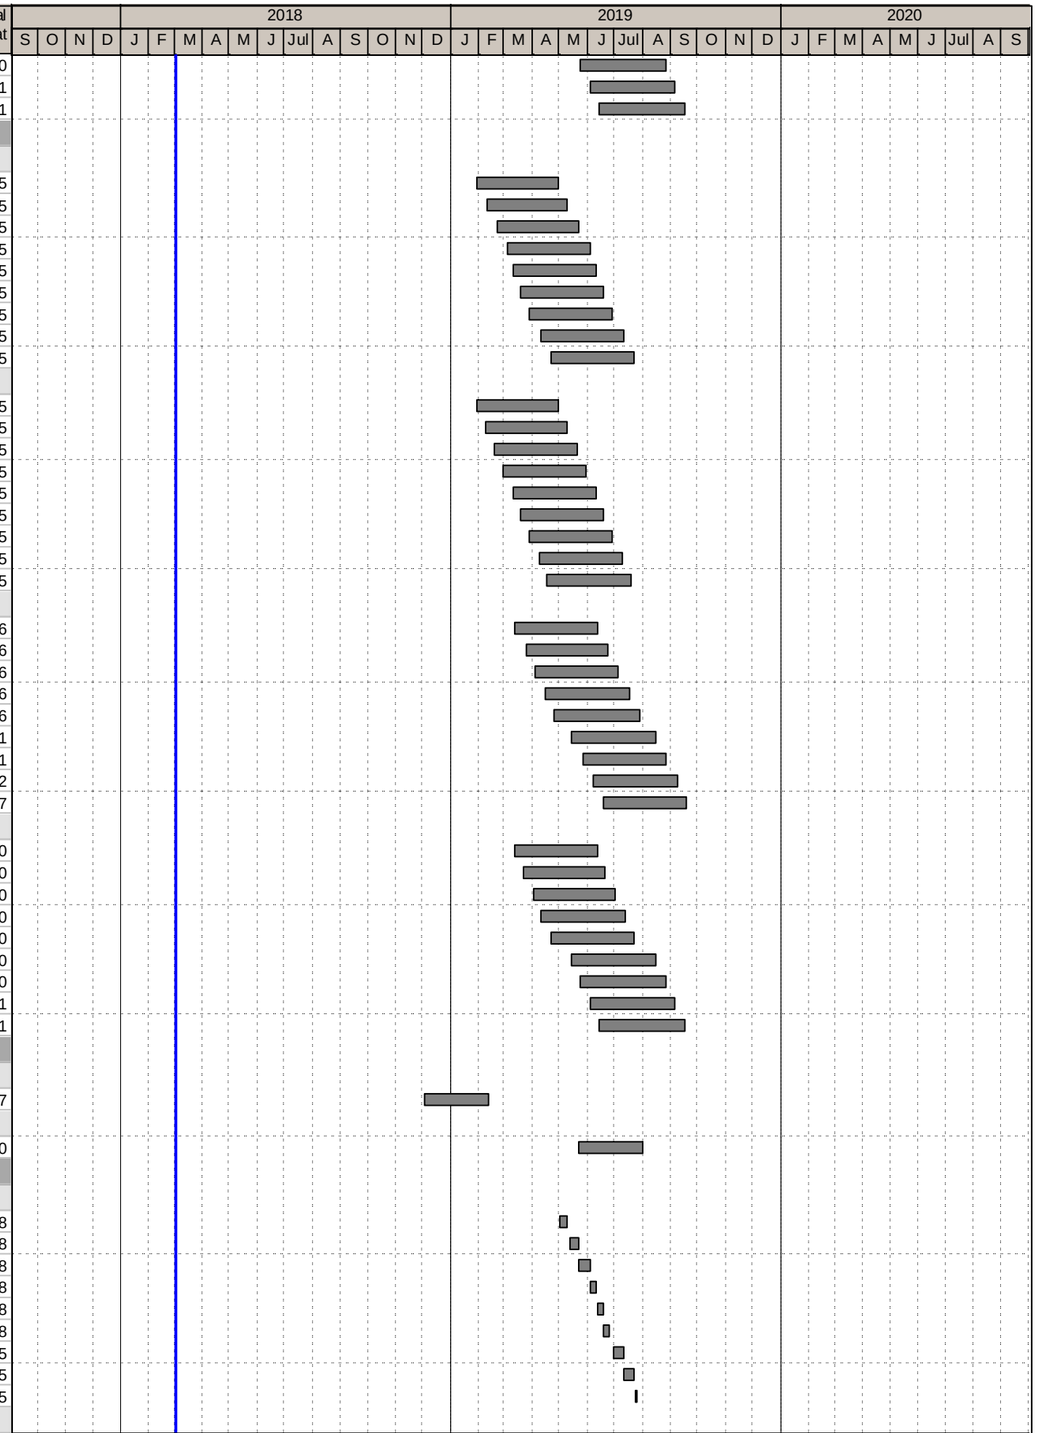

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S00-5Q3S2040	Curtainwall - Unit Assembly (East Stack 1)	6	01-May-19	08-May-19	15
S00-5Q3S2050	Curtainwall - Unit Assembly (East Stack 2)	6	10-May-19	17-May-19	15
S00-5Q3S2060	Curtainwall - Unit Assembly (East Stack 3)	6	21-May-19	29-May-19	15
S00-5Q3S2070	Curtainwall - Unit Assembly (East Stack 4)	6	31-May-19	07-Jun-19	15
S00-5Q3S2080	Curtainwall - Unit Assembly (East Stack 5)	6	11-Jun-19	18-Jun-19	15
S00-5Q3S2090	Curtainwall - Unit Assembly (East Stack 6)	6	20-Jun-19	27-Jun-19	15
S00-5Q3S2100	Curtainwall - Unit Assembly (East Stack 7)	6	01-Jul-19	09-Jul-19	15
S00-5Q3S2110	Curtainwall - Unit Assembly (East Stack 8)	6	11-Jul-19	18-Jul-19	15
S00-5Q3S2120	Curtainwall - Unit Assembly (East Stack 9)	6	22-Jul-19	29-Jul-19	15
S00-5Q3S2130	Curtainwall - Unit Assembly (South Stack 1)	8	29-Jul-19	07-Aug-19	15
S00-5Q3S2140	Curtainwall - Unit Assembly (South Stack 2)	8	08-Aug-19	19-Aug-19	15
S00-5Q3S2150	Curtainwall - Unit Assembly (South Stack 3)	8	20-Aug-19	29-Aug-19	15
S00-5Q3S2160	Curtainwall - Unit Assembly (South Stack 4)	8	30-Aug-19	11-Sep-19	15
S00-5Q3S2170	Curtainwall - Unit Assembly (South Stack 5)	8	12-Sep-19	23-Sep-19	15
S00-5Q3S2180	Curtainwall - Unit Assembly (South Stack 6)	8	24-Sep-19	03-Oct-19	15
S00-5Q3S2190	Curtainwall - Unit Assembly (South Stack 7)	8	04-Oct-19	15-Oct-19	15
S00-5Q3S2200	Curtainwall - Unit Assembly (South Stack 8)	8	16-Oct-19	25-Oct-19	16
S00-5Q3S2210	Curtainwall - Unit Assembly (South Stack 9)	3	28-Oct-19	30-Oct-19	21
S00-5Q3S2220	Curtainwall - Unit Assembly (West Stack 1)	6	19-Jul-19	26-Jul-19	25
S00-5Q3S2230	Curtainwall - Unit Assembly (West Stack 2)	6	29-Jul-19	05-Aug-19	26
S00-5Q3S2240	Curtainwall - Unit Assembly (West Stack 3)	6	06-Aug-19	13-Aug-19	27
S00-5Q3S2250	Curtainwall - Unit Assembly (West Stack 4)	6	14-Aug-19	21-Aug-19	28
S00-5Q3S2260	Curtainwall - Unit Assembly (West Stack 5)	6	22-Aug-19	29-Aug-19	29
S00-5Q3S2270	Curtainwall - Unit Assembly (West Stack 6)	6	30-Aug-19	09-Sep-19	30
S00-5Q3S2280	Curtainwall - Unit Assembly (West Stack 7)	6	10-Sep-19	17-Sep-19	31
S00-5Q3S2290	Curtainwall - Unit Assembly (West Stack 8)	6	18-Sep-19	25-Sep-19	33
S00-5Q3S2300	Curtainwall - Unit Assembly (West Stack 9)	6	26-Sep-19	03-Oct-19	34
Arch Louver Assembly					
S00-5Q3S2380	Arch Louvers - Assembly - East	50	13-Feb-19	23-Apr-19	47
S00-5Q3S2370	Arch Louvers - Assembly - West	50	26-Jul-19	04-Oct-19	10
Storefront Glazing System					
Storefront Engineering					
S00-5Q3S570	Storefront Glazing Systems Engineering - Prepare Shop	60	08-Oct-18	03-Jan-19	81
S00-5Q3S580	Storefront Glazing Systems Engineering - MMCJVLV Reivew Shop Dwgs	3	04-Jan-19	08-Jan-19	81
S00-5Q3S590	Storefront Glazing Systems Engineering - Design Team Reivew and Approve Shop Dwgs	10	09-Jan-19	22-Jan-19	81
S00-5Q3S600	Storefront Glazing Systems Engineering - Revise and Resubmit Shop Dwgs	5	23-Jan-19	29-Jan-19	81
S00-5Q3S610	Storefront Glazing Systems Engineering - MMCJVLV Review Shop Dwgs	2	30-Jan-19	31-Jan-19	81
S00-5Q3S620	Storefront Glazing Systems Engineering - Design Team Review and Approve Shop Dwgs	10	01-Feb-19	14-Feb-19	81
S00-5Q3S630	Storefront Glazing Systems Engineering - Prepare CC Package	10	15-Feb-19	28-Feb-19	101
S00-5Q3S640	Storefront Glazing Systems Engineering - CC Deferred Submittal Review and Approval	20	01-Mar-19	28-Mar-19	101
Storefront Production Drawings					
S00-5Q3S930	Storefront Glazing Systems - Production Drawings	50	15-Feb-19	25-Apr-19	81
S00-5Q3S940	Storefront Glazing Systems - Production Dwg Takeoffs	25	22-Mar-19	25-Apr-19	81
Storefront Procurment					
S00-5Q3S1870	Storefront Glazing Systems - Metal Procurement/Fabrication	60	26-Apr-19	22-Jul-19	81
S00-5Q3S1880	Storefront Glazing Systems - Glass Procurement/Assembly	60	26-Apr-19	22-Jul-19	81
Specialty Entrances					
Operable Curtainwall Door Frames					
S00-5Q3S10	Op Doors - Prepare Shop Drawings - Steel Structure & Mech Equip	180	09-Feb-18 A	19-Oct-18	15
S00-5Q3S20	Op Doors - MMCJVLV Reivew Shop Dwgs	3	22-Oct-18	24-Oct-18	15
S00-5Q3S30	Op Doors - Design Team Reivew and Approve Shop Dwgs	10	25-Oct-18	07-Nov-18	15

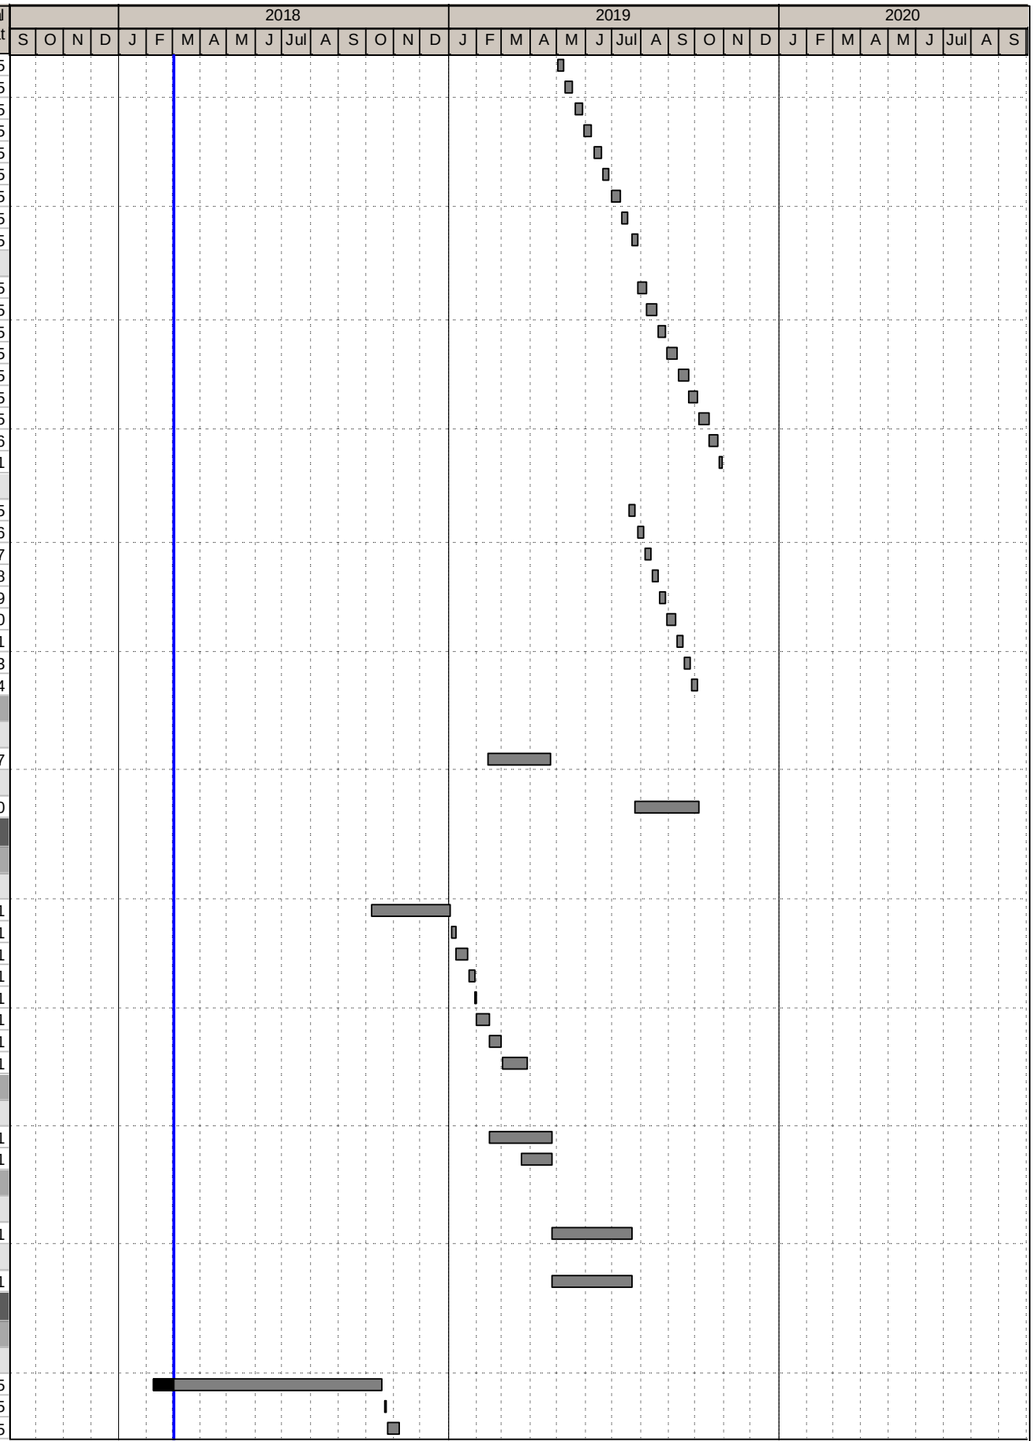

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S00-5Q3S40	Op Doors - Revise and Resubmit Shop Dwgs	10	08-Nov-18	21-Nov-18	43
S00-5Q3S50	Op Doors - MMCJVLV Review Shop Dwgs	2	26-Nov-18	27-Nov-18	43
S00-5Q3S60	Op Doors - Design Team Review and Approve Shop Dwgs	10	28-Nov-18	11-Dec-18	43
S00-5Q3S70	Op Doors - Prepare Permit Package	11	12-Dec-18	27-Dec-18	43
S00-5Q3S80	Op Doors - CC Approval & Permit	30	28-Dec-18	08-Feb-19	43
Operable CW Door Production Drawings					
S00-5Q3S740	Op Doors - Production Dwg Takeoffs	36	08-Nov-18	02-Jan-19	15
S00-5Q3S730	Op Doors - Production Drawings	61	08-Nov-18	06-Feb-19	15
Operable Door Steel and Mech Procurement					
S00-5Q3S950	Op Doors - Steel Fabrication	70	03-Jan-19	10-Apr-19	15
S00-5Q3S960	Op Doors - Mechanization Procurement	120	07-Feb-19	26-Jul-19	50
Curtainwall Infil Procurement					
S00-5Q3S1330	Op Door Curtainwall - Infill Fabrication (Door 1)	65	11-Feb-19	10-May-19	43
S00-5Q3S1340	Op Door Curtainwall - Infill Fabrication (Door 2)	65	20-Feb-19	21-May-19	46
S00-5Q3S1350	Op Door Curtainwall - Infill Fabrication (Door 3)	65	01-Mar-19	31-May-19	49
S00-5Q3S1360	Op Door Curtainwall - Infill Fabrication (Door 4)	65	12-Mar-19	11-Jun-19	52
S00-5Q3S1370	Op Door Curtainwall - Infill Fabrication (Door 5)	65	22-Mar-19	21-Jun-19	54
S00-5Q3S1380	Op Door Curtainwall - Infill Fabrication (Door 6)	65	02-Apr-19	02-Jul-19	57
Curtainwall Metal Procurement					
S00-5Q3S1750	Op Door Curtainwall - Metal Fabrication (Door 1)	65	11-Feb-19	10-May-19	43
S00-5Q3S1760	Op Door Curtainwall - Metal Fabrication (Door 2)	65	20-Feb-19	21-May-19	46
S00-5Q3S1770	Op Door Curtainwall - Metal Fabrication (Door 3)	65	01-Mar-19	31-May-19	49
S00-5Q3S1780	Op Door Curtainwall - Metal Fabrication (Door 4)	65	12-Mar-19	11-Jun-19	52
S00-5Q3S1790	Op Door Curtainwall - Metal Fabrication (Door 5)	65	22-Mar-19	21-Jun-19	54
S00-5Q3S1800	Op Door Curtainwall - Metal Fabrication (Door 6)	65	02-Apr-19	02-Jul-19	57
Curtainwall Assembly					
S00-5Q3S2310	Op Door Curtainwall - Unit Assembly (Door 1)	5	13-May-19	17-May-19	43
S00-5Q3S2320	Op Door Curtainwall - Unit Assembly (Door 2)	5	22-May-19	29-May-19	46
S00-5Q3S2330	Op Door Curtainwall - Unit Assembly (Door 3)	5	03-Jun-19	07-Jun-19	49
S00-5Q3S2340	Op Door Curtainwall - Unit Assembly (Door 4)	5	12-Jun-19	18-Jun-19	52
S00-5Q3S2350	Op Door Curtainwall - Unit Assembly (Door 5)	5	24-Jun-19	28-Jun-19	54
S00-5Q3S2360	Op Door Curtainwall - Unit Assembly (Door 6)	5	03-Jul-19	10-Jul-19	57
Roof Systems					
S00-5P5P40	Submit/Approve/Procure - Roof System / ETFE	254	13-Mar-18	12-Mar-19	85
Elevators					
S00-5P5P60	Submit/Approve/Procure - Elevators	220	02-Apr-18	12-Feb-19	121
Escalators					
000 Event Level					
Submit					
S1AA1-5R3S	Escalator - Prepare Submittal - Esc A3 (Event to Lower Mezz)	10	08-Jan-18 A	16-Mar-18	68
S1BB1-5R3S	Escalator - Prepare Submittal - Esc B3 (Event to Lower Mezz)	10	08-Jan-18 A	16-Mar-18	66
S1AA2-5R3S	Escalator - Prepare Submittal - Esc A1 & D1 (Event to Lower Mezz)	10	08-Jan-18 A	16-Mar-18	117
S1BB2-5R3S	Escalator - Prepare Submittal - Esc B1 & C1 (Event to Lower Mezz)	10	08-Jan-18 A	16-Mar-18	137
S1AA1-5R3R	Escalator - MMCJV Submittal Review - Esc A3 (Event to Lower Mezz)	2	19-Mar-18	20-Mar-18	68
S1BB1-5R3R	Escalator - MMCJV Submittal Review - Esc B3 (Event to Lower Mezz)	2	19-Mar-18	20-Mar-18	66
S1AA2-5R3R	Escalator - MMCJV Submittal Review - Esc A1 & D1 (Event to Lower Mezz)	2	19-Mar-18	20-Mar-18	117
S1BB2-5R3R	Escalator - MMCJV Submittal Review - Esc B1 & C1 (Event to Lower Mezz)	2	19-Mar-18	20-Mar-18	137
S1AA1-5R3A	Escalator - Design Team Submittal Review - Esc A3 (Event to Lower Mezz)	10	21-Mar-18	03-Apr-18	68

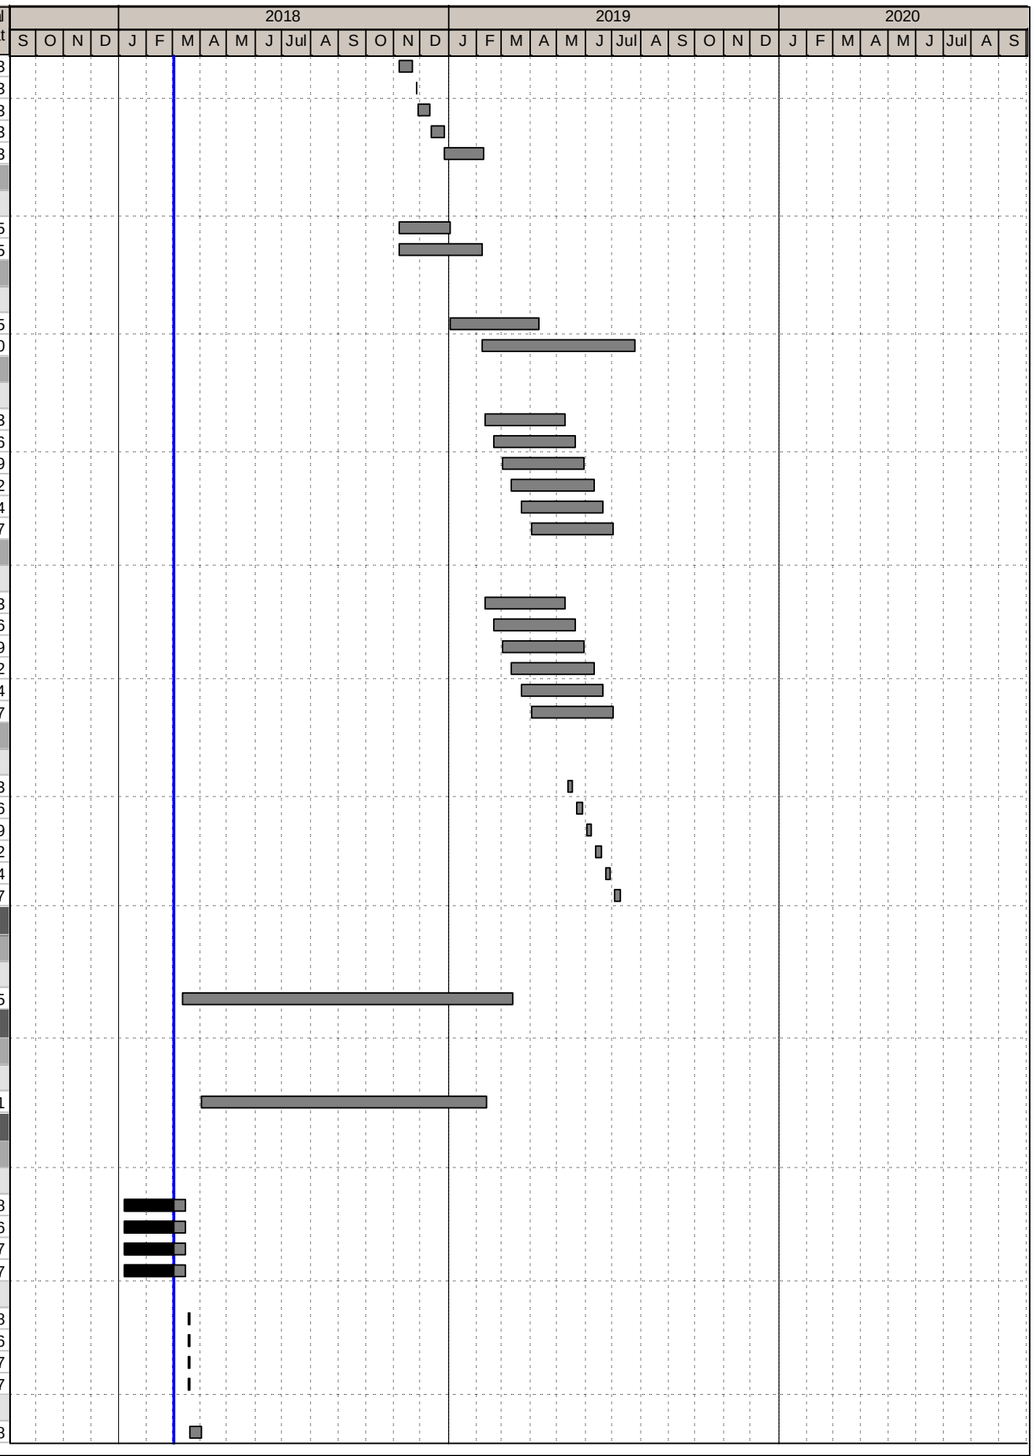

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S1BB1-5R3A	Escalator - Design Team Submittal Review - Esc B3 (Event to Lower Mezz)	10	21-Mar-18	03-Apr-18	66
S1AA2-5R3A	Escalator - Design Team Submittal Review - Esc A1 & D1 (Event to Lower Mezz)	10	21-Mar-18	03-Apr-18	117
S1BB2-5R3A	Escalator - Design Team Submittal Review - Esc B1 & C1 (Event to Lower Mezz)	10	21-Mar-18	03-Apr-18	137
S1AA1-5R3F	Escalator - Fabrication & Delivery to LV - Esc A3 (Event to Lower Mezz)	100	04-Apr-18	23-Aug-18	68
S1BB1-5R3F	Escalator - Fabrication & Delivery to LV - Esc B3 (Event to Lower Mezz)	100	04-Apr-18	23-Aug-18	66
S1AA2-5R3F	Escalator - Fabrication & Delivery to LV - Esc A1 & D1 (Event to Lower Mezz)	100	04-Apr-18	23-Aug-18	117
S1BB2-5R3F	Escalator - Fabrication & Delivery to LV - Esc B1 & C1 (Event to Lower Mezz)	100	04-Apr-18	23-Aug-18	137
S1AA1-5R3F1	Escalator - Off Site Assembly - Esc A3 (Event to Lower Mezz)	20	24-Aug-18	21-Sep-18	68
S1BB1-5R3F1	Escalator - Off Site Assembly - Esc B3 (Event to Lower Mezz)	20	24-Aug-18	21-Sep-18	66
S1AA2-5R3F1	Escalator - Off Site Assembly - Esc A1 & D1 (Event to Lower Mezz)	20	24-Aug-18	21-Sep-18	117
S1BB2-5R3F1	Escalator - Off Site Assembly - Esc B1 & C1 (Event to Lower Mezz)	20	24-Aug-18	21-Sep-18	137
050 Lower Mezz Level					
Submit					
S2AA1-5R3S	Escalator - Prepare Submittal - Esc A5 & A6 (Lower Mezz to Main Conc)	10	08-Jan-18 A	26-Jan-18 A	
S2BB1-5R3S	Escalator - Prepare Submittal - Esc B5 & B6 (Lower Mezz to Main Conc)	10	08-Jan-18 A	26-Jan-18 A	
S2AA2-5R3S	Escalator - Prepare Submittal - Esc A2 & D2 (Lower Mezz to Main Conc)	10	08-Jan-18 A	16-Mar-18	157
S2BB2-5R3S	Escalator - Prepare Submittal - Esc B2 & C2 (Lower Mezz to Main Conc)	10	08-Jan-18 A	16-Mar-18	128
S2AA1-5R3R	Escalator - MMCJV Submittal Review - Esc A5 & A6 (Lower Mezz to Main Conc)	2	29-Jan-18 A	31-Jan-18 A	
S2BB1-5R3R	Escalator - MMCJV Submittal Review - Esc B5 & B6 (Lower Mezz to Main Conc)	2	29-Jan-18 A	31-Jan-18 A	
S2AA2-5R3R	Escalator - MMCJV Submittal Review - Esc A2 & D2 (Lower Mezz to Main Conc)	2	19-Mar-18	20-Mar-18	157
S2BB2-5R3R	Escalator - MMCJV Submittal Review - Esc B2 & C2 (Lower Mezz to Main Conc)	2	19-Mar-18	20-Mar-18	128
S2AA1-5R3A	Escalator - Design Team Submittal Review - Esc A5 & A6 (Lower Mezz to Main Conc)	10	01-Feb-18 A	05-Mar-18	6
S2BB1-5R3A	Escalator - Design Team Submittal Review - Esc B5 & B6 (Lower Mezz to Main Conc)	10	01-Feb-18 A	05-Mar-18	1
S2AA2-5R3A	Escalator - Design Team Submittal Review - Esc A2 & D2 (Lower Mezz to Main Conc)	10	21-Mar-18	03-Apr-18	157
S2BB2-5R3A	Escalator - Design Team Submittal Review - Esc B2 & C2 (Lower Mezz to Main Conc)	10	21-Mar-18	03-Apr-18	128
S2AA1-5R3F	Escalator - Fabrication & Delivery to LV - Esc A5 & A6 (Lower Mezz to Main Conc)	100	08-Mar-18	27-Jul-18	6
S2BB1-5R3F	Escalator - Fabrication & Delivery to LV - Esc B5 & B6 (Lower Mezz to Main Conc)	100	08-Mar-18	27-Jul-18	1
S2AA2-5R3F	Escalator - Fabrication & Delivery to LV - Esc A2 & D2 (Lower Mezz to Main Conc)	100	06-Apr-18	27-Aug-18	157
S2BB2-5R3F	Escalator - Fabrication & Delivery to LV - Esc B2 & C2 (Lower Mezz to Main Conc)	100	06-Apr-18	27-Aug-18	128
S2AA1-5R3F1	Escalator - Off Site Assembly - Esc A5 & A6 (Lower Mezz to Main Conc)	40	30-Jul-18	24-Sep-18	6
S2BB1-5R3F1	Escalator - Off Site Assembly - Esc B5 & B6 (Lower Mezz to Main Conc)	40	30-Jul-18	24-Sep-18	1
S2AA2-5R3F1	Escalator - Off Site Assembly - Esc A2 & D2 (Lower Mezz to Main Conc)	40	28-Aug-18	23-Oct-18	157
S2BB2-5R3F1	Escalator - Off Site Assembly - Esc B2 & C2 (Lower Mezz to Main Conc)	40	28-Aug-18	23-Oct-18	128
100 Main Concourse					
Submit					
S3AA1-5R3S	Escalator - Prepare Submittal - Esc A7 & A8 (Main Conc to Lower Suite)	10	08-Jan-18 A	16-Mar-18	53
S3BB1-5R3S	Escalator - Prepare Submittal - Esc B7 & B8 (Main Conc to Lower Suite)	10	08-Jan-18 A	16-Mar-18	46
S3AA2-5R3S	Escalator - Prepare Submittal - Esc A11 & D3 (Main Conc to Lower Suite)	10	08-Jan-18 A	16-Mar-18	54
S3BB2-5R3S	Escalator - Prepare Submittal - Esc B11 & C3 (Main Conc to Lower Suite)	10	08-Jan-18 A	16-Mar-18	28
S3CC1-5R3S	Escalator - Prepare Submittal - Esc C4 & C5 (Main Conc to Upper Suite)	10	08-Jan-18 A	16-Mar-18	173
S3DD1-5R3S	Escalator - Prepare Submittal - Esc D4 & D5 (Main Conc to Upper Suite)	10	08-Jan-18 A	16-Mar-18	183
S3AA1-5R3R	Escalator - MMCJV Submittal Review - Esc A7 & A8 (Main Conc to Lower Suite)	2	19-Mar-18	20-Mar-18	53
S3BB1-5R3R	Escalator - MMCJV Submittal Review - Esc B7 & B8 (Main Conc to Lower Suite)	2	19-Mar-18	20-Mar-18	46
S3AA2-5R3R	Escalator - MMCJV Submittal Review - Esc A11 & D3 (Main Conc to Lower Suite)	2	19-Mar-18	20-Mar-18	54
S3BB2-5R3R	Escalator - MMCJV Submittal Review - Esc B11 & C3 (Main Conc to Lower Suite)	2	19-Mar-18	20-Mar-18	28
S3CC1-5R3R	Escalator - MMCJV Submittal Review - Esc C4 & C5 (Main Conc to Upper Suite)	2	19-Mar-18	20-Mar-18	173
S3DD1-5R3R	Escalator - MMCJV Submittal Review - Esc D4 & D5 (Main Conc to Upper Suite)	2	19-Mar-18	20-Mar-18	183
S3AA1-5R3A	Escalator - Design Team Submittal Review - Esc A7 & A8 (Main Conc to Lower Suite)	10	21-Mar-18	03-Apr-18	53
S3BB1-5R3A	Escalator - Design Team Submittal Review - Esc B7 & B8 (Main Conc to Lower Suite)	10	21-Mar-18	03-Apr-18	46
S3AA2-5R3A	Escalator - Design Team Submittal Review - Esc A11 & D3 (Main Conc to Lower Suite)	10	21-Mar-18	03-Apr-18	54
S3BB2-5R3A	Escalator - Design Team Submittal Review - Esc B11 & C3 (Main Conc to Lower Suite)	10	21-Mar-18	03-Apr-18	28
S3CC1-5R3A	Escalator - Design Team Submittal Review - Esc C4 & C5 (Main Conc to Upper Suite)	10	21-Mar-18	03-Apr-18	173
S3DD1-5R3A	Escalator - Design Team Submittal Review - Esc D4 & D5 (Main Conc to Upper Suite)	10	21-Mar-18	03-Apr-18	183

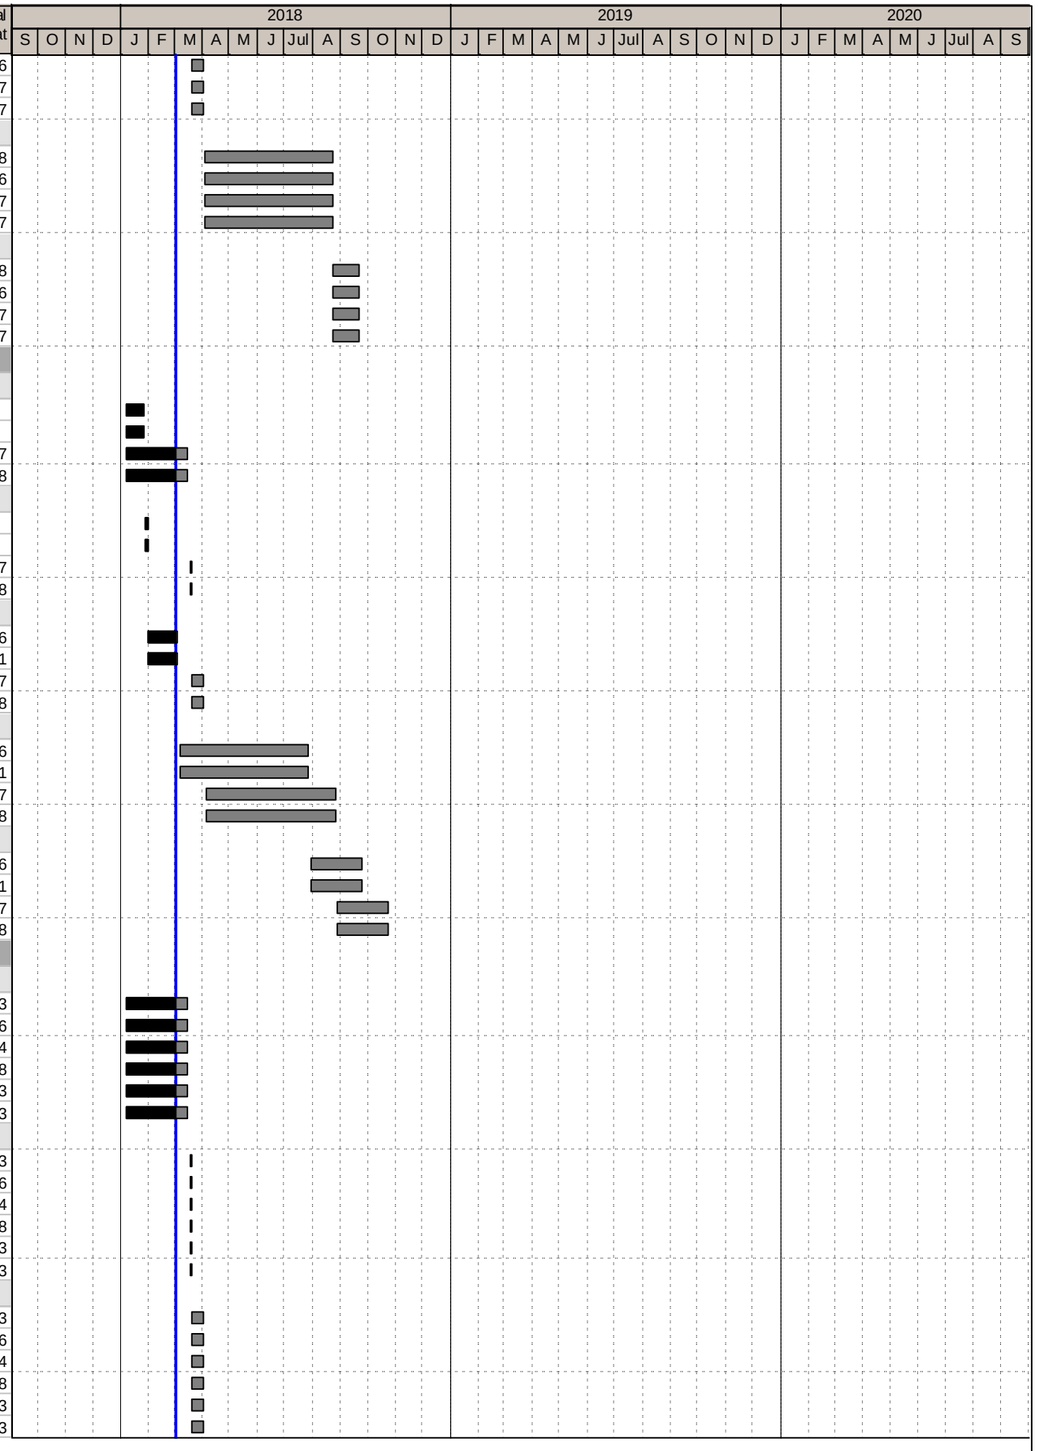

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S3AA1-5R3F	Escalator - Fabrication & Delivery to LV - Esc A7 & A8 (Main Conc to Lower Suite)	100	06-Apr-18	27-Aug-18	53
S3BB1-5R3F	Escalator - Fabrication & Delivery to LV - Esc B7 & B8 (Main Conc to Lower Suite)	100	06-Apr-18	27-Aug-18	46
S3AA2-5R3F	Escalator - Fabrication & Delivery to LV - Esc A11 & D3 (Main Conc to Lower Suite)	100	06-Apr-18	27-Aug-18	54
S3BB2-5R3F	Escalator - Fabrication & Delivery to LV - Esc B11 & C3 (Main Conc to Lower Suite)	100	06-Apr-18	27-Aug-18	28
S3CC1-5R3F	Escalator - Fabrication & Delivery to LV - Esc C4 & C5 (Main Conc to Upper Suite)	140	06-Apr-18	23-Oct-18	173
S3DD1-5R3F	Escalator - Fabrication & Delivery to LV - Esc D4 & D5 (Main Conc to Upper Suite)	140	06-Apr-18	23-Oct-18	183
S3AA1-5R3F1	Escalator - Off Site Assembly - Esc A7 & A8 (Main Conc to Lower Suite)	40	28-Aug-18	23-Oct-18	53
S3BB1-5R3F1	Escalator - Off Site Assembly - Esc B5 & B6 (Main Conc to Lower Suite)	40	28-Aug-18	23-Oct-18	46
S3AA2-5R3F1	Escalator - Off Site Assembly - Esc A7 & A8 (Main Conc to Lower Suite)	40	28-Aug-18	23-Oct-18	54
S3BB2-5R3F1	Escalator - Off Site Assembly - Esc B5 & B6 (Main Conc to Lower Suite)	40	28-Aug-18	23-Oct-18	28
150 Lower Suite Level					
Submit					
S4BB1-5R3S	Escalator - Prepare Submittal - Esc B9 & B10 (Lower Suite to Upper Suite)	10	08-Jan-18 A	16-Mar-18	46
S4AA1-5R3S	Escalator - Prepare Submittal - Esc A9 & A10 (Lower Suite to Upper Suite)	10	08-Jan-18 A	16-Mar-18	53
S4AA2-5R3S	Escalator - Prepare Submittal - Esc A14 & D8 (Lower Suite to Upper Suite)	10	08-Jan-18 A	16-Mar-18	145
S4BB2-5R3S	Escalator - Prepare Submittal - Esc B14 & C8 (Lower Suite to Upper Suite)	10	08-Jan-18 A	16-Mar-18	146
S4BB1-5R3R	Escalator - MMCJV Submittal Review - Esc B9 & B10 (Lower Suite to Upper Suite)	2	19-Mar-18	20-Mar-18	46
S4AA1-5R3R	Escalator - MMCJV Submittal Review - Esc A9 & A10 (Lower Suite to Upper Suite)	2	19-Mar-18	20-Mar-18	53
S4AA2-5R3R	Escalator - MMCJV Submittal Review - Esc A14 & D8 (Lower Suite to Upper Suite)	2	19-Mar-18	20-Mar-18	145
S4BB2-5R3R	Escalator - MMCJV Submittal Review - Esc B14 & C8 (Lower Suite to Upper Suite)	2	19-Mar-18	20-Mar-18	146
S4BB1-5R3A	Escalator - Design Team Submittal Review - Esc B9 & B10 (Lower Suite to Upper Suite)	10	21-Mar-18	03-Apr-18	46
S4AA1-5R3A	Escalator - Design Team Submittal Review - Esc A9 & A10 (Lower Suite to Upper Suite)	10	21-Mar-18	03-Apr-18	53
S4AA2-5R3A	Escalator - Design Team Submittal Review - Esc A14 & D8 (Lower Suite to Upper Suite)	10	21-Mar-18	03-Apr-18	145
S4BB2-5R3A	Escalator - Design Team Submittal Review - Esc B14 & C8 (Lower Suite to Upper Suite)	10	21-Mar-18	03-Apr-18	146
S4BB1-5R3F	Escalator - Fabrication & Delivery to LV - Esc B9 & B10 (Lower Suite to Upper Suite)	100	06-Apr-18	27-Aug-18	46
S4AA1-5R3F	Escalator - Fabrication & Delivery to LV - Esc A9 & A10 (Lower Suite to Upper Suite)	100	06-Apr-18	27-Aug-18	53
S4AA2-5R3F	Escalator - Fabrication & Delivery to LV - Esc A14 & D8 (Lower Suite to Upper Suite)	100	06-Apr-18	27-Aug-18	145
S4BB2-5R3F	Escalator - Fabrication & Delivery to LV - Esc B14 & C8 (Lower Suite to Upper Suite)	100	06-Apr-18	27-Aug-18	146
S4BB1-5R3F1	Escalator - Off Site Assembly - Esc B9 & B10 (Lower Suite to Upper Suite)	40	28-Aug-18	23-Oct-18	46
S4AA1-5R3F1	Escalator - Off Site Assembly - Esc A9 & A10 (Lower Suite to Upper Suite)	40	28-Aug-18	23-Oct-18	53
S4AA2-5R3F1	Escalator - Off Site Assembly - Esc A14 & D8 (Lower Suite to Upper Suite)	40	28-Aug-18	23-Oct-18	145
S4BB2-5R3F1	Escalator - Off Site Assembly - Esc B14 & C8 (Lower Suite to Upper Suite)	40	28-Aug-18	23-Oct-18	146
200 Upper Suite Level					
Submit					
S5DD1-5R3S	Escalator - Prepare Submittal - Esc D6 & D7 (Upper Suite to Mid-Bowl Mezz)	10	08-Jan-18 A	16-Mar-18	119
S5CC1-5R3S	Escalator - Prepare Submittal - Esc C6 & C7 (Upper Suite to Mid-Bowl Mezz)	10	08-Jan-18 A	16-Mar-18	122
S5AA1-5R3S	Escalator - Prepare Submittal - Esc A12 & A13 (Upper Suite to Upper Conc)	10	20-Mar-18	02-Apr-18	42
S5BB1-5R3S	Escalator - Prepare Submittal - Esc B12 & B13 (Upper Suite to Upper Conc)	10	20-Mar-18	02-Apr-18	35
S5DD1-5R3R	Escalator - MMCJV Submittal Review - Esc D6 & D7 (Upper Suite to Mid-Bowl Mezz)	2	19-Mar-18	20-Mar-18	119
S5CC1-5R3R	Escalator - MMCJV Submittal Review - Esc C6 & C7 (Upper Suite to Mid-Bowl Mezz)	2	19-Mar-18	20-Mar-18	122
S5AA1-5R3R	Escalator - MMCJV Submittal Review - Esc A12 & A13 (Upper Suite to Upper Conc)	2	03-Apr-18	04-Apr-18	42
S5BB1-5R3R	Escalator - MMCJV Submittal Review - Esc B12 & B13 (Upper Suite to Upper Conc)	2	03-Apr-18	04-Apr-18	35
S5DD1-5R3A	Escalator - Design Team Submittal Review - Esc D6 & D7 (Upper Suite to Mid-Bowl Mezz)	10	21-Mar-18	03-Apr-18	119
S5CC1-5R3A	Escalator - Design Team Submittal Review - Esc C6 & C7 (Upper Suite to Mid-Bowl Mezz)	10	21-Mar-18	03-Apr-18	122
S5AA1-5R3A	Escalator - Design Team Submittal Review - Esc A12 & A13 (Upper Suite to Upper Conc)	10	05-Apr-18	18-Apr-18	42
S5BB1-5R3A	Escalator - Design Team Submittal Review - Esc B12 & B13 (Upper Suite to Upper Conc)	10	05-Apr-18	18-Apr-18	35
S5DD1-5R3F	Escalator - Fabrication & Delivery to LV - Esc D6 & D7 (Upper Suite to Mid-Bowl Mezz)	100	06-Apr-18	27-Aug-18	119
S5CC1-5R3F	Escalator - Fabrication & Delivery to LV - Esc C6 & C7 (Upper Suite to Mid-Bowl Mezz)	100	06-Apr-18	27-Aug-18	122
S5AA1-5R3F	Escalator - Fabrication & Delivery to LV - Esc A12 & A13 (Upper Suite to Upper Conc)	140	23-Apr-18	07-Nov-18	42
S5BB1-5R3F	Escalator - Fabrication & Delivery to LV - Esc B12 & B13 (Upper Suite to Upper Conc)	140	23-Apr-18	07-Nov-18	35
S5DD1-5R3F1	Escalator - Off Site Assembly - Esc D6 & D7 (Upper Suite to Mid-Bowl Mezz)	40	28-Aug-18	23-Oct-18	119

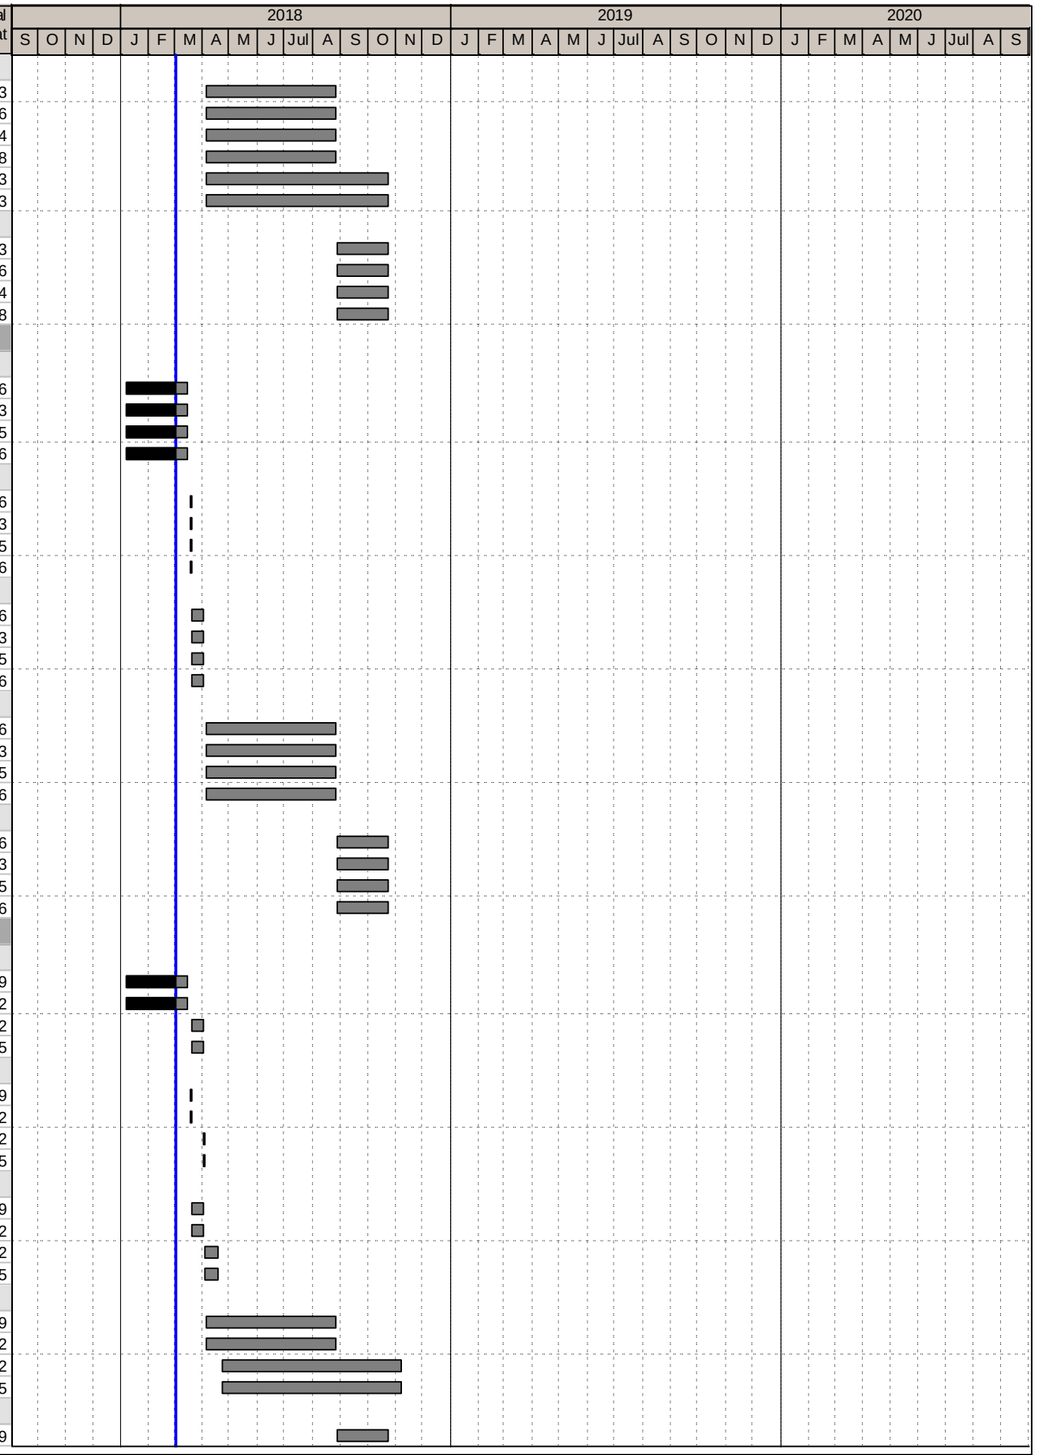

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S5CC1-5R3F1	Escalator - Off Site Assembly - Esc C6 & C7 (Upper Suite to Mid-Bowl Mezz)	40	28-Aug-18	23-Oct-18	122
250 Mid Bowl Mezz Level					
Submit					
S6CC1-5R3S	Escalator - Prepare Submittal - Esc C9 & C10 (Mid-Bowl Mezz to Upper Conc)	10	08-Jan-18 A	16-Mar-18	120
S6DD1-5R3S	Escalator - Prepare Submittal - Esc D9 & D10 (Mid-Bowl Mezz to Upper Conc)	10	08-Jan-18 A	16-Mar-18	120
S6CC1-5R3R	Escalator - MMCJV Submittal Review - Esc C9 & C10 (Mid-Bowl Mezz to Upper Conc)	2	19-Mar-18	20-Mar-18	120
S6DD1-5R3R	Escalator - MMCJV Submittal Review - Esc D9 & D10 (Mid-Bowl Mezz to Upper Conc)	2	19-Mar-18	20-Mar-18	120
S6CC1-5R3A	Escalator - Design Team Submittal Review - Esc C9 & C10 (Mid-Bowl Mezz to Upper Conc)	10	21-Mar-18	03-Apr-18	120
S6DD1-5R3A	Escalator - Design Team Submittal Review - Esc D9 & D10 (Mid-Bowl Mezz to Upper Conc)	10	21-Mar-18	03-Apr-18	120
S6CC1-5R3F	Escalator - Fabrication & Delivery to LV - Esc C9 & C10 (Mid-Bowl Mezz to Upper Conc)	100	06-Apr-18	27-Aug-18	120
S6DD1-5R3F	Escalator - Fabrication & Delivery to LV - Esc D9 & D10 (Mid-Bowl Mezz to Upper Conc)	100	06-Apr-18	27-Aug-18	120
S6CC1-5R3F1	Escalator - Off Site Assembly - Esc C9 & C10 (Mid-Bowl Mezz to Upper Conc)	40	28-Aug-18	23-Oct-18	120
S6DD1-5R3F1	Escalator - Off Site Assembly - Esc D9 & D10 (Mid-Bowl Mezz to Upper Conc)	40	28-Aug-18	23-Oct-18	120
Interior Rough-In					
S00-5P5P30	Submit/Approve/Procure - MEP Equipment	188	02-Apr-18	27-Dec-18	55
Riser & Mech/Elec Spaces Coord (Tied to Deck Rebar & Steel)					
SEA2-5S0	Fabricate MEP Materials - Area A Risers	30	05-Mar-18	13-Apr-18	182
SEF2-5S0	Fabricate MEP Materials - Area F Risers	30	05-Mar-18	13-Apr-18	182
SEB2-5S0	Fabricate MEP Materials - Area B Risers	30	12-Mar-18	20-Apr-18	177
SEE2-5S0	Fabricate MEP Materials - Area E Risers	30	12-Mar-18	20-Apr-18	177
SEC2-5S0	Fabricate MEP Materials - Area C Risers	30	09-Apr-18	18-May-18	157
SED2-5S0	Fabricate MEP Materials - Area D Risers	30	09-Apr-18	18-May-18	157
Underground /Foundation Coordination (Tied to SOG Rebar)					
SEA2-5S00	Fabricate MEP Materials - Area A Deep Underground	30	26-Feb-18 A	06-Apr-18	2
SEB2-5S00	Fabricate MEP Materials - Area B Deep Underground	30	26-Feb-18 A	06-Apr-18	21
SEF2-5S00	Fabricate MEP Materials - Area F Deep Underground	30	26-Feb-18 A	06-Apr-18	3
SEE2-5S00	Fabricate MEP Materials - Area E Deep Underground	30	26-Feb-18 A	06-Apr-18	25
SEC2-5S00	Fabricate MEP Materials - Area C Deep Underground	30	09-Apr-18	18-May-18	42
SED2-5S00	Fabricate MEP Materials - Area D Deep Underground	30	09-Apr-18	18-May-18	44
000 Event Level					
S1F60-5S00	Fabricate MEP Materials - Area F Event Lvl	30	13-Mar-18	23-Apr-18	176
S1E60-5S00	Fabricate MEP Materials - Area E Event Lvl	30	13-Mar-18	23-Apr-18	227
S1A60-5S00	Fabricate MEP Materials - Area A Event Lvl	30	03-Apr-18	14-May-18	161
S1B60-5S00	Fabricate MEP Materials - Area B Event Lvl	30	03-Apr-18	14-May-18	207
S1C60-5S00	Fabricate MEP Materials - Area C Event Lvl	30	24-Apr-18	05-Jun-18	217
S1D60-5S00	Fabricate MEP Materials - Area D Event Lvl	30	15-May-18	26-Jun-18	222
050 Lower Mezz Level					
S2F60-5S00	Fabricate MEP Materials - Area F Lower Mezz Lvl	30	24-Apr-18	05-Jun-18	280
S2E60-5S00	Fabricate MEP Materials - Area E Lower Mezz Lvl	30	24-Apr-18	05-Jun-18	239
S2A60-5S00	Fabricate MEP Materials - Area A Lower Mezz Lvl	30	15-May-18	26-Jun-18	265
S2B60-5S00	Fabricate MEP Materials - Area B Lower Mezz Lvl	30	15-May-18	26-Jun-18	175
S2C60-5S00	Fabricate MEP Materials - Area C Lower Mezz Lvl	30	06-Jun-18	18-Jul-18	215
S2D60-5S00	Fabricate MEP Materials - Area D Lower Mezz Lvl	30	27-Jun-18	08-Aug-18	229
100 Main Concourse					
S3F60-5S00	Fabricate MEP Materials - Area F Main Conc	30	27-Jun-18	08-Aug-18	135
S3E60-5S00	Fabricate MEP Materials - Area E Main Conc	30	27-Jun-18	08-Aug-18	175
S3A60-5S00	Fabricate MEP Materials - Area A Main Conc	30	19-Jul-18	29-Aug-18	120
S3B60-5S00	Fabricate MEP Materials - Area B Main Conc	30	19-Jul-18	29-Aug-18	150
S3C60-5S00	Fabricate MEP Materials - Area C Main Conc	30	09-Aug-18	20-Sep-18	185

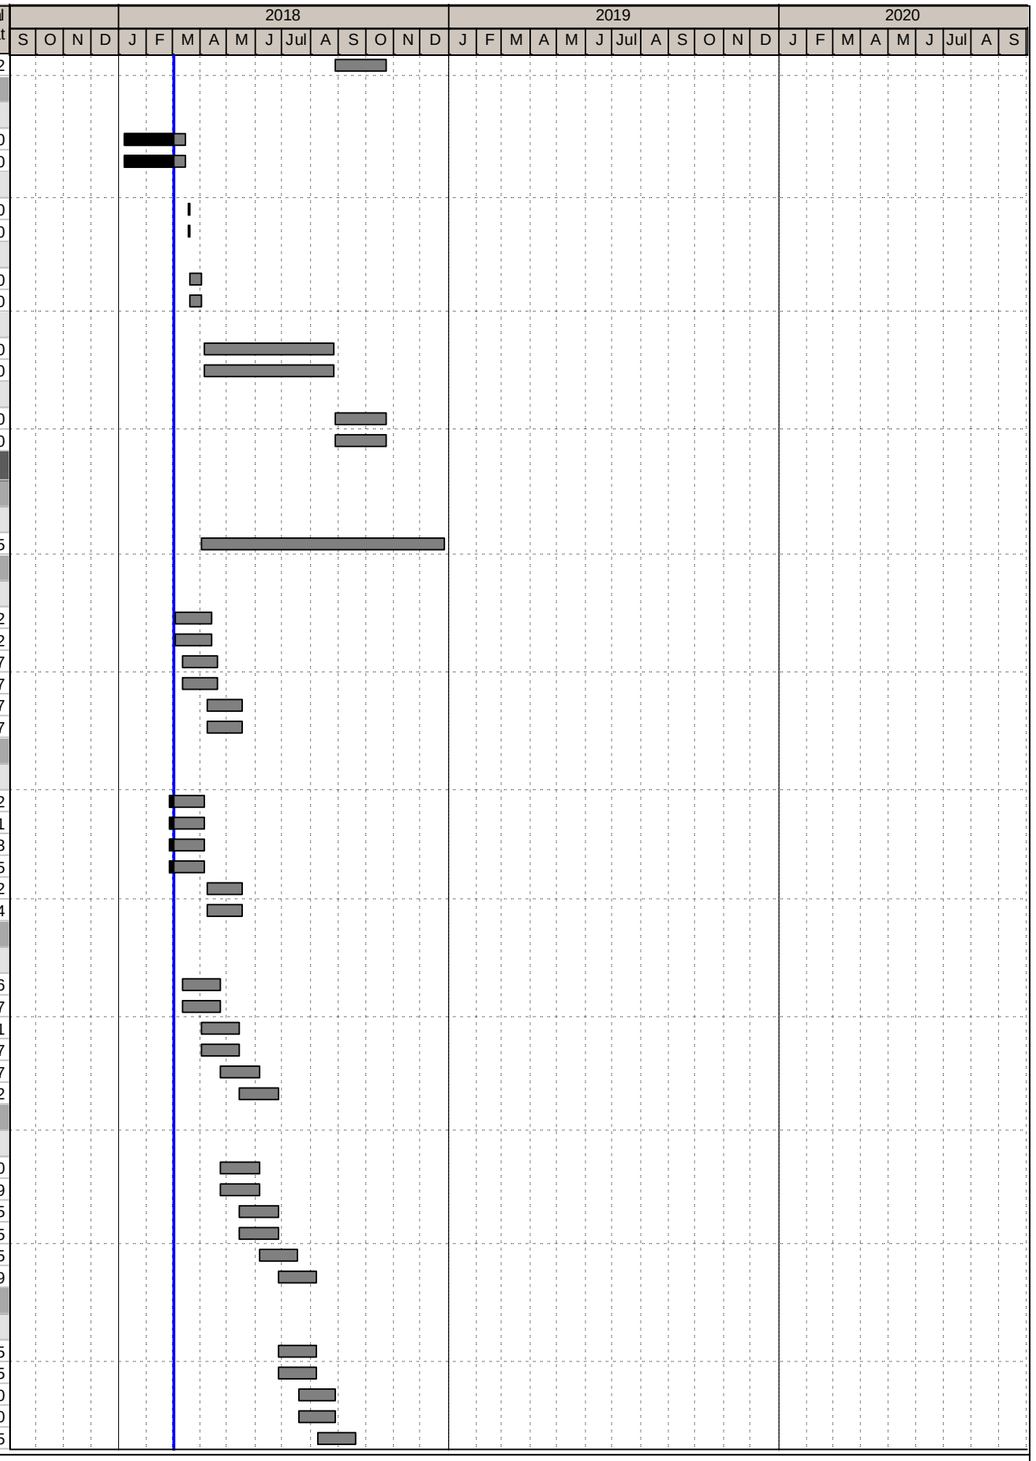

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S3D60-5S00	Fabricate MEP Materials - Area D Main Conc	30	30-Aug-18	11-Oct-18	180
150 Lower Suite Level					
S4F60-5S00	Fabricate MEP Materials - Area F Lower Suite Lvl	30	19-Jul-18	29-Aug-18	134
S4E60-5S00	Fabricate MEP Materials - Area E Lower Suite Lvl	30	19-Jul-18	29-Aug-18	187
S4A60-5S00	Fabricate MEP Materials - Area A Lower Suite Lvl	30	09-Aug-18	20-Sep-18	140
S4B60-5S00	Fabricate MEP Materials - Area B Lower Suite Lvl	30	09-Aug-18	20-Sep-18	173
S4C60-5S00	Fabricate MEP Materials - Area C Lower Suite Lvl	30	30-Aug-18	11-Oct-18	210
S4D60-5S00	Fabricate MEP Materials - Area D Lower Suite Lvl	30	21-Sep-18	01-Nov-18	204
200 Upper Suite Level					
S5F60-5S00	Fabricate MEP Materials - Area F Upper Suite Lvl	30	16-Aug-18	27-Sep-18	129
S5E60-5S00	Fabricate MEP Materials - Area E Upper Suite Lvl	30	16-Aug-18	27-Sep-18	144
S5A60-5S00	Fabricate MEP Materials - Area A Upper Suite Lvl	30	07-Sep-18	18-Oct-18	135
S5B60-5S00	Fabricate MEP Materials - Area B Upper Suite Lvl	30	07-Sep-18	18-Oct-18	155
S5C60-5S00	Fabricate MEP Materials - Area C Upper Suite Lvl	30	28-Sep-18	08-Nov-18	185
S5D60-5S00	Fabricate MEP Materials - Area D Upper Suite Lvl	30	19-Oct-18	03-Dec-18	159
250 Mid Bowl Mezz Level					
S6F60-5S00	Fabricate MEP Materials - Area F Upper Mezz Lvl	30	07-Sep-18	18-Oct-18	173
S6E60-5S00	Fabricate MEP Materials - Area E Upper Mezz Lvl	30	07-Sep-18	18-Oct-18	185
S6A60-5S00	Fabricate MEP Materials - Area A Upper Mezz Lvl	30	28-Sep-18	08-Nov-18	121
S6B60-5S00	Fabricate MEP Materials - Area B Upper Mezz Lvl	30	28-Sep-18	08-Nov-18	133
S6C60-5S00	Fabricate MEP Materials - Area C Upper Mezz Lvl	30	19-Oct-18	03-Dec-18	148
S6D60-5S00	Fabricate MEP Materials - Area D Upper Mezz Lvl	30	09-Nov-18	24-Dec-18	180
300 Upper Concourse					
S7F60-5S00	Fabricate MEP Materials - Area F Upper Conc	30	28-Sep-18	08-Nov-18	158
S7E60-5S00	Fabricate MEP Materials - Area E Upper Conc	30	28-Sep-18	08-Nov-18	170
S7A60-5S00	Fabricate MEP Materials - Area A Upper Conc	30	19-Oct-18	03-Dec-18	106
S7B60-5S00	Fabricate MEP Materials - Area B Upper Conc	30	19-Oct-18	03-Dec-18	118
S7C60-5S00	Fabricate MEP Materials - Area C Upper Conc	30	09-Nov-18	24-Dec-18	133
S7D60-5S00	Fabricate MEP Materials - Area D Upper Conc	30	04-Dec-18	16-Jan-19	165
400 Press Level					
S9F60-5S00	Fabricate MEP Materials - Area F Press Lvl	30	19-Oct-18	03-Dec-18	132
S9E60-5S00	Fabricate MEP Materials - Area E Press Lvl	30	19-Oct-18	03-Dec-18	132
S9A60-5S00	Fabricate MEP Materials - Area A Press Lvl	30	09-Nov-18	24-Dec-18	117
S9B60-5S00	Fabricate MEP Materials - Area B Press Lvl	30	26-Dec-18	06-Feb-19	87
S9C60-5S00	Fabricate MEP Materials - Area C Press Lvl	30	26-Dec-18	06-Feb-19	87
S9D60-5S00	Fabricate MEP Materials - Area D Press Lvl	30	26-Dec-18	06-Feb-19	87
Steel Stairs					
Stair Embed Submittals					
SS2A0-5S2AS	Stair Embeds - Subcontractor Develop/Submit Shop Drawings - Core 3 Stair	10	05-Feb-18 A	28-Feb-18 A	
SS2F0-5S2AS	Stair Embeds - Subcontractor Develop/Submit Shop Drawings - Core 2 Stair	10	05-Feb-18 A	28-Feb-18 A	
SS2B0-5S2AS	Stair Embeds - Subcontractor Develop/Submit Shop Drawings - Core 4 Stair	10	05-Mar-18	16-Mar-18	19
SS2E1-5S2AS	Stair Embeds - Subcontractor Develop/Submit Shop Drawings - Core 1 Stair	10	05-Mar-18	16-Mar-18	23
SS2E0-5S2AS	Stair Embeds - Subcontractor Develop/Submit Shop Drawings - Core 8 Stair	10	19-Mar-18	30-Mar-18	36
SS2B1-5S2AS	Stair Embeds - Subcontractor Develop/Submit Shop Drawings - Core 5 Stair	10	19-Mar-18	30-Mar-18	32
SS2C0-5S2AS	Stair Embeds - Subcontractor Develop/Submit Shop Drawings - Core 6 Stair	10	02-Apr-18	13-Apr-18	51
SS2D0-5S2AS	Stair Embeds - Subcontractor Develop/Submit Shop Drawings - Core 7 Stair	10	02-Apr-18	13-Apr-18	56
SS2A0-5S2AS1	Stair Embeds - MMCJV Review Shop Drawings - Core 3 Stair	2	28-Feb-18 A	28-Feb-18 A	
SS2F0-5S2AS1	Stair Embeds - MMCJV Review Shop Drawings - Core 2 Stair	2	28-Feb-18 A	28-Feb-18 A	
SS2B0-5S2AS1	Stair Embeds - MMCJV Review Shop Drawings - Core 4 Stair	2	19-Mar-18	20-Mar-18	19
SS2E1-5S2AS1	Stair Embeds - MMCJV Review Shop Drawings - Core 1 Stair	2	19-Mar-18	20-Mar-18	23
SS2E0-5S2AS1	Stair Embeds - MMCJV Review Shop Drawings - Core 8 Stair	2	02-Apr-18	03-Apr-18	36
SS2B1-5S2AS1	Stair Embeds - MMCJV Review Shop Drawings - Core 5 Stair	2	02-Apr-18	03-Apr-18	32
SS2C0-5S2AS1	Stair Embeds - MMCJV Review Shop Drawings - Core 6 Stair	2	16-Apr-18	17-Apr-18	51
SS2D0-5S2AS1	Stair Embeds - MMCJV Review Shop Drawings - Core 7 Stair	2	16-Apr-18	17-Apr-18	56

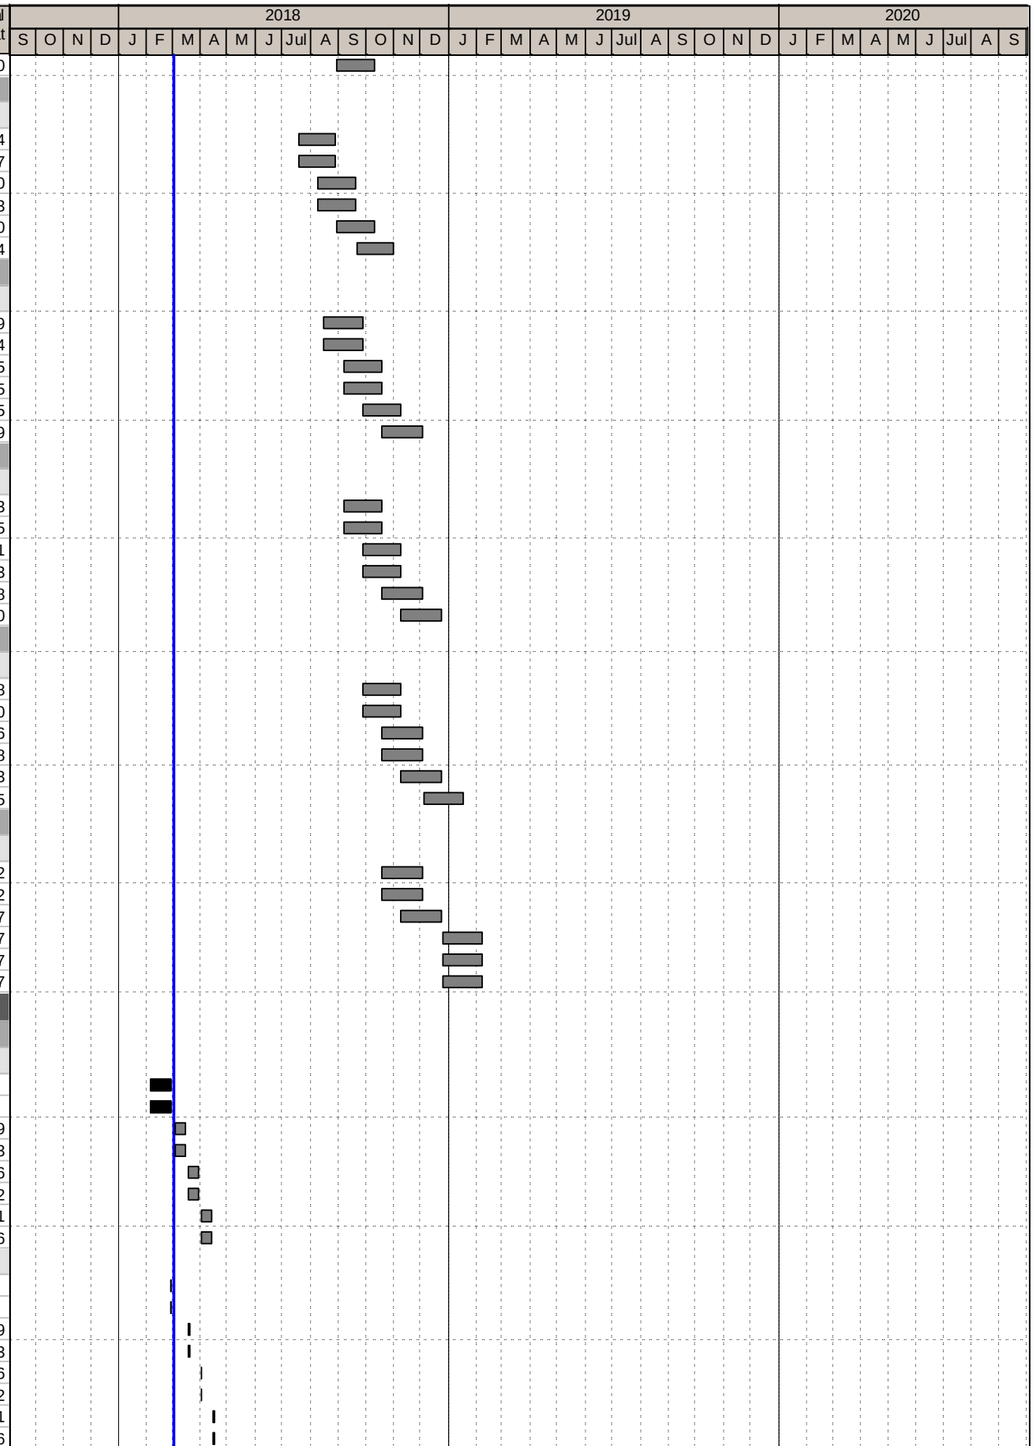

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
SS2A0-5S2AA	Stair Embeds - Design Team Review/Approve Shop Drawings - Core 3 Stair	10	01-Mar-18 A	14-Mar-18	15
SS2F0-5S2AA	Stair Embeds - Design Team Review/Approve Shop Drawings - Core 2 Stair	10	01-Mar-18 A	14-Mar-18	16
SS2B0-5S2AA	Stair Embeds - Design Team Review/Approve Shop Drawings - Core 4 Stair	10	21-Mar-18	03-Apr-18	19
SS2E1-5S2AA	Stair Embeds - Design Team Review/Approve Shop Drawings - Core 1 Stair	10	21-Mar-18	03-Apr-18	23
SS2E0-5S2AA	Stair Embeds - Design Team Review/Approve Shop Drawings - Core 8 Stair	10	04-Apr-18	17-Apr-18	36
SS2B1-5S2AA	Stair Embeds - Design Team Review/Approve Shop Drawings - Core 5 Stair	10	04-Apr-18	17-Apr-18	32
SS2C0-5S2AA	Stair Embeds - Design Team Review/Approve Shop Drawings - Core 6 Stair	10	18-Apr-18	01-May-18	51
SS2D0-5S2AA	Stair Embeds - Design Team Review/Approve Shop Drawings - Core 7 Stair	10	18-Apr-18	01-May-18	56
SS2A0-5S2AF	Stair Embeds - Fabricate - Core 3 Stair	10	15-Mar-18	28-Mar-18	15
SS2F0-5S2AF	Stair Embeds - Fabricate - Core 2 Stair	10	15-Mar-18	28-Mar-18	16
SS2B0-5S2AF	Stair Embeds - Fabricate - Core 4 Stair	10	04-Apr-18	17-Apr-18	19
SS2E1-5S2AF	Stair Embeds - Fabricate - Core 1 Stair	10	04-Apr-18	17-Apr-18	23
SS2E0-5S2AF	Stair Embeds - Fabricate - Core 8 Stair	10	18-Apr-18	01-May-18	36
SS2B1-5S2AF	Stair Embeds - Fabricate - Core 5 Stair	10	18-Apr-18	01-May-18	32
SS2C0-5S2AF	Stair Embeds - Fabricate - Core 6 Stair	10	02-May-18	15-May-18	51
SS2D0-5S2AF	Stair Embeds - Fabricate - Core 7 Stair	10	02-May-18	15-May-18	56
AHUs					
050 Lower Mezz Level					
S2A1-5T1BS	AHU - Subcontractor Prepare Shop Drawings - Lower Mezz Level Quad A (AHU-050-A-1)	10	13-Mar-18	26-Mar-18	30
S2B1-5T1BS	AHU - Subcontractor Prepare Shop Drawings - Lower Mezz Level Quad B (AHU-050-B-1)	10	13-Mar-18	26-Mar-18	25
S2A2-5T1BS	AHU - Subcontractor Prepare Shop Drawings - Lower Mezz Level Quad A (AHU-050-A-2)	10	13-Mar-18	26-Mar-18	30
S2B2-5T1BS	AHU - Subcontractor Prepare Shop Drawings - Lower Mezz Level Quad B (AHU-050-B-2)	10	13-Mar-18	26-Mar-18	25
S2A3-5T1BS	AHU - Subcontractor Prepare Shop Drawings - Lower Mezz Level Quad A (AHU-050-A-3)	10	13-Mar-18	26-Mar-18	30
S2B3-5T1BS	AHU - Subcontractor Prepare Shop Drawings - Lower Mezz Level Quad B (AHU-050-B-3)	10	13-Mar-18	26-Mar-18	25
S2B4-5T1BS	AHU - Subcontractor Prepare Shop Drawings - Lower Mezz Level Quad B (AHU-050-B-4)	10	13-Mar-18	26-Mar-18	25
S2C1-5T1BS	AHU - Subcontractor Prepare Shop Drawings - Lower Mezz Level Quad C (AHU-050-C-1)	15	20-Mar-18	09-Apr-18	75
S2D1-5T1BS	AHU - Subcontractor Prepare Shop Drawings - Lower Mezz Level Quad D (AHU-050-D-1)	15	20-Mar-18	09-Apr-18	101
S2C2-5T1BS	AHU - Subcontractor Prepare Shop Drawings - Lower Mezz Level Quad C (AHU-050-C-3)	15	20-Mar-18	09-Apr-18	75
S2A1-5T1BR	AHU - MMCJV Review Shop Dwgs - Lower Mezz Level Quad A (AHU-050-A-1)	2	27-Mar-18	28-Mar-18	30
S2B1-5T1BR	AHU - MMCJV Review Shop Dwgs - Lower Mezz Level Quad B (AHU-050-B-1)	2	27-Mar-18	28-Mar-18	25
S2A2-5T1BR	AHU - MMCJV Review Shop Dwgs - Lower Mezz Level Quad A (AHU-050-A-2)	2	27-Mar-18	28-Mar-18	30
S2B2-5T1BR	AHU - MMCJV Review Shop Dwgs - Lower Mezz Level Quad B (AHU-050-B-2)	2	27-Mar-18	28-Mar-18	25
S2A3-5T1BR	AHU - MMCJV Review Shop Dwgs - Lower Mezz Level Quad A (AHU-050-A-3)	2	27-Mar-18	28-Mar-18	30
S2B3-5T1BR	AHU - MMCJV Review Shop Dwgs - Lower Mezz Level Quad B (AHU-050-B-3)	2	27-Mar-18	28-Mar-18	25
S2B4-5T1BR	AHU - MMCJV Review Shop Dwgs - Lower Mezz Level Quad B (AHU-050-B-4)	2	27-Mar-18	28-Mar-18	25
S2C1-5T1BR	AHU - MMCJV Review Shop Dwgs - Lower Mezz Level Quad C (AHU-050-C-1)	2	10-Apr-18	11-Apr-18	75
S2D1-5T1BR	AHU - MMCJV Review Shop Dwgs - Lower Mezz Level Quad D (AHU-050-D-1)	2	10-Apr-18	11-Apr-18	101
S2C2-5T1BR	AHU - MMCJV Review Shop Dwgs - Lower Mezz Level Quad C (AHU-050-C-3)	2	10-Apr-18	11-Apr-18	75
S2A1-5T1BA	AHU - Design Team Review/Approve - Lower Mezz Level Quad A (AHU-050-A-1)	10	29-Mar-18	11-Apr-18	30
S2B1-5T1BA	AHU - Design Team Review/Approve - Lower Mezz Level Quad B (AHU-050-B-1)	10	29-Mar-18	11-Apr-18	25
S2A2-5T1BA	AHU - Design Team Review/Approve - Lower Mezz Level Quad A (AHU-050-A-2)	10	29-Mar-18	11-Apr-18	30
S2B2-5T1BA	AHU - Design Team Review/Approve - Lower Mezz Level Quad B (AHU-050-B-2)	10	29-Mar-18	11-Apr-18	25
S2A3-5T1BA	AHU - Design Team Review/Approve - Lower Mezz Level Quad A (AHU-050-A-3)	10	29-Mar-18	11-Apr-18	30
S2B3-5T1BA	AHU - Design Team Review/Approve - Lower Mezz Level Quad B (AHU-050-B-3)	10	29-Mar-18	11-Apr-18	25
S2B4-5T1BA	AHU - Design Team Review/Approve - Lower Mezz Level Quad B (AHU-050-B-4)	10	29-Mar-18	11-Apr-18	25
S2C1-5T1BA	AHU - Design Team Review/Approve - Lower Mezz Level Quad C (AHU-050-C-1)	10	12-Apr-18	25-Apr-18	75
S2D1-5T1BA	AHU - Design Team Review/Approve - Lower Mezz Level Quad D (AHU-050-D-1)	10	12-Apr-18	25-Apr-18	101
S2C2-5T1BA	AHU - Design Team Review/Approve - Lower Mezz Level Quad C (AHU-050-C-3)	10	12-Apr-18	25-Apr-18	75
S2A1-5T1BF	AHU - Subcontractor Procure - Lower Mezz Level Quad A (AHU-050-A-1)	80	12-Apr-18	03-Aug-18	30
S2B1-5T1BF	AHU - Subcontractor Procure - Lower Mezz Level Quad B (AHU-050-B-1)	80	12-Apr-18	03-Aug-18	25
S2A2-5T1BF	AHU - Subcontractor Procure - Lower Mezz Level Quad A (AHU-050-A-2)	80	12-Apr-18	03-Aug-18	30
S2B2-5T1BF	AHU - Subcontractor Procure - Lower Mezz Level Quad B (AHU-050-B-2)	80	12-Apr-18	03-Aug-18	25
S2A3-5T1BF	AHU - Subcontractor Procure - Lower Mezz Level Quad A (AHU-050-A-3)	80	12-Apr-18	03-Aug-18	30
S2B3-5T1BF	AHU - Subcontractor Procure - Lower Mezz Level Quad B (AHU-050-B-3)	80	12-Apr-18	03-Aug-18	25
S2B4-5T1BF	AHU - Subcontractor Procure - Lower Mezz Level Quad B (AHU-050-B-4)	80	12-Apr-18	03-Aug-18	25
S2C1-5T1BF	AHU - Subcontractor Procure - Lower Mezz Level Quad C (AHU-050-C-1)	80	26-Apr-18	17-Aug-18	75

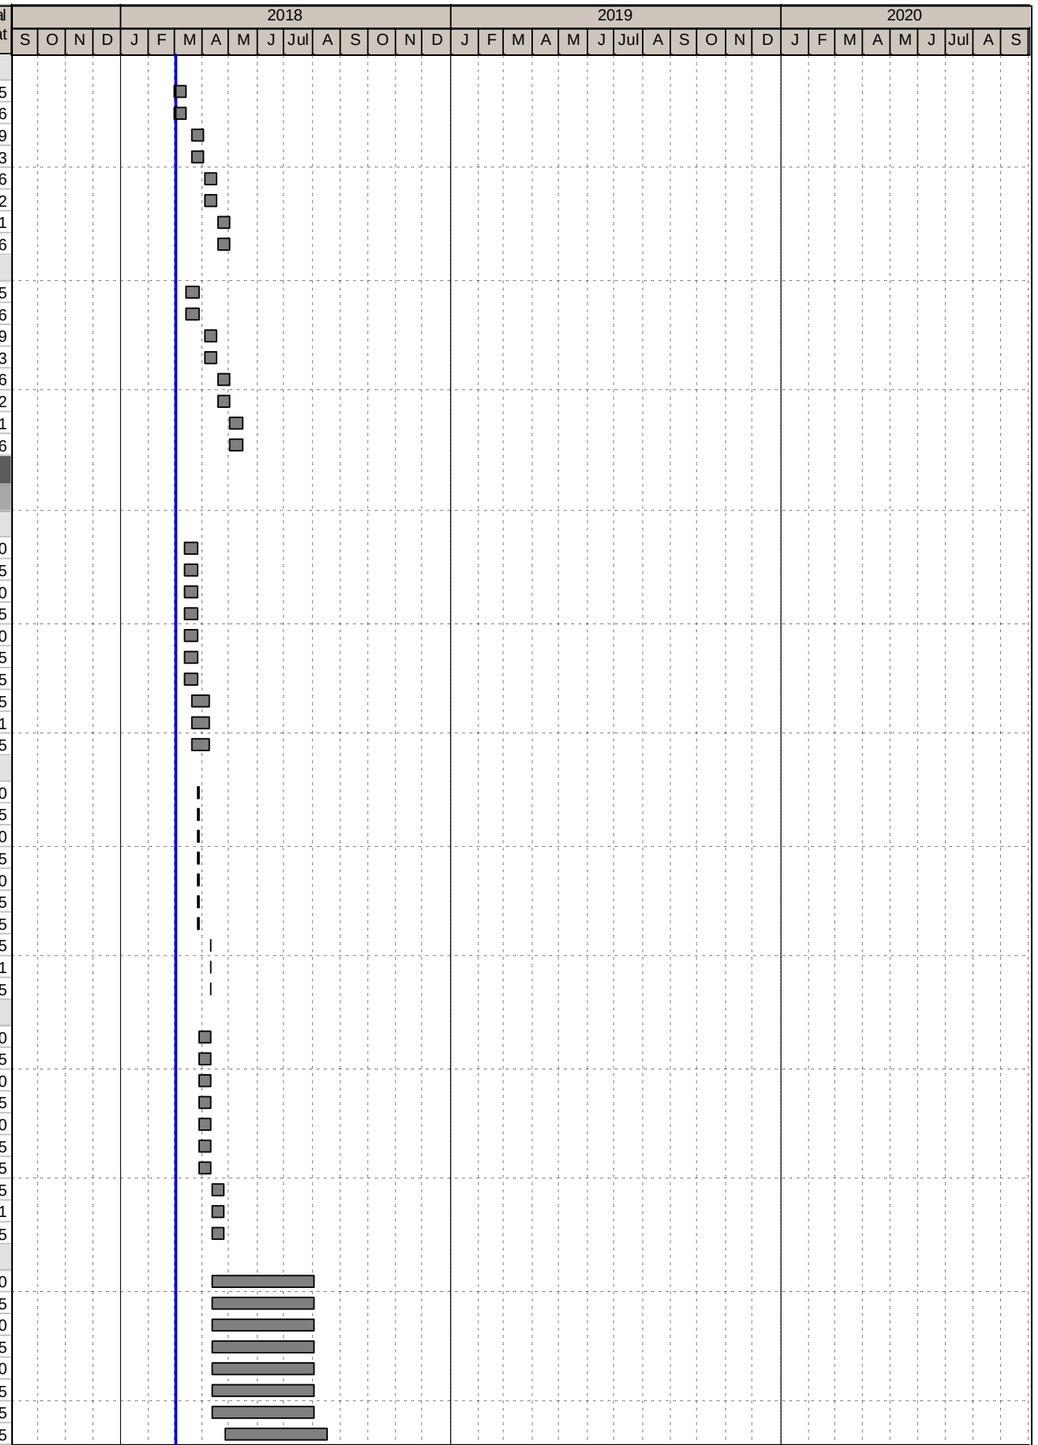

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S2D1-5T1BF	AHU - Subcontractor Procure - Lower Mezz Level Quad D (AHU-050-D-1)	80	26-Apr-18	17-Aug-18	101
S2C2-5T1BF	AHU - Subcontractor Procure - Lower Mezz Level Quad C (AHU-050-C-3)	80	26-Apr-18	17-Aug-18	75
150 Lower Suite Level					
S4A1-5T1BS	AHU - Subcontractor Prepare Shop Drawings - Lower Suite Level Quad A (AHU-150-A-1)	15	20-Mar-18	09-Apr-18	229
S4B1-5T1BS	AHU - Subcontractor Prepare Shop Drawings - Lower Suite Level Quad B (AHU-150-B-1)	15	20-Mar-18	09-Apr-18	245
S4C1-5T1BS	AHU - Subcontractor Prepare Shop Drawings - Lower Suite Level Quad C (AHU-150-C-1)	15	20-Mar-18	09-Apr-18	260
S4D1-5T1BS	AHU - Subcontractor Prepare Shop Drawings - Lower Suite Level Quad D (AHU-150-D-1)	15	20-Mar-18	09-Apr-18	264
S4A1-5T1BR	AHU - MMCJV Review Shop Dwgs - Lower Suite Level Quad A (AHU-150-A-1)	2	10-Apr-18	11-Apr-18	229
S4B1-5T1BR	AHU - MMCJV Review Shop Dwgs - Lower Suite Level Quad B (AHU-150-B-1)	2	10-Apr-18	11-Apr-18	245
S4C1-5T1BR	AHU - MMCJV Review Shop Dwgs - Lower Suite Level Quad C (AHU-150-C-1)	2	10-Apr-18	11-Apr-18	260
S4D1-5T1BR	AHU - MMCJV Review Shop Dwgs - Lower Suite Level Quad D (AHU-150-D-1)	2	10-Apr-18	11-Apr-18	264
S4A1-5T1BA	AHU - Design Team Review/Approve - Lower Suite Level Quad A (AHU-150-A-1)	10	12-Apr-18	25-Apr-18	229
S4B1-5T1BA	AHU - Design Team Review/Approve - Lower Suite Level Quad B (AHU-150-B-1)	10	12-Apr-18	25-Apr-18	245
S4C1-5T1BA	AHU - Design Team Review/Approve - Lower Suite Level Quad C (AHU-150-C-1)	10	12-Apr-18	25-Apr-18	260
S4D1-5T1BA	AHU - Design Team Review/Approve - Lower Suite Level Quad D (AHU-150-D-1)	10	12-Apr-18	25-Apr-18	264
S4A1-5T1BF	AHU - Subcontractor Procure - Lower Suite Level Quad A (AHU-150-A-1)	80	26-Apr-18	17-Aug-18	229
S4B1-5T1BF	AHU - Subcontractor Procure - Lower Suite Level Quad B (AHU-150-B-1)	80	26-Apr-18	17-Aug-18	245
S4C1-5T1BF	AHU - Subcontractor Procure - Lower Suite Level Quad C (AHU-150-C-1)	80	26-Apr-18	17-Aug-18	260
S4D1-5T1BF	AHU - Subcontractor Procure - Lower Suite Level Quad D (AHU-150-D-1)	80	26-Apr-18	17-Aug-18	264
250 Mid Bowl Mezz Level					
S6A1-5T1BS	AHU - Subcontractor Prepare Shop Drawings - Mid Bowl Mezz Level Quad A (AHU-250-A-1)	15	20-Mar-18	09-Apr-18	119
S6B1-5T1BS	AHU - Subcontractor Prepare Shop Drawings - Mid Bowl Mezz Level Quad B (AHU-250-B-1)	15	20-Mar-18	09-Apr-18	112
S6C1-5T1BS	AHU - Subcontractor Prepare Shop Drawings - Mid Bowl Mezz Level Quad C (AHU-250-C-1)	15	20-Mar-18	09-Apr-18	139
S6D1-5T1BS	AHU - Subcontractor Prepare Shop Drawings - Mid Bowl Mezz Level Quad D (AHU-250-D-1)	15	20-Mar-18	09-Apr-18	143
S6A2-5T1BS	AHU - Subcontractor Prepare Shop Drawings - Mid Bowl Mezz Level Quad A (AHU-250-A-2)	15	20-Mar-18	09-Apr-18	119
S6B2-5T1BS	AHU - Subcontractor Prepare Shop Drawings - Mid Bowl Mezz Level Quad B (AHU-250-B-2)	15	20-Mar-18	09-Apr-18	112
S6A1-5T1BR	AHU - MMCJV Review Shop Dwgs - Mid Bowl Mezz Level Quad A (AHU-250-A-1)	2	10-Apr-18	11-Apr-18	119
S6B1-5T1BR	AHU - MMCJV Review Shop Dwgs - Mid Bowl Mezz Level Quad B (AHU-250-B-1)	2	10-Apr-18	11-Apr-18	112
S6C1-5T1BR	AHU - MMCJV Review Shop Dwgs - Mid Bowl Mezz Level Quad C (AHU-250-C-1)	2	10-Apr-18	11-Apr-18	139
S6D1-5T1BR	AHU - MMCJV Review Shop Dwgs - Mid Bowl Mezz Level Quad D (AHU-250-D-1)	2	10-Apr-18	11-Apr-18	143
S6A2-5T1BR	AHU - MMCJV Review Shop Dwgs - Mid Bowl Mezz Level Quad A (AHU-250-A-2)	2	10-Apr-18	11-Apr-18	119
S6B2-5T1BR	AHU - MMCJV Review Shop Dwgs - Mid Bowl Mezz Level Quad B (AHU-250-B-2)	2	10-Apr-18	11-Apr-18	112
S6A1-5T1BA	AHU - Design Team Review/Approve - Mid Bowl Mezz Level Quad A (AHU-250-A-1)	10	12-Apr-18	25-Apr-18	119
S6B1-5T1BA	AHU - Design Team Review/Approve - Mid Bowl Mezz Level Quad B (AHU-250-B-1)	10	12-Apr-18	25-Apr-18	112
S6C1-5T1BA	AHU - Design Team Review/Approve - Mid Bowl Mezz Level Quad C (AHU-250-C-1)	10	12-Apr-18	25-Apr-18	139
S6D1-5T1BA	AHU - Design Team Review/Approve - Mid Bowl Mezz Level Quad D (AHU-250-D-1)	10	12-Apr-18	25-Apr-18	143
S6A2-5T1BA	AHU - Design Team Review/Approve - Mid Bowl Mezz Level Quad A (AHU-250-A-2)	10	12-Apr-18	25-Apr-18	119
S6B2-5T1BA	AHU - Design Team Review/Approve - Mid Bowl Mezz Level Quad B (AHU-250-B-2)	10	12-Apr-18	25-Apr-18	112
S6A1-5T1BF	AHU - Subcontractor Procure - Mid Bowl Mezz Level Quad A (AHU-250-A-1)	80	26-Apr-18	17-Aug-18	119
S6B1-5T1BF	AHU - Subcontractor Procure - Mid Bowl Mezz Level Quad B (AHU-250-B-1)	80	26-Apr-18	17-Aug-18	112
S6C1-5T1BF	AHU - Subcontractor Procure - Mid Bowl Mezz Level Quad C (AHU-250-C-1)	80	26-Apr-18	17-Aug-18	139
S6D1-5T1BF	AHU - Subcontractor Procure - Mid Bowl Mezz Level Quad D (AHU-250-D-1)	80	26-Apr-18	17-Aug-18	143
S6A2-5T1BF	AHU - Subcontractor Procure - Mid Bowl Mezz Level Quad A (AHU-250-A-2)	80	26-Apr-18	17-Aug-18	119
S6B2-5T1BF	AHU - Subcontractor Procure - Mid Bowl Mezz Level Quad B (AHU-250-B-2)	80	26-Apr-18	17-Aug-18	112
350 Upper Mezz Level					
S8A1-5T1BS	AHU - Subcontractor Prepare Shop Drawings - Upper Mezz Level Quad A (AHU-350-A-1)	15	20-Mar-18	09-Apr-18	116
S8B1-5T1BS	AHU - Subcontractor Prepare Shop Drawings - Upper Mezz Level Quad B (AHU-350-B-1)	15	20-Mar-18	09-Apr-18	107
S8C1-5T1BS	AHU - Subcontractor Prepare Shop Drawings - Upper Mezz Level Quad C (AHU-350-C-1)	15	20-Mar-18	09-Apr-18	171
S8D1-5T1BS	AHU - Subcontractor Prepare Shop Drawings - Upper Mezz Level Quad D (AHU-350-D-1)	15	20-Mar-18	09-Apr-18	171
S8A1-5T1BR	AHU - MMCJV Review Shop Dwgs - Upper Mezz Level Quad A (AHU-350-A-1)	2	10-Apr-18	11-Apr-18	116
S8B1-5T1BR	AHU - MMCJV Review Shop Dwgs - Upper Mezz Level Quad B (AHU-350-B-1)	2	10-Apr-18	11-Apr-18	107

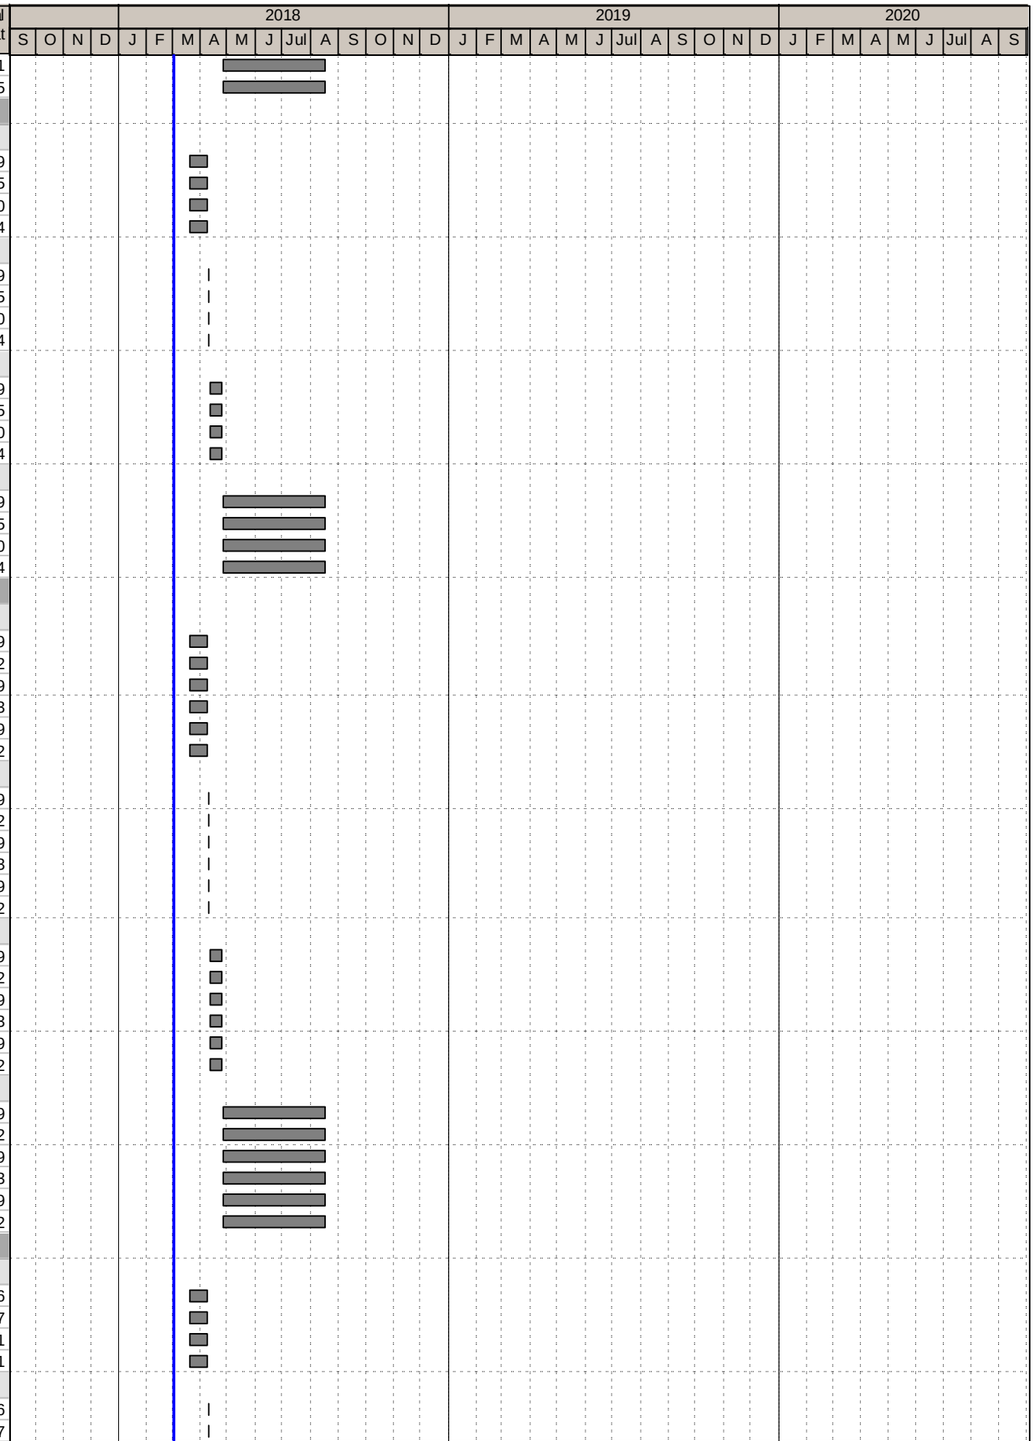

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S8C1-5T1BR	AHU - MMCJV Review Shop Dwgs - Upper Mezz Level Quad C (AHU-350-C-1)	2	10-Apr-18	11-Apr-18	171
S8D1-5T1BR	AHU - MMCJV Review Shop Dwgs - Upper Mezz Level Quad D (AHU-350-D-1)	2	10-Apr-18	11-Apr-18	171
S8A1-5T1BA	AHU - Design Team Review/Approve - Upper Mezz Level Quad A (AHU-350-A-1)	10	12-Apr-18	25-Apr-18	116
S8B1-5T1BA	AHU - Design Team Review/Approve - Upper Mezz Level Quad B (AHU-350-B-1)	10	12-Apr-18	25-Apr-18	107
S8C1-5T1BA	AHU - Design Team Review/Approve - Upper Mezz Level Quad C (AHU-350-C-1)	10	12-Apr-18	25-Apr-18	171
S8D1-5T1BA	AHU - Design Team Review/Approve - Upper Mezz Level Quad D (AHU-350-D-1)	10	12-Apr-18	25-Apr-18	171
S8A1-5T1BF	AHU - Subcontractor Procure - Upper Mezz Level Quad A (AHU-350-A-1)	80	26-Apr-18	17-Aug-18	116
S8B1-5T1BF	AHU - Subcontractor Procure - Upper Mezz Level Quad B (AHU-350-B-1)	80	26-Apr-18	17-Aug-18	107
S8C1-5T1BF	AHU - Subcontractor Procure - Upper Mezz Level Quad C (AHU-350-C-1)	80	26-Apr-18	17-Aug-18	171
S8D1-5T1BF	AHU - Subcontractor Procure - Upper Mezz Level Quad D (AHU-350-D-1)	80	26-Apr-18	17-Aug-18	171
400 Press Level					
S9A1-5T1BS	AHU - Subcontractor Prepare Shop Drawings - Press Level Quad A (AHU-400-A-1)	15	20-Mar-18	09-Apr-18	127
S9A1-5T1BR	AHU - MMCJV Review Shop Dwgs - Press Level Quad A (AHU-400-A-1)	2	10-Apr-18	11-Apr-18	127
S9A1-5T1BA	AHU - Design Team Review/Approve - Press Level Quad A (AHU-400-A-1)	10	12-Apr-18	25-Apr-18	127
S9A1-5T1BF	AHU - Subcontractor Procure - Press Level Quad A (AHU-400-A-1)	80	26-Apr-18	17-Aug-18	127
Drywall and Interior Finishes					
S00-5P5P230	Submit/Approve/Procure - Rough-in	176	02-Oct-18	11-Jun-19	49
S00-5P5P50	Submit/Approve/Procure - Interior Finishes	176	04-Jan-19	11-Sep-19	34
S00-5P5P240	Submit/Approve/Procure - Hardscape and Landscape	176	01-Mar-19	06-Nov-19	10
Construction					
Set-Up Office Trailer					
Trailer City					
ST00-8L101	Trailer City - Approval to Proceed	1	20-Nov-17 A	20-Nov-17 A	
ST00-8L105	Trailer City - Site Clear & Grub	2	20-Nov-17 A	20-Nov-17 A	
ST00-8L106	Trailer City - Scarify / Compact	3	21-Nov-17 A	27-Nov-17 A	
ST00-8L103	Trailer City - Layout Water / Site	3	06-Dec-17 A	08-Dec-17 A	
ST00-8L107	Trailer City - Sub-Grade Site	13	22-Nov-17 A	11-Dec-17 A	
ST00-8L102	Trailer City - Temp Hydrant / Testing / B-Test	5	11-Dec-17 A	19-Dec-17 A	
ST00-8L154	Trailer City - Setup Traffic Control for Off Site Water/Sewer	1	02-Jan-18 A	02-Jan-18 A	
ST00-8L153	Trailer City - Trench Storm Drains (E/W)	3	28-Dec-17 A	08-Jan-18 A	
ST00-8L155	Trailer City - Trench Storm Drains (N/S)	3	05-Jan-18 A	08-Jan-18 A	
ST00-8L156	Trailer City - Trench Fire Line (E/W)	1	17-Jan-18 A	17-Jan-18 A	
ST00-8L157	Trailer City - Trench Fire Line (N/S)	3	17-Jan-18 A	18-Jan-18 A	
ST00-8L109	Trailer City - Domestic / Fire LInes Loop / Testing / B-Test	20	14-Dec-17 A	20-Jan-18 A	
ST00-8L104	Trailer City - Off-Site Water (LVVWD)	10	16-Jan-18 A	26-Jan-18 A	
ST00-8L111	Trailer City - Sewer Lines	10	03-Jan-18 A	26-Jan-18 A	
ST00-8L108	Trailer City - Install Drive Approach	5	26-Jan-18 A	30-Jan-18 A	
ST00-8L112	Trailer City - Install Millings	3	30-Jan-18 A	01-Feb-18 A	
ST00-8L114	Trailer City - Dust Palliative	1	02-Feb-18 A	02-Feb-18 A	
ST00-8L116	Trailer City - Trailer Installation (15-28)	15	27-Nov-17 A	18-Dec-17 A	
ST00-8L115	Trailer City - Trailer Deliveries & Store on Site	31	20-Nov-17 A	02-Jan-18 A	
ST00-8L117	Trailer City - Trailer Installation (1-14)	11	19-Dec-17 A	03-Jan-18 A	
ST00-8L118	Trailer City - Trailer Installation Inspection	1	16-Jan-18 A	16-Jan-18 A	
ST00-8L119	Trailer City - Housing Authority Inspections	1	16-Jan-18 A	16-Jan-18 A	
ST00-8L120	Trailer City - Fire Marshall Inspection	1	07-Feb-18 A	07-Feb-18 A	
ST00-8L122	Trailer City - Electrical Layout	1	28-Nov-17 A	28-Nov-17 A	
ST00-8L123	Trailer City - Trenching for NVE Primary & Secondary	5	30-Nov-17 A	06-Dec-17 A	
ST00-8L146	Trailer City - Install Conduits to N side of Entrance	5	30-Nov-17 A	06-Dec-17 A	
ST00-8L125	Trailer City - Excavate for RS-82 Pullbox	1	07-Dec-17 A	07-Dec-17 A	

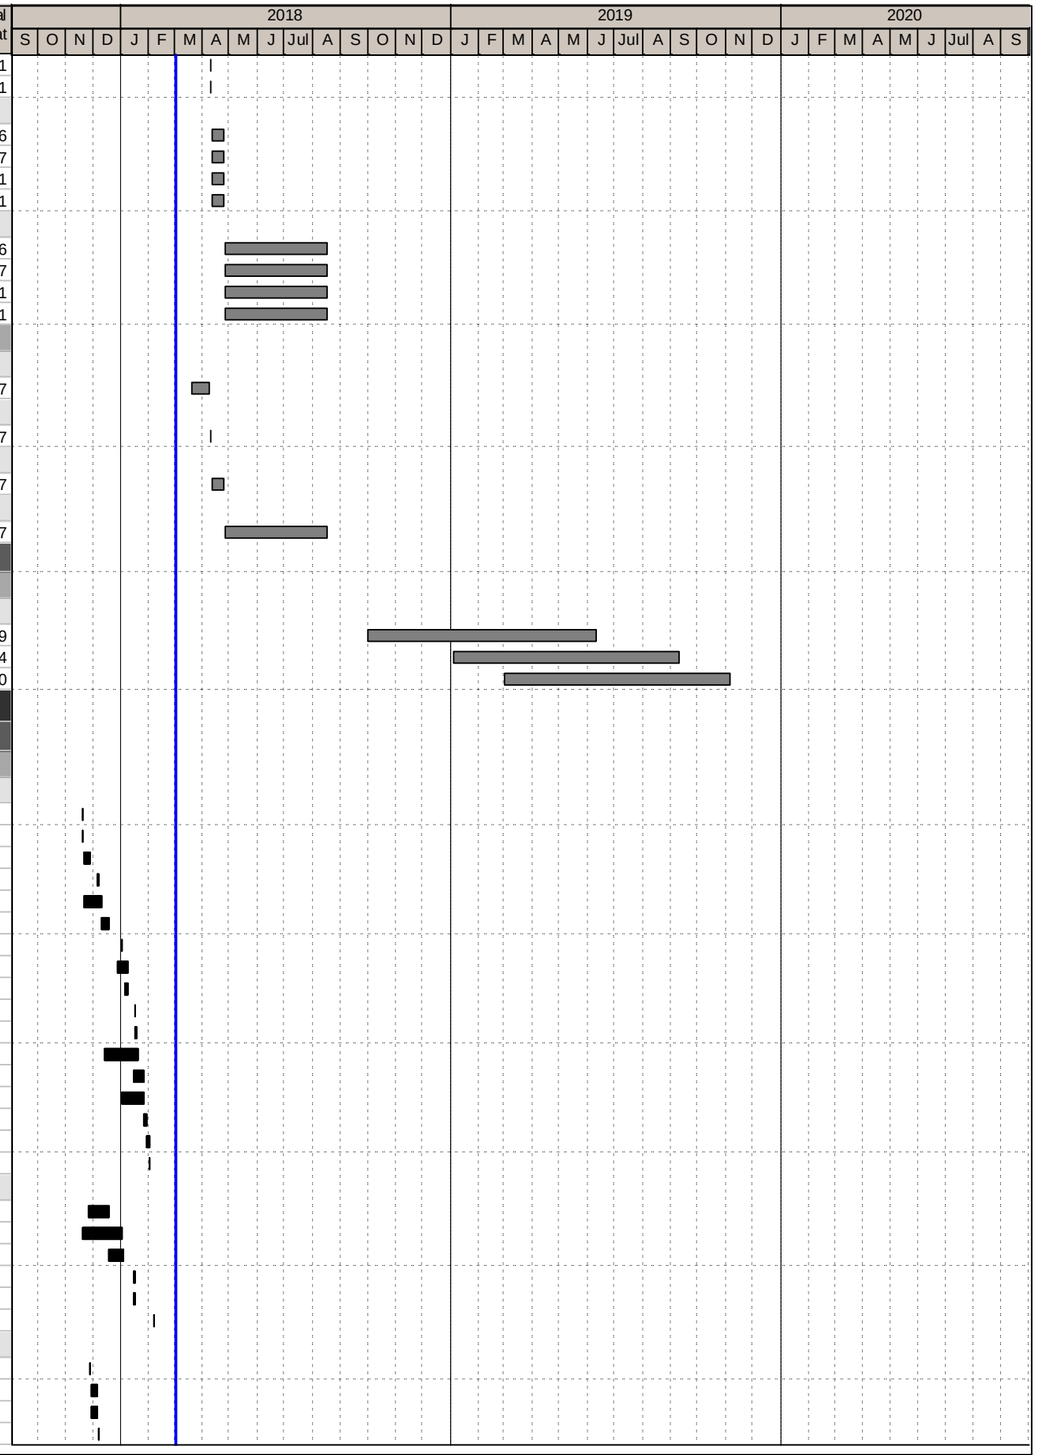

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
ST00-8L126	Trailer City - Install U/G RS-82 Pullbox	1	08-Dec-17 A	08-Dec-17 A	
ST00-8L124	Trailer City - Water Trenching	1	08-Dec-17 A	08-Dec-17 A	
ST00-8L127	Trailer City - Trench Sand Bed	2	28-Nov-17 A	12-Dec-17 A	
ST00-8L128	Trailer City - Install NVE Raceways	5	05-Dec-17 A	12-Dec-17 A	
ST00-8L149	Trailer City - As-built Drawings to NVE	2	18-Dec-17 A	19-Dec-17 A	
ST00-8L150	Trailer City - Call for Inspection (NVE Raceways)	1	22-Dec-17 A	22-Dec-17 A	
ST00-8L140	Trailer City - Trench & Install Domestic Mains	8	12-Dec-17 A	19-Dec-17 A	
ST00-8L152	Trailer City - Install Batch Plant Raceway across Russell Ramp	1	08-Jan-18 A	08-Jan-18 A	
ST00-8L165	Trailer City - Exc & Sand & Conduit (E/W Trench) Russell Ramp	3	05-Jan-18 A	08-Jan-18 A	
ST00-8L166	Trailer City - NVE Inspection (E/W Trench) Russell Ramp	1	10-Jan-18 A	10-Jan-18 A	
ST00-8L167	Trailer City - Sand & Native (E/W Trench) Russell Ramp	1	11-Jan-18 A	11-Jan-18 A	
ST00-8L168	Trailer City - NVE Inspection (E/W Trench) Russell Ramp (FINAL)	1	12-Jan-18 A	12-Jan-18 A	
ST00-8L169	Trailer City - Backfill (E/W Trench) Russell Ramp	1	13-Jan-18 A	13-Jan-18 A	
ST00-8L171	Trailer City - Exc & Sand & Conduit (E/W Trench Russell Ramp to TC PB)	3	12-Jan-18 A	13-Jan-18 A	
ST00-8L200	Trailer City - Exc & Sand & Conduit (E/W Trench TC PB to TC SG)	4	13-Jan-18 A	15-Jan-18 A	
ST00-8L172	Trailer City - NVE Inspection (E/W Trench Russell Ramp to TC PB)	1	16-Jan-18 A	16-Jan-18 A	
ST00-8L174	Trailer City - NVE Inspection (E/W Trench Russell Ramp to TC PB) (FINAL)	1	16-Jan-18 A	16-Jan-18 A	
ST00-8L201	Trailer City - NVE Inspection (E/W Trench TC PB to TC SG)	1	16-Jan-18 A	16-Jan-18 A	
ST00-8L170	Trailer City - Backfill Russell Ramp	3	15-Jan-18 A	17-Jan-18 A	
ST00-8L173	Trailer City - 12" Sand (E/W Trench Russell Ramp to TC PB)	1	16-Jan-18 A	17-Jan-18 A	
ST00-8L175	Trailer City - Backfill (E/W Trench Russell Ramp to TC PB)	2	16-Jan-18 A	17-Jan-18 A	
ST00-8L176	Trailer City - Bring Area to Grade (E/W Trench Ex Russell XFMR to TC SG)	1	18-Jan-18 A	18-Jan-18 A	
ST00-8L202	Trailer City - 12" Sand (E/W Trench TC PB to TC SG)	1	17-Jan-18 A	18-Jan-18 A	
ST00-8L204	Trailer City - Backfill (E/W Trench TC PB to TC SG)	1	17-Jan-18 A	18-Jan-18 A	
ST00-8L177	Trailer City - Set Precast Pads for Transformer & Switchgear (E/W Trench Ex Russell XFMR to TC SG)	1	19-Jan-18 A	19-Jan-18 A	
ST00-8L193	Trailer City - Set Switchgear for Trailer City	1	19-Jan-18 A	20-Jan-18 A	
ST00-8L196	Trailer City - Mandrel & Mule Tape (E/W Trench Ex Russell XFMR to TC SG)	1	23-Jan-18 A	23-Jan-18 A	
ST00-8L195	Trailer City - Clark County Inspection on Trailer City Swtichgear (E-Tag for Trailer Power)	1	25-Jan-18 A	25-Jan-18 A	
ST00-8L197	Trailer City - NVE Final Inspection (E/W Trench Ex Russell XFMR to TC SG)	1	25-Jan-18 A	25-Jan-18 A	
ST00-8L194	Trailer City - Install Bollards	1	27-Jan-18 A	27-Jan-18 A	
ST00-8L198	Trailer City - NVE Set Transformer & Pull/Terminate (Trailer Switchgear)	5	29-Jan-18 A	29-Jan-18 A	
ST00-8L199	Trailer City - NVE Set Meters and Energize (Trailer Switchgear)	1	31-Jan-18 A	31-Jan-18 A	
ST00-8L148	Trailer City - Trench & Install Domestic to Trailer	4	04-Jan-18 A	12-Jan-18 A	
ST00-8L141	Trailer City - Trench & Install SS to Main/Trailers	5	15-Jan-18 A	23-Jan-18 A	
ST00-8L110	Trailer City - Fire Connection to Trailer Risers	3	29-Jan-18 A	31-Jan-18 A	
ST00-8L142	Trailer City - Move Furniture into Site Office	7	22-Jan-18 A	06-Feb-18 A	
ST00-8L143	Trailer City - Start Occupying Site Office	1	08-Feb-18 A	08-Feb-18 A	
ST00-8L139	Trailer City - LV & Data Installation (By Others)	1	31-Jan-18 A	06-Feb-18 A	
Crawler Crane In-Place					
S0B2-8L30	Crane in Place - Concrete 2 (Area F)	94	09-Mar-18	20-Jul-18	12
S0B1-8L30	Crane in Place - Concrete 1 (Area A)	96	09-Mar-18	24-Jul-18	4
S0B4-8L30	Crane in Place - Concrete 4 (Area E)	123	06-Apr-18	28-Sep-18	6
S0B3-8L30	Crane in Place - Concrete 3 (Area B)	132	28-Mar-18	02-Oct-18	8
S0B4-8L40	Crane in Place - Concrete 6 (Area D)	120	17-May-18	05-Nov-18	9
S0B3-8L40	Crane in Place - Concrete 5 (Area C)	130	04-May-18	06-Nov-18	9
S0B1-8L40	Crane in Place - Concrete Core Walls (Core 3 & 4)	30	21-Jun-18	02-Aug-18	7
S0B1-8L50	Crane in Place - Concrete Core Walls (Core 2 & 1)	57	19-Jun-18	07-Sep-18	11
S0B1-8L60	Crane in Place - Concrete Core Walls (Core 5 & 6)	45	04-Sep-18	05-Nov-18	4
S0B1-8L70	Crane in Place - Concrete Core Walls (Core 8 & 7)	45	04-Sep-18	05-Nov-18	17
S0BA-8L41	Crane in Place - Precast 4 (CC-DD)	23	12-Sep-18	12-Oct-18	8
S0BC-8L40	Crane in Place - Precast 2 (F to D Upper Bowls)	69	17-Jan-19	24-Apr-19	4
S0BA-8L42	Crane in Place - Precast 5 (A to B, F to E Suite Levels)	103	28-Nov-18	24-Apr-19	0

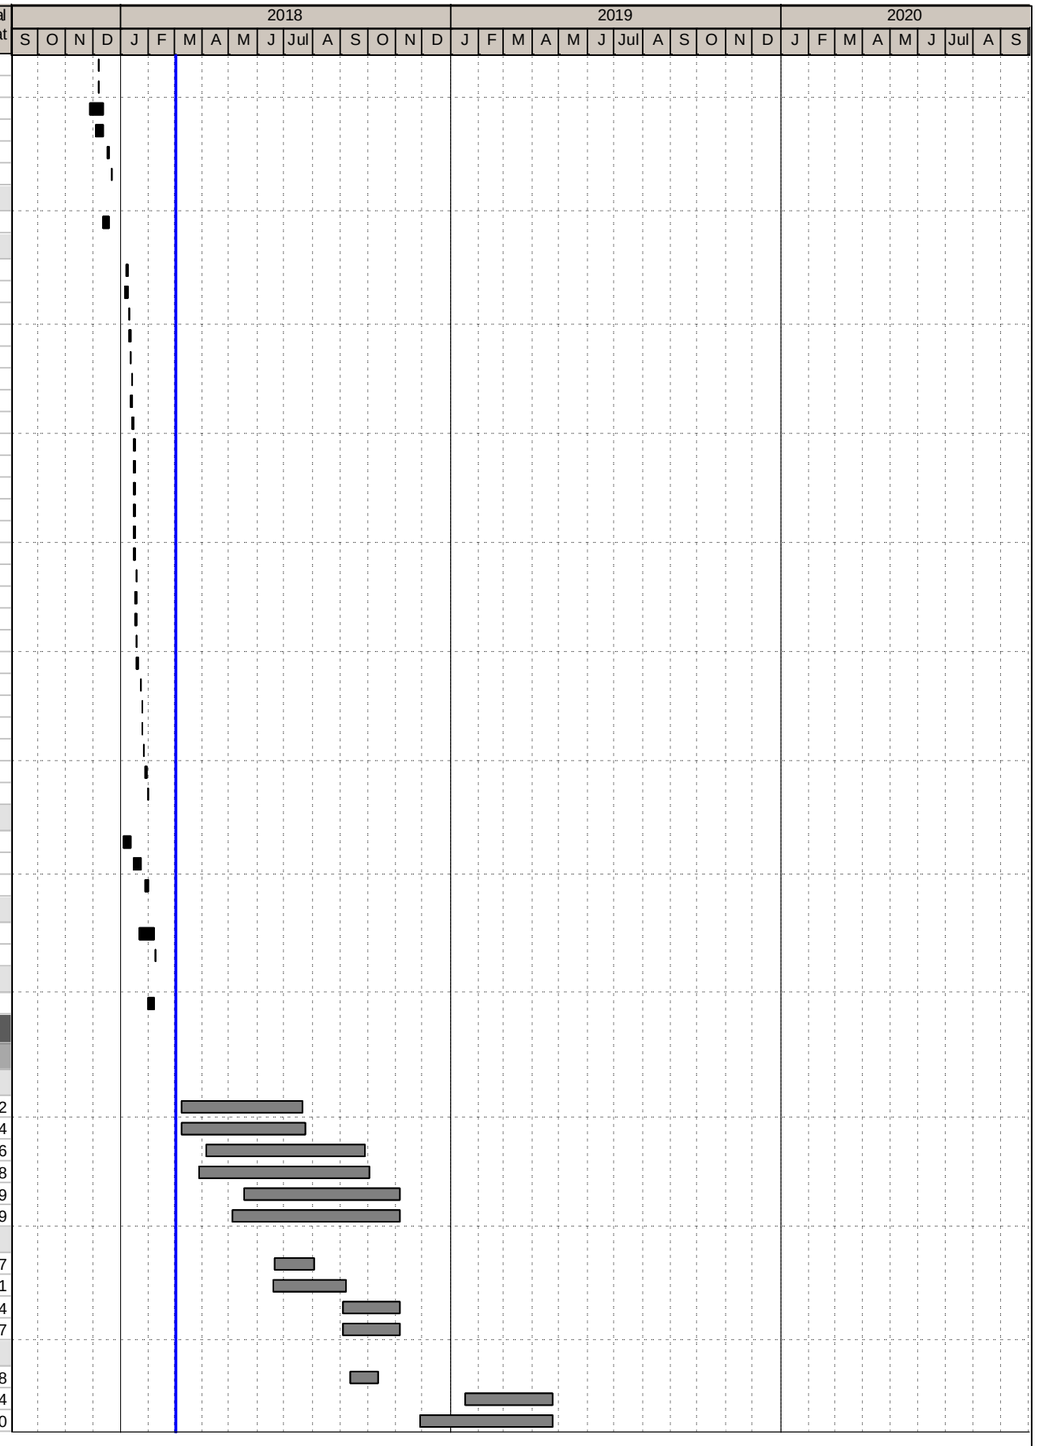

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S0BA-8L40	Crane in Place - Precast 1 (A to C Upper Bowls)	94	17-Dec-18	30-Apr-19	0
S0BC-8L50	Crane in Place - Precast 3 (Lower Bowl)	30	10-Sep-19	21-Oct-19	0
S0B5-8L80	Crane in Place - Steel Truss Column Erection 1 (A to C)	67	09-Aug-18	13-Nov-18	4
S0B5-8L50	Crane in Place - Steel Truss Column Assembly 1 (A to C)	96	11-Jul-18	27-Nov-18	10
S0B5-8L90	Crane in Place - Steel Truss Column Erection 2 (F to D)	61	29-Aug-18	27-Nov-18	9
S0B5-8L70	Crane in Place - Steel Truss Column Assembly 2 (F to D)	82	08-Aug-18	05-Dec-18	24
S0B5-8L100	Crane in Place - Steel Long Span at Operable Field Assembly	45	16-Oct-18	20-Dec-18	9
S0B5-8L110	Crane in Place - Steel Long Span at Operable Field Erect	34	06-Nov-18	27-Dec-18	9
S0B6-8L50	Crane in Place - Steel Concourses 2 (F to D)	74	27-Sep-18	15-Jan-19	9
S0B5-8L60	Crane in Place - Steel Concourses 1 (A to C)	81	27-Sep-18	24-Jan-19	9
S0B8-8L50	Crane in Place - Steel Concourses 3 (A to C)	51	09-Nov-18	25-Jan-19	20
S0B7-8L50	Crane in Place - Steel Concourses 4 (F to D)	57	26-Nov-18	14-Feb-19	9
S0B9-8L90	Crane in Place - Steel Roof Canopy Preassembly 2 (F to D)	82	13-Dec-18	10-Apr-19	9
S0BD-8L90	Crane in Place - Steel Roof Canopy Preassembly 1 (A to C)	91	11-Dec-18	19-Apr-19	9
S0BB-8L90	Crane in Place - Steel Roof Canopy Erect (A to C)	79	02-Jan-19	23-Apr-19	9
S0BB-8L100	Crane in Place - Steel Roof Canopy Erect (F to D)	88	03-Jan-19	07-May-19	9
Temporary Utilities					
Stadium Temp Power					
ST00-8L159	Stadium Temp Power - NVE Provide Revised Drawings	5	05-Jan-18 A	09-Jan-18 A	
ST00-8L113	Stadium Temp Power - Exc & Sand and Install Conduit from Pull Box to NVE Equip (N/S Trench 90+00 to PB)	5	09-Jan-18 A	15-Jan-18 A	
ST00-8L129	Stadium Temp Power - NVE Inspection on N/S (90+00 to Stadium PB)	1	16-Jan-18 A	16-Jan-18 A	
ST00-8L158	Stadium Temp Power - Staking & Layout of NVE Equip	1	16-Jan-18 A	17-Jan-18 A	
ST00-8L160	Stadium Temp Power - 12" Sand (90+00 to Stadium PB)	1	17-Jan-18 A	18-Jan-18 A	
ST00-8L205	Stadium Temp Power - Exc & Sand and Install Conduit from Pull Box to NVE Equip (N/S at Stadium SG)	3	18-Jan-18 A	20-Jan-18 A	
ST00-8L162	Stadium Temp Power - Complete Backfill of Primary Run (90+00 to Stadium PB)	1	22-Jan-18 A	22-Jan-18 A	
ST00-8L206	Stadium Temp Power - NVE Inspection on N/S (N/S at Stadium SG)	1	22-Jan-18 A	22-Jan-18 A	
ST00-8L207	Stadium Temp Power - 12" Sand (N/S at Stadium SG)	1	24-Jan-18 A	24-Jan-18 A	
ST00-8L208	Stadium Temp Power - NVE Inspection (N/S at Stadium SG) (FINAL)	1	26-Jan-18 A	26-Jan-18 A	
ST00-8L209	Stadium Temp Power - Complete Backfill of Primary Run (N/S at Stadium SG)	1	26-Jan-18 A	29-Jan-18 A	
ST00-8L130	Stadium Temp Power - Set Precast Pads for Transformer & Switchgear (N/S 90+00 to Stadium Switchgear)	1	30-Jan-18 A	30-Jan-18 A	
ST00-8L163	Stadium Temp Power - Set Switchgear (N/S 90+00 to Stadium Switchgear)	1	30-Jan-18 A	31-Jan-18 A	
ST00-8L132	Stadium Temp Power - Clark County Inspection on Stadium Switchgear (E-Tag for Stadium Power)	1	01-Feb-18 A	01-Feb-18 A	
ST00-8L164	Stadium Temp Power - Install Bollards at Transformer & Switchgear	3	01-Feb-18 A	01-Feb-18 A	
ST00-8L144	Stadium Temp Power - NVE Final Inspection - Witness Mandrel	1	02-Feb-18 A	02-Feb-18 A	
ST00-8L145	Stadium Temp Power - Mandrell & Mule Tape (N/S 90+00 to Stadium Switchgear)	1	02-Feb-18 A	02-Feb-18 A	
ST00-8L131	Stadium Temp Power - NVE Set Transformer & Pull/Terminate (90+00 to Stadium Switchgear)	4	12-Feb-18 A	15-Feb-18 A	
ST00-8L133	Stadium Temp Power - Set Meters and Energize for Stadium Switchgear	1	12-Mar-18	12-Mar-18	26
ST00-8L186	Stadium Temp Power - Exc & Sand & Conduit (N/S 90+00 South to Perm Pull Box RS82)	2	15-Jan-18 A	16-Jan-18 A	
ST00-8L187	Stadium Temp Power - NVE Inspection (N/S 90+00 South to Perm Pull Box RS82)	1	17-Jan-18 A	17-Jan-18 A	
ST00-8L188	Stadium Temp Power - 12" Sand (N/S 90+00 South to Perm Pull Box RS82)	1	18-Jan-18 A	19-Jan-18 A	
ST00-8L190	Stadium Temp Power - Backfill (N/S 90+00 South to Perm Pull Box RS82)	2	20-Jan-18 A	20-Jan-18 A	
ST00-8L191	Stadium Temp Power - Mandrel & Mule Tape (N/S 90+00 South to Perm Pull Box RS82)	1	22-Jan-18 A	22-Jan-18 A	
ST00-8L192	Stadium Temp Power - Bring Area to Grade (N/S 90+00 South to Perm Pull Box RS82)	3	24-Jan-18 A	24-Jan-18 A	
ST00-8L178	Stadium Temp Power - Exc & Sand & Conduit (N/S Tie In to Existing RS 82 68+00)	1	03-Jan-18 A	03-Jan-18 A	
ST00-8L180	Stadium Temp Power - Sand & Native (N/S Tie In to Existing RS 82 68+00)	1	19-Jan-18 A	19-Jan-18 A	
ST00-8L182	Stadium Temp Power - Backfill (N/S Tie In to Existing RS 82 68+00)	1	19-Jan-18 A	19-Jan-18 A	
ST00-8L183	Stadium Temp Power - Coordinate w/ NVE Tie-in with Existing for Tie-in Requirements	2	19-Jan-18 A	19-Jan-18 A	
ST00-8L184	Stadium Temp Power - Complete Tie-in with Existing	2	19-Jan-18 A	19-Jan-18 A	
ST00-8L185	Stadium Temp Power - Mandrel & Mule Tape (N/S Tie In to Existing RS 82 68+00)	1	23-Jan-18 A	23-Jan-18 A	
Site Preparation and Excavation					
S1F-8M7100	Demo & Site Preparation	15	19-Dec-17 A	27-Dec-17 A	

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S1F-8M7790	Box Culvert - Begin Road Shutdown and Box Culvert Work in Polaris	0	09-Mar-18		43
S1F-8M7793	Box Culvert - Expose Phase 2 Box Culvert	0	19-Mar-18		46
S1F3-8MP52	Box Culvert - Last Wall Pour in Phase 3	0		21-Mar-18	79
S1F-8M7794	Box Culvert - Phase 1 Construction (Summary)	10	05-Dec-17 A	27-Apr-18	52
S1F-8M7791	Box Culvert - Phase 3 Connector Road Construction (Summary)	1	23-Jan-18 A	10-May-18	48
S1F2-8MP66	Box Culvert - Last Wall Pour in Phase 2	0		10-May-18	63
S1F-8M7792	Box Culvert - Phase 2 Polaris Construction (Summary)	73	09-Mar-18	20-Jun-18	40
S1F-8M7757	Box Culvert - NVE Clash with Box Culvert Discovered	1	11-Jan-18 A	11-Jan-18 A	
S1F-8M7758	Box Culvert - KH Coordinating Clash Resolution between NVE & Box Culvert	3	12-Jan-18 A	23-Jan-18 A	
S1F-8M7763	Box Culvert - KH Delivers Structural and H&H Model for Temp Tie-in to USACE / Public Works	3	24-Jan-18 A	26-Jan-18 A	
S1F-8M7764	Box Culvert - USACE Reviews Temp Tie-in Design	2	29-Jan-18 A	02-Feb-18 A	
S1F-8M7765	Box Culvert - Public Works Reviews Temp Tie-in Design	2	29-Jan-18 A	02-Feb-18 A	
S1F-8M7766	Box Culvert - Approval Received to Proceed with Temp Tie-in at Polaris	1	02-Feb-18 A	02-Feb-18 A	
S1F-8M7772	Box Culvert - NVE Survey for Pole Layout	1	10-Feb-18 A	10-Feb-18 A	
S1F-8M7767	Box Culvert - Potholing in Polaris (MH 4347 & 4348 & 1433)	4	09-Feb-18 A	14-Feb-18 A	
S1F-8M7782	Box Culvert - Potholing in Polaris (MH 4349 & 1434 & 4350)	4	14-Feb-18 A	16-Feb-18 A	
S1F-8M7759	Box Culvert - NVE Re-design Ductbank in Polaris	26	24-Jan-18 A	20-Feb-18 A	
S1F-8M7768	Box Culvert - Excavation from MH 4347 & 4348 to Power Pole	2	21-Feb-18 A	22-Feb-18 A	
S1F-8M7773	Box Culvert - NVE Excavate & Set Power Poles	4	20-Feb-18 A	22-Feb-18 A	
S1F-8M7774	Box Culvert - Excavation from MH 1434 & 4350 to Power Pole	2	22-Feb-18 A	23-Feb-18 A	
S1F-8M7778	Box Culvert - Excavation from MH 1433 & 4349 to Power Pole	2	22-Feb-18 A	23-Feb-18 A	
S1F-8M7769	Box Culvert - Remove Knockout / Sand Trench / Install Conduits to Pole / Top Sand (MH 4347 & 4348)	2	23-Feb-18 A	26-Feb-18 A	
S1F-8M7770	Box Culvert - Concrete Encase / Mandrell & Mule Tape (MH 4347 & 4348)	1	26-Feb-18 A	26-Feb-18 A	
S1F-8M7771	Box Culvert - Backfill Install / Patch Asphalt (MH 4347 & 4348)	1	26-Feb-18 A	26-Feb-18 A	
S1F-8M7775	Box Culvert - Remove Knockout / Sand Trench / Install Conduits to Pole / Top Sand (MH 1434 & 4350)	2	24-Feb-18 A	26-Feb-18 A	
S1F-8M7776	Box Culvert - Concrete Encase / Mandrell & Mule Tape (MH 1434 & 4350)	1	26-Feb-18 A	26-Feb-18 A	
S1F-8M7777	Box Culvert - Backfill Install / Patch Asphalt (MH 1434 & 4350)	1	26-Feb-18 A	26-Feb-18 A	
S1F-8M7779	Box Culvert - Remove Knockout / Sand Trench / Install Conduits to Pole / Top Sand (MH 1433 & 4349)	2	24-Feb-18 A	26-Feb-18 A	
S1F-8M7780	Box Culvert - Concrete Encase / Mandrell & Mule Tape (MH 1433 & 4349)	1	26-Feb-18 A	26-Feb-18 A	
S1F-8M7781	Box Culvert - Backfill Install / Patch Asphalt (MH 1433 & 4349)	1	26-Feb-18 A	26-Feb-18 A	
S1F-8M7783	Box Culvert - NVE Customer Outages / OH Shoofly and Million Cable Removal	8	27-Feb-18 A	08-Mar-18	41
S1F-8M7784	Box Culvert - ZAYO Remove / Splice & Test Fiber	8	28-Feb-18 A	09-Mar-18	43
S1F-8M7785	Box Culvert - Demo & Replace NVE Ductbank	10	09-Mar-18	22-Mar-18	41
S1F-8M7788	Box Culvert - ZAYO Replace Fiber	3	26-Mar-18	28-Mar-18	781
S1F-8M7787	Box Culvert - NVE Customer Outages / New Line Construction	6	23-Mar-18	30-Mar-18	41
S1F-8M7789	Box Culvert - NVE Removal of Shoofly Powerlines	6	30-Mar-18	06-Apr-18	41
S1F2-8MP59	Box Culvert - Prepare Rebar Shop Drawings (Phase 2 Temp Connection)	2	29-Jan-18 A	01-Feb-18 A	
S1F2-8MP60	Box Culvert - Approve Rebar Shop Drawings (Phase 2 Temp Connection)	2	02-Feb-18 A	05-Feb-18 A	
S1F2-8MP61	Box Culvert - Procure Rebar (Phase 2 Temp Connection)	3	02-Feb-18 A	07-Feb-18 A	
S1F-8M7760	Box Culvert - Mass Excavate & Type II for Temp Box Culvert (Phase 2 Temp Connection)	5	24-Jan-18 A	02-Feb-18 A	
S1F-8M7761	Box Culvert - Saw Cut & Demo Existing P2 South of Polaris (Phase 2 Temp Connection)	4	01-Feb-18 A	06-Feb-18 A	
S1F2-8MP57	Box Culvert - Set Slab Forms (Phase 2 Temp Connection)	2	07-Feb-18 A	08-Feb-18 A	
S1F2-8MP62	Box Culvert - Install Rebar Pours #1 & #2 (Phase 2 Temp Connection)	4	08-Feb-18 A	08-Feb-18 A	
S1F2-8MP65	Box Culvert - Install Rebar Pour #3 (Phase 2 Temp Connection)	2	08-Feb-18 A	08-Feb-18 A	
S1F2-8MP64	Box Culvert - Pour Slabs #1 & #3 (Phase 2 Temp Connection)	1	12-Feb-18 A	12-Feb-18 A	
S1F2-8MP63	Box Culvert - Pour Slab #2 (Phase 2 Temp Connection)	1	13-Feb-18 A	13-Feb-18 A	
S1F2-8MP58	Box Culvert - FRP Walls - Connection to Existing (Phase 2 Temp Connection)	5	14-Feb-18 A	23-Feb-18 A	
S1F-8M7740	Box Culvert - Moblize Box Culvert	5	01-Dec-17 A	07-Dec-17 A	
S1F-8M7741	Box Culvert - Clean Marnell Yard (Phase 2)	7	14-Dec-17 A	20-Dec-17 A	
S1F-8M7470	Box Culvert - Mass Excavate / Type II (Phase 1 to 106+30)	10	05-Dec-17 A	05-Jan-18 A	
S1F-8M7742	Box Culvert - Temp Fence at Marnell Yard (Phase 2)	10	20-Dec-17 A	09-Jan-18 A	
S1F-8M7751	Box Culvert - Potholing in Polaris (Phase 2)	1	11-Jan-18 A	11-Jan-18 A	
S1F-8M7755	Box Culvert - Saw Cut Opening (Phase 2)	1	11-Jan-18 A	11-Jan-18 A	
S1F-8M7756	Box Culvert - Setup Traffic Control (Phase 2 - Partial)	1	15-Jan-18 A	15-Jan-18 A	
S1F-8M7754	Box Culvert - Relocate Palm Trees (Phase 2)	1	16-Jan-18 A	16-Jan-18 A	
S1F-8M7753	Box Culvert - Temp Fence at Breslin (Phase 2)	3	15-Jan-18 A	17-Jan-18 A	
S1F-8M7643	Box Culvert - Setup Traffic Control (Phase 3)	1	23-Jan-18 A	23-Jan-18 A	
S1F-8M7644	Box Culvert - Demo Site, C&G, Asphalt, Etc (Phase 3)	4	24-Jan-18 A	25-Jan-18 A	

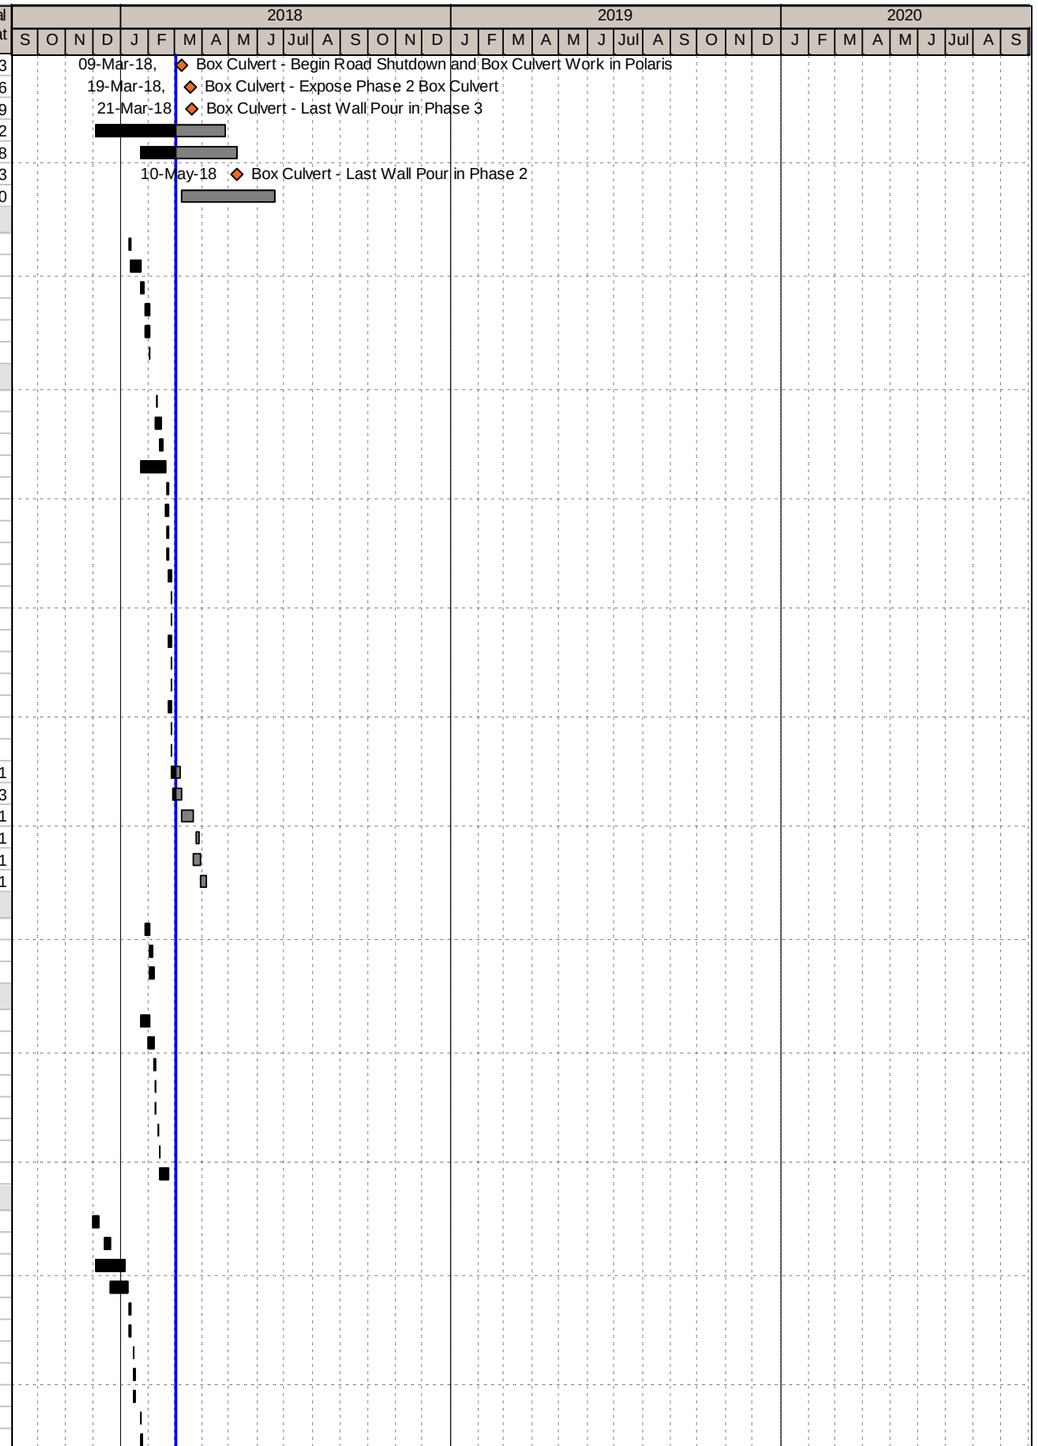

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S1F-8M7645	Box Culvert - Expose Box Culvert End Connections (Phase 3)	1	30-Jan-18 A	31-Jan-18 A	
S1F-8M7647	Box Culvert - Relocate Water (Phase 3)	2	01-Feb-18 A	01-Feb-18 A	
S1F-8M7646	Box Culvert - Setup Shoring & Saw Cut Box Ends (Phase 3)	4	01-Feb-18 A	06-Feb-18 A	
S1F-8M7743	Box Culvert - Setup Traffic Control (Phase 2)	1	09-Mar-18	09-Mar-18	43
S1F-8M7744	Box Culvert - Demo Site, C&G, Asphalt, Etc (Phase 2)	4	12-Mar-18	15-Mar-18	43
S1F-8M7745	Box Culvert - Expose Box Culvert End Connections (Phase 2)	1	19-Mar-18	19-Mar-18	46
S1F-8M7746	Box Culvert - Setup Shoring & Saw Cut Box Ends (Phase 2)	4	20-Mar-18	23-Mar-18	46
S1F-8M7752	Box Culvert - Sewer Encasement & Sleeves (Phase 2)	3	26-Mar-18	28-Mar-18	48
S1F-8M7747	Box Culvert - Water Line Realignment (Phase 2)	5	02-Apr-18	06-Apr-18	42
S1F-8M7750	Box Culvert - Mass Excavate (Phase 3 to 103)	5	08-Jan-18 A	12-Jan-18 A	
S1F-8M7640	Box Culvert - Mass Excavate (Phase 3 103 to End)	10	01-Feb-18 A	14-Feb-18 A	
S1F-8M7720	Box Culvert - Demo Existing (Phase 3)	5	07-Feb-18 A	14-Feb-18 A	
S1F-8M7730	Box Culvert - Demo Existing (Phase 1)	10	12-Feb-18 A	20-Feb-18 A	
S1F3-8MP11	Box Culvert - Install Type II (Phase 3)	4	15-Feb-18 A	23-Feb-18 A	
S1F-8M7749	Box Culvert - Install Liner (Phase 3)	3	21-Feb-18 A	23-Feb-18 A	
S1F-8M7630	Box Culvert - Mass Excavate (Phase 2)	10	19-Mar-18	30-Mar-18	43
S1F-8M7710	Box Culvert - Demo Existing (Phase 2)	5	02-Apr-18	06-Apr-18	41
S1F2-8MP11	Box Culvert - Install Type II (Phase 2)	4	05-Apr-18	10-Apr-18	41
S1F-8M7748	Box Culvert - Install Liner (Phase 2)	4	10-Apr-18	13-Apr-18	41
S1F1-8MP24	Box Culvert - Pour #1 (Partial) - SOG (Phase 1)	1	29-Dec-17 A	29-Dec-17 A	
S1F1-8MP20	Box Culvert - Outside Forms - SOG (Phase 1)	9	22-Dec-17 A	05-Jan-18 A	
S1F1-8MP60	Box Culvert - Pour #1 (Remainder) - SOG (Phase 1)	1	05-Jan-18 A	05-Jan-18 A	
S1F1-8MP25	Box Culvert - Strip Bulkheads Pour #1 - SOG (Phase 1)	1	08-Jan-18 A	08-Jan-18 A	
S1F1-8MP26	Box Culvert - Pour #2 - SOG (Phase 1)	1	08-Jan-18 A	08-Jan-18 A	
S1F1-8MP61	Box Culvert - Pour #3 - SOG (Phase 1)	1	12-Jan-18 A	12-Jan-18 A	
S1F1-8MP21	Box Culvert - Rebar Slabs & Walls - SOG (Phase 1)	9	26-Dec-17 A	17-Jan-18 A	
S1F1-8MP22	Box Culvert - Bulkheads @ CJs - SOG (Phase 1)	7	28-Dec-17 A	17-Jan-18 A	
S1F1-8MP23	Box Culvert - Starter Wall Forming - SOG (Phase 1)	7	28-Dec-17 A	17-Jan-18 A	
S1F1-8MP28	Box Culvert - Strip Bulkheads Pour #3 - SOG (Phase 1)	1	17-Jan-18 A	17-Jan-18 A	
S1F2-8MP53	Box Culvert - Outside Forms & Rebar - SOG (Phase 2 114+25 to 115+50)	4	15-Jan-18 A	17-Jan-18 A	
S1F1-8MP27	Box Culvert - Pour #4 - SOG (Phase 1)	1	18-Jan-18 A	18-Jan-18 A	
S1F2-8MP54	Box Culvert - Pour #1 - SOG (Phase 2 114+25 to 115+50)	1	19-Jan-18 A	19-Jan-18 A	
S1F1-8MP29	Box Culvert - Pour #5 - SOG (Phase 1)	1	23-Jan-18 A	23-Jan-18 A	
S1F2-8MP55	Box Culvert - Strip Bulkheads Pour #1 - SOG (Phase 2 114+25 to 115+50)	1	24-Jan-18 A	24-Jan-18 A	
S1F2-8MP56	Box Culvert - Pour #2 - SOG (Phase 2 114+25 to 115+50)	1	26-Jan-18 A	26-Jan-18 A	
S1F3-8MP20	Box Culvert - Outside Forms - SOG (Phase 3)	4	23-Feb-18 A	28-Feb-18 A	
S1F3-8MP21	Box Culvert - Rebar Slabs & Walls - SOG (Phase 3)	4	27-Feb-18 A	02-Mar-18 A	
S1F3-8MP22	Box Culvert - Bulkheads @ CJs - SOG (Phase 3)	3	01-Mar-18 A	05-Mar-18	48
S1F3-8MP23	Box Culvert - Starter Wall Forming - SOG (Phase 3)	3	01-Mar-18 A	05-Mar-18	48
S1F3-8MP24	Box Culvert - Pour #1 - SOG (Phase 3)	1	06-Mar-18	06-Mar-18	48
S1F3-8MP25	Box Culvert - Strip Bulkheads Pour #1 - SOG (Phase 3)	1	07-Mar-18	07-Mar-18	48
S1F3-8MP26	Box Culvert - Pour #2 - SOG (Phase 3)	1	07-Mar-18	07-Mar-18	48
S1F2-8MP20	Box Culvert - Outside Forms - SOG (Phase 2)	4	16-Apr-18	19-Apr-18	41
S1F2-8MP21	Box Culvert - Rebar Slabs & Walls - SOG (Phase 2)	4	17-Apr-18	20-Apr-18	41
S1F2-8MP22	Box Culvert - Bulkheads @ CJs - SOG (Phase 2)	3	19-Apr-18	23-Apr-18	41
S1F2-8MP23	Box Culvert - Starter Wall Forming - SOG (Phase 2)	3	19-Apr-18	23-Apr-18	41
S1F2-8MP24	Box Culvert - Pour #1 - SOG (Phase 2)	1	24-Apr-18	24-Apr-18	41
S1F2-8MP25	Box Culvert - Strip Bulkheads Pour #1 - SOG (Phase 2)	1	25-Apr-18	25-Apr-18	41
S1F2-8MP26	Box Culvert - Pour #2 - SOG (Phase 2)	1	26-Apr-18	26-Apr-18	41
S1F1-8MP30	Box Culvert - Interior Wall Form Pours #1 & 2 - Walls (Phase 1)	6	10-Jan-18 A	12-Jan-18 A	
S1F1-8MP31	Box Culvert - Wall Bulkheads Pours #1 & 2 - Walls (Phase 1)	5	10-Jan-18 A	12-Jan-18 A	
S1F1-8MP32	Box Culvert - Pour #1 - Walls (Phase 1)	1	12-Jan-18 A	12-Jan-18 A	
S1F1-8MP34	Box Culvert - Cure Walls Pour #1 - Walls (Phase 1)	2	13-Jan-18 A	14-Jan-18 A	
S1F1-8MP33	Box Culvert - Strip Bulkheads Pour #1 - Walls (Phase 1)	1	15-Jan-18 A	15-Jan-18 A	
S1F1-8MP35	Box Culvert - Pour #2 - Walls (Phase 1)	1	16-Jan-18 A	16-Jan-18 A	
S1F1-8MP3E	Box Culvert - Cure Walls Pour #2 - Walls (Phase 1)	2	17-Jan-18 A	18-Jan-18 A	
S1F1-8MP36	Box Culvert - Strip Interior Wall Forms Pours #1 & 2 - Walls (Phase 1)	2	18-Jan-18 A	19-Jan-18 A	
S1F1-8MP3C	Box Culvert - Interior Wall Form for Pours #3 & 4 - Walls (Phase 1)	7	17-Jan-18 A	19-Jan-18 A	
S1F1-8MP3D	Box Culvert - Wall Bulkheads Pours #3 & 4- Walls (Phase 1)	4	23-Jan-18 A	23-Jan-18 A	
S1F1-8MP37	Box Culvert - Pour #3 - Walls (Phase 1)	1	26-Jan-18 A	26-Jan-18 A	

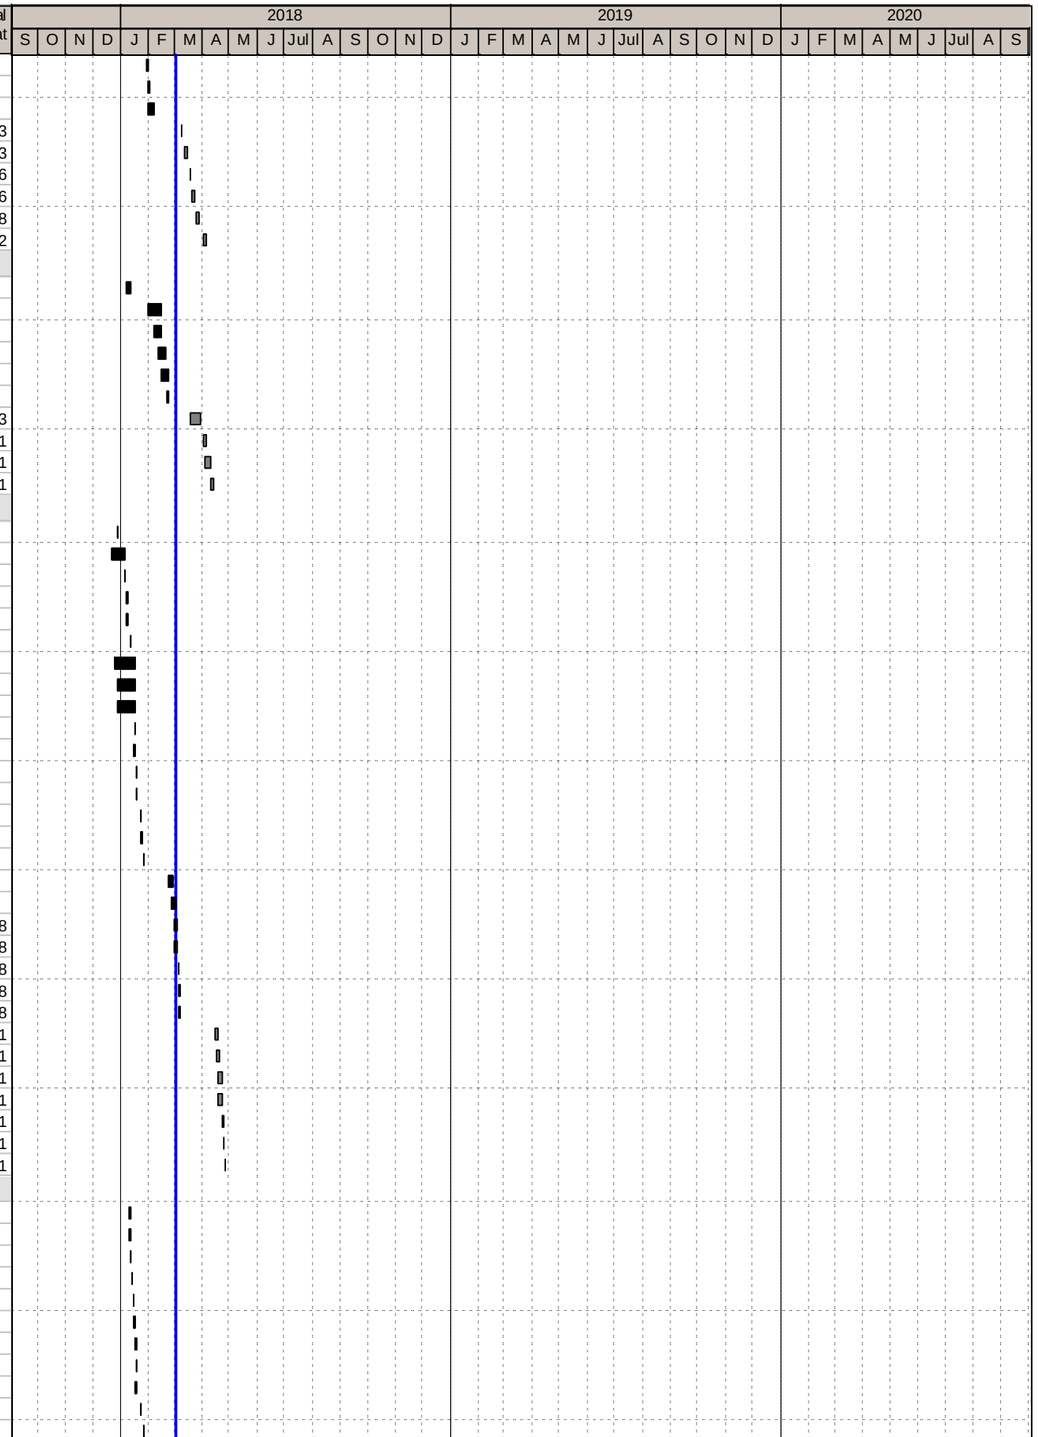

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S1F1-8MP39	Box Culvert - Cure Walls Pour #3- Walls (Phase 1)	2	27-Jan-18 A	28-Jan-18 A	
S1F1-8MP38	Box Culvert - Strip Bulkheads Pour #3 - Walls (Phase 1)	2	29-Jan-18 A	30-Jan-18 A	
S1F1-8MP3A	Box Culvert - Pour #4 - Walls (Phase 1)	1	03-Feb-18 A	03-Feb-18 A	
S1F1-8MP3F	Box Culvert - Cure Walls Pour #4- Walls (Phase 1)	1	04-Feb-18 A	04-Feb-18 A	
S1F1-8MP3A1	Box Culvert - Strip Interior Wall Forms Pours #3 & 4 - Walls (Phase 1)	2	07-Feb-18 A	09-Feb-18 A	
S1F3-8MP32	Box Culvert - FRP Wall Pour #1 - Walls (Phase 3)	4	09-Mar-18	14-Mar-18	48
S1F3-8MP34	Box Culvert - Cure Walls Pour #1 - Walls (Phase 3)	2	15-Mar-18	16-Mar-18	68
S1F3-8MP35	Box Culvert - FRP Wall Pour #2 - Walls (Phase 3)	4	16-Mar-18	21-Mar-18	48
S1F3-8MP37	Box Culvert - Cure Walls Pour #2 - Walls (Phase 3)	2	22-Mar-18	23-Mar-18	69
S1F2-8MP32	Box Culvert - FRP Wall Pour #1 - Walls (Phase 2)	4	27-Apr-18	02-May-18	41
S1F2-8MP34	Box Culvert - Cure Walls Pour #1 - Walls (Phase 2)	2	03-May-18	04-May-18	58
S1F2-8MP35	Box Culvert - FRP Wall Pour #2 - Walls (Phase 2)	4	07-May-18	10-May-18	39
S1F2-8MP37	Box Culvert - Cure Walls Pour #2 - Walls (Phase 2)	2	11-May-18	12-May-18	58
S1F1-8MP40	Box Culvert - Set Deck Formwork Pours #A & B - Decks (Phase 1)	5	24-Jan-18 A	30-Jan-18 A	
S1F1-8MP41	Box Culvert - Rebar Pours #A & B - Decks (Phase 1)	3	26-Jan-18 A	31-Jan-18 A	
S1F1-8MP42	Box Culvert - Install Bulkheads Pours #A & B - Decks (Phase 1)	2	01-Feb-18 A	01-Feb-18 A	
S1F1-8MP43	Box Culvert - Pour #A - Decks (Phase 1)	1	02-Feb-18 A	02-Feb-18 A	
S1F1-8MP44	Box Culvert - Strip Bulkheads Pour #A - Decks (Phase 1)	1	03-Feb-18 A	03-Feb-18 A	
S1F1-8MP51	Box Culvert - Rebar Pours #1 & 2 - Decks (Phase 1)	4	05-Feb-18 A	05-Feb-18 A	
S1F1-8MP45	Box Culvert - Cure Decks Pour #A - Decks (Phase 1)	10	03-Feb-18 A	06-Feb-18 A	
S1F1-8MP46	Box Culvert - Pour #B - Decks (Phase 1)	1	06-Feb-18 A	06-Feb-18 A	
S1F1-8MP50	Box Culvert - Set Deck Formwork Pours #1 & 2 - Decks (Phase 1)	5	02-Feb-18 A	06-Feb-18 A	
S1F1-8MP53	Box Culvert - Cure Decks Pour #B - Decks (Phase 1)	10	06-Feb-18 A	15-Feb-18 A	
S1F1-8MP47	Box Culvert - Strip Outside Wall Forms Pours #A & B - Decks (Phase 1)	2	07-Feb-18 A	05-Mar-18	48
S1F1-8MP49	Box Culvert - FRP Deck Pour #1 - Decks (Phase 1)	1	09-Mar-18	09-Mar-18	50
S1F1-8MP4B	Box Culvert - Cure Decks Pour #1 - Decks (Phase 1)	3	10-Mar-18	12-Mar-18	70
S1F1-8MP4C	Box Culvert - FRP Deck #2 - Decks (Phase 1)	4	13-Mar-18	16-Mar-18	50
S1F1-8MP4B1	Box Culvert - Cure Decks Pour #2 - Decks (Phase 1)	3	17-Mar-18	19-Mar-18	70
S1F1-8MP59	Box Culvert - FRP Deck #3 - Decks (Phase 1)	4	20-Mar-18	23-Mar-18	49
S1F1-8MP4B2	Box Culvert - Cure Decks Pour #3 - Decks (Phase 1)	3	24-Mar-18	26-Mar-18	70
S1F3-8MP43	Box Culvert - FRP Deck Pour #1 - Decks (Phase 3)	5	26-Mar-18	30-Mar-18	48
S1F1-8MP4C1	Box Culvert - FRP Deck #4 - Decks (Phase 1)	4	27-Mar-18	30-Mar-18	49
S1F3-8MP45	Box Culvert - Cure Decks Pour #1 - Decks (Phase 3)	3	31-Mar-18	02-Apr-18	69
S1F1-8MP4B3	Box Culvert - Cure Decks Pour #4 - Decks (Phase 1)	3	31-Mar-18	02-Apr-18	70
S1F3-8MP46	Box Culvert - FRP Deck Pour #2 - Decks (Phase 3)	4	03-Apr-18	06-Apr-18	48
S1F1-8MP4C2	Box Culvert - FRP Deck #5 - Decks (Phase 1)	4	03-Apr-18	06-Apr-18	49
S1F3-8MP48	Box Culvert - Cure Decks Pour #2 - Decks (Phase 3)	3	07-Apr-18	09-Apr-18	69
S1F1-8MP4B4	Box Culvert - Cure Decks Pour #5 - Decks (Phase 1)	3	07-Apr-18	09-Apr-18	71
S1F1-8MP4C3	Box Culvert - FRP Deck #6 - Decks (Phase 1)	4	10-Apr-18	13-Apr-18	50
S1F3-8MP53	Box Culvert - FRP Deck Pour #3 - Decks (Phase 3)	4	10-Apr-18	13-Apr-18	48
S1F1-8MP4B5	Box Culvert - Cure Decks Pour #6 - Decks (Phase 1)	3	14-Apr-18	16-Apr-18	73
S1F3-8MP54	Box Culvert - Cure Decks Pour #3 - Decks (Phase 3)	3	14-Apr-18	16-Apr-18	69
S1F3-8MP47	Box Culvert - Strip Deck Formwork - Decks (Phase 3)	3	17-Apr-18	19-Apr-18	48
S1F3-8MP49	Box Culvert - Form Closure Deck Pour - Decks (Phase 3)	1	19-Apr-18	19-Apr-18	53
S1F3-8MP4A	Box Culvert - Rebar at Closure Deck Pour - Decks (Phase 3)	1	19-Apr-18	19-Apr-18	53
S1F3-8MP4B	Box Culvert - Pour Closure Deck - Decks (Phase 3)	1	20-Apr-18	20-Apr-18	53
S1F1-8MP4C4	Box Culvert - FRP Deck #7 - Decks (Phase 1)	4	17-Apr-18	20-Apr-18	52
S1F3-8MP4C	Box Culvert - Cure Closure Deck - Decks (Phase 3)	3	21-Apr-18	23-Apr-18	77
S1F3-8MP4D	Box Culvert - Strip Closure Deck - Decks (Phase 3)	1	23-Apr-18	23-Apr-18	53
S1F1-8MP4B6	Box Culvert - Cure Decks Pour #7 - Decks (Phase 1)	3	21-Apr-18	23-Apr-18	76
S1F1-8MP55	Box Culvert - Filter Fabric & Backfill (Phase 1)	10	16-Apr-18	27-Apr-18	52
S1F3-8MP4D1	Box Culvert - Filter Fabric & Backfill (Phase 3)	10	20-Apr-18	03-May-18	48
S1F2-8MP43	Box Culvert - FRP Deck Pour #1 - Decks (Phase 2)	4	14-May-18	17-May-18	39
S1F2-8MP45	Box Culvert - Cure Decks Pour #1 - Decks (Phase 2)	3	18-May-18	20-May-18	58
S1F2-8MP46	Box Culvert - FRP Deck Pour #2 - Decks (Phase 2)	4	21-May-18	24-May-18	40
S1F2-8MP4A	Box Culvert - Rebar at Closure Deck Pour - Decks (Phase 2)	1	25-May-18	25-May-18	42
S1F2-8MP48	Box Culvert - Cure Decks Pour #2 - Decks (Phase 2)	3	25-May-18	27-May-18	60
S1F2-8MP47	Box Culvert - Strip Deck Formwork - Decks (Phase 2)	3	23-May-18	29-May-18	42
S1F2-8MP49	Box Culvert - Form Closure Deck Pour - Decks (Phase 2)	1	25-May-18	29-May-18	42
S1F2-8MP4B	Box Culvert - Pour Closure Deck - Decks (Phase 2)	1	29-May-18	29-May-18	42
S1F2-8MP4C	Box Culvert - Cure Closure Deck - Decks (Phase 2)	10	30-May-18	08-Jun-18	59
S1F2-8MP4D	Box Culvert - Strip Closure Deck - Decks (Phase 2)	1	08-Jun-18	08-Jun-18	40

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S1F2-8MP51	Box Culvert - Filter Fabric & Backfill (Phase 2)	10	31-May-18	13-Jun-18	40
S1F3-8MP51	Box Culvert - C&G and Asphalt Paving (Phase 3)	5	04-May-18	10-May-18	48
S1F2-8MP52	Box Culvert - C&G and Asphalt Paving (Phase 2)	5	14-Jun-18	20-Jun-18	40
Excavation					
S0A0-8M43	Initial Drilling & Blasting for Mass Ex - Event A	2	28-Dec-17 A	29-Dec-17 A	
S0A0-8M40	Drilling for Mass Ex - Event A	6	02-Jan-18 A	10-Jan-18 A	
S0F0-8M40	Drilling for Mass Ex - Event F	8	11-Jan-18 A	18-Jan-18 A	
S0B0-8M40	Drilling for Mass Ex - Event B	20	19-Jan-18 A	07-Feb-18 A	
S0C0-8M40	Drilling for Mass Ex - Event C	7	08-Feb-18 A	23-Feb-18 A	
S0E0-8M40	Drilling for Mass Ex - Event E	20	23-Feb-18 A	20-Mar-18	3
S0D0-8M40	Drilling for Mass Ex - Event D	7	21-Mar-18	29-Mar-18	51
S0D0-8M80	Mass Excavation - Exterior Field Tray (Phase 2)	10	22-May-19	05-Jun-19	28
S0A0-8M41	Blasting for Mass Ex - Event A	7	04-Jan-18 A	12-Jan-18 A	
S0B0-8M43	Blasting for Mass Ex - Event B (Day 1)	1	22-Jan-18 A	22-Jan-18 A	
S0F0-8M41	Blasting for Mass Ex - Event F	7	15-Jan-18 A	26-Jan-18 A	
S0B0-8M41	Blasting for Mass Ex - Event B	19	27-Jan-18 A	16-Feb-18 A	
S0C0-8M41	Blasting for Mass Ex - Event C	7	20-Feb-18 A	27-Feb-18 A	
S0E0-8M41	Blasting for Mass Ex - Event E	20	28-Feb-18 A	27-Mar-18	13
S0D0-8M101	Blasting for Mass Ex - Event D	7	28-Mar-18	05-Apr-18	48
S0A0-8M42	Mass Excavation - Event A	9	08-Jan-18 A	22-Jan-18 A	
S0F0-8M42	Mass Excavation - Event F	9	16-Jan-18 A	01-Feb-18 A	
S0B0-8M42	Mass Excavation - Event B	18	29-Jan-18 A	22-Feb-18 A	
S0C0-8M42	Mass Excavation - Event C	8	23-Feb-18 A	08-Mar-18	13
S0E0-8M42	Mass Excavation - Event E	21	05-Mar-18	02-Apr-18	13
S0D0-8M102	Mass Excavation - Event D	9	02-Apr-18	12-Apr-18	46
S0D0-8M60	Mass & Structural Excavation - Event Interior Field Tray (Phase 3)	10	22-Oct-19	04-Nov-19	0
S0D0-8M90	Structural Excavation - Event Interior Field Tray	10	29-Oct-19	12-Nov-19	0
S0D0-8M100	Mass & Structural Excavation - Under C/D Structure (Phase 4)	10	26-Nov-19	11-Dec-19	16
000 Event Level					
S1A1-8M42	Structural Excavation - at Spread Footings - Event A1	3	16-Mar-18	20-Mar-18	4
S1F1-8M42	Structural Excavation - at Spread Footings - Event F1	3	16-Mar-18	20-Mar-18	4
S1A2-8M42	Structural Excavation - at Spread Footings - Event A2	3	21-Mar-18	23-Mar-18	12
S1F2-8M42	Structural Excavation - at Spread Footings - Event F2	3	21-Mar-18	23-Mar-18	13
S1A3-8M42	Structural Excavation - at Spread Footings - Event A3	3	26-Mar-18	28-Mar-18	14
S1F3-8M42	Structural Excavation - at Spread Footings - Event F3	3	26-Mar-18	28-Mar-18	16
S1B1-8M42	Structural Excavation - at Spread Footings - Event B1	3	02-Apr-18	04-Apr-18	15
S1B2-8M42	Structural Excavation - at Spread Footings - Event B2	4	05-Apr-18	10-Apr-18	26
S1E1-8M42	Structural Excavation - at Spread Footings - Event E1	3	06-Apr-18	10-Apr-18	16
S1E2-8M42	Structural Excavation - at Spread Footings - Event E2	3	11-Apr-18	13-Apr-18	29
S1E3-8M42	Structural Excavation - at Spread Footings - Event E3	3	16-Apr-18	18-Apr-18	33
S1B3-8M42	Structural Excavation - at Spread Footings - Event B3	2	18-Apr-18	19-Apr-18	35
S1B4-8M42	Structural Excavation - at Spread Footings - Event B4	3	20-Apr-18	24-Apr-18	35
S1B5-8M42	Structural Excavation - at Spread Footings - Event B5	3	25-Apr-18	27-Apr-18	35
S1E4-8M42	Structural Excavation - at Spread Footings - Event E4	3	26-Apr-18	30-Apr-18	33
S1E5-8M42	Structural Excavation - at Spread Footings - Event E5	3	01-May-18	03-May-18	33
S1C1-8M42	Structural Excavation - at Spread Footings - Event C1	2	14-May-18	15-May-18	35
S1C2-8M42	Structural Excavation - at Spread Footings - Event C2	3	16-May-18	18-May-18	38
S1D1-8M42	Structural Excavation - at Spread Footings - Event D1	2	18-May-18	21-May-18	33
S1C3-8M42	Structural Excavation - at Spread Footings - Event C3	2	21-May-18	22-May-18	42
S1D2-8M42	Structural Excavation - at Spread Footings - Event D2	3	22-May-18	24-May-18	38
S1D3-8M42	Structural Excavation - at Spread Footings - Event D3	2	25-May-18	29-May-18	42
S1A3-8M43	Structural Excavation - at Wall/Mat Foundations - Event A3	3	12-Mar-18	14-Mar-18	3
S1A1-8M43	Structural Excavation - at Wall/Mat Foundations - Event A1	2	15-Mar-18	16-Mar-18	4

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S1F3-8M43	Structural Excavation - at Wall/Mat Foundations - Event F3	3	14-Mar-18	16-Mar-18	3
S1A2-8M43	Structural Excavation - at Wall/Mat Foundations - Event A2	2	19-Mar-18	20-Mar-18	6
S1F1-8M43	Structural Excavation - at Wall/Mat Foundations - Event F1	2	19-Mar-18	20-Mar-18	4
S1A4-8M43	Structural Excavation - at Wall/Mat Foundations - Event A4	2	21-Mar-18	22-Mar-18	17
S1F2-8M43	Structural Excavation - at Wall/Mat Foundations - Event F2	2	21-Mar-18	22-Mar-18	6
S1F4-8M43	Structural Excavation - at Wall/Mat Foundations - Event F4	2	23-Mar-18	26-Mar-18	14
S1B2-8M43	Structural Excavation - at Wall/Mat Foundations - Event B2	3	23-Mar-18	27-Mar-18	19
S1B1-8M43	Structural Excavation - at Wall/Mat Foundations - Event B1	2	28-Mar-18	29-Mar-18	20
S1B3-8M43	Structural Excavation - at Wall/Mat Foundations - Event B3	2	30-Mar-18	02-Apr-18	25
S1B5-8M43	Structural Excavation - at Wall/Mat Foundations - Event B5	3	03-Apr-18	05-Apr-18	30
S1B4-8M43	Structural Excavation - at Wall/Mat Foundations - Event B4	2	06-Apr-18	09-Apr-18	30
S1E2-8M43	Structural Excavation - at Wall/Mat Foundations - Event E2	3	06-Apr-18	10-Apr-18	13
S1B6-8M43	Structural Excavation - at Wall/Mat Foundations - Event B6	2	10-Apr-18	11-Apr-18	46
S1E1-8M43	Structural Excavation - at Wall/Mat Foundations - Event E1	2	11-Apr-18	12-Apr-18	14
S1E3-8M43	Structural Excavation - at Wall/Mat Foundations - Event E3	2	13-Apr-18	16-Apr-18	19
S1E5-8M43	Structural Excavation - at Wall/Mat Foundations - Event E5	3	17-Apr-18	19-Apr-18	21
S1C1-8M43	Structural Excavation - at Wall/Mat Foundations - Event C1	2	20-Apr-18	23-Apr-18	46
S1E4-8M43	Structural Excavation - at Wall/Mat Foundations - Event E4	2	20-Apr-18	23-Apr-18	21
S1C2-8M43	Structural Excavation - at Wall/Mat Foundations - Event C2	2	24-Apr-18	25-Apr-18	51
S1E6-8M43	Structural Excavation - at Wall/Mat Foundations - Event E6	2	24-Apr-18	25-Apr-18	38
S1C3-8M43	Structural Excavation - at Wall/Mat Foundations - Event C3	2	26-Apr-18	27-Apr-18	52
S1D1-8M43	Structural Excavation - at Wall/Mat Foundations - Event D1	2	26-Apr-18	27-Apr-18	46
S1D2-8M43	Structural Excavation - at Wall/Mat Foundations - Event D2	2	30-Apr-18	01-May-18	52
S1C4-8M43	Structural Excavation - at Wall/Mat Foundations - Event C4	3	30-Apr-18	02-May-18	52
S1D3-8M43	Structural Excavation - at Wall/Mat Foundations - Event D3	2	02-May-18	03-May-18	53
S1D4-8M43	Structural Excavation - at Wall/Mat Foundations - Event D4	3	04-May-18	08-May-18	53
S1A1-8M45	Structural Excavation - at Elev/Esc Pits - Event A1	2	15-Mar-18	16-Mar-18	21
S1F1-8M45	Structural Excavation - at Elev/Esc Pits - Event F1	2	19-Mar-18	20-Mar-18	20
S1B1-8M45	Structural Excavation - at Elev/Esc Pits - Event B1	2	28-Mar-18	29-Mar-18	25
S1B2-8M45	Structural Excavation - at Elev/Esc Pits - Event B2	3	10-Apr-18	12-Apr-18	30
S1B5-8M45	Structural Excavation - at Elev/Esc Pits - Event B5	2	13-Apr-18	16-Apr-18	74
S1E2-8M45	Structural Excavation - at Elev/Esc Pits - Event E2	3	24-Apr-18	26-Apr-18	21
S1E3-8M45	Structural Excavation - at Elev/Esc Pits - Event E3	2	27-Apr-18	30-Apr-18	34
S1E5-8M45	Structural Excavation - at Elev/Esc Pits - Event E5	2	01-May-18	02-May-18	50
S1D1-8M45	Structural Excavation - at Elev/Esc Pits - Event D1	2	03-May-18	04-May-18	50
Deep Foundations					
000 Event Level					
S1A0-8N71	Deep Foundations - Test Pile Area A	15	23-Jan-18 A	12-Feb-18 A	
S1A0-8N00	Deep Foundations - Event A	10	20-Feb-18 A	05-Mar-18	3
S1F0-8N00	Deep Foundations - Event F	10	01-Mar-18 A	13-Mar-18	3
S1C1-8N00	Deep Foundations - Event C (Crew #2)	5	15-Mar-18	21-Mar-18	14
S1B-8N00	Deep Foundations - Event B	17	06-Mar-18	28-Mar-18	14
S1C0-8N00	Deep Foundations - Event C	7	29-Mar-18	06-Apr-18	14
S1E1-8N00	Deep Foundations - Event E (Crew #1)	2	10-Apr-18	11-Apr-18	14
S1E0-8N00	Deep Foundations - Event E	15	23-Mar-18	12-Apr-18	13
S1D1-8N00	Deep Foundations - Event D (Crew #1)	2	12-Apr-18	13-Apr-18	54
S1D0-8N00	Deep Foundations - Event D	10	13-Apr-18	26-Apr-18	46
FRP Mat Foundations					
000 Event Level					
S1A3-8N2B	FRP Wall/Mat Foundations - Event A3	7	15-Mar-18	23-Mar-18	3
S1F3-8N2B	FRP Wall/Mat Foundations - Event F3	7	19-Mar-18	27-Mar-18	3
S1A1-8N2B	FRP Wall/Mat Foundations - Event A1	7	20-Mar-18	28-Mar-18	3
S1A2-8N2B	FRP Wall/Mat Foundations - Event A2	6	23-Mar-18	30-Mar-18	4
S1F1-8N2B	FRP Wall/Mat Foundations - Event F1	7	22-Mar-18	30-Mar-18	3
S1F2-8N2B	FRP Wall/Mat Foundations - Event F2	6	27-Mar-18	03-Apr-18	4
S1A4-8N2B	FRP Wall/Mat Foundations - Event A4	6	28-Mar-18	04-Apr-18	14
S1F4-8N2B	FRP Wall/Mat Foundations - Event F4	6	30-Mar-18	06-Apr-18	11
S1B2-8N2B	FRP Wall/Mat Foundations - Event B2	7	02-Apr-18	10-Apr-18	16
S1B1-8N2B	FRP Wall/Mat Foundations - Event B1	6	05-Apr-18	12-Apr-18	16

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S1B3-8N2B	FRP Wall/Mat Foundations - Event B3	7	10-Apr-18	18-Apr-18	20
S1E2-8N2B	FRP Wall/Mat Foundations - Event E2	7	11-Apr-18	19-Apr-18	13
S1B5-8N2B	FRP Wall/Mat Foundations - Event B5	7	13-Apr-18	23-Apr-18	28
S1E1-8N2B	FRP Wall/Mat Foundations - Event E1	6	16-Apr-18	23-Apr-18	13
S1B4-8N2B	FRP Wall/Mat Foundations - Event B4	7	18-Apr-18	26-Apr-18	28
S1B6-8N2B	FRP Wall/Mat Foundations - Event B6	6	23-Apr-18	30-Apr-18	43
S1E3-8N2B	FRP Wall/Mat Foundations - Event E3	7	24-Apr-18	02-May-18	14
S1C1-8N2B	FRP Wall/Mat Foundations - Event C1	7	26-Apr-18	04-May-18	44
S1E5-8N2B	FRP Wall/Mat Foundations - Event E5	7	27-Apr-18	07-May-18	16
S1C2-8N2B	FRP Wall/Mat Foundations - Event C2	7	01-May-18	09-May-18	48
S1E4-8N2B	FRP Wall/Mat Foundations - Event E4	7	02-May-18	10-May-18	16
S1C3-8N2B	FRP Wall/Mat Foundations - Event C3	6	04-May-18	11-May-18	48
S1E6-8N2B	FRP Wall/Mat Foundations - Event E6	6	07-May-18	14-May-18	31
S1C4-8N2B	FRP Wall/Mat Foundations - Event C4	7	09-May-18	17-May-18	48
S1D1-8N2B	FRP Wall/Mat Foundations - Event D1	7	10-May-18	18-May-18	38
S1D2-8N2B	FRP Wall/Mat Foundations - Event D2	7	15-May-18	23-May-18	43
S1D3-8N2B	FRP Wall/Mat Foundations - Event D3	6	18-May-18	25-May-18	43
S1D4-8N2B	FRP Wall/Mat Foundations - Event D4	7	23-May-18	01-Jun-18	43
FRP Spread Footings					
000 Event Level					
S1A1-8N2C	FRP Spread Footings - Event A1	4	21-Mar-18	26-Mar-18	4
S1F1-8N2C	FRP Spread Footings - Event F1	5	21-Mar-18	27-Mar-18	4
S1A2-8N2C	FRP Spread Footings - Event A2	5	27-Mar-18	02-Apr-18	11
S1F2-8N2C	FRP Spread Footings - Event F2	5	28-Mar-18	03-Apr-18	11
S1A3-8N2C	FRP Spread Footings - Event A3	6	03-Apr-18	10-Apr-18	11
S1F3-8N2C	FRP Spread Footings - Event F3	6	04-Apr-18	11-Apr-18	12
S1B1-8N2C	FRP Spread Footings - Event B1	4	11-Apr-18	16-Apr-18	11
S1F4-8N2C	FRP Spread Footings - Event F4	6	09-Apr-18	16-Apr-18	12
S1E1-8N2C	FRP Spread Footings - Event E1	4	17-Apr-18	20-Apr-18	12
S1B2-8N2C	FRP Spread Footings - Event B2	6	17-Apr-18	24-Apr-18	22
S1E2-8N2C	FRP Spread Footings - Event E2	5	23-Apr-18	27-Apr-18	24
S1B3-8N2C	FRP Spread Footings - Event B3	4	25-Apr-18	30-Apr-18	34
S1E3-8N2C	FRP Spread Footings - Event E3	5	30-Apr-18	04-May-18	27
S1B4-8N2C	FRP Spread Footings - Event B4	6	01-May-18	08-May-18	34
S1E4-8N2C	FRP Spread Footings - Event E4	6	07-May-18	14-May-18	32
S1B5-8N2C	FRP Spread Footings - Event B5	6	09-May-18	16-May-18	34
S1E5-8N2C	FRP Spread Footings - Event E5	6	15-May-18	22-May-18	32
S1C1-8N2C	FRP Spread Footings - Event C1	6	17-May-18	24-May-18	34
S1D1-8N2C	FRP Spread Footings - Event D1	6	23-May-18	31-May-18	32
S1C2-8N2C	FRP Spread Footings - Event C2	6	25-May-18	04-Jun-18	34
S1D2-8N2C	FRP Spread Footings - Event D2	6	01-Jun-18	08-Jun-18	34
S1C3-8N2C	FRP Spread Footings - Event C3	6	05-Jun-18	12-Jun-18	34
S1D3-8N2C	FRP Spread Footings - Event D3	6	11-Jun-18	18-Jun-18	34
050 Lower Mezz Level					
S2A1-8N2C	FRP Spread Footings & Tie Beams - Mezz Level North	3	04-May-18	08-May-18	8
Foundation Walls					
000 Event Level					
S1A0-8N30	FRP Wing Walls/Foundation Walls - Event A (Summary)	25	29-Mar-18	02-May-18	5
S1F0-8N30	FRP Wing Walls/Foundation Walls - Event F (Summary)	24	02-Apr-18	03-May-18	8
S1B0-8N30	FRP Wing Walls/Foundation Walls - Event B (Summary)	36	30-Apr-18	19-Jun-18	16
S1E0-8N30	FRP Wing Walls/Foundation Walls - Event E (Summary)	38	30-Apr-18	21-Jun-18	15
S1C0-8N30	FRP Wing Walls/Foundation Walls - Event C (Summary)	32	14-Jun-18	30-Jul-18	57
S1D0-8N30	FRP Wing Walls/Foundation Walls - Event D (Summary)	32	18-Jun-18	01-Aug-18	53
S1A1-8N60	Backfill Foundation Walls - Event A/F North	3	01-May-18	03-May-18	8
S1A0-8N60	Backfill Foundation Walls - Event A (First 11 Feet)	10	12-Jun-18	25-Jun-18	119
S1F0-8N60	Backfill Foundation Walls - Event F (First 11 Feet)	10	22-Jun-18	06-Jul-18	126
S1E0-8N60	Backfill Foundation Walls - Event E (First 11 Feet)	15	24-Jul-18	13-Aug-18	144
S1B0-8N60	Backfill Foundation Walls - Event B (First 11 Feet)	15	24-Jul-18	13-Aug-18	105

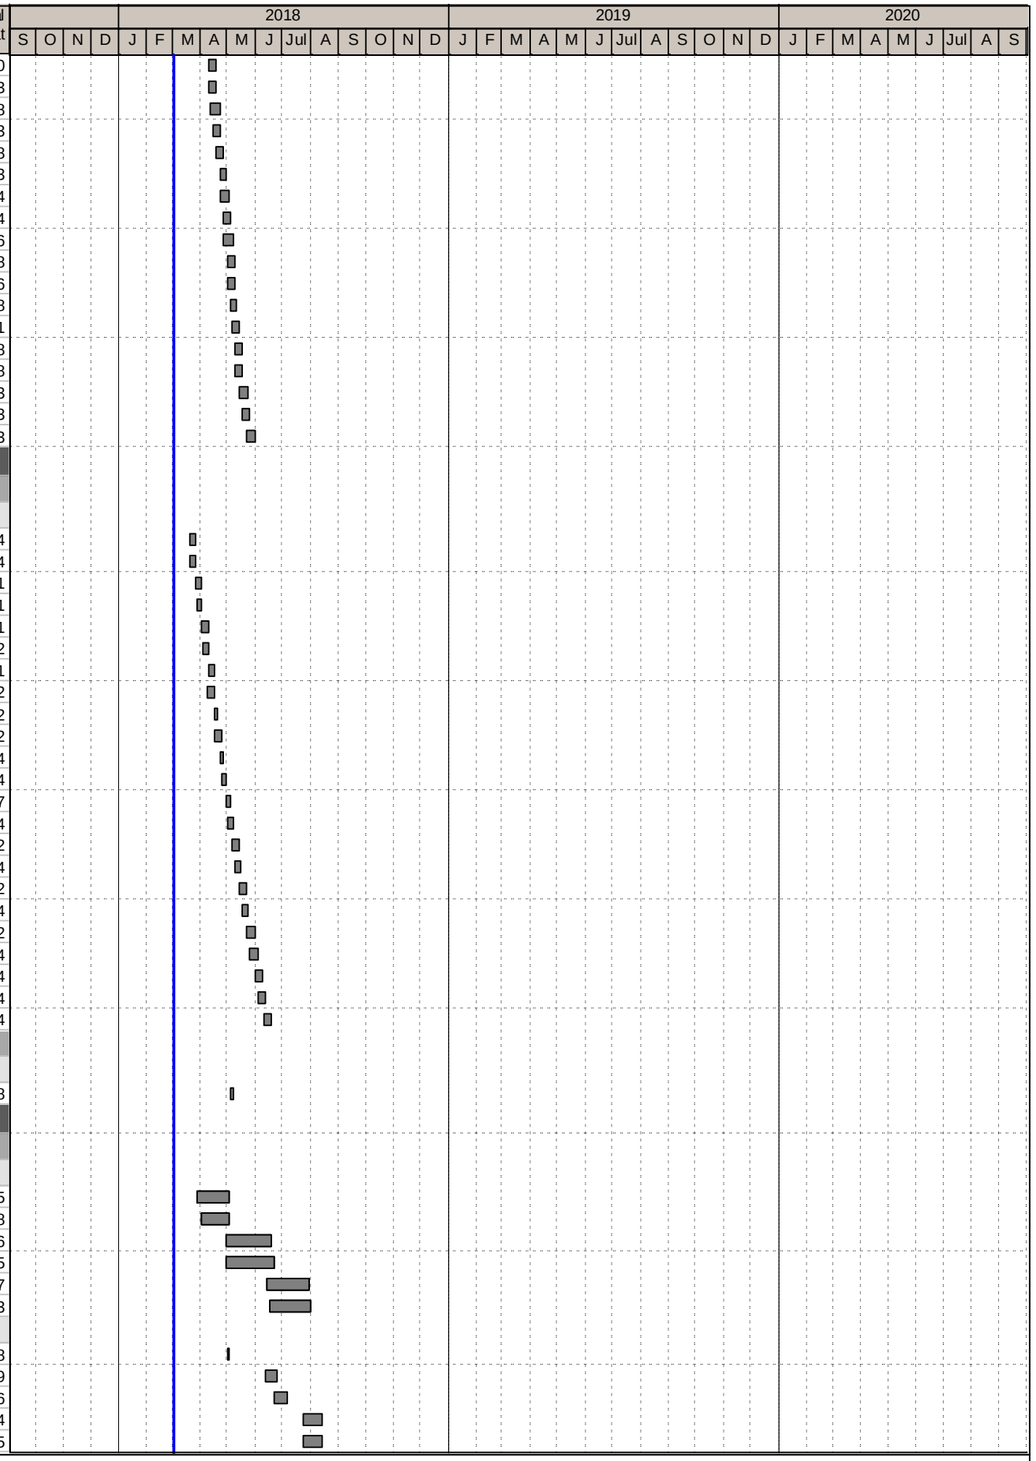

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S1C0-8N60	Backfill Foundation Walls - Event C (First 11 Feet)	10	16-Aug-18	29-Aug-18	133
S1D0-8N60	Backfill Foundation Walls - Event D (First 11 Feet)	10	17-Aug-18	30-Aug-18	146
S1A0-8N72	Backfill Foundation Walls - Event A	10	24-Aug-18	07-Sep-18	67
S1F0-8N71	Backfill Foundation Walls - Event F	10	01-Oct-18	12-Oct-18	57
S1B0-8N71	Backfill Foundation Walls - Event B	15	19-Nov-18	11-Dec-18	46
S1E0-8N71	Backfill Foundation Walls - Event E	15	13-Dec-18	04-Jan-19	37
S1C0-8N71	Backfill Foundation Walls - Event C	10	11-Jan-19	24-Jan-19	33
S1D0-8N91	Backfill Foundation Walls - Event D	10	15-Feb-19	01-Mar-19	22
FRP Foundation Walls					
000 Event Level					
S1A1-8N3B0	Fdn Walls - Set Lead Panels - Event A1	2	29-Mar-18	30-Mar-18	3
S1A2-8N3B0	Fdn Walls - Set Lead Panels - Event A2	2	02-Apr-18	03-Apr-18	4
S1F1-8N3B0	Fdn Walls - Set Lead Panels - Event F1	2	02-Apr-18	03-Apr-18	3
S1F2-8N3B0	Fdn Walls - Set Lead Panels - Event F2	2	04-Apr-18	05-Apr-18	4
S1A3-8N3B0	Fdn Walls - Set Lead Panels - Event A3	2	10-Apr-18	11-Apr-18	6
S1F3-8N3B0	Fdn Walls - Set Lead Panels - Event F3	2	12-Apr-18	13-Apr-18	5
S1A4-8N3B0	Fdn Walls - Set Lead Panels - Event A4	2	16-Apr-18	17-Apr-18	7
S1F4-8N3B0	Fdn Walls - Set Lead Panels - Event F4	2	17-Apr-18	18-Apr-18	5
S1A5-8N3B0	Fdn Walls - Set Lead Panels - Event A5	2	23-Apr-18	24-Apr-18	5
S1F5-8N3B0	Fdn Walls - Set Lead Panels - Event F5	2	24-Apr-18	25-Apr-18	8
S1B1-8N3B0	Fdn Walls - Set Lead Panels - Event B1	2	30-Apr-18	01-May-18	5
S1E1-8N3B0	Fdn Walls - Set Lead Panels - Event E1	2	30-Apr-18	01-May-18	9
S1B2-8N3B0	Fdn Walls - Set Lead Panels - Event B2	2	04-May-18	07-May-18	4
S1E2-8N3B0	Fdn Walls - Set Lead Panels - Event E2	2	07-May-18	08-May-18	7
S1B3-8N3B0	Fdn Walls - Set Lead Panels - Event B3	2	10-May-18	11-May-18	5
S1E3-8N3B0	Fdn Walls - Set Lead Panels - Event E3	2	14-May-18	15-May-18	7
S1B4-8N3B0	Fdn Walls - Set Lead Panels - Event B4	2	16-May-18	17-May-18	12
S1E4-8N3B0	Fdn Walls - Set Lead Panels - Event E4	2	18-May-18	21-May-18	11
S1B5-8N3B0	Fdn Walls - Set Lead Panels - Event B5	2	22-May-18	23-May-18	11
S1E5-8N3B0	Fdn Walls - Set Lead Panels - Event E5	2	24-May-18	25-May-18	10
S1B6-8N3B0	Fdn Walls - Set Lead Panels - Event B6	2	29-May-18	30-May-18	16
S1E6-8N3B0	Fdn Walls - Set Lead Panels - Event E6	2	31-May-18	01-Jun-18	15
S1B7-8N3B0	Fdn Walls - Set Lead Panels - Event B7	2	04-Jun-18	05-Jun-18	17
S1E7-8N3B0	Fdn Walls - Set Lead Panels - Event E7	2	06-Jun-18	07-Jun-18	16
S1B8-8N3B0	Fdn Walls - Set Lead Panels - Event B8	2	08-Jun-18	11-Jun-18	16
S1E8-8N3B0	Fdn Walls - Set Lead Panels - Event E8	2	12-Jun-18	13-Jun-18	15
S1C1-8N3B0	Fdn Walls - Set Lead Panels - Event C1	2	14-Jun-18	15-Jun-18	17
S1D1-8N3B0	Fdn Walls - Set Lead Panels - Event D1	2	18-Jun-18	19-Jun-18	19
S1C2-8N3B0	Fdn Walls - Set Lead Panels - Event C2	2	20-Jun-18	21-Jun-18	18
S1D2-8N3B0	Fdn Walls - Set Lead Panels - Event D2	2	22-Jun-18	25-Jun-18	20
S1C3-8N3B0	Fdn Walls - Set Lead Panels - Event C3	2	26-Jun-18	27-Jun-18	17
S1D3-8N3B0	Fdn Walls - Set Lead Panels - Event D3	2	28-Jun-18	29-Jun-18	19
S1C4-8N3B0	Fdn Walls - Set Lead Panels - Event C4	2	02-Jul-18	03-Jul-18	58
S1D4-8N3B0	Fdn Walls - Set Lead Panels - Event D4	2	05-Jul-18	06-Jul-18	54
S1C5-8N3B0	Fdn Walls - Set Lead Panels - Event C5	2	09-Jul-18	10-Jul-18	57
S1D5-8N3B0	Fdn Walls - Set Lead Panels - Event D5	2	11-Jul-18	12-Jul-18	53
S1C6-8N3B0	Fdn Walls - Set Lead Panels - Event C6	2	13-Jul-18	16-Jul-18	58
S1D6-8N3B0	Fdn Walls - Set Lead Panels - Event D6	2	17-Jul-18	18-Jul-18	54
S1C7-8N3B0	Fdn Walls - Set Lead Panels - Event C7	2	19-Jul-18	20-Jul-18	57
S1D7-8N3B0	Fdn Walls - Set Lead Panels - Event D7	2	23-Jul-18	24-Jul-18	53
Reinforce					
S1A1-8N3BC	Fdn Walls - Rebar - Event A1	2	02-Apr-18	03-Apr-18	3
S1A2-8N3BC	Fdn Walls - Rebar - Event A2	2	04-Apr-18	05-Apr-18	4
S1F1-8N3BC	Fdn Walls - Rebar - Event F1	2	04-Apr-18	05-Apr-18	3
S1F2-8N3BC	Fdn Walls - Rebar - Event F2	2	06-Apr-18	09-Apr-18	4
S1A3-8N3BC	Fdn Walls - Rebar - Event A3	2	12-Apr-18	13-Apr-18	6
S1F3-8N3BC	Fdn Walls - Rebar - Event F3	2	16-Apr-18	17-Apr-18	5
S1A4-8N3BC	Fdn Walls - Rebar - Event A4	2	18-Apr-18	19-Apr-18	7
S1F4-8N3BC	Fdn Walls - Rebar - Event F4	2	19-Apr-18	20-Apr-18	5
S1A5-8N3BC	Fdn Walls - Rebar - Event A5	2	25-Apr-18	26-Apr-18	5

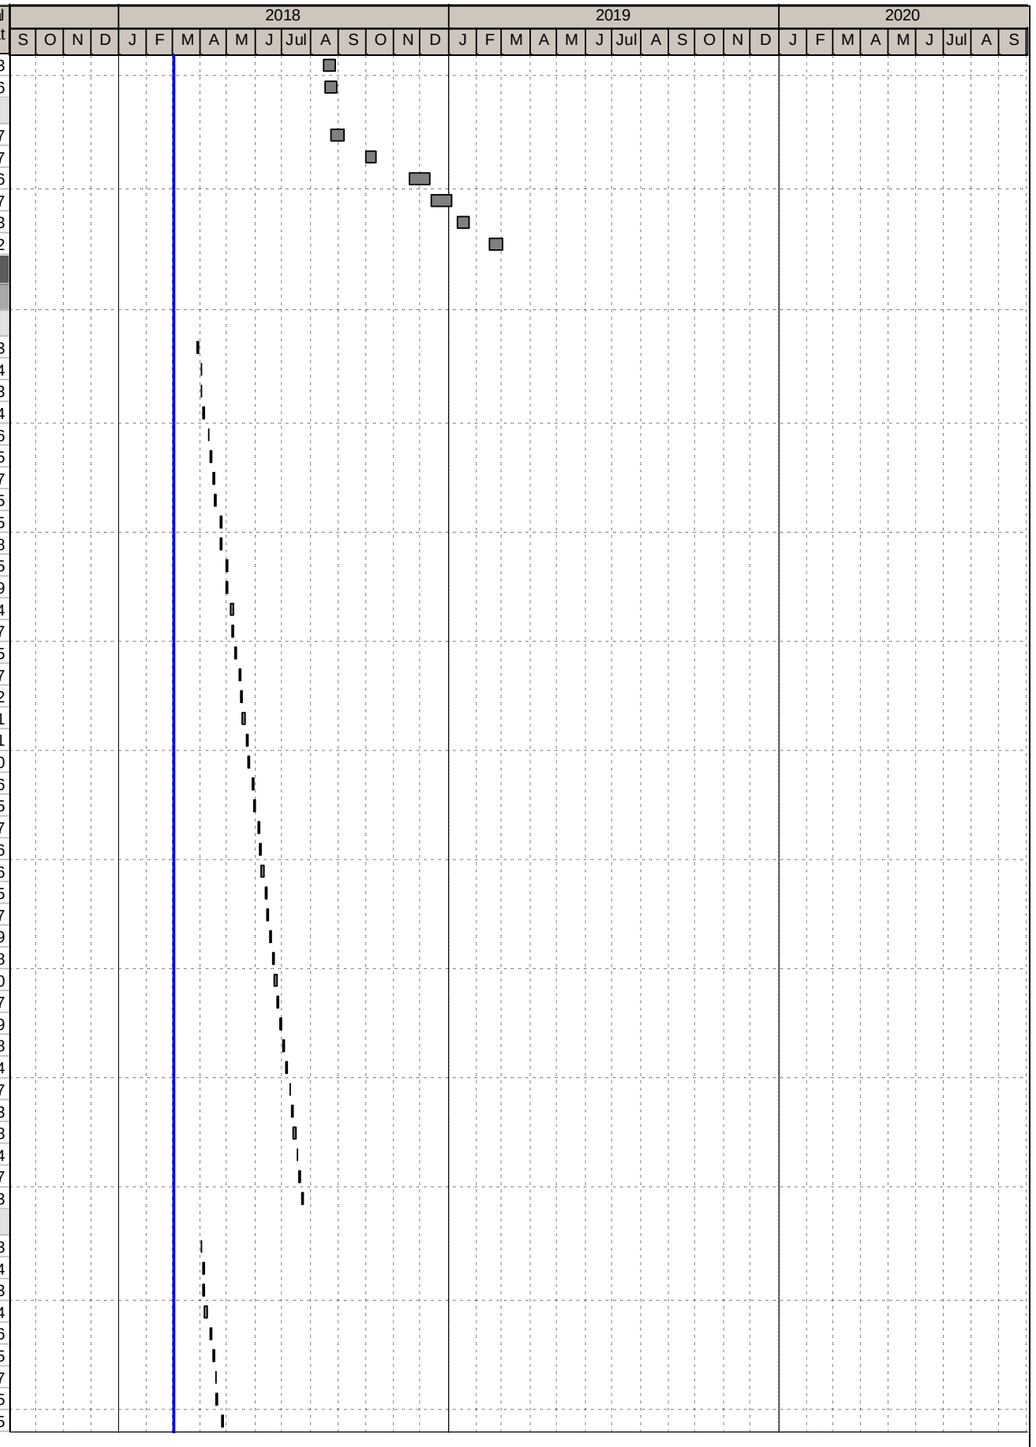

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S1F5-8N3BC	Fdn Walls - Rebar - Event F5	2	26-Apr-18	27-Apr-18	8
S1B1-8N3BC	Fdn Walls - Rebar - Event B1	2	02-May-18	03-May-18	5
S1E1-8N3BC	Fdn Walls - Rebar - Event E1	2	02-May-18	03-May-18	9
S1B2-8N3BC	Fdn Walls - Rebar - Event B2	2	08-May-18	09-May-18	4
S1E2-8N3BC	Fdn Walls - Rebar - Event E2	2	09-May-18	10-May-18	7
S1B3-8N3BC	Fdn Walls - Rebar - Event B3	2	14-May-18	15-May-18	5
S1E3-8N3BC	Fdn Walls - Rebar - Event E3	2	16-May-18	17-May-18	7
S1B4-8N3BC	Fdn Walls - Rebar - Event B4	2	18-May-18	21-May-18	12
S1E4-8N3BC	Fdn Walls - Rebar - Event E4	2	22-May-18	23-May-18	11
S1B5-8N3BC	Fdn Walls - Rebar - Event B5	2	24-May-18	25-May-18	11
S1E5-8N3BC	Fdn Walls - Rebar - Event E5	2	29-May-18	30-May-18	10
S1B6-8N3BC	Fdn Walls - Rebar - Event B6	2	31-May-18	01-Jun-18	16
S1E6-8N3BC	Fdn Walls - Rebar - Event E6	2	04-Jun-18	05-Jun-18	15
S1B7-8N3BC	Fdn Walls - Rebar - Event B7	2	06-Jun-18	07-Jun-18	17
S1E7-8N3BC	Fdn Walls - Rebar - Event E7	2	08-Jun-18	11-Jun-18	16
S1B8-8N3BC	Fdn Walls - Rebar - Event B8	2	12-Jun-18	13-Jun-18	16
S1E8-8N3BC	Fdn Walls - Rebar - Event E8	2	14-Jun-18	15-Jun-18	15
S1C1-8N3BC	Fdn Walls - Rebar - Event C1	2	18-Jun-18	19-Jun-18	17
S1D1-8N3BC	Fdn Walls - Rebar - Event D1	2	20-Jun-18	21-Jun-18	19
S1C2-8N3BC	Fdn Walls - Rebar - Event C2	2	22-Jun-18	25-Jun-18	18
S1D2-8N3BC	Fdn Walls - Rebar - Event D2	2	26-Jun-18	27-Jun-18	20
S1C3-8N3BC	Fdn Walls - Rebar - Event C3	2	28-Jun-18	29-Jun-18	17
S1D3-8N3BC	Fdn Walls - Rebar - Event D3	2	02-Jul-18	03-Jul-18	19
S1C4-8N3BC	Fdn Walls - Rebar - Event C4	2	05-Jul-18	06-Jul-18	58
S1D4-8N3BC	Fdn Walls - Rebar - Event D4	2	09-Jul-18	10-Jul-18	54
S1C5-8N3BC	Fdn Walls - Rebar - Event C5	2	11-Jul-18	12-Jul-18	57
S1D5-8N3BC	Fdn Walls - Rebar - Event D5	2	13-Jul-18	16-Jul-18	53
S1C6-8N3BC	Fdn Walls - Rebar - Event C6	2	17-Jul-18	18-Jul-18	58
S1D6-8N3BC	Fdn Walls - Rebar - Event D6	2	19-Jul-18	20-Jul-18	54
S1C7-8N3BC	Fdn Walls - Rebar - Event C7	2	23-Jul-18	24-Jul-18	57
S1D7-8N3BC	Fdn Walls - Rebar - Event D7	2	25-Jul-18	26-Jul-18	53
S1A1-8N3B3	Fdn Walls - Bulkheads & Blockouts - Event A1	1	03-Apr-18	03-Apr-18	3
S1A2-8N3B3	Fdn Walls - Bulkheads & Blockouts - Event A2	1	05-Apr-18	05-Apr-18	4
S1F1-8N3B3	Fdn Walls - Bulkheads & Blockouts - Event F1	1	05-Apr-18	05-Apr-18	3
S1F2-8N3B3	Fdn Walls - Bulkheads & Blockouts - Event F2	1	09-Apr-18	09-Apr-18	4
S1A3-8N3B3	Fdn Walls - Bulkheads & Blockouts - Event A3	1	13-Apr-18	13-Apr-18	6
S1F3-8N3B3	Fdn Walls - Bulkheads & Blockouts - Event F3	1	17-Apr-18	17-Apr-18	5
S1A4-8N3B3	Fdn Walls - Bulkheads & Blockouts - Event A4	1	19-Apr-18	19-Apr-18	7
S1F4-8N3B3	Fdn Walls - Bulkheads & Blockouts - Event F4	1	20-Apr-18	20-Apr-18	5
S1A5-8N3B3	Fdn Walls - Bulkheads & Blockouts - Event A5	1	26-Apr-18	26-Apr-18	5
S1F5-8N3B3	Fdn Walls - Bulkheads & Blockouts - Event F5	1	27-Apr-18	27-Apr-18	8
S1B1-8N3B3	Fdn Walls - Bulkheads & Blockouts - Event B1	1	03-May-18	03-May-18	5
S1E1-8N3B3	Fdn Walls - Bulkheads & Blockouts - Event E1	1	03-May-18	03-May-18	9
S1B2-8N3B3	Fdn Walls - Bulkheads & Blockouts - Event B2	1	09-May-18	09-May-18	4
S1E2-8N3B3	Fdn Walls - Bulkheads & Blockouts - Event E2	1	10-May-18	10-May-18	7
S1B3-8N3B3	Fdn Walls - Bulkheads & Blockouts - Event B3	1	15-May-18	15-May-18	5
S1E3-8N3B3	Fdn Walls - Bulkheads & Blockouts - Event E3	1	17-May-18	17-May-18	7
S1B4-8N3B3	Fdn Walls - Bulkheads & Blockouts - Event B4	1	21-May-18	21-May-18	12
S1E4-8N3B3	Fdn Walls - Bulkheads & Blockouts - Event E4	1	23-May-18	23-May-18	11
S1B5-8N3B3	Fdn Walls - Bulkheads & Blockouts - Event B5	1	25-May-18	25-May-18	11
S1E5-8N3B3	Fdn Walls - Bulkheads & Blockouts - Event E5	1	30-May-18	30-May-18	10
S1B6-8N3B3	Fdn Walls - Bulkheads & Blockouts - Event B6	1	01-Jun-18	01-Jun-18	16
S1E6-8N3B3	Fdn Walls - Bulkheads & Blockouts - Event E6	1	05-Jun-18	05-Jun-18	15
S1B7-8N3B3	Fdn Walls - Bulkheads & Blockouts - Event B7	1	07-Jun-18	07-Jun-18	17
S1E7-8N3B3	Fdn Walls - Bulkheads & Blockouts - Event E7	1	11-Jun-18	11-Jun-18	16
S1B8-8N3B3	Fdn Walls - Bulkheads & Blockouts - Event B8	1	13-Jun-18	13-Jun-18	16
S1E8-8N3B3	Fdn Walls - Bulkheads & Blockouts - Event E8	1	15-Jun-18	15-Jun-18	15
S1C1-8N3B3	Fdn Walls - Bulkheads & Blockouts - Event C1	1	19-Jun-18	19-Jun-18	17
S1D1-8N3B3	Fdn Walls - Bulkheads & Blockouts - Event D1	1	21-Jun-18	21-Jun-18	19
S1C2-8N3B3	Fdn Walls - Bulkheads & Blockouts - Event C2	1	25-Jun-18	25-Jun-18	18
S1D2-8N3B3	Fdn Walls - Bulkheads & Blockouts - Event D2	1	27-Jun-18	27-Jun-18	20
S1C3-8N3B3	Fdn Walls - Bulkheads & Blockouts - Event C3	1	29-Jun-18	29-Jun-18	17

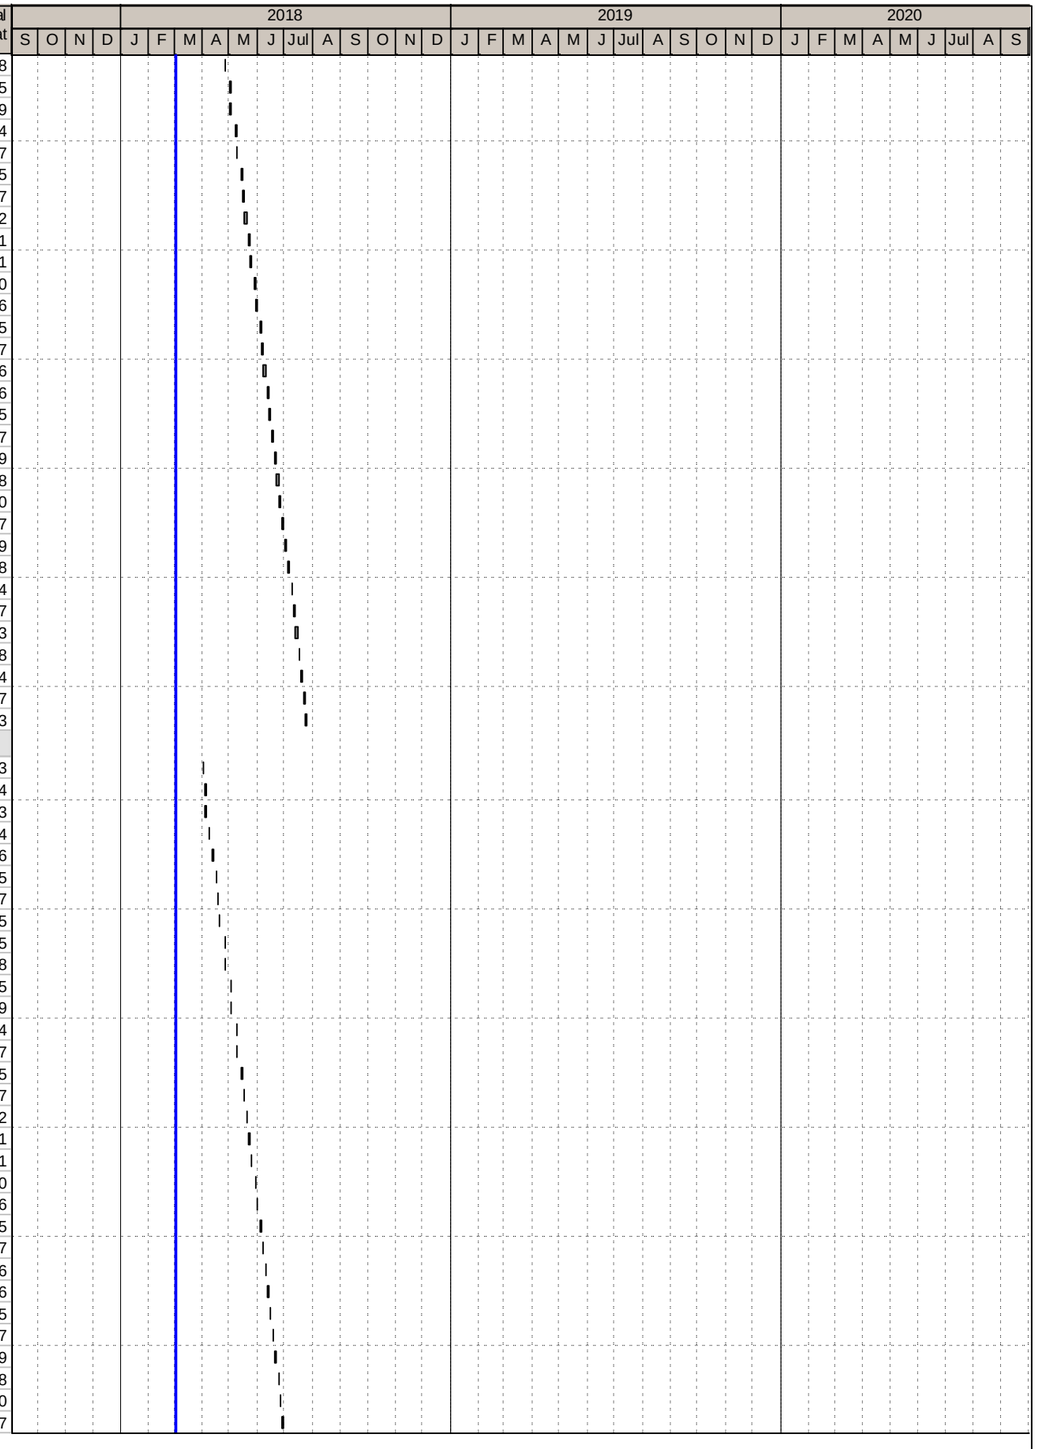

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S1D3-8N3B3	Fdn Walls - Bulkheads & Blockouts - Event D3	1	03-Jul-18	03-Jul-18	19
S1C4-8N3B3	Fdn Walls - Bulkheads & Blockouts - Event C4	1	06-Jul-18	06-Jul-18	58
S1D4-8N3B3	Fdn Walls - Bulkheads & Blockouts - Event D4	1	10-Jul-18	10-Jul-18	54
S1C5-8N3B3	Fdn Walls - Bulkheads & Blockouts - Event C5	1	12-Jul-18	12-Jul-18	57
S1D5-8N3B3	Fdn Walls - Bulkheads & Blockouts - Event D5	1	16-Jul-18	16-Jul-18	53
S1C6-8N3B3	Fdn Walls - Bulkheads & Blockouts - Event C6	1	18-Jul-18	18-Jul-18	58
S1D6-8N3B3	Fdn Walls - Bulkheads & Blockouts - Event D6	1	20-Jul-18	20-Jul-18	54
S1C7-8N3B3	Fdn Walls - Bulkheads & Blockouts - Event C7	1	24-Jul-18	24-Jul-18	57
S1D7-8N3B3	Fdn Walls - Bulkheads & Blockouts - Event D7	1	26-Jul-18	26-Jul-18	53
S1A1-8N3BN	Fdn Walls - Inspect & Close Wall - Event A1	2	04-Apr-18	05-Apr-18	3
S1F1-8N3BN	Fdn Walls - Inspect & Close Wall - Event F1	2	06-Apr-18	09-Apr-18	3
S1A2-8N3BN	Fdn Walls - Inspect & Close Wall - Event A2	2	09-Apr-18	10-Apr-18	3
S1F2-8N3BN	Fdn Walls - Inspect & Close Wall - Event F2	2	11-Apr-18	12-Apr-18	3
S1A3-8N3BN	Fdn Walls - Inspect & Close Wall - Event A3	2	16-Apr-18	17-Apr-18	6
S1F3-8N3BN	Fdn Walls - Inspect & Close Wall - Event F3	2	18-Apr-18	19-Apr-18	5
S1A4-8N3BN	Fdn Walls - Inspect & Close Wall - Event A4	2	20-Apr-18	23-Apr-18	7
S1F4-8N3BN	Fdn Walls - Inspect & Close Wall - Event F4	2	23-Apr-18	24-Apr-18	5
S1A5-8N3BN	Fdn Walls - Inspect & Close Wall - Event A5	2	27-Apr-18	30-Apr-18	5
S1F5-8N3BN	Fdn Walls - Inspect & Close Wall - Event F5	2	30-Apr-18	01-May-18	8
S1B1-8N3BN	Fdn Walls - Inspect & Close Wall - Event B1	2	04-May-18	07-May-18	5
S1E1-8N3BN	Fdn Walls - Inspect & Close Wall - Event E1	2	04-May-18	07-May-18	9
S1B2-8N3BN	Fdn Walls - Inspect & Close Wall - Event B2	2	10-May-18	11-May-18	4
S1E2-8N3BN	Fdn Walls - Inspect & Close Wall - Event E2	2	11-May-18	14-May-18	7
S1B3-8N3BN	Fdn Walls - Inspect & Close Wall - Event B3	2	16-May-18	17-May-18	5
S1E3-8N3BN	Fdn Walls - Inspect & Close Wall - Event E3	2	18-May-18	21-May-18	7
S1B4-8N3BN	Fdn Walls - Inspect & Close Wall - Event B4	2	22-May-18	23-May-18	12
S1E4-8N3BN	Fdn Walls - Inspect & Close Wall - Event E4	2	24-May-18	25-May-18	11
S1B5-8N3BN	Fdn Walls - Inspect & Close Wall - Event B5	2	29-May-18	30-May-18	11
S1E5-8N3BN	Fdn Walls - Inspect & Close Wall - Event E5	2	31-May-18	01-Jun-18	10
S1B6-8N3BN	Fdn Walls - Inspect & Close Wall - Event B6	2	04-Jun-18	05-Jun-18	16
S1E6-8N3BN	Fdn Walls - Inspect & Close Wall - Event E6	2	06-Jun-18	07-Jun-18	15
S1B7-8N3BN	Fdn Walls - Inspect & Close Wall - Event B7	2	08-Jun-18	11-Jun-18	17
S1E7-8N3BN	Fdn Walls - Inspect & Close Wall - Event E7	2	12-Jun-18	13-Jun-18	16
S1B8-8N3BN	Fdn Walls - Inspect & Close Wall - Event B8	2	14-Jun-18	15-Jun-18	16
S1E8-8N3BN	Fdn Walls - Inspect & Close Wall - Event E8	2	18-Jun-18	19-Jun-18	15
S1C1-8N3BN	Fdn Walls - Inspect & Close Wall - Event C1	2	20-Jun-18	21-Jun-18	17
S1D1-8N3BN	Fdn Walls - Inspect & Close Wall - Event D1	2	22-Jun-18	25-Jun-18	19
S1C2-8N3BN	Fdn Walls - Inspect & Close Wall - Event C2	2	26-Jun-18	27-Jun-18	18
S1D2-8N3BN	Fdn Walls - Inspect & Close Wall - Event D2	2	28-Jun-18	29-Jun-18	20
S1C3-8N3BN	Fdn Walls - Inspect & Close Wall - Event C3	2	02-Jul-18	03-Jul-18	17
S1D3-8N3BN	Fdn Walls - Inspect & Close Wall - Event D3	2	05-Jul-18	06-Jul-18	19
S1C4-8N3BN	Fdn Walls - Inspect & Close Wall - Event C4	2	09-Jul-18	10-Jul-18	58
S1D4-8N3BN	Fdn Walls - Inspect & Close Wall - Event D4	2	11-Jul-18	12-Jul-18	54
S1C5-8N3BN	Fdn Walls - Inspect & Close Wall - Event C5	2	13-Jul-18	16-Jul-18	57
S1D5-8N3BN	Fdn Walls - Inspect & Close Wall - Event D5	2	17-Jul-18	18-Jul-18	53
S1C6-8N3BN	Fdn Walls - Inspect & Close Wall - Event C6	2	19-Jul-18	20-Jul-18	58
S1D6-8N3BN	Fdn Walls - Inspect & Close Wall - Event D6	2	23-Jul-18	24-Jul-18	54
S1C7-8N3BN	Fdn Walls - Inspect & Close Wall - Event C7	2	25-Jul-18	26-Jul-18	57
S1D7-8N3BN	Fdn Walls - Inspect & Close Wall - Event D7	2	27-Jul-18	30-Jul-18	53
S1A1-8N3BH	Fdn Walls - Pour Wall - Event A1	1	06-Apr-18	06-Apr-18	3
S1F1-8N3BH	Fdn Walls - Pour Wall - Event F1	1	10-Apr-18	10-Apr-18	3
S1A2-8N3BH	Fdn Walls - Pour Wall - Event A2	1	11-Apr-18	11-Apr-18	3
S1F2-8N3BH	Fdn Walls - Pour Wall - Event F2	1	13-Apr-18	13-Apr-18	3
S1A3-8N3BH	Fdn Walls - Pour Wall - Event A3	1	18-Apr-18	18-Apr-18	6
S1F3-8N3BH	Fdn Walls - Pour Wall - Event F3	1	20-Apr-18	20-Apr-18	5
S1A4-8N3BH	Fdn Walls - Pour Wall - Event A4	1	24-Apr-18	24-Apr-18	7
S1F4-8N3BH	Fdn Walls - Pour Wall - Event F4	1	25-Apr-18	25-Apr-18	5
S1A5-8N3BH	Fdn Walls - Pour Wall - Event A5	1	01-May-18	01-May-18	5
S1F5-8N3BH	Fdn Walls - Pour Wall - Event F5	1	02-May-18	02-May-18	8
S1B1-8N3BH	Fdn Walls - Pour Wall - Event B1	1	08-May-18	08-May-18	5
S1E1-8N3BH	Fdn Walls - Pour Wall - Event E1	1	08-May-18	08-May-18	9

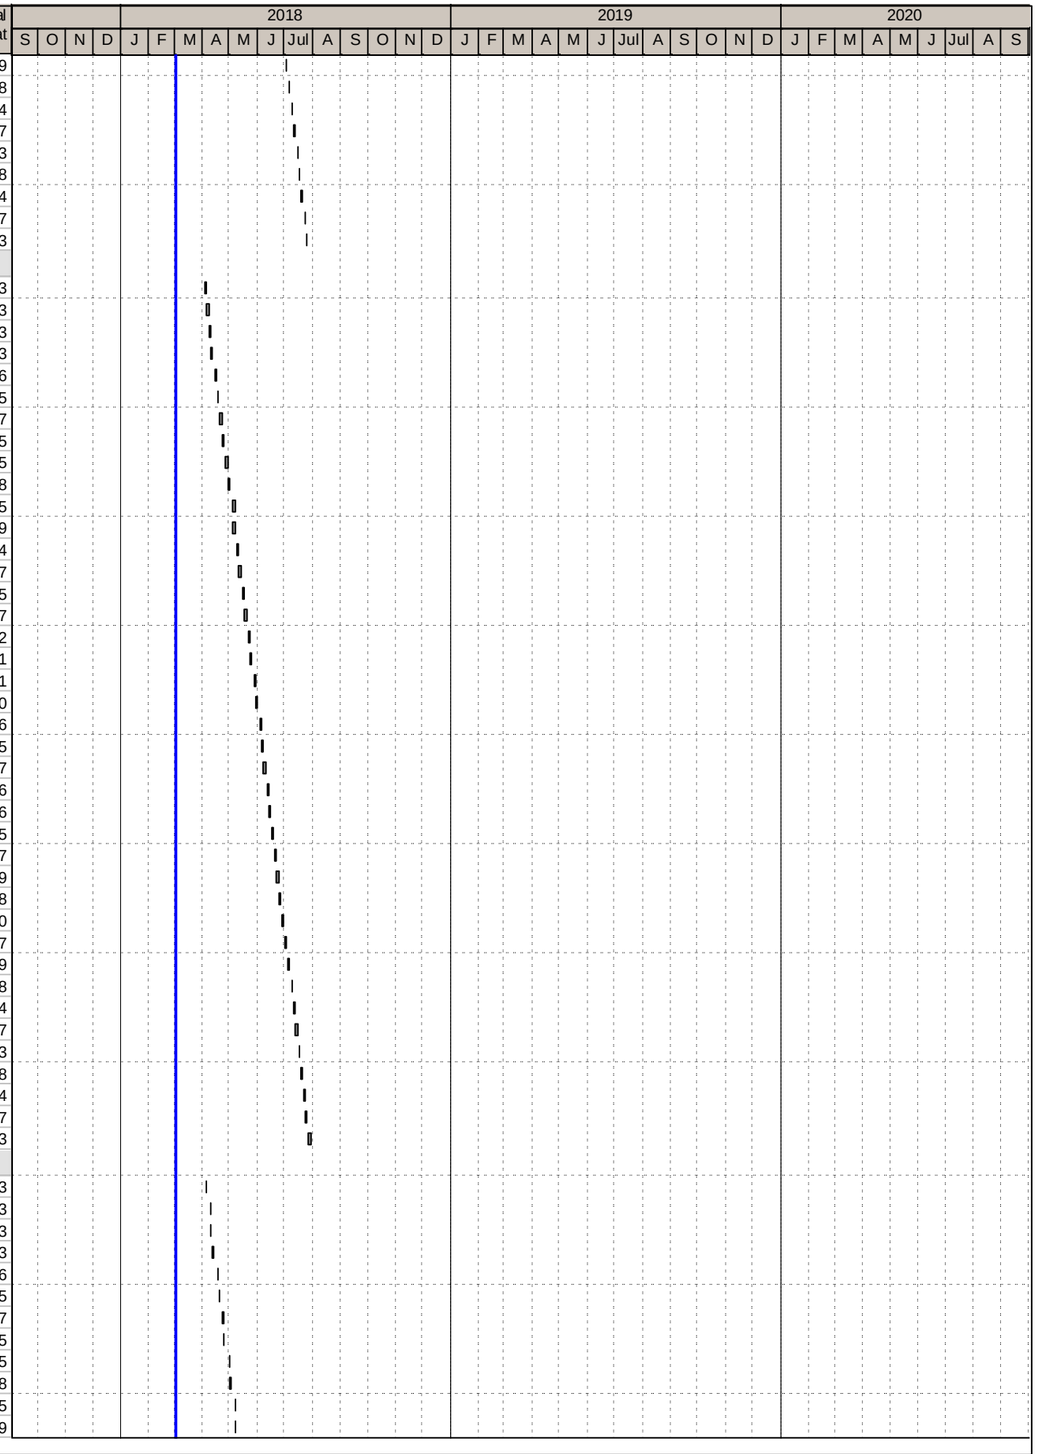

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S1B2-8N3BH	Fdn Walls - Pour Wall - Event B2	1	14-May-18	14-May-18	4
S1E2-8N3BH	Fdn Walls - Pour Wall - Event E2	1	15-May-18	15-May-18	7
S1B3-8N3BH	Fdn Walls - Pour Wall - Event B3	1	18-May-18	18-May-18	5
S1E3-8N3BH	Fdn Walls - Pour Wall - Event E3	1	22-May-18	22-May-18	7
S1B4-8N3BH	Fdn Walls - Pour Wall - Event B4	1	24-May-18	24-May-18	12
S1E4-8N3BH	Fdn Walls - Pour Wall - Event E4	1	29-May-18	29-May-18	11
S1B5-8N3BH	Fdn Walls - Pour Wall - Event B5	1	31-May-18	31-May-18	11
S1E5-8N3BH	Fdn Walls - Pour Wall - Event E5	1	04-Jun-18	04-Jun-18	10
S1B6-8N3BH	Fdn Walls - Pour Wall - Event B6	1	06-Jun-18	06-Jun-18	16
S1E6-8N3BH	Fdn Walls - Pour Wall - Event E6	1	08-Jun-18	08-Jun-18	15
S1B7-8N3BH	Fdn Walls - Pour Wall - Event B7	1	12-Jun-18	12-Jun-18	17
S1E7-8N3BH	Fdn Walls - Pour Wall - Event E7	1	14-Jun-18	14-Jun-18	16
S1B8-8N3BH	Fdn Walls - Pour Wall - Event B8	1	18-Jun-18	18-Jun-18	16
S1E8-8N3BH	Fdn Walls - Pour Wall - Event E8	1	20-Jun-18	20-Jun-18	15
S1C1-8N3BH	Fdn Walls - Pour Wall - Event C1	1	22-Jun-18	22-Jun-18	17
S1D1-8N3BH	Fdn Walls - Pour Wall - Event D1	1	26-Jun-18	26-Jun-18	19
S1C2-8N3BH	Fdn Walls - Pour Wall - Event C2	1	28-Jun-18	28-Jun-18	18
S1D2-8N3BH	Fdn Walls - Pour Wall - Event D2	1	02-Jul-18	02-Jul-18	20
S1C3-8N3BH	Fdn Walls - Pour Wall - Event C3	1	05-Jul-18	05-Jul-18	17
S1D3-8N3BH	Fdn Walls - Pour Wall - Event D3	1	09-Jul-18	09-Jul-18	19
S1C4-8N3BH	Fdn Walls - Pour Wall - Event C4	1	11-Jul-18	11-Jul-18	58
S1D4-8N3BH	Fdn Walls - Pour Wall - Event D4	1	13-Jul-18	13-Jul-18	54
S1C5-8N3BH	Fdn Walls - Pour Wall - Event C5	1	17-Jul-18	17-Jul-18	57
S1D5-8N3BH	Fdn Walls - Pour Wall - Event D5	1	19-Jul-18	19-Jul-18	53
S1C6-8N3BH	Fdn Walls - Pour Wall - Event C6	1	23-Jul-18	23-Jul-18	58
S1D6-8N3BH	Fdn Walls - Pour Wall - Event D6	1	25-Jul-18	25-Jul-18	54
S1C7-8N3BH	Fdn Walls - Pour Wall - Event C7	1	27-Jul-18	27-Jul-18	57
S1D7-8N3BH	Fdn Walls - Pour Wall - Event D7	1	31-Jul-18	31-Jul-18	53
S1A1-8N3BJ	Fdn Walls - Strip - Event A1	1	09-Apr-18	09-Apr-18	3
S1F1-8N3BJ	Fdn Walls - Strip - Event F1	1	11-Apr-18	11-Apr-18	3
S1A2-8N3BJ	Fdn Walls - Strip - Event A2	1	12-Apr-18	12-Apr-18	3
S1F2-8N3BJ	Fdn Walls - Strip - Event F2	1	16-Apr-18	16-Apr-18	3
S1A3-8N3BJ	Fdn Walls - Strip - Event A3	1	19-Apr-18	19-Apr-18	6
S1F3-8N3BJ	Fdn Walls - Strip - Event F3	1	23-Apr-18	23-Apr-18	5
S1A4-8N3BJ	Fdn Walls - Strip - Event A4	1	25-Apr-18	25-Apr-18	7
S1F4-8N3BJ	Fdn Walls - Strip - Event F4	1	26-Apr-18	26-Apr-18	5
S1A5-8N3BJ	Fdn Walls - Strip - Event A5	1	02-May-18	02-May-18	5
S1F5-8N3BJ	Fdn Walls - Strip - Event F5	1	03-May-18	03-May-18	8
S1B1-8N3BJ	Fdn Walls - Strip - Event B1	1	09-May-18	09-May-18	5
S1E1-8N3BJ	Fdn Walls - Strip - Event E1	1	09-May-18	09-May-18	9
S1B2-8N3BJ	Fdn Walls - Strip - Event B2	1	15-May-18	15-May-18	4
S1E2-8N3BJ	Fdn Walls - Strip - Event E2	1	16-May-18	16-May-18	7
S1B3-8N3BJ	Fdn Walls - Strip - Event B3	1	21-May-18	21-May-18	5
S1E3-8N3BJ	Fdn Walls - Strip - Event E3	1	23-May-18	23-May-18	7
S1B4-8N3BJ	Fdn Walls - Strip - Event B4	1	25-May-18	25-May-18	12
S1E4-8N3BJ	Fdn Walls - Strip - Event E4	1	30-May-18	30-May-18	11
S1B5-8N3BJ	Fdn Walls - Strip - Event B5	1	01-Jun-18	01-Jun-18	11
S1E5-8N3BJ	Fdn Walls - Strip - Event E5	1	05-Jun-18	05-Jun-18	10
S1B6-8N3BJ	Fdn Walls - Strip - Event B6	1	07-Jun-18	07-Jun-18	16
S1E6-8N3BJ	Fdn Walls - Strip - Event E6	1	11-Jun-18	11-Jun-18	15
S1B7-8N3BJ	Fdn Walls - Strip - Event B7	1	13-Jun-18	13-Jun-18	17
S1E7-8N3BJ	Fdn Walls - Strip - Event E7	1	15-Jun-18	15-Jun-18	16
S1B8-8N3BJ	Fdn Walls - Strip - Event B8	1	19-Jun-18	19-Jun-18	16
S1E8-8N3BJ	Fdn Walls - Strip - Event E8	1	21-Jun-18	21-Jun-18	15
S1C1-8N3BJ	Fdn Walls - Strip - Event C1	1	25-Jun-18	25-Jun-18	17
S1D1-8N3BJ	Fdn Walls - Strip - Event D1	1	27-Jun-18	27-Jun-18	19
S1C2-8N3BJ	Fdn Walls - Strip - Event C2	1	29-Jun-18	29-Jun-18	18
S1D2-8N3BJ	Fdn Walls - Strip - Event D2	1	03-Jul-18	03-Jul-18	20
S1C3-8N3BJ	Fdn Walls - Strip - Event C3	1	06-Jul-18	06-Jul-18	17
S1D3-8N3BJ	Fdn Walls - Strip - Event D3	1	10-Jul-18	10-Jul-18	19
S1C4-8N3BJ	Fdn Walls - Strip - Event C4	1	12-Jul-18	12-Jul-18	58
S1D4-8N3BJ	Fdn Walls - Strip - Event D4	1	16-Jul-18	16-Jul-18	54

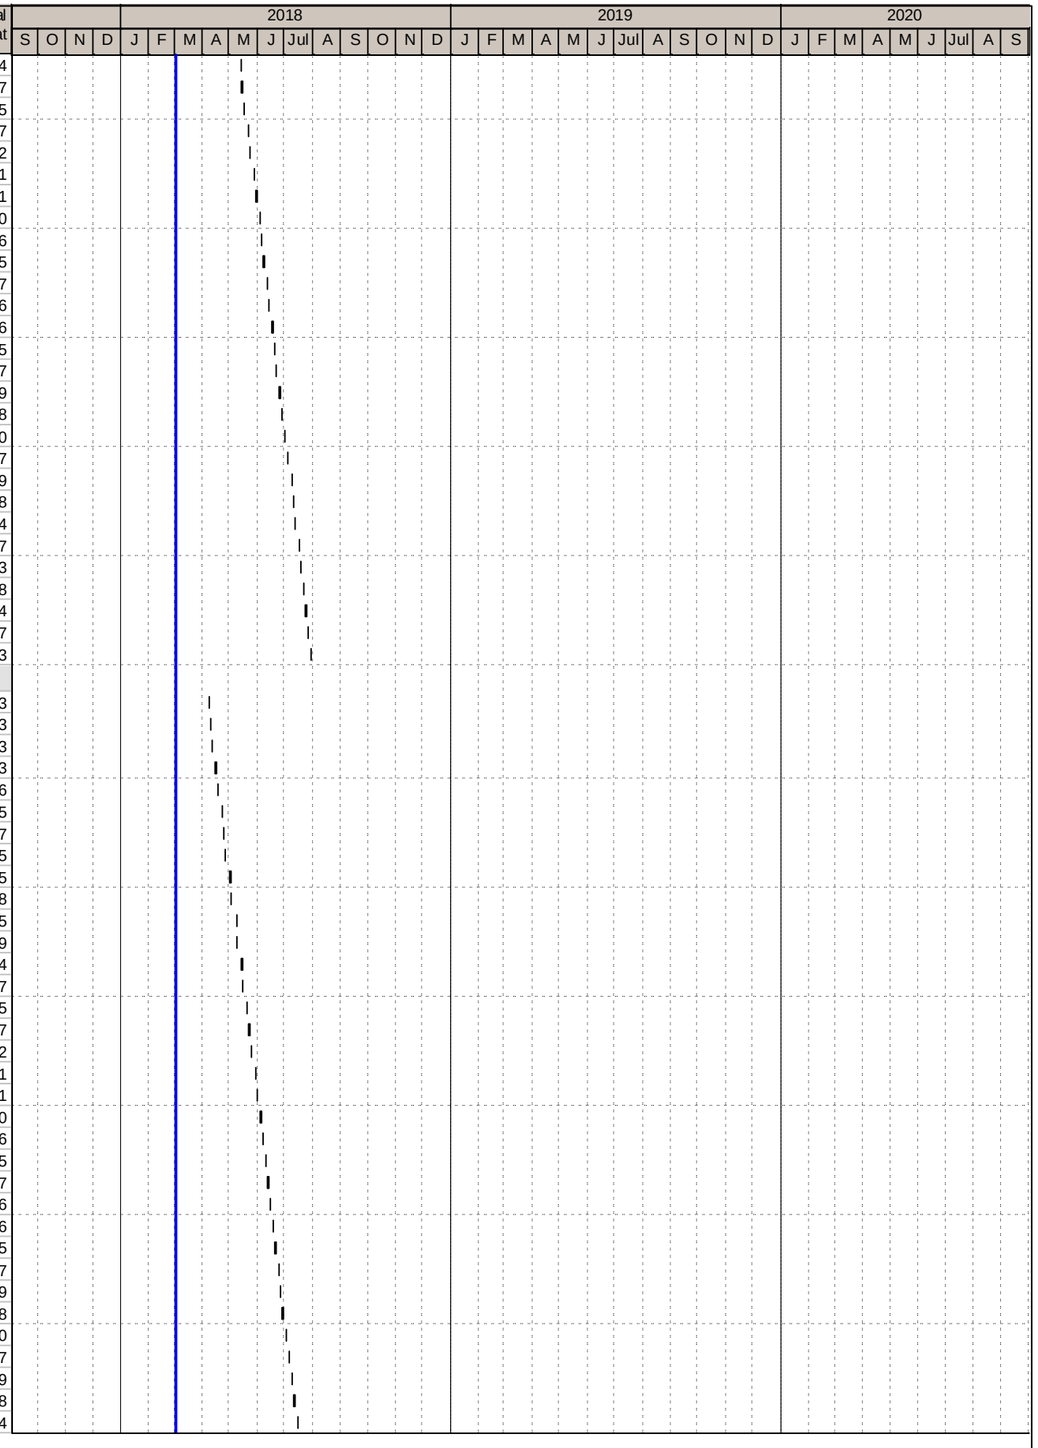

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S1C5-8N3BJ	Fdn Walls - Strip - Event C5	1	18-Jul-18	18-Jul-18	57
S1D5-8N3BJ	Fdn Walls - Strip - Event D5	1	20-Jul-18	20-Jul-18	53
S1C6-8N3BJ	Fdn Walls - Strip - Event C6	1	24-Jul-18	24-Jul-18	58
S1D6-8N3BJ	Fdn Walls - Strip - Event D6	1	26-Jul-18	26-Jul-18	54
S1C7-8N3BJ	Fdn Walls - Strip - Event C7	1	30-Jul-18	30-Jul-18	57
S1D7-8N3BJ	Fdn Walls - Strip - Event D7	1	01-Aug-18	01-Aug-18	53
Elevator Pits					
000 Event Level					
S1A1-8N5A	FRP Elev/Esc Pits - Event A1	12	27-Mar-18	11-Apr-18	15
S1F1-8N5A	FRP Elev/Esc Pits - Event F1	12	27-Mar-18	11-Apr-18	16
S1B1-8N5A	FRP Elev/Esc Pits - Event B1	12	16-Apr-18	01-May-18	14
S1B5-8N5A	FRP Elev/Esc Pits - Event B5	12	17-Apr-18	02-May-18	74
S1B2-8N5A	FRP Elev/Esc Pits - Event B2	16	20-Apr-18	11-May-18	25
S1E3-8N5A	FRP Elev/Esc Pits - Event E3	12	01-May-18	16-May-18	34
S1E2-8N5A	FRP Elev/Esc Pits - Event E2	16	27-Apr-18	18-May-18	21
S1E5-8N5A	FRP Elev/Esc Pits - Event E5	12	03-May-18	18-May-18	61
S1D1-8N5A	FRP Elev/Esc Pits - Event D1	14	07-May-18	24-May-18	50
S1F2-8N5A	FRP Elev/Esc Pits - Event F @ Core #2	13	08-Jun-18	26-Jun-18	72
S1A2-8N5A	FRP Elev/Esc Pits - Event A @ Core #3	13	12-Jun-18	28-Jun-18	50
S1E1-8N5A	FRP Elev/Esc Pits - Event E @ Core #1	13	28-Jun-18	17-Jul-18	98
S1B3-8N5A	FRP Elev/Esc Pits - Event B @ Core #4	13	05-Jul-18	23-Jul-18	64
S1B4-8N5A	FRP Elev/Esc Pits - Event B @ Core #5	13	24-Jul-18	09-Aug-18	51
S1E4-8N5A	FRP Elev/Esc Pits - Event E @ Core #8	13	24-Jul-18	09-Aug-18	81
S1C1-8N5A	FRP Elev/Esc Pits - Event C @ Core #6	13	16-Aug-18	04-Sep-18	94
S1D2-8N5A	FRP Elev/Esc Pits - Event D @ Core #7	13	17-Aug-18	05-Sep-18	123
UG M/E and Slab on Grade					
000 Event Level					
S1A0-8N70	Deep Underground Mech/P - Sewer Mains / Greas Mains - Event A1	7	05-Apr-18	13-Apr-18	2
S1A0-8N73	Deep Underground Mech/P - Grease Int / Sewage Pit / Bldg Drain Pit - Event A1 (AT1)	8	04-Apr-18	13-Apr-18	2
S1A0-8N74	Deep Underground Mech/P - Sand Interceptors / Sample Box - Event A1 (AT2)	6	06-Apr-18	13-Apr-18	2
S1F0-8N70	Deep Underground Mech/P - Sewer Mains / Grease Mains - Event F1	6	09-Apr-18	16-Apr-18	3
S1A2-8N70	Deep Underground Mech/P - Sewer Mains / Sand Oil Mains - Event A2	6	16-Apr-18	23-Apr-18	7
S1F2-8N70	Deep Underground Mech/P - Sewer Mains - Event F2	6	17-Apr-18	24-Apr-18	7
S1B0-8N70	Deep Underground Mech/P - Sewer Mains / Sand Oil Mains - Event B1	6	24-Apr-18	01-May-18	14
S1E0-8N70	Deep Underground Mech/P - Sewer Mains / Grease Mains / Sand Oil Mains - Event E1	6	26-Apr-18	03-May-18	16
S1E1-8N70	Deep Underground Mech/P - Sewage Pit / Drainage Pit / Grease Int Tank - Event E1 (ET1)	10	26-Apr-18	09-May-18	12
S1B2-8N74	Deep Underground Mech/P - Sand Interceptors / Sample Box - Event B2 (BT2)	6	03-May-18	10-May-18	26
S1B2-8N70	Deep Underground Mech/P - Sewer Mains / Grease Mains / Pumped Drains - Event B2	7	03-May-18	11-May-18	25
S1E2-8N70	Deep Underground Mech/P - Sewer Mains / Grease Mains / Sand Oil Mains - Event E2	7	07-May-18	15-May-18	24
S1B2-8N73	Deep Underground Mech/P - Sewage Pit / Bldg Drain Water Pit - Event B2 (BT1)	10	03-May-18	16-May-18	22
S1B3-8N70	Deep Underground Mech/P - Sewer Mains - Event B3	6	14-May-18	21-May-18	36
S1E3-8N70	Deep Underground Mech/P - Sewer Mains - Event E3	7	16-May-18	24-May-18	28
S1E3-8N73	Deep Underground Mech/P - Sewage Pit / Drainage Pit - Event E3 (ET2)	9	16-May-18	29-May-18	26
S1D0-8N70	Deep Underground Mech/P - Sewer Mains - Event D1	7	07-Jun-18	15-Jun-18	35
S1C0-8N70	Deep Underground Mech/P - Sewer Mains / Grease Mains / Sand Oil Mains - Event C1	8	06-Jun-18	15-Jun-18	31
S1D2-8N70	Deep Underground Mech/P - Sand Oil Mains - Event D2	7	18-Jun-18	26-Jun-18	62
S1C2-8N70	Deep Underground Mech/P - Sewer Mains / Grease Mains / Sand Oil Mains - Event C2	8	18-Jun-18	27-Jun-18	57
S1F3-8N70	Deep Underground Mech/P - Sewer Mains / Grease Mains / Sand Oil Mains - Event F3	6	23-Jul-18	30-Jul-18	35
S1A3-8N70	Deep Underground Mech/P - Sewer Mains / Grease Mains / Sand Oil Mains - Event A3	6	25-Jul-18	01-Aug-18	28
S1E4-8N70	Deep Underground Mech/P - Sewer Mains / Grease Mains / Sand Oil Mains - Event E4	7	24-Aug-18	04-Sep-18	14
S1B4-8N70	Deep Underground Mech/P - Sewer Mains / Grease Mains / Saind Oil Mains - Event B4	6	30-Aug-18	07-Sep-18	13
S1E5-8N70	Deep Underground Mech/P - Sewer Mains / Grease Mains / Sand Oil Mains - Event E5	7	11-Oct-18	19-Oct-18	6
S1B5-8N70	Deep Underground Mech/P - Sewer Mains / Grease Mains / Sand Oil Mains - Event B5	7	15-Oct-18	23-Oct-18	8
S1D3-8N70	Deep Underground Mech/P - Sewer Mains / Sand Oil Mains - Event D3	7	06-Nov-18	15-Nov-18	18
S1C3-8N70	Deep Underground Mech/P - Sewer Mains / Grease Mains / Sand Oil Mains - Event C3	6	07-Nov-18	15-Nov-18	13
S1D3-8N73	Deep Underground Mech/P - Sewage Pit / Bldg Drain Water Pit - Event D3 (DT1)	9	06-Nov-18	19-Nov-18	16
S1C3-8N73	Deep Underground Mech/P - Sewage Pit / Bldg Drain Water Pit - Event C3 (CT1)	10	07-Nov-18	21-Nov-18	9
S1C3-8N74	Deep Underground Mech/P - Sand Interceptors / Sample Box - Event C3 (CT2)	10	07-Nov-18	21-Nov-18	9
S1C3-8N75	Deep Underground Mech/P - Sand & Grease Interceptors / 2 Sample Box - Event C3 (CT3)	10	07-Nov-18	21-Nov-18	9
S1L1-8P1E10	Underground MEP - Exterior Field Tray	20	30-May-19	26-Jun-19	40

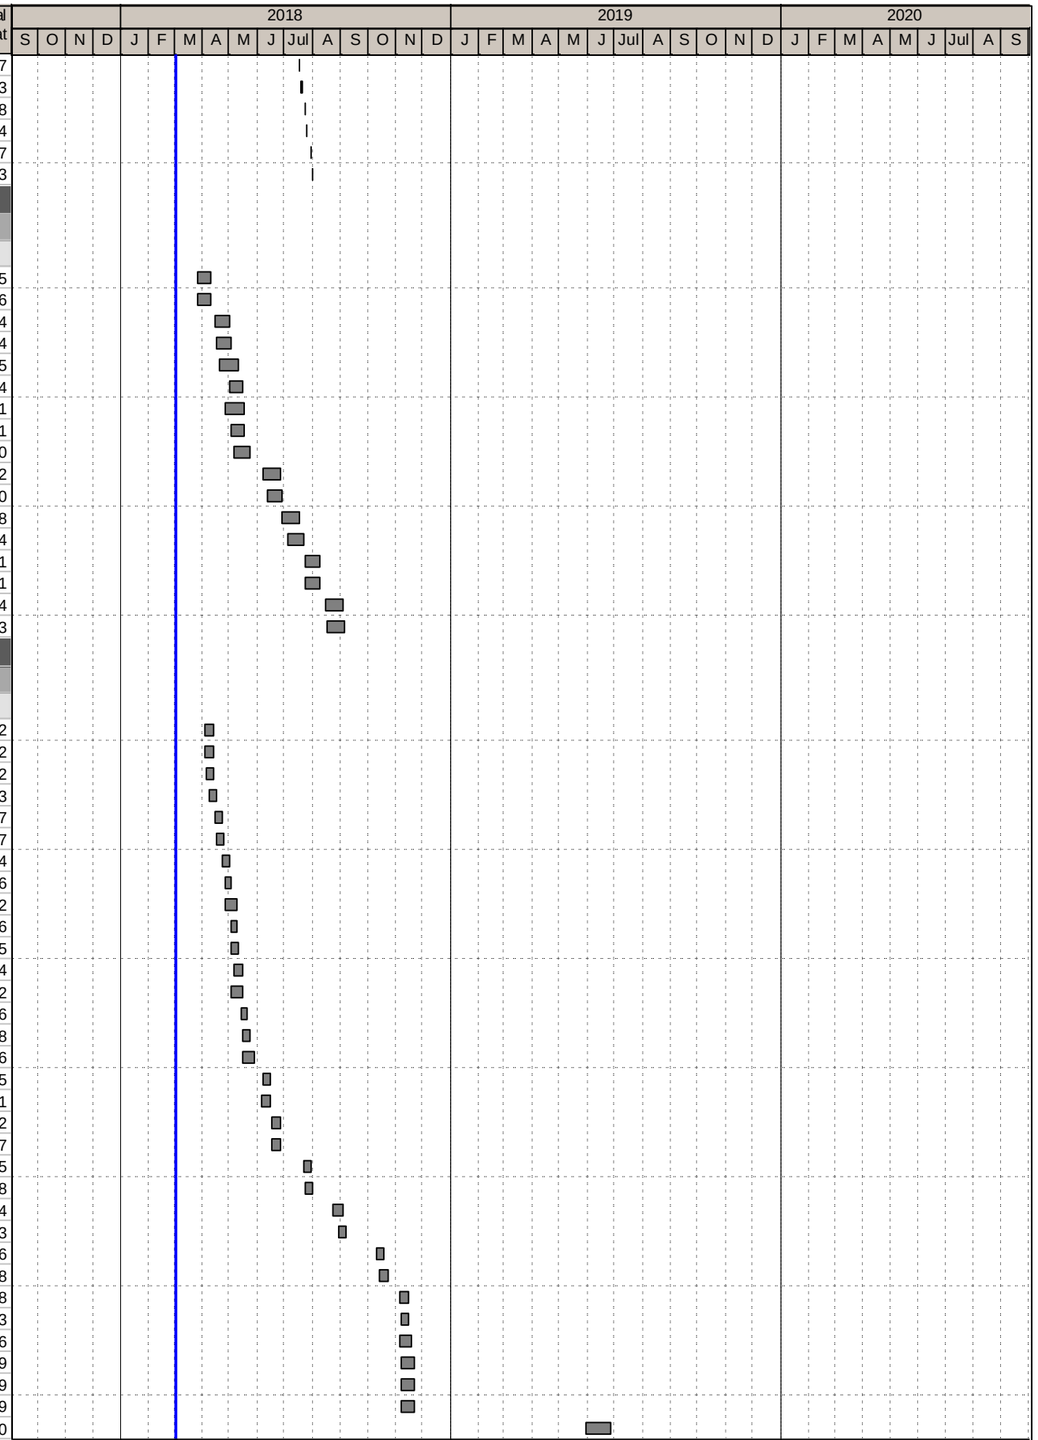

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S1L3-8P1E20	Underground MEP - Interior Field Tray	30	29-Oct-19	12-Dec-19	0
S1L2-8P1E10	Underground MEP - Under Structure C/D	15	13-Dec-19	06-Jan-20	10
S1A0-8N76	Deep Underground Elec - Event A1	5	06-Apr-18	12-Apr-18	3
S1F0-8N73	Deep Underground Elec - Event F1	5	09-Apr-18	13-Apr-18	4
S1A2-8N72	Deep Underground Elec - Event A2	4	11-Apr-18	16-Apr-18	12
S1F2-8N72	Deep Underground Elec - Event F2	5	12-Apr-18	18-Apr-18	11
S1B0-8N73	Deep Underground Elec - Event B1	10	23-Apr-18	04-May-18	11
S1E0-8N73	Deep Underground Elec - Event E1	10	26-Apr-18	09-May-18	12
S1E2-8N72	Deep Underground Elec - Event E2	5	04-May-18	10-May-18	27
S1B2-8N72	Deep Underground Elec - Event B2	10	02-May-18	15-May-18	23
S1B3-8N72	Deep Underground Elec - Event B3	8	10-May-18	21-May-18	36
S1E3-8N72	Deep Underground Elec - Event E3	10	15-May-18	29-May-18	26
S1C0-8N73	Deep Underground Elec - Event C1	5	06-Jun-18	12-Jun-18	34
S1C2-8N72	Deep Underground Elec - Event C2	4	11-Jun-18	14-Jun-18	66
S1D0-8N93	Deep Underground Elec - Event D1	10	07-Jun-18	20-Jun-18	32
S1D2-8N72	Deep Underground Elec - Event D2	4	15-Jun-18	20-Jun-18	66
S1F3-8N72	Deep Underground Elec - Event F3	3	23-Jul-18	25-Jul-18	38
S1A3-8N72	Deep Underground Elec - Event A3	2	25-Jul-18	26-Jul-18	31
S1E4-8N72	Deep Underground Elec - Event E4	3	24-Aug-18	28-Aug-18	18
S1B4-8N72	Deep Underground Elec - Event B4	6	30-Aug-18	07-Sep-18	13
S1E5-8N72	Deep Underground Elec - Event E5	5	11-Oct-18	17-Oct-18	8
S1B5-8N72	Deep Underground Elec - Event B5	5	15-Oct-18	19-Oct-18	10
S1D3-8N72	Deep Underground Elec - Event D3	5	06-Nov-18	13-Nov-18	20
S1C3-8N72	Deep Underground Elec - Event C3	5	07-Nov-18	14-Nov-18	14
FRP Slab on Grade					
000 Event Level					
S1A0-8P1E	FRP Slab On Grade - Event A	30	27-Jul-18	07-Sep-18	31
S1F0-8P1E	FRP Slab On Grade - Event F	40	24-Aug-18	19-Oct-18	31
S1B0-8P1E	FRP Slab On Grade - Event B	60	21-Sep-18	18-Dec-18	22
S1E0-8P1E	FRP Slab On Grade - Event E	60	22-Oct-18	18-Jan-19	31
S1C0-8P1E	FRP Slab On Grade - Event C	40	19-Dec-18	14-Feb-19	22
S1D0-8P1E	FRP Slab On Grade - Event D	40	01-Feb-19	29-Mar-19	22
S1L1-8P1E	FRP Slab On Grade/Field Rail Install - Exterior Field Tray	30	06-Jun-19	18-Jul-19	40
S1L5-8P1E	FRP Slab On Grade - Inner Bowl A/F	20	09-Aug-19	06-Sep-19	0
S1L3-8P1E	FRP Slab On Grade - Inner Bowl	40	10-Sep-19	04-Nov-19	4
S1L4-8P1E10	FRP Slab On Grade/Field Rail Install - Interior Field Tray	40	05-Nov-19	06-Jan-20	0
S1L2-8P1E	FRP Slab On Grade/Field Rail Install - Under Structure C/D	20	07-Jan-20	03-Feb-20	0
FRP Concrete Walls					
000 Event Level					
Structure					
S1A1-8P20	Concrete Core Walls - Core 3 Event to Mezz (Summary)	13	26-Mar-18	11-Apr-18	15
S1F1-8P20	Concrete Core Walls - Core 2 Event to Mezz (Summary)	11	02-Apr-18	16-Apr-18	13
S1B1-8P20	Concrete Core Walls - Core 4 Event to Mezz (Summary)	15	11-Apr-18	01-May-18	19
S1E1-8P20	Concrete Core Walls - Core 1 Event to Mezz (Summary)	11	20-Apr-18	04-May-18	20
S1B2-8P20	Concrete Core Walls - Core 5 Event to Mezz (Summary)	11	01-May-18	15-May-18	32
S1E2-8P20	Concrete Core Walls - Core 8 Event to Mezz (Summary)	11	08-May-18	22-May-18	31
S1C1-8P20	Concrete Core Walls - Core 6 Event to Mezz (Summary)	11	18-May-18	04-Jun-18	48
S1D1-8P20	Concrete Core Walls - Core 7 Event to Mezz (Summary)	11	04-Jun-18	18-Jun-18	43
S1AC5-8P2B0	Core Walls - Set Inside Lead Panels - Event to Lower Mezz Core #3	2	26-Mar-18	27-Mar-18	17
S1FC4-8P2B0	Core Walls - Set Inside Lead Panels - Event to Lower Mezz Core #2	2	02-Apr-18	03-Apr-18	13
S1BC6-8P2B0	Core Walls - Set Inside Lead Panels - Event to Lower Mezz Core #4	2	11-Apr-18	12-Apr-18	23
S1EC3-8P2B0	Core Walls - Set Inside Lead Panels - Event to Lower Mezz Core #1	2	20-Apr-18	23-Apr-18	20
S1BC7-8P2B0	Core Walls - Set Inside Lead Panels - Event to Lower Mezz Core #5	2	01-May-18	02-May-18	32
S1EC2-8P2B0	Core Walls - Set Inside Lead Panels - Event to Lower Mezz Core #8	2	08-May-18	09-May-18	31
S1CC8-8P2B0	Core Walls - Set Inside Lead Panels - Event to Lower Mezz Core #6	2	18-May-18	21-May-18	48
S1DC1-8P2B0	Core Walls - Set Inside Lead Panels - Event to Lower Mezz Core #7	2	04-Jun-18	05-Jun-18	43
S1AC5-8P2B2	Core Walls - Install Embeds - Event to Lower Mezz Core #3	1	29-Mar-18	29-Mar-18	15
S1FC4-8P2B2	Core Walls - Install Embeds - Event to Lower Mezz Core #2	1	03-Apr-18	03-Apr-18	13

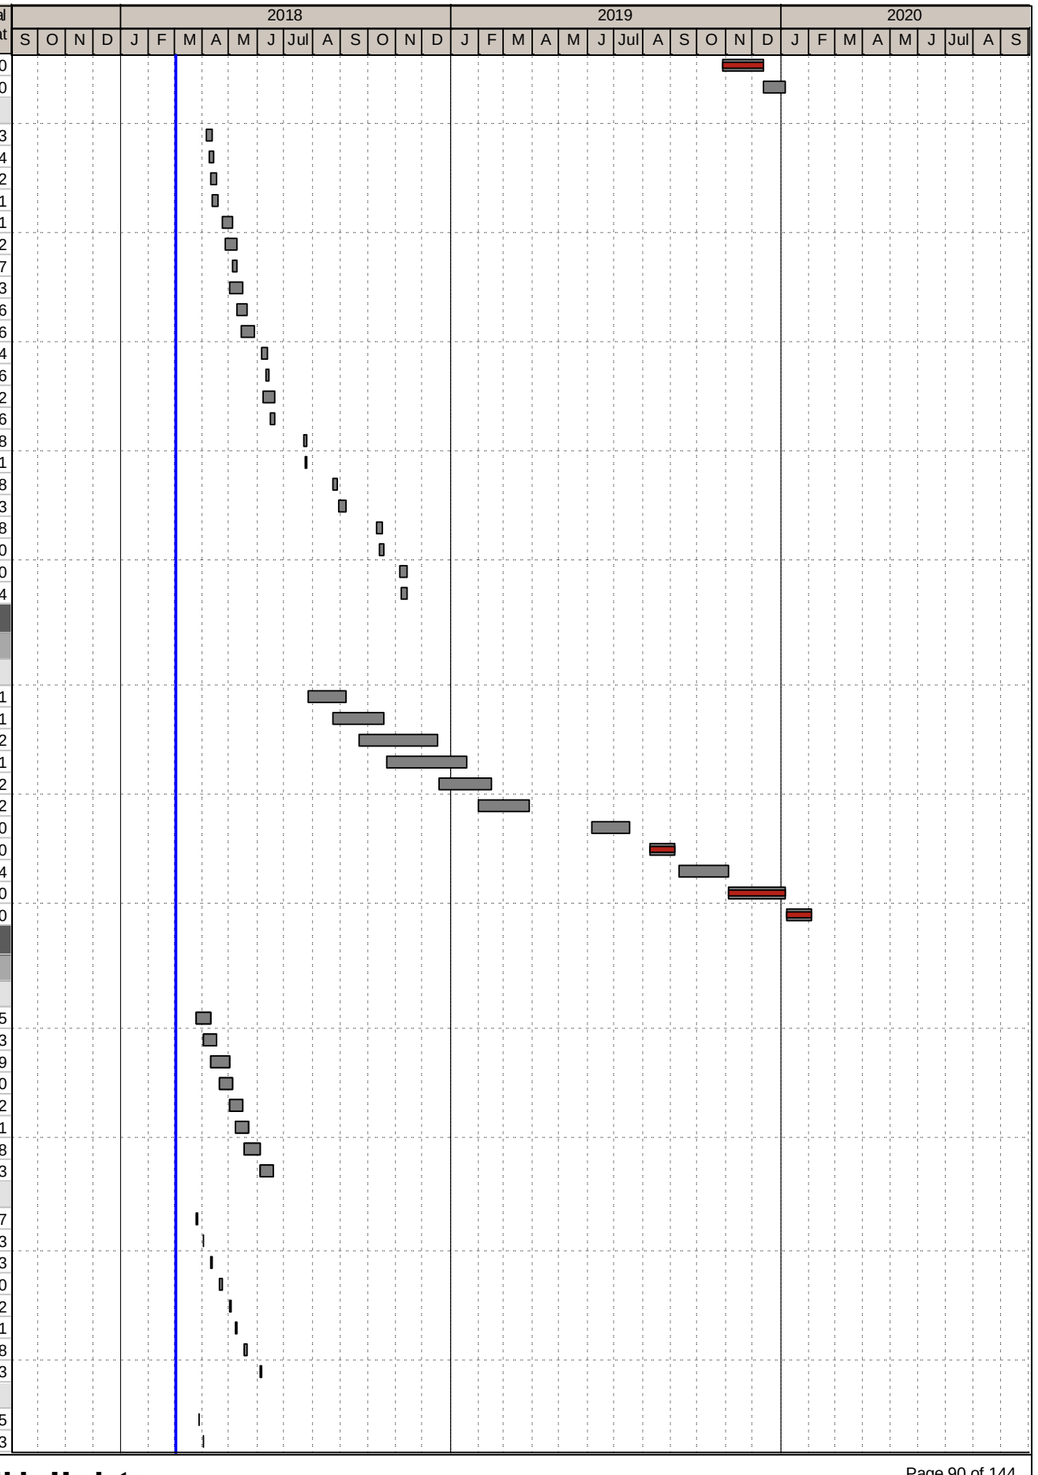

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S1BC6-8P2B2	Core Walls - Install Embeds - Event to Lower Mezz Core #4	1	18-Apr-18	18-Apr-18	19
S1EC3-8P2B2	Core Walls - Install Embeds - Event to Lower Mezz Core #1	1	23-Apr-18	23-Apr-18	20
S1BC7-8P2B2	Core Walls - Install Embeds - Event to Lower Mezz Core #5	1	02-May-18	02-May-18	32
S1EC2-8P2B2	Core Walls - Install Embeds - Event to Lower Mezz Core #8	1	09-May-18	09-May-18	31
S1CC8-8P2B2	Core Walls - Install Embeds - Event to Lower Mezz Core #6	1	21-May-18	21-May-18	48
S1DC1-8P2B2	Core Walls - Install Embeds - Event to Lower Mezz Core #7	1	05-Jun-18	05-Jun-18	43
Reinforce					
S1AC5-8P2BC	Core Walls - Install Rebar - Event to Lower Mezz Core #3	3	30-Mar-18	03-Apr-18	15
S1FC4-8P2BC	Core Walls - Install Rebar - Event to Lower Mezz Core #2	3	04-Apr-18	06-Apr-18	13
S1BC6-8P2BC	Core Walls - Install Rebar - Event to Lower Mezz Core #4	3	19-Apr-18	23-Apr-18	19
S1EC3-8P2BC	Core Walls - Install Rebar - Event to Lower Mezz Core #1	3	24-Apr-18	26-Apr-18	20
S1BC7-8P2BC	Core Walls - Install Rebar - Event to Lower Mezz Core #5	3	03-May-18	07-May-18	32
S1EC2-8P2BC	Core Walls - Install Rebar - Event to Lower Mezz Core #8	3	10-May-18	14-May-18	31
S1CC8-8P2BC	Core Walls - Install Rebar - Event to Lower Mezz Core #6	3	22-May-18	24-May-18	48
S1DC1-8P2BC	Core Walls - Install Rebar - Event to Lower Mezz Core #7	3	06-Jun-18	08-Jun-18	43
S1AC5-8P2B3	Core Walls - Bulkheads & Blockouts - Event to Lower Mezz Core #3	4	30-Mar-18	04-Apr-18	15
S1FC4-8P2B3	Core Walls - Bulkheads & Blockouts - Event to Lower Mezz Core #2	4	04-Apr-18	09-Apr-18	13
S1BC6-8P2B3	Core Walls - Bulkheads & Blockouts - Event to Lower Mezz Core #4	4	19-Apr-18	24-Apr-18	19
S1EC3-8P2B3	Core Walls - Bulkheads & Blockouts - Event to Lower Mezz Core #1	4	24-Apr-18	27-Apr-18	20
S1BC7-8P2B3	Core Walls - Bulkheads & Blockouts - Event to Lower Mezz Core #5	4	03-May-18	08-May-18	32
S1EC2-8P2B3	Core Walls - Bulkheads & Blockouts - Event to Lower Mezz Core #8	4	10-May-18	15-May-18	31
S1CC8-8P2B3	Core Walls - Bulkheads & Blockouts - Event to Lower Mezz Core #6	4	22-May-18	25-May-18	48
S1DC1-8P2B3	Core Walls - Bulkheads & Blockouts - Event to Lower Mezz Core #7	4	06-Jun-18	11-Jun-18	43
Form 2nd Side					
S1AC5-8P2BN	Core Walls - Inspect & Close Wall - Event to Lower Mezz Core #3	4	03-Apr-18	06-Apr-18	15
S1FC4-8P2BN	Core Walls - Inspect & Close Wall - Event to Lower Mezz Core #2	4	06-Apr-18	11-Apr-18	13
S1BC6-8P2BN	Core Walls - Inspect & Close Wall - Event to Lower Mezz Core #4	4	23-Apr-18	26-Apr-18	19
S1EC3-8P2BN	Core Walls - Inspect & Close Wall - Event to Lower Mezz Core #1	4	26-Apr-18	01-May-18	20
S1BC7-8P2BN	Core Walls - Inspect & Close Wall - Event to Lower Mezz Core #5	4	07-May-18	10-May-18	32
S1EC2-8P2BN	Core Walls - Inspect & Close Wall - Event to Lower Mezz Core #8	4	14-May-18	17-May-18	31
S1CC8-8P2BN	Core Walls - Inspect & Close Wall - Event to Lower Mezz Core #6	4	24-May-18	30-May-18	48
S1DC1-8P2BN	Core Walls - Inspect & Close Wall - Event to Lower Mezz Core #7	4	08-Jun-18	13-Jun-18	43
Pour					
S1AC5-8P2BH	Core Walls - Pour - Event to Lower Mezz Core #3	1	09-Apr-18	09-Apr-18	15
S1FC4-8P2BH	Core Walls - Pour - Event to Lower Mezz Core #2	1	12-Apr-18	12-Apr-18	13
S1BC6-8P2BH	Core Walls - Pour - Event to Lower Mezz Core #4	1	27-Apr-18	27-Apr-18	19
S1EC3-8P2BH	Core Walls - Pour - Event to Lower Mezz Core #1	1	02-May-18	02-May-18	20
S1BC7-8P2BH	Core Walls - Pour - Event to Lower Mezz Core #5	1	11-May-18	11-May-18	32
S1EC2-8P2BH	Core Walls - Pour - Event to Lower Mezz Core #8	1	18-May-18	18-May-18	31
S1CC8-8P2BH	Core Walls - Pour - Event to Lower Mezz Core #6	1	31-May-18	31-May-18	48
S1DC1-8P2BH	Core Walls - Pour - Event to Lower Mezz Core #7	1	14-Jun-18	14-Jun-18	43
Strip					
S1AC5-8P2BJ	Core Walls - Strip - Event to Lower Mezz Core #3	2	10-Apr-18	11-Apr-18	15
S1FC4-8P2BJ	Core Walls - Strip - Event to Lower Mezz Core #2	2	13-Apr-18	16-Apr-18	13
S1BC6-8P2BJ	Core Walls - Strip - Event to Lower Mezz Core #4	2	30-Apr-18	01-May-18	19
S1EC3-8P2BJ	Core Walls - Strip - Event to Lower Mezz Core #1	2	03-May-18	04-May-18	20
S1BC7-8P2BJ	Core Walls - Strip - Event to Lower Mezz Core #5	2	14-May-18	15-May-18	32
S1EC2-8P2BJ	Core Walls - Strip - Event to Lower Mezz Core #8	2	21-May-18	22-May-18	31
S1CC8-8P2BJ	Core Walls - Strip - Event to Lower Mezz Core #6	2	01-Jun-18	04-Jun-18	48
S1DC1-8P2BJ	Core Walls - Strip - Event to Lower Mezz Core #7	2	15-Jun-18	18-Jun-18	43
050 Lower Mezz Level					
Structure					
S2A1-8P20	Concrete Core Walls - Core 3 Mezz to Main (Summary)	9	21-May-18	01-Jun-18	5
S2F1-8P20	Concrete Core Walls - Core 2 Mezz to Main (Summary)	10	23-May-18	06-Jun-18	5
S2B1-8P20	Concrete Core Walls - Core 4 Mezz to Main (Summary)	10	15-Jun-18	28-Jun-18	4
S2E1-8P20	Concrete Core Walls - Core 1 Mezz to Main (Summary)	10	15-Jun-18	28-Jun-18	7
S2B2-8P20	Concrete Core Walls - Core 5 Mezz to Main (Summary)	10	13-Jul-18	26-Jul-18	16
S2E2-8P20	Concrete Core Walls - Core 8 Mezz to Main (Summary)	10	16-Jul-18	27-Jul-18	15
S2C1-8P20	Concrete Core Walls - Core 6 Mezz to Main (Summary)	10	07-Aug-18	20-Aug-18	20
S2D1-8P20	Concrete Core Walls - Core 7 Mezz to Main (Summary)	10	08-Aug-18	21-Aug-18	23

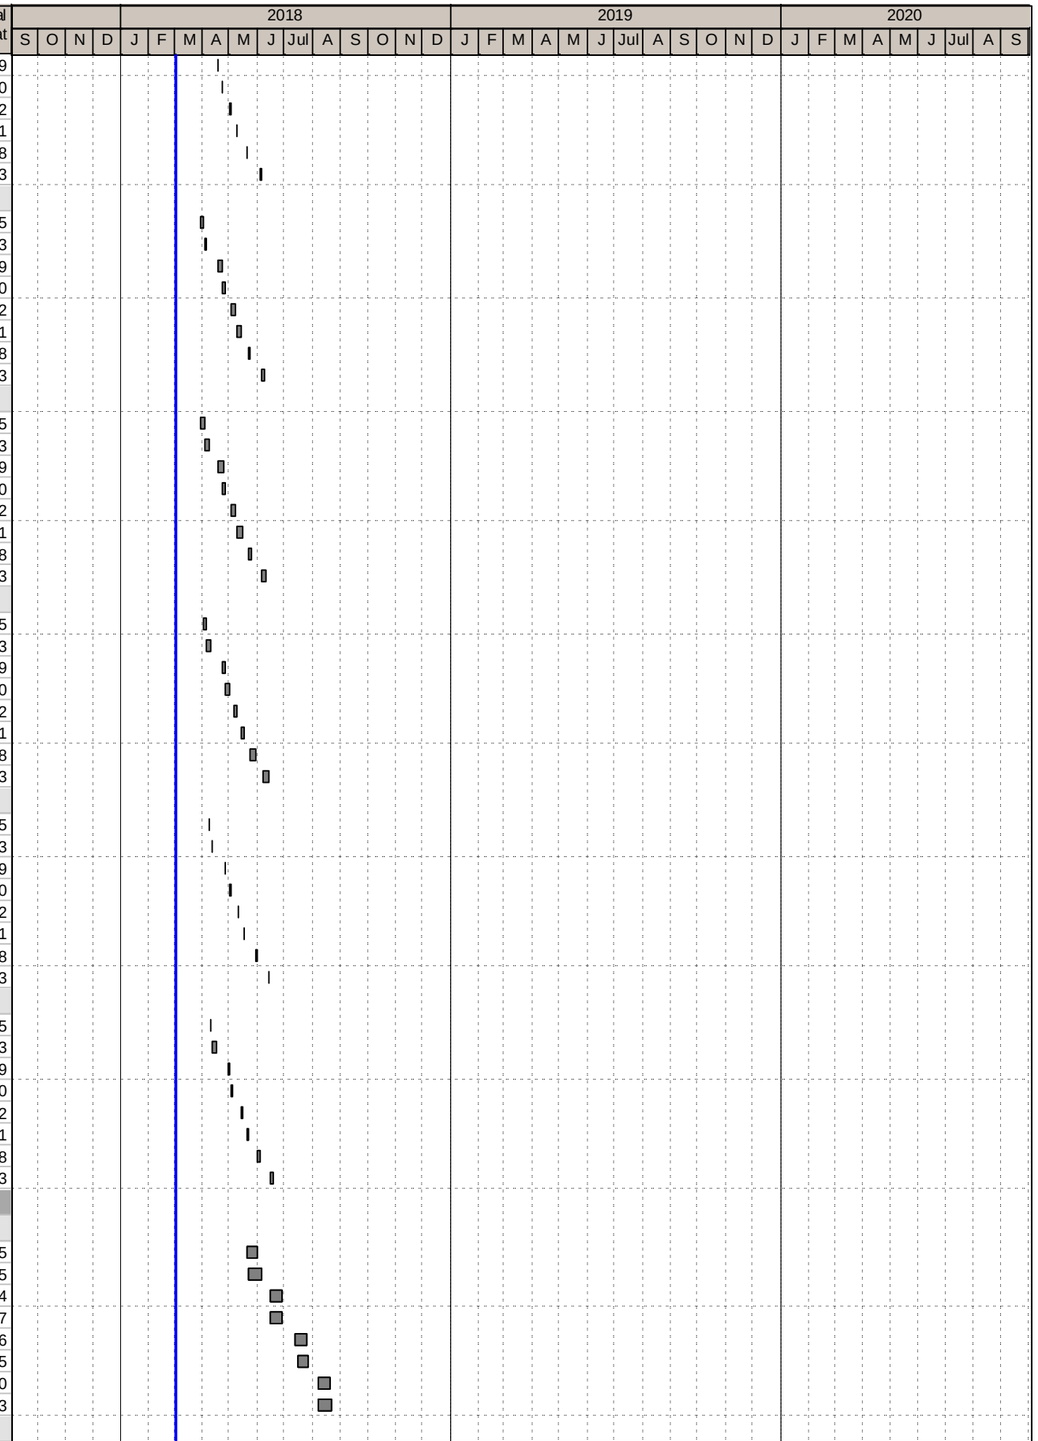

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S2AC5-8P2B0	Core Walls - Set Inside Lead Panels - Lower Mezz to Main Conc Core #3	3	19-May-18	22-May-18	6
S2FC4-8P2B0	Core Walls - Set Inside Lead Panels - Lower Mezz to Main Conc Core #2	3	23-May-18	25-May-18	6
S2BC6-8P2B0	Core Walls - Set Inside Lead Panels - Lower Mezz to Main Conc Core #4	3	15-Jun-18	18-Jun-18	5
S2EC3-8P2B0	Core Walls - Set Inside Lead Panels - Lower Mezz to Main Conc Core #1	3	15-Jun-18	18-Jun-18	9
S2BC7-8P2B0	Core Walls - Set Inside Lead Panels - Lower Mezz to Main Conc Core #5	3	13-Jul-18	16-Jul-18	19
S2EC2-8P2B0	Core Walls - Set Inside Lead Panels - Lower Mezz to Main Conc Core #8	3	14-Jul-18	17-Jul-18	18
S2CC8-8P2B0	Core Walls - Set Inside Lead Panels - Lower Mezz to Main Conc Core #6	3	07-Aug-18	09-Aug-18	24
S2DC1-8P2B0	Core Walls - Set Inside Lead Panels - Lower Mezz to Main Conc Core #7	3	08-Aug-18	10-Aug-18	28
S2AC5-8P2B2	Core Walls - Install Embeds - Lower Mezz to Main Conc Core #3	2	21-May-18	22-May-18	8
S2FC4-8P2B2	Core Walls - Install Embeds - Lower Mezz to Main Conc Core #2	2	24-May-18	25-May-18	8
S2BC6-8P2B2	Core Walls - Install Embeds - Lower Mezz to Main Conc Core #4	2	16-Jun-18	18-Jun-18	7
S2EC3-8P2B2	Core Walls - Install Embeds - Lower Mezz to Main Conc Core #1	2	16-Jun-18	18-Jun-18	11
S2BC7-8P2B2	Core Walls - Install Embeds - Lower Mezz to Main Conc Core #5	2	14-Jul-18	16-Jul-18	21
S2EC2-8P2B2	Core Walls - Install Embeds - Lower Mezz to Main Conc Core #8	2	16-Jul-18	17-Jul-18	20
S2CC8-8P2B2	Core Walls - Install Embeds - Lower Mezz to Main Conc Core #6	2	08-Aug-18	09-Aug-18	26
S2DC1-8P2B2	Core Walls - Install Embeds - Lower Mezz to Main Conc Core #7	2	09-Aug-18	10-Aug-18	30
Reinforce					
S2AC5-8P2BC	Core Walls - Install Rebar - Lower Mezz to Main Conc Core #3	3	23-May-18	25-May-18	6
S2FC4-8P2BC	Core Walls - Install Rebar - Lower Mezz to Main Conc Core #2	3	26-May-18	30-May-18	6
S2BC6-8P2BC	Core Walls - Install Rebar - Lower Mezz to Main Conc Core #4	3	19-Jun-18	21-Jun-18	5
S2EC3-8P2BC	Core Walls - Install Rebar - Lower Mezz to Main Conc Core #1	3	19-Jun-18	21-Jun-18	9
S2BC7-8P2BC	Core Walls - Install Rebar - Lower Mezz to Main Conc Core #5	3	17-Jul-18	19-Jul-18	19
S2EC2-8P2BC	Core Walls - Install Rebar - Lower Mezz to Main Conc Core #8	3	18-Jul-18	20-Jul-18	18
S2CC8-8P2BC	Core Walls - Install Rebar - Lower Mezz to Main Conc Core #6	3	10-Aug-18	13-Aug-18	24
S2DC1-8P2BC	Core Walls - Install Rebar - Lower Mezz to Main Conc Core #7	3	11-Aug-18	14-Aug-18	28
S2AC5-8P2B3	Core Walls - Bulkheads & Blockouts - Lower Mezz to Main Conc Core #3	4	23-May-18	26-May-18	6
S2FC4-8P2B3	Core Walls - Bulkheads & Blockouts - Lower Mezz to Main Conc Core #2	4	26-May-18	31-May-18	6
S2BC6-8P2B3	Core Walls - Bulkheads & Blockouts - Lower Mezz to Main Conc Core #4	4	19-Jun-18	22-Jun-18	5
S2EC3-8P2B3	Core Walls - Bulkheads & Blockouts - Lower Mezz to Main Conc Core #1	4	19-Jun-18	22-Jun-18	9
S2BC7-8P2B3	Core Walls - Bulkheads & Blockouts - Lower Mezz to Main Conc Core #5	4	17-Jul-18	20-Jul-18	19
S2EC2-8P2B3	Core Walls - Bulkheads & Blockouts - Lower Mezz to Main Conc Core #8	4	18-Jul-18	21-Jul-18	18
S2CC8-8P2B3	Core Walls - Bulkheads & Blockouts - Lower Mezz to Main Conc Core #6	4	10-Aug-18	14-Aug-18	24
S2DC1-8P2B3	Core Walls - Bulkheads & Blockouts - Lower Mezz to Main Conc Core #7	4	11-Aug-18	15-Aug-18	28
Form 2nd Side					
S2AC5-8P2BN	Core Walls - Inspect & Close Wall - Lower Mezz to Main Conc Core #3	4	25-May-18	30-May-18	6
S2FC4-8P2BN	Core Walls - Inspect & Close Wall - Lower Mezz to Main Conc Core #2	4	30-May-18	02-Jun-18	6
S2BC6-8P2BN	Core Walls - Inspect & Close Wall - Lower Mezz to Main Conc Core #4	4	21-Jun-18	25-Jun-18	5
S2EC3-8P2BN	Core Walls - Inspect & Close Wall - Lower Mezz to Main Conc Core #1	4	21-Jun-18	25-Jun-18	9
S2BC7-8P2BN	Core Walls - Inspect & Close Wall - Lower Mezz to Main Conc Core #5	4	19-Jul-18	23-Jul-18	19
S2EC2-8P2BN	Core Walls - Inspect & Close Wall - Lower Mezz to Main Conc Core #8	4	20-Jul-18	24-Jul-18	18
S2CC8-8P2BN	Core Walls - Inspect & Close Wall - Lower Mezz to Main Conc Core #6	4	13-Aug-18	16-Aug-18	24
S2DC1-8P2BN	Core Walls - Inspect & Close Wall - Lower Mezz to Main Conc Core #7	4	14-Aug-18	17-Aug-18	28
Pour					
S2AC5-8P2BH	Core Walls - Pour - Lower Mezz to Main Conc Core #3	1	31-May-18	31-May-18	6
S2FC4-8P2BH	Core Walls - Pour - Lower Mezz to Main Conc Core #2	1	04-Jun-18	04-Jun-18	6
S2BC6-8P2BH	Core Walls - Pour - Lower Mezz to Main Conc Core #4	1	26-Jun-18	26-Jun-18	5
S2EC3-8P2BH	Core Walls - Pour - Lower Mezz to Main Conc Core #1	1	26-Jun-18	26-Jun-18	9
S2BC7-8P2BH	Core Walls - Pour - Lower Mezz to Main Conc Core #5	1	24-Jul-18	24-Jul-18	19
S2EC2-8P2BH	Core Walls - Pour - Lower Mezz to Main Conc Core #8	1	25-Jul-18	25-Jul-18	18
S2CC8-8P2BH	Core Walls - Pour - Lower Mezz to Main Conc Core #6	1	17-Aug-18	17-Aug-18	24
S2DC1-8P2BH	Core Walls - Pour - Lower Mezz to Main Conc Core #7	1	18-Aug-18	18-Aug-18	28
Strip					
S2AC5-8P2BJ	Core Walls - Strip - Lower Mezz to Main Conc Core #3	2	01-Jun-18	02-Jun-18	6
S2FC4-8P2BJ	Core Walls - Strip - Lower Mezz to Main Conc Core #2	2	05-Jun-18	06-Jun-18	6
S2BC6-8P2BJ	Core Walls - Strip - Lower Mezz to Main Conc Core #4	2	27-Jun-18	28-Jun-18	5
S2EC3-8P2BJ	Core Walls - Strip - Lower Mezz to Main Conc Core #1	2	27-Jun-18	28-Jun-18	9
S2BC7-8P2BJ	Core Walls - Strip - Lower Mezz to Main Conc Core #5	2	25-Jul-18	26-Jul-18	19
S2EC2-8P2BJ	Core Walls - Strip - Lower Mezz to Main Conc Core #8	2	26-Jul-18	27-Jul-18	18
S2CC8-8P2BJ	Core Walls - Strip - Lower Mezz to Main Conc Core #6	2	18-Aug-18	20-Aug-18	24
S2DC1-8P2BJ	Core Walls - Strip - Lower Mezz to Main Conc Core #7	2	20-Aug-18	21-Aug-18	28

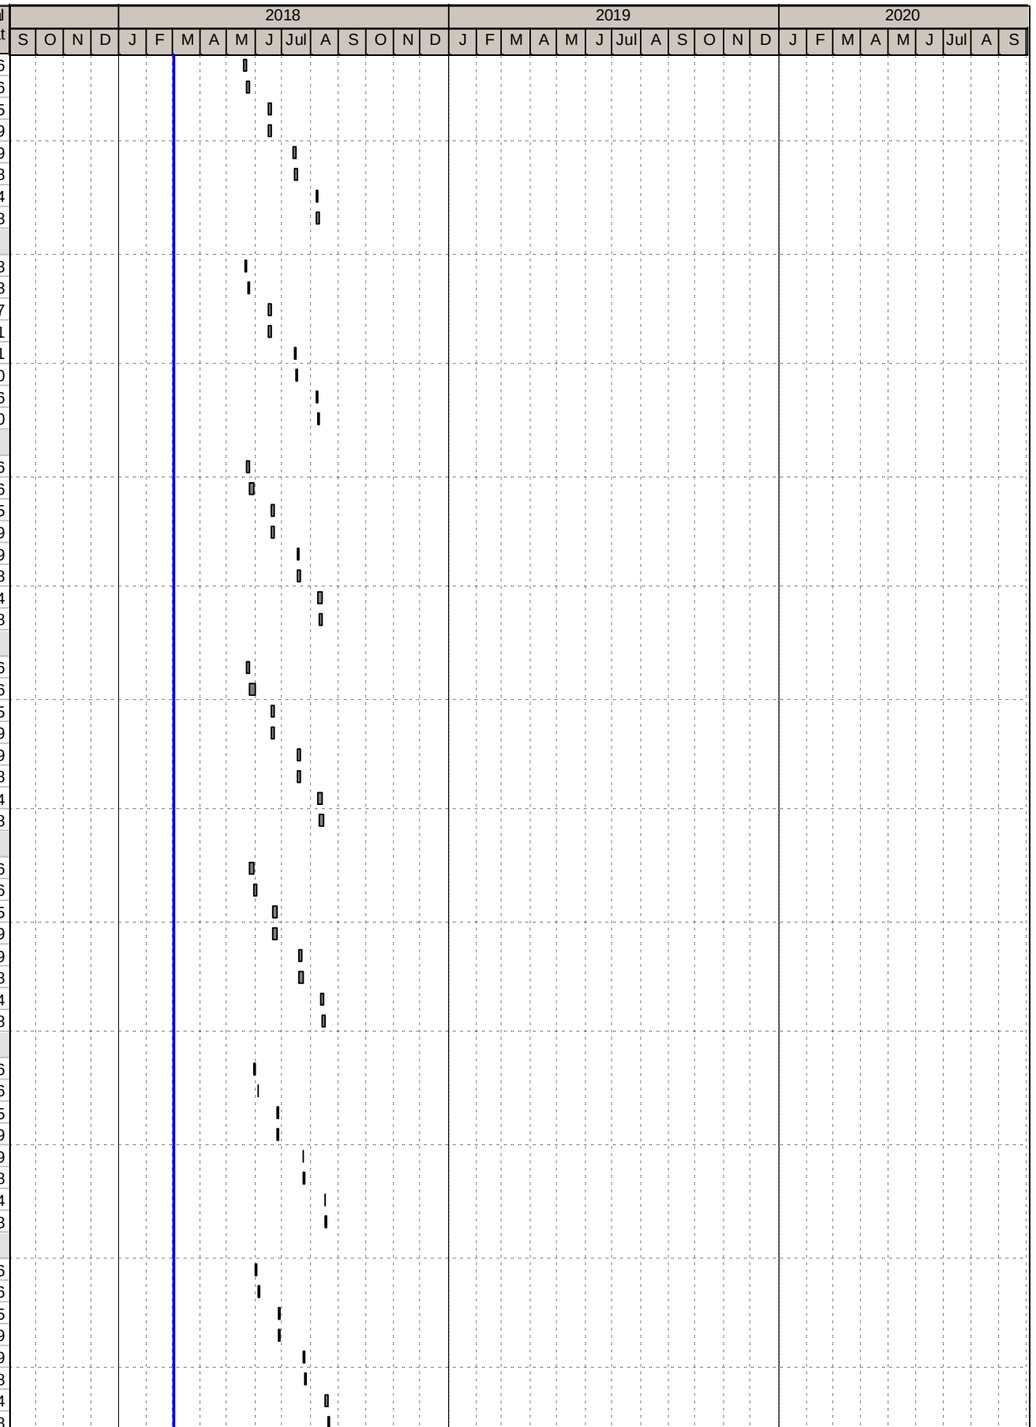

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
100 Main Concourse					
Structure					
S3F1-8P50	Concrete Core Walls - Core 2 Main to TOC (Summary)	25	02-Jul-18	06-Aug-18	23
S3A1-8P50	Concrete Core Walls - Core 3 Main to TOC (Summary)	26	03-Jul-18	08-Aug-18	7
S3B1-8P50	Concrete Core Walls - Core 4 Main to TOC (Summary)	22	31-Jul-18	29-Aug-18	10
S3E1-8P50	Concrete Core Walls - Core 1 Main to TOC (Summary)	29	30-Jul-18	07-Sep-18	11
S3B2-8P50	Concrete Core Walls - Core 5 Main to TOC (Summary)	21	17-Sep-18	15-Oct-18	7
S3E2-8P50	Concrete Core Walls - Core 8 Main to TOC (Summary)	30	17-Sep-18	26-Oct-18	8
S3C1-8P50	Concrete Core Walls - Core 6 Main to TOC (Summary)	21	08-Oct-18	05-Nov-18	4
S3D1-8P50	Concrete Core Walls - Core 7 Main to TOC (Summary)	21	08-Oct-18	05-Nov-18	17
Core Walls Above Main Conc					
S3F1-8P2B6	Concrete Core Walls - Clean & Survey - Core 2 (Main to TOC)	2	07-Aug-18	08-Aug-18	23
S3A1-8P2B6	Concrete Core Walls - Clean & Survey - Core 3 (Main to TOC)	2	09-Aug-18	10-Aug-18	7
S3B1-8P2B6	Concrete Core Walls - Clean & Survey - Core 4 (Main to TOC)	2	30-Aug-18	31-Aug-18	10
S3E1-8P2B6	Concrete Core Walls - Clean & Survey - Core 1 (Main to TOC)	2	10-Sep-18	11-Sep-18	11
S3B2-8P2B6	Concrete Core Walls - Clean & Survey - Core 5 (Main to TOC)	2	16-Oct-18	17-Oct-18	7
S3E2-8P2B6	Concrete Core Walls - Clean & Survey - Core 8 (Main to TOC)	2	29-Oct-18	30-Oct-18	8
S3C1-8P2B6	Concrete Core Walls - Clean & Survey - Core 6 (Main to TOC)	2	06-Nov-18	07-Nov-18	4
S3D1-8P2B6	Concrete Core Walls - Clean & Survey - Core 7 (Main to TOC)	2	06-Nov-18	07-Nov-18	17
S3F1-8P2B7	Concrete Core Walls - Survey & Pre-Weld Clips Truss Column Side - Core 2 (Main to TOC)	3	07-Aug-18	09-Aug-18	23
S3A1-8P2B7	Concrete Core Walls - Survey & Pre-Weld Clips Truss Column Side - Core 3 (Main to TOC)	3	09-Aug-18	13-Aug-18	7
S3B1-8P2B7	Concrete Core Walls - Survey & Pre-Weld Clips Truss Column Side - Core 4 (Main to TOC)	3	30-Aug-18	04-Sep-18	10
S3E1-8P2B7	Concrete Core Walls - Survey & Pre-Weld Clips Truss Column Side - Core 1 (Main to TOC)	3	10-Sep-18	12-Sep-18	11
S3B2-8P2B7	Concrete Core Walls - Survey & Pre-Weld Clips Truss Column Side - Core 5 (Main to TOC)	3	16-Oct-18	18-Oct-18	7
S3E2-8P2B7	Concrete Core Walls - Survey & Pre-Weld Clips Truss Column Side - Core 8 (Main to TOC)	3	29-Oct-18	31-Oct-18	8
S3C1-8P2B7	Concrete Core Walls - Survey & Pre-Weld Clips Truss Column Side - Core 6 (Main to TOC)	3	06-Nov-18	08-Nov-18	4
S3D1-8P2B7	Concrete Core Walls - Survey & Pre-Weld Clips Truss Column Side - Core 7 (Main to TOC)	3	06-Nov-18	08-Nov-18	17
S3F1-8P2B8	Concrete Core Walls - Pre-Weld Clips Bowl Framing Side - Core 2 (Main to TOC)	8	09-Aug-18	20-Aug-18	32
S3A1-8P2B8	Concrete Core Walls - Pre-Weld Clips Bowl Framing Side - Core 3 (Main to TOC)	8	13-Aug-18	22-Aug-18	25
S3B1-8P2B8	Concrete Core Walls - Pre-Weld Clips Bowl Framing Side - Core 4 (Main to TOC)	8	04-Sep-18	13-Sep-18	12
S3E1-8P2B8	Concrete Core Walls - Pre-Weld Clips Bowl Framing Side - Core 1 (Main to TOC)	8	12-Sep-18	21-Sep-18	18
S3B2-8P2B8	Concrete Core Walls - Pre-Weld Clips Bowl Framing Side - Core 5 (Main to TOC)	8	18-Oct-18	29-Oct-18	11
S3E2-8P2B8	Concrete Core Walls - Pre-Weld Clips Bowl Framing Side - Core 8 (Main to TOC)	8	31-Oct-18	09-Nov-18	14
S3C1-8P2B8	Concrete Core Walls - Pre-Weld Clips Bowl Framing Side - Core 6 (Main to TOC)	8	08-Nov-18	20-Nov-18	10
S3D1-8P2B8	Concrete Core Walls - Pre-Weld Clips Bowl Framing Side - Core 7 (Main to TOC)	8	08-Nov-18	20-Nov-18	36
Lift 1					
S3FC4-8P2B0	Core Walls - Set Inside Lead Panels - Main Conc to Top Lift 1 Core #2	2	30-Jun-18	02-Jul-18	28
S3AC5-8P2B0	Core Walls - Set Inside Lead Panels - Main Conc to Top Lift 1 Core #3	2	03-Jul-18	05-Jul-18	9
S3EC3-8P2B0	Core Walls - Set Inside Lead Panels - Main Conc to Top Lift 1 Core #1	2	28-Jul-18	30-Jul-18	13
S3BC6-8P2B0	Core Walls - Set Inside Lead Panels - Main Conc to Top Lift 1 Core #4	2	31-Jul-18	01-Aug-18	12
S3BC7-8P2B0	Core Walls - Set Inside Lead Panels - Main Conc to Top Lift 1 Core #5	2	15-Sep-18	17-Sep-18	8
S3EC2-8P2B0	Core Walls - Set Inside Lead Panels - Main Conc to Top Lift 1 Core #8	2	15-Sep-18	17-Sep-18	10
S3CC8-8P2B0	Core Walls - Set Inside Lead Panels - Main Conc to Top Lift 1 Core #6	2	06-Oct-18	08-Oct-18	6
S3DC1-8P2B0	Core Walls - Set Inside Lead Panels - Main Conc to Top Lift 1 Core #7	2	06-Oct-18	08-Oct-18	22
S3FC4-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 1 Core #2	3	02-Jul-18	05-Jul-18	28
S3AC5-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 1 Core #3	3	05-Jul-18	07-Jul-18	9
S3EC3-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 1 Core #1	3	30-Jul-18	01-Aug-18	13
S3BC6-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 1 Core #4	3	01-Aug-18	03-Aug-18	12
S3BC7-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 1 Core #5	3	17-Sep-18	19-Sep-18	8
S3EC2-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 1 Core #8	3	17-Sep-18	19-Sep-18	10
S3CC8-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 1 Core #6	3	08-Oct-18	10-Oct-18	6
S3DC1-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 1 Core #7	3	08-Oct-18	10-Oct-18	22
Reinforce					
S3FC4-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 1 Core #2	2	02-Jul-18	03-Jul-18	28
S3AC5-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 1 Core #3	2	05-Jul-18	06-Jul-18	9
S3EC3-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 1 Core #1	2	30-Jul-18	31-Jul-18	13
S3BC6-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 1 Core #4	2	01-Aug-18	02-Aug-18	12

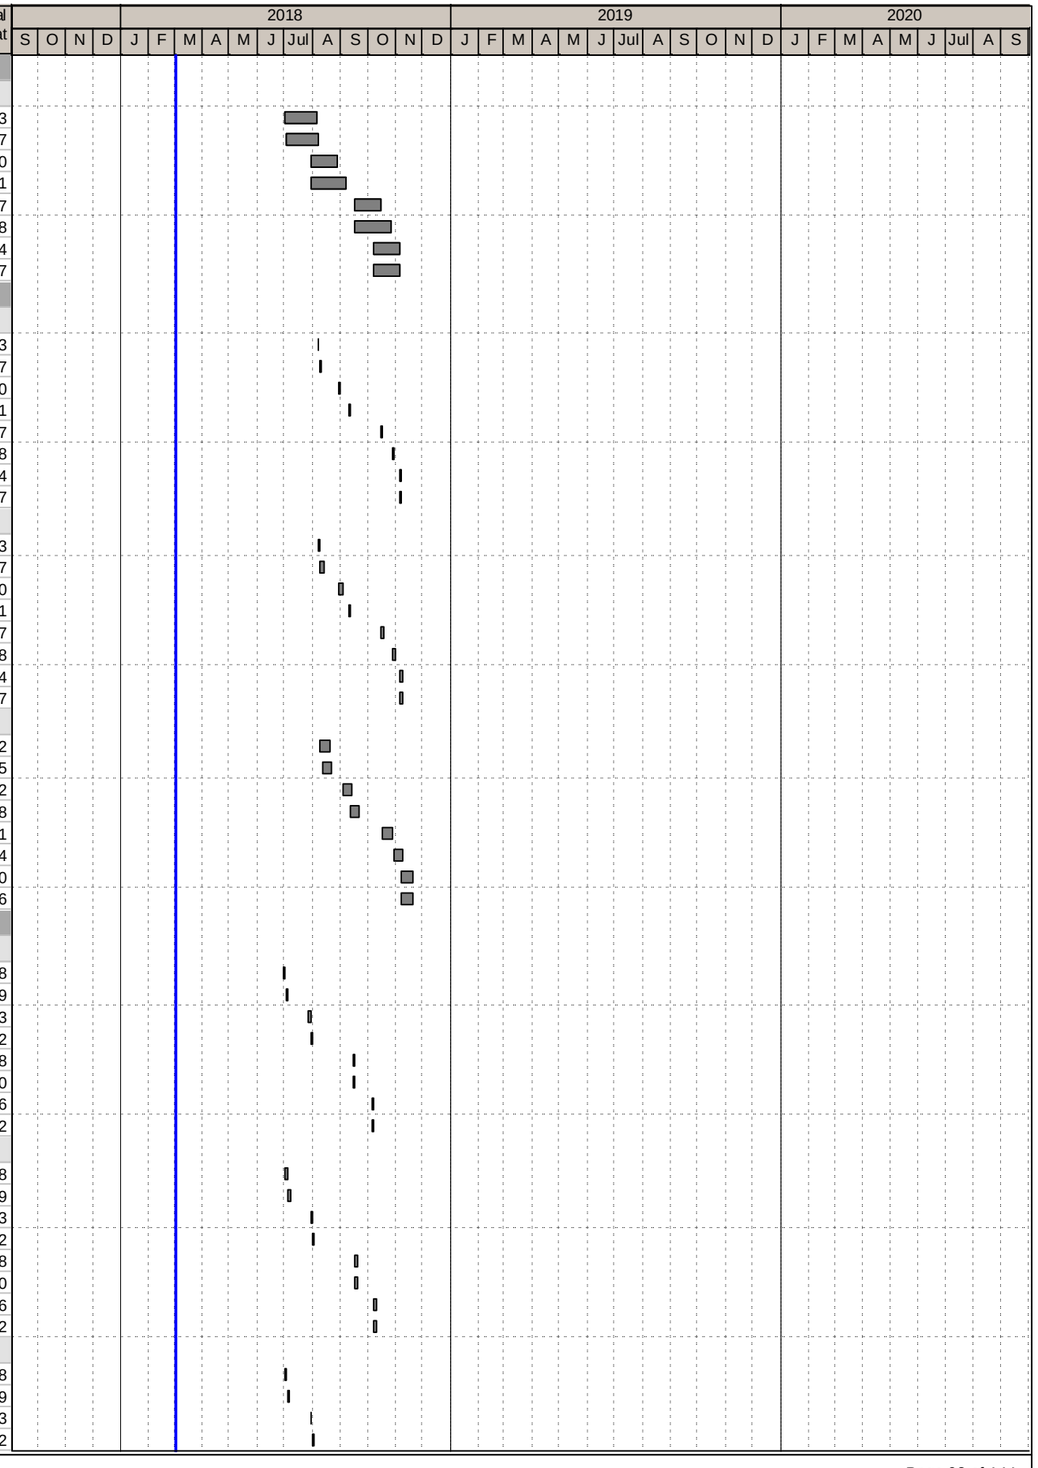

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S3BC7-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 1 Core #5	2	17-Sep-18	18-Sep-18	8
S3EC2-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 1 Core #8	2	17-Sep-18	18-Sep-18	10
S3CC8-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 1 Core #6	2	08-Oct-18	09-Oct-18	6
S3DC1-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 1 Core #7	2	08-Oct-18	09-Oct-18	22
S3FC4-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 1 Core #2	2	02-Jul-18	03-Jul-18	28
S3AC5-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 1 Core #3	2	05-Jul-18	06-Jul-18	9
S3EC3-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 1 Core #1	2	30-Jul-18	31-Jul-18	13
S3BC6-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 1 Core #4	2	01-Aug-18	02-Aug-18	12
S3BC7-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 1 Core #5	2	17-Sep-18	18-Sep-18	8
S3EC2-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 1 Core #8	2	17-Sep-18	18-Sep-18	10
S3CC8-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 1 Core #6	2	08-Oct-18	09-Oct-18	6
S3DC1-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 1 Core #7	2	08-Oct-18	09-Oct-18	22
S3FC4-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 1 Core #2	1	05-Jul-18	05-Jul-18	28
S3AC5-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 1 Core #3	1	07-Jul-18	07-Jul-18	9
S3EC3-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 1 Core #1	1	01-Aug-18	01-Aug-18	13
S3BC6-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 1 Core #4	1	03-Aug-18	03-Aug-18	12
S3BC7-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 1 Core #5	1	19-Sep-18	19-Sep-18	8
S3EC2-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 1 Core #8	1	19-Sep-18	19-Sep-18	10
S3CC8-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 1 Core #6	1	10-Oct-18	10-Oct-18	6
S3DC1-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 1 Core #7	1	10-Oct-18	10-Oct-18	22
Form 2nd Side					
S3FC4-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 1 Core #2	2	05-Jul-18	06-Jul-18	28
S3AC5-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 1 Core #3	2	07-Jul-18	09-Jul-18	9
S3EC3-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 1 Core #1	2	01-Aug-18	02-Aug-18	13
S3BC6-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 1 Core #4	2	03-Aug-18	04-Aug-18	12
S3BC7-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 1 Core #5	2	19-Sep-18	20-Sep-18	8
S3EC2-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 1 Core #8	2	19-Sep-18	20-Sep-18	10
S3CC8-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 1 Core #6	2	10-Oct-18	11-Oct-18	6
S3DC1-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 1 Core #7	2	10-Oct-18	11-Oct-18	22
Pour					
S3FC4-8P2BH	Core Walls - Pour - Main Conc to Top Lift 1 Core #2	1	06-Jul-18	06-Jul-18	28
S3AC5-8P2BH	Core Walls - Pour - Main Conc to Top Lift 1 Core #3	1	09-Jul-18	09-Jul-18	9
S3EC3-8P2BH	Core Walls - Pour - Main Conc to Top Lift 1 Core #1	1	02-Aug-18	02-Aug-18	13
S3BC6-8P2BH	Core Walls - Pour - Main Conc to Top Lift 1 Core #4	1	04-Aug-18	04-Aug-18	12
S3BC7-8P2BH	Core Walls - Pour - Main Conc to Top Lift 1 Core #5	1	20-Sep-18	20-Sep-18	8
S3EC2-8P2BH	Core Walls - Pour - Main Conc to Top Lift 1 Core #8	1	20-Sep-18	20-Sep-18	10
S3CC8-8P2BH	Core Walls - Pour - Main Conc to Top Lift 1 Core #6	1	11-Oct-18	11-Oct-18	6
S3DC1-8P2BH	Core Walls - Pour - Main Conc to Top Lift 1 Core #7	1	11-Oct-18	11-Oct-18	22
Strip					
S3FC4-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 1 Core #2	1	07-Jul-18	07-Jul-18	28
S3AC5-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 1 Core #3	1	10-Jul-18	10-Jul-18	9
S3EC3-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 1 Core #1	1	03-Aug-18	03-Aug-18	13
S3BC6-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 1 Core #4	1	06-Aug-18	06-Aug-18	12
S3BC7-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 1 Core #5	1	21-Sep-18	21-Sep-18	8
S3EC2-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 1 Core #8	1	21-Sep-18	21-Sep-18	10
S3CC8-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 1 Core #6	1	12-Oct-18	12-Oct-18	6
S3DC1-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 1 Core #7	1	12-Oct-18	12-Oct-18	22
Lift 2					
S4FC4-8P2B0	Core Walls - Jump Inside Panels - Main Conc to Top Lift 2 Core #2	1	07-Jul-18	07-Jul-18	28
S4AC5-8P2B0	Core Walls - Jump Inside Panels - Main Conc to Top Lift 2 Core #3	1	10-Jul-18	10-Jul-18	9
S4EC3-8P2B0	Core Walls - Jump Inside Panels - Main Conc to Top Lift 2 Core #1	1	03-Aug-18	03-Aug-18	13
S4BC6-8P2B0	Core Walls - Jump Inside Panels - Main Conc to Top Lift 2 Core #4	1	06-Aug-18	06-Aug-18	12
S4BC7-8P2B0	Core Walls - Jump Inside Panels - Main Conc to Top Lift 2 Core #5	1	21-Sep-18	21-Sep-18	8
S4EC2-8P2B0	Core Walls - Jump Inside Panels - Main Conc to Top Lift 2 Core #8	1	21-Sep-18	21-Sep-18	10
S4CC8-8P2B0	Core Walls - Jump Inside Panels - Main Conc to Top Lift 2 Core #6	1	12-Oct-18	12-Oct-18	6
S4DC1-8P2B0	Core Walls - Jump Inside Panels - Main Conc to Top Lift 2 Core #7	1	12-Oct-18	12-Oct-18	22
S4FC4-8P2B1	Core Walls - Roll up Inside / Square Up - Main Conc to Top Lift 2 Core #2	1	09-Jul-18	09-Jul-18	28
S4AC5-8P2B1	Core Walls - Roll up Inside / Square Up - Main Conc to Top Lift 2 Core #3	1	11-Jul-18	11-Jul-18	9

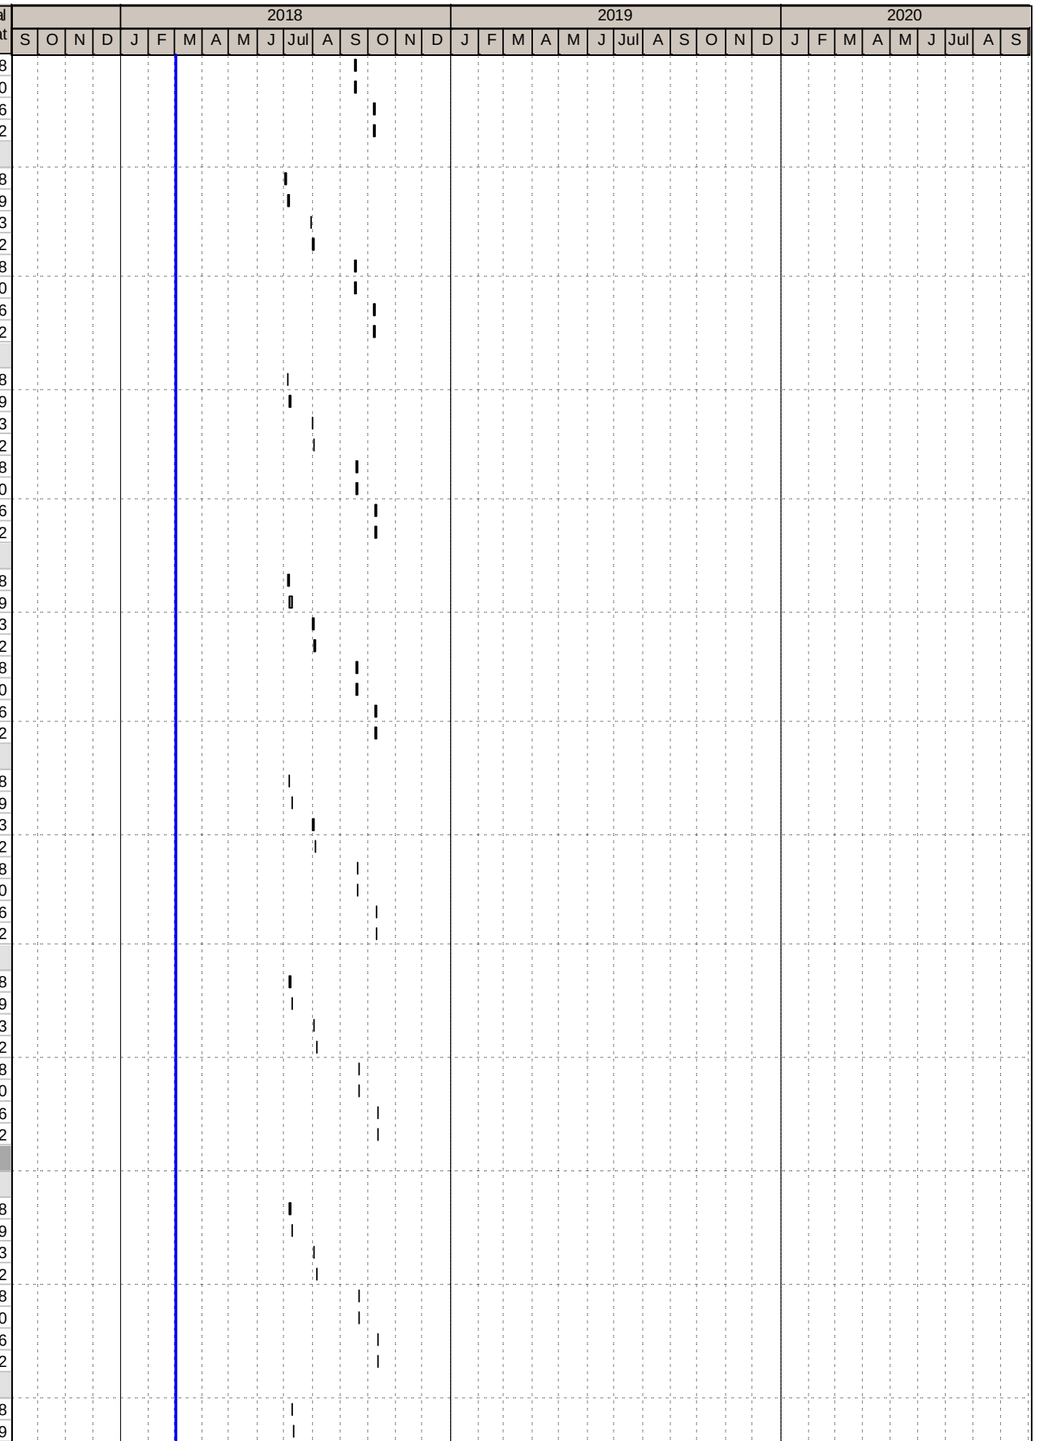

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S4EC3-8P2B1	Core Walls - Roll up Inside / Square Up - Main Conc to Top Lift 2 Core #1	1	04-Aug-18	04-Aug-18	13
S4BC6-8P2B1	Core Walls - Roll up Inside / Square Up - Main Conc to Top Lift 2 Core #4	1	07-Aug-18	07-Aug-18	12
S4BC7-8P2B1	Core Walls - Roll up Inside / Square Up - Main Conc to Top Lift 2 Core #5	1	22-Sep-18	22-Sep-18	8
S4EC2-8P2B1	Core Walls - Roll up Inside / Square Up - Main Conc to Top Lift 2 Core #8	1	22-Sep-18	22-Sep-18	10
S4CC8-8P2B1	Core Walls - Roll up Inside / Square Up - Main Conc to Top Lift 2 Core #6	1	13-Oct-18	13-Oct-18	6
S4DC1-8P2B1	Core Walls - Roll up Inside / Square Up - Main Conc to Top Lift 2 Core #7	1	13-Oct-18	13-Oct-18	22
S4FC4-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 2 Core #2	1	09-Jul-18	09-Jul-18	29
S4AC5-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 2 Core #3	1	11-Jul-18	11-Jul-18	10
S4EC3-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 2 Core #1	1	04-Aug-18	04-Aug-18	14
S4BC6-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 2 Core #4	1	07-Aug-18	07-Aug-18	13
S4BC7-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 2 Core #5	1	22-Sep-18	22-Sep-18	9
S4EC2-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 2 Core #8	1	22-Sep-18	22-Sep-18	11
S4CC8-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 2 Core #6	1	13-Oct-18	13-Oct-18	7
S4DC1-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 2 Core #7	1	13-Oct-18	13-Oct-18	23
Reinforce					
S4FC4-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 2 Core #2	2	09-Jul-18	10-Jul-18	28
S4AC5-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 2 Core #3	2	11-Jul-18	12-Jul-18	9
S4EC3-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 2 Core #1	2	04-Aug-18	06-Aug-18	13
S4BC6-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 2 Core #4	2	07-Aug-18	08-Aug-18	12
S4BC7-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 2 Core #5	2	22-Sep-18	24-Sep-18	8
S4EC2-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 2 Core #8	2	22-Sep-18	24-Sep-18	10
S4CC8-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 2 Core #6	2	13-Oct-18	15-Oct-18	6
S4DC1-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 2 Core #7	2	13-Oct-18	15-Oct-18	22
S4FC4-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 2 Core #2	2	09-Jul-18	10-Jul-18	28
S4AC5-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 2 Core #3	2	11-Jul-18	12-Jul-18	9
S4EC3-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 2 Core #1	2	04-Aug-18	06-Aug-18	13
S4BC6-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 2 Core #4	2	07-Aug-18	08-Aug-18	12
S4BC7-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 2 Core #5	2	22-Sep-18	24-Sep-18	8
S4EC2-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 2 Core #8	2	22-Sep-18	24-Sep-18	10
S4CC8-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 2 Core #6	2	13-Oct-18	15-Oct-18	6
S4DC1-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 2 Core #7	2	13-Oct-18	15-Oct-18	22
S4FC4-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 2 Core #2	1	11-Jul-18	11-Jul-18	28
S4AC5-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 2 Core #3	1	13-Jul-18	13-Jul-18	9
S4EC3-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 2 Core #1	1	07-Aug-18	07-Aug-18	13
S4BC6-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 2 Core #4	1	09-Aug-18	09-Aug-18	12
S4BC7-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 2 Core #5	1	25-Sep-18	25-Sep-18	8
S4EC2-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 2 Core #8	1	25-Sep-18	25-Sep-18	10
S4CC8-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 2 Core #6	1	16-Oct-18	16-Oct-18	6
S4DC1-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 2 Core #7	1	16-Oct-18	16-Oct-18	22
Form 2nd Side					
S4FC4-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 2 Core #2	2	11-Jul-18	12-Jul-18	28
S4AC5-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 2 Core #3	2	13-Jul-18	14-Jul-18	9
S4EC3-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 2 Core #1	2	07-Aug-18	08-Aug-18	13
S4BC6-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 2 Core #4	2	09-Aug-18	10-Aug-18	12
S4BC7-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 2 Core #5	2	25-Sep-18	26-Sep-18	8
S4EC2-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 2 Core #8	2	25-Sep-18	26-Sep-18	10
S4CC8-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 2 Core #6	2	16-Oct-18	17-Oct-18	6
S4DC1-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 2 Core #7	2	16-Oct-18	17-Oct-18	22
Pour					
S4FC4-8P2BH	Core Walls - Pour - Main Conc to Top Lift 2 Core #2	1	12-Jul-18	12-Jul-18	28
S4AC5-8P2BH	Core Walls - Pour - Main Conc to Top Lift 2 Core #3	1	14-Jul-18	14-Jul-18	9
S4EC3-8P2BH	Core Walls - Pour - Main Conc to Top Lift 2 Core #1	1	08-Aug-18	08-Aug-18	13
S4BC6-8P2BH	Core Walls - Pour - Main Conc to Top Lift 2 Core #4	1	10-Aug-18	10-Aug-18	12
S4BC7-8P2BH	Core Walls - Pour - Main Conc to Top Lift 2 Core #5	1	26-Sep-18	26-Sep-18	8
S4EC2-8P2BH	Core Walls - Pour - Main Conc to Top Lift 2 Core #8	1	26-Sep-18	26-Sep-18	10
S4CC8-8P2BH	Core Walls - Pour - Main Conc to Top Lift 2 Core #6	1	17-Oct-18	17-Oct-18	6
S4DC1-8P2BH	Core Walls - Pour - Main Conc to Top Lift 2 Core #7	1	17-Oct-18	17-Oct-18	22
Strip					
S4FC4-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 2 Core #2	1	13-Jul-18	13-Jul-18	28

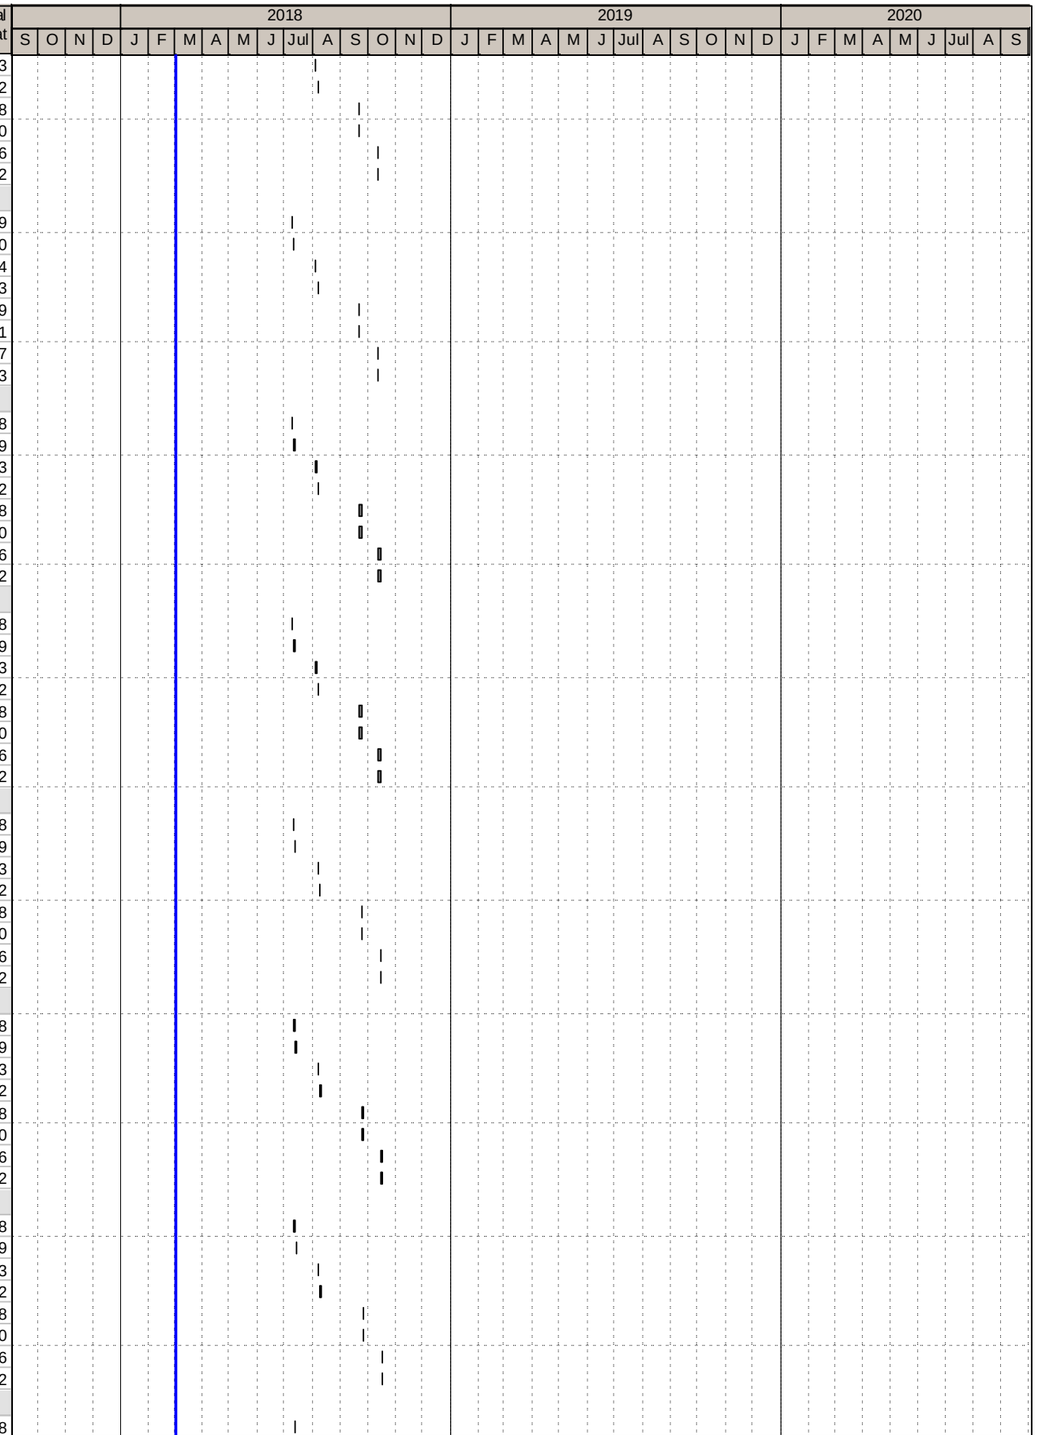

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S4AC5-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 2 Core #3	1	16-Jul-18	16-Jul-18	9
S4EC3-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 2 Core #1	1	09-Aug-18	09-Aug-18	13
S4BC6-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 2 Core #4	1	11-Aug-18	11-Aug-18	12
S4BC7-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 2 Core #5	1	27-Sep-18	27-Sep-18	8
S4EC2-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 2 Core #8	1	27-Sep-18	27-Sep-18	10
S4CC8-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 2 Core #6	1	18-Oct-18	18-Oct-18	6
S4DC1-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 2 Core #7	1	18-Oct-18	18-Oct-18	22
Lift 3					
S5FC4-8P2B0	Core Walls - Jump Inside Panels - Main Conc to Top Lift 3 Core #2	1	13-Jul-18	13-Jul-18	28
S5AC5-8P2B0	Core Walls - Jump Inside Panels - Main Conc to Top Lift 3 Core #3	1	16-Jul-18	16-Jul-18	9
S5EC3-8P2B0	Core Walls - Jump Inside Panels - Main Conc to Top Lift 3 Core #1	1	09-Aug-18	09-Aug-18	13
S5BC6-8P2B0	Core Walls - Jump Inside Panels - Main Conc to Top Lift 3 Core #4	1	11-Aug-18	11-Aug-18	12
S5BC7-8P2B0	Core Walls - Jump Inside Panels - Main Conc to Top Lift 3 Core #5	1	27-Sep-18	27-Sep-18	8
S5EC2-8P2B0	Core Walls - Jump Inside Panels - Main Conc to Top Lift 3 Core #8	1	27-Sep-18	27-Sep-18	10
S5CC8-8P2B0	Core Walls - Jump Inside Panels - Main Conc to Top Lift 3 Core #6	1	18-Oct-18	18-Oct-18	6
S5DC1-8P2B0	Core Walls - Jump Inside Panels - Main Conc to Top Lift 3 Core #7	1	18-Oct-18	18-Oct-18	22
S5FC4-8P2B1	Core Walls - Roll up Inside / Square Up - Main Conc to Top Lift 3 Core #2	1	14-Jul-18	14-Jul-18	28
S5AC5-8P2B1	Core Walls - Roll up Inside / Square Up - Main Conc to Top Lift 3 Core #3	1	17-Jul-18	17-Jul-18	9
S5EC3-8P2B1	Core Walls - Roll up Inside / Square Up - Main Conc to Top Lift 3 Core #1	1	10-Aug-18	10-Aug-18	13
S5BC6-8P2B1	Core Walls - Roll up Inside / Square Up - Main Conc to Top Lift 3 Core #4	1	13-Aug-18	13-Aug-18	12
S5BC7-8P2B1	Core Walls - Roll up Inside / Square Up - Main Conc to Top Lift 3 Core #5	1	28-Sep-18	28-Sep-18	8
S5EC2-8P2B1	Core Walls - Roll up Inside / Square Up - Main Conc to Top Lift 3 Core #8	1	28-Sep-18	28-Sep-18	10
S5CC8-8P2B1	Core Walls - Roll up Inside / Square Up - Main Conc to Top Lift 3 Core #6	1	19-Oct-18	19-Oct-18	6
S5DC1-8P2B1	Core Walls - Roll up Inside / Square Up - Main Conc to Top Lift 3 Core #7	1	19-Oct-18	19-Oct-18	22
S5FC4-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 3 Core #2	1	14-Jul-18	14-Jul-18	29
S5AC5-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 3 Core #3	1	17-Jul-18	17-Jul-18	10
S5EC3-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 3 Core #1	1	10-Aug-18	10-Aug-18	14
S5BC6-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 3 Core #4	1	13-Aug-18	13-Aug-18	13
S5BC7-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 3 Core #5	1	28-Sep-18	28-Sep-18	9
S5EC2-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 3 Core #8	1	28-Sep-18	28-Sep-18	11
S5CC8-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 3 Core #6	1	19-Oct-18	19-Oct-18	7
S5DC1-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 3 Core #7	1	19-Oct-18	19-Oct-18	23
Reinforce					
S5FC4-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 3 Core #2	2	14-Jul-18	16-Jul-18	28
S5AC5-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 3 Core #3	2	17-Jul-18	18-Jul-18	9
S5EC3-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 3 Core #1	2	10-Aug-18	11-Aug-18	13
S5BC6-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 3 Core #4	2	13-Aug-18	14-Aug-18	12
S5BC7-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 3 Core #5	2	28-Sep-18	29-Sep-18	8
S5EC2-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 3 Core #8	2	28-Sep-18	29-Sep-18	10
S5CC8-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 3 Core #6	2	19-Oct-18	20-Oct-18	6
S5DC1-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 3 Core #7	2	19-Oct-18	20-Oct-18	22
S5FC4-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 3 Core #2	2	14-Jul-18	16-Jul-18	28
S5AC5-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 3 Core #3	2	17-Jul-18	18-Jul-18	9
S5EC3-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 3 Core #1	2	10-Aug-18	11-Aug-18	13
S5BC6-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 3 Core #4	2	13-Aug-18	14-Aug-18	12
S5BC7-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 3 Core #5	2	28-Sep-18	29-Sep-18	8
S5EC2-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 3 Core #8	2	28-Sep-18	29-Sep-18	10
S5CC8-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 3 Core #6	2	19-Oct-18	20-Oct-18	6
S5DC1-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 3 Core #7	2	19-Oct-18	20-Oct-18	22
S5FC4-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 3 Core #2	1	17-Jul-18	17-Jul-18	28
S5AC5-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 3 Core #3	1	19-Jul-18	19-Jul-18	9
S5EC3-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 3 Core #1	1	13-Aug-18	13-Aug-18	13
S5BC6-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 3 Core #4	1	15-Aug-18	15-Aug-18	12
S5BC7-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 3 Core #5	1	01-Oct-18	01-Oct-18	8
S5EC2-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 3 Core #8	1	01-Oct-18	01-Oct-18	10
S5CC8-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 3 Core #6	1	22-Oct-18	22-Oct-18	6
S5DC1-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 3 Core #7	1	22-Oct-18	22-Oct-18	22

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
Form 2nd Side					
S5FC4-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 3 Core #2	2	17-Jul-18	18-Jul-18	28
S5AC5-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 3 Core #3	2	19-Jul-18	20-Jul-18	9
S5EC3-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 3 Core #1	2	13-Aug-18	14-Aug-18	13
S5BC6-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 3 Core #4	2	15-Aug-18	16-Aug-18	12
S5BC7-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 3 Core #5	2	01-Oct-18	02-Oct-18	8
S5EC2-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 3 Core #8	2	01-Oct-18	02-Oct-18	10
S5CC8-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 3 Core #6	2	22-Oct-18	23-Oct-18	6
S5DC1-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 3 Core #7	2	22-Oct-18	23-Oct-18	22
Pour					
S5FC4-8P2BH	Core Walls - Pour - Main Conc to Top Lift 3 Core #2	1	18-Jul-18	18-Jul-18	28
S5AC5-8P2BH	Core Walls - Pour - Main Conc to Top Lift 3 Core #3	1	20-Jul-18	20-Jul-18	9
S5EC3-8P2BH	Core Walls - Pour - Main Conc to Top Lift 3 Core #1	1	14-Aug-18	14-Aug-18	13
S5BC6-8P2BH	Core Walls - Pour - Main Conc to Top Lift 3 Core #4	1	16-Aug-18	16-Aug-18	12
S5BC7-8P2BH	Core Walls - Pour - Main Conc to Top Lift 3 Core #5	1	02-Oct-18	02-Oct-18	8
S5EC2-8P2BH	Core Walls - Pour - Main Conc to Top Lift 3 Core #8	1	02-Oct-18	02-Oct-18	10
S5CC8-8P2BH	Core Walls - Pour - Main Conc to Top Lift 3 Core #6	1	23-Oct-18	23-Oct-18	6
S5DC1-8P2BH	Core Walls - Pour - Main Conc to Top Lift 3 Core #7	1	23-Oct-18	23-Oct-18	22
Strip					
S5FC4-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 3 Core #2	1	19-Jul-18	19-Jul-18	28
S5AC5-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 3 Core #3	1	21-Jul-18	21-Jul-18	9
S5EC3-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 3 Core #1	1	15-Aug-18	15-Aug-18	13
S5BC6-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 3 Core #4	1	17-Aug-18	17-Aug-18	12
S5BC7-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 3 Core #5	1	03-Oct-18	03-Oct-18	8
S5EC2-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 3 Core #8	1	03-Oct-18	03-Oct-18	10
S5CC8-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 3 Core #6	1	24-Oct-18	24-Oct-18	6
S5DC1-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 3 Core #7	1	24-Oct-18	24-Oct-18	22
Lift 4					
S6FC4-8P2B0	Core Walls - Jump Inside Panels - Main Conc to Top Lift 4 Core #2	1	19-Jul-18	19-Jul-18	28
S6AC5-8P2B0	Core Walls - Jump Inside Panels - Main Conc to Top Lift 4 Core #3	1	21-Jul-18	21-Jul-18	9
S6EC3-8P2B0	Core Walls - Jump Inside Panels - Main Conc to Top Lift 4 Core #1	1	15-Aug-18	15-Aug-18	13
S6BC6-8P2B0	Core Walls - Jump Inside Panels - Main Conc to Top Lift 4 Core #4	1	17-Aug-18	17-Aug-18	12
S6BC7-8P2B0	Core Walls - Jump Inside Panels - Main Conc to Top Lift 4 Core #5	1	03-Oct-18	03-Oct-18	8
S6EC2-8P2B0	Core Walls - Jump Inside Panels - Main Conc to Top Lift 4 Core #8	1	03-Oct-18	03-Oct-18	10
S6CC8-8P2B0	Core Walls - Jump Inside Panels - Main Conc to Top Lift 4 Core #6	1	24-Oct-18	24-Oct-18	6
S6DC1-8P2B0	Core Walls - Jump Inside Panels - Main Conc to Top Lift 4 Core #7	1	24-Oct-18	24-Oct-18	22
S6FC4-8P2B1	Core Walls - Roll up Inside / Square Up - Main Conc to Top Lift 4 Core #2	1	20-Jul-18	20-Jul-18	28
S6AC5-8P2B1	Core Walls - Roll up Inside / Square Up - Main Conc to Top Lift 4 Core #3	1	23-Jul-18	23-Jul-18	9
S6EC3-8P2B1	Core Walls - Roll up Inside / Square Up - Main Conc to Top Lift 4 Core #1	1	16-Aug-18	16-Aug-18	13
S6BC6-8P2B1	Core Walls - Roll up Inside / Square Up - Main Conc to Top Lift 4 Core #4	1	18-Aug-18	18-Aug-18	12
S6BC7-8P2B1	Core Walls - Roll up Inside / Square Up - Main Conc to Top Lift 4 Core #5	1	04-Oct-18	04-Oct-18	8
S6EC2-8P2B1	Core Walls - Roll up Inside / Square Up - Main Conc to Top Lift 4 Core #8	1	04-Oct-18	04-Oct-18	10
S6CC8-8P2B1	Core Walls - Roll up Inside / Square Up - Main Conc to Top Lift 4 Core #6	1	25-Oct-18	25-Oct-18	6
S6DC1-8P2B1	Core Walls - Roll up Inside / Square Up - Main Conc to Top Lift 4 Core #7	1	25-Oct-18	25-Oct-18	22
S6FC4-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 4 Core #2	1	20-Jul-18	20-Jul-18	29
S6AC5-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 4 Core #3	1	23-Jul-18	23-Jul-18	10
S6EC3-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 4 Core #1	1	16-Aug-18	16-Aug-18	14
S6BC6-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 4 Core #4	1	18-Aug-18	18-Aug-18	13
S6BC7-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 4 Core #5	1	04-Oct-18	04-Oct-18	9
S6EC2-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 4 Core #8	1	04-Oct-18	04-Oct-18	11
S6CC8-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 4 Core #6	1	25-Oct-18	25-Oct-18	7
S6DC1-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 4 Core #7	1	25-Oct-18	25-Oct-18	23
Reinforce					
S6FC4-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 4 Core #2	2	20-Jul-18	21-Jul-18	28
S6AC5-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 4 Core #3	2	23-Jul-18	24-Jul-18	9
S6EC3-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 4 Core #1	2	16-Aug-18	17-Aug-18	13
S6BC6-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 4 Core #4	2	18-Aug-18	20-Aug-18	12
S6BC7-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 4 Core #5	2	04-Oct-18	05-Oct-18	8
S6EC2-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 4 Core #8	2	04-Oct-18	05-Oct-18	10

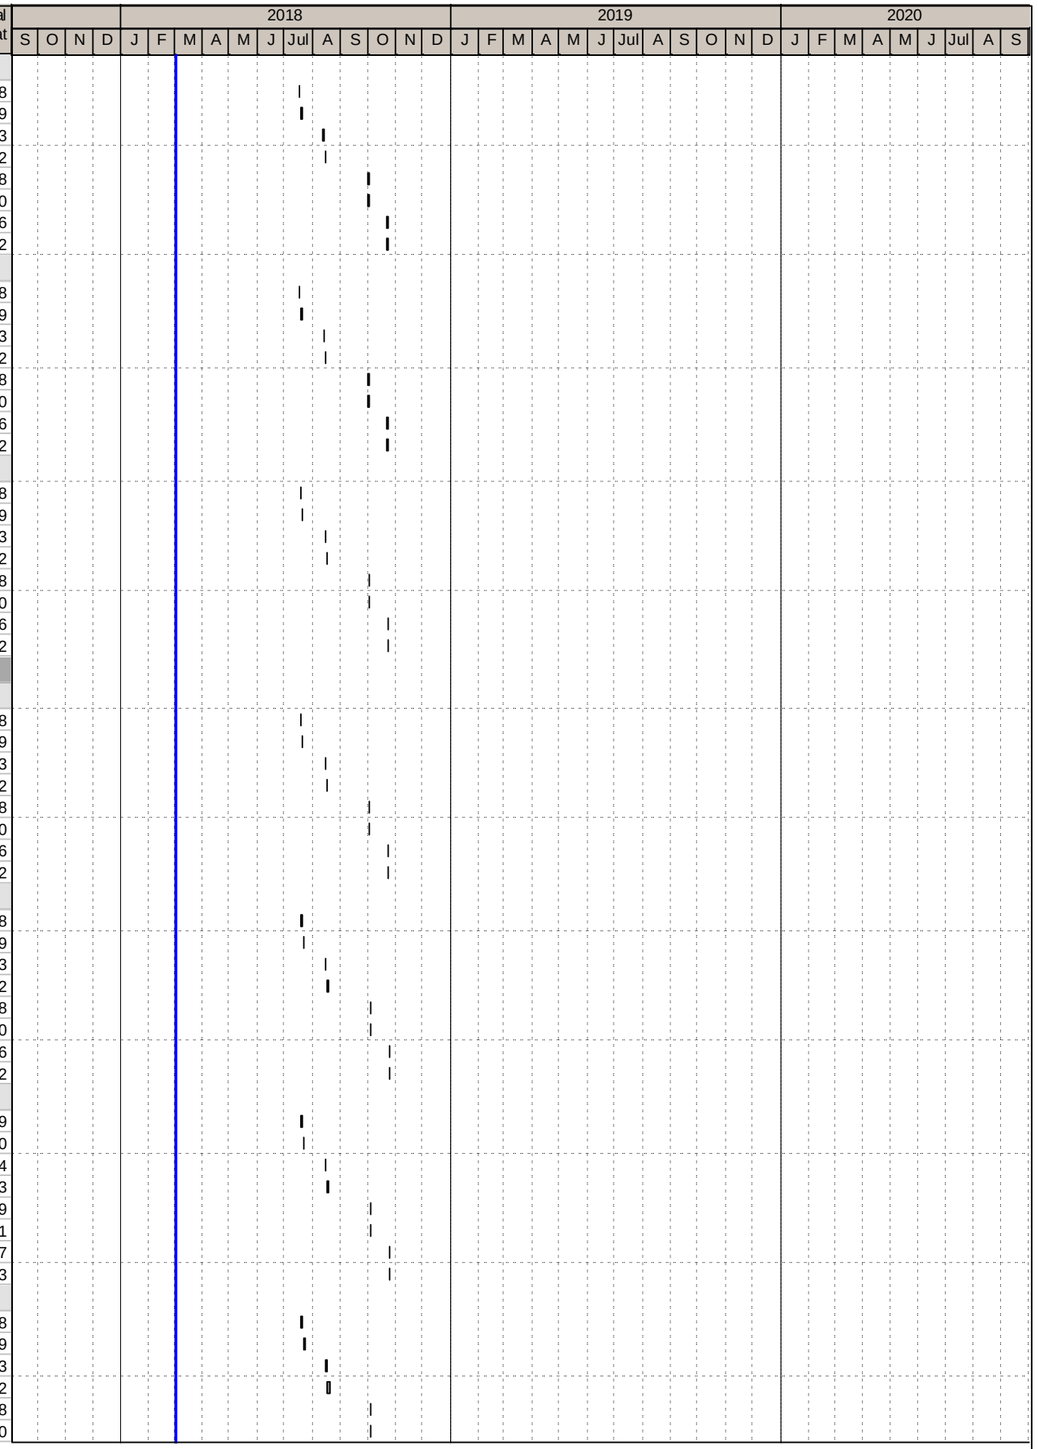

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S6CC8-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 4 Core #6	2	25-Oct-18	26-Oct-18	6
S6DC1-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 4 Core #7	2	25-Oct-18	26-Oct-18	22
S6FC4-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 4 Core #2	2	20-Jul-18	21-Jul-18	28
S6AC5-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 4 Core #3	2	23-Jul-18	24-Jul-18	9
S6EC3-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 4 Core #1	2	16-Aug-18	17-Aug-18	13
S6BC6-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 4 Core #4	2	18-Aug-18	20-Aug-18	12
S6BC7-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 4 Core #5	2	04-Oct-18	05-Oct-18	8
S6EC2-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 4 Core #8	2	04-Oct-18	05-Oct-18	10
S6CC8-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 4 Core #6	2	25-Oct-18	26-Oct-18	6
S6DC1-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 4 Core #7	2	25-Oct-18	26-Oct-18	22
S6FC4-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 4 Core #2	1	23-Jul-18	23-Jul-18	28
S6AC5-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 4 Core #3	1	25-Jul-18	25-Jul-18	9
S6EC3-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 4 Core #1	1	18-Aug-18	18-Aug-18	13
S6BC6-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 4 Core #4	1	21-Aug-18	21-Aug-18	12
S6BC7-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 4 Core #5	1	06-Oct-18	06-Oct-18	8
S6EC2-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 4 Core #8	1	06-Oct-18	06-Oct-18	10
S6CC8-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 4 Core #6	1	27-Oct-18	27-Oct-18	6
S6DC1-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 4 Core #7	1	27-Oct-18	27-Oct-18	22
Form 2nd Side					
S6FC4-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 4 Core #2	2	23-Jul-18	24-Jul-18	28
S6AC5-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 4 Core #3	2	25-Jul-18	26-Jul-18	9
S6EC3-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 4 Core #1	2	18-Aug-18	20-Aug-18	13
S6BC6-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 4 Core #4	2	21-Aug-18	22-Aug-18	12
S6BC7-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 4 Core #5	2	06-Oct-18	08-Oct-18	8
S6EC2-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 4 Core #8	2	06-Oct-18	08-Oct-18	10
S6CC8-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 4 Core #6	2	27-Oct-18	29-Oct-18	6
S6DC1-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 4 Core #7	2	27-Oct-18	29-Oct-18	22
Pour					
S6FC4-8P2BH	Core Walls - Pour - Main Conc to Top Lift 4 Core #2	1	24-Jul-18	24-Jul-18	28
S6AC5-8P2BH	Core Walls - Pour - Main Conc to Top Lift 4 Core #3	1	26-Jul-18	26-Jul-18	9
S6EC3-8P2BH	Core Walls - Pour - Main Conc to Top Lift 4 Core #1	1	20-Aug-18	20-Aug-18	13
S6BC6-8P2BH	Core Walls - Pour - Main Conc to Top Lift 4 Core #4	1	22-Aug-18	22-Aug-18	12
S6BC7-8P2BH	Core Walls - Pour - Main Conc to Top Lift 4 Core #5	1	08-Oct-18	08-Oct-18	8
S6EC2-8P2BH	Core Walls - Pour - Main Conc to Top Lift 4 Core #8	1	08-Oct-18	08-Oct-18	10
S6CC8-8P2BH	Core Walls - Pour - Main Conc to Top Lift 4 Core #6	1	29-Oct-18	29-Oct-18	6
S6DC1-8P2BH	Core Walls - Pour - Main Conc to Top Lift 4 Core #7	1	29-Oct-18	29-Oct-18	22
Strip					
S6FC4-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 4 Core #2	1	25-Jul-18	25-Jul-18	28
S6AC5-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 4 Core #3	1	27-Jul-18	27-Jul-18	9
S6EC3-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 4 Core #1	1	21-Aug-18	21-Aug-18	13
S6BC6-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 4 Core #4	1	23-Aug-18	23-Aug-18	12
S6BC7-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 4 Core #5	1	09-Oct-18	09-Oct-18	8
S6EC2-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 4 Core #8	1	09-Oct-18	09-Oct-18	10
S6CC8-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 4 Core #6	1	30-Oct-18	30-Oct-18	6
S6DC1-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 4 Core #7	1	30-Oct-18	30-Oct-18	22
Lift 5					
S7FC4-8P2B0	Core Walls - Jump Inside Panels - Main Conc to Top Lift 5 Core #2	1	25-Jul-18	25-Jul-18	28
S7AC5-8P2B0	Core Walls - Jump Inside Panels - Main Conc to Top Lift 5 Core #3	1	27-Jul-18	27-Jul-18	9
S7EC3-8P2B0	Core Walls - Jump Inside Panels - Main Conc to Top Lift 5 Core #1	1	21-Aug-18	21-Aug-18	13
S7BC6-8P2B0	Core Walls - Jump Inside Panels - Main Conc to Top Lift 5 Core #4	1	23-Aug-18	23-Aug-18	12
S7BC7-8P2B0	Core Walls - Jump Inside Panels - Main Conc to Top Lift 5 Core #5	1	09-Oct-18	09-Oct-18	8
S7EC2-8P2B0	Core Walls - Jump Inside Panels - Main Conc to Top Lift 5 Core #8	1	09-Oct-18	09-Oct-18	10
S7CC8-8P2B0	Core Walls - Jump Inside Panels - Main Conc to Top Lift 5 Core #6	1	30-Oct-18	30-Oct-18	6
S7DC1-8P2B0	Core Walls - Jump Inside Panels - Main Conc to Top Lift 5 Core #7	1	30-Oct-18	30-Oct-18	22
S7FC4-8P2B1	Core Walls - Roll up Inside / Square Up - Main Conc to Top Lift 5 Core #2	1	26-Jul-18	26-Jul-18	28
S7AC5-8P2B1	Core Walls - Roll up Inside / Square Up - Main Conc to Top Lift 5 Core #3	1	28-Jul-18	28-Jul-18	9
S7EC3-8P2B1	Core Walls - Roll up Inside / Square Up - Main Conc to Top Lift 5 Core #1	1	22-Aug-18	22-Aug-18	13
S7BC6-8P2B1	Core Walls - Roll up Inside / Square Up - Main Conc to Top Lift 5 Core #4	1	24-Aug-18	24-Aug-18	12

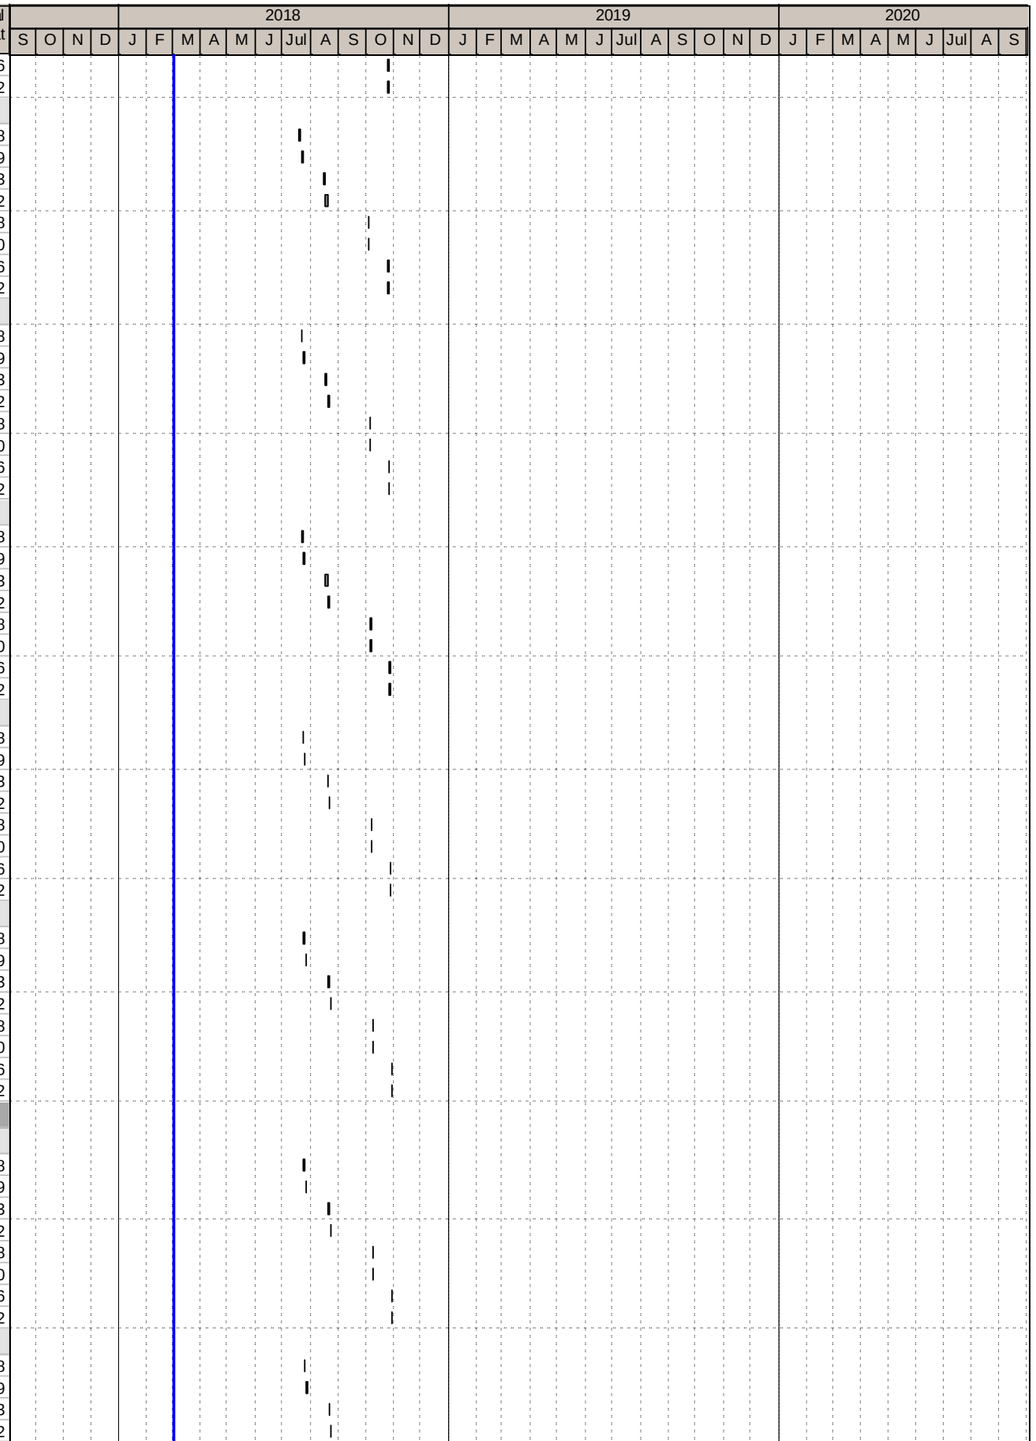

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S7BC7-8P2B1	Core Walls - Roll up Inside / Square Up - Main Conc to Top Lift 5 Core #5	1	10-Oct-18	10-Oct-18	8
S7EC2-8P2B1	Core Walls - Roll up Inside / Square Up - Main Conc to Top Lift 5 Core #8	1	10-Oct-18	10-Oct-18	10
S7CC8-8P2B1	Core Walls - Roll up Inside / Square Up - Main Conc to Top Lift 5 Core #6	1	31-Oct-18	31-Oct-18	6
S7DC1-8P2B1	Core Walls - Roll up Inside / Square Up - Main Conc to Top Lift 5 Core #7	1	31-Oct-18	31-Oct-18	22
S7FC4-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 5 Core #2	1	26-Jul-18	26-Jul-18	29
S7AC5-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 5 Core #3	1	28-Jul-18	28-Jul-18	10
S7EC3-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 5 Core #1	1	22-Aug-18	22-Aug-18	14
S7BC6-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 5 Core #4	1	24-Aug-18	24-Aug-18	13
S7BC7-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 5 Core #5	1	10-Oct-18	10-Oct-18	9
S7EC2-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 5 Core #8	1	10-Oct-18	10-Oct-18	11
S7CC8-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 5 Core #6	1	31-Oct-18	31-Oct-18	7
S7DC1-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 5 Core #7	1	31-Oct-18	31-Oct-18	23
Reinforce					
S7FC4-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 5 Core #2	2	26-Jul-18	27-Jul-18	28
S7AC5-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 5 Core #3	2	28-Jul-18	30-Jul-18	9
S7EC3-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 5 Core #1	2	22-Aug-18	23-Aug-18	13
S7BC6-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 5 Core #4	2	24-Aug-18	25-Aug-18	12
S7BC7-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 5 Core #5	2	10-Oct-18	11-Oct-18	8
S7EC2-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 5 Core #8	2	10-Oct-18	11-Oct-18	10
S7CC8-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 5 Core #6	2	31-Oct-18	01-Nov-18	6
S7DC1-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 5 Core #7	2	31-Oct-18	01-Nov-18	22
S7FC4-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 5 Core #2	2	26-Jul-18	27-Jul-18	28
S7AC5-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 5 Core #3	2	28-Jul-18	30-Jul-18	9
S7EC3-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 5 Core #1	2	22-Aug-18	23-Aug-18	13
S7BC6-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 5 Core #4	2	24-Aug-18	25-Aug-18	12
S7BC7-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 5 Core #5	2	10-Oct-18	11-Oct-18	8
S7EC2-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 5 Core #8	2	10-Oct-18	11-Oct-18	10
S7CC8-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 5 Core #6	2	31-Oct-18	01-Nov-18	6
S7DC1-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 5 Core #7	2	31-Oct-18	01-Nov-18	22
S7FC4-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 5 Core #2	1	28-Jul-18	28-Jul-18	28
S7AC5-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 5 Core #3	1	31-Jul-18	31-Jul-18	9
S7EC3-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 5 Core #1	1	24-Aug-18	24-Aug-18	13
S7BC6-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 5 Core #4	1	27-Aug-18	27-Aug-18	12
S7BC7-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 5 Core #5	1	12-Oct-18	12-Oct-18	8
S7EC2-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 5 Core #8	1	12-Oct-18	12-Oct-18	10
S7CC8-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 5 Core #6	1	02-Nov-18	02-Nov-18	6
S7DC1-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 5 Core #7	1	02-Nov-18	02-Nov-18	22
Form 2nd Side					
S7FC4-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 5 Core #2	2	28-Jul-18	30-Jul-18	28
S7AC5-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 5 Core #3	2	31-Jul-18	01-Aug-18	9
S7EC3-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 5 Core #1	2	24-Aug-18	25-Aug-18	13
S7BC6-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 5 Core #4	2	27-Aug-18	28-Aug-18	12
S7BC7-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 5 Core #5	2	12-Oct-18	13-Oct-18	8
S7EC2-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 5 Core #8	2	12-Oct-18	13-Oct-18	10
S7CC8-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 5 Core #6	2	02-Nov-18	03-Nov-18	6
S7DC1-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 5 Core #7	2	02-Nov-18	03-Nov-18	22
Pour					
S7FC4-8P2BH	Core Walls - Pour - Main Conc to Top Lift 5 Core #2	1	30-Jul-18	30-Jul-18	28
S7AC5-8P2BH	Core Walls - Pour - Main Conc to Top Lift 5 Core #3	1	01-Aug-18	01-Aug-18	9
S7EC3-8P2BH	Core Walls - Pour - Main Conc to Top Lift 5 Core #1	1	25-Aug-18	25-Aug-18	13
S7BC6-8P2BH	Core Walls - Pour - Main Conc to Top Lift 5 Core #4	1	28-Aug-18	28-Aug-18	12
S7BC7-8P2BH	Core Walls - Pour - Main Conc to Top Lift 5 Core #5	1	13-Oct-18	13-Oct-18	8
S7EC2-8P2BH	Core Walls - Pour - Main Conc to Top Lift 5 Core #8	1	13-Oct-18	13-Oct-18	10
S7CC8-8P2BH	Core Walls - Pour - Main Conc to Top Lift 5 Core #6	1	03-Nov-18	03-Nov-18	6
S7DC1-8P2BH	Core Walls - Pour - Main Conc to Top Lift 5 Core #7	1	03-Nov-18	03-Nov-18	22
Strip					
S7FC4-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 5 Core #2	1	31-Jul-18	31-Jul-18	28
S7AC5-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 5 Core #3	1	02-Aug-18	02-Aug-18	9
S7EC3-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 5 Core #1	1	27-Aug-18	27-Aug-18	13

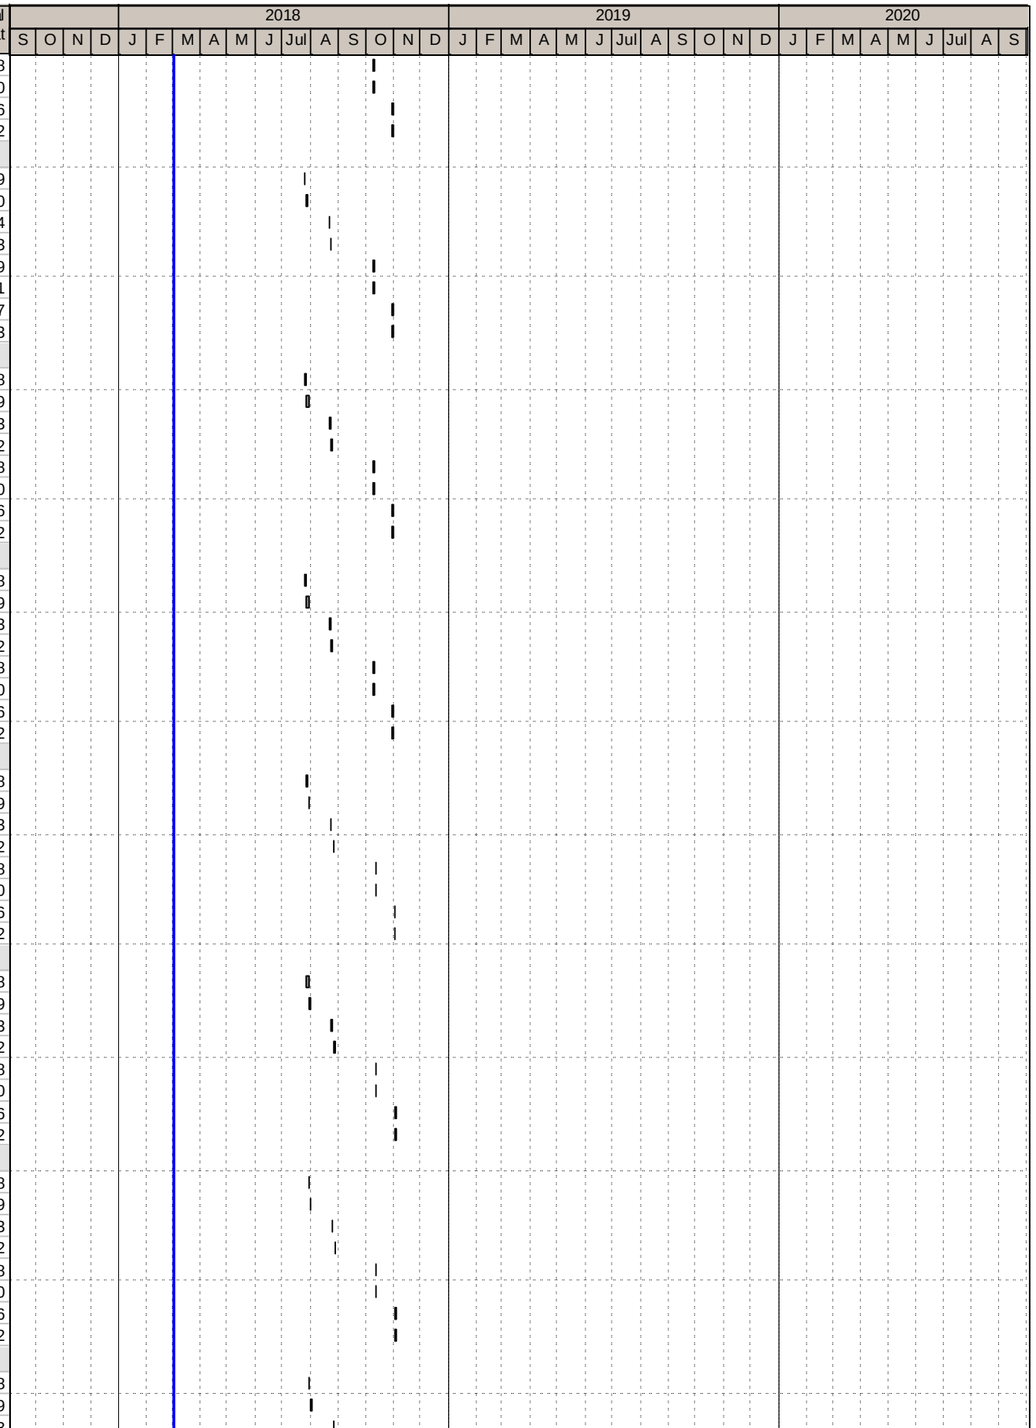

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S7BC6-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 5 Core #4	1	29-Aug-18	29-Aug-18	12
S7BC7-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 5 Core #5	1	15-Oct-18	15-Oct-18	8
S7EC2-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 5 Core #8	1	15-Oct-18	15-Oct-18	10
S7CC8-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 5 Core #6	1	05-Nov-18	05-Nov-18	6
S7DC1-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 5 Core #7	1	05-Nov-18	05-Nov-18	22
Lift 6					
S8FC4-8P2B0	Core Walls - Jump Inside Panels - Main Conc to Top Lift 6 Core #2	1	31-Jul-18	31-Jul-18	28
S8AC5-8P2B0	Core Walls - Jump Inside Panels - Main Conc to Top Lift 6 Core #3	1	02-Aug-18	02-Aug-18	9
S8EC3-8P2B0	Core Walls - Jump Inside Panels - Main Conc to Top Lift 6 Core #1	1	27-Aug-18	27-Aug-18	13
S8EC2-8P2B0	Core Walls - Jump Inside Panels - Main Conc to Top Lift 6 Core #8	1	15-Oct-18	15-Oct-18	10
S8FC4-8P2B1	Core Walls - Roll up Inside / Square Up - Main Conc to Top Lift 6 Core #2	1	01-Aug-18	01-Aug-18	28
S8AC5-8P2B1	Core Walls - Roll up Inside / Square Up - Main Conc to Top Lift 6 Core #3	1	03-Aug-18	03-Aug-18	9
S8EC3-8P2B1	Core Walls - Roll up Inside / Square Up - Main Conc to Top Lift 6 Core #1	1	28-Aug-18	28-Aug-18	13
S8EC2-8P2B1	Core Walls - Roll up Inside / Square Up - Main Conc to Top Lift 6 Core #8	1	16-Oct-18	16-Oct-18	10
S8FC4-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 6 Core #2	1	01-Aug-18	01-Aug-18	29
S8AC5-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 6 Core #3	1	03-Aug-18	03-Aug-18	10
S8EC3-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 6 Core #1	1	28-Aug-18	28-Aug-18	14
S8EC2-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 6 Core #8	1	16-Oct-18	16-Oct-18	11
Reinforce					
S8FC4-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 6 Core #2	2	01-Aug-18	02-Aug-18	28
S8AC5-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 6 Core #3	2	03-Aug-18	04-Aug-18	9
S8EC3-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 6 Core #1	2	28-Aug-18	29-Aug-18	13
S8EC2-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 6 Core #8	2	16-Oct-18	17-Oct-18	10
S8FC4-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 6 Core #2	2	01-Aug-18	02-Aug-18	28
S8AC5-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 6 Core #3	2	03-Aug-18	04-Aug-18	9
S8EC3-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 6 Core #1	2	28-Aug-18	29-Aug-18	13
S8EC2-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 6 Core #8	2	16-Oct-18	17-Oct-18	10
S8FC4-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 6 Core #2	1	03-Aug-18	03-Aug-18	28
S8AC5-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 6 Core #3	1	06-Aug-18	06-Aug-18	9
S8EC3-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 6 Core #1	1	30-Aug-18	30-Aug-18	13
S8EC2-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 6 Core #8	1	18-Oct-18	18-Oct-18	10
Form 2nd Side					
S8FC4-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 6 Core #2	2	03-Aug-18	04-Aug-18	28
S8AC5-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 6 Core #3	2	06-Aug-18	07-Aug-18	9
S8EC3-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 6 Core #1	2	30-Aug-18	31-Aug-18	13
S8EC2-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 6 Core #8	2	18-Oct-18	19-Oct-18	10
Pour					
S8FC4-8P2BH	Core Walls - Pour - Main Conc to Top Lift 6 Core #2	1	04-Aug-18	04-Aug-18	28
S8AC5-8P2BH	Core Walls - Pour - Main Conc to Top Lift 6 Core #3	1	07-Aug-18	07-Aug-18	9
S8EC3-8P2BH	Core Walls - Pour - Main Conc to Top Lift 6 Core #1	1	31-Aug-18	31-Aug-18	13
S8EC2-8P2BH	Core Walls - Pour - Main Conc to Top Lift 6 Core #8	1	19-Oct-18	19-Oct-18	10
Strip					
S8FC4-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 6 Core #2	1	06-Aug-18	06-Aug-18	28
S8AC5-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 6 Core #3	1	08-Aug-18	08-Aug-18	9
S8EC3-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 6 Core #1	1	01-Sep-18	01-Sep-18	13
S8EC2-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 6 Core #8	1	20-Oct-18	20-Oct-18	10
Lift 7					
S9EC3-8P2B0	Core Walls - Jump Inside Panels - Main Conc to Top Lift 7 Core #1	1	01-Sep-18	01-Sep-18	13
S9EC2-8P2B0	Core Walls - Jump Inside Panels - Main Conc to Top Lift 7 Core #8	1	20-Oct-18	20-Oct-18	10
S9EC3-8P2B1	Core Walls - Roll up Inside / Square Up - Main Conc to Top Lift 7 Core #1	1	04-Sep-18	04-Sep-18	13
S9EC2-8P2B1	Core Walls - Roll up Inside / Square Up - Main Conc to Top Lift 7 Core #8	1	22-Oct-18	22-Oct-18	10
S9EC3-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 7 Core #1	1	04-Sep-18	04-Sep-18	14
S9EC2-8P2B2	Core Walls - Install Embeds - Main Conc to Top Lift 7 Core #8	1	22-Oct-18	22-Oct-18	11

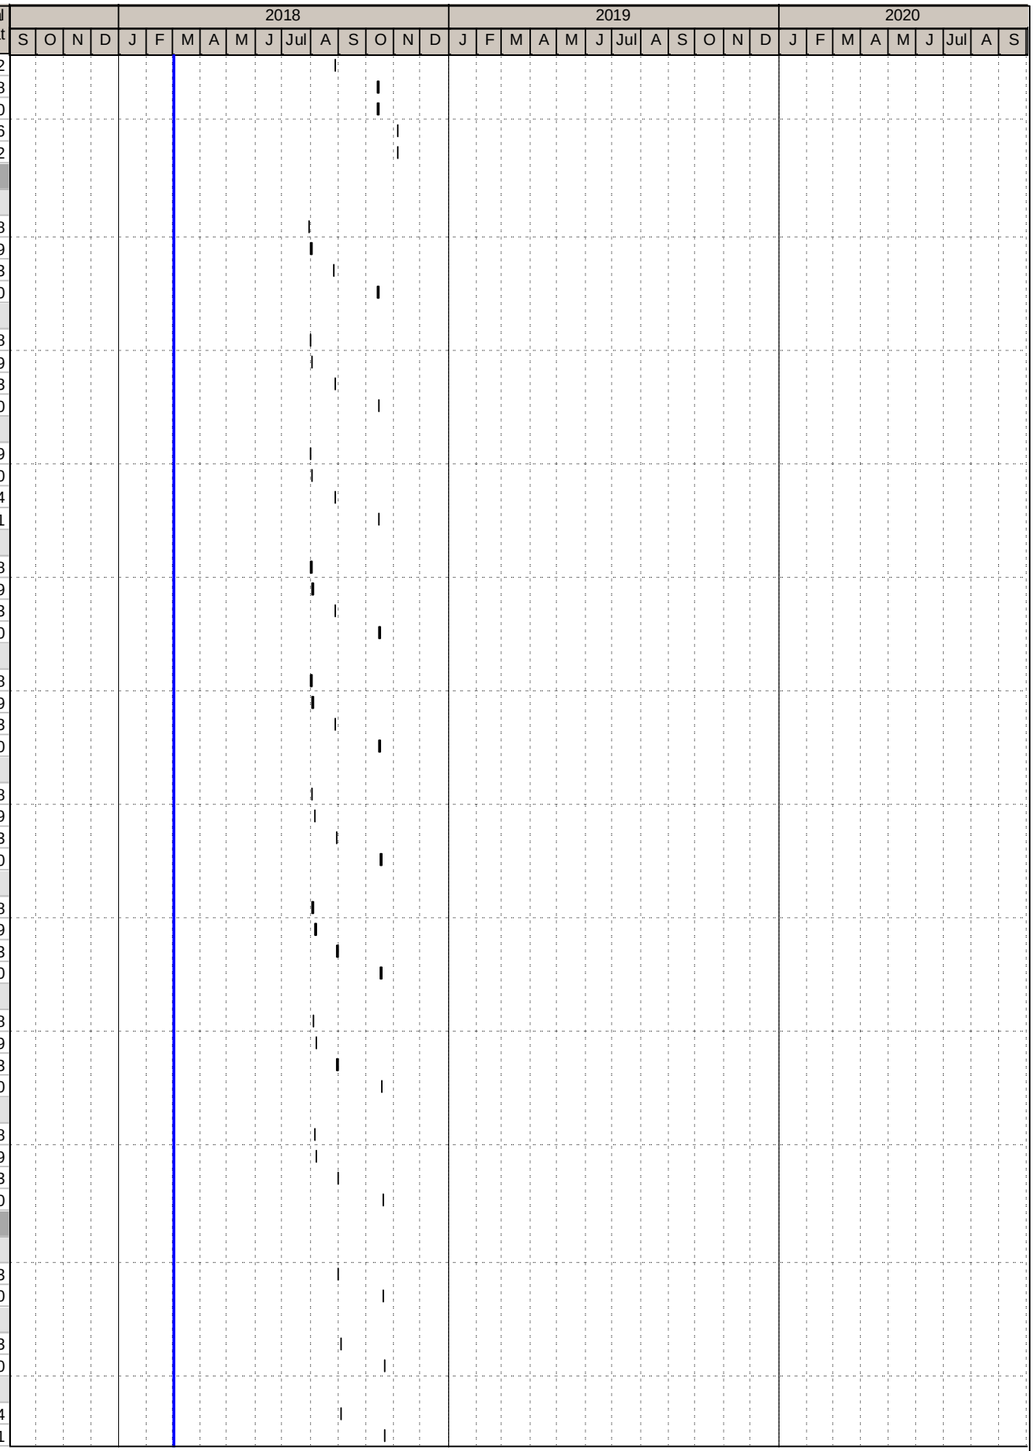

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
Reinforce					
S9EC3-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 7 Core #1	2	04-Sep-18	05-Sep-18	13
S9EC2-8P2BC	Core Walls - Install Rebar - Main Conc to Top Lift 7 Core #8	2	22-Oct-18	23-Oct-18	10
S9EC3-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 7 Core #1	2	04-Sep-18	05-Sep-18	13
S9EC2-8P2B3	Core Walls - Blockouts - Main Conc to Top Lift 7 Core #8	2	22-Oct-18	23-Oct-18	10
S9EC3-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 7 Core #1	1	06-Sep-18	06-Sep-18	13
S9EC2-8P2B4	Core Walls - Inspection - Main Conc to Top Lift 7 Core #8	1	24-Oct-18	24-Oct-18	10
Form 2nd Side					
S9EC3-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 7 Core #1	2	06-Sep-18	07-Sep-18	13
S9EC2-8P2BN	Core Walls - Close Wall - Main Conc to Top Lift 7 Core #8	2	24-Oct-18	25-Oct-18	10
Pour					
S9EC3-8P2BH	Core Walls - Pour - Main Conc to Top Lift 7 Core #1	1	07-Sep-18	07-Sep-18	13
S9EC2-8P2BH	Core Walls - Pour - Main Conc to Top Lift 7 Core #8	1	25-Oct-18	25-Oct-18	10
Strip					
S9EC3-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 7 Core #1	1	08-Sep-18	08-Sep-18	13
S9EC2-8P2BJ	Core Walls - Strip - Main Conc to Top Lift 7 Core #8	1	26-Oct-18	26-Oct-18	10
FRP Columns					
000 Event Level					
S1A0-8P30	Concrete Columns - Event A (Summary)	12	27-Mar-18	11-Apr-18	10
S1F0-8P30	Concrete Columns - Event F (Summary)	12	28-Mar-18	12-Apr-18	10
S1B0-8P30	Concrete Columns - Event B (Summary)	18	17-Apr-18	10-May-18	36
S1E0-8P30	Concrete Columns - Event E (Summary)	18	23-Apr-18	16-May-18	26
S1C0-8P30	Concrete Columns - Event C (Summary)	11	25-May-18	11-Jun-18	62
S1D0-8P30	Concrete Columns - Event D (Summary)	11	01-Jun-18	15-Jun-18	63
Pour					
S1A1-8P2C	FRP Columns - Event A1	6	27-Mar-18	03-Apr-18	4
S1F1-8P2C	FRP Columns - Event F1	6	28-Mar-18	04-Apr-18	4
S1A2-8P2C	FRP Columns - Event A2	6	04-Apr-18	11-Apr-18	10
S1F2-8P2C	FRP Columns - Event F2	6	05-Apr-18	12-Apr-18	10
S1B1-8P2C	FRP Columns - Event B1	5	17-Apr-18	23-Apr-18	11
S1E1-8P2C	FRP Columns - Event E1	4	23-Apr-18	26-Apr-18	12
S1B2-8P2C	FRP Columns - Event B2	7	25-Apr-18	03-May-18	22
S1E2-8P2C	FRP Columns - Event E2	6	30-Apr-18	07-May-18	24
S1B3-8P2C	FRP Columns - Event B3	5	04-May-18	10-May-18	36
S1E3-8P2C	FRP Columns - Event E3	7	08-May-18	16-May-18	26
S1C1-8P2C	FRP Columns - Event C1	5	25-May-18	01-Jun-18	34
S1D1-8P2C	FRP Columns - Event D1	5	01-Jun-18	07-Jun-18	32
S1C2-8P2C	FRP Columns - Event C2	5	05-Jun-18	11-Jun-18	62
S1D2-8P2C	FRP Columns - Event D2	5	11-Jun-18	15-Jun-18	63
050 Lower Mezz Level					
S2A0-8P30	Concrete Columns - Mezz Lvl A (Summary)	13	15-May-18	01-Jun-18	11
S2F0-8P30	Concrete Columns - Mezz Lvl F (Summary)	15	15-May-18	05-Jun-18	13
S2B0-8P30	Concrete Columns - Mezz Lvl B (Summary)	36	07-Jun-18	27-Jul-18	21
S2E0-8P30	Concrete Columns - Mezz Lvl E (Summary)	36	08-Jun-18	30-Jul-18	20
S2C0-8P30	Concrete Columns - Mezz Lvl C (Summary)	11	31-Jul-18	14-Aug-18	24
S2D0-8P30	Concrete Columns - Mezz Lvl D (Summary)	11	01-Aug-18	15-Aug-18	27
Pour					
S2A4-8P2C	FRP Columns & Walls - Lower Mezz North Exterior	5	09-May-18	15-May-18	8
S2A1-8P2C	FRP Columns - Lower Mezz A1	3	15-May-18	17-May-18	0
S2F1-8P2C	FRP Columns - Lower Mezz F1	3	15-May-18	17-May-18	0
S2A2-8P2C	FRP Columns - Lower Mezz A2	4	21-May-18	24-May-18	5
S2F2-8P2C	FRP Columns - Lower Mezz F2	4	23-May-18	29-May-18	5
S2A3-8P2C	FRP Columns - Lower Mezz A3	4	29-May-18	01-Jun-18	11
S2F3-8P2C	FRP Columns - Lower Mezz F3	4	31-May-18	05-Jun-18	13
S2B1-8P2C	FRP Columns - Lower Mezz B1	4	07-Jun-18	12-Jun-18	10
S2E1-8P2C	FRP Columns - Lower Mezz E1	4	08-Jun-18	13-Jun-18	13
S2E2-8P2C	FRP Columns - Lower Mezz E2	2	15-Jun-18	18-Jun-18	15

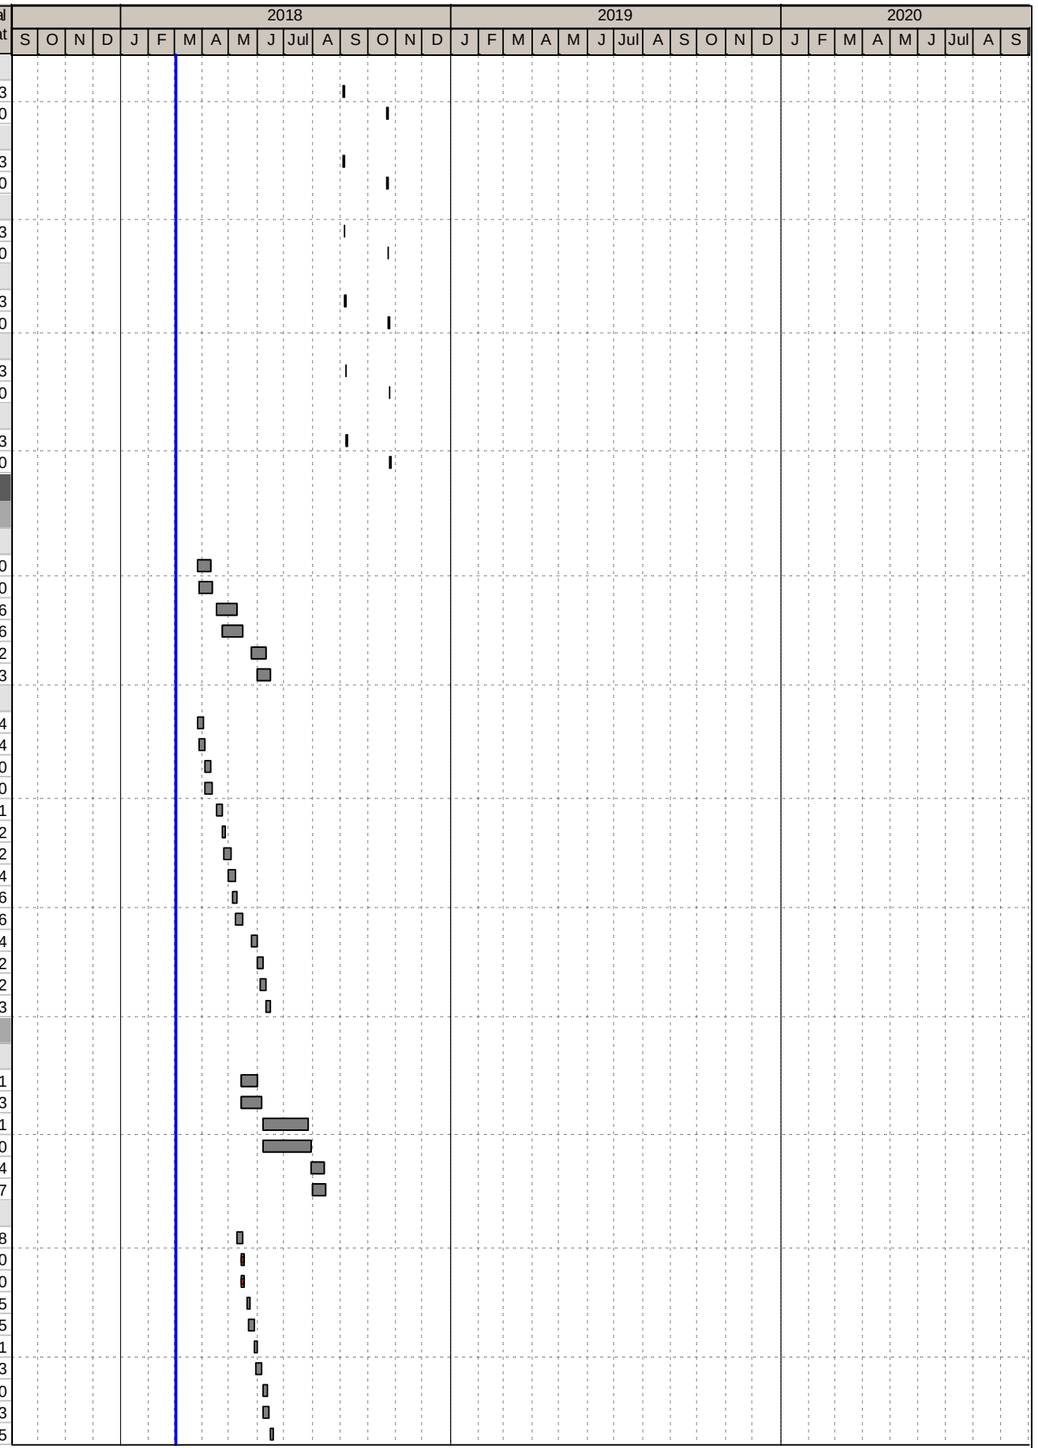

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S2B2-8P2C	FRP Columns - Lower Mezz B2	4	15-Jun-18	20-Jun-18	10
S2B3-8P2C	FRP Columns - Lower Mezz B3	4	25-Jun-18	28-Jun-18	11
S2B4-8P2C	Start	4	02-Jul-18	06-Jul-18	15
S2E3-8P2C	FRP Columns - Lower Mezz E3	6	28-Jun-18	06-Jul-18	10
S2E4-8P2C	FRP Columns - Lower Mezz E4	4	09-Jul-18	12-Jul-18	15
S2B5-8P2C	FRP Columns - Lower Mezz B5	11	13-Jul-18	27-Jul-18	21
S2E5-8P2C	FRP Columns - Lower Mezz E5	11	16-Jul-18	30-Jul-18	20
S2C2-8P2C	FRP Columns - Lower Mezz C2	4	07-Aug-18	10-Aug-18	26
S2D2-8P2C	FRP Columns - Lower Mezz D2	4	08-Aug-18	13-Aug-18	29
S2C1-8P2C	FRP Columns - Lower Mezz C1	11	31-Jul-18	14-Aug-18	17
S2D1-8P2C	FRP Columns - Lower Mezz D1	11	01-Aug-18	15-Aug-18	19
FRP Pan & Joist Deck					
050 Lower Mezz Level					
S2F0-8P10	Concrete Structure - Mezz Lvl F (Summary)	42	17-Apr-18	14-Jun-18	29
S2A0-8P10	Concrete Structure - Mezz Lvl A (Summary)	45	16-Apr-18	18-Jun-18	21
S2E0-8P10	Concrete Structure - Mezz Lvl E (Summary)	46	17-May-18	23-Jul-18	42
S2B0-8P10	Concrete Structure - Mezz Lvl B (Summary)	47	16-May-18	23-Jul-18	43
S2C0-8P10	Concrete Structure - Mezz Lvl C (Summary)	28	09-Jul-18	15-Aug-18	39
S2D0-8P10	Concrete Structure - Mezz Lvl D (Summary)	27	11-Jul-18	16-Aug-18	34
Structure					
S2A1-8P2G6	P&J Deck - Lower Mezz A1 (Summary for 4D)	21	16-Apr-18	14-May-18	0
S2F1-8P2G6	P&J Deck - Lower Mezz F1 (Summary for 4D)	20	17-Apr-18	14-May-18	0
S2A2-8P2G6	P&J Deck - Lower Mezz A2 (Summary for 4D)	17	26-Apr-18	18-May-18	5
S2F2-8P2G6	P&J Deck - Lower Mezz F2 (Summary for 4D)	18	27-Apr-18	22-May-18	5
S2A3-8P2G6	P&J Deck - Lower Mezz A3 (Summary for 4D)	15	07-May-18	25-May-18	11
S2F3-8P2G6	P&J Deck - Lower Mezz F3 (Summary for 4D)	15	09-May-18	30-May-18	13
S2B1-8P2G6	P&J Deck - Lower Mezz B1 (Summary for 4D)	15	16-May-18	06-Jun-18	10
S2E1-8P2G6	P&J Deck - Lower Mezz E1 (Summary for 4D)	15	17-May-18	07-Jun-18	13
S2B2-8P2G6	P&J Deck - Lower Mezz B2 (Summary for 4D)	16	23-May-18	14-Jun-18	4
S2E2-8P2G6	P&J Deck - Lower Mezz E2 (Summary for 4D)	15	24-May-18	14-Jun-18	7
S2B3-8P2G6	P&J Deck - Lower Mezz B3 (Summary for 4D)	15	04-Jun-18	22-Jun-18	11
S2E3-8P2G6	P&J Deck - Lower Mezz E3 (Summary for 4D)	16	06-Jun-18	27-Jun-18	10
S2B4-8P2G6	P&J Deck - Lower Mezz B4 (Summary for 4D)	15	11-Jun-18	29-Jun-18	15
S2E4-8P2G6	P&J Deck - Lower Mezz E4 (Summary for 4D)	16	14-Jun-18	06-Jul-18	15
S2B5-8P2G6	P&J Deck - Lower Mezz B5 (Summary for 4D)	16	20-Jun-18	12-Jul-18	16
S2E5-8P2G6	P&J Deck - Lower Mezz E5 (Summary for 4D)	15	22-Jun-18	13-Jul-18	15
S2C1-8P2G6	P&J Deck - Lower Mezz C1 (Summary for 4D)	16	09-Jul-18	30-Jul-18	17
S2D1-8P2G6	P&J Deck - Lower Mezz D1 (Summary for 4D)	15	11-Jul-18	31-Jul-18	19
S2C2-8P2G6	P&J Deck - Lower Mezz C2 (Summary for 4D)	16	16-Jul-18	06-Aug-18	20
S2D2-8P2G6	P&J Deck - Lower Mezz D2 (Summary for 4D)	15	18-Jul-18	07-Aug-18	23
S2A1-8P2G0	Shore P&J Deck - Lower Mezz A1	8	16-Apr-18	25-Apr-18	2
S2F1-8P2G0	Shore P&J Deck - Lower Mezz F1	7	17-Apr-18	25-Apr-18	3
S2A2-8P2G0	Shore P&J Deck - Lower Mezz A2	7	26-Apr-18	04-May-18	5
S2F2-8P2G0	Shore P&J Deck - Lower Mezz F2	8	27-Apr-18	08-May-18	5
S2A3-8P2G0	Shore P&J Deck - Lower Mezz A3	5	07-May-18	11-May-18	6
S2F3-8P2G0	Shore P&J Deck - Lower Mezz F3	5	09-May-18	15-May-18	8
S2B1-8P2G0	Shore P&J Deck - Lower Mezz B1	5	16-May-18	22-May-18	4
S2E1-8P2G0	Shore P&J Deck - Lower Mezz E1	5	17-May-18	23-May-18	7
S2B2-8P2G0	Shore P&J Deck - Lower Mezz B2	6	23-May-18	31-May-18	4
S2E2-8P2G0	Shore P&J Deck - Lower Mezz E2	5	24-May-18	31-May-18	7
S2B3-8P2G0	Shore P&J Deck - Lower Mezz B3	5	04-Jun-18	08-Jun-18	11
S2E3-8P2G0	Shore P&J Deck - Lower Mezz E3	6	06-Jun-18	13-Jun-18	10
S2B4-8P2G0	Shore P&J Deck - Lower Mezz B4	5	11-Jun-18	15-Jun-18	15
S2E4-8P2G0	Shore P&J Deck - Lower Mezz E4	6	14-Jun-18	21-Jun-18	15
S2B5-8P2G0	Shore P&J Deck - Lower Mezz B5	5	20-Jun-18	26-Jun-18	16
S2E5-8P2G0	Shore P&J Deck - Lower Mezz E5	4	22-Jun-18	27-Jun-18	15
S2C1-8P2G0	Shore P&J Deck - Lower Mezz C1	5	09-Jul-18	13-Jul-18	17
S2D1-8P2G0	Shore P&J Deck - Lower Mezz D1	5	11-Jul-18	17-Jul-18	19
S2C2-8P2G0	Shore P&J Deck - Lower Mezz C2	5	16-Jul-18	20-Jul-18	20
S2D2-8P2G0	Shore P&J Deck - Lower Mezz D2	5	18-Jul-18	24-Jul-18	23

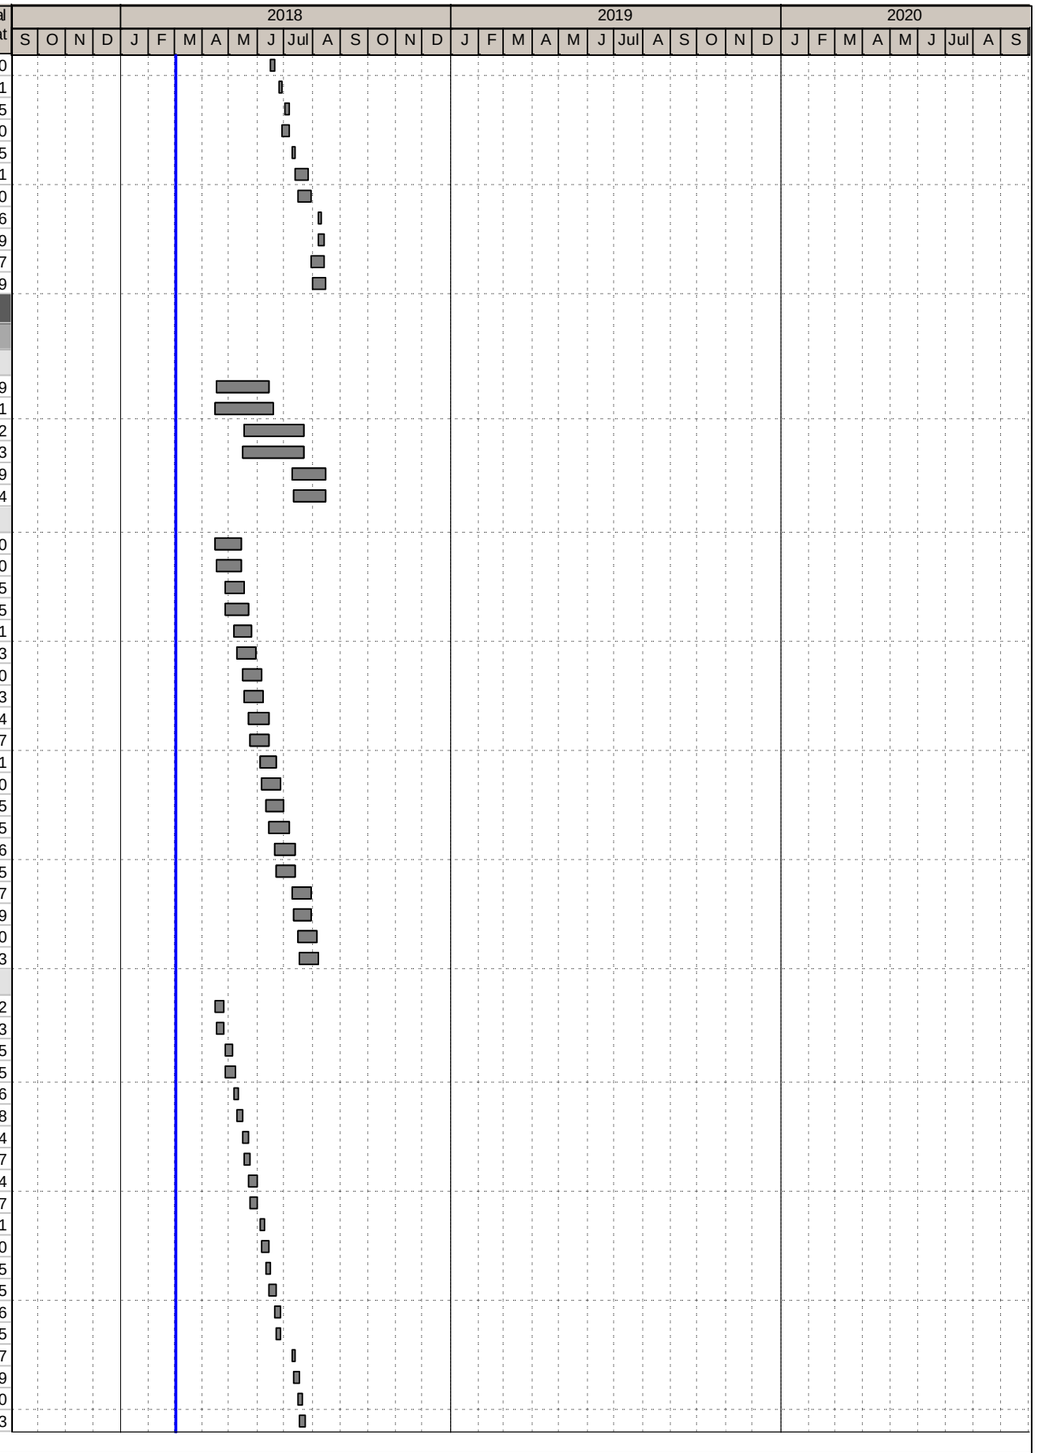

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S2A1-8P2G1	Set Pans - Lower Mezz A1	7	19-Apr-18	27-Apr-18	2
S2F1-8P2G1	Set Pans - Lower Mezz F1	6	20-Apr-18	27-Apr-18	3
S2A2-8P2G1	Set Pans - Lower Mezz A2	6	01-May-18	08-May-18	5
S2F2-8P2G1	Set Pans - Lower Mezz F2	7	02-May-18	10-May-18	5
S2A3-8P2G1	Set Pans - Lower Mezz A3	4	10-May-18	15-May-18	9
S2F3-8P2G1	Set Pans - Lower Mezz F3	4	14-May-18	17-May-18	12
S2B1-8P2G1	Set Pans - Lower Mezz B1	4	21-May-18	24-May-18	6
S2E1-8P2G1	Set Pans - Lower Mezz E1	4	22-May-18	25-May-18	9
S2B2-8P2G1	Set Pans - Lower Mezz B2	5	29-May-18	04-Jun-18	4
S2E2-8P2G1	Set Pans - Lower Mezz E2	4	30-May-18	04-Jun-18	7
S2B3-8P2G1	Set Pans - Lower Mezz B3	4	07-Jun-18	12-Jun-18	11
S2E3-8P2G1	Set Pans - Lower Mezz E3	5	11-Jun-18	15-Jun-18	10
S2B4-8P2G1	Set Pans - Lower Mezz B4	4	14-Jun-18	19-Jun-18	15
S2E4-8P2G1	Set Pans - Lower Mezz E4	5	19-Jun-18	25-Jun-18	15
S2B5-8P2G1	Set Pans - Lower Mezz B5	4	25-Jun-18	28-Jun-18	16
S2E5-8P2G1	Set Pans - Lower Mezz E5	4	26-Jun-18	29-Jun-18	15
S2C1-8P2G1	Set Pans - Lower Mezz C1	4	12-Jul-18	17-Jul-18	17
S2D1-8P2G1	Set Pans - Lower Mezz D1	4	16-Jul-18	19-Jul-18	19
S2C2-8P2G1	Set Pans - Lower Mezz C2	4	19-Jul-18	24-Jul-18	20
S2D2-8P2G1	Set Pans - Lower Mezz D2	4	23-Jul-18	26-Jul-18	23
S2A1-8P2G2	Layout in P&J Deck - Lower Mezz A1	2	26-Apr-18	27-Apr-18	2
S2F1-8P2G2	Layout in P&J Deck - Lower Mezz F1	2	26-Apr-18	27-Apr-18	3
S2A2-8P2G2	Layout in P&J Deck - Lower Mezz A2	2	07-May-18	08-May-18	5
S2F2-8P2G2	Layout in P&J Deck - Lower Mezz F2	2	09-May-18	10-May-18	5
S2A3-8P2G2	Layout in P&J Deck - Lower Mezz A3	2	14-May-18	15-May-18	9
S2F3-8P2G2	Layout in P&J Deck - Lower Mezz F3	2	16-May-18	17-May-18	12
S2B1-8P2G2	Layout in P&J Deck - Lower Mezz B1	2	23-May-18	24-May-18	6
S2E1-8P2G2	Layout in P&J Deck - Lower Mezz E1	2	24-May-18	25-May-18	9
S2B2-8P2G2	Layout in P&J Deck - Lower Mezz B2	2	01-Jun-18	04-Jun-18	4
S2E2-8P2G2	Layout in P&J Deck - Lower Mezz E2	2	01-Jun-18	04-Jun-18	7
S2B3-8P2G2	Layout in P&J Deck - Lower Mezz B3	2	11-Jun-18	12-Jun-18	11
S2E3-8P2G2	Layout in P&J Deck - Lower Mezz E3	2	14-Jun-18	15-Jun-18	10
S2B4-8P2G2	Layout in P&J Deck - Lower Mezz B4	2	18-Jun-18	19-Jun-18	15
S2E4-8P2G2	Layout in P&J Deck - Lower Mezz E4	2	22-Jun-18	25-Jun-18	15
S2B5-8P2G2	Layout in P&J Deck - Lower Mezz B5	2	27-Jun-18	28-Jun-18	16
S2E5-8P2G2	Layout in P&J Deck - Lower Mezz E5	2	28-Jun-18	29-Jun-18	15
S2C1-8P2G2	Layout in P&J Deck - Lower Mezz C1	2	16-Jul-18	17-Jul-18	17
S2D1-8P2G2	Layout in P&J Deck - Lower Mezz D1	2	18-Jul-18	19-Jul-18	19
S2C2-8P2G2	Layout in P&J Deck - Lower Mezz C2	2	23-Jul-18	24-Jul-18	20
S2D2-8P2G2	Layout in P&J Deck - Lower Mezz D2	2	25-Jul-18	26-Jul-18	23
Form					
S2F1-8P2GM	Edge Form / Bulkheads - Lower Mezz F1	3	02-May-18	04-May-18	4
S2A1-8P2GM	Edge Form / Bulkheads - Lower Mezz A1	3	03-May-18	07-May-18	3
S2A2-8P2GM	Edge Form / Bulkheads - Lower Mezz A2	3	11-May-18	15-May-18	6
S2F2-8P2GM	Edge Form / Bulkheads - Lower Mezz F2	3	15-May-18	17-May-18	6
S2A3-8P2GM	Edge Form / Bulkheads - Lower Mezz A3	3	18-May-18	22-May-18	12
S2F3-8P2GM	Edge Form / Bulkheads - Lower Mezz F3	3	22-May-18	24-May-18	14
S2B1-8P2GM	Edge Form / Bulkheads - Lower Mezz B1	3	30-May-18	01-Jun-18	8
S2E1-8P2GM	Edge Form / Bulkheads - Lower Mezz E1	2	01-Jun-18	04-Jun-18	10
S2B2-8P2GM	Edge Form / Bulkheads - Lower Mezz B2	3	07-Jun-18	11-Jun-18	5
S2E2-8P2GM	Edge Form / Bulkheads - Lower Mezz E2	3	07-Jun-18	11-Jun-18	8
S2B3-8P2GM	Edge Form / Bulkheads - Lower Mezz B3	3	15-Jun-18	19-Jun-18	12
S2E3-8P2GM	Edge Form / Bulkheads - Lower Mezz E3	3	20-Jun-18	22-Jun-18	11
S2B4-8P2GM	Edge Form / Bulkheads - Lower Mezz B4	3	22-Jun-18	26-Jun-18	16
S2E4-8P2GM	Edge Form / Bulkheads - Lower Mezz E4	3	28-Jun-18	02-Jul-18	16
S2B5-8P2GM	Edge Form / Bulkheads - Lower Mezz B5	4	05-Jul-18	10-Jul-18	16
S2E5-8P2GM	Edge Form / Bulkheads - Lower Mezz E5	4	06-Jul-18	11-Jul-18	15
S2C1-8P2GM	Edge Form / Bulkheads - Lower Mezz C1	4	23-Jul-18	26-Jul-18	17
S2D1-8P2GM	Edge Form / Bulkheads - Lower Mezz D1	3	25-Jul-18	27-Jul-18	19
S2C2-8P2GM	Edge Form / Bulkheads - Lower Mezz C2	4	30-Jul-18	02-Aug-18	20
S2D2-8P2GM	Edge Form / Bulkheads - Lower Mezz D2	3	01-Aug-18	03-Aug-18	23

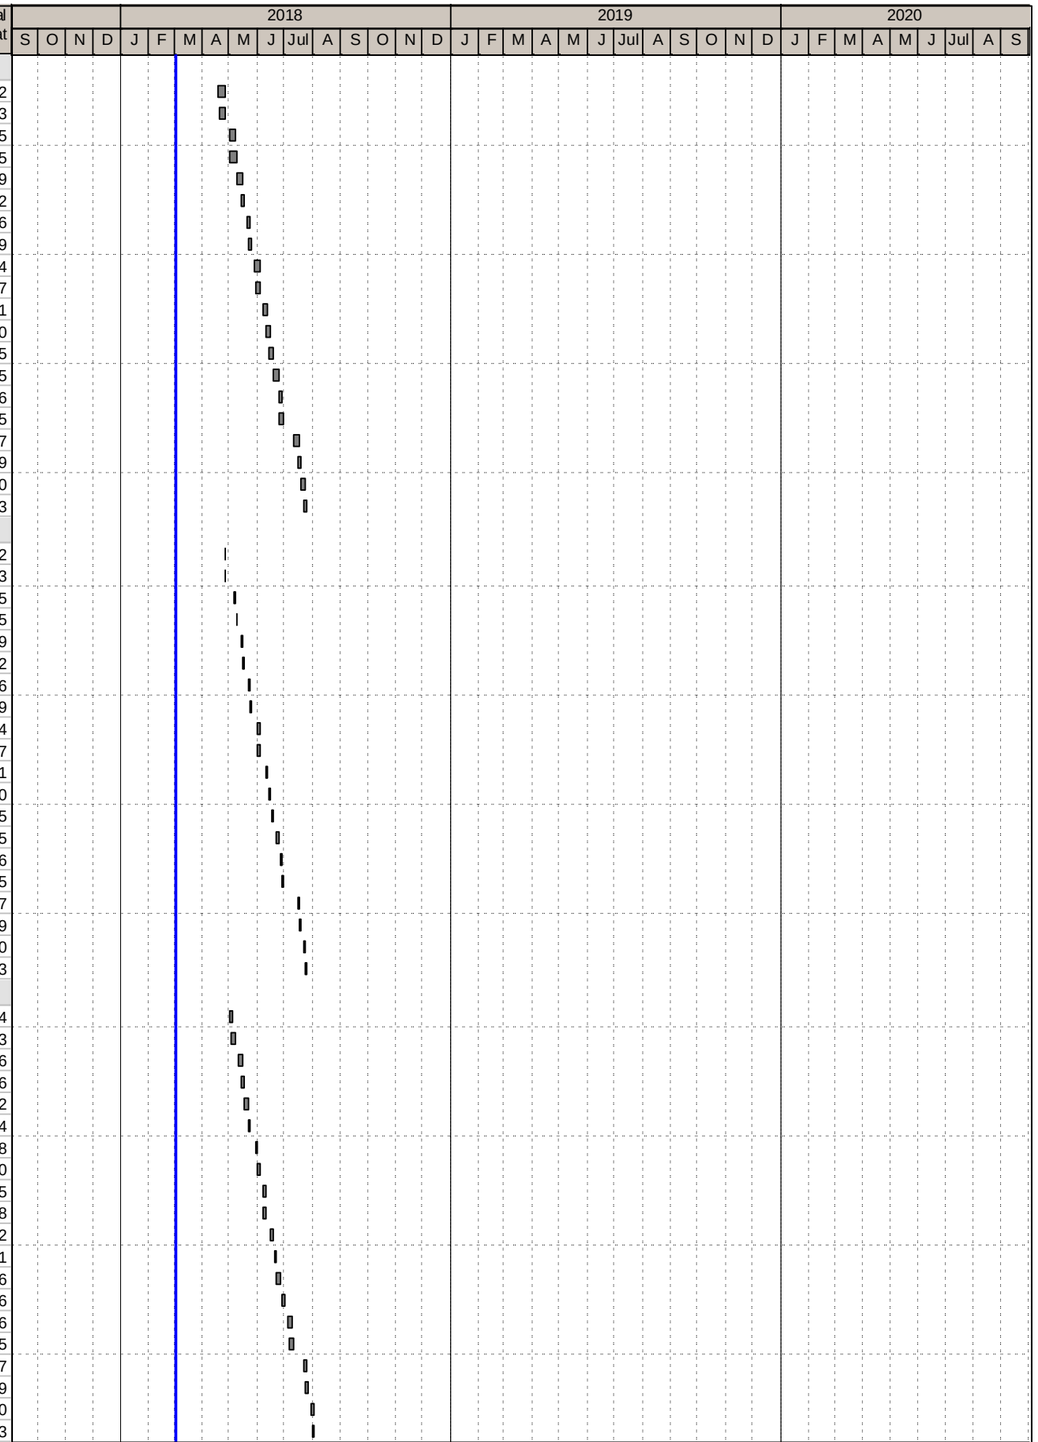

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
Reinforce					
S2F1-8P2GC	Girder Reinforcing - Lower Mezz F1	4	26-Apr-18	01-May-18	3
S2A1-8P2GC	Girder Reinforcing - Lower Mezz A1	5	26-Apr-18	02-May-18	2
S2A2-8P2GC	Girder Reinforcing - Lower Mezz A2	4	07-May-18	10-May-18	5
S2F2-8P2GC	Girder Reinforcing - Lower Mezz F2	4	09-May-18	14-May-18	5
S2A3-8P2GC	Girder Reinforcing - Lower Mezz A3	2	16-May-18	17-May-18	9
S2F3-8P2GC	Girder Reinforcing - Lower Mezz F3	3	17-May-18	21-May-18	12
S2B1-8P2GC	Girder Reinforcing - Lower Mezz B1	4	23-May-18	29-May-18	6
S2E1-8P2GC	Girder Reinforcing - Lower Mezz E1	3	25-May-18	30-May-18	9
S2B2-8P2GC	Girder Reinforcing - Lower Mezz B2	3	04-Jun-18	06-Jun-18	4
S2E2-8P2GC	Girder Reinforcing - Lower Mezz E2	3	04-Jun-18	06-Jun-18	7
S2B3-8P2GC	Girder Reinforcing - Lower Mezz B3	2	13-Jun-18	14-Jun-18	11
S2E3-8P2GC	Girder Reinforcing - Lower Mezz E3	3	15-Jun-18	19-Jun-18	10
S2B4-8P2GC	Girder Reinforcing - Lower Mezz B4	3	19-Jun-18	21-Jun-18	15
S2E4-8P2GC	Girder Reinforcing - Lower Mezz E4	3	25-Jun-18	27-Jun-18	15
S2B5-8P2GC	Girder Reinforcing - Lower Mezz B5	3	28-Jun-18	02-Jul-18	16
S2E5-8P2GC	Girder Reinforcing - Lower Mezz E5	3	29-Jun-18	03-Jul-18	15
S2C1-8P2GC	Girder Reinforcing - Lower Mezz C1	4	16-Jul-18	19-Jul-18	17
S2D1-8P2GC	Girder Reinforcing - Lower Mezz D1	3	19-Jul-18	23-Jul-18	19
S2C2-8P2GC	Girder Reinforcing - Lower Mezz C2	3	24-Jul-18	26-Jul-18	20
S2D2-8P2GC	Girder Reinforcing - Lower Mezz D2	3	26-Jul-18	30-Jul-18	23
S2F1-8P2G3	Beams/Joists Reinforcing - Lower Mezz F1	4	30-Apr-18	03-May-18	3
S2A1-8P2G3	Beams/Joists Reinforcing - Lower Mezz A1	5	30-Apr-18	04-May-18	2
S2A2-8P2G3	Beams/Joists Reinforcing - Lower Mezz A2	4	09-May-18	14-May-18	5
S2F2-8P2G3	Beams/Joists Reinforcing - Lower Mezz F2	4	11-May-18	16-May-18	5
S2A3-8P2G3	Beams/Joists Reinforcing - Lower Mezz A3	3	17-May-18	21-May-18	10
S2F3-8P2G3	Beams/Joists Reinforcing - Lower Mezz F3	3	21-May-18	23-May-18	12
S2B1-8P2G3	Beams/Joists Reinforcing - Lower Mezz B1	3	29-May-18	31-May-18	6
S2E1-8P2G3	Beams/Joists Reinforcing - Lower Mezz E1	3	30-May-18	01-Jun-18	9
S2B2-8P2G3	Beams/Joists Reinforcing - Lower Mezz B2	4	05-Jun-18	08-Jun-18	4
S2E2-8P2G3	Beams/Joists Reinforcing - Lower Mezz E2	3	06-Jun-18	08-Jun-18	7
S2B3-8P2G3	Beams/Joists Reinforcing - Lower Mezz B3	3	14-Jun-18	18-Jun-18	11
S2E3-8P2G3	Beams/Joists Reinforcing - Lower Mezz E3	4	18-Jun-18	21-Jun-18	10
S2B4-8P2G3	Beams/Joists Reinforcing - Lower Mezz B4	3	21-Jun-18	25-Jun-18	15
S2E4-8P2G3	Beams/Joists Reinforcing - Lower Mezz E4	3	27-Jun-18	29-Jun-18	15
S2B5-8P2G3	Beams/Joists Reinforcing - Lower Mezz B5	2	03-Jul-18	05-Jul-18	16
S2E5-8P2G3	Beams/Joists Reinforcing - Lower Mezz E5	2	05-Jul-18	06-Jul-18	15
S2C1-8P2G3	Beams/Joists Reinforcing - Lower Mezz C1	2	20-Jul-18	23-Jul-18	17
S2D1-8P2G3	Beams/Joists Reinforcing - Lower Mezz D1	2	24-Jul-18	25-Jul-18	19
S2C2-8P2G3	Beams/Joists Reinforcing - Lower Mezz C2	2	27-Jul-18	30-Jul-18	20
S2D2-8P2G3	Beams/Joists Reinforcing - Lower Mezz D2	2	31-Jul-18	01-Aug-18	23
Mech Embeds					
S2F1-8P2GL	Mech in P&J - Lower Mezz F1	3	02-May-18	04-May-18	3
S2A1-8P2GL	Mech in P&J - Lower Mezz A1	3	03-May-18	07-May-18	2
S2A2-8P2GL	Mech in P&J - Lower Mezz A2	3	11-May-18	15-May-18	5
S2F2-8P2GL	Mech in P&J - Lower Mezz F2	3	15-May-18	17-May-18	5
S2A3-8P2GL	Mech in P&J - Lower Mezz A3	2	21-May-18	22-May-18	11
S2F3-8P2GL	Mech in P&J - Lower Mezz F3	2	23-May-18	24-May-18	13
S2B1-8P2GL	Mech in P&J - Lower Mezz B1	2	31-May-18	01-Jun-18	7
S2E1-8P2GL	Mech in P&J - Lower Mezz E1	2	01-Jun-18	04-Jun-18	10
S2B2-8P2GL	Mech in P&J - Lower Mezz B2	3	07-Jun-18	11-Jun-18	4
S2E2-8P2GL	Mech in P&J - Lower Mezz E2	2	08-Jun-18	11-Jun-18	7
S2B3-8P2GL	Mech in P&J - Lower Mezz B3	2	18-Jun-18	19-Jun-18	11
S2E3-8P2GL	Mech in P&J - Lower Mezz E3	3	20-Jun-18	22-Jun-18	10
S2B4-8P2GL	Mech in P&J - Lower Mezz B4	3	22-Jun-18	26-Jun-18	15
S2E4-8P2GL	Mech in P&J - Lower Mezz E4	3	28-Jun-18	02-Jul-18	15
S2B5-8P2GL	Mech in P&J - Lower Mezz B5	2	05-Jul-18	06-Jul-18	17
S2E5-8P2GL	Mech in P&J - Lower Mezz E5	2	06-Jul-18	09-Jul-18	16
S2C1-8P2GL	Mech in P&J - Lower Mezz C1	2	23-Jul-18	24-Jul-18	18
S2D1-8P2GL	Mech in P&J - Lower Mezz D1	2	25-Jul-18	26-Jul-18	19
S2C2-8P2GL	Mech in P&J - Lower Mezz C2	2	30-Jul-18	31-Jul-18	21
S2D2-8P2GL	Mech in P&J - Lower Mezz D2	2	01-Aug-18	02-Aug-18	23

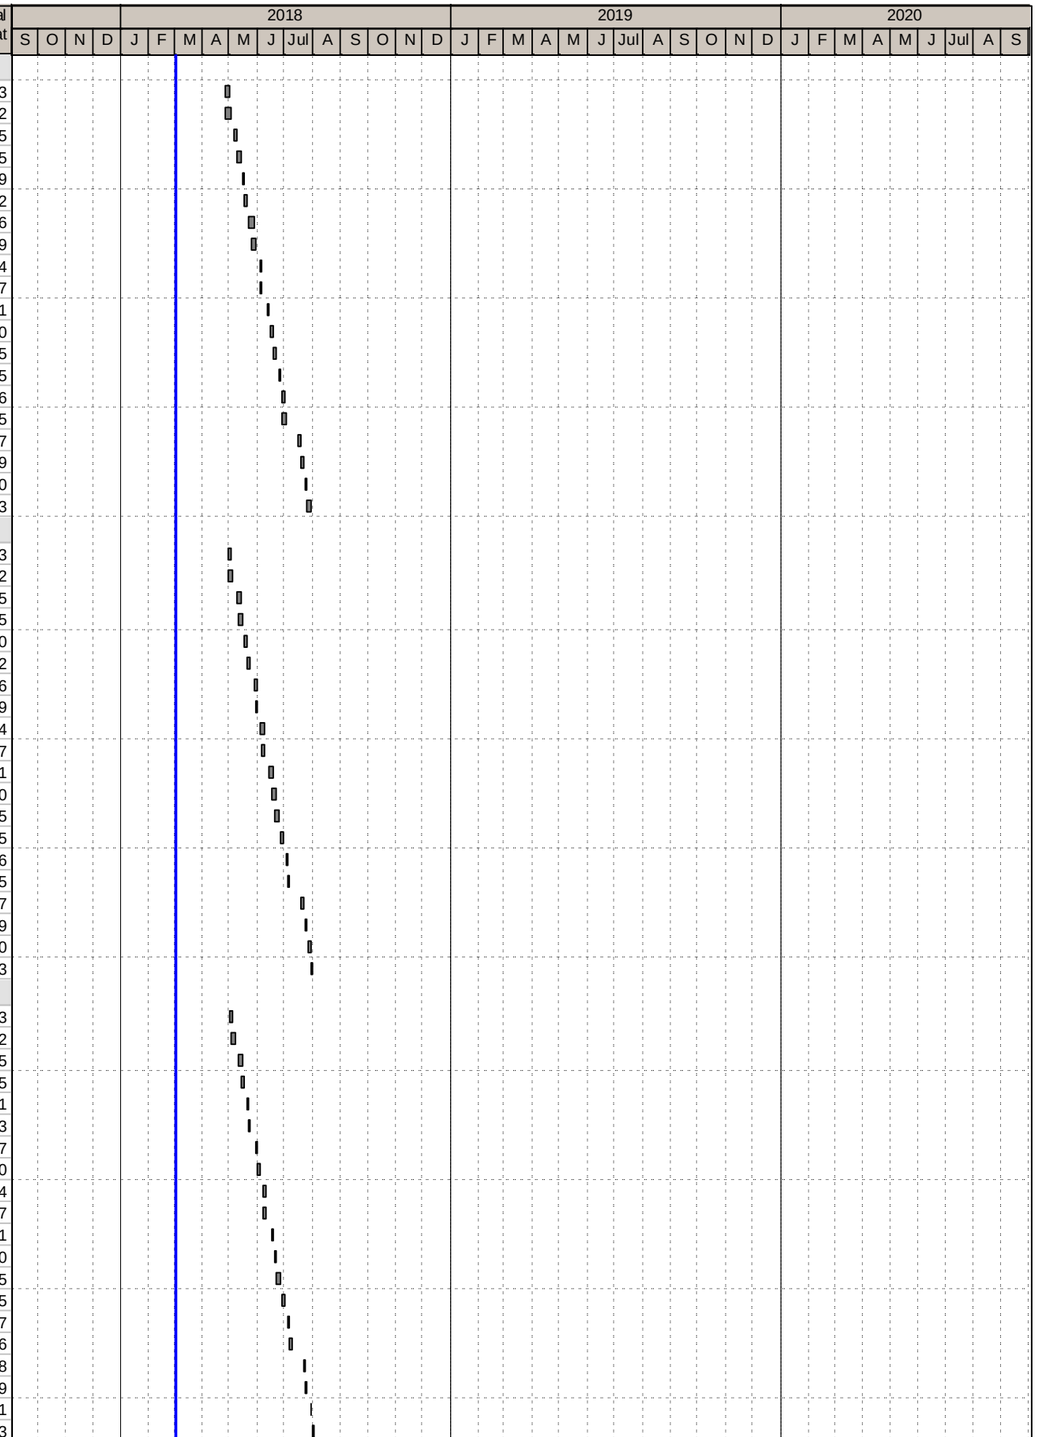

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
Elec Embeds					
S2F1-8P2GE	Elec in P&J - Lower Mezz F1	3	02-May-18	04-May-18	3
S2A1-8P2GE	Elec in P&J - Lower Mezz A1	3	03-May-18	07-May-18	2
S2A2-8P2GE	Elec in P&J - Lower Mezz A2	3	11-May-18	15-May-18	5
S2F2-8P2GE	Elec in P&J - Lower Mezz F2	3	15-May-18	17-May-18	5
S2A3-8P2GE	Elec in P&J - Lower Mezz A3	2	21-May-18	22-May-18	11
S2F3-8P2GE	Elec in P&J - Lower Mezz F3	2	23-May-18	24-May-18	13
S2B1-8P2GE	Elec in P&J - Lower Mezz B1	2	31-May-18	01-Jun-18	7
S2E1-8P2GE	Elec in P&J - Lower Mezz E1	2	01-Jun-18	04-Jun-18	10
S2B2-8P2GE	Elec in P&J - Lower Mezz B2	3	07-Jun-18	11-Jun-18	4
S2E2-8P2GE	Elec in P&J - Lower Mezz E2	2	08-Jun-18	11-Jun-18	7
S2B3-8P2GE	Elec in P&J - Lower Mezz B3	2	18-Jun-18	19-Jun-18	11
S2E3-8P2GE	Elec in P&J - Lower Mezz E3	3	20-Jun-18	22-Jun-18	10
S2B4-8P2GE	Elec in P&J - Lower Mezz B4	3	22-Jun-18	26-Jun-18	15
S2E4-8P2GE	Elec in P&J - Lower Mezz E4	3	28-Jun-18	02-Jul-18	15
S2B5-8P2GE	Elec in P&J - Lower Mezz B5	2	05-Jul-18	06-Jul-18	17
S2E5-8P2GE	Elec in P&J - Lower Mezz E5	2	06-Jul-18	09-Jul-18	16
S2C1-8P2GE	Elec in P&J - Lower Mezz C1	2	23-Jul-18	24-Jul-18	18
S2D1-8P2GE	Elec in P&J - Lower Mezz D1	2	25-Jul-18	26-Jul-18	19
S2C2-8P2GE	Elec in P&J - Lower Mezz C2	2	30-Jul-18	31-Jul-18	21
S2D2-8P2GE	Elec in P&J - Lower Mezz D2	2	01-Aug-18	02-Aug-18	23
S2F1-8P2G4	Slab Reinforcing - Lower Mezz F1	2	04-May-18	07-May-18	3
S2A1-8P2G4	Slab Reinforcing - Lower Mezz A1	2	07-May-18	08-May-18	2
S2A2-8P2G4	Slab Reinforcing - Lower Mezz A2	2	15-May-18	16-May-18	5
S2F2-8P2G4	Slab Reinforcing - Lower Mezz F2	2	17-May-18	18-May-18	5
S2A3-8P2G4	Slab Reinforcing - Lower Mezz A3	2	22-May-18	23-May-18	11
S2F3-8P2G4	Slab Reinforcing - Lower Mezz F3	2	24-May-18	25-May-18	13
S2B1-8P2G4	Slab Reinforcing - Lower Mezz B1	2	01-Jun-18	04-Jun-18	10
S2E1-8P2G4	Slab Reinforcing - Lower Mezz E1	2	04-Jun-18	05-Jun-18	13
S2B2-8P2G4	Slab Reinforcing - Lower Mezz B2	2	11-Jun-18	12-Jun-18	4
S2E2-8P2G4	Slab Reinforcing - Lower Mezz E2	2	11-Jun-18	12-Jun-18	7
S2B3-8P2G4	Slab Reinforcing - Lower Mezz B3	2	19-Jun-18	20-Jun-18	11
S2E3-8P2G4	Slab Reinforcing - Lower Mezz E3	2	22-Jun-18	25-Jun-18	10
S2B4-8P2G4	Slab Reinforcing - Lower Mezz B4	2	26-Jun-18	27-Jun-18	15
S2E4-8P2G4	Slab Reinforcing - Lower Mezz E4	2	02-Jul-18	03-Jul-18	15
S2B5-8P2G4	Slab Reinforcing - Lower Mezz B5	2	06-Jul-18	09-Jul-18	17
S2E5-8P2G4	Slab Reinforcing - Lower Mezz E5	1	10-Jul-18	10-Jul-18	16
S2C1-8P2G4	Slab Reinforcing - Lower Mezz C1	1	25-Jul-18	25-Jul-18	18
S2D1-8P2G4	Slab Reinforcing - Lower Mezz D1	1	27-Jul-18	27-Jul-18	19
S2C2-8P2G4	Slab Reinforcing - Lower Mezz C2	1	01-Aug-18	01-Aug-18	21
S2D2-8P2G4	Slab Reinforcing - Lower Mezz D2	1	03-Aug-18	03-Aug-18	23
S2F1-8P2G5	Clean P&J Deck - Lower Mezz F1	1	08-May-18	08-May-18	3
S2A1-8P2G5	Clean P&J Deck - Lower Mezz A1	1	09-May-18	09-May-18	2
S2A2-8P2G5	Clean P&J Deck - Lower Mezz A2	1	17-May-18	17-May-18	5
S2F2-8P2G5	Clean P&J Deck - Lower Mezz F2	1	21-May-18	21-May-18	5
S2A3-8P2G5	Clean P&J Deck - Lower Mezz A3	1	24-May-18	24-May-18	11
S2F3-8P2G5	Clean P&J Deck - Lower Mezz F3	1	29-May-18	29-May-18	13
S2B1-8P2G5	Clean P&J Deck - Lower Mezz B1	1	05-Jun-18	05-Jun-18	10
S2E1-8P2G5	Clean P&J Deck - Lower Mezz E1	1	06-Jun-18	06-Jun-18	13
S2B2-8P2G5	Clean P&J Deck - Lower Mezz B2	1	13-Jun-18	13-Jun-18	4
S2E2-8P2G5	Clean P&J Deck - Lower Mezz E2	1	13-Jun-18	13-Jun-18	7
S2B3-8P2G5	Clean P&J Deck - Lower Mezz B3	1	21-Jun-18	21-Jun-18	11
S2E3-8P2G5	Clean P&J Deck - Lower Mezz E3	1	26-Jun-18	26-Jun-18	10
S2B4-8P2G5	Clean P&J Deck - Lower Mezz B4	1	28-Jun-18	28-Jun-18	15
S2E4-8P2G5	Clean P&J Deck - Lower Mezz E4	1	05-Jul-18	05-Jul-18	15
S2B5-8P2G5	Clean P&J Deck - Lower Mezz B5	1	11-Jul-18	11-Jul-18	16
S2E5-8P2G5	Clean P&J Deck - Lower Mezz E5	1	12-Jul-18	12-Jul-18	15
S2C1-8P2G5	Clean P&J Deck - Lower Mezz C1	1	27-Jul-18	27-Jul-18	17
S2D1-8P2G5	Clean P&J Deck - Lower Mezz D1	1	30-Jul-18	30-Jul-18	19
S2C2-8P2G5	Clean P&J Deck - Lower Mezz C2	1	03-Aug-18	03-Aug-18	20
S2D2-8P2G5	Clean P&J Deck - Lower Mezz D2	1	06-Aug-18	06-Aug-18	23

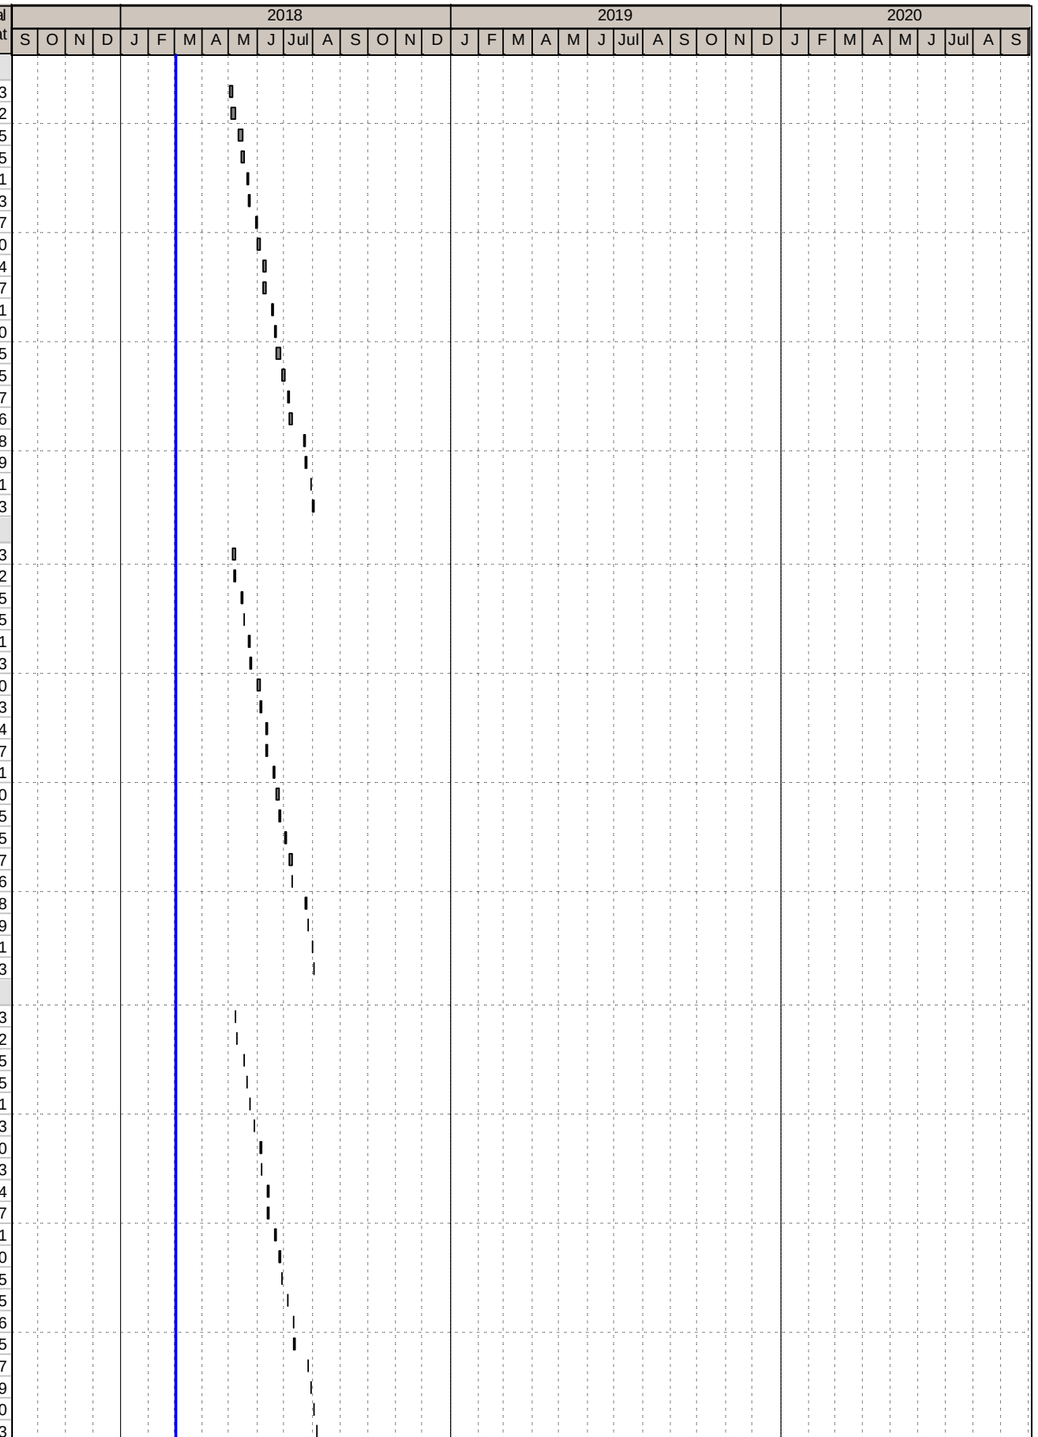

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S2A1-8P2GH	Pour P&J Deck - Lower Mezz A1	1	14-May-18	14-May-18	0
S2F1-8P2GH	Pour P&J Deck - Lower Mezz F1	1	14-May-18	14-May-18	0
S2A2-8P2GH	Pour P&J Deck - Lower Mezz A2	1	18-May-18	18-May-18	5
S2F2-8P2GH	Pour P&J Deck - Lower Mezz F2	1	22-May-18	22-May-18	5
S2A3-8P2GH	Pour P&J Deck - Lower Mezz A3	1	25-May-18	25-May-18	11
S2F3-8P2GH	Pour P&J Deck - Lower Mezz F3	1	30-May-18	30-May-18	13
S2B1-8P2GH	Pour P&J Deck - Lower Mezz B1	1	06-Jun-18	06-Jun-18	10
S2E1-8P2GH	Pour P&J Deck - Lower Mezz E1	1	07-Jun-18	07-Jun-18	13
S2B2-8P2GH	Pour P&J Deck - Lower Mezz B2	1	14-Jun-18	14-Jun-18	4
S2E2-8P2GH	Pour P&J Deck - Lower Mezz E2	1	14-Jun-18	14-Jun-18	7
S2B3-8P2GH	Pour P&J Deck - Lower Mezz B3	1	22-Jun-18	22-Jun-18	11
S2E3-8P2GH	Pour P&J Deck - Lower Mezz E3	1	27-Jun-18	27-Jun-18	10
S2B4-8P2GH	Pour P&J Deck - Lower Mezz B4	1	29-Jun-18	29-Jun-18	15
S2E4-8P2GH	Pour P&J Deck - Lower Mezz E4	1	06-Jul-18	06-Jul-18	15
S2B5-8P2GH	Pour P&J Deck - Lower Mezz B5	1	12-Jul-18	12-Jul-18	16
S2E5-8P2GH	Pour P&J Deck - Lower Mezz E5	1	13-Jul-18	13-Jul-18	15
S2C1-8P2GH	Pour P&J Deck - Lower Mezz C1	1	30-Jul-18	30-Jul-18	17
S2D1-8P2GH	Pour P&J Deck - Lower Mezz D1	1	31-Jul-18	31-Jul-18	19
S2C2-8P2GH	Pour P&J Deck - Lower Mezz C2	1	06-Aug-18	06-Aug-18	20
S2D2-8P2GH	Pour P&J Deck - Lower Mezz D2	1	07-Aug-18	07-Aug-18	23
S2A1-8P2GU	Cure P&J Deck - Lower Mezz A1	3	15-May-18	17-May-18	18
S2F1-8P2GU	Cure P&J Deck - Lower Mezz F1	3	15-May-18	17-May-18	20
S2A2-8P2GU	Cure P&J Deck - Lower Mezz A2	3	19-May-18	21-May-18	29
S2F2-8P2GU	Cure P&J Deck - Lower Mezz F2	3	23-May-18	25-May-18	32
S2A3-8P2GU	Cure P&J Deck - Lower Mezz A3	3	26-May-18	28-May-18	44
S2F3-8P2GU	Cure P&J Deck - Lower Mezz F3	3	31-May-18	02-Jun-18	47
S2B1-8P2GU	Cure P&J Deck - Lower Mezz B1	3	07-Jun-18	09-Jun-18	39
S2E1-8P2GU	Cure P&J Deck - Lower Mezz E1	3	08-Jun-18	10-Jun-18	49
S2B2-8P2GU	Cure P&J Deck - Lower Mezz B2	3	15-Jun-18	17-Jun-18	38
S2E2-8P2GU	Cure P&J Deck - Lower Mezz E2	3	15-Jun-18	17-Jun-18	46
S2B3-8P2GU	Cure P&J Deck - Lower Mezz B3	3	23-Jun-18	25-Jun-18	41
S2E3-8P2GU	Cure P&J Deck - Lower Mezz E3	3	28-Jun-18	30-Jun-18	40
S2B4-8P2GU	Cure P&J Deck - Lower Mezz B4	3	30-Jun-18	02-Jul-18	45
S2E4-8P2GU	Cure P&J Deck - Lower Mezz E4	3	07-Jul-18	09-Jul-18	45
S2B5-8P2GU	Cure P&J Deck - Lower Mezz B5	3	13-Jul-18	15-Jul-18	65
S2E5-8P2GU	Cure P&J Deck - Lower Mezz E5	3	14-Jul-18	16-Jul-18	62
S2C1-8P2GU	Cure P&J Deck - Lower Mezz C1	3	31-Jul-18	02-Aug-18	60
S2D1-8P2GU	Cure P&J Deck - Lower Mezz D1	3	01-Aug-18	03-Aug-18	53
S2C2-8P2GU	Cure P&J Deck - Lower Mezz C2	3	07-Aug-18	09-Aug-18	56
S2D2-8P2GU	Cure P&J Deck - Lower Mezz D2	3	08-Aug-18	10-Aug-18	51
S2F1-8P2GJ	Strip & Re-shore P&J Deck - Lower Mezz F1	7	18-May-18	29-May-18	13
S2A1-8P2GJ	Strip & Re-Shore P&J Deck - Lower Mezz A1	9	18-May-18	31-May-18	11
S2F2-8P2GJ	Strip & Re-Shore P&J Deck - Lower Mezz F2	7	30-May-18	07-Jun-18	20
S2A2-8P2GJ	Strip & Re-Shore P&J Deck - Lower Mezz A2	7	01-Jun-18	11-Jun-18	13
S2F3-8P2GJ	Strip & Re-Shore P&J Deck - Lower Mezz F3	5	08-Jun-18	14-Jun-18	29
S2A3-8P2GJ	Strip & Re-Shore P&J Deck - Lower Mezz A3	5	12-Jun-18	18-Jun-18	21
S2E1-8P2GJ	Strip & Re-Shore P&J Deck - Lower Mezz E1	4	15-Jun-18	20-Jun-18	30
S2B1-8P2GJ	Strip & Re-Shore P&J Deck - Lower Mezz B1	5	19-Jun-18	25-Jun-18	21
S2E2-8P2GJ	Strip & Re-Shore P&J Deck - Lower Mezz E2	5	21-Jun-18	27-Jun-18	30
S2B2-8P2GJ	Strip & Re-Shore P&J Deck - Lower Mezz B2	6	26-Jun-18	03-Jul-18	21
S2E3-8P2GJ	Strip & Re-Shore P&J Deck - Lower Mezz E3	6	02-Jul-18	10-Jul-18	28
S2B3-8P2GJ	Strip & Re-Shore P&J Deck - Lower Mezz B3	5	05-Jul-18	11-Jul-18	22
S2E4-8P2GJ	Strip & Re-Shore P&J Deck - Lower Mezz E4	5	11-Jul-18	17-Jul-18	32
S2B4-8P2GJ	Strip & Re-Shore P&J Deck - Lower Mezz B4	5	12-Jul-18	18-Jul-18	26
S2B5-8P2GJ	Strip & Re-Shore P&J Deck - Lower Mezz B5	3	19-Jul-18	23-Jul-18	43
S2E5-8P2GJ	Strip & Re-Shore P&J Deck - Lower Mezz E5	4	18-Jul-18	23-Jul-18	42
S2C1-8P2GJ	Strip & Re-Shore P&J Deck - Lower Mezz C1	3	03-Aug-18	07-Aug-18	41
S2D1-8P2GJ	Strip & Re-Shore P&J Deck - Lower Mezz D1	3	06-Aug-18	08-Aug-18	36
S2C2-8P2GJ	Strip & Re-Shore P&J Deck - Lower Mezz C2	4	10-Aug-18	15-Aug-18	39
S2D2-8P2GJ	Strip & Re-Shore P&J Deck - Lower Mezz D2	4	13-Aug-18	16-Aug-18	34

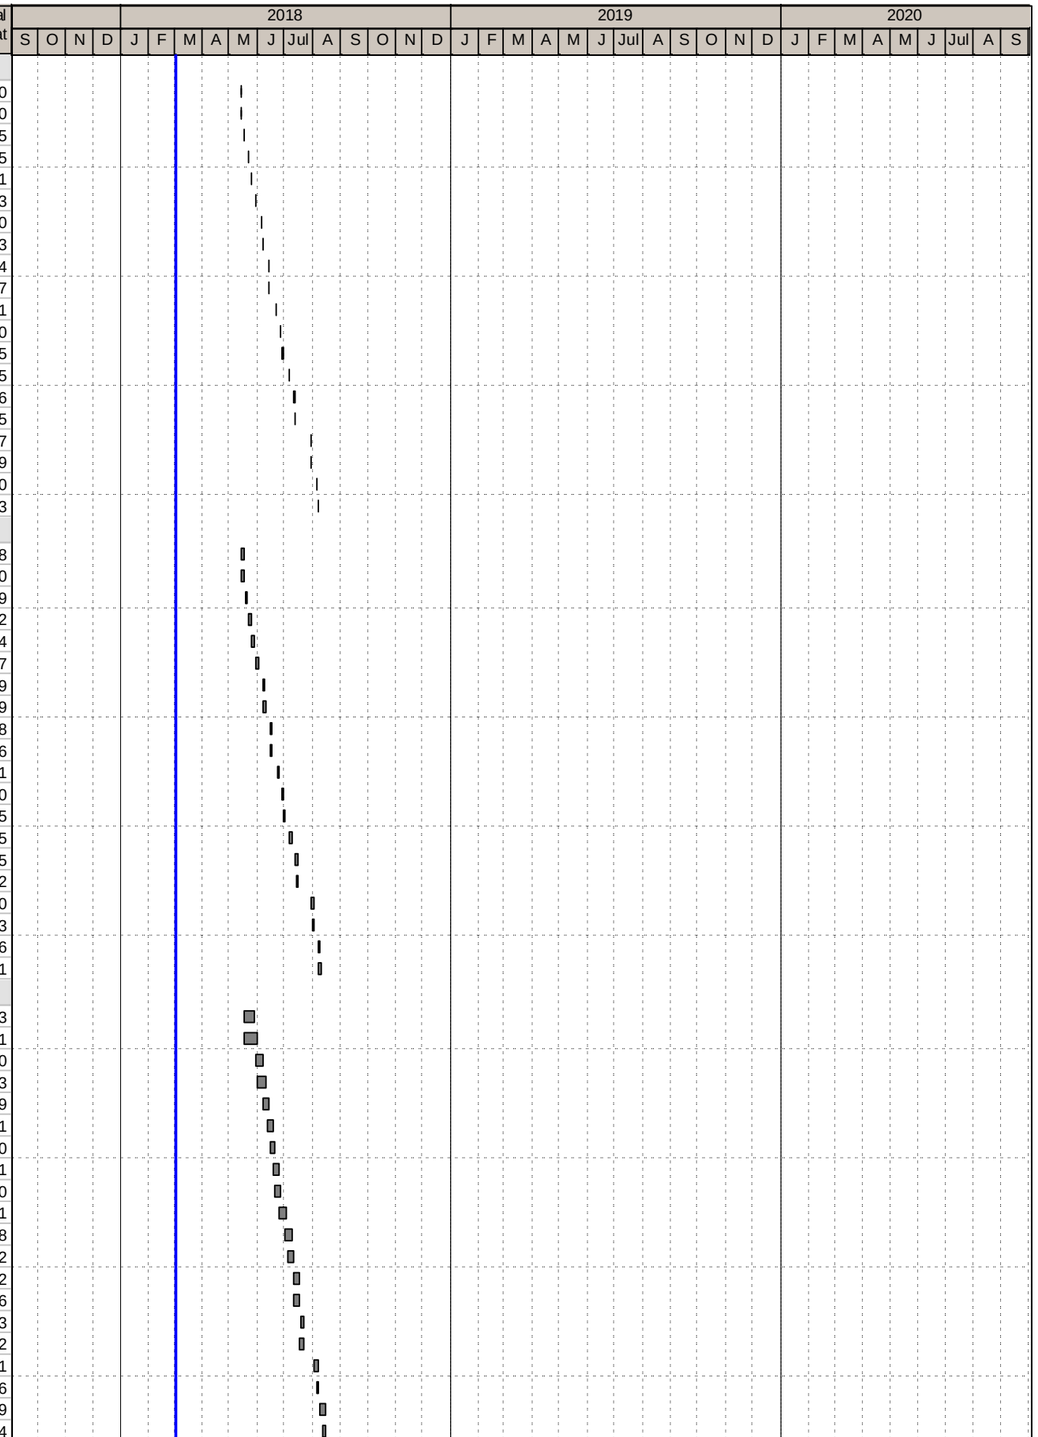

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
100 Main Concourse					
S3F0-8P10	Concrete Structure - Main Concourse F (Summary)	39	25-May-18	20-Jul-18	12
S3A0-8P10	Concrete Structure - Main Concourse A (Summary)	46	18-May-18	24-Jul-18	4
S3E0-8P10	Concrete Structure - Main Concourse E (Summary)	67	26-Jun-18	28-Sep-18	6
S3B0-8P10	Concrete Structure - Main Concourse B (Summary)	68	27-Jun-18	02-Oct-18	8
S3D0-8P10	Concrete Structure - Main Concourse D (Summary)	46	31-Aug-18	05-Nov-18	9
S3C0-8P10	Concrete Structure - Main Concourse C (Summary)	47	31-Aug-18	06-Nov-18	9
Structure					
S3A1-8P2G6	P&J Deck - Main Concourse A1 (Summary for 4D)	18	18-May-18	13-Jun-18	3
S3F1-8P2G6	P&J Deck - Main Concourse F1 (Summary for 4D)	18	25-May-18	20-Jun-18	12
S3A2-8P2G6	P&J Deck - Main Concourse A2 (Summary for 4D)	17	31-May-18	22-Jun-18	5
S3F2-8P2G6	P&J Deck - Main Concourse F2 (Summary for 4D)	17	07-Jun-18	29-Jun-18	14
S3A3-8P2G6	P&J Deck - Main Concourse A3 (Summary for 4D)	16	11-Jun-18	02-Jul-18	7
S3F3-8P2G6	P&J Deck - Main Concourse F3 (Summary for 4D)	16	18-Jun-18	10-Jul-18	13
S3A4-8P2G6	P&J Deck - Main Concourse A4 (Summary for 4D)	16	19-Jun-18	11-Jul-18	7
S3E1-8P2G6	P&J Deck - Main Concourse E1 (Summary for 4D)	15	26-Jun-18	17-Jul-18	13
S3B1-8P2G6	P&J Deck - Main Concourse B1 (Summary for 4D)	16	27-Jun-18	19-Jul-18	6
S3E2-8P2G6	P&J Deck - Main Concourse E2 (Summary for 4D)	18	03-Jul-18	27-Jul-18	10
S3B2-8P2G6	P&J Deck - Main Concourse B2 (Summary for 4D)	17	06-Jul-18	30-Jul-18	4
S3E3-8P2G6	P&J Deck - Main Concourse E3 (Summary for 4D)	20	16-Jul-18	10-Aug-18	6
S3B3-8P2G6	P&J Deck - Main Concourse B3 (Summary for 4D)	20	17-Jul-18	13-Aug-18	0
S3E4-8P2G6	P&J Deck - Main Concourse E4 (Summary for 4D)	20	27-Jul-18	23-Aug-18	6
S3B4-8P2G6	P&J Deck - Main Concourse B4 (Summary for 4D)	20	30-Jul-18	24-Aug-18	0
S3B5-8P2G6	P&J Deck - Main Concourse B5 (Summary for 4D)	17	10-Aug-18	04-Sep-18	12
S3E5-8P2G6	P&J Deck - Main Concourse E5 (Summary for 4D)	18	09-Aug-18	04-Sep-18	8
S3B6-8P2G6	P&J Deck - Main Concourse B6 (Summary for 4D)	18	21-Aug-18	14-Sep-18	6
S3E6-8P2G6	P&J Deck - Main Concourse E6 (Summary for 4D)	18	21-Aug-18	14-Sep-18	5
S3C1-8P2G6	P&J Deck - Main Concourse C1 (Summary for 4D)	17	31-Aug-18	25-Sep-18	12
S3D1-8P2G6	P&J Deck - Main Concourse D1 (Summary for 4D)	17	31-Aug-18	25-Sep-18	8
S3C2-8P2G6	P&J Deck - Main Concourse C2 (Summary for 4D)	18	12-Sep-18	05-Oct-18	5
S3D2-8P2G6	P&J Deck - Main Concourse D2 (Summary for 4D)	18	12-Sep-18	05-Oct-18	10
S3C3-8P2G6	P&J Deck - Main Concourse C3 (Summary for 4D)	17	24-Sep-18	16-Oct-18	12
S3D3-8P2G6	P&J Deck - Main Concourse D3 (Summary for 4D)	17	24-Sep-18	16-Oct-18	9
S3C4-8P2G6	P&J Deck - Main Concourse C4 (Summary for 4D)	16	03-Oct-18	24-Oct-18	12
S3D4-8P2G6	P&J Deck - Main Concourse D4 (Summary for 4D)	16	03-Oct-18	24-Oct-18	10
S3A1-8P2G0	Shore P&J Deck - Main Concourse A1	8	18-May-18	30-May-18	0
S3F1-8P2G0	Shore P&J Deck - Main Concourse F1	8	25-May-18	06-Jun-18	5
S3A2-8P2G0	Shore P&J Deck - Main Concourse A2	7	31-May-18	08-Jun-18	0
S3F2-8P2G0	Shore P&J Deck - Main Concourse F2	7	07-Jun-18	15-Jun-18	5
S3A3-8P2G0	Shore P&J Deck - Main Concourse A3	6	11-Jun-18	18-Jun-18	0
S3F3-8P2G0	Shore P&J Deck - Main Concourse F3	6	18-Jun-18	25-Jun-18	5
S3A4-8P2G0	Shore P&J Deck - Main Concourse A4	6	19-Jun-18	26-Jun-18	0
S3E1-8P2G0	Shore P&J Deck - Main Concourse E1	5	26-Jun-18	02-Jul-18	5
S3B1-8P2G0	Shore P&J Deck - Main Concourse B1	6	27-Jun-18	05-Jul-18	0
S3E2-8P2G0	Shore P&J Deck - Main Concourse E2	8	03-Jul-18	13-Jul-18	5
S3B2-8P2G0	Shore P&J Deck - Main Concourse B2	7	06-Jul-18	16-Jul-18	0
S3E3-8P2G0	Shore P&J Deck - Main Concourse E3	9	16-Jul-18	26-Jul-18	5
S3B3-8P2G0	Shore P&J Deck - Main Concourse B3	9	17-Jul-18	27-Jul-18	0
S3E4-8P2G0	Shore P&J Deck - Main Concourse E4	9	27-Jul-18	08-Aug-18	5
S3B4-8P2G0	Shore P&J Deck - Main Concourse B4	9	30-Jul-18	09-Aug-18	0
S3B5-8P2G0	Shore P&J Deck - Main Concourse B5	7	10-Aug-18	20-Aug-18	5
S3E5-8P2G0	Shore P&J Deck - Main Concourse E5	8	09-Aug-18	20-Aug-18	5
S3B6-8P2G0	Shore P&J Deck - Main Concourse B6	8	21-Aug-18	30-Aug-18	5
S3E6-8P2G0	Shore P&J Deck - Main Concourse E6	8	21-Aug-18	30-Aug-18	5
S3C1-8P2G0	Shore P&J Deck - Main Concourse C1	7	31-Aug-18	11-Sep-18	5
S3D1-8P2G0	Shore P&J Deck - Main Concourse D1	7	31-Aug-18	11-Sep-18	8
S3C2-8P2G0	Shore P&J Deck - Main Concourse C2	8	12-Sep-18	21-Sep-18	5
S3D2-8P2G0	Shore P&J Deck - Main Concourse D2	8	12-Sep-18	21-Sep-18	9
S3C3-8P2G0	Shore P&J Deck - Main Concourse C3	7	24-Sep-18	02-Oct-18	12
S3D3-8P2G0	Shore P&J Deck - Main Concourse D3	7	24-Sep-18	02-Oct-18	9
S3C4-8P2G0	Shore P&J Deck - Main Concourse C4	6	03-Oct-18	10-Oct-18	12

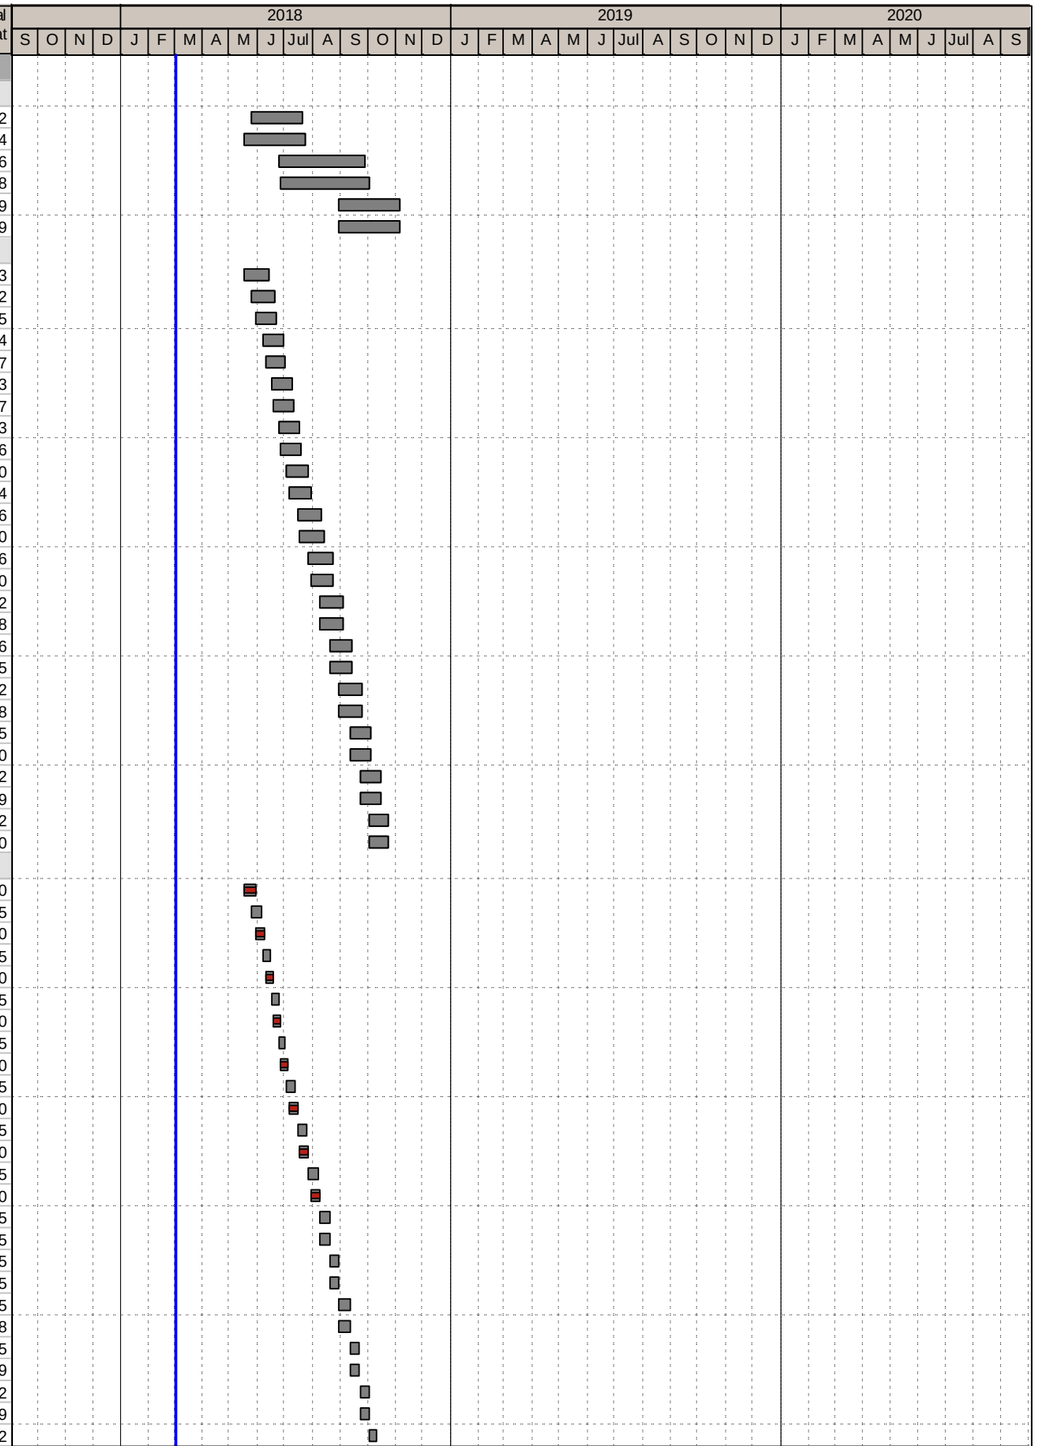

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S3D4-8P2G0	Shore P&J Deck - Main Concourse D4	6	03-Oct-18	10-Oct-18	10
S3A1-8P2G1	Set Pans - Main Concourse A1	6	24-May-18	01-Jun-18	3
S3F1-8P2G1	Set Pans - Main Concourse F1	6	01-Jun-18	08-Jun-18	12
S3A2-8P2G1	Set Pans - Main Concourse A2	6	05-Jun-18	12-Jun-18	5
S3F2-8P2G1	Set Pans - Main Concourse F2	5	13-Jun-18	19-Jun-18	14
S3A3-8P2G1	Set Pans - Main Concourse A3	5	14-Jun-18	20-Jun-18	7
S3F3-8P2G1	Set Pans - Main Concourse F3	5	21-Jun-18	27-Jun-18	13
S3A4-8P2G1	Set Pans - Main Concourse A4	5	22-Jun-18	28-Jun-18	7
S3E1-8P2G1	Set Pans - Main Concourse E1	4	29-Jun-18	05-Jul-18	13
S3B1-8P2G1	Set Pans - Main Concourse B1	5	02-Jul-18	09-Jul-18	6
S3E2-8P2G1	Set Pans - Main Concourse E2	6	10-Jul-18	17-Jul-18	10
S3B2-8P2G1	Set Pans - Main Concourse B2	6	11-Jul-18	18-Jul-18	4
S3E3-8P2G1	Set Pans - Main Concourse E3	7	20-Jul-18	30-Jul-18	6
S3B3-8P2G1	Set Pans - Main Concourse B3	7	23-Jul-18	31-Jul-18	0
S3E4-8P2G1	Set Pans - Main Concourse E4	7	02-Aug-18	10-Aug-18	6
S3B4-8P2G1	Set Pans - Main Concourse B4	7	03-Aug-18	13-Aug-18	0
S3B5-8P2G1	Set Pans - Main Concourse B5	6	15-Aug-18	22-Aug-18	10
S3E5-8P2G1	Set Pans - Main Concourse E5	6	15-Aug-18	22-Aug-18	8
S3B6-8P2G1	Set Pans - Main Concourse B6	7	24-Aug-18	04-Sep-18	6
S3E6-8P2G1	Set Pans - Main Concourse E6	6	27-Aug-18	04-Sep-18	5
S3C1-8P2G1	Set Pans - Main Concourse C1	6	06-Sep-18	13-Sep-18	9
S3D1-8P2G1	Set Pans - Main Concourse D1	5	07-Sep-18	13-Sep-18	8
S3C2-8P2G1	Set Pans - Main Concourse C2	7	17-Sep-18	25-Sep-18	5
S3D2-8P2G1	Set Pans - Main Concourse D2	6	18-Sep-18	25-Sep-18	10
S3C3-8P2G1	Set Pans - Main Concourse C3	6	27-Sep-18	04-Oct-18	12
S3D3-8P2G1	Set Pans - Main Concourse D3	5	28-Sep-18	04-Oct-18	9
S3C4-8P2G1	Set Pans - Main Concourse C4	5	08-Oct-18	12-Oct-18	12
S3D4-8P2G1	Set Pans - Main Concourse D4	5	08-Oct-18	12-Oct-18	10
S3A1-8P2G2	Layout in P&J Deck - Main Concourse A1	2	31-May-18	01-Jun-18	3
S3F1-8P2G2	Layout in P&J Deck - Main Concourse F1	2	07-Jun-18	08-Jun-18	12
S3A2-8P2G2	Layout in P&J Deck - Main Concourse A2	2	11-Jun-18	12-Jun-18	5
S3F2-8P2G2	Layout in P&J Deck - Main Concourse F2	2	18-Jun-18	19-Jun-18	14
S3A3-8P2G2	Layout in P&J Deck - Main Concourse A3	2	19-Jun-18	20-Jun-18	7
S3F3-8P2G2	Layout in P&J Deck - Main Concourse F3	2	26-Jun-18	27-Jun-18	13
S3A4-8P2G2	Layout in P&J Deck - Main Concourse A4	2	27-Jun-18	28-Jun-18	7
S3E1-8P2G2	Layout in P&J Deck - Main Concourse E1	2	03-Jul-18	05-Jul-18	13
S3B1-8P2G2	Layout in P&J Deck - Main Concourse B1	2	06-Jul-18	09-Jul-18	6
S3E2-8P2G2	Layout in P&J Deck - Main Concourse E2	2	16-Jul-18	17-Jul-18	10
S3B2-8P2G2	Layout in P&J Deck - Main Concourse B2	2	17-Jul-18	18-Jul-18	4
S3E3-8P2G2	Layout in P&J Deck - Main Concourse E3	2	27-Jul-18	30-Jul-18	6
S3B3-8P2G2	Layout in P&J Deck - Main Concourse B3	2	30-Jul-18	31-Jul-18	0
S3E4-8P2G2	Layout in P&J Deck - Main Concourse E4	2	09-Aug-18	10-Aug-18	6
S3B4-8P2G2	Layout in P&J Deck - Main Concourse B4	2	10-Aug-18	13-Aug-18	0
S3B5-8P2G2	Layout in P&J Deck - Main Concourse B5	2	21-Aug-18	22-Aug-18	10
S3E5-8P2G2	Layout in P&J Deck - Main Concourse E5	2	21-Aug-18	22-Aug-18	8
S3B6-8P2G2	Layout in P&J Deck - Main Concourse B6	2	31-Aug-18	04-Sep-18	6
S3E6-8P2G2	Layout in P&J Deck - Main Concourse E6	2	31-Aug-18	04-Sep-18	5
S3C1-8P2G2	Layout in P&J Deck - Main Concourse C1	2	12-Sep-18	13-Sep-18	9
S3D1-8P2G2	Layout in P&J Deck - Main Concourse D1	2	12-Sep-18	13-Sep-18	8
S3C2-8P2G2	Layout in P&J Deck - Main Concourse C2	2	24-Sep-18	25-Sep-18	5
S3D2-8P2G2	Layout in P&J Deck - Main Concourse D2	2	24-Sep-18	25-Sep-18	10
S3C3-8P2G2	Layout in P&J Deck - Main Concourse C3	2	03-Oct-18	04-Oct-18	12
S3D3-8P2G2	Layout in P&J Deck - Main Concourse D3	2	03-Oct-18	04-Oct-18	9
S3C4-8P2G2	Layout in P&J Deck - Main Concourse C4	2	11-Oct-18	12-Oct-18	12
S3D4-8P2G2	Layout in P&J Deck - Main Concourse D4	2	11-Oct-18	12-Oct-18	10
Form					
S3A1-8P2GM	Edge Form / Bulkheads - Main Concourse A1	3	06-Jun-18	08-Jun-18	4
S3F1-8P2GM	Edge Form / Bulkheads - Main Concourse F1	3	13-Jun-18	15-Jun-18	13
S3A2-8P2GM	Edge Form / Bulkheads - Main Concourse A2	3	15-Jun-18	19-Jun-18	6
S3F2-8P2GM	Edge Form / Bulkheads - Main Concourse F2	3	22-Jun-18	26-Jun-18	15
S3A3-8P2GM	Edge Form / Bulkheads - Main Concourse A3	3	25-Jun-18	27-Jun-18	8

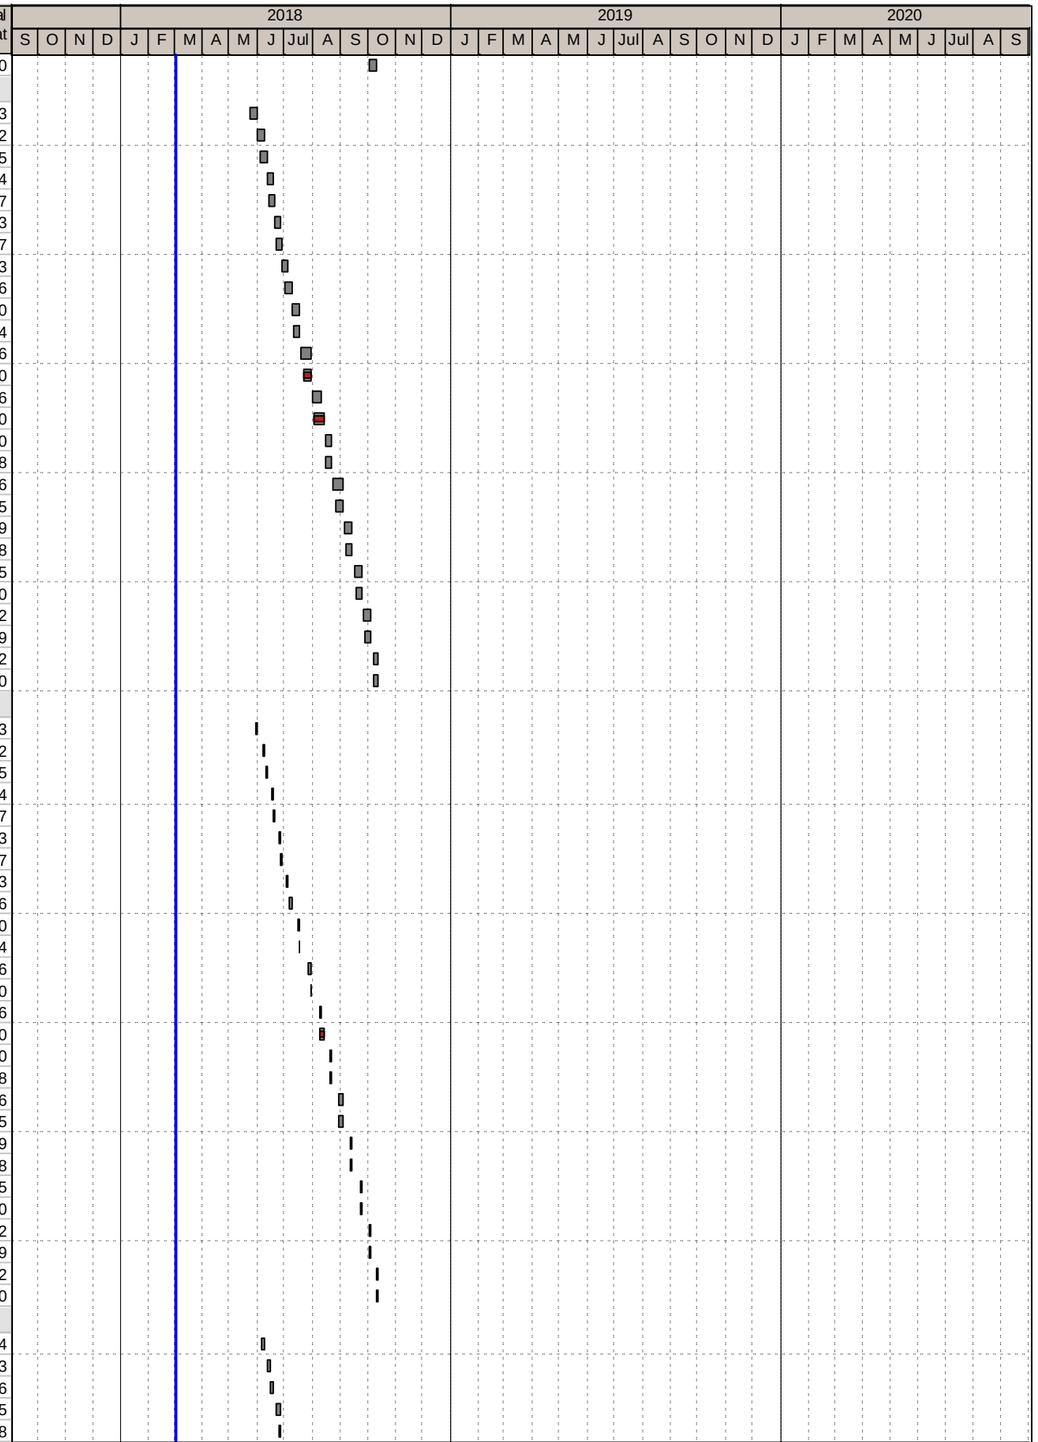

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S3F3-8P2GM	Edge Form / Bulkheads - Main Concourse F3	3	02-Jul-18	05-Jul-18	14
S3A4-8P2GM	Edge Form / Bulkheads - Main Concourse A4	3	03-Jul-18	06-Jul-18	8
S3E1-8P2GM	Edge Form / Bulkheads - Main Concourse E1	3	10-Jul-18	12-Jul-18	14
S3B1-8P2GM	Edge Form / Bulkheads - Main Concourse B1	3	12-Jul-18	16-Jul-18	7
S3E2-8P2GM	Edge Form / Bulkheads - Main Concourse E2	3	20-Jul-18	24-Jul-18	11
S3B2-8P2GM	Edge Form / Bulkheads - Main Concourse B2	3	23-Jul-18	25-Jul-18	5
S3E3-8P2GM	Edge Form / Bulkheads - Main Concourse E3	3	03-Aug-18	07-Aug-18	7
S3B3-8P2GM	Edge Form / Bulkheads - Main Concourse B3	3	06-Aug-18	08-Aug-18	1
S3E4-8P2GM	Edge Form / Bulkheads - Main Concourse E4	3	16-Aug-18	20-Aug-18	7
S3B4-8P2GM	Edge Form / Bulkheads - Main Concourse B4	3	17-Aug-18	21-Aug-18	1
S3B5-8P2GM	Edge Form / Bulkheads - Main Concourse B5	3	27-Aug-18	29-Aug-18	12
S3E5-8P2GM	Edge Form / Bulkheads - Main Concourse E5	3	27-Aug-18	29-Aug-18	9
S3B6-8P2GM	Edge Form / Bulkheads - Main Concourse B6	3	07-Sep-18	11-Sep-18	7
S3E6-8P2GM	Edge Form / Bulkheads - Main Concourse E6	3	07-Sep-18	11-Sep-18	6
S3C1-8P2GM	Edge Form / Bulkheads - Main Concourse C1	3	18-Sep-18	20-Sep-18	11
S3D1-8P2GM	Edge Form / Bulkheads - Main Concourse D1	3	18-Sep-18	20-Sep-18	9
S3C2-8P2GM	Edge Form / Bulkheads - Main Concourse C2	3	28-Sep-18	02-Oct-18	6
S3D2-8P2GM	Edge Form / Bulkheads - Main Concourse D2	3	28-Sep-18	02-Oct-18	11
S3C3-8P2GM	Edge Form / Bulkheads - Main Concourse C3	3	09-Oct-18	11-Oct-18	13
S3D3-8P2GM	Edge Form / Bulkheads - Main Concourse D3	3	09-Oct-18	11-Oct-18	10
S3C4-8P2GM	Edge Form / Bulkheads - Main Concourse C4	3	17-Oct-18	19-Oct-18	13
S3D4-8P2GM	Edge Form / Bulkheads - Main Concourse D4	3	17-Oct-18	19-Oct-18	11
Reinforce					
S3A1-8P2GC	Girder Reinforcing - Main Concourse A1	4	31-May-18	05-Jun-18	3
S3F1-8P2GC	Girder Reinforcing - Main Concourse F1	3	08-Jun-18	12-Jun-18	12
S3A2-8P2GC	Girder Reinforcing - Main Concourse A2	3	12-Jun-18	14-Jun-18	5
S3F2-8P2GC	Girder Reinforcing - Main Concourse F2	3	19-Jun-18	21-Jun-18	14
S3A3-8P2GC	Girder Reinforcing - Main Concourse A3	3	20-Jun-18	22-Jun-18	7
S3F3-8P2GC	Girder Reinforcing - Main Concourse F3	3	27-Jun-18	29-Jun-18	13
S3A4-8P2GC	Girder Reinforcing - Main Concourse A4	2	29-Jun-18	02-Jul-18	7
S3E1-8P2GC	Girder Reinforcing - Main Concourse E1	3	05-Jul-18	09-Jul-18	13
S3B1-8P2GC	Girder Reinforcing - Main Concourse B1	4	06-Jul-18	11-Jul-18	6
S3E2-8P2GC	Girder Reinforcing - Main Concourse E2	4	16-Jul-18	19-Jul-18	10
S3B2-8P2GC	Girder Reinforcing - Main Concourse B2	3	18-Jul-18	20-Jul-18	4
S3E3-8P2GC	Girder Reinforcing - Main Concourse E3	3	30-Jul-18	01-Aug-18	6
S3B3-8P2GC	Girder Reinforcing - Main Concourse B3	3	31-Jul-18	02-Aug-18	0
S3E4-8P2GC	Girder Reinforcing - Main Concourse E4	3	10-Aug-18	14-Aug-18	6
S3B4-8P2GC	Girder Reinforcing - Main Concourse B4	3	13-Aug-18	15-Aug-18	0
S3B5-8P2GC	Girder Reinforcing - Main Concourse B5	3	22-Aug-18	24-Aug-18	10
S3E5-8P2GC	Girder Reinforcing - Main Concourse E5	3	22-Aug-18	24-Aug-18	8
S3B6-8P2GC	Girder Reinforcing - Main Concourse B6	3	04-Sep-18	06-Sep-18	6
S3E6-8P2GC	Girder Reinforcing - Main Concourse E6	4	31-Aug-18	06-Sep-18	5
S3C1-8P2GC	Girder Reinforcing - Main Concourse C1	4	12-Sep-18	17-Sep-18	9
S3D1-8P2GC	Girder Reinforcing - Main Concourse D1	4	12-Sep-18	17-Sep-18	8
S3C2-8P2GC	Girder Reinforcing - Main Concourse C2	4	24-Sep-18	27-Sep-18	5
S3D2-8P2GC	Girder Reinforcing - Main Concourse D2	3	25-Sep-18	27-Sep-18	10
S3C3-8P2GC	Girder Reinforcing - Main Concourse C3	3	04-Oct-18	08-Oct-18	12
S3D3-8P2GC	Girder Reinforcing - Main Concourse D3	3	04-Oct-18	08-Oct-18	9
S3C4-8P2GC	Girder Reinforcing - Main Concourse C4	3	12-Oct-18	16-Oct-18	12
S3D4-8P2GC	Girder Reinforcing - Main Concourse D4	3	12-Oct-18	16-Oct-18	10
S3A1-8P2G3	Beams/Joists Reinforcing - Main Concourse A1	4	04-Jun-18	07-Jun-18	3
S3F1-8P2G3	Beams/Joists Reinforcing - Main Concourse F1	4	11-Jun-18	14-Jun-18	12
S3A2-8P2G3	Beams/Joists Reinforcing - Main Concourse A2	4	13-Jun-18	18-Jun-18	5
S3F2-8P2G3	Beams/Joists Reinforcing - Main Concourse F2	4	20-Jun-18	25-Jun-18	14
S3A3-8P2G3	Beams/Joists Reinforcing - Main Concourse A3	4	21-Jun-18	26-Jun-18	7
S3F3-8P2G3	Beams/Joists Reinforcing - Main Concourse F3	3	29-Jun-18	03-Jul-18	13
S3A4-8P2G3	Beams/Joists Reinforcing - Main Concourse A4	3	02-Jul-18	05-Jul-18	7
S3E1-8P2G3	Beams/Joists Reinforcing - Main Concourse E1	3	09-Jul-18	11-Jul-18	13
S3B1-8P2G3	Beams/Joists Reinforcing - Main Concourse B1	3	11-Jul-18	13-Jul-18	6
S3E2-8P2G3	Beams/Joists Reinforcing - Main Concourse E2	4	18-Jul-18	23-Jul-18	10
S3B2-8P2G3	Beams/Joists Reinforcing - Main Concourse B2	4	19-Jul-18	24-Jul-18	4
S3E3-8P2G3	Beams/Joists Reinforcing - Main Concourse E3	5	31-Jul-18	06-Aug-18	6

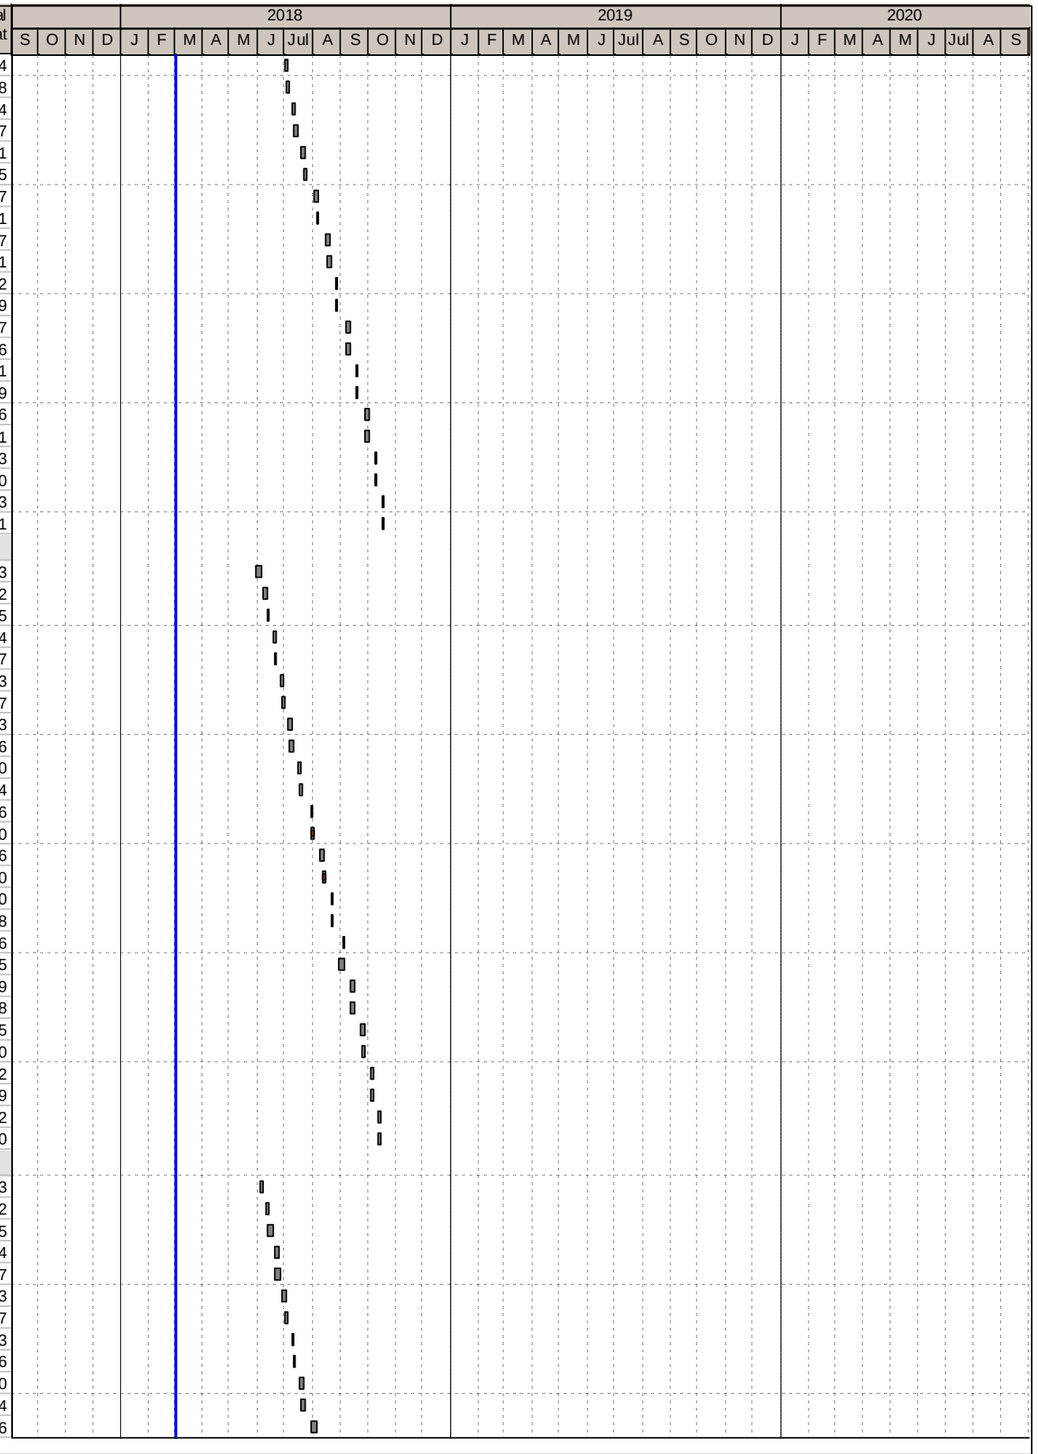

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S3B3-8P2G3	Beams/Joists Reinforcing - Main Concourse B3	5	01-Aug-18	07-Aug-18	0
S3E4-8P2G3	Beams/Joists Reinforcing - Main Concourse E4	5	13-Aug-18	17-Aug-18	6
S3B4-8P2G3	Beams/Joists Reinforcing - Main Concourse B4	5	14-Aug-18	20-Aug-18	0
S3B5-8P2G3	Beams/Joists Reinforcing - Main Concourse B5	4	23-Aug-18	28-Aug-18	10
S3E5-8P2G3	Beams/Joists Reinforcing - Main Concourse E5	4	23-Aug-18	28-Aug-18	8
S3B6-8P2G3	Beams/Joists Reinforcing - Main Concourse B6	4	05-Sep-18	10-Sep-18	6
S3E6-8P2G3	Beams/Joists Reinforcing - Main Concourse E6	4	05-Sep-18	10-Sep-18	5
S3C1-8P2G3	Beams/Joists Reinforcing - Main Concourse C1	3	17-Sep-18	19-Sep-18	9
S3D1-8P2G3	Beams/Joists Reinforcing - Main Concourse D1	4	14-Sep-18	19-Sep-18	8
S3C2-8P2G3	Beams/Joists Reinforcing - Main Concourse C2	4	26-Sep-18	01-Oct-18	5
S3D2-8P2G3	Beams/Joists Reinforcing - Main Concourse D2	4	26-Sep-18	01-Oct-18	10
S3C3-8P2G3	Beams/Joists Reinforcing - Main Concourse C3	4	05-Oct-18	10-Oct-18	12
S3D3-8P2G3	Beams/Joists Reinforcing - Main Concourse D3	4	05-Oct-18	10-Oct-18	9
S3C4-8P2G3	Beams/Joists Reinforcing - Main Concourse C4	3	16-Oct-18	18-Oct-18	12
S3D4-8P2G3	Beams/Joists Reinforcing - Main Concourse D4	3	16-Oct-18	18-Oct-18	10
Mech Embeds					
S3A1-8P2GL	Mech in P&J - Main Concourse A1	3	06-Jun-18	08-Jun-18	3
S3F1-8P2GL	Mech in P&J - Main Concourse F1	3	13-Jun-18	15-Jun-18	12
S3A2-8P2GL	Mech in P&J - Main Concourse A2	3	15-Jun-18	19-Jun-18	5
S3F2-8P2GL	Mech in P&J - Main Concourse F2	3	22-Jun-18	26-Jun-18	14
S3A3-8P2GL	Mech in P&J - Main Concourse A3	3	25-Jun-18	27-Jun-18	7
S3F3-8P2GL	Mech in P&J - Main Concourse F3	3	02-Jul-18	05-Jul-18	13
S3A4-8P2GL	Mech in P&J - Main Concourse A4	3	03-Jul-18	06-Jul-18	7
S3E1-8P2GL	Mech in P&J - Main Concourse E1	2	11-Jul-18	12-Jul-18	13
S3B1-8P2GL	Mech in P&J - Main Concourse B1	3	12-Jul-18	16-Jul-18	6
S3E2-8P2GL	Mech in P&J - Main Concourse E2	3	20-Jul-18	24-Jul-18	10
S3B2-8P2GL	Mech in P&J - Main Concourse B2	3	23-Jul-18	25-Jul-18	4
S3E3-8P2GL	Mech in P&J - Main Concourse E3	3	03-Aug-18	07-Aug-18	6
S3B3-8P2GL	Mech in P&J - Main Concourse B3	3	06-Aug-18	08-Aug-18	0
S3E4-8P2GL	Mech in P&J - Main Concourse E4	3	16-Aug-18	20-Aug-18	6
S3B4-8P2GL	Mech in P&J - Main Concourse B4	3	17-Aug-18	21-Aug-18	0
S3B5-8P2GL	Mech in P&J - Main Concourse B5	3	27-Aug-18	29-Aug-18	11
S3E5-8P2GL	Mech in P&J - Main Concourse E5	3	27-Aug-18	29-Aug-18	8
S3B6-8P2GL	Mech in P&J - Main Concourse B6	3	07-Sep-18	11-Sep-18	6
S3E6-8P2GL	Mech in P&J - Main Concourse E6	3	07-Sep-18	11-Sep-18	5
S3C1-8P2GL	Mech in P&J - Main Concourse C1	3	18-Sep-18	20-Sep-18	10
S3D1-8P2GL	Mech in P&J - Main Concourse D1	3	18-Sep-18	20-Sep-18	8
S3C2-8P2GL	Mech in P&J - Main Concourse C2	3	28-Sep-18	02-Oct-18	5
S3D2-8P2GL	Mech in P&J - Main Concourse D2	2	01-Oct-18	02-Oct-18	10
S3C3-8P2GL	Mech in P&J - Main Concourse C3	2	10-Oct-18	11-Oct-18	12
S3D3-8P2GL	Mech in P&J - Main Concourse D3	2	10-Oct-18	11-Oct-18	9
S3C4-8P2GL	Mech in P&J - Main Concourse C4	2	18-Oct-18	19-Oct-18	12
S3D4-8P2GL	Mech in P&J - Main Concourse D4	2	18-Oct-18	19-Oct-18	10
Elec Embeds					
S3A1-8P2GE	Elec in P&J - Main Concourse A1	3	06-Jun-18	08-Jun-18	3
S3F1-8P2GE	Elec in P&J - Main Concourse F1	3	13-Jun-18	15-Jun-18	12
S3A2-8P2GE	Elec in P&J - Main Concourse A2	3	15-Jun-18	19-Jun-18	5
S3F2-8P2GE	Elec in P&J - Main Concourse F2	3	22-Jun-18	26-Jun-18	14
S3A3-8P2GE	Elec in P&J - Main Concourse A3	3	25-Jun-18	27-Jun-18	7
S3F3-8P2GE	Elec in P&J - Main Concourse F3	3	02-Jul-18	05-Jul-18	13
S3A4-8P2GE	Elec in P&J - Main Concourse A4	3	03-Jul-18	06-Jul-18	7
S3E1-8P2GE	Elec in P&J - Main Concourse E1	2	11-Jul-18	12-Jul-18	13
S3B1-8P2GE	Elec in P&J - Main Concourse B1	3	12-Jul-18	16-Jul-18	6
S3E2-8P2GE	Elec in P&J - Main Concourse E2	3	20-Jul-18	24-Jul-18	10
S3B2-8P2GE	Elec in P&J - Main Concourse B2	3	23-Jul-18	25-Jul-18	4
S3E3-8P2GE	Elec in P&J - Main Concourse E3	3	03-Aug-18	07-Aug-18	6
S3B3-8P2GE	Elec in P&J - Main Concourse B3	3	06-Aug-18	08-Aug-18	0
S3E4-8P2GE	Elec in P&J - Main Concourse E4	3	16-Aug-18	20-Aug-18	6
S3B4-8P2GE	Elec in P&J - Main Concourse B4	3	17-Aug-18	21-Aug-18	0
S3B5-8P2GE	Elec in P&J - Main Concourse B5	3	27-Aug-18	29-Aug-18	11
S3E5-8P2GE	Elec in P&J - Main Concourse E5	3	27-Aug-18	29-Aug-18	8
S3B6-8P2GE	Elec in P&J - Main Concourse B6	3	07-Sep-18	11-Sep-18	6
S3E6-8P2GE	Elec in P&J - Main Concourse E6	3	07-Sep-18	11-Sep-18	5

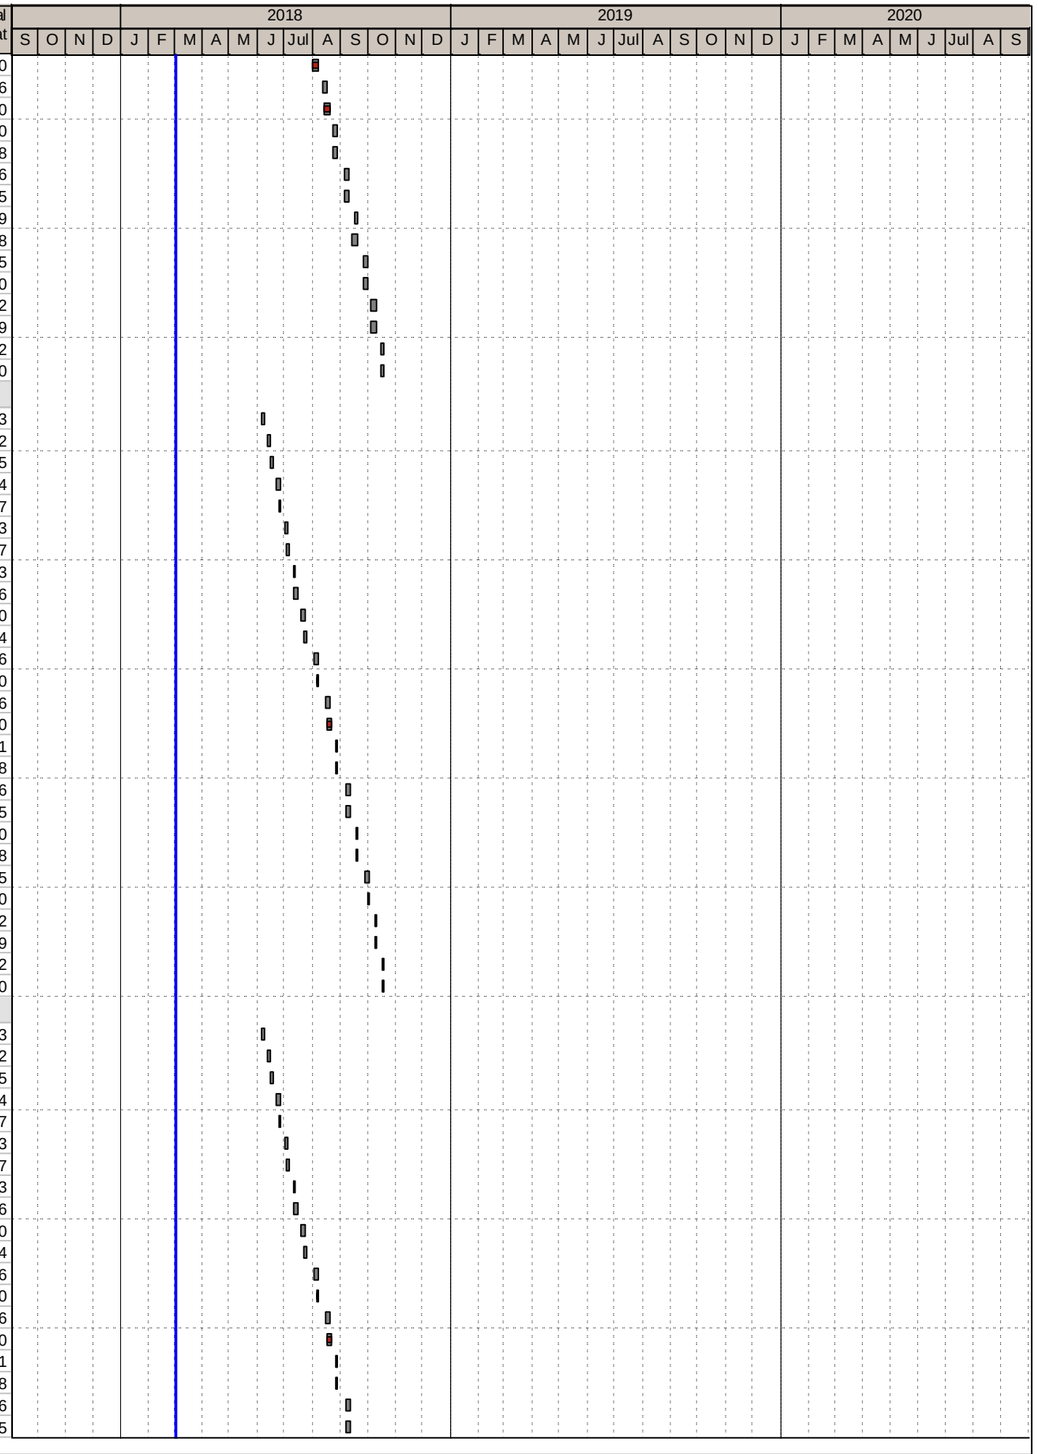

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S3C1-8P2GE	Elec in P&J - Main Concourse C1	3	18-Sep-18	20-Sep-18	10
S3D1-8P2GE	Elec in P&J - Main Concourse D1	3	18-Sep-18	20-Sep-18	8
S3C2-8P2GE	Elec in P&J - Main Concourse C2	3	28-Sep-18	02-Oct-18	5
S3D2-8P2GE	Elec in P&J - Main Concourse D2	2	01-Oct-18	02-Oct-18	10
S3C3-8P2GE	Elec in P&J - Main Concourse C3	2	10-Oct-18	11-Oct-18	12
S3D3-8P2GE	Elec in P&J - Main Concourse D3	2	10-Oct-18	11-Oct-18	9
S3C4-8P2GE	Elec in P&J - Main Concourse C4	2	18-Oct-18	19-Oct-18	12
S3D4-8P2GE	Elec in P&J - Main Concourse D4	2	18-Oct-18	19-Oct-18	10
S3A1-8P2G4	Slab Reinforcing - Main Concourse A1	2	08-Jun-18	11-Jun-18	3
S3F1-8P2G4	Slab Reinforcing - Main Concourse F1	2	15-Jun-18	18-Jun-18	12
S3A2-8P2G4	Slab Reinforcing - Main Concourse A2	2	19-Jun-18	20-Jun-18	5
S3F2-8P2G4	Slab Reinforcing - Main Concourse F2	2	26-Jun-18	27-Jun-18	14
S3A3-8P2G4	Slab Reinforcing - Main Concourse A3	2	27-Jun-18	28-Jun-18	7
S3F3-8P2G4	Slab Reinforcing - Main Concourse F3	2	05-Jul-18	06-Jul-18	13
S3A4-8P2G4	Slab Reinforcing - Main Concourse A4	2	06-Jul-18	09-Jul-18	7
S3E1-8P2G4	Slab Reinforcing - Main Concourse E1	2	12-Jul-18	13-Jul-18	13
S3B1-8P2G4	Slab Reinforcing - Main Concourse B1	2	16-Jul-18	17-Jul-18	6
S3E2-8P2G4	Slab Reinforcing - Main Concourse E2	2	24-Jul-18	25-Jul-18	10
S3B2-8P2G4	Slab Reinforcing - Main Concourse B2	2	25-Jul-18	26-Jul-18	4
S3E3-8P2G4	Slab Reinforcing - Main Concourse E3	2	07-Aug-18	08-Aug-18	6
S3B3-8P2G4	Slab Reinforcing - Main Concourse B3	2	08-Aug-18	09-Aug-18	0
S3E4-8P2G4	Slab Reinforcing - Main Concourse E4	2	20-Aug-18	21-Aug-18	6
S3B4-8P2G4	Slab Reinforcing - Main Concourse B4	2	21-Aug-18	22-Aug-18	0
S3B5-8P2G4	Slab Reinforcing - Main Concourse B5	2	29-Aug-18	30-Aug-18	12
S3E5-8P2G4	Slab Reinforcing - Main Concourse E5	2	29-Aug-18	30-Aug-18	8
S3B6-8P2G4	Slab Reinforcing - Main Concourse B6	2	11-Sep-18	12-Sep-18	6
S3E6-8P2G4	Slab Reinforcing - Main Concourse E6	2	11-Sep-18	12-Sep-18	5
S3C1-8P2G4	Slab Reinforcing - Main Concourse C1	2	20-Sep-18	21-Sep-18	12
S3D1-8P2G4	Slab Reinforcing - Main Concourse D1	2	20-Sep-18	21-Sep-18	8
S3C2-8P2G4	Slab Reinforcing - Main Concourse C2	2	02-Oct-18	03-Oct-18	5
S3D2-8P2G4	Slab Reinforcing - Main Concourse D2	2	02-Oct-18	03-Oct-18	10
S3C3-8P2G4	Slab Reinforcing - Main Concourse C3	2	11-Oct-18	12-Oct-18	12
S3D3-8P2G4	Slab Reinforcing - Main Concourse D3	2	11-Oct-18	12-Oct-18	9
S3C4-8P2G4	Slab Reinforcing - Main Concourse C4	2	19-Oct-18	22-Oct-18	12
S3D4-8P2G4	Slab Reinforcing - Main Concourse D4	2	19-Oct-18	22-Oct-18	10
S3A1-8P2G5	Clean P&J Deck - Main Concourse A1	1	12-Jun-18	12-Jun-18	3
S3F1-8P2G5	Clean P&J Deck - Main Concourse F1	1	19-Jun-18	19-Jun-18	12
S3A2-8P2G5	Clean P&J Deck - Main Concourse A2	1	21-Jun-18	21-Jun-18	5
S3F2-8P2G5	Clean P&J Deck - Main Concourse F2	1	28-Jun-18	28-Jun-18	14
S3A3-8P2G5	Clean P&J Deck - Main Concourse A3	1	29-Jun-18	29-Jun-18	7
S3F3-8P2G5	Clean P&J Deck - Main Concourse F3	1	09-Jul-18	09-Jul-18	13
S3A4-8P2G5	Clean P&J Deck - Main Concourse A4	1	10-Jul-18	10-Jul-18	7
S3E1-8P2G5	Clean P&J Deck - Main Concourse E1	1	16-Jul-18	16-Jul-18	13
S3B1-8P2G5	Clean P&J Deck - Main Concourse B1	1	18-Jul-18	18-Jul-18	6
S3E2-8P2G5	Clean P&J Deck - Main Concourse E2	1	26-Jul-18	26-Jul-18	10
S3B2-8P2G5	Clean P&J Deck - Main Concourse B2	1	27-Jul-18	27-Jul-18	4
S3E3-8P2G5	Clean P&J Deck - Main Concourse E3	1	09-Aug-18	09-Aug-18	6
S3B3-8P2G5	Clean P&J Deck - Main Concourse B3	1	10-Aug-18	10-Aug-18	0
S3E4-8P2G5	Clean P&J Deck - Main Concourse E4	1	22-Aug-18	22-Aug-18	6
S3B4-8P2G5	Clean P&J Deck - Main Concourse B4	1	23-Aug-18	23-Aug-18	0
S3B5-8P2G5	Clean P&J Deck - Main Concourse B5	1	31-Aug-18	31-Aug-18	12
S3E5-8P2G5	Clean P&J Deck - Main Concourse E5	1	31-Aug-18	31-Aug-18	8
S3B6-8P2G5	Clean P&J Deck - Main Concourse B6	1	13-Sep-18	13-Sep-18	6
S3E6-8P2G5	Clean P&J Deck - Main Concourse E6	1	13-Sep-18	13-Sep-18	5
S3C1-8P2G5	Clean P&J Deck - Main Concourse C1	1	24-Sep-18	24-Sep-18	12
S3D1-8P2G5	Clean P&J Deck - Main Concourse D1	1	24-Sep-18	24-Sep-18	8
S3C2-8P2G5	Clean P&J Deck - Main Concourse C2	1	04-Oct-18	04-Oct-18	5
S3D2-8P2G5	Clean P&J Deck - Main Concourse D2	1	04-Oct-18	04-Oct-18	10
S3C3-8P2G5	Clean P&J Deck - Main Concourse C3	1	15-Oct-18	15-Oct-18	12
S3D3-8P2G5	Clean P&J Deck - Main Concourse D3	1	15-Oct-18	15-Oct-18	9
S3C4-8P2G5	Clean P&J Deck - Main Concourse C4	1	23-Oct-18	23-Oct-18	12

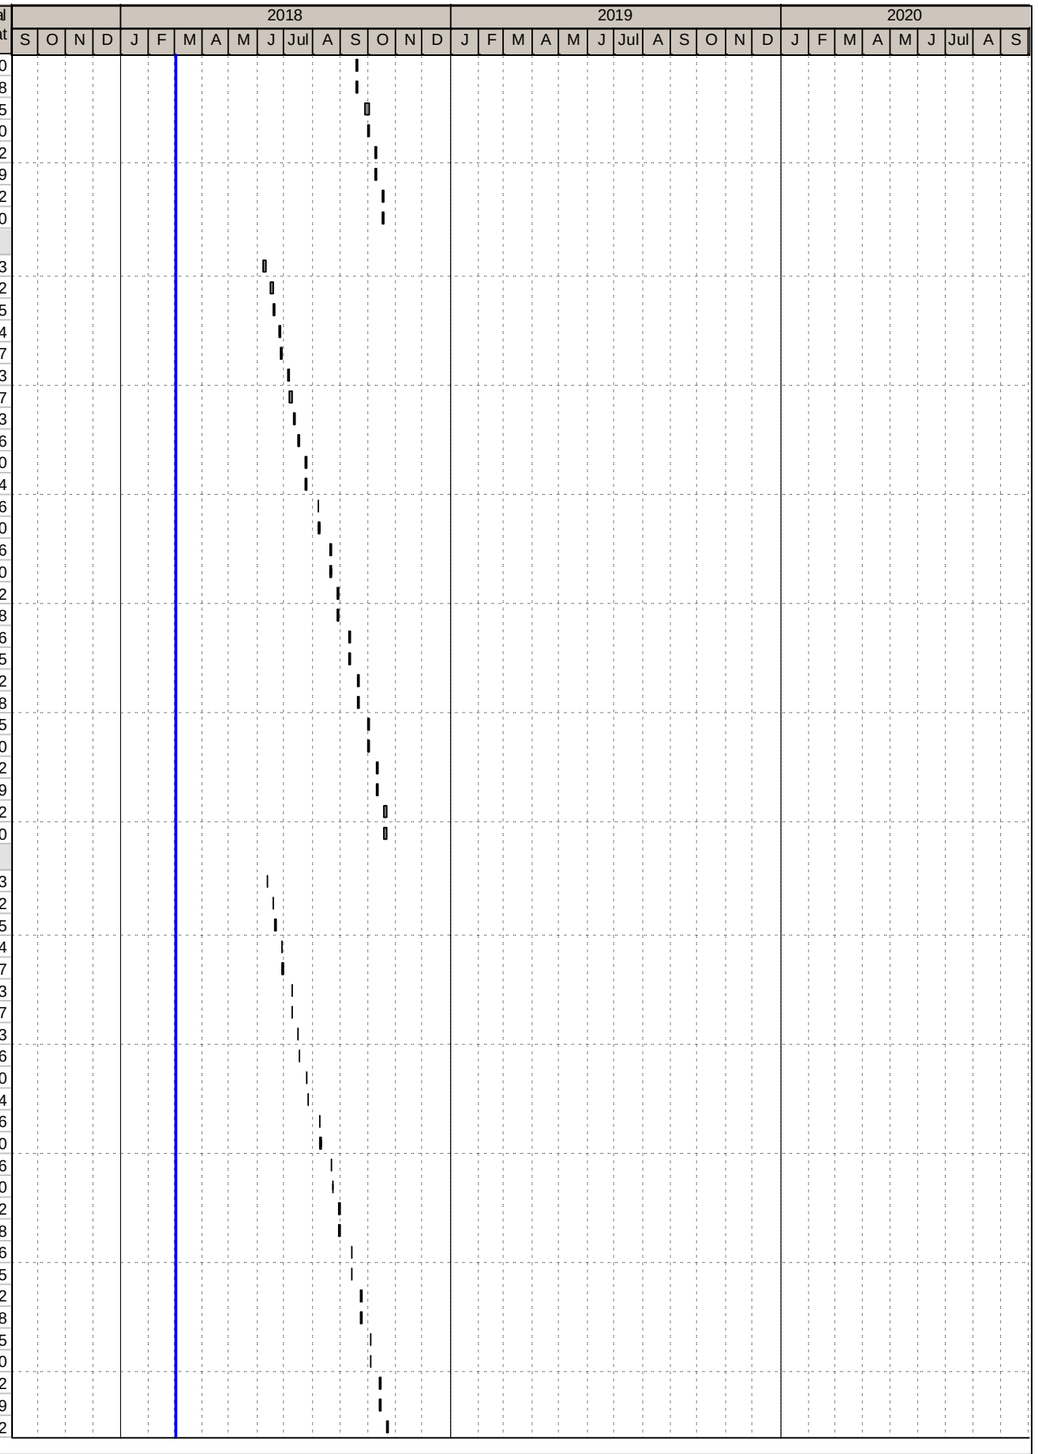

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S3D4-8P2G5	Clean P&J Deck - Main Concourse D4	1	23-Oct-18	23-Oct-18	10
S3A1-8P2GH	Pour P&J Deck - Main Concourse A1	1	13-Jun-18	13-Jun-18	3
S3F1-8P2GH	Pour P&J Deck - Main Concourse F1	1	20-Jun-18	20-Jun-18	12
S3A2-8P2GH	Pour P&J Deck - Main Concourse A2	1	22-Jun-18	22-Jun-18	5
S3F2-8P2GH	Pour P&J Deck - Main Concourse F2	1	29-Jun-18	29-Jun-18	14
S3A3-8P2GH	Pour P&J Deck - Main Concourse A3	1	02-Jul-18	02-Jul-18	7
S3F3-8P2GH	Pour P&J Deck - Main Concourse F3	1	10-Jul-18	10-Jul-18	13
S3A4-8P2GH	Pour P&J Deck - Main Concourse A4	1	11-Jul-18	11-Jul-18	7
S3E1-8P2GH	Pour P&J Deck - Main Concourse E1	1	17-Jul-18	17-Jul-18	13
S3B1-8P2GH	Pour P&J Deck - Main Concourse B1	1	19-Jul-18	19-Jul-18	6
S3E2-8P2GH	Pour P&J Deck - Main Concourse E2	1	27-Jul-18	27-Jul-18	10
S3B2-8P2GH	Pour P&J Deck - Main Concourse B2	1	30-Jul-18	30-Jul-18	4
S3E3-8P2GH	Pour P&J Deck - Main Concourse E3	1	10-Aug-18	10-Aug-18	6
S3B3-8P2GH	Pour P&J Deck - Main Concourse B3	1	13-Aug-18	13-Aug-18	0
S3E4-8P2GH	Pour P&J Deck - Main Concourse E4	1	23-Aug-18	23-Aug-18	6
S3B4-8P2GH	Pour P&J Deck - Main Concourse B4	1	24-Aug-18	24-Aug-18	0
S3B5-8P2GH	Pour P&J Deck - Main Concourse B5	1	04-Sep-18	04-Sep-18	12
S3E5-8P2GH	Pour P&J Deck - Main Concourse E5	1	04-Sep-18	04-Sep-18	8
S3B6-8P2GH	Pour P&J Deck - Main Concourse B6	1	14-Sep-18	14-Sep-18	6
S3E6-8P2GH	Pour P&J Deck - Main Concourse E6	1	14-Sep-18	14-Sep-18	5
S3C1-8P2GH	Pour P&J Deck - Main Concourse C1	1	25-Sep-18	25-Sep-18	12
S3D1-8P2GH	Pour P&J Deck - Main Concourse D1	1	25-Sep-18	25-Sep-18	8
S3C2-8P2GH	Pour P&J Deck - Main Concourse C2	1	05-Oct-18	05-Oct-18	5
S3D2-8P2GH	Pour P&J Deck - Main Concourse D2	1	05-Oct-18	05-Oct-18	10
S3C3-8P2GH	Pour P&J Deck - Main Concourse C3	1	16-Oct-18	16-Oct-18	12
S3D3-8P2GH	Pour P&J Deck - Main Concourse D3	1	16-Oct-18	16-Oct-18	9
S3C4-8P2GH	Pour P&J Deck - Main Concourse C4	1	24-Oct-18	24-Oct-18	12
S3D4-8P2GH	Pour P&J Deck - Main Concourse D4	1	24-Oct-18	24-Oct-18	10
S3A1-8P2GU	Cure P&J Deck - Main Concourse A1	3	14-Jun-18	16-Jun-18	5
S3F1-8P2GU	Cure P&J Deck - Main Concourse F1	3	21-Jun-18	23-Jun-18	19
S3A2-8P2GU	Cure P&J Deck - Main Concourse A2	3	23-Jun-18	25-Jun-18	9
S3F2-8P2GU	Cure P&J Deck - Main Concourse F2	3	30-Jun-18	02-Jul-18	21
S3A3-8P2GU	Cure P&J Deck - Main Concourse A3	3	03-Jul-18	05-Jul-18	10
S3F3-8P2GU	Cure P&J Deck - Main Concourse F3	3	11-Jul-18	13-Jul-18	18
S3A4-8P2GU	Cure P&J Deck - Main Concourse A4	3	12-Jul-18	14-Jul-18	9
S3E1-8P2GU	Cure P&J Deck - Main Concourse E1	3	18-Jul-18	20-Jul-18	18
S3B1-8P2GU	Cure P&J Deck - Main Concourse B1	3	20-Jul-18	22-Jul-18	8
S3E2-8P2GU	Cure P&J Deck - Main Concourse E2	3	28-Jul-18	30-Jul-18	15
S3B2-8P2GU	Cure P&J Deck - Main Concourse B2	3	31-Jul-18	02-Aug-18	5
S3E3-8P2GU	Cure P&J Deck - Main Concourse E3	3	11-Aug-18	13-Aug-18	10
S3B3-8P2GU	Cure P&J Deck - Main Concourse B3	3	14-Aug-18	16-Aug-18	0
S3E4-8P2GU	Cure P&J Deck - Main Concourse E4	3	24-Aug-18	26-Aug-18	10
S3B4-8P2GU	Cure P&J Deck - Main Concourse B4	3	25-Aug-18	27-Aug-18	2
S3B5-8P2GU	Cure P&J Deck - Main Concourse B5	3	05-Sep-18	07-Sep-18	16
S3E5-8P2GU	Cure P&J Deck - Main Concourse E5	3	05-Sep-18	07-Sep-18	10
S3B6-8P2GU	Cure P&J Deck - Main Concourse B6	3	15-Sep-18	17-Sep-18	15
S3E6-8P2GU	Cure P&J Deck - Main Concourse E6	3	15-Sep-18	17-Sep-18	9
S3C1-8P2GU	Cure P&J Deck - Main Concourse C1	3	26-Sep-18	28-Sep-18	16
S3D1-8P2GU	Cure P&J Deck - Main Concourse D1	3	26-Sep-18	28-Sep-18	10
S3C2-8P2GU	Cure P&J Deck - Main Concourse C2	3	06-Oct-18	08-Oct-18	15
S3D2-8P2GU	Cure P&J Deck - Main Concourse D2	3	06-Oct-18	08-Oct-18	15
S3C3-8P2GU	Cure P&J Deck - Main Concourse C3	3	17-Oct-18	19-Oct-18	16
S3D3-8P2GU	Cure P&J Deck - Main Concourse D3	3	17-Oct-18	19-Oct-18	13
S3C4-8P2GU	Cure P&J Deck - Main Concourse C4	3	25-Oct-18	27-Oct-18	17
S3D4-8P2GU	Cure P&J Deck - Main Concourse D4	3	25-Oct-18	27-Oct-18	16
S3A1-8P2GJ	Strip P&J Deck - Main Concourse A1	8	18-Jun-18	27-Jun-18	4
S3F1-8P2GJ	Strip P&J Deck - Main Concourse F1	7	25-Jun-18	03-Jul-18	13
S3A2-8P2GJ	Strip P&J Deck - Main Concourse A2	7	28-Jun-18	09-Jul-18	4
S3F2-8P2GJ	Strip P&J Deck - Main Concourse F2	6	05-Jul-18	12-Jul-18	13
S3A3-8P2GJ	Strip P&J Deck - Main Concourse A3	6	10-Jul-18	17-Jul-18	4

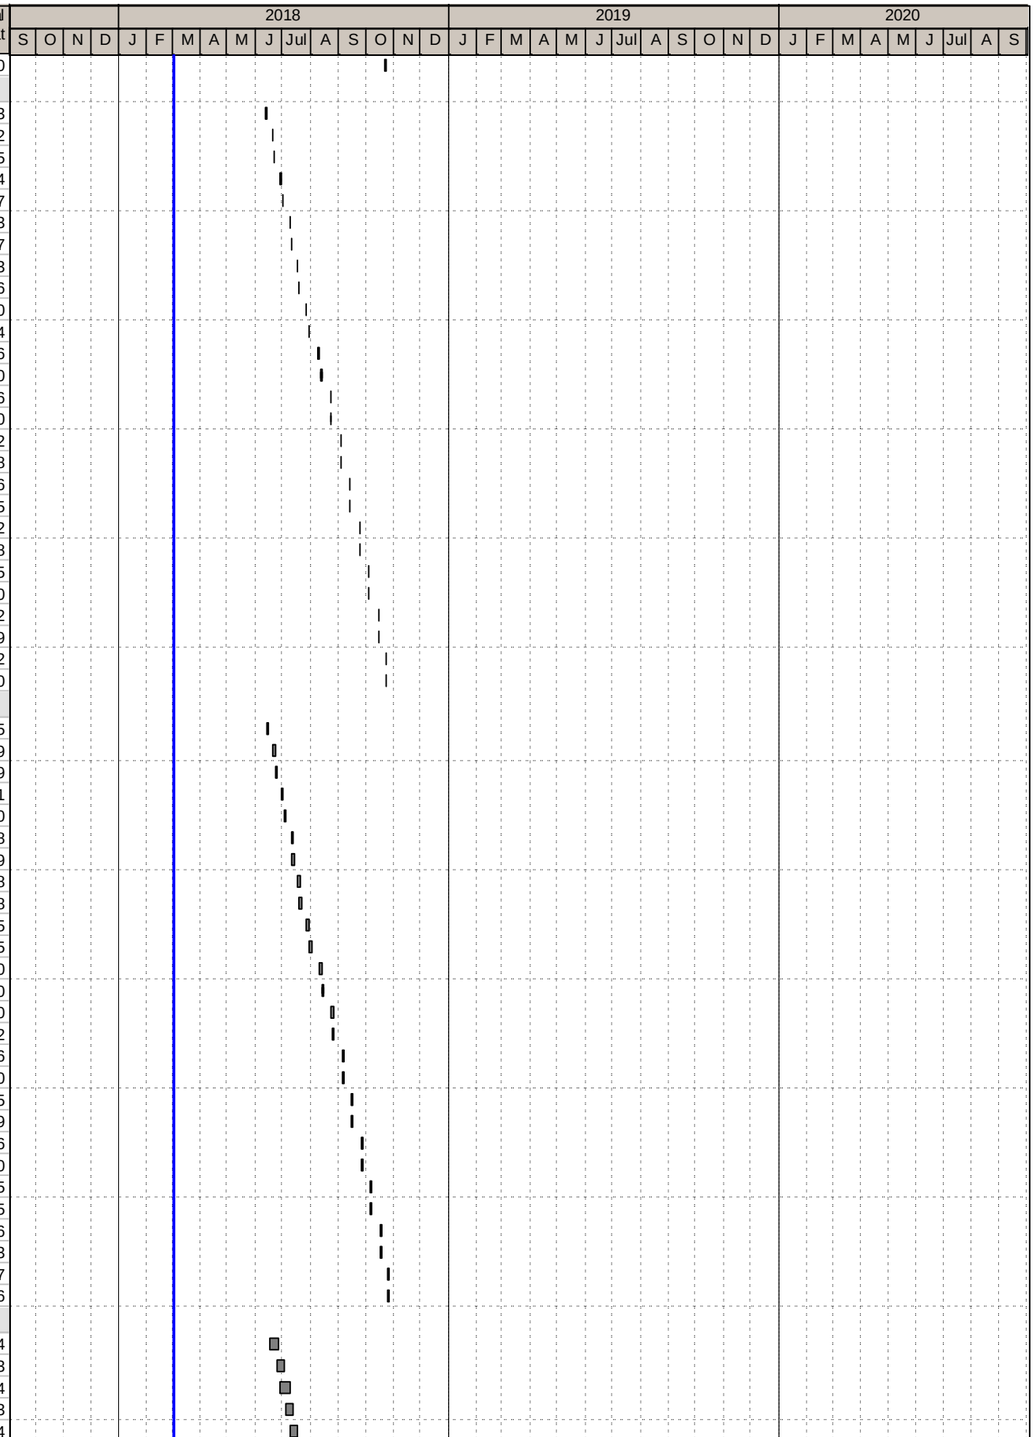

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S3F3-8P2GJ	Strip P&J Deck - Main Concourse F3	5	16-Jul-18	20-Jul-18	12
S3A4-8P2GJ	Strip P&J Deck - Main Concourse A4	5	18-Jul-18	24-Jul-18	4
S3E1-8P2GJ	Strip P&J Deck - Main Concourse E1	5	23-Jul-18	27-Jul-18	12
S3B1-8P2GJ	Strip P&J Deck - Main Concourse B1	6	25-Jul-18	01-Aug-18	4
S3E2-8P2GJ	Strip P&J Deck - Main Concourse E2	7	31-Jul-18	08-Aug-18	11
S3B2-8P2GJ	Strip P&J Deck - Main Concourse B2	7	03-Aug-18	13-Aug-18	3
S3E3-8P2GJ	Strip P&J Deck - Main Concourse E3	8	14-Aug-18	23-Aug-18	8
S3B3-8P2GJ	Strip P&J Deck - Main Concourse B3	9	17-Aug-18	29-Aug-18	0
S3E4-8P2GJ	Strip P&J Deck - Main Concourse E4	8	27-Aug-18	06-Sep-18	7
S3B4-8P2GJ	Strip P&J Deck - Main Concourse B4	8	30-Aug-18	11-Sep-18	0
S3E5-8P2GJ	Strip P&J Deck - Main Concourse E5	7	10-Sep-18	18-Sep-18	6
S3B5-8P2GJ	Strip P&J Deck - Main Concourse B5	7	12-Sep-18	20-Sep-18	8
S3E6-8P2GJ	Strip P&J Deck - Main Concourse E6	8	19-Sep-18	28-Sep-18	6
S3B6-8P2GJ	Strip P&J Deck - Main Concourse B6	8	21-Sep-18	02-Oct-18	8
S3D1-8P2GJ	Strip P&J Deck - Main Concourse D1	6	01-Oct-18	08-Oct-18	6
S3C1-8P2GJ	Strip P&J Deck - Main Concourse C1	6	03-Oct-18	10-Oct-18	8
S3D2-8P2GJ	Strip P&J Deck - Main Concourse D2	7	09-Oct-18	17-Oct-18	11
S3C2-8P2GJ	Strip P&J Deck - Main Concourse C2	8	11-Oct-18	22-Oct-18	9
S3D3-8P2GJ	Strip P&J Deck - Main Concourse D3	6	22-Oct-18	29-Oct-18	9
S3C3-8P2GJ	Strip P&J Deck - Main Concourse C3	6	23-Oct-18	30-Oct-18	9
S3D4-8P2GJ	Strip P&J Deck - Main Concourse D4	5	30-Oct-18	05-Nov-18	9
S3C4-8P2GJ	Strip P&J Deck - Main Concourse C4	5	31-Oct-18	06-Nov-18	9
Steel Structure					
100 Main Concourse					
S5A-8P2G385	Steel Structure - Survey/Clips (Main Concourse C)	16	17-Oct-18	07-Nov-18	23
S5A-8P2G395	Steel Structure - Survey/Clips (Main Concourse D)	16	23-Oct-18	14-Nov-18	10
200/250 Lower Suite & Upper Suite Lvl					
S5A42-8P2G1	Steel Structure (Erect) - Area A Lower & Upper Suite Lvl (Seq 1108)	5	27-Sep-18	03-Oct-18	1
S5F70-8P2G1	Steel Structure (Erect) - Area F Lower & Upper Suite Lvl (Seq 1107)	5	27-Sep-18	03-Oct-18	6
S5B44-8P2G1	Steel Structure (Erect) - Area B Lower & Upper Suite Lvl (Seq 1111)	6	02-Oct-18	09-Oct-18	0
S5A109-8P2G1	Steel Structure (Erect) - Area A Lower & Upper Suite Lvl (Seq 1109)	5	04-Oct-18	10-Oct-18	1
S5F106-8P2G1	Steel Structure (Erect) - Area F Lower & Upper Suite Lvl (Seq 1106)	5	04-Oct-18	10-Oct-18	6
S5B112-8P2G1	Steel Structure (Erect) - Area B Lower & Upper Suite Lvl (Seq 1112)	4	10-Oct-18	15-Oct-18	0
S5A110-8P2G1	Steel Structure (Erect) - Area A Lower & Upper Suite Lvl (Seq 1110)	4	11-Oct-18	16-Oct-18	1
S5F105-8P2G1	Steel Structure (Erect) - Area F Lower & Upper Suite Lvl (Seq 1105)	5	11-Oct-18	17-Oct-18	6
S5E103-8P2G1	Steel Structure (Erect) - Area E Lower & Upper Suite Lvl (Seq 1103)	5	17-Oct-18	23-Oct-18	1
S5E67-8P2G1	Steel Structure (Erect) - Area E Lower & Upper Suite Lvl (Seq 1104)	5	18-Oct-18	24-Oct-18	6
S5E102-8P2G1	Steel Structure (Erect) - Area E Lower & Upper Suite Lvl (Seq 1102)	3	24-Oct-18	26-Oct-18	1
S5E64-8P2G1	Steel Structure (Erect) - Area E Lower & Upper Suite Lvl (Seq 1101)	4	29-Oct-18	01-Nov-18	1
S5B47-8P2G1	Steel Structure (Erect) - Area B Lower & Upper Suite Lvl (Seq 1113)	3	02-Nov-18	06-Nov-18	1
S5B114-8P2G1	Steel Structure (Erect) - Area B Lower & Upper Suite Lvl (Seq 1114)	4	07-Nov-18	13-Nov-18	1
S5B50-8P2G1	Steel Structure (Erect) - Area B Lower & Upper Suite Lvl (Seq 1115)	3	14-Nov-18	16-Nov-18	1
S5B116-8P2G1	Steel Structure (Erect) - Area B Lower & Upper Suite Lvl (Seq 1116)	5	28-Nov-18	04-Dec-18	2
S5E125-8P2G1	Steel Structure (Erect) - Area E Lower & Upper Suite Lvl (Seq 1125)	4	29-Nov-18	04-Dec-18	0
S5E61-8P2G1	Steel Structure (Erect) - Area E Lower & Upper Suite Lvl (Seq 1124)	3	05-Dec-18	07-Dec-18	0
S5C53-8P2G1	Steel Structure (Erect) - Area C Lower & Upper Suite Lvl (Seq 1117)	6	06-Dec-18	13-Dec-18	1
S5E123-8P2G1	Steel Structure (Erect) - Area E Lower & Upper Suite Lvl (Seq 1123)	6	10-Dec-18	17-Dec-18	4
S5C118-8P2G1	Steel Structure (Erect) - Area C Lower & Upper Suite Lvl (Seq 1118)	5	14-Dec-18	20-Dec-18	1
S5D59-8P2G1	Steel Structure (Erect) - Area D Lower & Upper Suite Lvl (Seq 1122)	5	02-Jan-19	08-Jan-19	10
S5D57-8P2G1	Steel Structure (Erect) - Area D Lower & Upper Suite Lvl (Seq 1121)	4	10-Jan-19	15-Jan-19	9
S5C126-8P2G1	Steel Structure (Erect) - Area C Lower & Upper Suite Lvl (Seq 1126)	4	10-Jan-19	15-Jan-19	9
S5C120-8P2G1	Steel Structure (Erect) - Area C Lower & Upper Suite Lvl (Seq 1120)	3	16-Jan-19	18-Jan-19	9
S5C55-8P2G1	Steel Structure (Erect) - Area C Lower & Upper Suite Lvl (Seq 1119)	4	21-Jan-19	24-Jan-19	9
S5C127-8P2G1	Steel Structure (Erect) - Area C Lower & Upper Suite Lvl (Seq 127A / 128A)	2	31-Jan-19	01-Feb-19	25
S5C128-8P2G1	Steel Structure (Erect) - Area C Lower & Upper Suite Lvl (Seq 127B / 128B)	2	21-Feb-19	22-Feb-19	9
S5A42-8P2G2	Steel Structure (Detail) - Area A Lower & Upper Suite Lvl (Seq 1108)	10	01-Oct-18	12-Oct-18	21
S5F70-8P2G2	Steel Structure (Detail) - Area F Lower & Upper Suite Lvl (Seq 1107)	10	01-Oct-18	12-Oct-18	25
S5B44-8P2G2	Steel Structure (Detail) - Area B Lower & Upper Suite Lvl (Seq 1111)	10	04-Oct-18	17-Oct-18	19
S5A109-8P2G2	Steel Structure (Detail) - Area A Lower & Upper Suite Lvl (Seq 1109)	10	08-Oct-18	19-Oct-18	22

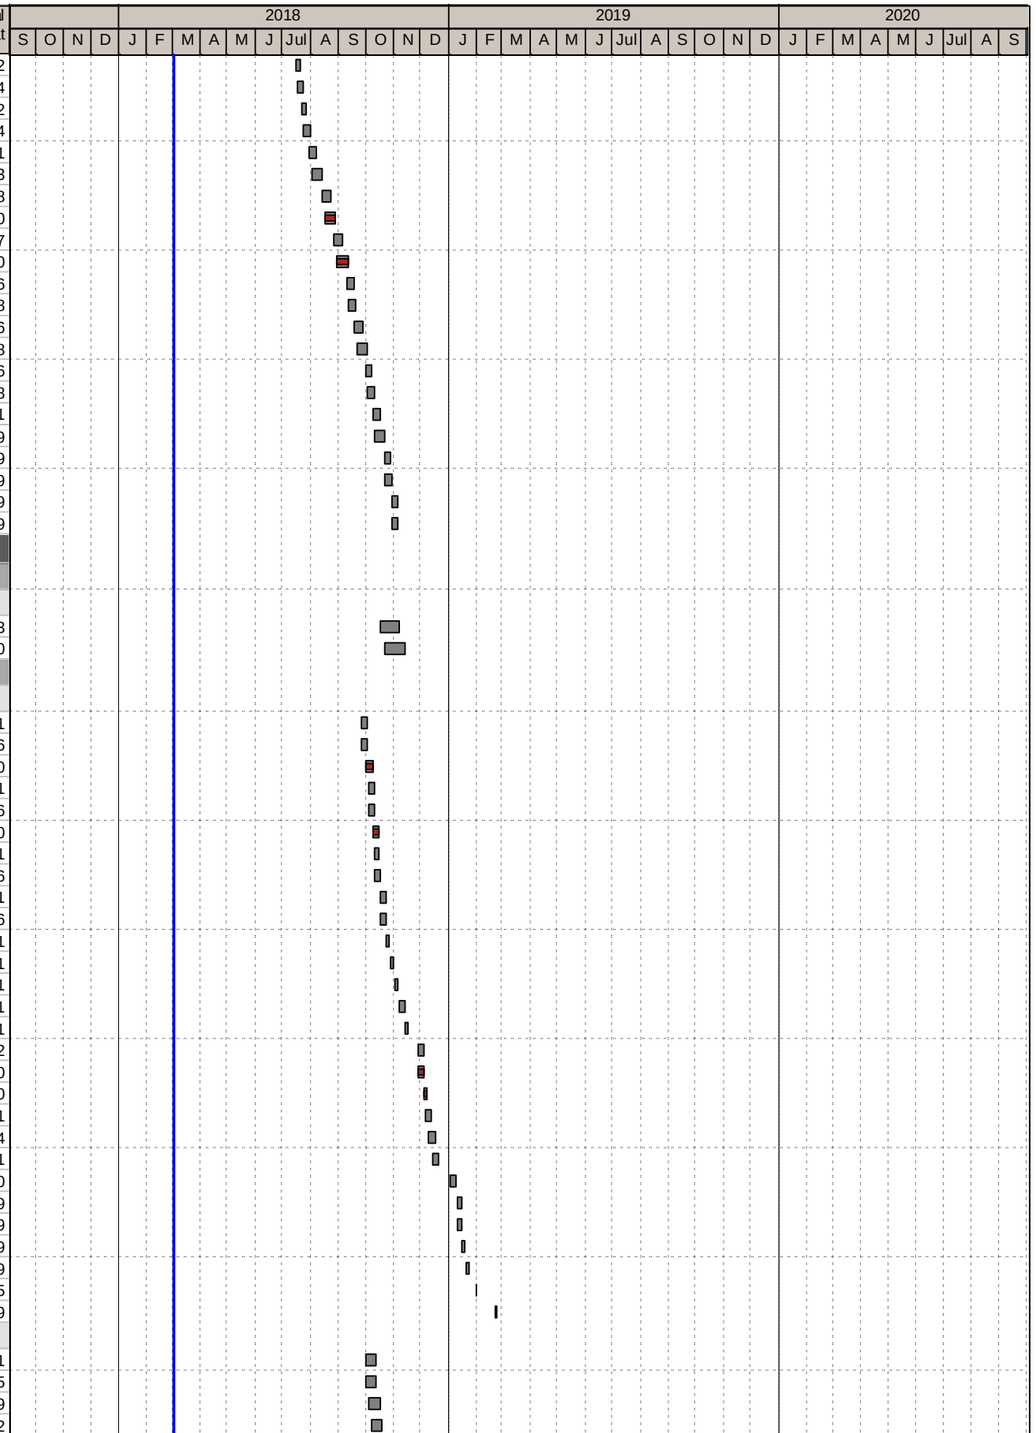

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S5F106-8P2G2	Steel Structure (Detail) - Area F Lower & Upper Suite Lvl (Seq 1106)	10	08-Oct-18	19-Oct-18	22
S5B112-8P2G2	Steel Structure (Detail) - Area B Lower & Upper Suite Lvl (Seq 1112)	8	12-Oct-18	23-Oct-18	40
S5A110-8P2G2	Steel Structure (Detail) - Area A Lower & Upper Suite Lvl (Seq 1110)	8	15-Oct-18	24-Oct-18	20
S5F105-8P2G2	Steel Structure (Detail) - Area F Lower & Upper Suite Lvl (Seq 1105)	8	15-Oct-18	24-Oct-18	20
S5E103-8P2G2	Steel Structure (Detail) - Area E Lower & Upper Suite Lvl (Seq 1103)	10	19-Oct-18	01-Nov-18	38
S5E67-8P2G2	Steel Structure (Detail) - Area E Lower & Upper Suite Lvl (Seq 1104)	10	22-Oct-18	02-Nov-18	20
S5E102-8P2G2	Steel Structure (Detail) - Area E Lower & Upper Suite Lvl (Seq 1102)	10	26-Oct-18	08-Nov-18	34
S5E64-8P2G2	Steel Structure (Detail) - Area E Lower & Upper Suite Lvl (Seq 1101)	10	31-Oct-18	14-Nov-18	18
S5B47-8P2G2	Steel Structure (Detail) - Area B Lower & Upper Suite Lvl (Seq 1113)	10	06-Nov-18	20-Nov-18	1
S5B114-8P2G2	Steel Structure (Detail) - Area B Lower & Upper Suite Lvl (Seq 1114)	10	09-Nov-18	27-Nov-18	30
S5B50-8P2G2	Steel Structure (Detail) - Area B Lower & Upper Suite Lvl (Seq 1115)	8	16-Nov-18	29-Nov-18	1
S5B116-8P2G2	Steel Structure (Detail) - Area B Lower & Upper Suite Lvl (Seq 1116)	10	30-Nov-18	13-Dec-18	6
S5E125-8P2G2	Steel Structure (Detail) - Area E Lower & Upper Suite Lvl (Seq 1125)	10	03-Dec-18	14-Dec-18	14
S5E61-8P2G2	Steel Structure (Detail) - Area E Lower & Upper Suite Lvl (Seq 1124)	9	07-Dec-18	19-Dec-18	0
S5C53-8P2G2	Steel Structure (Detail) - Area C Lower & Upper Suite Lvl (Seq 1117)	10	10-Dec-18	21-Dec-18	65
S5E123-8P2G2	Steel Structure (Detail) - Area E Lower & Upper Suite Lvl (Seq 1123)	10	12-Dec-18	26-Dec-18	10
S5C118-8P2G2	Steel Structure (Detail) - Area C Lower & Upper Suite Lvl (Seq 1118)	9	18-Dec-18	31-Dec-18	61
S5D59-8P2G2	Steel Structure (Detail) - Area D Lower & Upper Suite Lvl (Seq 1122)	9	04-Jan-19	16-Jan-19	43
S5D57-8P2G2	Steel Structure (Detail) - Area D Lower & Upper Suite Lvl (Seq 1121)	8	14-Jan-19	23-Jan-19	42
S5C126-8P2G2	Steel Structure (Detail) - Area C Lower & Upper Suite Lvl (Seq 1126)	9	14-Jan-19	24-Jan-19	40
S5C120-8P2G2	Steel Structure (Detail) - Area C Lower & Upper Suite Lvl (Seq 1120)	9	18-Jan-19	30-Jan-19	38
S5C55-8P2G2	Steel Structure (Detail) - Area C Lower & Upper Suite Lvl (Seq 1119)	8	23-Jan-19	01-Feb-19	27
S5A42-8P2G13	Steel Structure (Deck/Stud) - Area A Lower & Upper Suite Lvl (Seq 1108)	4	11-Oct-18	16-Oct-18	21
S5B44-8P2G13	Steel Structure (Deck/Stud) - Area B Lower & Upper Suite Lvl (Seq 1111)	5	16-Oct-18	22-Oct-18	19
S5F70-8P2G13	Steel Structure (Deck/Stud) - Area F Lower & Upper Suite Lvl (Seq 1107)	4	17-Oct-18	22-Oct-18	21
S5A109-8P2G13	Steel Structure (Deck/Stud) - Area A Lower & Upper Suite Lvl (Seq 1109)	5	18-Oct-18	24-Oct-18	22
S5F106-8P2G13	Steel Structure (Deck/Stud) - Area F Lower & Upper Suite Lvl (Seq 1106)	5	18-Oct-18	24-Oct-18	22
S5B112-8P2G13	Steel Structure (Deck/Stud) - Area B Lower & Upper Suite Lvl (Seq 1112)	4	22-Oct-18	25-Oct-18	40
S5A110-8P2G13	Steel Structure (Deck/Stud) - Area A Lower & Upper Suite Lvl (Seq 1110)	4	23-Oct-18	26-Oct-18	20
S5F105-8P2G13	Steel Structure (Deck/Stud) - Area F Lower & Upper Suite Lvl (Seq 1105)	4	23-Oct-18	26-Oct-18	20
S5E103-8P2G13	Steel Structure (Deck/Stud) - Area E Lower & Upper Suite Lvl (Seq 1103)	4	31-Oct-18	05-Nov-18	38
S5E67-8P2G13	Steel Structure (Deck/Stud) - Area E Lower & Upper Suite Lvl (Seq 1104)	5	01-Nov-18	07-Nov-18	20
S5E102-8P2G13	Steel Structure (Deck/Stud) - Area E Lower & Upper Suite Lvl (Seq 1102)	5	07-Nov-18	14-Nov-18	34
S5E64-8P2G13	Steel Structure (Deck/Stud) - Area E Lower & Upper Suite Lvl (Seq 1101)	5	13-Nov-18	19-Nov-18	18
S5B47-8P2G13	Steel Structure (Deck/Stud) - Area B Lower & Upper Suite Lvl (Seq 1113)	5	19-Nov-18	27-Nov-18	1
S5B114-8P2G13	Steel Structure (Deck/Stud) - Area B Lower & Upper Suite Lvl (Seq 1114)	5	26-Nov-18	30-Nov-18	30
S5B50-8P2G13	Steel Structure (Deck/Stud) - Area B Lower & Upper Suite Lvl (Seq 1115)	4	28-Nov-18	03-Dec-18	1
S5B116-8P2G13	Steel Structure (Deck/Stud) - Area B Lower & Upper Suite Lvl (Seq 1116)	5	12-Dec-18	18-Dec-18	20
S5E125-8P2G13	Steel Structure (Deck/Stud) - Area E Lower & Upper Suite Lvl (Seq 1125)	4	13-Dec-18	18-Dec-18	14
S5E61-8P2G13	Steel Structure (Deck/Stud) - Area E Lower & Upper Suite Lvl (Seq 1124)	4	18-Dec-18	21-Dec-18	0
S5C53-8P2G13	Steel Structure (Deck/Stud) - Area C Lower & Upper Suite Lvl (Seq 1117)	5	20-Dec-18	27-Dec-18	65
S5E123-8P2G13	Steel Structure (Deck/Stud) - Area E Lower & Upper Suite Lvl (Seq 1123)	5	24-Dec-18	31-Dec-18	10
S5C118-8P2G13	Steel Structure (Deck/Stud) - Area C Lower & Upper Suite Lvl (Seq 1118)	4	28-Dec-18	03-Jan-19	61
S5D59-8P2G13	Steel Structure (Deck/Stud) - Area D Lower & Upper Suite Lvl (Seq 1122)	4	15-Jan-19	18-Jan-19	43
S5D57-8P2G13	Steel Structure (Deck/Stud) - Area D Lower & Upper Suite Lvl (Seq 1121)	4	22-Jan-19	25-Jan-19	42
S5C120-8P2G13	Steel Structure (Deck/Stud) - Area C Lower & Upper Suite Lvl (Seq 1120)	5	29-Jan-19	04-Feb-19	38
S5C55-8P2G13	Steel Structure (Deck/Stud) - Area C Lower & Upper Suite Lvl (Seq 1119)	4	31-Jan-19	05-Feb-19	27
250/300 Upper Mezz & Upper Conc					
S5A43-8P2G1	Steel Structure (Erect) - Area A Upper Mezz & Upper Conc (Seq 2209)	4	16-Oct-18	19-Oct-18	0
S5A210-8P2G1	Steel Structure (Erect) - Area A Upper Mezz & Upper Conc (Seq 2210)	3	22-Oct-18	24-Oct-18	0
S5B45-8P2G1	Steel Structure (Erect) - Area B Upper Mezz & Upper Conc (Seq 2211)	4	25-Oct-18	30-Oct-18	0
S5F71-8P2G1	Steel Structure (Erect) - Area F Upper Mezz & Upper Conc (Seq 2205)	5	25-Oct-18	31-Oct-18	6
S5B212-8P2G1	Steel Structure (Erect) - Area B Upper Mezz & Upper Conc (Seq 2212)	3	31-Oct-18	02-Nov-18	0
S5F204-8P2G1	Steel Structure (Erect) - Area F Upper Mezz & Upper Conc (Seq 2204)	3	01-Nov-18	05-Nov-18	6
S5B48-8P2G1	Steel Structure (Erect) - Area B Upper Mezz & Upper Conc (Seq 2213)	2	09-Nov-18	13-Nov-18	0
S5E68-8P2G1	Steel Structure (Erect) - Area E Upper Mezz & Upper Conc (Seq 2203)	5	13-Nov-18	19-Nov-18	6
S5B214-8P2G1	Steel Structure (Erect) - Area B Upper Mezz & Upper Conc (Seq 2214)	3	19-Nov-18	21-Nov-18	1
S5E202-8P2G1	Steel Structure (Erect) - Area E Upper Mezz & Upper Conc (Seq 2202)	2	20-Nov-18	21-Nov-18	6
S5B51-8P2G1	Steel Structure (Erect) - Area B Upper Mezz & Upper Conc (Seq 2215)	2	26-Nov-18	27-Nov-18	1
S5E65-8P2G1	Steel Structure (Erect) - Area E Upper Mezz & Upper Conc (Seq 2201)	3	26-Nov-18	28-Nov-18	6
S5E62-8P2G1	Steel Structure (Erect) - Area E Upper Mezz & Upper Conc (Seq 2225)	3	18-Dec-18	20-Dec-18	4

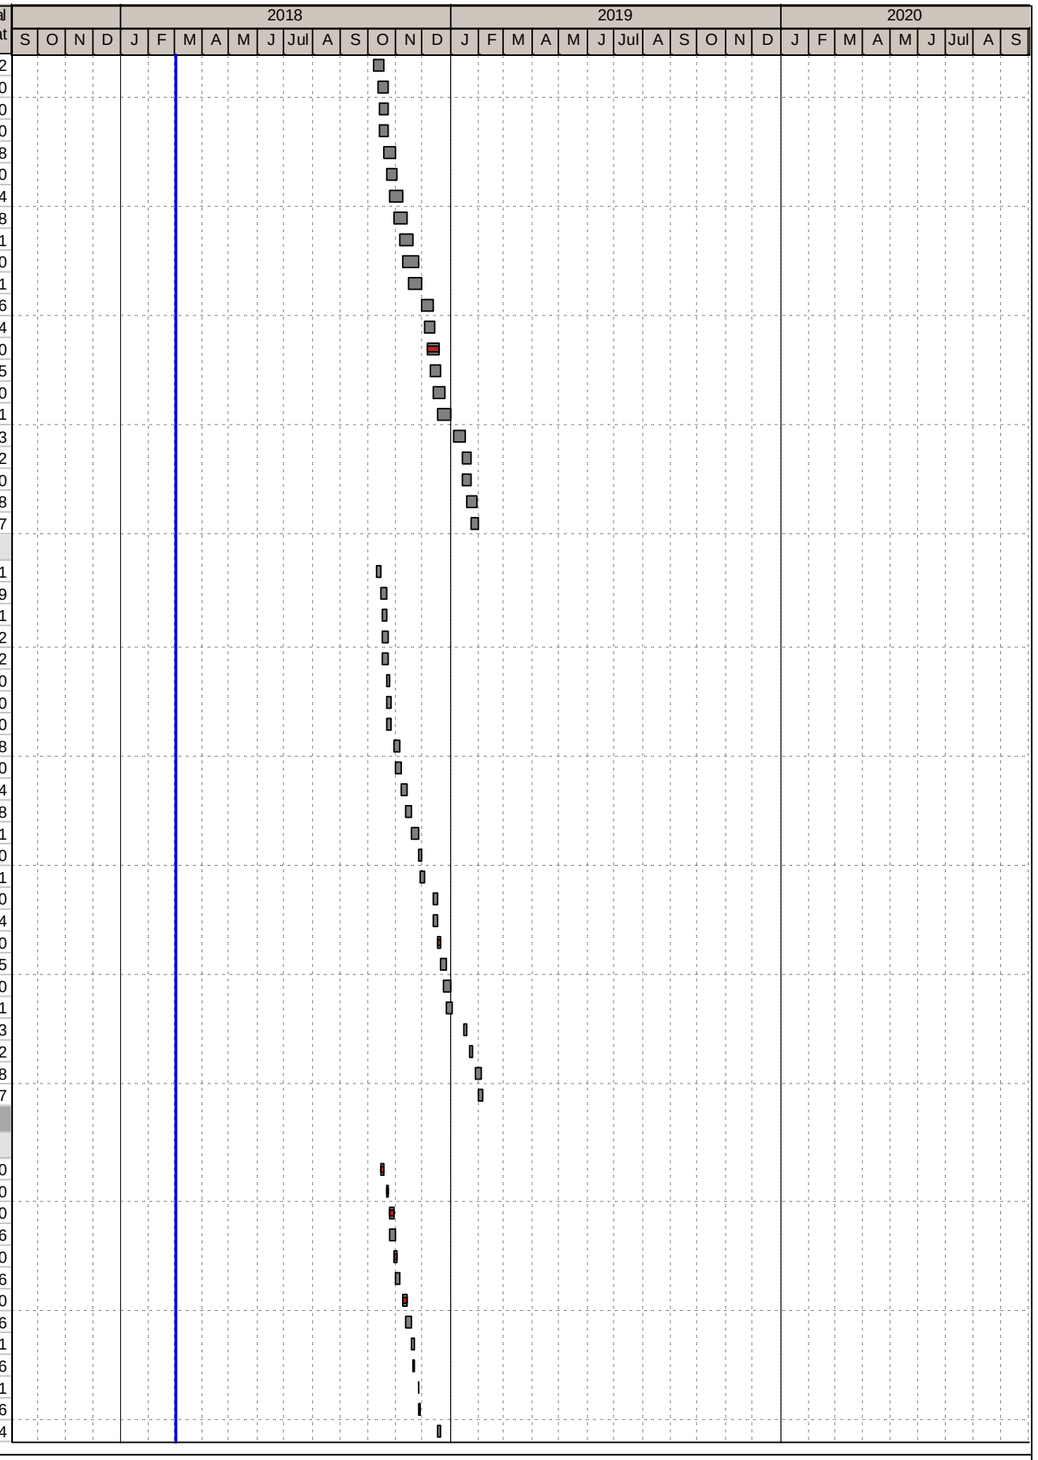

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S5B216-8P2G1	Steel Structure (Erect) - Area B Upper Mezz & Upper Conc (Seq 2216)	5	21-Dec-18	28-Dec-18	1
S5E224-8P2G1	Steel Structure (Erect) - Area E Upper Mezz & Upper Conc (Seq 2224)	5	21-Dec-18	28-Dec-18	4
S5C54-8P2G1	Steel Structure (Erect) - Area C Upper Mezz & Upper Conc (Seq 2217)	6	10-Jan-19	17-Jan-19	20
S5C218-8P2G1	Steel Structure (Erect) - Area C Upper Mezz & Upper Conc (Seq 2218)	4	18-Jan-19	23-Jan-19	20
S5C56-8P2G1	Steel Structure (Erect) - Area C Upper Mezz & Upper Conc (Seq 2219)	2	24-Jan-19	25-Jan-19	20
S5D60-8P2G1	Steel Structure (Erect) - Area D Upper Mezz & Upper Conc (Seq 2223)	4	25-Jan-19	30-Jan-19	9
S5C226-8P2G1	Steel Structure (Erect) - Area C Upper Mezz & Upper Conc (Seq 2226)	3	28-Jan-19	30-Jan-19	20
S5D222-8P2G1	Steel Structure (Erect) - Area D Upper Mezz & Upper Conc (Seq 2222)	6	31-Jan-19	07-Feb-19	9
S5D58-8P2G1	Steel Structure (Erect) - Area D Upper Mezz & Upper Conc (Seq 2221)	2	13-Feb-19	14-Feb-19	9
S5C220-8P2G1	Steel Structure (Erect) - Area C Upper Mezz & Upper Conc (Seq 2220)	3	15-Feb-19	20-Feb-19	9
S5A43-8P2G2	Steel Structure (Detail) - Area A Upper Mezz & Upper Conc (Seq 2209)	8	17-Oct-18	26-Oct-18	19
S5A210-8P2G2	Steel Structure (Detail) - Area A Upper Mezz & Upper Conc (Seq 2210)	8	24-Oct-18	02-Nov-18	25
S5F71-8P2G2	Steel Structure (Detail) - Area F Upper Mezz & Upper Conc (Seq 2205)	8	26-Oct-18	06-Nov-18	17
S5B45-8P2G2	Steel Structure (Detail) - Area B Upper Mezz & Upper Conc (Seq 2211)	9	29-Oct-18	08-Nov-18	30
S5B212-8P2G2	Steel Structure (Detail) - Area B Upper Mezz & Upper Conc (Seq 2212)	8	02-Nov-18	14-Nov-18	28
S5F204-8P2G2	Steel Structure (Detail) - Area F Upper Mezz & Upper Conc (Seq 2204)	8	13-Nov-18	26-Nov-18	11
S5E68-8P2G2	Steel Structure (Detail) - Area E Upper Mezz & Upper Conc (Seq 2203)	10	15-Nov-18	30-Nov-18	17
S5B214-8P2G2	Steel Structure (Detail) - Area B Upper Mezz & Upper Conc (Seq 2214)	8	21-Nov-18	04-Dec-18	32
S5E202-8P2G2	Steel Structure (Detail) - Area E Upper Mezz & Upper Conc (Seq 2202)	9	26-Nov-18	06-Dec-18	33
S5B48-8P2G2	Steel Structure (Detail) - Area B Upper Mezz & Upper Conc (Seq 2213)	8	28-Nov-18	07-Dec-18	16
S5B51-8P2G2	Steel Structure (Detail) - Area B Upper Mezz & Upper Conc (Seq 2215)	8	28-Nov-18	07-Dec-18	24
S5E65-8P2G2	Steel Structure (Detail) - Area E Upper Mezz & Upper Conc (Seq 2201)	8	13-Dec-18	24-Dec-18	6
S5E62-8P2G2	Steel Structure (Detail) - Area E Upper Mezz & Upper Conc (Seq 2225)	9	20-Dec-18	03-Jan-19	4
S5B216-8P2G2	Steel Structure (Detail) - Area B Upper Mezz & Upper Conc (Seq 2216)	9	07-Jan-19	17-Jan-19	1
S5E224-8P2G2	Steel Structure (Detail) - Area E Upper Mezz & Upper Conc (Seq 2224)	10	10-Jan-19	23-Jan-19	4
S5C54-8P2G2	Steel Structure (Detail) - Area C Upper Mezz & Upper Conc (Seq 2217)	10	14-Jan-19	25-Jan-19	36
S5C218-8P2G2	Steel Structure (Detail) - Area C Upper Mezz & Upper Conc (Seq 2218)	8	22-Jan-19	31-Jan-19	36
S5C56-8P2G2	Steel Structure (Detail) - Area C Upper Mezz & Upper Conc (Seq 2219)	8	28-Jan-19	06-Feb-19	33
S5D60-8P2G2	Steel Structure (Detail) - Area D Upper Mezz & Upper Conc (Seq 2223)	8	29-Jan-19	07-Feb-19	29
S5C226-8P2G2	Steel Structure (Detail) - Area C Upper Mezz & Upper Conc (Seq 2226)	8	30-Jan-19	08-Feb-19	29
S5D222-8P2G2	Steel Structure (Detail) - Area D Upper Mezz & Upper Conc (Seq 2222)	10	04-Feb-19	15-Feb-19	25
S5D58-8P2G2	Steel Structure (Detail) - Area D Upper Mezz & Upper Conc (Seq 2221)	9	15-Feb-19	28-Feb-19	19
S5C220-8P2G2	Steel Structure (Detail) - Area C Upper Mezz & Upper Conc (Seq 2220)	8	04-Mar-19	13-Mar-19	15
S5A43-8P2G13	Steel Structure (Deck/Stud) - Area A Upper Mezz & Upper Conc (Seq 2209)	4	25-Oct-18	30-Oct-18	19
S5A210-8P2G13	Steel Structure (Deck/Stud) - Area A Upper Mezz & Upper Conc (Seq 2210)	4	01-Nov-18	06-Nov-18	25
S5F71-8P2G13	Steel Structure (Deck/Stud) - Area F Upper Mezz & Upper Conc (Seq 2205)	6	02-Nov-18	09-Nov-18	17
S5B45-8P2G13	Steel Structure (Deck/Stud) - Area B Upper Mezz & Upper Conc (Seq 2211)	4	07-Nov-18	13-Nov-18	30
S5B212-8P2G13	Steel Structure (Deck/Stud) - Area B Upper Mezz & Upper Conc (Seq 2212)	5	13-Nov-18	19-Nov-18	28
S5F204-8P2G13	Steel Structure (Deck/Stud) - Area F Upper Mezz & Upper Conc (Seq 2204)	4	21-Nov-18	28-Nov-18	19
S5B214-8P2G13	Steel Structure (Deck/Stud) - Area B Upper Mezz & Upper Conc (Seq 2214)	4	29-Nov-18	04-Dec-18	32
S5E202-8P2G13	Steel Structure (Deck/Stud) - Area E Upper Mezz & Upper Conc (Seq 2202)	4	05-Dec-18	10-Dec-18	33
S5B48-8P2G13	Steel Structure (Deck/Stud) - Area B Upper Mezz & Upper Conc (Seq 2213)	4	06-Dec-18	11-Dec-18	16
S5B51-8P2G13	Steel Structure (Deck/Stud) - Area B Upper Mezz & Upper Conc (Seq 2215)	5	12-Dec-18	18-Dec-18	20
S5E68-8P2G13	\Steel Structure (Deck/Stud) - Area E Upper Mezz & Upper Conc (Seq 2203)	5	24-Dec-18	31-Dec-18	0
S5E65-8P2G13	Steel Structure (Deck/Stud) - Area E Upper Mezz & Upper Conc (Seq 2201)	4	02-Jan-19	07-Jan-19	0
S5E62-8P2G13	Steel Structure (Deck/Stud) - Area E Upper Mezz & Upper Conc (Seq 2225)	4	08-Jan-19	11-Jan-19	0
S5B216-8P2G13	Steel Structure (Deck/Stud) - Area B Upper Mezz & Upper Conc (Seq 2216)	5	16-Jan-19	22-Jan-19	1
S5E224-8P2G13	Steel Structure (Deck/Stud) - Area E Upper Mezz & Upper Conc (Seq 2224)	5	22-Jan-19	28-Jan-19	4
S5C218-8P2G13	Steel Structure (Deck/Stud) - Area C Upper Mezz & Upper Conc (Seq 2218)	5	31-Jan-19	06-Feb-19	35
S5D60-8P2G13	Steel Structure (Deck/Stud) - Area D Upper Mezz & Upper Conc (Seq 2223)	4	06-Feb-19	11-Feb-19	29
S5C54-8P2G13	Steel Structure (Deck/Stud) - Area C Upper Mezz & Upper Conc (Seq 2217)	5	06-Feb-19	12-Feb-19	27
S5C56-8P2G13	Steel Structure (Deck/Stud) - Area C Upper Mezz & Upper Conc (Seq 2219)	5	13-Feb-19	20-Feb-19	27
S5D222-8P2G13	Steel Structure (Deck/Stud) - Area D Upper Mezz & Upper Conc (Seq 2222)	5	14-Feb-19	21-Feb-19	25
S5D58-8P2G13	Steel Structure (Deck/Stud) - Area D Upper Mezz & Upper Conc (Seq 2221)	4	27-Feb-19	04-Mar-19	19
S5C220-8P2G13	Steel Structure (Deck/Stud) - Area C Upper Mezz & Upper Conc (Seq 2220)	4	12-Mar-19	15-Mar-19	15
350/400 Upper Stadia Support & Press Lvl					
S5A303-8P2G1	Steel Structure (Erect) - Area A Upper Stadia Support & Press Lvl (Seq 3303)	4	05-Nov-18	08-Nov-18	0
S5F302-8P2G1	Steel Structure (Erect) - Area F Upper Stadia Support & Press Lvl (Seq 3302)	4	06-Nov-18	09-Nov-18	6
S5C312-8P2G1	Steel Structure (Erect) - Area A Upper Stadia Support & Press Lvl (Seq 3312)	4	14-Nov-18	19-Nov-18	0
S5B46-8P2G1	Steel Structure (Erect) - Area B Upper Stadia Support & Press Lvl (Seq 3304)	5	20-Nov-18	28-Nov-18	0

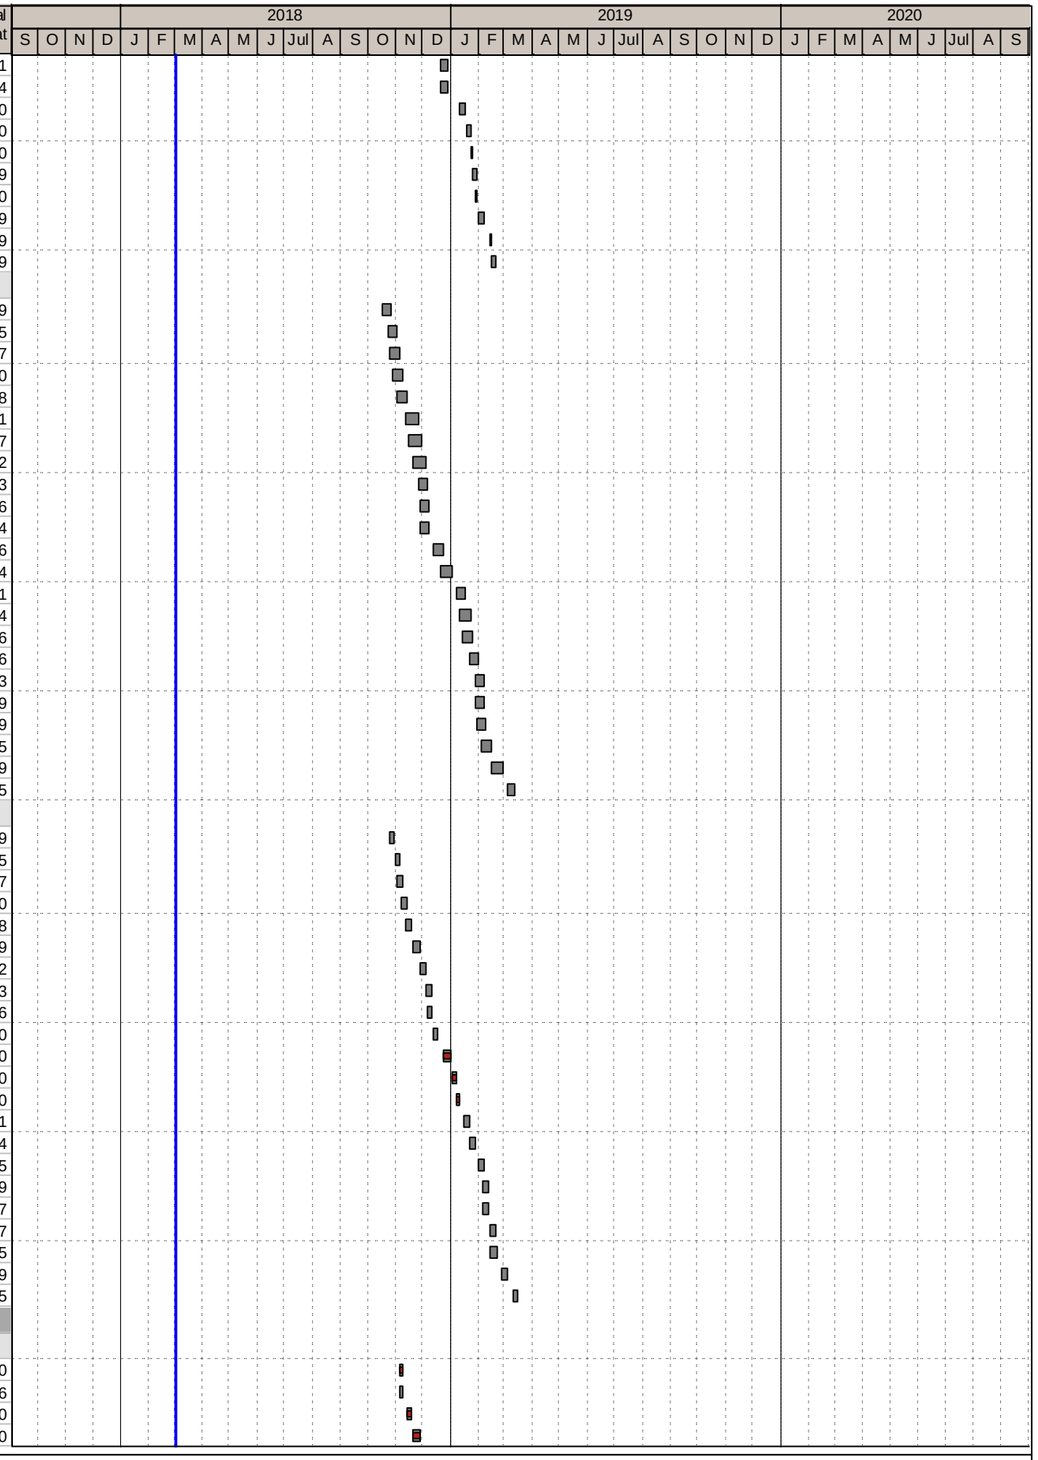

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S5C313-8P2G1	Steel Structure (Erect) - Area F Upper Stadia Support & Press Lvl (Seq 3313)	4	29-Nov-18	04-Dec-18	6
S5E69-8P2G1	Steel Structure (Erect) - Area E Upper Stadia Support & Press Lvl (Seq 3301)	6	05-Dec-18	12-Dec-18	6
S5B49-8P2G1	Steel Structure (Erect) - Area B Upper Stadia Support & Press Lvl (Seq 3305)	4	31-Dec-18	04-Jan-19	1
S5E66-8P2G1	Steel Structure (Erect) - Area E Upper Stadia Support & Press Lvl (Seq 3310)	7	31-Dec-18	09-Jan-19	4
S5C306-8P2G1	Steel Structure (Erect) - Area C Upper Stadia Support & Press Lvl (Seq 3306)	3	28-Jan-19	30-Jan-19	25
S5D309-8P2G1	Steel Structure (Erect) - Area D Upper Stadia Support & Press Lvl (Seq 3309)	3	08-Feb-19	12-Feb-19	9
S5C314-8P2G1	Steel Structure (Erect) - Area C Upper Stadia Support & Press Lvl (Seq 3314)	2	20-Feb-19	21-Feb-19	15
S5C307-8P2G1	Steel Structure (Erect) - Area C Upper Stadia Support & Press Lvl (Seq 3307)	3	20-Feb-19	22-Feb-19	14
S5D308-8P2G1	Steel Structure (Erect) - Area D Upper Stadia Support & Press Lvl (Seq 3308)	5	25-Feb-19	01-Mar-19	9
S5B82-8P2G1	Steel Structure (Erect) - Area C/D Scoreboard Steel (Seq 3311)	3	04-Mar-19	06-Mar-19	9
S5A303-8P2G2	Steel Structure (Detail) - Area A Upper Stadia Support & Press Lvl (Seq 3303)	10	07-Nov-18	21-Nov-18	27
S5F302-8P2G2	Steel Structure (Detail) - Area F Upper Stadia Support & Press Lvl (Seq 3302)	10	08-Nov-18	26-Nov-18	12
S5C312-8P2G2	Steel Structure (Detail) - Area A Upper Stadia Support & Press Lvl (Seq 3312)	10	16-Nov-18	03-Dec-18	24
S5B46-8P2G2	Steel Structure (Detail) - Area B Upper Stadia Support & Press Lvl (Seq 3304)	10	26-Nov-18	07-Dec-18	16
S5C313-8P2G2	Steel Structure (Detail) - Area F Upper Stadia Support & Press Lvl (Seq 3313)	10	03-Dec-18	14-Dec-18	23
S5E69-8P2G2	Steel Structure (Detail) - Area E Upper Stadia Support & Press Lvl (Seq 3301)	12	07-Dec-18	24-Dec-18	19
S5B49-8P2G2	Steel Structure (Detail) - Area B Upper Stadia Support & Press Lvl (Seq 3305)	10	03-Jan-19	16-Jan-19	3
S5E66-8P2G2	Steel Structure (Detail) - Area E Upper Stadia Support & Press Lvl (Seq 3310)	12	03-Jan-19	18-Jan-19	7
S5C306-8P2G2	Steel Structure (Detail) - Area C Upper Stadia Support & Press Lvl (Seq 3306)	8	30-Jan-19	08-Feb-19	30
S5D309-8P2G2	Steel Structure (Detail) - Area D Upper Stadia Support & Press Lvl (Seq 3309)	8	12-Feb-19	22-Feb-19	23
S5C307-8P2G2	Steel Structure (Detail) - Area C Upper Stadia Support & Press Lvl (Seq 3307)	8	22-Feb-19	05-Mar-19	19
S5C314-8P2G2	Steel Structure (Detail) - Area C Upper Stadia Support & Press Lvl (Seq 3314)	8	22-Feb-19	05-Mar-19	20
S5D308-8P2G2	Steel Structure (Detail) - Area D Upper Stadia Support & Press Lvl (Seq 3308)	8	27-Feb-19	08-Mar-19	16
S5B82-8P2G2	Steel Structure (Detail) - Area C/D Scoreboard Steel (Seq 3311)	10	06-Mar-19	19-Mar-19	9
S5A303-8P2G13	Steel Structure (Deck/Stud) - Area A Upper Stadia Support & Press Lvl (Seq 3303)	5	20-Nov-18	28-Nov-18	27
S5F302-8P2G13	Steel Structure (Deck/Stud) - Area F Upper Stadia Support & Press Lvl (Seq 3302)	5	21-Nov-18	29-Nov-18	18
S5E69-8P2G13	Steel Structure (Deck/Stud) - Area E Upper Stadia Support & Press Lvl (Seq 3301)	5	14-Jan-19	18-Jan-19	5
S5E66-8P2G13	Steel Structure (Deck/Stud) - Area E Upper Stadia Support & Press Lvl (Seq 3310)	5	21-Jan-19	25-Jan-19	5
S5C306-8P2G13	Steel Structure (Deck/Stud) - Area C Upper Stadia Support & Press Lvl (Seq 3306)	5	07-Feb-19	13-Feb-19	30
S5D309-8P2G13	Steel Structure (Deck/Stud) - Area D Upper Stadia Support & Press Lvl (Seq 3309)	5	21-Feb-19	27-Feb-19	23
S5C307-8P2G13	Steel Structure (Deck/Stud) - Area C Upper Stadia Support & Press Lvl (Seq 3307)	5	04-Mar-19	08-Mar-19	20
S5D308-8P2G13	Steel Structure (Deck/Stud) - Area D Upper Stadia Support & Press Lvl (Seq 3308)	5	07-Mar-19	13-Mar-19	18
Erect Structural Steel/Metal Deck					
100 Main Concourse					
S5A1-8P2G55	Steel Structure - Ground Assembly / Detailing (Seq 0031)	6	16-Oct-18	23-Oct-18	9
S5A-8P2G75	Steel Structure - Ground Assembly / Detailing (Seq 0041)	6	19-Oct-18	26-Oct-18	9
S5A1-8P2G75	Steel Structure - Ground Assembly / Detailing (Seq 0051)	6	24-Oct-18	31-Oct-18	9
S5A-8P2G95	Steel Structure - Ground Assembly / Detailing (Seq 0061)	6	29-Oct-18	05-Nov-18	9
S5A1-8P2G95	Steel Structure - Ground Assembly / Detailing (Seq 0071)	6	01-Nov-18	08-Nov-18	9
S5A-8P2G115	Steel Structure - Ground Assembly / Detailing (Seq 0081)	6	06-Nov-18	14-Nov-18	9
S5A1-8P2G115	Steel Structure - Ground Assembly / Detailing (Seq 0091)	6	09-Nov-18	19-Nov-18	9
S5A1-8P2G135	Steel Structure - Ground Assembly / Detailing (Seq 0032)	6	15-Nov-18	26-Nov-18	9
S5A-8P2G155	Steel Structure - Ground Assembly / Detailing (Seq 0042)	6	20-Nov-18	29-Nov-18	9
S5A1-8P2G155	Steel Structure - Ground Assembly / Detailing (Seq 0052)	6	27-Nov-18	04-Dec-18	9
S5A-8P2G175	Steel Structure - Ground Assembly / Detailing (Seq 0062)	6	30-Nov-18	07-Dec-18	9
S5A1-8P2G175	Steel Structure - Ground Assembly / Detailing (Seq 0072)	6	05-Dec-18	12-Dec-18	9
S5A-8P2G195	Steel Structure - Ground Assembly / Detailing (Seq 0082)	6	10-Dec-18	17-Dec-18	9
S5A1-8P2G195	Steel Structure - Ground Assembly / Detailing (Seq 0092)	6	13-Dec-18	20-Dec-18	9
S5A-8P2G428	Steel Structure - Ground Assembly / Detailing (Seq 0011)	3	05-Dec-18	07-Dec-18	9
S5A-8P2G55	Steel Structure - Ground Assembly / Detailing (Seq 0021)	3	10-Dec-18	12-Dec-18	9
S5A-8P2G427	Steel Structure - Ground Assembly / Detailing (Seq 0012)	3	13-Dec-18	17-Dec-18	9
S5A-8P2G135	Steel Structure - Ground Assembly / Detailing (Seq 0022)	3	18-Dec-18	20-Dec-18	9
S5A1-8P2G205	S	1	06-Nov-18	06-Nov-18	9
S5A-8P2G215	Steel Structure - Erect (41) L	1	07-Nov-18	07-Nov-18	9
S5A1-8P2G215	Steel Structure - Erect (51) L	1	13-Nov-18	13-Nov-18	9
S5A-8P2G225	Steel Structure - Erect (61) L	1	16-Nov-18	16-Nov-18	9
S5A1-8P2G225	Steel Structure - Erect (71) L	1	20-Nov-18	20-Nov-18	9

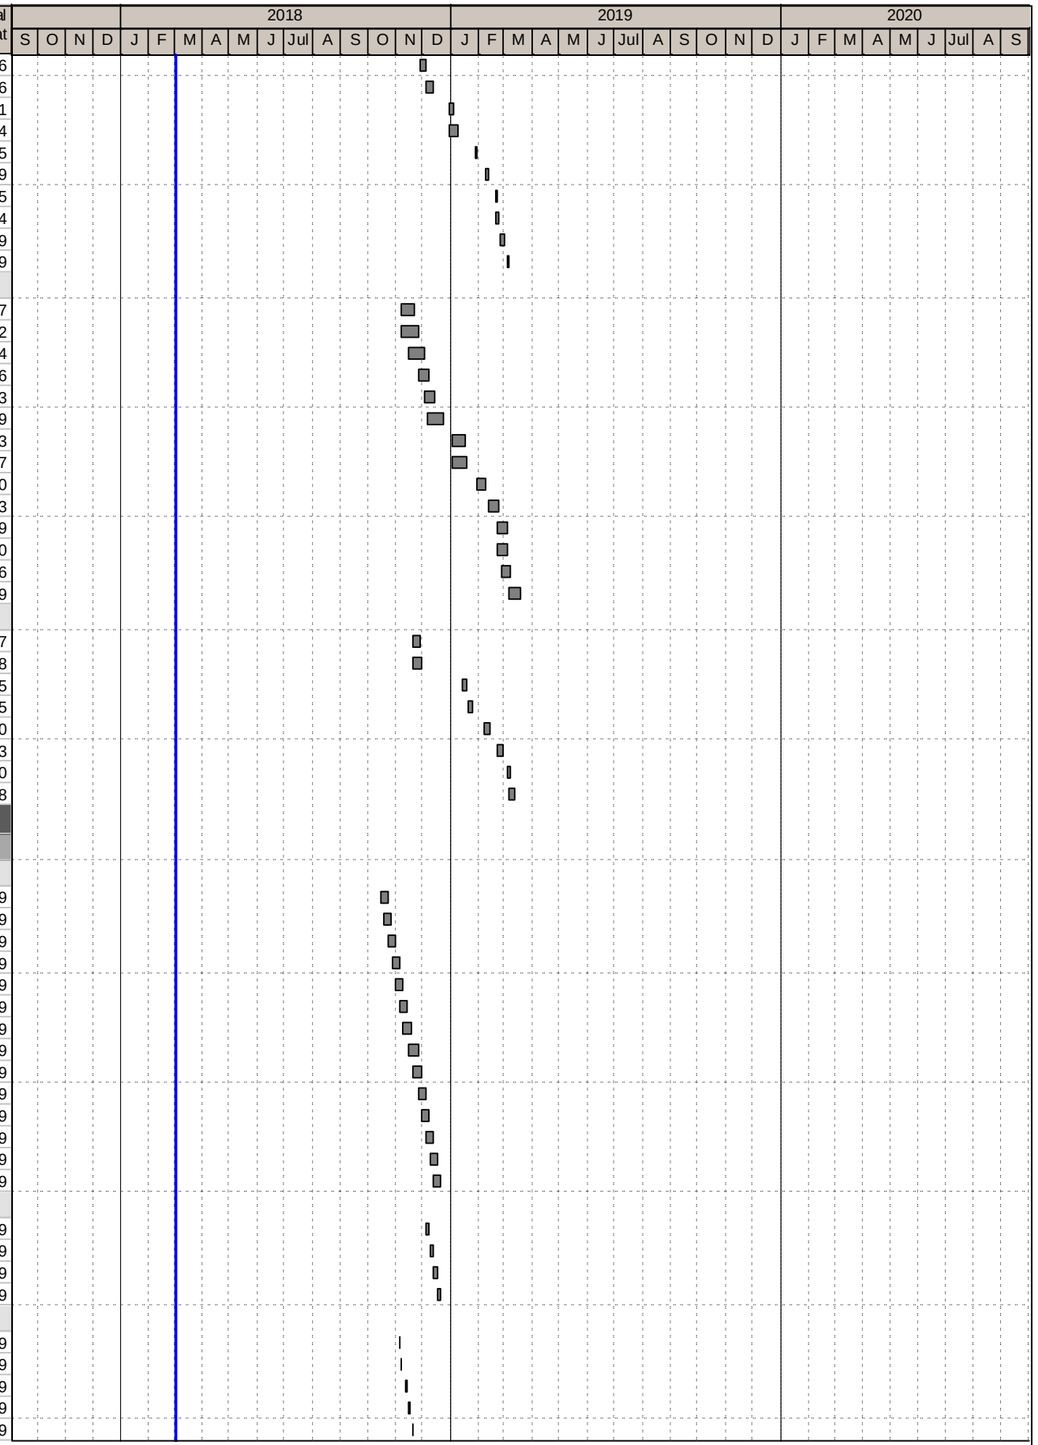

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S5A-8P2G235	Steel Structure - Erect (81) L	1	26-Nov-18	26-Nov-18	9
S5A1-8P2G235	Steel Structure - Erect (91) L	1	28-Nov-18	28-Nov-18	9
S5A1-8P2G385	Steel Structure - Move Crane Seq 91 to Seq 32	1	30-Nov-18	30-Nov-18	9
S5A1-8P2G245	Steel Structure - Erect (32) R	1	03-Dec-18	03-Dec-18	9
S5A-8P2G255	Steel Structure - Erect (42) R	1	04-Dec-18	04-Dec-18	9
S5A1-8P2G255	Steel Structure - Erect (52) R	1	07-Dec-18	07-Dec-18	9
S5A-8P2G265	Steel Structure - Erect (62) R	1	12-Dec-18	12-Dec-18	9
S5A-8P2G205	Steel Structure - Erect (21) L	1	13-Dec-18	13-Dec-18	9
S5A1-8P2G265	Steel Structure - Erect (72) R	1	17-Dec-18	17-Dec-18	9
S5A1-8P2G363	Steel Structure - Erect (11) L	1	18-Dec-18	18-Dec-18	9
S5A-8P2G275	Steel Structure - Erect (82) R	1	19-Dec-18	19-Dec-18	9
S5A-8P2G245	Steel Structure - Erect (22) R	1	21-Dec-18	21-Dec-18	9
S5A1-8P2G275	Steel Structure - Erect (92) R	1	21-Dec-18	21-Dec-18	9
S5A1-8P2G364	Steel Structure - Erect (12) R	1	27-Dec-18	27-Dec-18	9
S5A1-8P2G356	Steel Structure - Infill (33) L	2	08-Nov-18	09-Nov-18	9
S5A-8P2G397	Steel Structure - Infill (43) L	2	14-Nov-18	15-Nov-18	9
S5A1-8P2G357	Steel Structure - Infill (53) L	1	19-Nov-18	19-Nov-18	9
S5A-8P2G398	Steel Structure - Infill (63) L	1	21-Nov-18	21-Nov-18	9
S5A1-8P2G358	Steel Structure - Infill (73) L	1	27-Nov-18	27-Nov-18	9
S5A-8P2G399	Steel Structure - Infill (83) L	1	29-Nov-18	29-Nov-18	9
S5A1-8P2G360	Steel Structure - Infill (34) R	2	05-Dec-18	06-Dec-18	9
S5A-8P2G401	Steel Structure - Infill (44) R	2	10-Dec-18	11-Dec-18	9
S5A1-8P2G361	Steel Structure - Infill (54) R	2	13-Dec-18	14-Dec-18	9
S5A-8P2G396	Steel Structure - Infill (23) L	2	14-Dec-18	17-Dec-18	9
S5A-8P2G402	Steel Structure - Infill (64) R	1	18-Dec-18	18-Dec-18	9
S5A1-8P2G362	Steel Structure - Infill (74) R	1	20-Dec-18	20-Dec-18	9
S5A1-8P2G381	Steel Structure - Infill (13) L	2	19-Dec-18	20-Dec-18	9
S5A-8P2G403	Steel Structure - Infill (84) R	1	24-Dec-18	24-Dec-18	10
S5A-8P2G400	Steel Structure - Infill (24) R	2	24-Dec-18	26-Dec-18	9
S5A1-8P2G382	Steel Structure - Infill (14) R	2	28-Dec-18	31-Dec-18	10
S5A1-8P2G285	Steel Structure - Bolt/Weld (31) L	2	07-Nov-18	08-Nov-18	36
S5A-8P2G295	Steel Structure - Bolt/Weld (41) L	2	08-Nov-18	09-Nov-18	35
S5A1-8P2G295	Steel Structure - Bolt/Weld (51) L	2	14-Nov-18	15-Nov-18	32
S5A-8P2G305	Steel Structure - Bolt/Weld (61) L	2	19-Nov-18	20-Nov-18	29
S5A1-8P2G305	Steel Structure - Bolt/Weld (71) L	2	21-Nov-18	26-Nov-18	27
S5A-8P2G315	Steel Structure - Bolt/Weld (81) L	2	27-Nov-18	28-Nov-18	25
S5A1-8P2G315	Steel Structure - Bolt/Weld (91) L	2	29-Nov-18	30-Nov-18	23
S5A1-8P2G325	Steel Structure - Bolt/Weld (32) R	5	04-Dec-18	10-Dec-18	23
S5A-8P2G335	Steel Structure - Bolt/Weld (42) R	5	05-Dec-18	11-Dec-18	22
S5A1-8P2G335	Steel Structure - Bolt/Weld (52) R	5	10-Dec-18	14-Dec-18	19
S5A-8P2G285	Steel Structure - Bolt/Weld (21) L	2	14-Dec-18	17-Dec-18	12
S5A-8P2G345	Steel Structure - Bolt/Weld (62) R	5	13-Dec-18	19-Dec-18	16
S5A1-8P2G366	Steel Structure - Bolt/Weld (11) L	2	19-Dec-18	20-Dec-18	12
S5A1-8P2G345	Steel Structure - Bolt/Weld (72) R	5	18-Dec-18	24-Dec-18	13
S5A-8P2G355	Steel Structure - Bolt/Weld (82) R	5	20-Dec-18	27-Dec-18	11
S5A-8P2G325	Steel Structure - Bolt/Weld (22) R	5	24-Dec-18	31-Dec-18	12
S5A1-8P2G355	Steel Structure - Bolt/Weld (92) R	5	24-Dec-18	31-Dec-18	9
S5A1-8P2G365	Steel Structure - Bolt/Weld (12) R	5	28-Dec-18	04-Jan-19	9
S5A1-8P2G375	Steel Structure - Infill Bolt/Weld (33) L	4	13-Nov-18	16-Nov-18	31
S5A-8P2G413	Steel Structure - Infill Bolt/Weld (43) L	4	16-Nov-18	21-Nov-18	28
S5A1-8P2G376	Steel Structure - Infill Bolt/Weld (53) L	4	20-Nov-18	27-Nov-18	26
S5A-8P2G414	Steel Structure - Infill Bolt/Weld (63) L	3	26-Nov-18	28-Nov-18	25
S5A1-8P2G377	Steel Structure - Infill Bolt/Weld (73) L	3	28-Nov-18	30-Nov-18	23
S5A-8P2G415	Steel Structure - Infill Bolt/Weld (83) L	3	30-Nov-18	04-Dec-18	21
S5A1-8P2G378	Steel Structure - Infill Bolt/Weld (34) R	4	07-Dec-18	12-Dec-18	21
S5A-8P2G417	Steel Structure - Infill Bolt/Weld (44) R	4	12-Dec-18	17-Dec-18	18
S5A1-8P2G379	Steel Structure - Infill Bolt/Weld (54) R	4	17-Dec-18	20-Dec-18	15
S5A-8P2G418	Steel Structure - Infill Bolt/Weld (64) R	3	19-Dec-18	21-Dec-18	14
S5A1-8P2G383	Steel Structure - Infill Bolt/Weld (13) L	2	21-Dec-18	24-Dec-18	10
S5A-8P2G412	Steel Structure - Infill Bolt/Weld (23) L	6	18-Dec-18	26-Dec-18	9

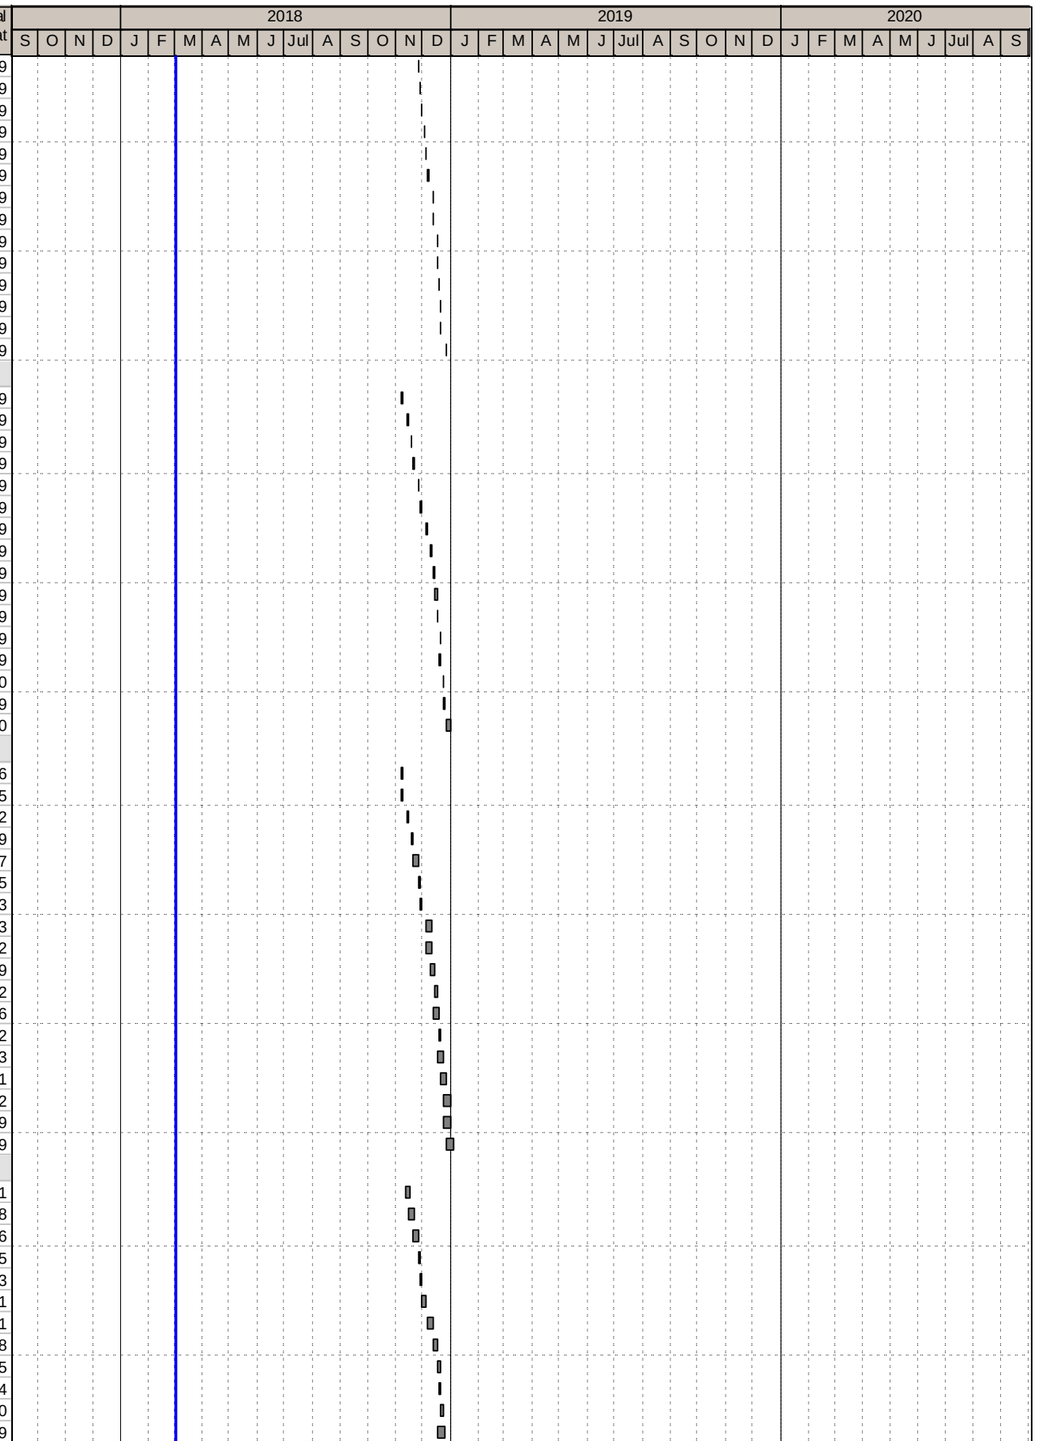

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S5A1-8P2G380	Steel Structure - Infill Bolt/Weld (74) R	3	21-Dec-18	26-Dec-18	12
S5A-8P2G419	Steel Structure - Infill Bolt/Weld (84) R	3	26-Dec-18	28-Dec-18	10
S5A-8P2G416	Steel Structure - Infill Bolt/Weld (24) R	5	27-Dec-18	03-Jan-19	10
S5A1-8P2G384	Steel Structure - Infill Bolt/Weld (14) R	2	02-Jan-19	03-Jan-19	10
S5A-8P2G420	Steel Structure - Deck Left Phase One	6	21-Dec-18	31-Dec-18	9
S5A-8P2G424	Steel Structure - Deck Right Phase One	6	02-Jan-19	09-Jan-19	9
S5A-8P2G430	Steel Structure - Install Shoring Towers for Field Long Span	5	30-Oct-18	05-Nov-18	9
S5A-8P2G429	Steel Structure - Deshore Long Span at Field	3	02-Jan-19	04-Jan-19	10
S5A-8P2G375	Steel Structure - Deck Long Span over Field Phase Two Post Loading	5	05-Mar-19	11-Mar-19	59
Steel Roof Trusses					
410 Canopy Roof Support					
SRB422-8P4D1	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4221 Lower	2	22-Aug-18	23-Aug-18	10
SRB423-8P4D1	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4231 Lower	2	24-Aug-18	27-Aug-18	10
SRB424-8P4D1	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4241 Lower	2	28-Aug-18	29-Aug-18	10
SRB425-8P4D1	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4251 Lower	2	30-Aug-18	31-Aug-18	10
SRB422-8P4D25	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4222 Upper	2	04-Sep-18	05-Sep-18	10
SRB423-8P4D25	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4232 Upper	2	06-Sep-18	07-Sep-18	10
SRB424-8P4D25	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4242 Upper	2	10-Sep-18	11-Sep-18	10
SRB425-8P4D25	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4252 Upper	2	12-Sep-18	13-Sep-18	10
SRB426-8P4D1	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4261 Lower	2	14-Sep-18	17-Sep-18	10
SRB427-8P4D1	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4271 Lower	2	18-Sep-18	19-Sep-18	10
SRB428-8P4D1	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4281 Lower	2	20-Sep-18	21-Sep-18	10
SRB426-8P4D25	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4262 Upper	2	24-Sep-18	25-Sep-18	10
SRB427-8P4D25	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4272 Upper	2	26-Sep-18	27-Sep-18	10
SRB428-8P4D25	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4282 Upper	2	28-Sep-18	01-Oct-18	10
SRB429-8P4D1	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4291 Lower	2	10-Oct-18	11-Oct-18	4
SRB430-8P4D1	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4301 Lower	2	12-Oct-18	15-Oct-18	4
SRB431-8P4D1	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4311 Lower	2	16-Oct-18	17-Oct-18	4
SRB429-8P4D25	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4292 Upper	2	18-Oct-18	19-Oct-18	4
SRB430-8P4D25	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4302 Upper	2	22-Oct-18	23-Oct-18	4
SRB431-8P4D25	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4312 Upper	2	24-Oct-18	25-Oct-18	4
SRB432-8P4D1	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4321 Lower	2	26-Oct-18	29-Oct-18	4
SRC433-8P4D1	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4331 Lower	2	30-Oct-18	31-Oct-18	4
SRC434-8P4D1	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4341 Lower	2	01-Nov-18	02-Nov-18	4
SRC435-8P4D1	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4351 Lower	2	05-Nov-18	06-Nov-18	4
SRC436-8P4D1	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4361 Lower	2	07-Nov-18	08-Nov-18	4
SRB432-8P4D25	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4322 Upper	2	09-Nov-18	13-Nov-18	4
SRC433-8P4D25	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4332 Upper	2	14-Nov-18	15-Nov-18	6
SRC434-8P4D25	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4342 Upper	2	16-Nov-18	19-Nov-18	6
SRC435-8P4D25	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4352 Upper	2	20-Nov-18	21-Nov-18	6
SRC436-8P4D25	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4362 Upper	2	26-Nov-18	27-Nov-18	10
SRA419-8P4D1	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4191 Lower	2	11-Jul-18	12-Jul-18	7
SRA420-8P4D1	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4201 Lower	2	13-Jul-18	16-Jul-18	7
SRB421-8P4D1	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4211 Lower	2	17-Jul-18	18-Jul-18	7
SRA418-8P4D1	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4181 Lower	2	19-Jul-18	20-Jul-18	7
SRA417-8P4D1	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4171 Lower	2	23-Jul-18	24-Jul-18	7
SRA419-8P4D15	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4192 Upper	2	25-Jul-18	26-Jul-18	7
SRA420-8P4D25	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4202 Upper	2	27-Jul-18	30-Jul-18	7
SRB421-8P4D25	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4212 Upper	2	31-Jul-18	01-Aug-18	7
SRA418-8P4D25	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4182 Upper	2	02-Aug-18	03-Aug-18	7
SRA417-8P4D25	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4172 Upper	2	06-Aug-18	07-Aug-18	7
SRF408-8P4D1	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4081 Lower	2	08-Aug-18	09-Aug-18	7
SRF407-8P4D1	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4071 Lower	2	10-Aug-18	13-Aug-18	7
SRE406-8P4D1	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4061 Lower	2	14-Aug-18	15-Aug-18	7
SRF409-8P4D1	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4091 Lower	2	16-Aug-18	17-Aug-18	7
SRF410--8P4D1	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4101 Lower	2	20-Aug-18	21-Aug-18	7
SRF408-8P4D15	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4082 Upper	2	22-Aug-18	23-Aug-18	7

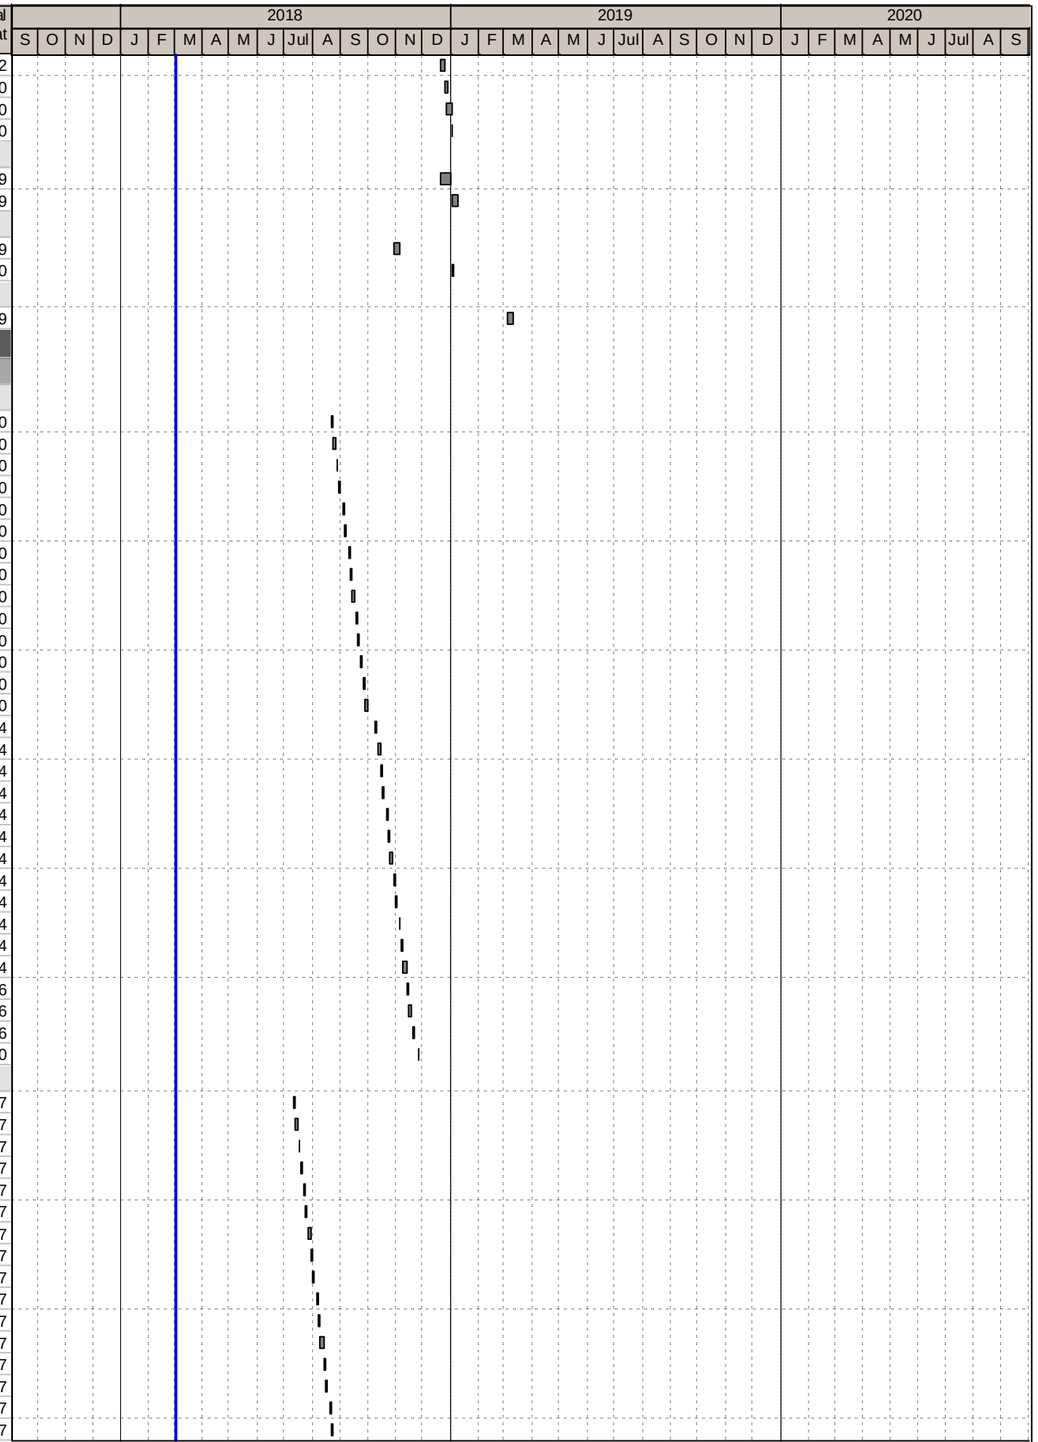

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
SRF407-8P4D25	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4072 Upper	2	24-Aug-18	27-Aug-18	7
SRE406-8P4D25	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4062 Upper	2	28-Aug-18	29-Aug-18	7
SRF409-8P4D25	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4092 Upper	2	30-Aug-18	31-Aug-18	7
SRF410--8P4D2	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4102 Upper	2	04-Sep-18	05-Sep-18	7
SRE405-8P4D1	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4051 Lower	2	06-Sep-18	07-Sep-18	7
SRE404-8P4D1	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4041 Lower	2	10-Sep-18	11-Sep-18	7
SRE403-8P4D1	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4031 Lower	2	12-Sep-18	13-Sep-18	7
SRE402-8P4D1	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4021 Lower	2	14-Sep-18	17-Sep-18	7
SRE401-8P4D1	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4011 Lower	2	18-Sep-18	19-Sep-18	7
SRE405-8P4D25	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4052 Upper	2	20-Sep-18	21-Sep-18	7
SRE404-8P4D25	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4042 Upper	2	24-Sep-18	25-Sep-18	7
SRE403-8P4D25	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4032 Upper	2	26-Sep-18	27-Sep-18	7
SRE402-8P4D25	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4022 Upper	2	28-Sep-18	01-Oct-18	7
SRE401-8P4D25	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4012 Upper	2	02-Oct-18	03-Oct-18	7
SRE450-8P4D1	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4501 Lower	2	04-Oct-18	05-Oct-18	7
SRE449-8P4D1	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4491 Lower	2	08-Oct-18	09-Oct-18	7
SRE450-8P4D25	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4502 Upper	2	10-Oct-18	11-Oct-18	7
SRE449-8P4D25	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4492 Upper	2	12-Oct-18	15-Oct-18	7
SRE448-8P4D1	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4481 Lower	2	18-Oct-18	19-Oct-18	9
SRE447-8P4D1	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4471 Lower	2	22-Oct-18	23-Oct-18	9
SRE446-8P4D1	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4461 Lower	2	24-Oct-18	25-Oct-18	9
SRE445-8P4D1	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4451 Lower	2	26-Oct-18	29-Oct-18	9
SRE448-8P4D25	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4482 Upper	2	30-Oct-18	31-Oct-18	9
SRE447-8P4D25	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4472 Upper	2	01-Nov-18	02-Nov-18	9
SRE446-8P4D25	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4462 Upper	2	05-Nov-18	06-Nov-18	9
SRE445-8P4D25	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4452 Upper	2	07-Nov-18	08-Nov-18	9
SRD444-8P4D1	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4441 Lower	2	09-Nov-18	13-Nov-18	9
SRD443-8P4D1	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4431 Lower	2	14-Nov-18	15-Nov-18	9
SRD442-8P4D1	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4421 Lower	2	16-Nov-18	19-Nov-18	9
SRD441-8P4D1	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4411 Lower	2	20-Nov-18	21-Nov-18	9
SRD444-8P4D25	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4442 Upper	2	26-Nov-18	27-Nov-18	9
SRD443-8P4D25	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4432 Upper	2	28-Nov-18	29-Nov-18	24
SRD442-8P4D25	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4422 Upper	2	30-Nov-18	03-Dec-18	24
SRD441-8P4D25	Steel Roof Truss Columns - Jobsite Preassembly - Seq 4412 Upper	2	04-Dec-18	05-Dec-18	24
SRA419-8P4D2	Steel Roof Truss Columns - Erect/Set - Seq 4191 Lower	1	09-Aug-18	09-Aug-18	7
SRA420-8P4D2	Steel Roof Truss Columns - Erect/Set - Seq 4201 Lower	1	10-Aug-18	10-Aug-18	7
SRA420-8P4D3	Steel Roof Truss Columns - Infill - Seq 6201 Lower	1	10-Aug-18	10-Aug-18	7
SRB421-8P4D2	Steel Roof Truss Columns - Erect/Set - Seq 4211 Lower	1	13-Aug-18	13-Aug-18	7
SRB421-8P4D3	Steel Roof Truss Columns - Infill - Seq 6211 Lower	1	13-Aug-18	13-Aug-18	7
SRA418-8P4D2	Steel Roof Truss Columns - Erect/Set - Seq 4181 Lower	1	14-Aug-18	14-Aug-18	7
SRA418-8P4D3	Steel Roof Truss Columns - Infill - Seq 6191 Lower	1	14-Aug-18	14-Aug-18	7
SRA417-8P4D2	Steel Roof Truss Columns - Erect/Set - Seq 4171 Lower	1	15-Aug-18	15-Aug-18	7
SRA417-8P4D3	Steel Roof Truss Columns - Infill - Seq 6181 Lower	1	15-Aug-18	15-Aug-18	7
SRA419-8P4D14	Steel Roof Truss Columns - Erect/Set - Seq 4192 Upper	1	16-Aug-18	16-Aug-18	7
SRA420-8P4D14	Steel Roof Truss Columns - Erect/Set - Seq 4202 Upper	1	17-Aug-18	17-Aug-18	7
SRA420-8P4D24	Steel Roof Truss Columns - Infill - Seq 6202 Upper	2	17-Aug-18	20-Aug-18	7
SRB421-8P4D14	Steel Roof Truss Columns - Erect/Set - Seq 4212 Upper	1	21-Aug-18	21-Aug-18	7
SRB421-8P4D24	Steel Roof Truss Columns - Infill - Seq 6212 Upper	2	21-Aug-18	22-Aug-18	7
SRA418-8P4D14	Steel Roof Truss Columns - Erect/Set - Seq 4182 Upper	1	23-Aug-18	23-Aug-18	7
SRA418-8P4D24	Steel Roof Truss Columns - Infill - Seq 6192 Upper	2	23-Aug-18	24-Aug-18	7
SRA417-8P4D14	Steel Roof Truss Columns - Erect/Set - Seq 4172 Upper	1	27-Aug-18	27-Aug-18	7
SRA417-8P4D24	Steel Roof Truss Columns - Infill - Seq 6182 Upper	2	27-Aug-18	28-Aug-18	7
SRF408-8P4D2	Steel Roof Truss Columns - Erect/Set - Seq 4081 Lower	1	29-Aug-18	29-Aug-18	7
SRF407-8P4D2	Steel Roof Truss Columns - Erect/Set - Seq 4071 Lower	1	30-Aug-18	30-Aug-18	7
SRF407-8P4D3	Steel Roof Truss Columns - Infill - Seq 6071 Lower	1	30-Aug-18	30-Aug-18	7
SRE406-8P4D2	Steel Roof Truss Columns - Erect/Set - Seq 4061 Lower	1	31-Aug-18	31-Aug-18	7
SRE406-8P4D3	Steel Roof Truss Columns - Infill - Seq 6061 Lower	1	31-Aug-18	31-Aug-18	7
SRF409-8P4D2	Steel Roof Truss Columns - Erect/Set - Seq 4091 Lower	1	04-Sep-18	04-Sep-18	7
SRF409-8P4D3	Steel Roof Truss Columns - Infill - Seq 6081 Lower	1	04-Sep-18	04-Sep-18	7
SRF410-8P4D2	Steel Roof Truss Columns - Erect/Set - Seq 4101 Lower	1	05-Sep-18	05-Sep-18	7
SRF410-8P4D3	Steel Roof Truss Columns - Infill - Seq 6091 Lower	1	05-Sep-18	05-Sep-18	7
SRF408-8P4D14	Steel Roof Truss Columns - Erect/Set - Seq 4082 Upper	1	06-Sep-18	06-Sep-18	7

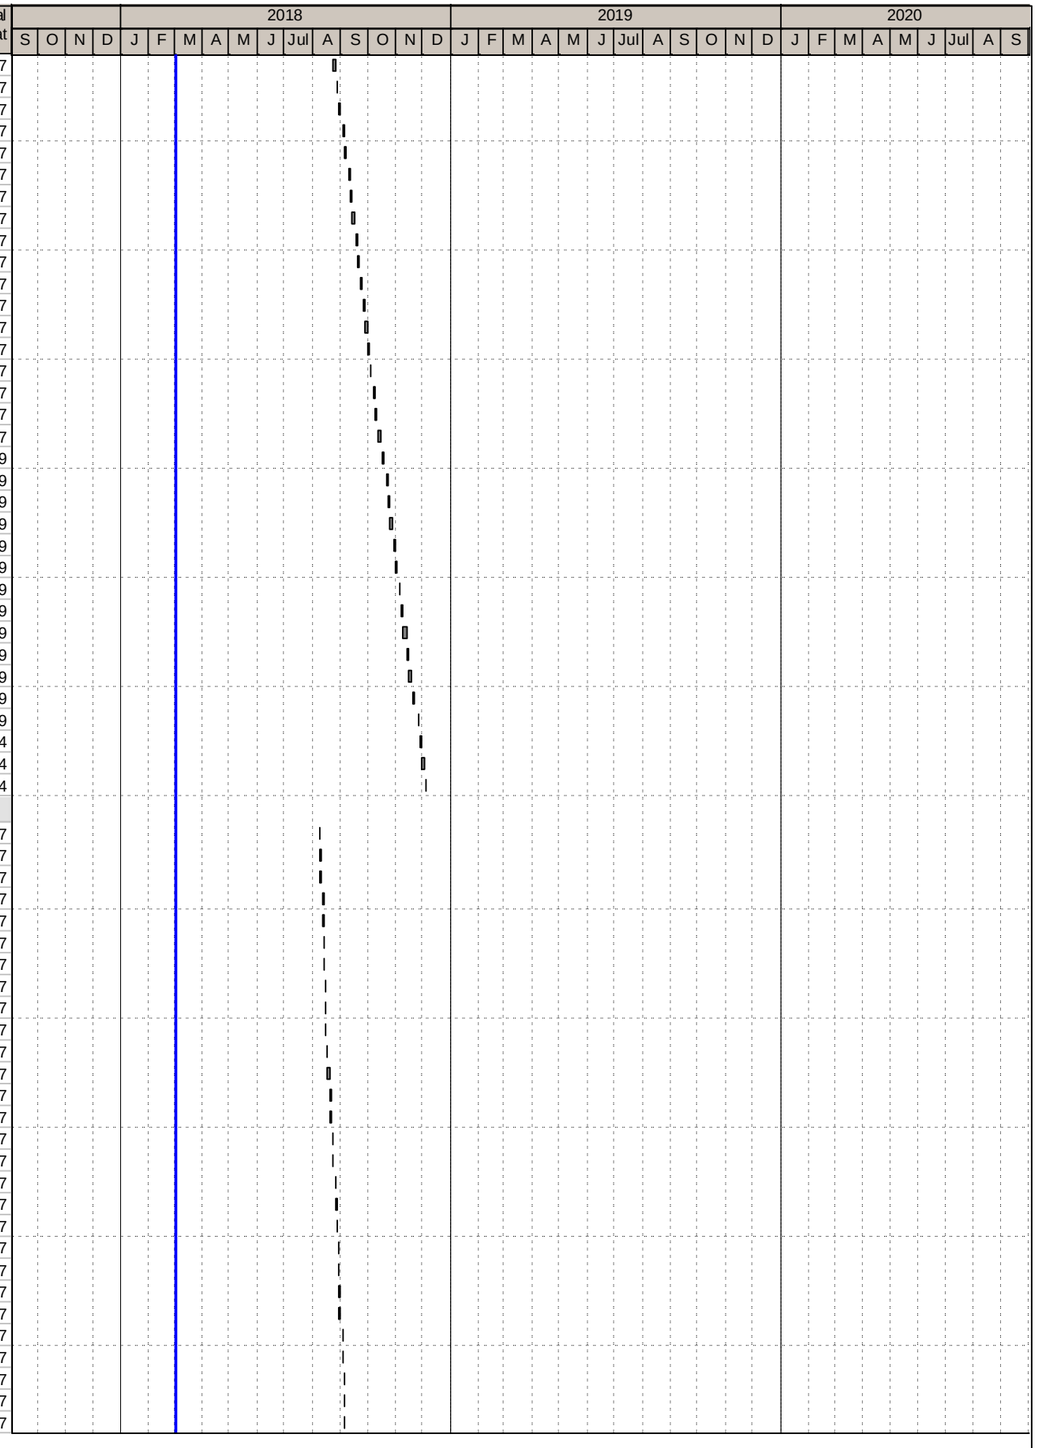

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
SRF407-8P4D14	Steel Roof Truss Columns - Erect/Set - Seq 4072 Upper	1	07-Sep-18	07-Sep-18	7
SRF407-8P4D24	Steel Roof Truss Columns - Infill - Seq 6072 Upper	2	07-Sep-18	10-Sep-18	7
SRE406-8P4D14	Steel Roof Truss Columns - Erect/Set - Seq 4062 Upper	1	11-Sep-18	11-Sep-18	7
SRE406-8P4D24	Steel Roof Truss Columns - Infill - Seq 6062 Upper	2	11-Sep-18	12-Sep-18	7
SRF409-8P4D14	Steel Roof Truss Columns - Erect/Set - Seq 4092 Upper	1	13-Sep-18	13-Sep-18	7
SRF409-8P4D24	Steel Roof Truss Columns - Infill - Seq 6082 Upper	2	13-Sep-18	14-Sep-18	7
SRF410-8P4D14	Steel Roof Truss Columns - Erect/Set - Seq 4102 Upper	1	17-Sep-18	17-Sep-18	7
SRF410-8P4D24	Steel Roof Truss Columns - Infill - Seq 6092 Upper	2	17-Sep-18	18-Sep-18	7
SRE405-8P4D2	Steel Roof Truss Columns - Erect/Set - Seq 4051 Lower	1	19-Sep-18	19-Sep-18	7
SRE405-8P4D3	Steel Roof Truss Columns - Infill - Seq 6051 Lower	1	19-Sep-18	19-Sep-18	7
SRE404-8P4D2	Steel Roof Truss Columns - Erect/Set - Seq 4041 Lower	1	20-Sep-18	20-Sep-18	7
SRE404-8P4D3	Steel Roof Truss Columns - Infill - Seq 6041 Lower	1	20-Sep-18	20-Sep-18	7
SRE403-8P4D2	Steel Roof Truss Columns - Erect/Set - Seq 4031 Lower	1	21-Sep-18	21-Sep-18	7
SRE403-8P4D3	Steel Roof Truss Columns - Infill - Seq 6031 Lower	1	21-Sep-18	21-Sep-18	7
SRE402-8P4D2	Steel Roof Truss Columns - Erect/Set - Seq 4021 Lower	1	24-Sep-18	24-Sep-18	7
SRE402-8P4D3	Steel Roof Truss Columns - Infill - Seq 6021 Lower	1	24-Sep-18	24-Sep-18	7
SRE401-8P4D2	Steel Roof Truss Columns - Erect/Set - Seq 4011 Lower	1	25-Sep-18	25-Sep-18	7
SRE401-8P4D3	Steel Roof Truss Columns - Infill - Seq 6011 Lower	1	25-Sep-18	25-Sep-18	7
SRE405-8P4D14	Steel Roof Truss Columns - Erect/Set - Seq 4052 Upper	1	26-Sep-18	26-Sep-18	7
SRE405-8P4D24	Steel Roof Truss Columns - Infill - Seq 6052 Upper	2	26-Sep-18	27-Sep-18	7
SRE404-8P4D14	Steel Roof Truss Columns - Erect/Set - Seq 4042 Upper	1	28-Sep-18	28-Sep-18	7
SRE404-8P4D24	Steel Roof Truss Columns - Infill - Seq 6042 Upper	2	28-Sep-18	01-Oct-18	7
SRE403-8P4D14	Steel Roof Truss Columns - Erect/Set - Seq 4032 Upper	1	02-Oct-18	02-Oct-18	7
SRE403-8P4D24	Steel Roof Truss Columns - Infill - Seq 6032 Upper	2	02-Oct-18	03-Oct-18	7
SRE402-8P4D14	Steel Roof Truss Columns - Erect/Set - Seq 4022 Upper	1	04-Oct-18	04-Oct-18	7
SRE402-8P4D24	Steel Roof Truss Columns - Infill - Seq 6022 Upper	2	04-Oct-18	05-Oct-18	7
SRE401-8P4D14	Steel Roof Truss Columns - Erect/Set - Seq 4012 Upper	1	08-Oct-18	08-Oct-18	7
SRE401-8P4D24	Steel Roof Truss Columns - Infill - Seq 6012 Upper	2	08-Oct-18	09-Oct-18	7
SRE450-8P4D2	Steel Roof Truss Columns - Erect/Set - Seq 4501 Lower	1	10-Oct-18	10-Oct-18	7
SRE450-8P4D3	Steel Roof Truss Columns - Infill - Seq 6501 Lower	1	10-Oct-18	10-Oct-18	7
SRE449-8P4D2	Steel Roof Truss Columns - Erect/Set - Seq 4491 Lower	1	11-Oct-18	11-Oct-18	7
SRE449-8P4D3	Steel Roof Truss Columns - Infill - Seq 6491 Lower	1	11-Oct-18	11-Oct-18	7
SRE450-8P4D14	Steel Roof Truss Columns - Erect/Set - Seq 4502 Upper	1	12-Oct-18	12-Oct-18	7
SRE450-8P4D24	Steel Roof Truss Columns - Infill - Seq 6502 Upper	2	12-Oct-18	15-Oct-18	7
SRE449-8P4D14	Steel Roof Truss Columns - Erect/Set - Seq 4492 Upper	1	16-Oct-18	16-Oct-18	7
SRE449-8P4D24	Steel Roof Truss Columns - Infill - Seq 6492 Upper	2	16-Oct-18	17-Oct-18	7
SRE448-8P4D2	Steel Roof Truss Columns - Erect/Set - Seq 4481 Lower	1	01-Nov-18	01-Nov-18	8
SRE448-8P4D3	Steel Roof Truss Columns - Infill - Seq 6481 Lower	1	01-Nov-18	01-Nov-18	8
SRE447-8P4D2	Steel Roof Truss Columns - Erect/Set - Seq 4471 Lower	1	02-Nov-18	02-Nov-18	8
SRE447-8P4D3	Steel Roof Truss Columns - Infill - Seq 6471 Lower	1	02-Nov-18	02-Nov-18	8
SRE446-8P4D2	Steel Roof Truss Columns - Erect/Set - Seq 4461 Lower	1	05-Nov-18	05-Nov-18	8
SRE446-8P4D3	Steel Roof Truss Columns - Infill - Seq 6461 Lower	1	05-Nov-18	05-Nov-18	8
SRE445-8P4D2	Steel Roof Truss Columns - Erect/Set - Seq 4451 Lower	1	06-Nov-18	06-Nov-18	8
SRE445-8P4D3	Steel Roof Truss Columns - Infill - Seq 6451 Lower	1	06-Nov-18	06-Nov-18	14
SRE448-8P4D14	Steel Roof Truss Columns - Erect/Set - Seq 4482 Upper	1	07-Nov-18	07-Nov-18	8
SRE448-8P4D24	Steel Roof Truss Columns - Infill - Seq 6482 Upper	2	07-Nov-18	08-Nov-18	8
SRE447-8P4D14	Steel Roof Truss Columns - Erect/Set - Seq 4472 Upper	1	09-Nov-18	09-Nov-18	8
SRE447-8P4D24	Steel Roof Truss Columns - Infill - Seq 6472 Upper	2	09-Nov-18	13-Nov-18	8
SRE446-8P4D14	Steel Roof Truss Columns - Erect/Set - Seq 4462 Upper	1	14-Nov-18	14-Nov-18	8
SRE446-8P4D24	Steel Roof Truss Columns - Infill - Seq 6462 Upper	2	14-Nov-18	15-Nov-18	8
SRE445-8P4D14	Steel Roof Truss Columns - Erect/Set - Seq 4452 Upper	1	16-Nov-18	16-Nov-18	8
SRE445-8P4D24	Steel Roof Truss Columns - Infill - Seq 6452 Upper	2	16-Nov-18	19-Nov-18	8
SRD444-8P4D2	Steel Roof Truss Columns - Erect/Set - Seq 4441 Lower	1	20-Nov-18	20-Nov-18	9
SRD444-8P4D3	Steel Roof Truss Columns - Infill - Seq 6441 Lower	1	20-Nov-18	20-Nov-18	9
SRD443-8P4D2	Steel Roof Truss Columns - Erect/Set - Seq 4431 Lower	1	21-Nov-18	21-Nov-18	9
SRD443-8P4D3	Steel Roof Truss Columns - Infill - Seq 6431 Lower	1	21-Nov-18	21-Nov-18	9
SRD442-8P4D2	Steel Roof Truss Columns - Erect/Set - Seq 4421 Lower	1	26-Nov-18	26-Nov-18	9
SRD442-8P4D3	Steel Roof Truss Columns - Infill - Seq 6421 Lower	1	26-Nov-18	26-Nov-18	9
SRD441-8P4D2	Steel Roof Truss Columns - Erect/Set - Seq 4411 Lower	1	27-Nov-18	27-Nov-18	9
SRD441-8P4D3	Steel Roof Truss Columns - Infill - Seq 6411 Lower	1	27-Nov-18	27-Nov-18	9
SRD444-8P4D14	Steel Roof Truss Columns - Erect/Set - Seq 4442 Upper	1	28-Nov-18	28-Nov-18	9
SRD444-8P4D24	Steel Roof Truss Columns - Infill - Seq 6442 Upper	2	28-Nov-18	29-Nov-18	9
SRD443-8P4D14	Steel Roof Truss Columns - Erect/Set - Seq 4432 Upper	1	30-Nov-18	30-Nov-18	24
SRD443-8P4D24	Steel Roof Truss Columns - Infill - Seq 6432 Upper	2	30-Nov-18	03-Dec-18	24

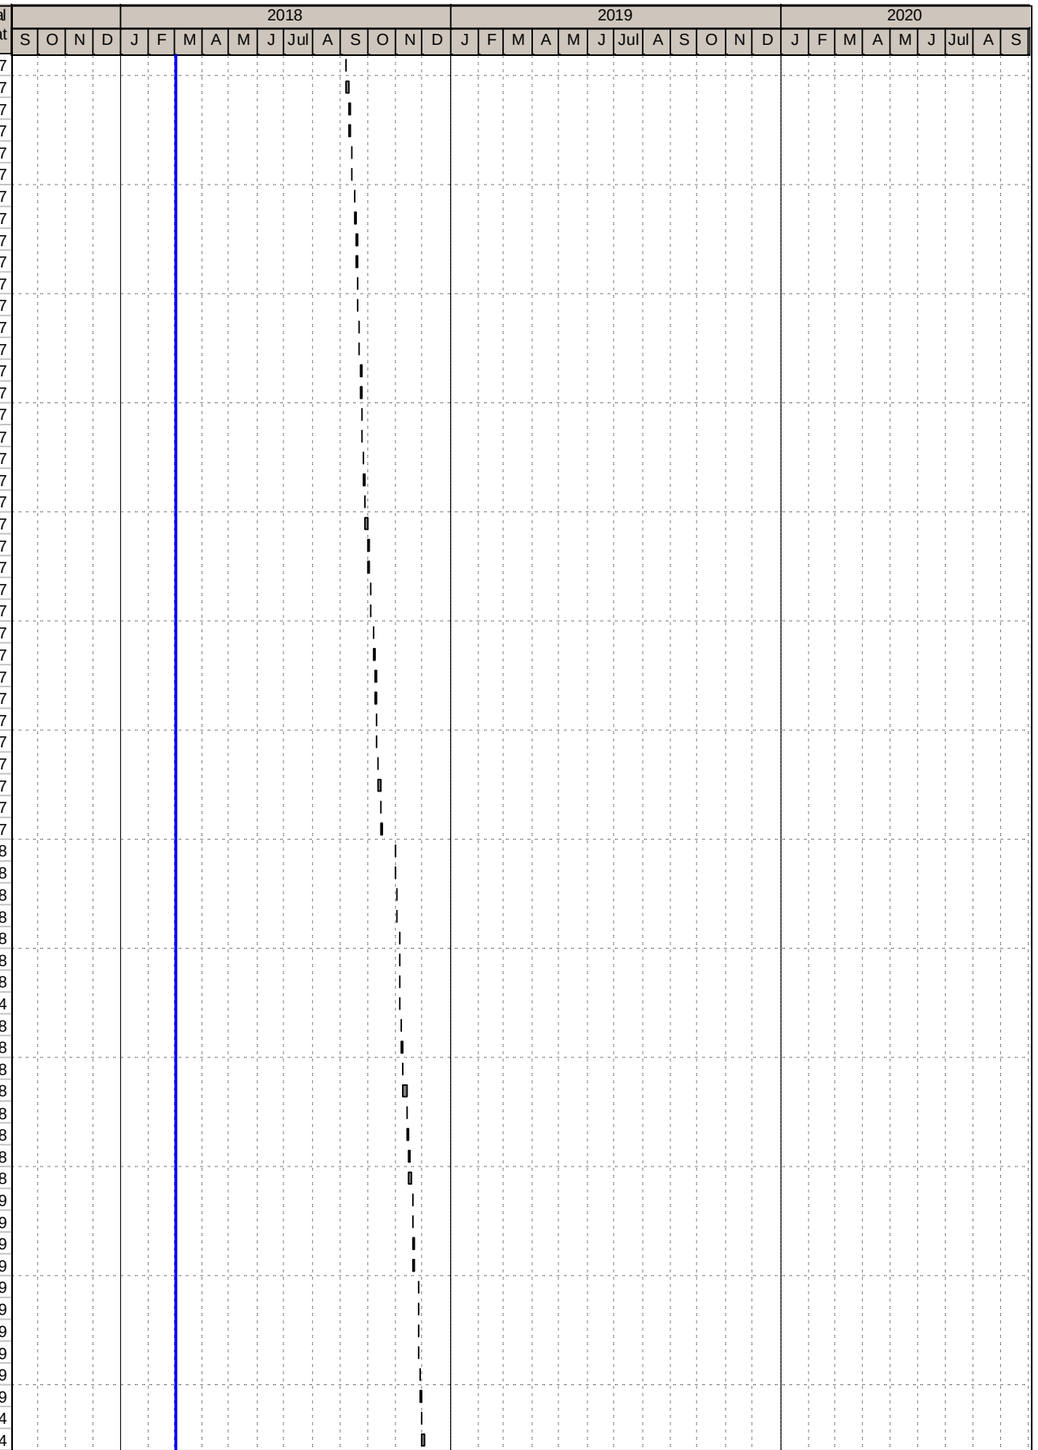

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
SRD442-8P4D14	Steel Roof Truss Columns - Erect/Set - Seq 4422 Upper	1	04-Dec-18	04-Dec-18	24
SRD442-8P4D24	Steel Roof Truss Columns - Infill - Seq 6422 Upper	2	04-Dec-18	05-Dec-18	24
SRD441-8P4D14	Steel Roof Truss Columns - Erect/Set - Seq 4412 Upper	1	06-Dec-18	06-Dec-18	24
SRD441-8P4D24	Steel Roof Truss Columns - Infill - Seq 6412 Upper	2	06-Dec-18	07-Dec-18	24
SRB422-8P4D2	Steel Roof Truss Columns - Erect/Set - Seq 4221 Lower	1	05-Sep-18	05-Sep-18	10
SRB422-8P4D3	Steel Roof Truss Columns - Infill - Seq 6221 Lower	1	05-Sep-18	05-Sep-18	10
SRB423-8P4D2	Steel Roof Truss Columns - Erect/Set - Seq 4231 Lower	1	06-Sep-18	06-Sep-18	10
SRB423-8P4D3	Steel Roof Truss Columns - Infill - Seq 6231 Lower	1	06-Sep-18	06-Sep-18	10
SRB424-8P4D2	Steel Roof Truss Columns - Erect/Set - Seq 4241 Lower	1	07-Sep-18	07-Sep-18	10
SRB424-8P4D3	Steel Roof Truss Columns - Infill - Seq 6241 Lower	1	07-Sep-18	07-Sep-18	10
SRB425-8P4D2	Steel Roof Truss Columns - Erect/Set - Seq 4251 Lower	1	10-Sep-18	10-Sep-18	10
SRB425-8P4D3	Steel Roof Truss Columns - Infill - Seq 6251 Lower	1	10-Sep-18	10-Sep-18	10
SRB422-8P4D14	Steel Roof Truss Columns - Erect/Set - Seq 4222 Upper	1	11-Sep-18	11-Sep-18	10
SRB422-8P4D24	Steel Roof Truss Columns - Infill - Seq 6222 Upper	2	11-Sep-18	12-Sep-18	10
SRB423-8P4D14	Steel Roof Truss Columns - Erect/Set - Seq 4232 Upper	1	13-Sep-18	13-Sep-18	10
SRB423-8P4D24	Steel Roof Truss Columns - Infill - Seq 6232 Upper	2	13-Sep-18	14-Sep-18	10
SRB424-8P4D14	Steel Roof Truss Columns - Erect/Set - Seq 4242 Upper	1	17-Sep-18	17-Sep-18	12
SRB424-8P4D24	Steel Roof Truss Columns - Infill - Seq 6242 Upper	2	17-Sep-18	18-Sep-18	12
SRB425-8P4D14	Steel Roof Truss Columns - Erect/Set - Seq 4252 Upper	1	19-Sep-18	19-Sep-18	12
SRB425-8P4D24	Steel Roof Truss Columns - Infill - Seq 6252 Upper	2	19-Sep-18	20-Sep-18	12
SRB426-8P4D2	Steel Roof Truss Columns - Erect/Set - Seq 4261 Lower	1	21-Sep-18	21-Sep-18	21
SRB426-8P4D3	Steel Roof Truss Columns - Infill - Seq 6261 Lower	1	21-Sep-18	21-Sep-18	21
SRB427-8P4D2	Steel Roof Truss Columns - Erect/Set - Seq 4271 Lower	1	24-Sep-18	24-Sep-18	21
SRB427-8P4D3	Steel Roof Truss Columns - Infill - Seq 6271 Lower	1	24-Sep-18	24-Sep-18	21
SRB428-8P4D2	Steel Roof Truss Columns - Erect/Set - Seq 4281 Lower	1	25-Sep-18	25-Sep-18	21
SRB428-8P4D3	Steel Roof Truss Columns - Infill - Seq 6281 Lower	1	25-Sep-18	25-Sep-18	21
SRB426-8P4D14	Steel Roof Truss Columns - Erect/Set - Seq 4262 Upper	1	26-Sep-18	26-Sep-18	21
SRB426-8P4D24	Steel Roof Truss Columns - Infill - Seq 6262 Upper	2	26-Sep-18	27-Sep-18	21
SRB427-8P4D14	Steel Roof Truss Columns - Erect/Set - Seq 4272 Upper	1	28-Sep-18	28-Sep-18	21
SRB427-8P4D24	Steel Roof Truss Columns - Infill - Seq 6272 Upper	2	28-Sep-18	01-Oct-18	21
SRB428-8P4D14	Steel Roof Truss Columns - Erect/Set - Seq 4282 Upper	1	02-Oct-18	02-Oct-18	21
SRB428-8P4D24	Steel Roof Truss Columns - Infill - Seq 6282 Upper	2	02-Oct-18	03-Oct-18	21
SRB429-8P4D2	Steel Roof Truss Columns - Erect/Set - Seq 4291 Lower	1	19-Oct-18	19-Oct-18	7
SRB429-8P4D3	Steel Roof Truss Columns - Infill - Seq 6291 Lower	1	19-Oct-18	19-Oct-18	7
SRB430-8P4D2	Steel Roof Truss Columns - Erect/Set - Seq 4301 Lower	1	22-Oct-18	22-Oct-18	7
SRB430-8P4D3	Steel Roof Truss Columns - Infill - Seq 6301 Lower	1	22-Oct-18	22-Oct-18	7
SRB431-8P4D2	Steel Roof Truss Columns - Erect/Set - Seq 4311 Lower	1	23-Oct-18	23-Oct-18	7
SRB431-8P4D3	Steel Roof Truss Columns - Infill - Seq 6311 Lower	1	23-Oct-18	23-Oct-18	7
SRB429-8P4D14	Steel Roof Truss Columns - Erect/Set - Seq 4292 Upper	1	24-Oct-18	24-Oct-18	7
SRB429-8P4D24	Steel Roof Truss Columns - Infill - Seq 6292 Upper	2	24-Oct-18	25-Oct-18	7
SRB430-8P4D14	Steel Roof Truss Columns - Erect/Set - Seq 4302 Upper	1	26-Oct-18	26-Oct-18	7
SRB430-8P4D24	Steel Roof Truss Columns - Infill - Seq 6302 Upper	2	26-Oct-18	29-Oct-18	7
SRB431-8P4D14	Steel Roof Truss Columns - Erect/Set - Seq 4312 Upper	1	30-Oct-18	30-Oct-18	7
SRB431-8P4D24	Steel Roof Truss Columns - Infill - Seq 6312 Upper	2	30-Oct-18	31-Oct-18	7
SRB432-8P4D2	Steel Roof Truss Columns - Erect/Set - Seq 4321 Lower	1	01-Nov-18	01-Nov-18	7
SRB432-8P4D3	Steel Roof Truss Columns - Infill - Seq 6321 Lower	1	01-Nov-18	01-Nov-18	7
SRC433-8P4D2	Steel Roof Truss Columns - Erect/Set - Seq 4331 Lower	1	02-Nov-18	02-Nov-18	7
SRC433-8P4D3	Steel Roof Truss Columns - Infill - Seq 6331 Lower	1	02-Nov-18	02-Nov-18	7
SRC434-8P4D2	Steel Roof Truss Columns - Erect/Set - Seq 4341 Lower	1	06-Nov-18	06-Nov-18	6
SRC434-8P4D3	Steel Roof Truss Columns - Infill - Seq 6341 Lower	1	06-Nov-18	06-Nov-18	6
SRC435-8P4D2	Steel Roof Truss Columns - Erect/Set - Seq 4351 Lower	1	09-Nov-18	09-Nov-18	4
SRC435-8P4D3	Steel Roof Truss Columns - Infill - Seq 6351 Lower	1	09-Nov-18	09-Nov-18	4
SRC436-8P4D2	Steel Roof Truss Columns - Erect/Set - Seq 4361 Lower	1	13-Nov-18	13-Nov-18	4
SRC436-8P4D3	Steel Roof Truss Columns - Infill - Seq 6361 Lower	1	13-Nov-18	13-Nov-18	4
SRB432-8P4D14	Steel Roof Truss Columns - Erect/Set - Seq 4322 Upper	1	14-Nov-18	14-Nov-18	4
SRB432-8P4D24	Steel Roof Truss Columns - Infill - Seq 6322 Upper	2	14-Nov-18	15-Nov-18	4
SRC433-8P4D14	Steel Roof Truss Columns - Erect/Set - Seq 4332 Upper	1	16-Nov-18	16-Nov-18	6
SRC433-8P4D24	Steel Roof Truss Columns - Infill - Seq 6332 Upper	2	16-Nov-18	19-Nov-18	6
SRC434-8P4D14	Steel Roof Truss Columns - Erect/Set - Seq 4342 Upper	1	20-Nov-18	20-Nov-18	6
SRC434-8P4D24	Steel Roof Truss Columns - Infill - Seq 6342 Upper	2	20-Nov-18	21-Nov-18	6
SRC435-8P4D14	Steel Roof Truss Columns - Erect/Set - Seq 4352 Upper	1	26-Nov-18	26-Nov-18	6
SRC435-8P4D24	Steel Roof Truss Columns - Infill - Seq 6352 Upper	2	26-Nov-18	27-Nov-18	6

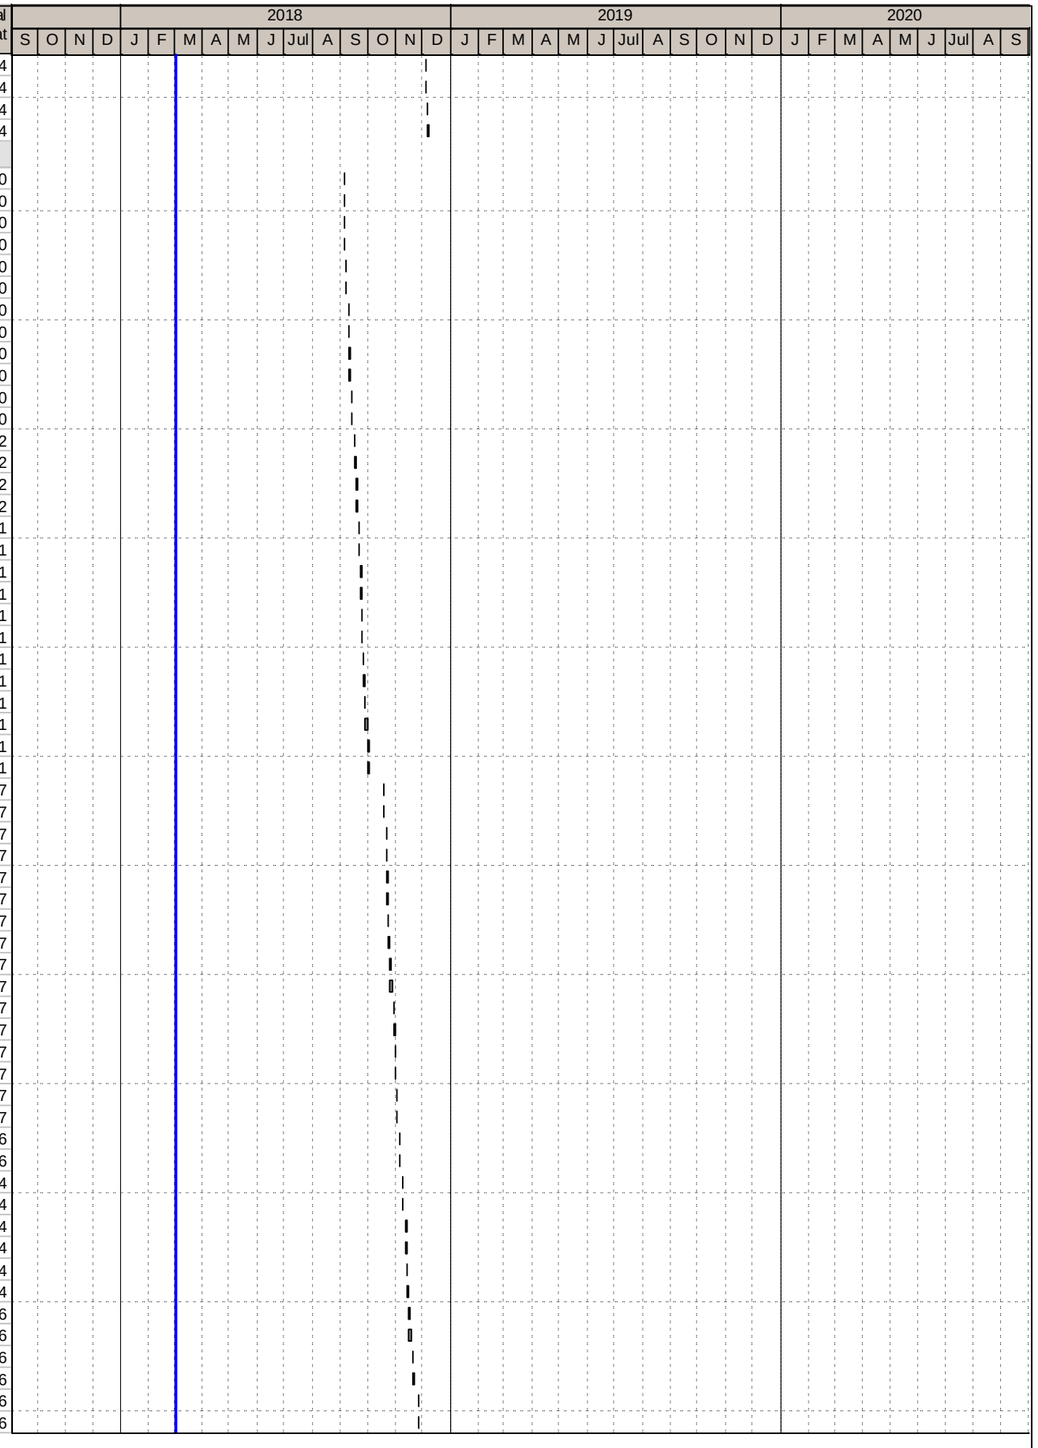

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
SRC436-8P4D14	Steel Roof Truss Columns - Erect/Set - Seq 4362 Upper	1	28-Nov-18	28-Nov-18	10
SRC436-8P4D24	Steel Roof Truss Columns - Infill - Seq 6362 Upper	2	28-Nov-18	29-Nov-18	10
SRB422-8P4D4	Steel Roof Truss Columns - Bolt-up/Detail - Seq 6222	3	11-Sep-18	13-Sep-18	12
SRB423-8P4D4	Steel Roof Truss Columns - Bolt-up/Detail - Seq 6232	3	13-Sep-18	17-Sep-18	10
SRB424-8P4D4	Steel Roof Truss Columns - Bolt-up/Detail - Seq 6242	3	17-Sep-18	19-Sep-18	14
SRB425-8P4D4	Steel Roof Truss Columns - Bolt-up/Detail - Seq 6252	3	19-Sep-18	21-Sep-18	12
SRB426-8P4D4	Steel Roof Truss Columns - Bolt-up/Detail - Seq 6262	3	26-Sep-18	28-Sep-18	25
SRB427-8P4D4	Steel Roof Truss Columns - Bolt-up/Detail - Seq 6272	3	28-Sep-18	02-Oct-18	23
SRB428-8P4D4	Steel Roof Truss Columns - Bolt-up/Detail - Seq 6282	3	02-Oct-18	04-Oct-18	24
SRB429-8P4D4	Steel Roof Truss Columns - Bolt-up/Detail - Seq 6292	3	24-Oct-18	26-Oct-18	12
SRB430-8P4D4	Steel Roof Truss Columns - Bolt-up/Detail - Seq 6302	3	26-Oct-18	30-Oct-18	10
SRB431-8P4D4	Steel Roof Truss Columns - Bolt-up/Detail - Seq 6312	3	30-Oct-18	01-Nov-18	8
SRB432-8P4D4	Steel Roof Truss Columns - Bolt-up/Detail - Seq 6322	3	14-Nov-18	16-Nov-18	4
SRC433-8P4D4	Steel Roof Truss Columns - Bolt-up/Detail - Seq 6332	3	16-Nov-18	20-Nov-18	10
SRC434-8P4D4	Steel Roof Truss Columns - Bolt-up/Detail - Seq 6342	3	20-Nov-18	26-Nov-18	8
SRC435-8P4D4	Steel Roof Truss Columns - Bolt-up/Detail - Seq 6352	3	26-Nov-18	28-Nov-18	6
SRC436-8P4D4	Steel Roof Truss Columns - Bolt-up/Detail - Seq 6362	3	28-Nov-18	30-Nov-18	10
SRA419-8P4D4	Steel Roof Truss Columns - Bolt-up/Detail - Seq 6192	3	16-Aug-18	20-Aug-18	37
SRA420-8P4D4	Steel Roof Truss Columns - Bolt-up/Detail - Seq 6202	3	17-Aug-18	21-Aug-18	36
SRB421-8P4D4	Steel Roof Truss Columns - Bolt-up/Detail - Seq 6212	3	21-Aug-18	23-Aug-18	26
SRA418-8P4D4	Steel Roof Truss Columns - Bolt-up/Detail - Seq 6182	3	23-Aug-18	27-Aug-18	27
SRA417-8P4D4	Steel Roof Truss Columns - Bolt-up/Detail - Seq 6172	3	27-Aug-18	29-Aug-18	20
SRF408-8P4D4	Steel Roof Truss Columns - Bolt-up/Detail - Seq 6082	3	06-Sep-18	10-Sep-18	18
SRF407-8P4D4	Steel Roof Truss Columns - Bolt-up/Detail - Seq 6072	3	07-Sep-18	11-Sep-18	27
SRE406-8P4D4	Steel Roof Truss Columns - Bolt-up/Detail - Seq 6062	3	11-Sep-18	13-Sep-18	24
SRF409-8P4D4	Steel Roof Truss Columns - Bolt-up/Detail - Seq 6092	3	13-Sep-18	17-Sep-18	13
SRF410-8P4D4	Steel Roof Truss Columns - Bolt-up/Detail - Seq 6102	3	17-Sep-18	19-Sep-18	11
SRE405-8P4D4	Steel Roof Truss Columns - Bolt-up/Detail - Seq 6052	3	26-Sep-18	28-Sep-18	13
SRE404-8P4D4	Steel Roof Truss Columns - Bolt-up/Detail - Seq 6042	3	28-Sep-18	02-Oct-18	11
SRE403-8P4D4	Steel Roof Truss Columns - Bolt-up/Detail - Seq 6032	3	02-Oct-18	04-Oct-18	9
SRE402-8P4D4	Steel Roof Truss Columns - Bolt-up/Detail - Seq 6022	3	04-Oct-18	08-Oct-18	12
SRE401-8P4D4	Steel Roof Truss Columns - Bolt-up/Detail - Seq 6012	3	08-Oct-18	10-Oct-18	10
SRE450-8P4D4	Steel Roof Truss Columns - Bolt-up/Detail - Seq 6502	3	12-Oct-18	16-Oct-18	9
SRE449-8P4D4	Steel Roof Truss Columns - Bolt-up/Detail - Seq 6492	3	16-Oct-18	18-Oct-18	7
SRE448-8P4D4	Steel Roof Truss Columns - Bolt-up/Detail - Seq 6482	3	07-Nov-18	09-Nov-18	10
SRE447-8P4D4	Steel Roof Truss Columns - Bolt-up/Detail - Seq 6472	3	09-Nov-18	14-Nov-18	8
SRE446-8P4D4	Steel Roof Truss Columns - Bolt-up/Detail - Seq 6462	3	14-Nov-18	16-Nov-18	10
SRE445-8P4D4	Steel Roof Truss Columns - Bolt-up/Detail - Seq 6452	3	16-Nov-18	20-Nov-18	8
SRD444-8P4D4	Steel Roof Truss Columns - Bolt-up/Detail - Seq 6442	3	28-Nov-18	30-Nov-18	9
SRD443-8P4D4	Steel Roof Truss Columns - Bolt-up/Detail - Seq 6432	3	30-Nov-18	04-Dec-18	28
SRD442-8P4D4	Steel Roof Truss Columns - Bolt-up/Detail - Seq 6422	3	04-Dec-18	06-Dec-18	26
SRD441-8P4D4	Steel Roof Truss Columns - Bolt-up/Detail - Seq 6412	3	06-Dec-18	10-Dec-18	24
400 Canopy Roof Lvl					
SRA501-8P4D1	Steel Roof Canopy - Jobsite Preassembly - Seq 5190	10	11-Dec-18	24-Dec-18	14
SRA511-8P4D1	Steel Roof Canopy - Jobsite Preassembly - Seq 5170	10	18-Dec-18	02-Jan-19	14
SRA516-8P4D1	Steel Roof Canopy - Jobsite Preassembly - Seq 5160	10	26-Dec-18	09-Jan-19	14
SRA521-8P4D1	Steel Roof Canopy - Jobsite Preassembly - Seq 5210	10	16-Jan-19	29-Jan-19	11
SRB502-8P4D1	Steel Roof Canopy - Jobsite Preassembly - Seq 5230	10	23-Jan-19	05-Feb-19	12
SRB503-8P4D1	Steel Roof Canopy - Jobsite Preassembly - Seq 5250	10	30-Jan-19	12-Feb-19	13
SRB504-8P4D1	Steel Roof Canopy - Jobsite Preassembly - Seq 5270	10	06-Feb-19	20-Feb-19	14
SRB505-8P4D1	Steel Roof Canopy - Jobsite Preassembly - Seq 5290	10	13-Feb-19	27-Feb-19	15
SRB506-8P4D1	Steel Roof Canopy - Jobsite Preassembly - Seq 5310	10	21-Feb-19	06-Mar-19	16
SRA522-8P4D1	Steel Roof Canopy - Jobsite Preassembly - Seq 5330	10	18-Mar-19	29-Mar-19	9
SRC525-8P4D1	Steel Roof Canopy - Jobsite Preassembly - Seq 5340	10	25-Mar-19	05-Apr-19	9
SRC526-8P4D1	Steel Roof Canopy - Jobsite Preassembly - Seq 5360	10	01-Apr-19	12-Apr-19	9
SRC527-8P4D1	Steel Roof Canopy - Jobsite Preassembly - Seq 5400	10	08-Apr-19	19-Apr-19	9
SRE516-8P4D1	Steel Roof Canopy - Jobsite Preassembly - Seq 5070	10	13-Dec-18	27-Dec-18	17
SRE515-8P4D1	Steel Roof Canopy - Jobsite Preassembly - Seq 5090	10	20-Dec-18	04-Jan-19	17
SRE518-8P4D1	Steel Roof Canopy - Jobsite Preassembly - Seq 5100	10	28-Dec-18	11-Jan-19	17

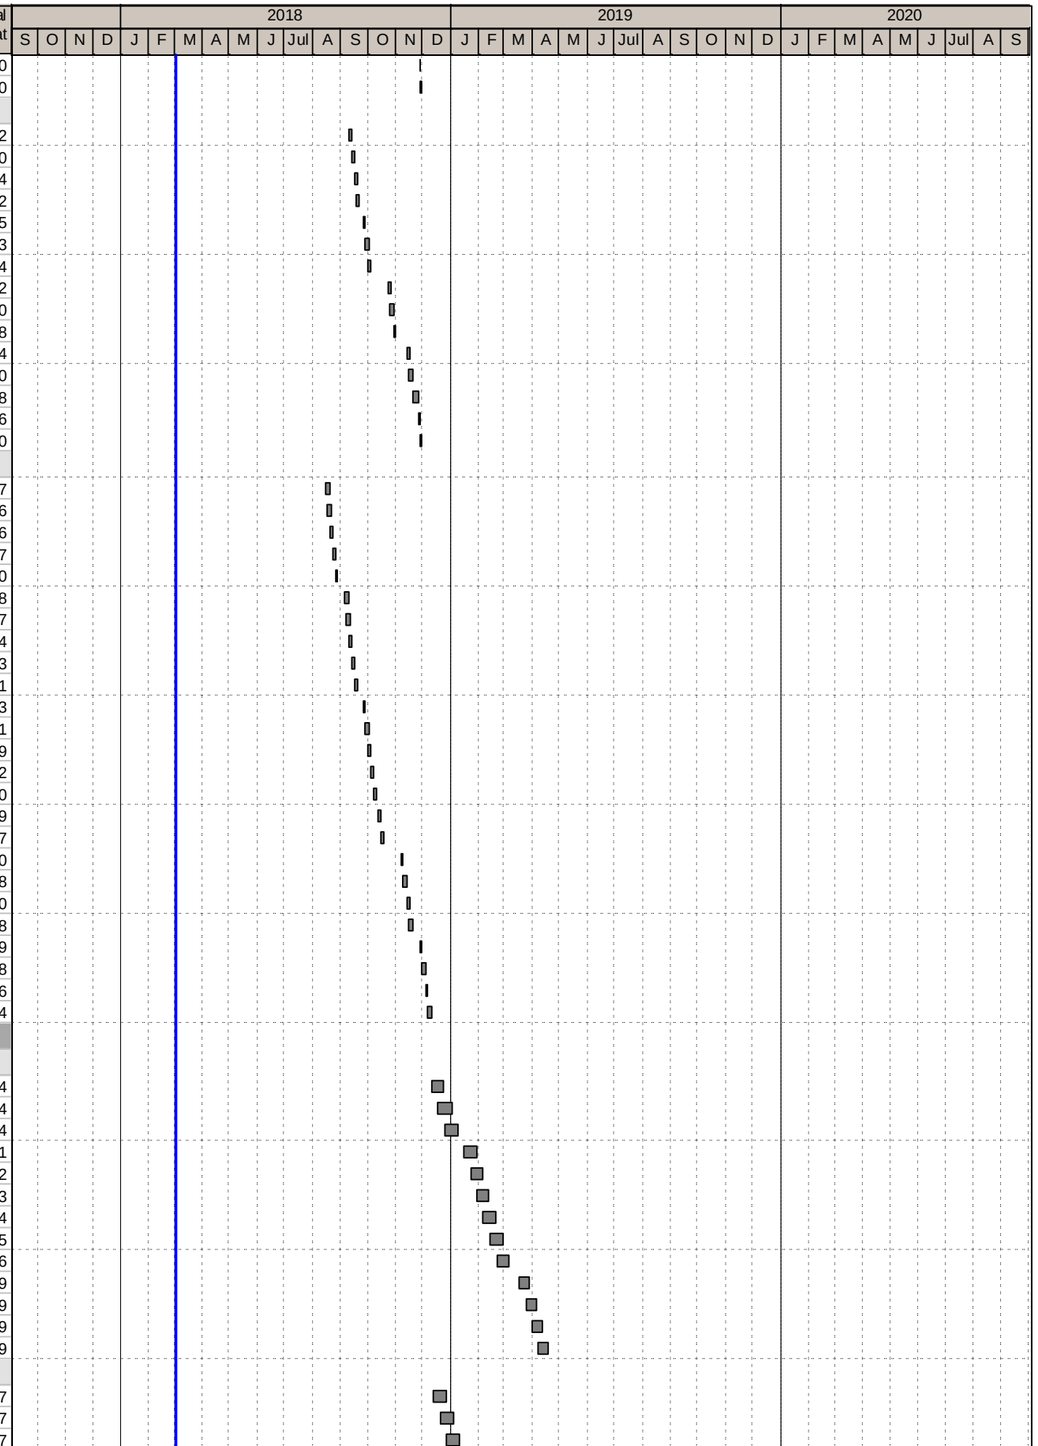

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
SRA523-8P4D1	Steel Roof Canopy - Jobsite Preassembly - Seq 5050	10	21-Jan-19	01-Feb-19	7
SRA512-8P4D1	Steel Roof Canopy - Jobsite Preassembly - Seq 5030	10	28-Jan-19	08-Feb-19	7
SRF513-8P4D1	Steel Roof Canopy - Jobsite Preassembly - Seq 5010	10	04-Feb-19	15-Feb-19	7
SRF514-8P4D1	Steel Roof Canopy - Jobsite Preassembly - Seq 5140	10	11-Feb-19	25-Feb-19	7
SRE517-8P4D1	Steel Roof Canopy - Jobsite Preassembly - Seq 5120	10	19-Feb-19	04-Mar-19	7
SRD520-8P4D1	Steel Roof Canopy - Jobsite Preassembly - Seq 5490	10	26-Feb-19	11-Mar-19	11
SRD510-8P4D1	Steel Roof Canopy - Jobsite Preassembly - Seq 5470	10	05-Mar-19	18-Mar-19	11
SRA524-8P4D1	Steel Roof Canopy - Jobsite Preassembly - Seq 5450	10	12-Mar-19	25-Mar-19	11
SRC507-8P4D1	Steel Roof Canopy - Jobsite Preassembly - Seq 5430	10	21-Mar-19	03-Apr-19	9
SRC508-8P4D1	Steel Roof Canopy - Jobsite Preassembly - Seq 5420	10	28-Mar-19	10-Apr-19	9
SRA501-8P4D2	Steel Roof Canopy - Erect/Set - Seq 5190	1	02-Jan-19	02-Jan-19	16
TRA501-8P4D2	Steel Roof Canopy - Move Crane 5190 to 5170	1	03-Jan-19	03-Jan-19	16
SRA511-8P4D2	Steel Roof Canopy - Erect/Set - Seq 5170	1	08-Jan-19	08-Jan-19	14
TRA511-8P4D2	Steel Roof Canopy - Move Crane 5170 to 5160	1	09-Jan-19	09-Jan-19	14
SRA516-8P4D2	Steel Roof Canopy - Erect/Set - Seq 5160	1	10-Jan-19	10-Jan-19	14
SRA511-8P4D3	Steel Roof Canopy - Infill - Seq 5180	4	08-Jan-19	11-Jan-19	15
TRA516-8P4D2	Steel Roof Canopy - Move Crane 5160 to 5210	1	11-Jan-19	11-Jan-19	23
SRA516-8P4D3	Steel Roof Canopy - Infill - Seq 5160	4	11-Jan-19	16-Jan-19	14
SRA511-8P4D15	Steel Roof Canopy - Erect/Set - Seq 5210	1	06-Feb-19	06-Feb-19	6
TRA511-8P4D15	Steel Roof Canopy - Move Crane 5210 to 5230	1	07-Feb-19	07-Feb-19	10
SRA511-8P4D25	Steel Roof Canopy - Infill - Seq 5200	4	06-Feb-19	11-Feb-19	6
SRB502-8P4D2	Steel Roof Canopy - Erect/Set - Seq 5230	1	12-Feb-19	12-Feb-19	8
TRB502-8P4D2	Steel Roof Canopy - Move Crane 5230 to 5250	1	13-Feb-19	13-Feb-19	12
SRA502-8P4D3	Steel Roof Canopy - Infill - Seq 5220	4	12-Feb-19	15-Feb-19	8
SRB503-8P4D2	Steel Roof Canopy - Erect/Set - Seq 5250	1	19-Feb-19	19-Feb-19	10
TRB503-8P4D2	Steel Roof Canopy - Move Crane 5250 to 5270	1	20-Feb-19	20-Feb-19	14
SRB503-8P4D3	Steel Roof Canopy - Infill - Seq 5240	4	19-Feb-19	22-Feb-19	10
SRB504-8P4D2	Steel Roof Canopy - Erect/Set - Seq 5270	1	25-Feb-19	25-Feb-19	12
TRB504-8P4D2	Steel Roof Canopy - Move Crane 5270 to 5290	1	26-Feb-19	26-Feb-19	16
SRB504-8P4D3	Steel Roof Canopy - Infill - Seq 5260	4	25-Feb-19	28-Feb-19	12
SRB505-8P4D2	Steel Roof Canopy - Erect/Set - Seq 5290	1	01-Mar-19	01-Mar-19	14
TRB505-8P4D2	Steel Roof Canopy - Move Crane 5290 to 5310	1	04-Mar-19	04-Mar-19	18
SRB505-8P4D3	Steel Roof Canopy - Infill - Seq 5280	4	01-Mar-19	06-Mar-19	14
SRB506-8P4D2	Steel Roof Canopy - Erect/Set - Seq 5310	1	07-Mar-19	07-Mar-19	16
TRB506-8P4D2	Steel Roof Canopy - Move Crane 5310 to 5330	1	08-Mar-19	08-Mar-19	28
SRB506-8P4D3	Steel Roof Canopy - Infill - Seq 5300	4	07-Mar-19	12-Mar-19	16
SRB506-8P4D15	Steel Roof Canopy - Erect/Set - Seq 5330	1	05-Apr-19	05-Apr-19	9
TRB506-8P4D15	Steel Roof Canopy - Move Crane 5330 to 5340	1	08-Apr-19	08-Apr-19	11
SRB506-8P4D25	Steel Roof Canopy - Infill - Seq 5320	4	05-Apr-19	10-Apr-19	9
SRB525-8P4D2	Steel Roof Canopy - Erect/Set - Seq 5340	1	11-Apr-19	11-Apr-19	9
TRB526-8P4D2	Steel Roof Canopy - Move Crane 5340 to 5360	1	12-Apr-19	12-Apr-19	11
SRB525-8P4D3	Steel Roof Canopy - Infill - Seq 5331	4	11-Apr-19	16-Apr-19	9
SRB526-8P4D2	Steel Roof Canopy - Erect/Set - Seq 5360	2	17-Apr-19	18-Apr-19	9
TRB527-8P4D2	Steel Roof Canopy - Move Crane 5360 to 5400	1	19-Apr-19	19-Apr-19	9
SRB527-8P4D2	Steel Roof Canopy - Erect/Set - Seq 5400	2	22-Apr-19	23-Apr-19	9
SRB526-8P4D3	Steel Roof Canopy - Infill - Seq 5412	3	23-Apr-19	25-Apr-19	9
SRB527-8P4D3	Steel Roof Canopy - Infill - Seq 5372	4	26-Apr-19	01-May-19	9
SRA501-8P4D6	Steel Roof Canopy - Erect - North End Zone Shoring Tower	10	15-Jan-19	28-Jan-19	28
SRE518-8P4D2	Steel Roof Canopy - Erect/Set - Seq 5111 (inside)	3	25-Mar-19	27-Mar-19	6
SRB525-8P4D6	Steel Roof Canopy - Erect - South End Zone Shoring Tower	10	14-Mar-19	27-Mar-19	23
SRE519-8P4D2	Steel Roof Canopy - Erect/Set - Seq 5131 (inside)	4	28-Mar-19	02-Apr-19	6
SRC509-8P4D2	Steel Roof Canopy - Erect/Set - Seq 5411	3	26-Apr-19	30-Apr-19	10
TRC509-8P4D2	Steel Roof Canopy - Erect/Set - Seq 5371	4	02-May-19	07-May-19	9
SRE516-8P4D2	Steel Roof Canopy - Erect/Set - Seq 5070	1	03-Jan-19	03-Jan-19	24
TRE516-8P4D2	Steel Roof Canopy - Move Crane 5070 to 5090	1	04-Jan-19	04-Jan-19	24
SRE515-8P4D2	Steel Roof Canopy - Erect/Set - Seq 5090	1	08-Jan-19	08-Jan-19	23
TRE515-8P4D2	Steel Roof Canopy - Move Crarne 5090 to 5100	1	09-Jan-19	09-Jan-19	25
SRE516-8P4D3	Steel Roof Canopy - Infill - Seq 5080	4	08-Jan-19	11-Jan-19	23
T	Steel Roof Canopy - Erect/Set - Seq 5100	1	14-Jan-19	14-Jan-19	23
T1	Steel Roof Canopy - Move Crane 5100 to 5050	1	15-Jan-19	15-Jan-19	25

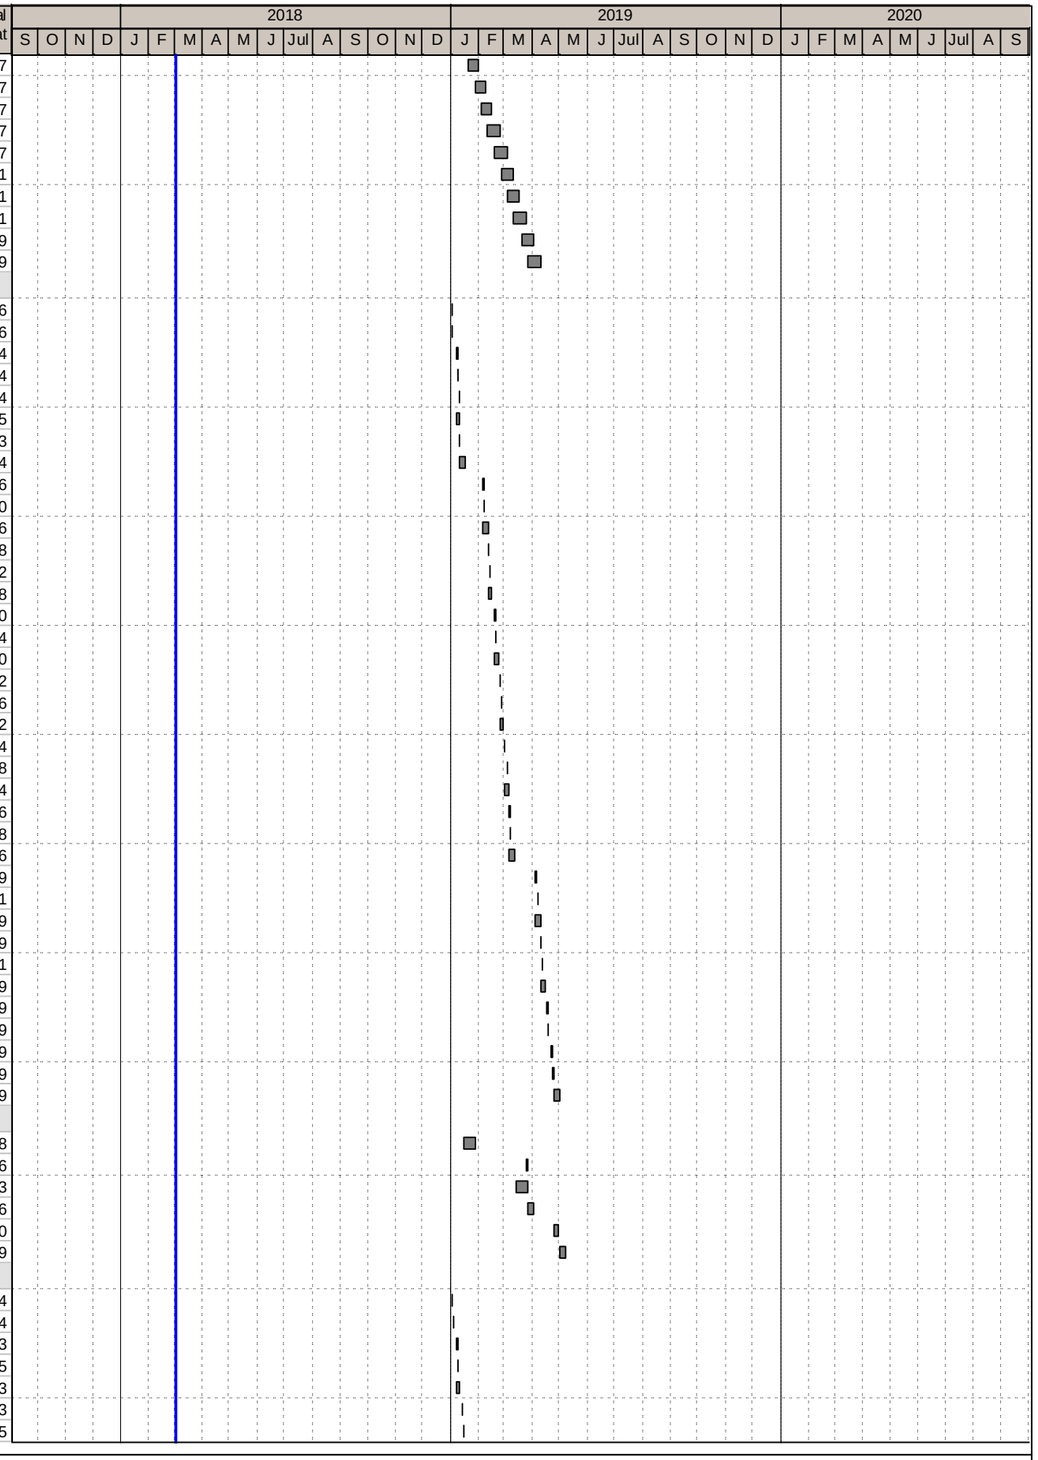

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
TRE516-8P4D3	Steel Roof Canopy - Infill - Seq 5100	4	14-Jan-19	17-Jan-19	23
SRE515-8P4D15	Steel Roof Canopy - Erect/Set - Seq 5050	1	12-Feb-19	12-Feb-19	6
TRE515-8P4D15	Steel Roof Canopy - Move Crane 5050 to 5030	1	13-Feb-19	13-Feb-19	8
SRE516-8P4D15	Steel Roof Canopy - Infill - Seq 5060	4	12-Feb-19	15-Feb-19	6
SRA512-8P4D2	Steel Roof Canopy - Erect/Set - Seq 5030	1	19-Feb-19	19-Feb-19	6
TRA512-8P4D2	Steel Roof Canopy - Move Crane 5030 to 5010	1	20-Feb-19	20-Feb-19	8
SRA512-8P4D3	Steel Roof Canopy - Infill - Seq 5040	4	19-Feb-19	22-Feb-19	6
SRF513-8P4D2	Steel Roof Canopy - Erect/Set - Seq 5010	1	25-Feb-19	25-Feb-19	6
TRF513-8P4D2	Steel Roof Canopy - Move Crane 5010 to 5140	1	26-Feb-19	26-Feb-19	8
SRF513-8P4D3	Steel Roof Canopy - Infill - Seq 5020	4	25-Feb-19	28-Feb-19	6
SRF514-8P4D2	Steel Roof Canopy - Erect/Set - Seq 5140	2	01-Mar-19	04-Mar-19	6
TRF514-8P4D2	Steel Roof Canopy - Move Crane 5140 to 5120	1	05-Mar-19	05-Mar-19	6
SRE517-8P4D2	Steel Roof Canopy - Erect/Set - Seq 5120	2	06-Mar-19	07-Mar-19	6
TRE517-8P4D2	Steel Roof Canopy - Move Crane 5120 to 5490	1	08-Mar-19	08-Mar-19	15
SRF514-8P4D3	Steel Roof Canopy - Infill - Seq 5112 (outside)	3	07-Mar-19	11-Mar-19	6
SRE517-8P4D3	Steel Roof Canopy - Infill - Seq 5132 (outside)	4	07-Mar-19	12-Mar-19	6
SRD520-8P4D2	Steel Roof Canopy - Erect/Set - Seq 5490	1	13-Mar-19	13-Mar-19	13
SRD520-8P4D3	Steel Roof Canopy - Infill - Seq 5500	4	13-Mar-19	18-Mar-19	13
TRE518-8P4D2	Steel Roof Canopy - Move Crane 5490 to 5470	3	14-Mar-19	18-Mar-19	13
SRD510-8P4D2	Steel Roof Canopy - Erect/Set - Seq 5470	1	19-Mar-19	19-Mar-19	13
SRD510-8P4D15	Steel Roof Canopy - Infill - Seq 5480	4	19-Mar-19	22-Mar-19	14
TRE519-8P4D2	Steel Roof Canopy - Move Crane 5470 to 5450	4	20-Mar-19	25-Mar-19	13
SRD521-8P4D2	Steel Roof Canopy - Erect/Set - Seq 5450	1	26-Mar-19	26-Mar-19	13
TRD520-8P4D2	Steel Roof Canopy - Move Crane 5450 to 5430	1	27-Mar-19	27-Mar-19	15
SRD521-8P4D15	Steel Roof Canopy - Infill - Seq 5460	4	26-Mar-19	29-Mar-19	13
SRC507-8P4D2	Steel Roof Canopy - Erect/Set - Seq 5430	1	05-Apr-19	05-Apr-19	9
TRD510-8P4D2	Steel Roof Canopy - Move Crane 5430 to 5420	1	08-Apr-19	08-Apr-19	11
SRC507-8P4D3	Steel Roof Canopy - Infill - Seq 5440	4	05-Apr-19	10-Apr-19	9
SRC508-8P4D2	Steel Roof Canopy - Erect/Set - Seq 5420	1	11-Apr-19	11-Apr-19	9
SRC508-8P4D3	Steel Roof Canopy - Infill - Seq 5421	4	11-Apr-19	16-Apr-19	9
SRA501-8P4D4	Steel Roof Canopy - Bolt-up/Detail - Seq 5190	6	03-Jan-19	10-Jan-19	24
SRA511-8P4D4	Steel Roof Canopy - Bolt-up/Detail - Seq 5170	6	09-Jan-19	16-Jan-19	20
SRA511-8P4D26	Steel Roof Canopy - Bolt-up/Detail - Seq 5180	10	10-Jan-19	23-Jan-19	15
SRA516-8P4D4	Steel Roof Canopy - Bolt-up/Detail - Seq 5160	10	11-Jan-19	24-Jan-19	14
SRA521-8P4D4	Steel Roof Canopy - Bolt-up/Detail - Seq 5210	6	07-Feb-19	14-Feb-19	14
SRB502-8P4D4	Steel Roof Canopy - Bolt-up/Detail - Seq 5230	6	13-Feb-19	21-Feb-19	16
SRA521-8P4D6	Steel Roof Canopy - Bolt-up/Detail - Seq 5200	10	08-Feb-19	22-Feb-19	6
SRB503-8P4D4	Steel Roof Canopy - Bolt-up/Detail - Seq 5250	6	20-Feb-19	27-Feb-19	18
SRB502-8P4D6	Steel Roof Canopy - Bolt-up/Detail - Seq 5220	10	14-Feb-19	28-Feb-19	8
SRB504-8P4D4	Steel Roof Canopy - Bolt-up/Detail - Seq 5270	6	26-Feb-19	05-Mar-19	20
SRB503-8P4D6	Steel Roof Canopy - Bolt-up/Detail - Seq 5240	10	21-Feb-19	06-Mar-19	10
SRB505-8P4D4	Steel Roof Canopy - Bolt-up/Detail - Seq 5290	6	04-Mar-19	11-Mar-19	22
SRB504-8P4D6	Steel Roof Canopy - Bolt-up/Detail - Seq 5260	10	27-Feb-19	12-Mar-19	12
SRB506-8P4D4	Steel Roof Canopy - Bolt-up/Detail - Seq 5310	6	08-Mar-19	15-Mar-19	24
SRB505-8P4D6	Steel Roof Canopy - Bolt-up/Detail - Seq 5280	10	05-Mar-19	18-Mar-19	14
SRB506-8P4D26	Steel Roof Canopy - Bolt-up/Detail - Seq 5300	10	11-Mar-19	22-Mar-19	16
SRB522-8P4D4	Steel Roof Canopy - Bolt-up/Detail - Seq 5330	6	08-Apr-19	15-Apr-19	26
SRB525-8P4D4	Steel Roof Canopy - Bolt-up/Detail - Seq 5340	6	12-Apr-19	19-Apr-19	33
SRB522-8P4D6	Steel Roof Canopy - Bolt-up/Detail - Seq 5320	10	09-Apr-19	22-Apr-19	18
SRB526-8P4D4	Steel Roof Canopy - Bolt-up/Detail - Seq 5360	6	19-Apr-19	26-Apr-19	15
SRB525-8P4D7	Steel Roof Canopy - Bolt-up/Detail - Seq 5331	10	15-Apr-19	26-Apr-19	25
SRB527-8P4D4	Steel Roof Canopy - Bolt-up/Detail - Seq 5400	6	24-Apr-19	01-May-19	15
SRB527-8P4D6	Steel Roof Canopy - Bolt-up/Detail - Seq 5412 (outside)	10	25-Apr-19	08-May-19	12
SRC528-8P4D4	Steel Roof Canopy - Bolt-up/Detail - Seq 5411 (inside)	10	29-Apr-19	10-May-19	13
SRB526-8P4D6	Steel Roof Canopy - Bolt-up/Detail - Seq 5372 (outside)	10	30-Apr-19	13-May-19	12
SRC509-8P4D4	Steel Roof Canopy - Bolt-up/Detail - Seq 5371 (inside)	10	03-May-19	16-May-19	9
SRE516-8P4D4	Steel Roof Canopy - Bolt-up/Detail - Seq 5070	6	04-Jan-19	11-Jan-19	52
SRE515-8P4D4	Steel Roof Canopy - Bolt-up/Detail - Seq 5090	6	09-Jan-19	16-Jan-19	43
SRE515-8P4D16	Steel Roof Canopy - Bolt-up/Detail - Seq 5080	10	10-Jan-19	23-Jan-19	41
SRE518-8P4D4	Steel Roof Canopy - Bolt-up/Detail - Seq 5100	10	15-Jan-19	28-Jan-19	32
SRE523-8P4D4	Steel Roof Canopy - Bolt-up/Detail - Seq 5050	6	13-Feb-19	21-Feb-19	30

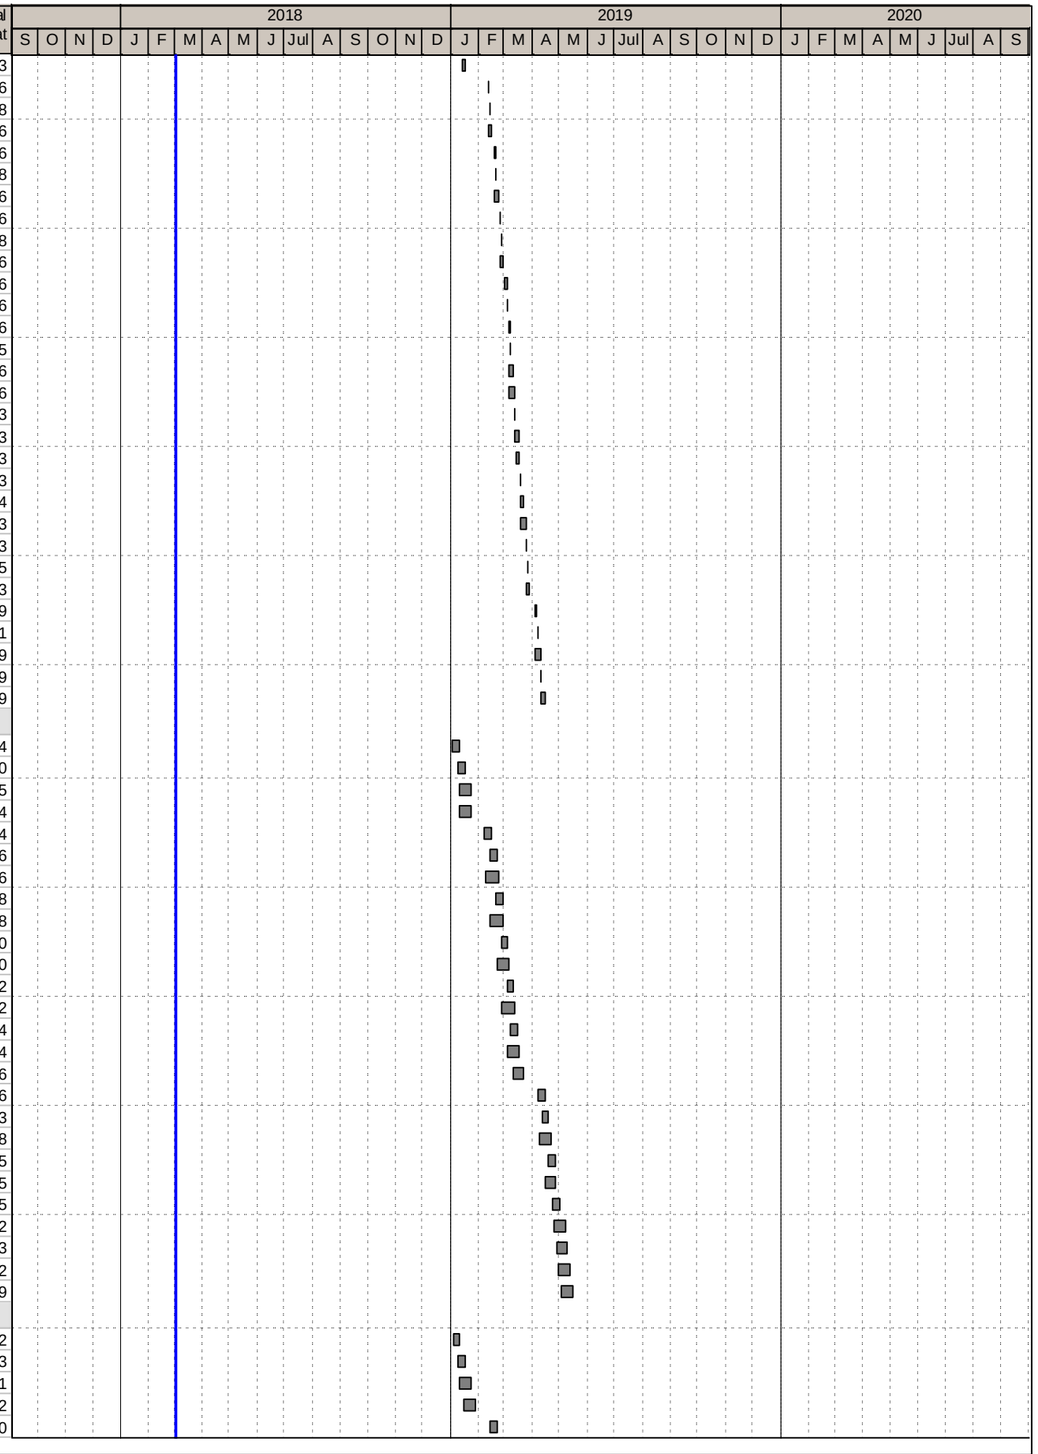

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
SRA512-8P4D4	Steel Roof Canopy - Bolt-up/Detail - Seq 5030	6	20-Feb-19	27-Feb-19	32
SRE523-8P4D6	Steel Roof Canopy - Bolt-up/Detail - Seq 5060	10	14-Feb-19	28-Feb-19	22
SRF513-8P4D4	Steel Roof Canopy - Bolt-up/Detail - Seq 5010	6	26-Feb-19	05-Mar-19	32
SRA512-8P4D6	Steel Roof Canopy - Bolt-up/Detail - Seq 5040	10	21-Feb-19	06-Mar-19	24
SRF514-8P4D4	Steel Roof Canopy - Bolt-up/Detail - Seq 5140	6	05-Mar-19	12-Mar-19	14
SRF513-8P4D6	Steel Roof Canopy - Bolt-up/Detail - Seq 5020	10	27-Feb-19	12-Mar-19	26
SRE517-8P4D4	Steel Roof Canopy - Bolt-up/Detail - Seq 5120	6	08-Mar-19	15-Mar-19	11
SRD520-8P4D4	Steel Roof Canopy - Bolt-up/Detail - Seq 5490	6	14-Mar-19	21-Mar-19	28
SRF514-8P4D6	Steel Roof Canopy - Bolt-up/Detail - Seq 5132 (outside)	10	11-Mar-19	22-Mar-19	6
SRE517-8P4D6	Steel Roof Canopy - Bolt-up/Detail - Seq 5112 (outside)	10	11-Mar-19	22-Mar-19	6
SRD520-8P4D6	Steel Roof Canopy - Bolt-up/Detail - Seq 5500	6	15-Mar-19	22-Mar-19	24
SRD510-8P4D4	Steel Roof Canopy - Bolt-up/Detail - Seq 5470	6	20-Mar-19	27-Mar-19	30
SRD521-8P4D4	Steel Roof Canopy - Bolt-up/Detail - Seq 5450	6	27-Mar-19	03-Apr-19	31
SRD510-8P4D16	Steel Roof Canopy - Bolt-up/Detail - Seq 5480	10	21-Mar-19	03-Apr-19	22
SRE519-8P4D4	Steel Roof Canopy - Bolt-up/Detail - Seq 5111 (inside)	10	27-Mar-19	09-Apr-19	7
SRD521-8P4D16	Steel Roof Canopy - Bolt-up/Detail - Seq 5460	10	28-Mar-19	10-Apr-19	23
SRE519-8P4D5	Steel Roof Canopy - Bolt-up/Detail - Seq 5131 (inside)	10	01-Apr-19	12-Apr-19	6
SRC507-8P4D4	Steel Roof Canopy - Bolt-up/Detail - Seq 5430	6	08-Apr-19	15-Apr-19	29
SRC508-8P4D4	Steel Roof Canopy - Bolt-up/Detail - Seq 5420	6	12-Apr-19	19-Apr-19	33
SRC507-8P4D6	Steel Roof Canopy - Bolt-up/Detail - Seq 5440	10	09-Apr-19	22-Apr-19	21
SRC508-8P4D6	Steel Roof Canopy - Bolt-up/Detail - Seq 5421	10	15-Apr-19	26-Apr-19	25
SRA511-8P4D27	Steel Roof Canopy - Deck - Seq 5160	3	25-Jan-19	29-Jan-19	14
SRA511-8P4D5	Steel Roof Canopy - Deck - Seq 5170	3	30-Jan-19	01-Feb-19	14
SRA501-8P4D7	Steel Roof Canopy - Deck - Seq 5180	3	04-Feb-19	06-Feb-19	14
SRA501-8P4D5	Steel Roof Canopy - Deck - Seq 5190	3	07-Feb-19	11-Feb-19	14
SRA521-8P4D7	Steel Roof Canopy - Deck - Seq 5200	3	25-Feb-19	27-Feb-19	6
SRA521-8P4D5	Steel Roof Canopy - Deck - Seq 5210	3	28-Feb-19	04-Mar-19	6
SRB502-8P4D7	Steel Roof Canopy - Deck - Seq 5220	3	05-Mar-19	07-Mar-19	6
SRB502-8P4D5	Steel Roof Canopy - Deck - Seq 5230	3	08-Mar-19	12-Mar-19	6
SRB503-8P4D7	Steel Roof Canopy - Deck - Seq 5240	3	13-Mar-19	15-Mar-19	6
SRB503-8P4D5	Steel Roof Canopy - Deck - Seq 5250	3	18-Mar-19	20-Mar-19	6
SRB504-8P4D7	Steel Roof Canopy - Deck - Seq 5260	3	21-Mar-19	25-Mar-19	6
SRB504-8P4D5	Steel Roof Canopy - Deck - Seq 5270	3	26-Mar-19	28-Mar-19	6
SRB505-8P4D7	Steel Roof Canopy - Deck - Seq 5280	3	29-Mar-19	02-Apr-19	6
SRB505-8P4D5	Steel Roof Canopy - Deck - Seq 5290	3	03-Apr-19	05-Apr-19	6
SRB506-8P4D27	Steel Roof Canopy - Deck - Seq 5300	3	08-Apr-19	10-Apr-19	6
SRB506-8P4D5	Steel Roof Canopy - Deck - Seq 5310	3	11-Apr-19	15-Apr-19	6
SRB522-8P4D7	Steel Roof Canopy - Deck - Seq 5320	3	23-Apr-19	25-Apr-19	18
SRB522-8P4D5	Steel Roof Canopy - Deck - Seq 5330	3	26-Apr-19	30-Apr-19	18
SRB525-8P4D8	Steel Roof Canopy - Deck - Seq 5331	3	01-May-19	03-May-19	23
SRB525-8P4D5	Steel Roof Canopy - Deck - Seq 5340	4	06-May-19	09-May-19	23
SRE515-8P4D17	Steel Roof Canopy - Deck - Seq 5100	3	29-Jan-19	31-Jan-19	32
SRE515-8P4D5	Steel Roof Canopy - Deck - Seq 5090	3	01-Feb-19	05-Feb-19	32
SRE516-8P4D16	Steel Roof Canopy - Deck - Seq 5080	3	06-Feb-19	08-Feb-19	32
SRE516-8P4D5	Steel Roof Canopy - Deck - Seq 5070	3	11-Feb-19	13-Feb-19	32
SRE523-8P4D7	Steel Roof Canopy - Deck - Seq 5060	3	01-Mar-19	05-Mar-19	22
SRE523-8P4D5	Steel Roof Canopy - Deck - Seq 5050	3	06-Mar-19	08-Mar-19	22
SRA512-8P4D7	Steel Roof Canopy - Deck - Seq 5040	3	11-Mar-19	13-Mar-19	22
SRA512-8P4D5	Steel Roof Canopy - Deck - Seq 5030	3	14-Mar-19	18-Mar-19	22
SRF513-8P4D7	Steel Roof Canopy - Deck - Seq 5020	3	19-Mar-19	21-Mar-19	22
SRF513-8P4D5	Steel Roof Canopy - Deck - Seq 5010	3	22-Mar-19	26-Mar-19	22
SRD520-8P4D7	Steel Roof Canopy - Deck - Seq 5500	3	27-Mar-19	29-Mar-19	22
SRD520-8P4D5	Steel Roof Canopy - Deck - Seq 5490	3	01-Apr-19	03-Apr-19	22
SRD510-8P4D17	Steel Roof Canopy - Deck - Seq 5480	3	04-Apr-19	08-Apr-19	22
SRD510-8P4D5	Steel Roof Canopy - Deck - Seq 5470	3	09-Apr-19	11-Apr-19	22
SRD521-8P4D17	Steel Roof Canopy - Deck - Seq 5460	3	12-Apr-19	16-Apr-19	22
SRD521-8P4D5	Steel Roof Canopy - Deck - Seq 5450	3	17-Apr-19	19-Apr-19	22
SRC507-8P4D7	Steel Roof Canopy - Deck - Seq 5440	3	23-Apr-19	25-Apr-19	21
SRC507-8P4D5	Steel Roof Canopy - Deck - Seq 5430	3	26-Apr-19	30-Apr-19	21
SRC508-8P4D7	Steel Roof Canopy - Deck - Seq 5421	3	01-May-19	03-May-19	23
SRC508-8P4D5	Steel Roof Canopy - Deck - Seq 5420	4	06-May-19	09-May-19	23

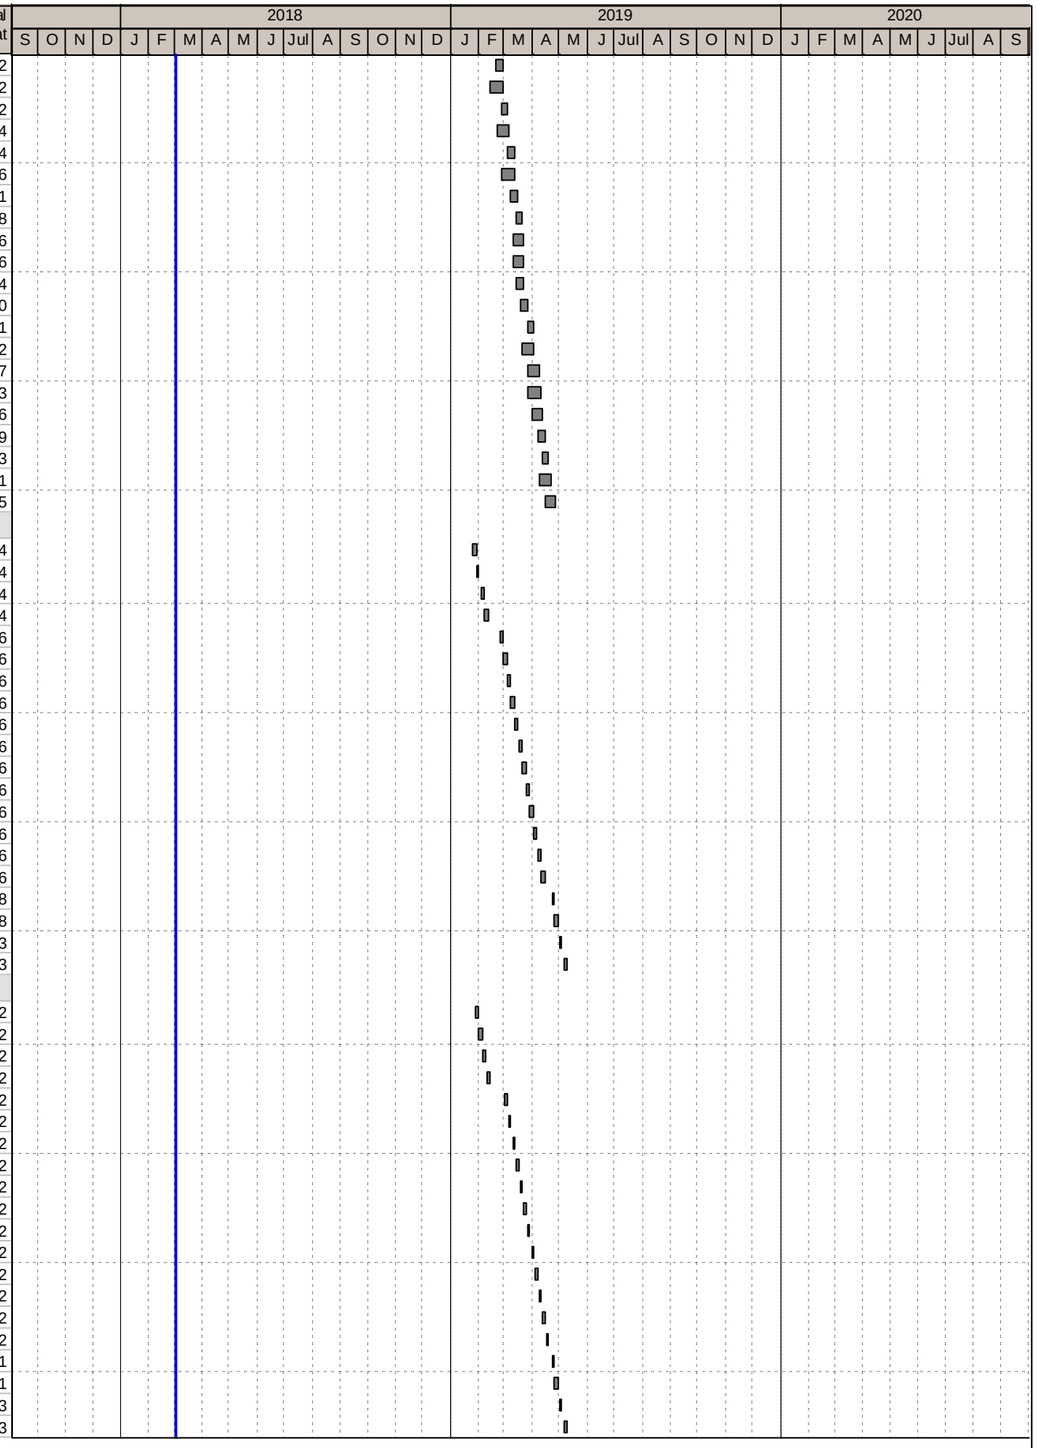

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
SRF514-8P4D5	Steel Roof Canopy - Deck - Seq 5140	3	13-Mar-19	15-Mar-19	15
SRE517-8P4D5	Steel Roof Canopy - Deck - Seq 5120	2	18-Mar-19	19-Mar-19	15
SRE517-8P4D8	Steel Roof Canopy - Deck - Seq 5112 (outside)	3	25-Mar-19	27-Mar-19	12
SRF514-8P4D8	Steel Roof Canopy - Deck - Seq 5132 (outside)	4	28-Mar-19	02-Apr-19	12
SRE517-8P4D7	Steel Roof Canopy - Deck - Seq 5111 (inside)	2	10-Apr-19	11-Apr-19	7
SRF514-8P4D7	Steel Roof Canopy - Deck - Seq 5131 (inside)	3	15-Apr-19	17-Apr-19	6
SRB526-8P4D5	Steel Roof Canopy - Deck - Seq 5360	3	29-Apr-19	01-May-19	15
SRB527-8P4D5	Steel Roof Canopy - Deck - Seq 5400	2	02-May-19	03-May-19	15
SRB527-8P4D7	Steel Roof Canopy - Deck - Seq 5412 (outside)	3	09-May-19	13-May-19	12
SRB526-8P4D7	Steel Roof Canopy - Deck - Seq 5372 (outside)	4	14-May-19	17-May-19	12
SRB527-8P4D8	Steel Roof Canopy - Deck - Seq 5411 (inside)	2	20-May-19	21-May-19	12
SRB526-8P4D8	Steel Roof Canopy - Deck - Seq 5371 (inside)	3	22-May-19	24-May-19	12
FRP Slab on Metal Deck					
100 Main Concourse					
S3C1-8P4F	FRP Slab on Metal Deck - Main Concourse C1	5	02-May-19	08-May-19	22
S3C2-8P4F	FRP Slab on Metal Deck - Main Concourse C2	5	07-May-19	13-May-19	22
S3D1-8P4F	FRP Slab on Metal Deck - Main Concourse D1	5	10-May-19	16-May-19	22
S3D2-8P4F	FRP Slab on Metal Deck - Main Concourse D2	5	15-May-19	21-May-19	22
150 Lower Suite Level					
S4A1-8P4F	FRP Slab on Metal Deck - Lower Suite A1	4	29-Oct-18	01-Nov-18	20
S4F1-8P4F	FRP Slab on Metal Deck - Lower Suite F1	4	29-Oct-18	01-Nov-18	20
S4B1-8P4F	FRP Slab on Metal Deck - Lower Suite B1	5	26-Oct-18	01-Nov-18	40
S4E1-8P4F	FRP Slab on Metal Deck - Lower Suite E1	5	08-Nov-18	15-Nov-18	36
S4E2-8P4F	FRP Slab on Metal Deck - Lower Suite E2	5	20-Nov-18	28-Nov-18	31
S4B2-8P4F	FRP Slab on Metal Deck - Lower Suite B2	5	28-Nov-18	04-Dec-18	33
S4B3-8P4F	FRP Slab on Metal Deck - Lower Suite B3	5	03-Dec-18	07-Dec-18	32
S4B4-8P4F	FRP Slab on Metal Deck - Lower Suite B4	5	04-Dec-18	10-Dec-18	31
S4B5-8P4F	FRP Slab on Metal Deck - Lower Suite B5	5	19-Dec-18	26-Dec-18	22
S4E3-8P4F	FRP Slab on Metal Deck - Lower Suite E3	5	19-Dec-18	26-Dec-18	14
S4E4-8P4F	FRP Slab on Metal Deck - Lower Suite E4	5	24-Dec-18	31-Dec-18	13
S4C1-8P4F	FRP Slab on Metal Deck - Lower Suite C1	4	28-Dec-18	03-Jan-19	111
S4E5-8P4F	FRP Slab on Metal Deck - Lower Suite E5	5	02-Jan-19	08-Jan-19	10
S4D1-8P4F	FRP Slab on Metal Deck - Lower Suite D1	4	21-Jan-19	24-Jan-19	49
S4D2-8P4F	FRP Slab on Metal Deck - Lower Suite D2	4	05-Feb-19	08-Feb-19	97
S4C2-8P4F	FRP Slab on Metal Deck - Lower Suite C2	4	06-Feb-19	11-Feb-19	86
S4C3-8P4F	FRP Slab on Metal Deck - Lower Suite C3	4	08-Feb-19	13-Feb-19	99
200 Upper Suite Level					
S5A1-8P4F	FRP Slab on Metal Deck - Upper Suite A1	5	23-Oct-18	29-Oct-18	29
S5F0-8P4F	FRP Slab on Metal Deck - Upper Suite F1	5	25-Oct-18	31-Oct-18	27
S5A2-8P4F	FRP Slab on Metal Deck - Upper Suite A2	5	31-Oct-18	06-Nov-18	25
S5A3-8P4F	FRP Slab on Metal Deck - Upper Suite A3	5	02-Nov-18	08-Nov-18	26
S5F2-8P4F	FRP Slab on Metal Deck - Upper Suite F2	5	13-Nov-18	19-Nov-18	17
S5B1-8P4F	FRP Slab on Metal Deck - Upper Suite B1	5	14-Nov-18	20-Nov-18	37
S5F3-8P4F	FRP Slab on Metal Deck - Upper Suite F3	5	15-Nov-18	21-Nov-18	18
S5B2-8P4F	FRP Slab on Metal Deck - Upper Suite B2	5	12-Dec-18	18-Dec-18	21
S5B3-8P4F	FRP Slab on Metal Deck - Upper Suite B3	5	14-Dec-18	20-Dec-18	21
S5B4-8P4F	FRP Slab on Metal Deck - Upper Suite B4	5	19-Dec-18	26-Dec-18	20
S5B5-8P4F	FRP Slab on Metal Deck - Upper Suite B5	5	21-Dec-18	28-Dec-18	20
S5E1-8P4F	FRP Slab on Metal Deck - Upper Suite E1	5	02-Jan-19	08-Jan-19	2
S5E2-8P4F	FRP Slab on Metal Deck - Upper Suite E2	5	08-Jan-19	14-Jan-19	0
S5E3-8P4F	FRP Slab on Metal Deck - Upper Suite E3	5	10-Jan-19	16-Jan-19	0
S5E4-8P4F	FRP Slab on Metal Deck - Upper Suite E4	5	14-Jan-19	18-Jan-19	0
S5E5-8P4F	FRP Slab on Metal Deck - Upper Suite E5	5	16-Jan-19	22-Jan-19	0
S5D1-8P4F	FRP Slab on Metal Deck - Upper Suite D1	5	12-Feb-19	19-Feb-19	31
S5C1-8P4F	FRP Slab on Metal Deck - Upper Suite C1	5	13-Feb-19	20-Feb-19	33
S5C2-8P4F	FRP Slab on Metal Deck - Upper Suite C2	5	21-Feb-19	27-Feb-19	30
S5C3-8P4F	FRP Slab on Metal Deck - Upper Suite C3	5	05-Mar-19	11-Mar-19	82
S5D2-8P4F	FRP Slab on Metal Deck - Upper Suite D2	5	05-Mar-19	11-Mar-19	19

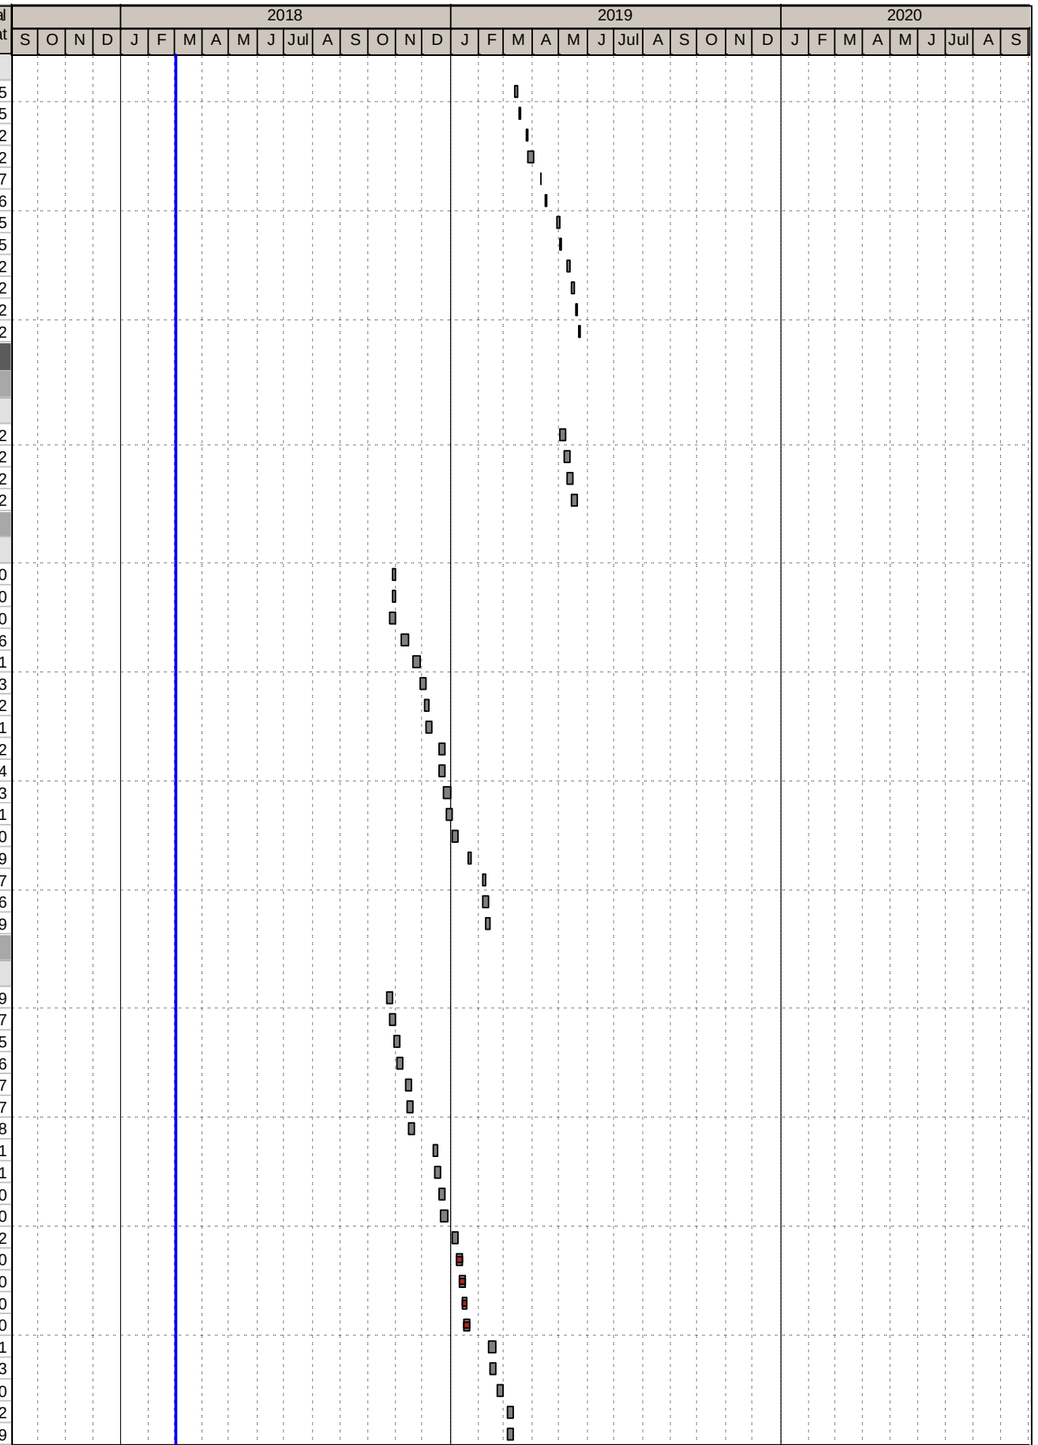

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
250 Mid Bowl Mezz Level					
S6B1-8P4F	FRP Slab on Metal Deck - Mid Bowl Mezzanine B1	4	14-Nov-18	19-Nov-18	42
S6B2-8P4F	FRP Slab on Metal Deck - Mid Bowl Mezzanine B2	4	19-Dec-18	24-Dec-18	27
S6E1-8P4F	FRP Slab on Metal Deck - Mid Bowl Mezzanine E1	4	02-Jan-19	07-Jan-19	18
S6E2-8P4F	FRP Slab on Metal Deck - Mid Bowl Mezzanine E2	4	21-Jan-19	24-Jan-19	13
S6D1-8P4F	FRP Slab on Metal Deck - Mid Bowl Mezzanine D1	4	12-Feb-19	15-Feb-19	34
S6C1-8P4F	FRP Slab on Metal Deck - Mid Bowl Mezzanine C1	4	13-Feb-19	19-Feb-19	34
S6D2-8P4F	FRP Slab on Metal Deck - Mid Bowl Mezzanine D2	5	05-Mar-19	11-Mar-19	22
300 Upper Concourse					
S7A1-8P4F	FRP Slab on Metal Deck - Upper Concourse A1	5	07-Nov-18	14-Nov-18	25
S7F1-8P4F	FRP Slab on Metal Deck - Upper Concourse F1	5	30-Nov-18	06-Dec-18	18
S7B1-8P4F	FRP Slab on Metal Deck - Upper Concourse B1	5	10-Dec-18	14-Dec-18	16
S7B2-8P4F	FRP Slab on Metal Deck - Upper Concourse B2	5	12-Dec-18	18-Dec-18	16
S7B3-8P4F	FRP Slab on Metal Deck - Upper Concourse B3	5	17-Jan-19	23-Jan-19	3
S7E1-8P4F	FRP Slab on Metal Deck - Upper Concourse E1	5	21-Jan-19	25-Jan-19	6
S7B4-8P4F	FRP Slab on Metal Deck - Upper Concourse B4	5	23-Jan-19	29-Jan-19	1
S7E2-8P4F	FRP Slab on Metal Deck - Upper Concourse E2	5	23-Jan-19	29-Jan-19	6
S7B5-8P4F	FRP Slab on Metal Deck - Upper Concourse B5	5	25-Jan-19	31-Jan-19	1
S7E3-8P4F	FRP Slab on Metal Deck - Upper Concourse E3	5	29-Jan-19	04-Feb-19	4
S7E4-8P4F	FRP Slab on Metal Deck - Upper Concourse E4	5	31-Jan-19	06-Feb-19	4
S7C1-8P4F	FRP Slab on Metal Deck - Upper Concourse C1	5	14-Feb-19	21-Feb-19	30
S7D1-8P4F	FRP Slab on Metal Deck - Upper Concourse D1	5	25-Feb-19	01-Mar-19	24
S7C2-8P4F	FRP Slab on Metal Deck - Upper Concourse C2	5	20-Mar-19	26-Mar-19	9
S7D2-8P4F	FRP Slab on Metal Deck - Upper Concourse D2	5	20-Mar-19	26-Mar-19	9
S7C3-8P4F	FRP Slab on Metal Deck - Upper Concourse C3	5	22-Mar-19	28-Mar-19	11
S7D3-8P4F	FRP Slab on Metal Deck - Upper Concourse D3	5	22-Mar-19	28-Mar-19	11
400 Press Level					
S9A1-8P4F	FRP Slab on Metal Deck - Upper Mezzanine A1	5	04-Dec-18	10-Dec-18	24
S9F1-8P4F	FRP Slab on Metal Deck - Upper Mezzanine F1	5	17-Dec-18	21-Dec-18	23
S9C1-8P4F	FRP Slab on Metal Deck - Upper Mezzanine C1	5	11-Mar-19	15-Mar-19	21
S9D1-8P4F	FRP Slab on Metal Deck - Upper Mezzanine D1	5	14-Mar-19	20-Mar-19	18
350/400 Upper Stadia Support & Press Lvl					
S95A1-8P4F	FRP Slab on Metal Deck - Press A1	5	04-Dec-18	10-Dec-18	25
S95F1-8P4F	FRP Slab on Metal Deck - Press F1	5	20-Dec-18	27-Dec-18	23
S95E1-8P4F	FRP Slab on Metal Deck - Press E1	6	22-Jan-19	29-Jan-19	7
S95E2-8P4F	FRP Slab on Metal Deck - Press E2	6	28-Jan-19	04-Feb-19	6
Misc. Structural Supports					
Lower Seating Bowl Grids AA-CC					
SS1A1-8P5G2	Steel Precast Bracing - Lower Bowl from AA-CC Area A1 (Seq 7080 & 7090)	2	11-Sep-19	12-Sep-19	41
SS1F1-8P5G2	Steel Precast Bracing - Lower Bowl from AA-CC Area F1 (Seq 7040 & 7090)	2	11-Sep-19	12-Sep-19	41
SS1E1-8P5G2	Steel Precast Bracing - Lower Bowl from AA-CC Area E1 (Seq 7030)	2	19-Sep-19	20-Sep-19	35
SS1B1-8P5G2	Steel Precast Bracing - Lower Bowl from AA-CC Area B1 (Seq 7070)	2	20-Sep-19	23-Sep-19	34
SS1E3-8P5G2	Steel Precast Bracing - Lower Bowl from AA-CC Area E3 (Seq 7020)	2	07-Oct-19	08-Oct-19	23
SS1B3-8P5G2	Steel Precast Bracing - Lower Bowl from AA-CC Area B3 (Seq 7060)	2	08-Oct-19	09-Oct-19	22
SS1D1-8P5G2	Steel Precast Bracing - Lower Bowl from AA-CC Area D1 (Seq 7010)	2	14-Oct-19	15-Oct-19	18
SS1C1-8P5G2	Steel Precast Bracing - Lower Bowl from AA-CC Area C1 (Seq 7050)	2	15-Oct-19	16-Oct-19	17
Lower Seating Bowl Grids CC-DD					
SS4A1-8P5G2	Steel Precast Bracing - Lower Bowl from CC-DD Area A1 (Seq 7085 & 7095)	1	12-Sep-18	12-Sep-18	182
SS4F1-8P5G2	Steel Precast Bracing - Lower Bowl from CC-DD Area F1 (Seq 7045 & 7095)	1	19-Sep-18	19-Sep-18	177
SS4E1-8P5G2	Steel Precast Bracing - Lower Bowl from CC-DD Area E1 (Seq 7035)	1	25-Sep-18	25-Sep-18	173
SS4B1-8P5G2	Steel Precast Bracing - Lower Bowl from CC-DD Area B1 (Seq 7075)	1	27-Sep-18	27-Sep-18	171
SS4E3-8P5G2	Steel Precast Bracing - Lower Bowl from CC-DD Area E3 (Seq 7025)	1	09-Oct-18	09-Oct-18	168
SS4B3-8P5G2	Steel Precast Bracing - Lower Bowl from CC-DD Area B3 (Seq 7065)	1	11-Oct-18	11-Oct-18	166
SS4D1-8P5G2	Steel Precast Bracing - Lower Bowl from CC-DD Area D1 (Seq 7015)	1	28-Mar-19	28-Mar-19	52
SS4C1-8P5G2	Steel Precast Bracing - Lower Bowl from CC-DD Area C1 (Seq 7075)	1	01-Apr-19	01-Apr-19	50

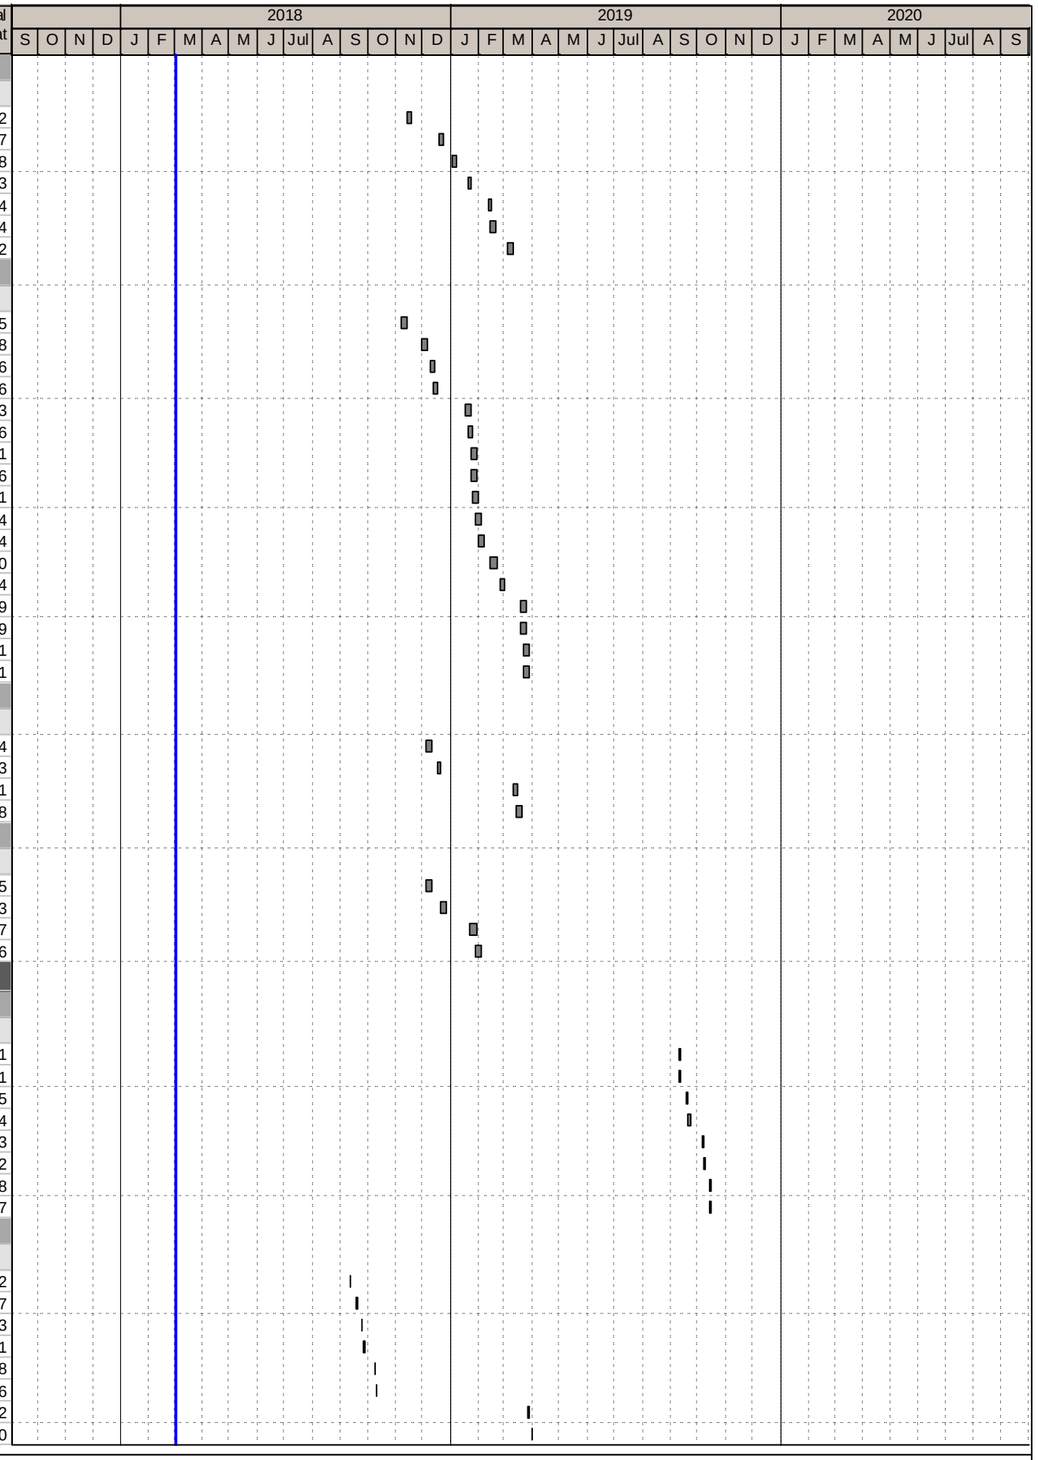

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
Exterior Elevations					
SXXN1-8Q3S3	Op Doors - Assemble Fixed Door Frame - North Operable Door #1	5	20-Nov-18	28-Nov-18	14
SXXN6-8Q3S3	Op Doors - Assemble Fixed Door Frame - North Operable Door #6	5	29-Nov-18	05-Dec-18	14
SXXN1-8Q3S4	Op Doors - Erect Fixed Door Frame - North Operable Door #1	2	29-Nov-18	30-Nov-18	17
SXXN6-8Q3S4	Op Doors - Erect Fixed Door Frame - North Operable Door #6	2	06-Dec-18	07-Dec-18	14
Precast Stadia					
Lower Seating Bowl					
SSL0-8P5G	Precast Stadia - Lower Bowl (Summary)	30	10-Sep-19	21-Oct-19	0
Lower Seating Bowl Grids AA-CC					
SS1F1-8P5G	Precast Stadia - Lower Bowl from AA-CC Area F1	6	10-Sep-19	17-Sep-19	0
SS1A1-8P5G	Precast Stadia - Lower Bowl from AA-CC Area A1	7	10-Sep-19	18-Sep-19	0
SS1E1-8P5G	Precast Stadia - Lower Bowl from AA-CC Area E1	5	18-Sep-19	24-Sep-19	0
SS1B1-8P5G	Precast Stadia - Lower Bowl from AA-CC Area B1	5	19-Sep-19	25-Sep-19	0
SS1E2-8P5G	Precast Stadia - Lower Bowl from AA-CC Area E2	7	25-Sep-19	03-Oct-19	0
SS1B2-8P5G	Precast Stadia - Lower Bowl from AA-CC Area B2	7	26-Sep-19	04-Oct-19	0
SS1E3-8P5G	Precast Stadia - Lower Bowl from AA-CC Area E3	5	04-Oct-19	10-Oct-19	0
SS1B3-8P5G	Precast Stadia - Lower Bowl from AA-CC Area B3	5	07-Oct-19	11-Oct-19	0
SS1D1-8P5G	Precast Stadia - Lower Bowl from AA-CC Area D1	5	11-Oct-19	17-Oct-19	0
SS1C1-8P5G	Precast Stadia - Lower Bowl from AA-CC Area C1	4	14-Oct-19	17-Oct-19	0
SS1D2-8P5G	Precast Stadia - Lower Bowl from AA-CC Area D2	2	18-Oct-19	21-Oct-19	0
SS1C2-8P5G	Precast Stadia - Lower Bowl from AA-CC Area C2	2	18-Oct-19	21-Oct-19	0
SS1F1-8P5G1	Precast Stadia - Detailing - Lower Bowl from AA-CC Area F1	6	11-Sep-19	18-Sep-19	37
SS1A1-8P5G1	Precast Stadia - Detailing - Lower Bowl from AA-CC Area A1	7	11-Sep-19	19-Sep-19	36
SS1E1-8P5G1	Precast Stadia - Detailing - Lower Bowl from AA-CC Area E1	5	19-Sep-19	25-Sep-19	32
SS1B1-8P5G1	Precast Stadia - Detailing - Lower Bowl from AA-CC Area B1	5	20-Sep-19	26-Sep-19	31
SS1E2-8P5G1	Precast Stadia - Detailing - Lower Bowl from AA-CC Area E2	7	26-Sep-19	04-Oct-19	25
SS1B2-8P5G1	Precast Stadia - Detailing - Lower Bowl from AA-CC Area B2	7	27-Sep-19	07-Oct-19	24
SS1E3-8P5G1	Precast Stadia - Detailing - Lower Bowl from AA-CC Area E3	5	07-Oct-19	11-Oct-19	20
SS1B3-8P5G1	Precast Stadia - Detailing - Lower Bowl from AA-CC Area B3	5	08-Oct-19	14-Oct-19	19
SS1D1-8P5G1	Precast Stadia - Detailing - Lower Bowl from AA-CC Area D1	5	14-Oct-19	18-Oct-19	15
SS1C1-8P5G1	Precast Stadia - Detailing - Lower Bowl from AA-CC Area C1	4	15-Oct-19	18-Oct-19	15
SS1D2-8P5G1	Precast Stadia - Detailing - Lower Bowl from AA-CC Area D2	2	21-Oct-19	22-Oct-19	13
SS1C2-8P5G1	Precast Stadia - Detailing - Lower Bowl from AA-CC Area C2	2	21-Oct-19	22-Oct-19	13
Upper Seating Bowl					
SSA0-8P5G	Precast Stadia - Upper Bowls A (Summary)	18	28-Nov-18	21-Dec-18	28
SSF0-8P5G	Precast Stadia - Upper Bowls F (Summary)	11	09-Jan-19	23-Jan-19	14
SSE0-8P5G	Precast Stadia - Upper Bowls E (Summary)	45	23-Jan-19	27-Mar-19	4
SSB0-8P5G	Precast Stadia - Upper Bowls B (Summary)	43	29-Jan-19	29-Mar-19	0
SSD0-8P5G	Precast Stadia - Upper Bowls D (Summary)	18	01-Apr-19	24-Apr-19	4
SSC0-8P5G	Precast Stadia - Upper Bowls C (Summary)	20	03-Apr-19	30-Apr-19	0
Lower Seating Bowl Grids CC-DD					
SS4A1-8P5G	Precast Stadia - Lower Bowl from CC-DD Area A1	5	12-Sep-18	18-Sep-18	0
SS4F1-8P5G	Precast Stadia - Lower Bowl from CC-DD Area F1	4	19-Sep-18	24-Sep-18	0
SS4E1-8P5G	Precast Stadia - Lower Bowl from CC-DD Area E1	2	25-Sep-18	26-Sep-18	0
SS4B1-8P5G	Precast Stadia - Lower Bowl from CC-DD Area B1	3	27-Sep-18	01-Oct-18	0
SS4B2-8P5G	Precast Stadia - Lower Bowl from CC-DD Area B2	2	02-Oct-18	03-Oct-18	4
SS4E2-8P5G	Precast Stadia - Lower Bowl from CC-DD Area E2	2	04-Oct-18	05-Oct-18	7
SS4E3-8P5G	Precast Stadia - Lower Bowl from CC-DD Area E3	2	09-Oct-18	10-Oct-18	6
SS4B3-8P5G	Precast Stadia - Lower Bowl from CC-DD Area B3	2	11-Oct-18	12-Oct-18	8
SS4D1-8P5G	Precast Stadia - Lower Bowl from CC-DD Area D1	2	28-Mar-19	29-Mar-19	4
SS4C1-8P5G	Precast Stadia - Lower Bowl from CC-DD Area C1	2	01-Apr-19	02-Apr-19	0
SS4A1-8P5G1	Precast Stadia - Detailing - Lower Bowl from CC-DD Area A1	5	13-Sep-18	19-Sep-18	177
SS4F1-8P5G1	Precast Stadia - Detailing - Lower Bowl from CC-DD Area F1	4	20-Sep-18	25-Sep-18	173

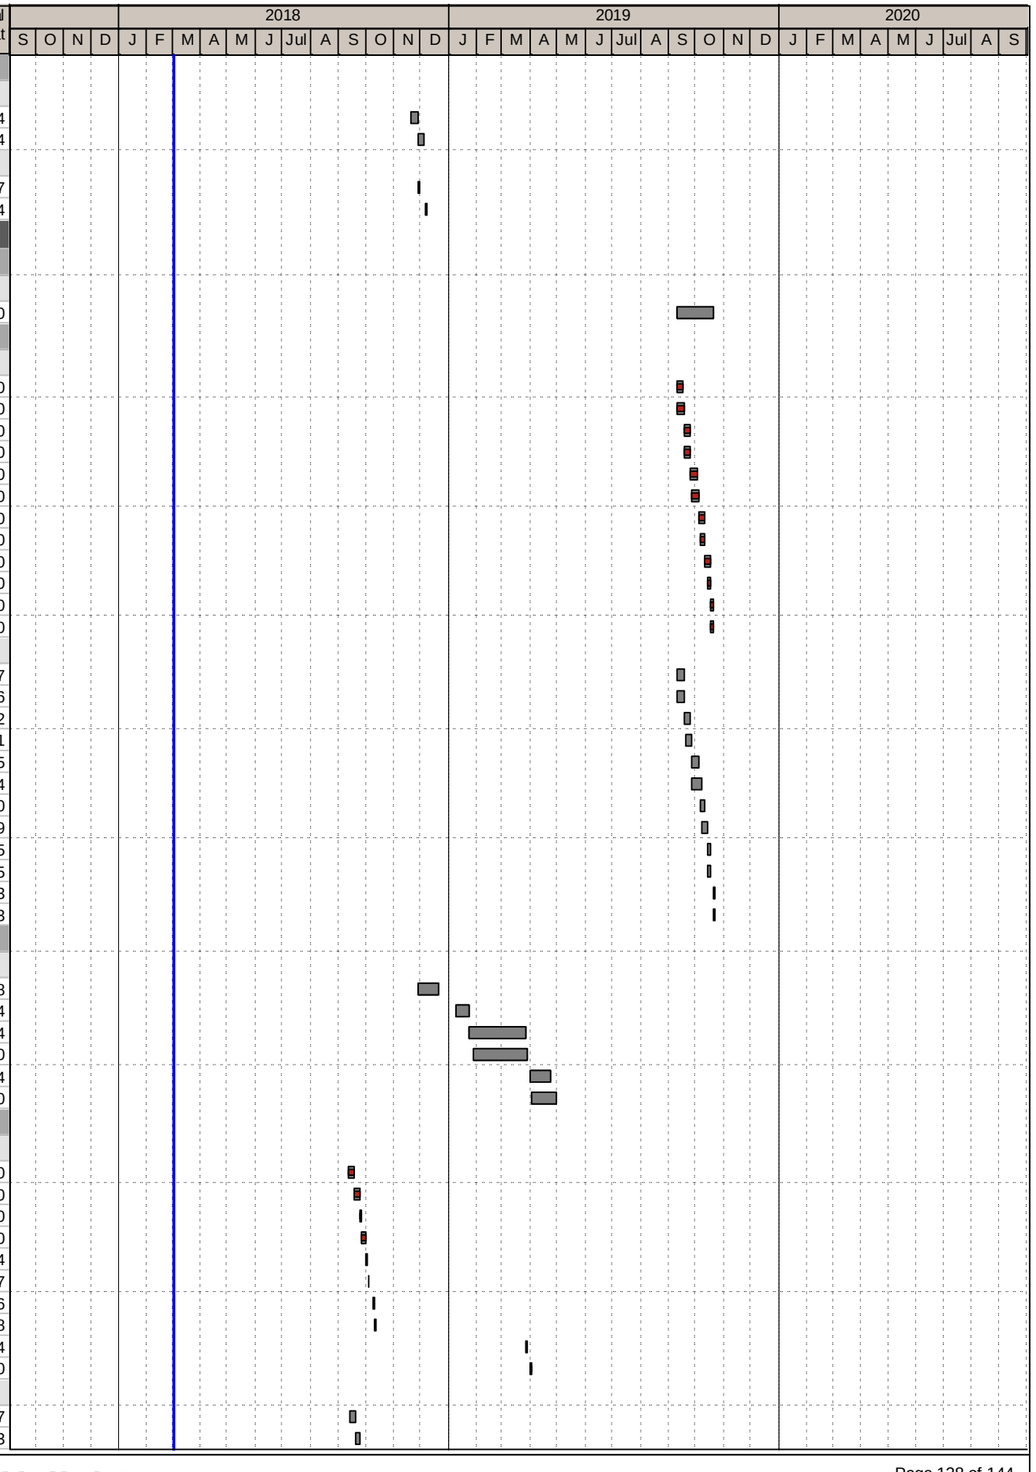

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
SS4E1-8P5G1	Precast Stadia - Detailing - Lower Bowl from CC-DD Area E1	2	26-Sep-18	27-Sep-18	171
SS4B1-8P5G1	Precast Stadia - Detailing - Lower Bowl from CC-DD Area B1	3	28-Sep-18	02-Oct-18	168
SS4B2-8P5G1	Precast Stadia - Detailing - Lower Bowl from CC-DD Area B2	2	03-Oct-18	04-Oct-18	166
SS4E2-8P5G1	Precast Stadia - Detailing - Lower Bowl from CC-DD Area E2	2	05-Oct-18	08-Oct-18	164
SS4E3-8P5G1	Precast Stadia - Detailing - Lower Bowl from CC-DD Area E3	2	10-Oct-18	11-Oct-18	166
SS4B3-8P5G1	Precast Stadia - Detailing - Lower Bowl from CC-DD Area B3	2	12-Oct-18	15-Oct-18	164
SS4D1-8P5G1	Precast Stadia - Detailing - Lower Bowl from CC-DD Area D1	2	29-Mar-19	01-Apr-19	50
SS4C1-8P5G1	Precast Stadia - Detailing - Lower Bowl from CC-DD Area C1	2	02-Apr-19	03-Apr-19	48
Suite Levels Seating Bowl (100 to 200)					
SS2A1-8P5G	Precast Stadia - Suite Levels 100 to 200 Area A1	7	28-Nov-18	06-Dec-18	25
SS2F1-8P5G	Precast Stadia - Suite Levels 100 to 200 Area F1	6	09-Jan-19	16-Jan-19	4
SS2E1-8P5G	Precast Stadia - Suite Levels 100 to 200 Area E1	4	23-Jan-19	28-Jan-19	0
SS2B1-8P5G	Precast Stadia - Suite Levels 100 to 200 Area B1	4	29-Jan-19	01-Feb-19	0
SS2B2-8P5G	Precast Stadia - Suite Levels 100 to 200 Area B2	5	04-Feb-19	08-Feb-19	8
SS2E2-8P5G	Precast Stadia - Suite Levels 100 to 200 Area E2	4	11-Feb-19	14-Feb-19	9
SS2E3-8P5G	Precast Stadia - Suite Levels 100 to 200 Area E3	4	15-Feb-19	21-Feb-19	9
SS2B3-8P5G	Precast Stadia - Suite Levels 100 to 200 Area B3	4	22-Feb-19	27-Feb-19	9
SS2D1-8P5G	Precast Stadia - Suite Levels 100 to 200 Area D1	4	01-Apr-19	04-Apr-19	4
SS2C1-8P5G	Precast Stadia - Suite Levels 100 to 200 Area C1	4	03-Apr-19	08-Apr-19	0
SS2D2-8P5G	Precast Stadia - Suite Levels 100 to 200 Area D2	2	17-Apr-19	18-Apr-19	4
SS2C2-8P5G	Precast Stadia - Suite Levels 100 to 200 Area C2	3	22-Apr-19	24-Apr-19	0
SS2A1-8P5G1	Precast Stadia - Detailing - Suite Levels 100 to 200 Area A1	7	29-Nov-18	07-Dec-18	123
SS2F1-8P5G1	Precast Stadia - Detailing - Suite Levels 100 to 200 Area F1	6	10-Jan-19	17-Jan-19	96
SS2E1-8P5G1	Precast Stadia - Detailing - Suite Levels 100 to 200 Area E1	4	24-Jan-19	29-Jan-19	88
SS2B1-8P5G1	Precast Stadia - Detailing - Suite Levels 100 to 200 Area B1	4	30-Jan-19	04-Feb-19	84
SS2B2-8P5G1	Precast Stadia - Detailing - Suite Levels 100 to 200 Area B2	5	05-Feb-19	11-Feb-19	79
SS2E2-8P5G1	Precast Stadia - Detailing - Suite Levels 100 to 200 Area E2	4	12-Feb-19	15-Feb-19	75
SS2E3-8P5G1	Precast Stadia - Detailing - Suite Levels 100 to 200 Area E3	4	19-Feb-19	22-Feb-19	76
SS2B3-8P5G1	Precast Stadia - Detailing - Suite Levels 100 to 200 Area B3	4	25-Feb-19	28-Feb-19	72
SS2D1-8P5G1	Precast Stadia - Detailing - Suite Levels 100 to 200 Area D1	4	02-Apr-19	05-Apr-19	46
SS2C1-8P5G1	Precast Stadia - Detailing - Suite Levels 100 to 200 Area C1	4	04-Apr-19	09-Apr-19	44
SS2D2-8P5G1	Precast Stadia - Detailing - Suite Levels 100 to 200 Area D2	2	18-Apr-19	19-Apr-19	36
SS2C2-8P5G1	Precast Stadia - Detailing - Suite Levels 100 to 200 Area C2	3	23-Apr-19	25-Apr-19	32
Upper Seating Bowl (250to 400)					
SS3A1-8P5G	Precast Stadia - Upper Bowl Levels 250 to 400 Area A1	5	17-Dec-18	21-Dec-18	28
SS3F1-8P5G	Precast Stadia - Upper Bowl Levels 250 to 400 Area F1	5	17-Jan-19	23-Jan-19	14
SS3B1-8P5G	Precast Stadia - Upper Bowl Levels 250 to 400 Area B1	13	04-Feb-19	21-Feb-19	0
SS3E1-8P5G	Precast Stadia - Upper Bowl Levels 250 to 400 Area E1	11	07-Feb-19	22-Feb-19	4
SS3E2-8P5G	Precast Stadia - Upper Bowl Levels 250 to 400 Area E2	12	25-Feb-19	12-Mar-19	4
SS3B2-8P5G	Precast Stadia - Upper Bowl Levels 250 to 400 Area B2	13	22-Feb-19	12-Mar-19	0
SS3E3-8P5G	Precast Stadia - Upper Bowl Levels 250 to 400 Area E3	11	13-Mar-19	27-Mar-19	4
SS3B3-8P5G	Precast Stadia - Upper Bowl Levels 250 to 400 Area B3	13	13-Mar-19	29-Mar-19	0
SS3D1-8P5G	Precast Stadia - Upper Bowl Levels 250 to 400 Area D1	8	05-Apr-19	16-Apr-19	4
SS3C1-8P5G	Precast Stadia - Upper Bowl Levels 250 to 400 Area C1	9	09-Apr-19	19-Apr-19	0
SS3D2-8P5G	Precast Stadia - Upper Bowl Levels 250 to 400 Area D2	4	19-Apr-19	24-Apr-19	4
SS3C2-8P5G	Precast Stadia - Upper Bowl Levels 250 to 400 Area C2	4	25-Apr-19	30-Apr-19	0
SS3A1-8P5G1	Precast Stadia - Detailing - Upper Bowl Levels 250 to 400 Area A1	5	18-Dec-18	24-Dec-18	81
SS3F1-8P5G1	Precast Stadia - Detailing - Upper Bowl Levels 250 to 400 Area F1	5	18-Jan-19	24-Jan-19	60
SS3B1-8P5G1	Precast Stadia - Detailing - Upper Bowl Levels 250 to 400 Area B1	13	05-Feb-19	22-Feb-19	122
SS3E1-8P5G1	Precast Stadia - Detailing - Upper Bowl Levels 250 to 400 Area E1	11	08-Feb-19	25-Feb-19	121
SS3E2-8P5G1	Precast Stadia - Detailing - Upper Bowl Levels 250 to 400 Area E2	12	26-Feb-19	13-Mar-19	27
SS3B2-8P5G1	Precast Stadia - Detailing - Upper Bowl Levels 250 to 400 Area B2	13	25-Feb-19	13-Mar-19	27
SS3E3-8P5G1	Precast Stadia - Detailing - Upper Bowl Levels 250 to 400 Area E3	11	14-Mar-19	28-Mar-19	52
SS3B3-8P5G1	Precast Stadia - Detailing - Upper Bowl Levels 250 to 400 Area B3	13	14-Mar-19	01-Apr-19	50
SS3D1-8P5G1	Precast Stadia - Detailing - Upper Bowl Levels 250 to 400 Area D1	8	08-Apr-19	17-Apr-19	84
SS3C1-8P5G1	Precast Stadia - Detailing - Upper Bowl Levels 250 to 400 Area C1	9	10-Apr-19	22-Apr-19	81
SS3D2-8P5G1	Precast Stadia - Detailing - Upper Bowl Levels 250 to 400 Area D2	4	22-Apr-19	25-Apr-19	4
SS3C2-8P5G1	Precast Stadia - Detailing - Upper Bowl Levels 250 to 400 Area C2	4	26-Apr-19	01-May-19	0

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
Wall Enclosure Systems					
Exterior Elevations					
SXA3-8Q11	Operable Retractable Wall Glazing System Animation	1	06-May-20	06-May-20	38
Metal Wall Panels					
Exterior Elevations					
SXXE-8Q1F1	Install Metal Panel Ribbons - East	20	12-Aug-19	09-Sep-19	40
SXXN-8Q1F1	Install Metal Panel Ribbons - North	20	23-Sep-19	18-Oct-19	11
SXXW-8Q1F1	Install Metal Panel Ribbons - West	20	15-Nov-19	16-Dec-19	13
SXXS-8Q1F1	Install Metal Panel Ribbons - South	20	21-Nov-19	20-Dec-19	9
Curtain Wall					
Exterior Elevations					
SXXE0-8Q2A0	Curtainwall - Complete Survey - East	5	19-Mar-19	25-Mar-19	21
SXXN0-8Q2A	Curtainwall - Complete Survey - North	5	25-Mar-19	29-Mar-19	19
SXXW0-8Q2A0	Curtainwall - Complete Survey - West	5	15-Apr-19	19-Apr-19	67
SXXS0-8Q2A0	Curtainwall - Complete Survey - South	5	17-May-19	23-May-19	36
SXXE1-8Q2A1	Curtainwall - Layout - East Stack 1	5	16-Apr-19	22-Apr-19	6
SXXN1-8Q2A1	Curtainwall - Layout - North Stack 1	5	18-Apr-19	24-Apr-19	6
SXXE2-8Q2A1	Curtainwall - Layout - East Stack 2	4	23-Apr-19	26-Apr-19	6
SXXN2-8Q2A1	Curtainwall - Layout - North Stack 2	5	25-Apr-19	01-May-19	6
SXXE3-8Q2A1	Curtainwall - Layout - East Stack 3	4	29-Apr-19	02-May-19	6
SXXN3-8Q2A1	Curtainwall - Layout - North Stack 3	5	02-May-19	08-May-19	6
SXXE4-8Q2A1	Curtainwall - Layout - East Stack 4	4	03-May-19	08-May-19	26
SXXN4-8Q2A1	Curtainwall - Layout - North Stack 4	3	09-May-19	13-May-19	31
SXXE5-8Q2A1	Curtainwall - Layout - East Stack 5	4	09-May-19	14-May-19	26
SXXN5-8Q2A1	Curtainwall - Layout - North Stack 5	3	14-May-19	16-May-19	31
SXXE6-8Q2A1	Curtainwall - Layout - East Stack 6	4	15-May-19	20-May-19	26
SXXN6-8Q2A1	Curtainwall - Layout - North Stack 6	3	17-May-19	21-May-19	31
SXXE7-8Q2A1	Curtainwall - Layout - East Stack 7	4	21-May-19	24-May-19	26
SXXN7-8Q2A1	Curtainwall - Layout - North Stack 7	5	22-May-19	29-May-19	31
SXXE8-8Q2A1	Curtainwall - Layout - East Stack 8	4	28-May-19	31-May-19	26
SXXN8-8Q2A1	Curtainwall - Layout - North Stack 8	5	30-May-19	05-Jun-19	31
SXXE9-8Q2A1	Curtainwall - Layout - East Stack 9	5	03-Jun-19	07-Jun-19	26
SXXN9-8Q2A1	Curtainwall - Layout - North Stack 9	4	06-Jun-19	11-Jun-19	31
SXXS1-8Q2A1	Curtainwall - Layout - South Stack 1	5	10-Jun-19	14-Jun-19	26
SXXW1-8Q2A1	Curtainwall - Layout - West Stack 1	5	12-Jun-19	18-Jun-19	31
SXXS2-8Q2A1	Curtainwall - Layout - South Stack 2	5	17-Jun-19	21-Jun-19	26
SXXW2-8Q2A1	Curtainwall - Layout - West Stack 2	4	19-Jun-19	24-Jun-19	31
SXXS3-8Q2A1	Curtainwall - Layout - South Stack 3	5	24-Jun-19	28-Jun-19	26
SXXW3-8Q2A1	Curtainwall - Layout - West Stack 3	4	25-Jun-19	28-Jun-19	31
SXXW4-8Q2A1	Curtainwall - Layout - West Stack 4	4	01-Jul-19	05-Jul-19	57
SXXS4-8Q2A1	Curtainwall - Layout - South Stack 4	5	01-Jul-19	08-Jul-19	32
SXXW5-8Q2A1	Curtainwall - Layout - West Stack 5	4	08-Jul-19	11-Jul-19	59
SXXS5-8Q2A1	Curtainwall - Layout - South Stack 5	5	09-Jul-19	15-Jul-19	53
SXXW6-8Q2A1	Curtainwall - Layout - West Stack 6	4	12-Jul-19	17-Jul-19	59
SXXS6-8Q2A1	Curtainwall - Layout - South Stack 6	5	16-Jul-19	22-Jul-19	53
SXXW7-8Q2A1	Curtainwall - Layout - West Stack 7	4	18-Jul-19	23-Jul-19	59
SXXS7-8Q2A1	Curtainwall - Layout - South Stack 7	5	23-Jul-19	29-Jul-19	53
SXXW8-8Q2A1	Curtainwall - Layout - West Stack 8	4	24-Jul-19	29-Jul-19	59
SXXS8-8Q2A1	Curtainwall - Layout - South Stack 8	5	30-Jul-19	05-Aug-19	53
SXXW9-8Q2A1	Curtainwall - Layout - West Stack 9	9	30-Jul-19	09-Aug-19	59
SXXS9-8Q2A1	Curtainwall - Layout - South Stack 9	4	06-Aug-19	09-Aug-19	73
SXXE1-8Q2A2	Curtainwall - Install Anchors - East Stack 1	9	03-May-19	15-May-19	6
SXXE2-8Q2A2	Curtainwall - Install Anchors - East Stack 2	4	16-May-19	21-May-19	6
SXXN1-8Q2A2	Curtainwall - Install Anchors - North Stack 1	11	09-May-19	23-May-19	6
SXXE3-8Q2A2	Curtainwall - Install Anchors - East Stack 3	4	22-May-19	28-May-19	16
SXXN2-8Q2A2	Curtainwall - Install Anchors - North Stack 2	5	24-May-19	31-May-19	6

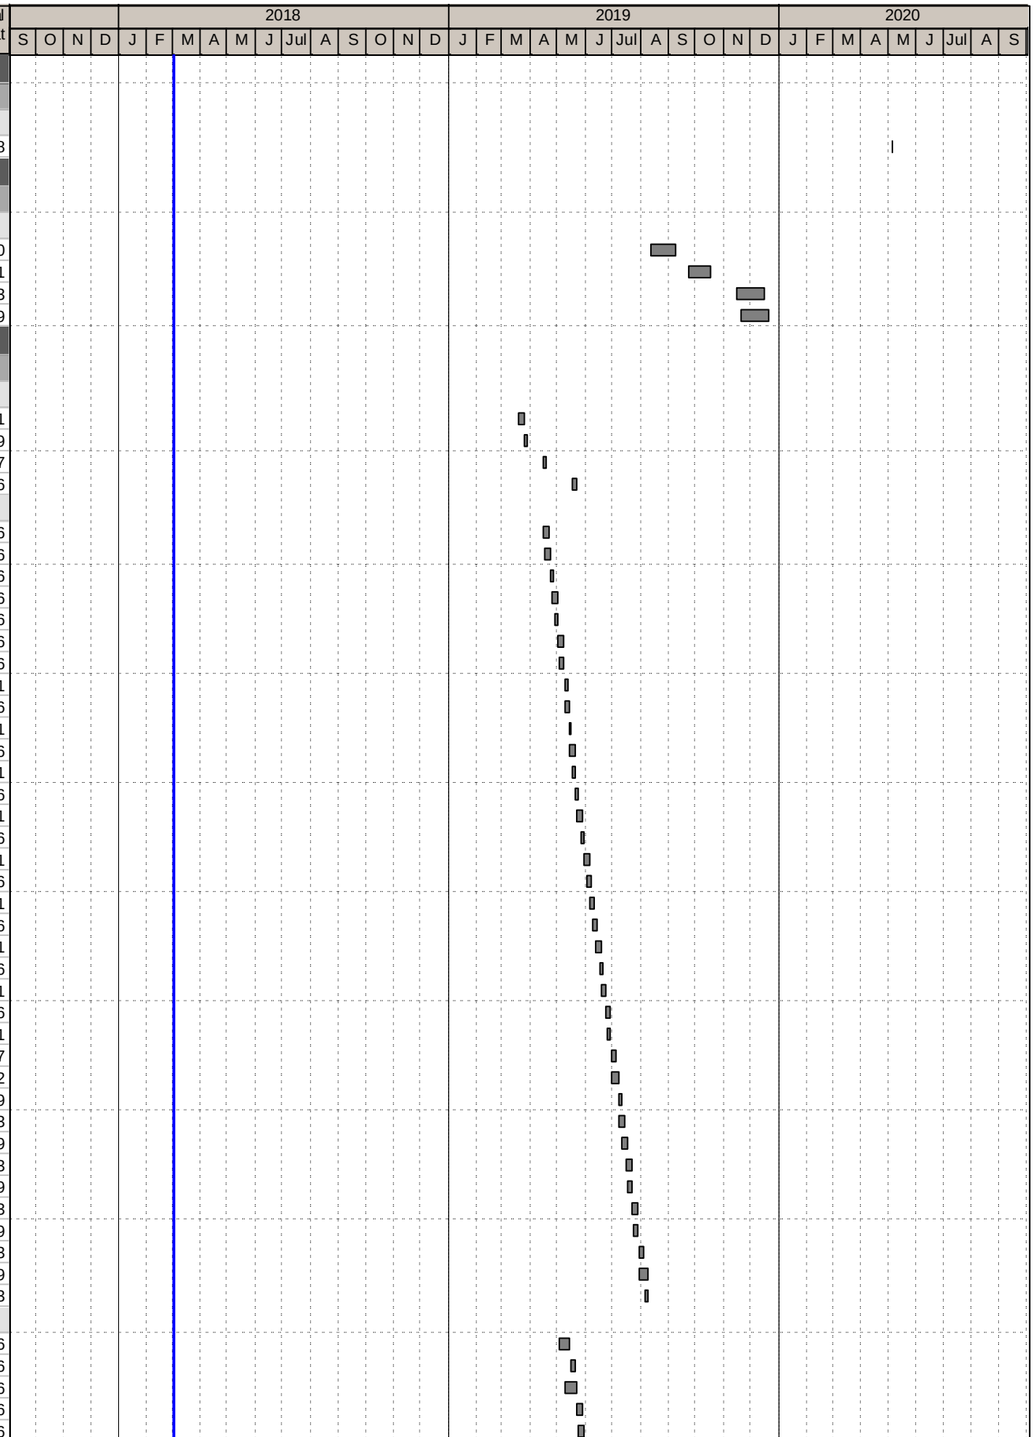

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
SXXE4-8Q2A2	Curtainwall - Install Anchors - East Stack 4	4	29-May-19	03-Jun-19	19
SXXN3-8Q2A2	Curtainwall - Install Anchors - North Stack 3	5	03-Jun-19	07-Jun-19	17
SXXE5-8Q2A2	Curtainwall - Install Anchors - East Stack 5	4	04-Jun-19	07-Jun-19	20
SXXN4-8Q2A2	Curtainwall - Install Anchors - North Stack 4	3	10-Jun-19	12-Jun-19	17
SXXE6-8Q2A2	Curtainwall - Install Anchors - East Stack 6	4	10-Jun-19	13-Jun-19	20
SXXN5-8Q2A2	Curtainwall - Install Anchors - North Stack 5	3	13-Jun-19	17-Jun-19	17
SXXE7-8Q2A2	Curtainwall - Install Anchors - East Stack 7	4	14-Jun-19	19-Jun-19	20
SXXN6-8Q2A2	Curtainwall - Install Anchors - North Stack 6	3	18-Jun-19	20-Jun-19	17
SXXE8-8Q2A2	Curtainwall - Install Anchors - East Stack 8	4	20-Jun-19	25-Jun-19	20
SXXN7-8Q2A2	Curtainwall - Install Anchors - North Stack 7	11	21-Jun-19	08-Jul-19	17
SXXE9-8Q2A2	Curtainwall - Install Anchors - East Stack 9	9	26-Jun-19	09-Jul-19	20
SXXN8-8Q2A2	Curtainwall - Install Anchors - North Stack 8	5	09-Jul-19	15-Jul-19	17
SXXN9-8Q2A2	Curtainwall - Install Anchors - North Stack 9	4	16-Jul-19	19-Jul-19	17
SXXS1-8Q2A2	Curtainwall - Install Anchors - South Stack 1	11	10-Jul-19	24-Jul-19	20
SXXS2-8Q2A2	Curtainwall - Install Anchors - South Stack 2	5	25-Jul-19	31-Jul-19	20
SXXW1-8Q2A2	Curtainwall - Install Anchors - West Stack 1	9	22-Jul-19	01-Aug-19	17
SXXS3-8Q2A2	Curtainwall - Install Anchors - South Stack 3	5	01-Aug-19	07-Aug-19	31
SXXW2-8Q2A2	Curtainwall - Install Anchors - West Stack 2	4	02-Aug-19	07-Aug-19	17
SXXW3-8Q2A2	Curtainwall - Install Anchors - West Stack 3	4	08-Aug-19	13-Aug-19	27
SXXS4-8Q2A2	Curtainwall - Install Anchors - South Stack 4	5	08-Aug-19	14-Aug-19	34
SXXW4-8Q2A2	Curtainwall - Install Anchors - West Stack 4	4	14-Aug-19	19-Aug-19	30
SXXS5-8Q2A2	Curtainwall - Install Anchors - South Stack 5	5	15-Aug-19	21-Aug-19	37
SXXW5-8Q2A2	Curtainwall - Install Anchors - West Stack 5	4	20-Aug-19	23-Aug-19	33
SXXS6-8Q2A2	Curtainwall - Install Anchors - South Stack 6	5	22-Aug-19	28-Aug-19	40
SXXW6-8Q2A2	Curtainwall - Install Anchors - West Stack 6	4	26-Aug-19	29-Aug-19	36
SXXS7-8Q2A2	Curtainwall - Install Anchors - South Stack 7	5	29-Aug-19	05-Sep-19	40
SXXW7-8Q2A2	Curtainwall - Install Anchors - West Stack 7	4	30-Aug-19	05-Sep-19	39
SXXW8-8Q2A2	Curtainwall - Install Anchors - West Stack 8	4	06-Sep-19	11-Sep-19	40
SXXS8-8Q2A2	Curtainwall - Install Anchors - South Stack 8	11	06-Sep-19	20-Sep-19	40
SXXW9-8Q2A2	Curtainwall - Install Anchors - West Stack 9	9	12-Sep-19	24-Sep-19	40
SXXS9-8Q2A2	Curtainwall - Install Anchors - South Stack 9	4	23-Sep-19	26-Sep-19	44
SXXE1-8Q2A3	Curtainwall - Install Units - East Stack 1	7	22-May-19	31-May-19	6
SXXE2-8Q2A3	Curtainwall - Install Units - East Stack 2	7	03-Jun-19	11-Jun-19	6
SXXN1-8Q2A3	Curtainwall - Install Units - North Stack 1	8	03-Jun-19	12-Jun-19	6
SXXE3-8Q2A3	Curtainwall - Install Units - East Stack 3	7	12-Jun-19	20-Jun-19	6
SXXN2-8Q2A3	Curtainwall - Install Units - North Stack 2	8	13-Jun-19	24-Jun-19	6
SXXE4-8Q2A3	Curtainwall - Install Units - East Stack 4	7	21-Jun-19	01-Jul-19	6
SXXN3-8Q2A3	Curtainwall - Install Units - North Stack 3	8	25-Jun-19	05-Jul-19	6
SXXE5-8Q2A3	Curtainwall - Install Units - East Stack 5	7	02-Jul-19	11-Jul-19	6
SXXN4-8Q2A3	Curtainwall - Install Units - North Stack 4	5	08-Jul-19	12-Jul-19	6
SXXN5-8Q2A3	Curtainwall - Install Units - North Stack 5	5	15-Jul-19	19-Jul-19	6
SXXE6-8Q2A3	Curtainwall - Install Units - East Stack 6	7	12-Jul-19	22-Jul-19	6
SXXN6-8Q2A3	Curtainwall - Install Units - North Stack 6	5	22-Jul-19	26-Jul-19	6
SXXE7-8Q2A3	Curtainwall - Install Units - East Stack 7	7	23-Jul-19	31-Jul-19	6
SXXN7-8Q2A3	Curtainwall - Install Units - North Stack 7	8	29-Jul-19	07-Aug-19	6
SXXE8-8Q2A3	Curtainwall - Install Units - East Stack 8	7	01-Aug-19	09-Aug-19	6
SXXN8-8Q2A3	Curtainwall - Install Units - North Stack 8	8	08-Aug-19	19-Aug-19	6
SXXE9-8Q2A3	Curtainwall - Install Units - East Stack 9	7	12-Aug-19	20-Aug-19	6
SXXN9-8Q2A3	Curtainwall - Install Units - North Stack 9	3	20-Aug-19	22-Aug-19	6
SXXS1-8Q2A3	Curtainwall - Install Units - South Stack 1	8	21-Aug-19	30-Aug-19	6
SXXW1-8Q2A3	Curtainwall - Install Units - West Stack 1	7	23-Aug-19	03-Sep-19	6
SXXS2-8Q2A3	Curtainwall - Install Units - South Stack 2	8	03-Sep-19	12-Sep-19	6
SXXW2-8Q2A3	Curtainwall - Install Units - West Stack 2	7	04-Sep-19	12-Sep-19	6
SXXW3-8Q2A3	Curtainwall - Install Units - West Stack 3	7	13-Sep-19	23-Sep-19	6
SXXS3-8Q2A3	Curtainwall - Install Units - South Stack 3	8	13-Sep-19	24-Sep-19	6
SXXW4-8Q2A3	Curtainwall - Install Units - West Stack 4	7	24-Sep-19	02-Oct-19	6
SXXS4-8Q2A3	Curtainwall - Install Units - South Stack 4	8	25-Sep-19	04-Oct-19	6
SXXW5-8Q2A3	Curtainwall - Install Units - West Stack 5	7	03-Oct-19	11-Oct-19	6
SXXS5-8Q2A3	Curtainwall - Install Units - South Stack 5	8	07-Oct-19	16-Oct-19	6
SXXW6-8Q2A3	Curtainwall - Install Units - West Stack 6	7	14-Oct-19	22-Oct-19	6
SXXS6-8Q2A3	Curtainwall - Install Units - South Stack 6	8	17-Oct-19	28-Oct-19	6
SXXW7-8Q2A3	Curtainwall - Install Units - West Stack 7	7	23-Oct-19	31-Oct-19	6

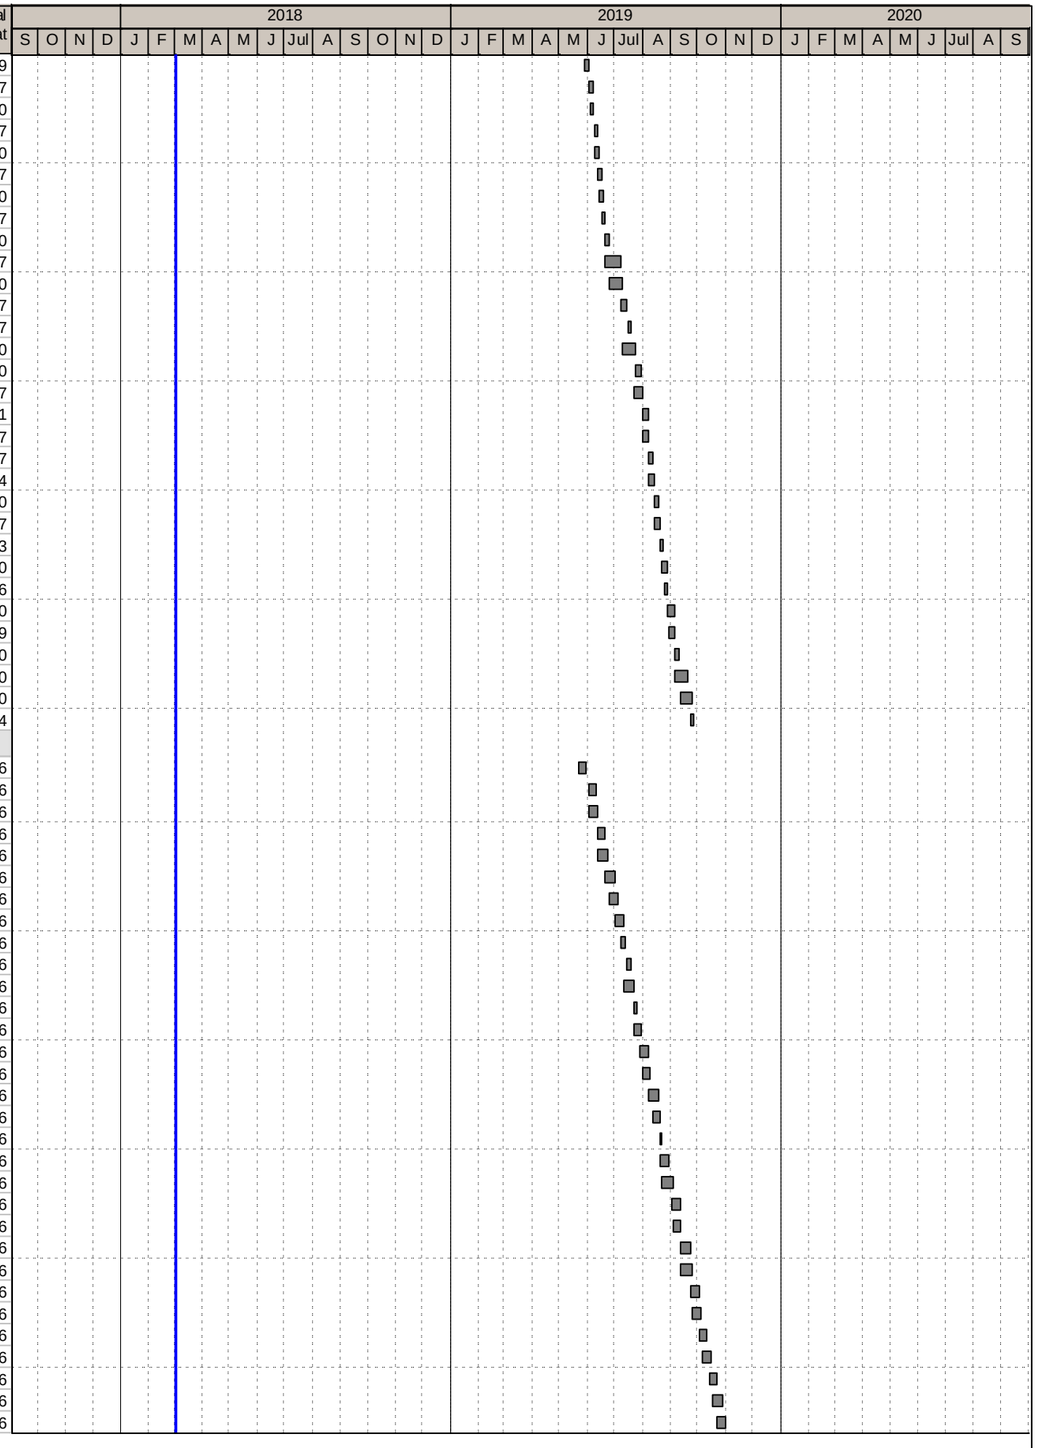

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
SXXS7-8Q2A3	Curtainwall - Install Units - South Stack 7	8	29-Oct-19	07-Nov-19	6
SXXW8-8Q2A3	Curtainwall - Install Units - West Stack 8	7	01-Nov-19	12-Nov-19	6
SXXS8-8Q2A3	Curtainwall - Install Units - South Stack 8	8	08-Nov-19	20-Nov-19	6
SXXW9-8Q2A3	Curtainwall - Install Units - West Stack 9	7	13-Nov-19	21-Nov-19	6
SXXS9-8Q2A3	Curtainwall - Install Units - South Stack 9	3	21-Nov-19	25-Nov-19	6
SXXE-8Q2A6	Install Expansion Joints - East	20	07-Aug-19	04-Sep-19	43
SXXN-8Q2A6	Install Expansion Joints - North	20	09-Aug-19	06-Sep-19	21
SXXW-8Q2A6	Install Expansion Joints - West	20	07-Nov-19	09-Dec-19	6
SXXS-8Q2A6	Install Expansion Joints - South	20	12-Nov-19	11-Dec-19	6
Storefront Glazing System					
Exterior Elevations					
SXXE-8Q3C1	Storefront - Layout - East	10	06-Aug-19	19-Aug-19	53
SXXN-8Q3C1	Storefront - Layout - North	10	12-Aug-19	23-Aug-19	59
SXXS-8Q3C1	Storefront - Layout - South	10	20-Aug-19	03-Sep-19	58
SXXW-8Q3C1	Storefront - Layout - West	10	26-Aug-19	09-Sep-19	68
SXXE-8Q3C2	Storefront - Install Anchors - East	10	16-Aug-19	29-Aug-19	53
SXXN-8Q3C2	Storefront - Install Anchors - North	10	22-Aug-19	05-Sep-19	59
SXXS-8Q3C2	Storefront - Install Anchors - South	10	30-Aug-19	13-Sep-19	58
SXXW-8Q3C2	Storefront - Install Anchors - West	10	06-Sep-19	19-Sep-19	68
SXXE-8Q3C3	Storefront - Install Storefront - East	6	30-Aug-19	09-Sep-19	52
SXXN-8Q3C3	Storefront - Install Storefront - North	7	16-Sep-19	24-Sep-19	51
SXXS-8Q3C3	Storefront - Install Storefront - South	7	14-Oct-19	22-Oct-19	36
SXXW-8Q3C3	Storefront - Install Storefront - West	7	28-Oct-19	05-Nov-19	40
SXXE-8Q3C4	Storefront - Install Doors - East	6	12-Sep-19	19-Sep-19	52
SXXN-8Q3C4	Storefront - Install Doors - North	7	26-Sep-19	04-Oct-19	51
SXXS-8Q3C4	Storefront - Install Doors - South	7	24-Oct-19	01-Nov-19	36
SXXW-8Q3C4	Storefront - Install Doors - West	7	07-Nov-19	18-Nov-19	40
Specialty Entrances					
Exterior Elevations					
SXXN-8Q3S1	Op Doors - Install Rails - North Operable Doors	50	26-Nov-18	05-Feb-19	60
SXXN-8Q3S2	Op Doors - Install Door Mechanization - North Operable Doors	40	24-Sep-19	19-Nov-19	10
SXXN2-8Q3S3	Op Doors - Assemble Door Frame - North Operable Door #2	5	07-Dec-18	13-Dec-18	14
SXXN3-8Q3S3	Op Doors - Assemble Door Frame - North Operable Door #3	5	14-Dec-18	20-Dec-18	14
SXXN4-8Q3S3	Op Doors - Assemble Door Frame - North Operable Door #4	5	21-Dec-18	28-Dec-18	14
SXXN5-8Q3S3	Op Doors - Assemble Door Frame - North Operable Door #5	5	31-Dec-18	07-Jan-19	14
SXXN2-8Q3S4	Op Doors - Erect Door Frame - North Operable Door #2	5	18-Apr-19	24-Apr-19	10
SXXN3-8Q3S4	Op Doors - Erect Door Frame - North Operable Door #3	5	25-Apr-19	01-May-19	25
SXXN4-8Q3S4	Op Doors - Erect Door Frame - North Operable Door #4	5	02-May-19	08-May-19	30
SXXN5-8Q3S4	Op Doors - Erect Door Frame - North Operable Door #5	5	09-May-19	15-May-19	65
SXXN1-8Q3S6	Op Doors - Layout Anchors - North Operable Door #1	10	25-Apr-19	08-May-19	10
SXXN2-8Q3S6	Op Doors - Layout Anchors - North Operable Door #2	10	09-May-19	22-May-19	10
SXXN3-8Q3S6	Op Doors - Layout Anchors - North Operable Door #3	10	23-May-19	06-Jun-19	10
SXXN4-8Q3S6	Op Doors - Layout Anchors - North Operable Door #4	10	07-Jun-19	20-Jun-19	10
SXXN5-8Q3S6	Op Doors - Layout Anchors - North Operable Door #5	10	21-Jun-19	05-Jul-19	40
SXXN6-8Q3S6	Op Doors - Layout Anchors - North Operable Door #6	10	08-Jul-19	19-Jul-19	40
SXXN1-8Q3S7	Op Doors - Install Anchors on Frame - North Operable Door #1	10	09-May-19	22-May-19	10
SXXN2-8Q3S7	Op Doors - Install Anchors on Frame - North Operable Door #2	10	23-May-19	06-Jun-19	10
SXXN3-8Q3S7	Op Doors - Install Anchors on Frame - North Operable Door #3	10	07-Jun-19	20-Jun-19	10
SXXN4-8Q3S7	Op Doors - Install Anchors on Frame - North Operable Door #4	10	21-Jun-19	05-Jul-19	10

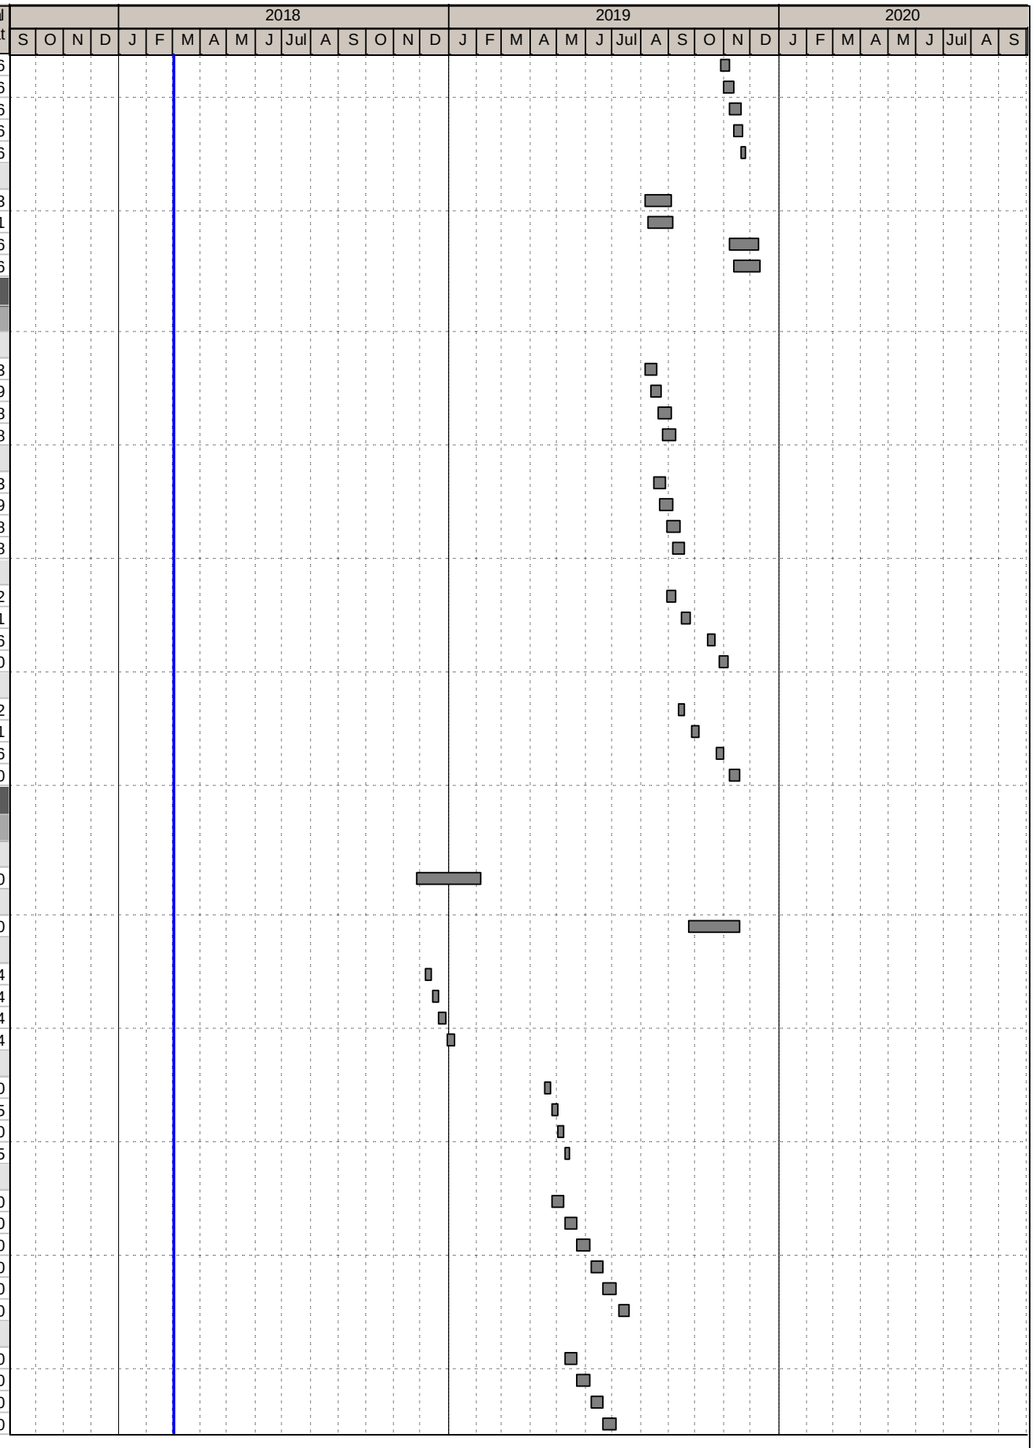

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
SXXN5-8Q3S7	Op Doors - Install Anchors on Frame - North Operable Door #5	10	08-Jul-19	19-Jul-19	40
SXXN6-8Q3S7	Op Doors - Install Anchors on Frame - North Operable Door #6	10	22-Jul-19	02-Aug-19	40
SXXN1-8Q3S8	Op Doors - Install CW Units - North Operable Door #1	5	08-Jul-19	12-Jul-19	10
SXXN2-8Q3S8	Op Doors - Install CW Units - North Operable Door #2	5	15-Jul-19	19-Jul-19	15
SXXN3-8Q3S8	Op Doors - Install CW Units - North Operable Door #3	5	22-Jul-19	26-Jul-19	20
SXXN4-8Q3S8	Op Doors - Install CW Units - North Operable Door #4	5	29-Jul-19	02-Aug-19	25
SXXN5-8Q3S8	Op Doors - Install CW Units - North Operable Door #5	5	05-Aug-19	09-Aug-19	30
SXXN6-8Q3S8	Op Doors - Install CW Units - North Operable Door #6	5	12-Aug-19	16-Aug-19	35
SXXN1-8Q3S9	Op Doors - Final Trim on Doors - North Operable Door #1	10	15-Jul-19	26-Jul-19	10
SXXN2-8Q3S9	Op Doors - Final Trim on Doors - North Operable Door #2	10	29-Jul-19	09-Aug-19	10
SXXN3-8Q3S9	Op Doors - Final Trim on Doors - North Operable Door #3	10	12-Aug-19	23-Aug-19	10
SXXN4-8Q3S9	Op Doors - Final Trim on Doors - North Operable Door #4	10	26-Aug-19	09-Sep-19	10
SXXN5-8Q3S9	Op Doors - Final Trim on Doors - North Operable Door #5	10	10-Sep-19	23-Sep-19	10
SXXN6-8Q3S9	Op Doors - Final Trim on Doors - North Operable Door #6	10	24-Sep-19	07-Oct-19	10
Roof Systems					
Roof Level					
SR10N-8Q502	Cable Net - Install Timber Crane Mats - North	5	18-Mar-19	22-Mar-19	45
SR100-8Q5031	Cable Net - Mob In Crane 1	2	04-Apr-19	05-Apr-19	37
SR10S-8Q502	Cable Net - Install Timber Crane Mats - South	5	06-May-19	10-May-19	10
SR100-8Q5032	Cable Net - Mob In Crane 2	2	22-May-19	23-May-19	3
SR100-8Q5041	Cable Net - Mob Out Crane 1	2	03-Jul-19	05-Jul-19	0
SR100-8Q5042	Cable Net - Mob Out Crane 2	2	03-Jul-19	05-Jul-19	0
SR101-8Q52	Cable Net - Set Temp Work Platforms & Pump Platforms - Area 1 Grids 7-20	7	18-Apr-19	26-Apr-19	14
SR103-8Q52	Cable Net - Set Temp Work Platforms & Pump Stations - Area 3 Grids 20-26	3	29-Apr-19	01-May-19	14
SR102-8Q52	Cable Net - Set Temp Work Platforms & Pump Stations - Area 2 Grids 7-1	3	02-May-19	06-May-19	14
SR105-8Q52	Cable Net - Set Temp Work Platforms & Pump Stations - Area 5 Grids 26-32	3	07-May-19	09-May-19	14
SR104-8Q52	Cable Net - Set Temp Work Platforms & Pump Stations - Area 4 Grids 1-45	3	10-May-19	14-May-19	14
SR106-8Q52	Cable Net - Set Temp Work Platforms & Pump Stations - Area 6 Grids 32-45	6	28-May-19	04-Jun-19	12
SR101-8Q53	Cable Net - Set Jacks & Pumps - Area 1 Grids 7-20	4	15-May-19	20-May-19	14
SR102-8Q53	Cable Net - Set Jacks & Pumps - Area 2 Grids 7-1	2	21-May-19	22-May-19	14
SR103-8Q53	Cable Net - Set Jacks & Pumps - Area 3 Grids 20-26	2	23-May-19	24-May-19	14
SR104-8Q53	Cable Net - Set Jacks & Pumps - Area 4 Grids 1-45	2	28-May-19	29-May-19	14
SR105-8Q53	Cable Net - Set Jacks & Pumps - Area 5 Grids 26-32	2	30-May-19	31-May-19	14
SR106-8Q53	Cable Net - Set Jacks & Pumps - Area 6 Grids 32-45	4	05-Jun-19	10-Jun-19	12
SR10N-8Q501	Cable Net - Survey/Marking at Strut Nodes on Ground - North	2	14-Mar-19	15-Mar-19	27
SR10N-8Q55	Cable Net - Install Node Templates on Ground - North	3	18-Mar-19	20-Mar-19	27
SR10N-8Q552	Cable Net - Install Cable Support Timber on Ground - North	10	21-Mar-19	03-Apr-19	27
SR10N-8Q553	Cable Net - Erect Temp Cable Support Towers & Pull Beam Platforms - North	20	14-Mar-19	10-Apr-19	36
SR10S-8Q501	Cable Net - Survey/Marking at Strut Nodes on Ground - South	2	02-May-19	03-May-19	3
SR10S-8Q55	Cable Net - Install Node Templates on Ground - South	3	06-May-19	08-May-19	3
SR10S-8Q552	Cable Net - Install Cable Support Timber on Ground - South	10	08-May-19	21-May-19	3
SR10S-8Q553	Cable Net - Erect Temp Cable Support Towers & Pull Beam Platforms - South	20	02-May-19	30-May-19	0
SR10N-8Q554	Cable Net - Survey/Marking on Temp Cable Support Towers - North	2	14-Mar-19	15-Mar-19	58
SR10N-8Q551	Cable Net - Install Clamp-Templates on Precast Concrete/Timber Supports on Towers - North	8	18-Mar-19	27-Mar-19	58
SR10N-8Q54	Cable Net - Install Timber Protection on Precast - North	5	28-Mar-19	03-Apr-19	58
SR10S-8Q554	Cable Net - Survey/Marking on Temp Cable Support Towers - South	2	02-May-19	03-May-19	28
SR10S-8Q551	Cable Net - Install Clamp-Templates on Precast Concrete/Timber Supports on Towers - South	8	06-May-19	15-May-19	28
SR10S-8Q54	Cable Net - Install Timber Protection on Precast - South	5	16-May-19	22-May-19	28
SR100-8Q541	Cable Net - Setup Turn Tables & Winches	1	24-May-19	24-May-19	3
SR100-8Q571	Cable Net - Install Longitudinal Bottom Cables	4	31-May-19	05-Jun-19	0
SR100-8Q573	Cable Net - Install Transverse Bot & Top Cables	8	06-Jun-19	17-Jun-19	0
SR100-8Q572	Cable Net - Install Longitudinal Top Cables	3	18-Jun-19	20-Jun-19	0
SR100-8Q574	Cable Net - Install Pulling Beams	10	07-Jun-19	20-Jun-19	0

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
SR100-8Q577	Cable Net - Lay Down Struts	8	21-Jun-19	02-Jul-19	0
SR100-8Q580	Cable Net - Survey at Compression Ring Lugs	3	28-May-19	30-May-19	23
SR100-8Q581	Cable Net - Make Final Connections from Pumps to Jacks	5	10-Jun-19	14-Jun-19	15
SR100-8Q582	Cable Net - Final Prep for Big Lift	3	03-Jul-19	06-Jul-19	0
SR100-8Q583	Cable Net - Jack Cables Lift Upper Net - Step 1 (2 shifts)	10	08-Jul-19	18-Jul-19	0
SR100-8Q584	Cable Net - Final Connection to Struts	10	08-Jul-19	18-Jul-19	3
SR100-8Q588	Cable Net - Jack Cables Lift Upper Net - Step 2	3	19-Jul-19	22-Jul-19	0
SR100-8Q585	Cable Net - Jack to Pin Upper	7	23-Jul-19	30-Jul-19	0
SR100-8Q586	Cable Net - Transfer Connecting Pieces (2 shifts)	8	24-Jul-19	01-Aug-19	0
SR100-8Q587	Cable Net - Jack to Pin Lower	6	02-Aug-19	08-Aug-19	0
SR100-8Q591	Cable Net - Remove Lower Pulling Beams	7	09-Aug-19	19-Aug-19	3
SR100-8Q592	Cable Net - Remove Platforms	7	09-Aug-19	19-Aug-19	3
SR100-8Q593	Cable Net - Re-Torque Bolts on Nodes - Bottom Net	9	09-Aug-19	21-Aug-19	3
SR100-8Q594	Cable Net - Re-Torque Bolts on Nodes - Top Net	9	09-Aug-19	21-Aug-19	3
SR00-8Q52	Install ETFE Roof System (Summary)	90	09-Aug-19	18-Dec-19	3
Membrane Roof					
Roof Level					
SRA0-8Q50	Roof Systems at Outer Canopy - Roof Level A	14	17-May-19	06-Jun-19	38
SRF0-8Q50	Roof Systems at Outer Canopy - Roof Level F	14	17-May-19	06-Jun-19	47
SRB0-8Q50	Roof Systems at Outer Canopy - Roof Level B	26	07-Jun-19	15-Jul-19	38
SRE0-8Q50	Roof Systems at Outer Canopy - Roof Level E	26	07-Jun-19	15-Jul-19	47
SRC0-8Q50	Roof Systems at Outer Canopy - Roof Level C	14	16-Jul-19	02-Aug-19	38
SRD0-8Q50	Roof Systems at Outer Canopy - Roof Level D	14	16-Jul-19	02-Aug-19	50
SRA0-8Q51	Complete Roof Systems at Outer Canopy after Big Lift - Roof Level A	5	19-Aug-19	23-Aug-19	16
SRF0-8Q51	Complete Roof Systems at Outer Canopy after Big Lift - Roof Level F	5	19-Aug-19	23-Aug-19	47
SRB0-8Q51	Complete Roof Systems at Outer Canopy after Big Lift - Roof Level B	7	26-Aug-19	04-Sep-19	16
SRE0-8Q51	Complete Roof Systems at Outer Canopy after Big Lift - Roof Level E	7	26-Aug-19	04-Sep-19	47
SRC0-8Q51	Complete Roof Systems at Outer Canopy after Big Lift - Roof Level C	5	05-Sep-19	11-Sep-19	16
SRD0-8Q51	Complete Roof Systems at Outer Canopy after Big Lift - Roof Level D	5	05-Sep-19	11-Sep-19	62
Roof Specialties & Accessories					
Roof Level					
SR101-8Q5J2	ETFE - Preassemble Sec Steel - ETFE Area 1	10	09-Aug-19	22-Aug-19	3
SR102-8Q5J2	ETFE - Preassemble Sec Steel - ETFE Area 2	15	23-Aug-19	13-Sep-19	3
SR103-8Q5J2	ETFE - Preassemble Sec Steel - ETFE Area 3	10	16-Sep-19	27-Sep-19	3
SR104-8Q5J2	ETFE - Preassemble Sec Steel - ETFE Area 4	10	30-Sep-19	11-Oct-19	3
SR105-8Q5J2	ETFE - Preassemble Sec Steel - ETFE Area 5	15	14-Oct-19	01-Nov-19	6
SR106-8Q5J2	ETFE - Preassemble Sec Steel - ETFE Area 6	10	04-Nov-19	18-Nov-19	7
SR101-8Q5J3	ETFE - Ground Install Extrusions - ETFE Area 1	10	09-Aug-19	22-Aug-19	6
SR102-8Q5J3	ETFE - Ground Install Extrusions - ETFE Area 2	15	23-Aug-19	13-Sep-19	6
SR103-8Q5J3	ETFE - Ground Install Extrusions - ETFE Area 3	10	16-Sep-19	27-Sep-19	6
SR104-8Q5J3	ETFE - Ground Install Extrusions - ETFE Area 4	10	30-Sep-19	11-Oct-19	6
SR105-8Q5J3	ETFE - Ground Install Extrusions - ETFE Area 5	15	14-Oct-19	01-Nov-19	9
SR106-8Q5J3	ETFE - Ground Install Extrusions - ETFE Area 6	10	04-Nov-19	18-Nov-19	10
SR101-8Q5J4	ETFE - Set Secondary Steel - ETFE Area 1	10	14-Aug-19	27-Aug-19	3
SR102-8Q5J4	ETFE - Set Secondary Steel - ETFE Area 2	15	28-Aug-19	18-Sep-19	3
SR103-8Q5J4	ETFE - Set Secondary Steel - ETFE Area 3	10	19-Sep-19	02-Oct-19	3
SR104-8Q5J4	ETFE - Set Secondary Steel - ETFE Area 4	10	03-Oct-19	16-Oct-19	3
SR105-8Q5J4	ETFE - Set Secondary Steel - ETFE Area 5	15	17-Oct-19	06-Nov-19	6
SR106-8Q5J4	ETFE - Set Secondary Steel - ETFE Area 6	10	07-Nov-19	21-Nov-19	7
SR101-8Q5J5	ETFE - Detail Sec Steel (Bolt/Painting) - ETFE Area 1	10	19-Aug-19	30-Aug-19	3
SR102-8Q5J5	ETFE - Detail Sec Steel (Bolt/Painting) - ETFE Area 2	15	03-Sep-19	23-Sep-19	3
SR103-8Q5J5	ETFE - Detail Sec Steel (Bolt/Painting) - ETFE Area 3	10	24-Sep-19	07-Oct-19	3

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
SR104-8Q5J5	ETFE - Detail Sec Steel (Bolt/Painting) - ETFE Area 4	10	08-Oct-19	21-Oct-19	3
SR105-8Q5J5	ETFE - Detail Sec Steel (Bolt/Painting) - ETFE Area 5	15	22-Oct-19	12-Nov-19	6
SR106-8Q5J5	ETFE - Detail Sec Steel (Bolt/Painting) - ETFE Area 6	10	13-Nov-19	26-Nov-19	7
SR101-8Q5J7	ETFE - Complete Extrusions - ETFE Area 1	8	29-Aug-19	10-Sep-19	10
SR102-8Q5J7	ETFE - Complete Extrusions - ETFE Area 2	10	18-Sep-19	01-Oct-19	7
SR103-8Q5J7	ETFE - Complete Extrusions - ETFE Area 3	8	04-Oct-19	15-Oct-19	6
SR104-8Q5J7	ETFE - Complete Extrusions - ETFE Area 4	8	22-Oct-19	31-Oct-19	6
SR105-8Q5J7	ETFE - Complete Extrusions - ETFE Area 5	10	07-Nov-19	21-Nov-19	6
SR106-8Q5J7	ETFE - Complete Extrusions - ETFE Area 6	8	25-Nov-19	06-Dec-19	7
SR101-8Q5J8	ETFE - Seals & Patches - ETFE Area 1	2	11-Sep-19	12-Sep-19	10
SR102-8Q5J8	ETFE - Seals & Patches - ETFE Area 2	3	30-Sep-19	02-Oct-19	7
SR103-8Q5J8	ETFE - Seals & Patches - ETFE Area 3	2	18-Oct-19	21-Oct-19	6
SR104-8Q5J8	ETFE - Seals & Patches - ETFE Area 4	2	05-Nov-19	06-Nov-19	6
SR105-8Q5J8	ETFE - Seals & Patches - ETFE Area 5	3	20-Nov-19	22-Nov-19	7
SR106-8Q5J8	ETFE - Seals & Patches - ETFE Area 6	2	09-Dec-19	10-Dec-19	8
SR101-8Q5J11	ETFE - Install Air Units - ETFE Area 1/2	3	18-Sep-19	20-Sep-19	4
SR102-8Q5J11	ETFE - Install Air Units - ETFE Area 2/3	3	10-Oct-19	14-Oct-19	3
SR104-8Q5J11	ETFE - Install Air Units - ETFE Area 4/5	3	31-Oct-19	04-Nov-19	3
SR105-8Q5J11	ETFE - Install Air Units - ETFE Area 5/6	3	22-Nov-19	26-Nov-19	9
SR101-8Q5J12	ETFE - Install Plenum - ETFE Area 1	12	30-Aug-19	17-Sep-19	4
SR102-8Q5J12	ETFE - Install Plenum - ETFE Area 2	12	24-Sep-19	09-Oct-19	3
SR104-8Q5J12	ETFE - Install Plenum - ETFE Area 4	12	15-Oct-19	30-Oct-19	3
SR105-8Q5J12	ETFE - Install Plenum - ETFE Area 5	12	05-Nov-19	21-Nov-19	3
SR101-8Q5J13	ETFE - Install ETFE Cushions - ETFE Area 1	8	23-Sep-19	02-Oct-19	7
SR102-8Q5J13	ETFE - Install ETFE Cushions - ETFE Area 2	12	09-Oct-19	24-Oct-19	3
SR103-8Q5J13	ETFE - Install ETFE Cushions - ETFE Area 3	8	25-Oct-19	05-Nov-19	3
SR104-8Q5J13	ETFE - Install ETFE Cushions - ETFE Area 4	8	06-Nov-19	18-Nov-19	3
SR105-8Q5J13	ETFE - Install ETFE Cushions - ETFE Area 5	12	19-Nov-19	06-Dec-19	3
SR106-8Q5J13	ETFE - Install ETFE Cushions - ETFE Area 6	8	09-Dec-19	18-Dec-19	3
SR101-8Q5J14	ETFE - Remove Netting - ETFE Area 1	8	23-Sep-19	02-Oct-19	7
SR102-8Q5J14	ETFE - Remove Netting - ETFE Area 2	12	09-Oct-19	24-Oct-19	3
SR103-8Q5J14	ETFE - Remove Netting - ETFE Area 3	8	25-Oct-19	05-Nov-19	3
SR104-8Q5J14	ETFE - Remove Netting - ETFE Area 4	8	06-Nov-19	18-Nov-19	3
SR105-8Q5J14	ETFE - Remove Netting - ETFE Area 5	12	19-Nov-19	06-Dec-19	3
SR106-8Q5J14	ETFE - Remove Netting - ETFE Area 6	8	09-Dec-19	18-Dec-19	3
SR101-8Q5J15	ETFE - Top Caps - ETFE Area 1	4	03-Oct-19	08-Oct-19	32
SR102-8Q5J15	ETFE - Top Caps - ETFE Area 2	6	25-Oct-19	01-Nov-19	20
SR103-8Q5J15	ETFE - Top Caps - ETFE Area 3	4	06-Nov-19	12-Nov-19	18
SR104-8Q5J15	ETFE - Top Caps - ETFE Area 4	4	19-Nov-19	22-Nov-19	14
SR105-8Q5J15	ETFE - Top Caps - ETFE Area 5	6	09-Dec-19	16-Dec-19	6
SR106-8Q5J15	ETFE - Top Caps - ETFE Area 6	4	19-Dec-19	24-Dec-19	12
SR101-8Q5J16	ETFE - Comissioning - ETFE Area 1	1	18-Dec-19	18-Dec-19	13
SR102-8Q5J16	ETFE - Comissioning - ETFE Area 2	1	19-Dec-19	19-Dec-19	13
SR103-8Q5J16	ETFE - Comissioning - ETFE Area 3	1	20-Dec-19	20-Dec-19	13
SR104-8Q5J16	ETFE - Comissioning - ETFE Area 4	1	23-Dec-19	23-Dec-19	13
SR105-8Q5J16	ETFE - Comissioning - ETFE Area 5	1	24-Dec-19	24-Dec-19	13
SR106-8Q5J16	ETFE - Comissioning - ETFE Area 6	1	26-Dec-19	26-Dec-19	13
Elevators					
S000-8R10	Elevators (Summary)	282	18-Jan-19	02-Mar-20	23
000 Event Level					

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S1D3-8R11	Elevator Installation - Pass Elev D6 (Event to Lower Suite)	60	19-Feb-19	13-May-19	129
S1A3-8R11	Elevator Installation - Pass Elev AX (Event to Lower Suite)	80	14-Feb-19	07-Jun-19	111
S1B2-8R11	Elevator Installation - Pass Elev B3 (Event to Upper Conc)	80	10-Apr-19	01-Aug-19	106
S1B48R11	Elevator Installation - Pass Elev B1 & B2 (Event to Upper Suite)	140	18-Jan-19	06-Aug-19	83
S1C2-8R11	Elevator Installation - Pass Elev C1 & C2 (Event to Upper Suite)	140	22-Feb-19	10-Sep-19	84
S1A2-8R11	Elevator Installation - Pass Elev A1 & A2 (Event to Upper Suite)	140	28-Feb-19	16-Sep-19	59
S1D4-8R11	Elevator Installation - Pass Elev D1 & D2 (Event to Upper Suite)	140	06-Mar-19	20-Sep-19	85
S1D5-8R11	Elevator Installation - Pass Elev DX (Event to Lower Suite)	80	20-Jun-19	11-Oct-19	95
S1C1-8R11	Elevator Installation - Pass Elev C4 (Event to Upper Mezz)	90	25-Jun-19	30-Oct-19	83
S1A1-8R11	Elevator Installation - Pass Elev A4 & A5 (Event to Upper Mezz)	170	12-Apr-19	13-Dec-19	74
S1B1-8R11	Elevator Installation - Pass Elev B5 & B6 (Event to Upper Mezz)	170	16-May-19	20-Jan-20	52
S1D2-8R11	Elevator Installation - Pass Elev D3 & D4 (Event to Press)	170	20-May-19	22-Jan-20	37
S1A1-8R15	Elevator Installation - Service Elev A3 (Event to Press)	100	26-Mar-19	14-Aug-19	101
S1C1-8R15	Elevator Installation - Freight Elev C3 (Event to Upper Conc)	175	26-Apr-19	07-Jan-20	44
S1D1-8R11	Elevator Installation - Freight Elev D5 (Event to Upper Conc)	175	20-Jun-19	02-Mar-20	23
Escalators					
S000-8R30	Escalators	125	01-Jul-19	30-Dec-19	18
000 Event Level					
S1BB1-8R31	Escalator - Set on Floor - Esc B3 (Event to Lower Mezz)	2	24-Sep-18	25-Sep-18	65
S1AA1-8R31	Escalator - Set on Floor - Esc A3 (Event to Lower Mezz)	2	22-Oct-18	23-Oct-18	47
S1BB2-8R31	Escalator - Set on Floor - Esc B1 & C1 (Event to Lower Mezz)	2	19-Dec-18	20-Dec-18	76
S1AA2-8R31	Escalator - Set on Floor - Esc A1 & D1 (Event to Lower Mezz)	2	21-Jan-19	22-Jan-19	35
S1BB1-8R33	Escalator - Hoist into Wellway - Esc B3 (Event to Lower Mezz)	2	26-Sep-18	27-Sep-18	65
S1AA1-8R33	Escalator - Hoist into Wellway - Esc A3 (Event to Lower Mezz)	2	24-Oct-18	25-Oct-18	47
S1BB2-8R33	Escalator - Hoist into Wellway - Esc B1 & C1 (Event to Lower Mezz)	2	21-Dec-18	24-Dec-18	76
S1AA2-8R33	Escalator - Hoist into Wellway - Esc A1 & D1 (Event to Lower Mezz)	2	23-Jan-19	24-Jan-19	35
S1BB1-8R35	Escalator - Build-out / Installation - Esc B3 (Event to Lower Mezz)	35	06-Feb-19	27-Mar-19	102
S1AA1-8R35	Escalator - Build-out / Installation - Esc A3 (Event to Lower Mezz)	65	06-Feb-19	08-May-19	72
S1AA2-8R35	Escalator - Build-out / Installation - Esc A1 & D1 (Event to Lower Mezz)	70	22-Apr-19	30-Jul-19	75
S1BB2-8R35	Escalator - Build-out / Installation - Esc B1 & C1 (Event to Lower Mezz)	75	25-Apr-19	09-Aug-19	92
050 Lower Mezz Level					
S2AA1-8R31	Escalator - Set on Floor - Esc A5 & A6 (Lower Mezz to Main Conc)	2	25-Sep-18	26-Sep-18	6
S2BB1-8R31	Escalator - Set on Floor - Esc B5 & B6 (Lower Mezz to Main Conc)	2	25-Sep-18	26-Sep-18	1
S2BB2-8R31	Escalator - Set on Floor - Esc B2 & C2 (Lower Mezz to Main Conc)	2	12-Dec-18	13-Dec-18	94
S2AA2-8R31	Escalator - Set on Floor - Esc A2 & D2 (Lower Mezz to Main Conc)	2	28-Dec-18	31-Dec-18	112
S2AA1-8R33	Escalator - Hoist into Wellway - Esc A5 & A6 (Lower Mezz to Main Conc)	2	27-Sep-18	28-Sep-18	136
S2BB1-8R33	Escalator - Hoist into Wellway - Esc B5 & B6 (Lower Mezz to Main Conc)	2	27-Sep-18	28-Sep-18	87
S2BB2-8R33	Escalator - Hoist into Wellway - Esc B2 & C2 (Lower Mezz to Main Conc)	2	14-Dec-18	17-Dec-18	94
S2AA2-8R33	Escalator - Hoist into Wellway - Esc A2 & D2 (Lower Mezz to Main Conc)	2	02-Jan-19	03-Jan-19	112
S2BB2-8R35	Escalator - Build-out / Installation - Esc B2 & C2 (Lower Mezz to Main Conc)	35	12-Jun-19	31-Jul-19	97
S2AA1-8R35	Escalator - Build-out / Installation - Esc A5 & A6 (Lower Mezz to Main Conc)	65	25-Jun-19	25-Sep-19	92
S2BB1-8R35	Escalator - Build-out / Installation - Esc B5 & B6 (Lower Mezz to Main Conc)	65	25-Jun-19	25-Sep-19	63
S2AA2-8R35	Escalator - Build-out / Installation - Esc A2 & D2 (Lower Mezz to Main Conc)	35	13-Sep-19	31-Oct-19	61
100 Main Concourse					
S3BB1-8R31	Escalator - Set on Floor - Esc B7 & B8 (Main Conc to Lower Suite)	2	07-Nov-18	08-Nov-18	35
S3AA1-8R31	Escalator - Set on Floor - Esc A7 & A8 (Main Conc to Lower Suite)	2	03-Dec-18	04-Dec-18	27
S3BB2-8R31	Escalator - Set on Floor - Esc B11 & C3 (Main Conc to Lower Suite)	2	04-Dec-18	05-Dec-18	1
S3AA2-8R31	Escalator - Set on Floor - Esc A11 & D3 (Main Conc to Lower Suite)	2	24-Dec-18	26-Dec-18	13
S3CC1-8R31	Escalator - Set on Floor - Esc C4 & C5 (Main Conc to Upper Suite)	2	30-May-19	31-May-19	22

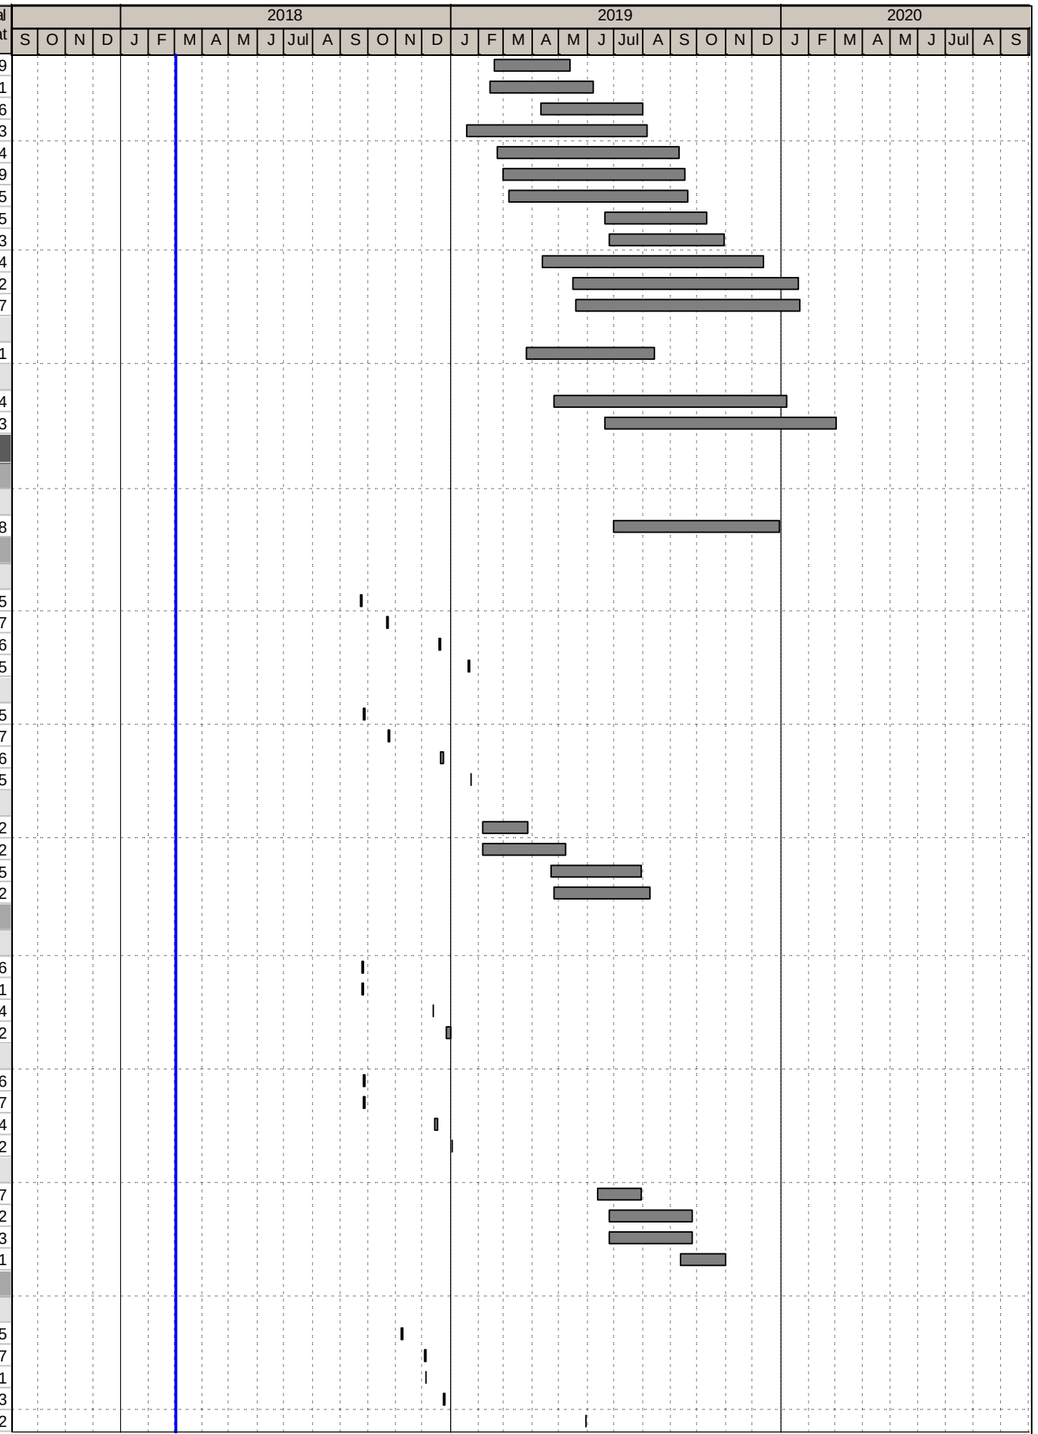

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S3DD1-8R31	Escalator - Set on Floor - Esc D4 & D5 (Main Conc to Upper Suite)	2	30-May-19	31-May-19	32
S3BB1-8R33	Escalator - Hoist into Wellway - Esc B7 & B8 (Main Conc to Lower Suite)	2	09-Nov-18	13-Nov-18	81
S3AA1-8R33	Escalator - Hoist into Wellway - Esc A7 & A8 (Main Conc to Lower Suite)	2	05-Dec-18	06-Dec-18	76
S3BB2-8R33	Escalator - Hoist into Wellway - Esc B11 & C3 (Main Conc to Lower Suite)	2	06-Dec-18	07-Dec-18	95
S3AA2-8R33	Escalator - Hoist into Wellway - Esc A11 & D3 (Main Conc to Lower Suite)	2	27-Dec-18	28-Dec-18	91
S3CC1-8R33	Escalator - Hoist into Wellway - Esc C4 & C5 (Main Conc to Upper Suite)	2	03-Jun-19	04-Jun-19	22
S3DD1-8R33	Escalator - Hoist into Wellway - Esc D4 & D5 (Main Conc to Upper Suite)	2	03-Jun-19	04-Jun-19	32
S3BB2-8R35	Escalator - Build-out / Installation - Esc B11 & C3 (Main Conc to Lower Suite)	30	15-Jul-19	23-Aug-19	87
S3AA1-8R35	Escalator - Build-out / Installation - Esc A7 & A8 (Main Conc to Lower Suite)	65	13-Jun-19	13-Sep-19	51
S3BB1-8R35	Escalator - Build-out / Installation - Esc B7 & B8 (Main Conc to Lower Suite)	65	13-Jun-19	13-Sep-19	41
S3AA2-8R35	Escalator - Build-out / Installation - Esc A11 & D3 (Main Conc to Lower Suite)	30	04-Sep-19	15-Oct-19	61
S3CC1-8R35	Escalator - Build-out / Installation - Esc C4 & C5 (Main Conc to Upper Suite)	95	03-Sep-19	20-Jan-20	20
S3DD1-8R35	Escalator - Build-out / Installation - Esc D4 & D5 (Main Conc to Upper Suite)	95	03-Sep-19	20-Jan-20	30
150 Lower Suite Level					
S4BB1-8R31	Escalator - Set on Floor - Esc B9 & B10 (Lower Suite to Upper Suite)	2	15-Nov-18	16-Nov-18	30
S4AA1-8R31	Escalator - Set on Floor - Esc A9 & A10 (Lower Suite to Upper Suite)	2	03-Dec-18	04-Dec-18	27
S4BB2-8R31	Escalator - Set on Floor - Esc B14 & C8 (Lower Suite to Upper Suite)	2	21-Dec-18	24-Dec-18	105
S4AA2-8R31	Escalator - Set on Floor - Esc A14 & D8 (Lower Suite to Upper Suite)	2	17-Jan-19	18-Jan-19	87
S4BB1-8R33	Escalator - Hoist into Wellway - Esc B9 & B10 (Lower Suite to Upper Suite)	2	19-Nov-18	20-Nov-18	96
S4AA1-8R33	Escalator - Hoist into Wellway - Esc A9 & A10 (Lower Suite to Upper Suite)	2	05-Dec-18	06-Dec-18	65
S4BB2-8R33	Escalator - Hoist into Wellway - Esc B14 & C8 (Lower Suite to Upper Suite)	2	26-Dec-18	27-Dec-18	105
S4AA2-8R33	Escalator - Hoist into Wellway - Esc A14 & D8 (Lower Suite to Upper Suite)	2	21-Jan-19	22-Jan-19	87
S4BB1-8R35	Escalator - Build-out / Installation - Esc B9 & B10 (Lower Suite to Upper Suite)	75	06-Feb-19	22-May-19	121
S4AA1-8R35	Escalator - Build-out / Installation - Esc A9 & A10 (Lower Suite to Upper Suite)	75	19-Mar-19	02-Jul-19	97
S4BB2-8R35	Escalator - Build-out / Installation - Esc B14 & C8 (Lower Suite to Upper Suite)	70	30-Apr-19	07-Aug-19	113
S4AA2-8R35	Escalator - Build-out / Installation - Esc A14 & D8 (Lower Suite to Upper Suite)	70	05-Jun-19	12-Sep-19	82
200 Upper Suite Level					
S5BB1-8R31	Escalator - Connect Sections - Esc B12 & B13 (Upper Suite to Upper Conc)	2	26-Nov-18	27-Nov-18	25
S5AA1-8R31	Escalator - Connect Sections - Esc A12 & A13 (Upper Suite to Upper Conc)	2	14-Dec-18	17-Dec-18	18
S5CC1-8R31	Escalator - Set on Floor - Esc C6 & C7 (Upper Suite to Mid-Bowl Mezz)	2	07-Mar-19	08-Mar-19	30
S5DD1-8R31	Escalator - Set on Floor - Esc D6 & D7 (Upper Suite to Mid-Bowl Mezz)	2	19-Mar-19	20-Mar-19	19
S5BB1-8R33	Escalator - Hoist into Wellway - Esc B12 & B13 (Upper Suite to Upper Conc)	2	28-Nov-18	29-Nov-18	106
S5AA1-8R33	Escalator - Hoist into Wellway - Esc A12 & A13 (Upper Suite to Upper Conc)	2	18-Dec-18	19-Dec-18	71
S5CC1-8R33	Escalator - Hoist into Wellway - Esc C6 & C7 (Upper Suite to Mid-Bowl Mezz)	2	11-Mar-19	12-Mar-19	101
S5DD1-8R33	Escalator - Hoist into Wellway - Esc D6 & D7 (Upper Suite to Mid-Bowl Mezz)	2	21-Mar-19	22-Mar-19	82
S5AA1-8R35	Escalator - Build-out / Installation - Esc A12 & A13 (Upper Suite to Upper Conc)	95	07-Jun-19	21-Oct-19	54
S5BB1-8R35	Escalator - Build-out / Installation - Esc B12 & B13 (Upper Suite to Upper Conc)	95	07-Jun-19	21-Oct-19	55
S5CC1-8R35	Escalator - Build-out / Installation - Esc C6 & C7 (Upper Suite to Mid-Bowl Mezz)	65	05-Aug-19	04-Nov-19	95
S5DD1-8R35	Escalator - Build-out / Installation - Esc D6 & D7 (Upper Suite to Mid-Bowl Mezz)	65	06-Sep-19	10-Dec-19	81
250 Mid Bowl Mezz Level					
S6CC1-8R31	Escalator - Set on Floor - Esc C9 & C10 (Mid-Bowl Mezz to Upper Conc)	2	03-Apr-19	04-Apr-19	9
S6DD1-8R31	Escalator - Set on Floor - Esc D9 & D10 (Mid-Bowl Mezz to Upper Conc)	2	03-Apr-19	04-Apr-19	9
S6CC1-8R33	Escalator - Hoist into Wellway - Esc C9 & C10 (Mid-Bowl Mezz to Upper Conc)	2	05-Apr-19	08-Apr-19	112
S6DD1-8R33	Escalator - Hoist into Wellway - Esc D9 & D10 (Mid-Bowl Mezz to Upper Conc)	2	05-Apr-19	08-Apr-19	102
S6CC1-8R35	Escalator - Build-out / Installation - Esc C9 & C10 (Mid-Bowl Mezz to Upper Conc)	65	03-Jul-19	03-Oct-19	122
S6DD1-8R35	Escalator - Build-out / Installation - Esc D9 & D10 (Mid-Bowl Mezz to Upper Conc)	65	03-Jul-19	03-Oct-19	112
Interior Rough-In					
000 Event Level					

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S1A1-8S0	MEP Rough-In & Interior Framing - Event Level Quad A1	80	26-Nov-18	20-Mar-19	57
S1AB1-8S0	MEP Rough-In & Interior Framing - Event Level Quad AB1	100	24-Oct-18	20-Mar-19	47
S1B1-8S0	MEP Rough-In & Interior Framing - Event Level Quad B1	80	26-Nov-18	20-Mar-19	52
S1B2-8S0	MEP Rough-In & Interior Framing - Event Level Quad B2	90	24-Dec-18	01-May-19	52
S1A2-8S0	MEP Rough-In & Interior Framing - Event Level Quad A2	90	25-Jan-19	03-Jun-19	35
S1C1-8S0	MEP Rough-In & Interior Framing - Event Level Quad C1	90	30-Jan-19	06-Jun-19	52
S1D1-8S0	MEP Rough-In & Interior Framing - Event Level Quad D1	80	04-Mar-19	24-Jun-19	50
S1D2-8S0	MEP Rough-In & Interior Framing - Event Level Quad D2	60	01-Apr-19	24-Jun-19	62
S1C2-8S0	MEP Rough-In & Interior Framing - Event Level Quad C2	80	07-Mar-19	27-Jun-19	52
S1C3-8S0	MEP Rough-In & Interior Framing - Event Level Quad C3	90	04-Apr-19	09-Aug-19	52
S1D3-8S0	MEP Rough-In & Interior Framing - Event Level Quad D3	80	18-Apr-19	09-Aug-19	62
S1C4-8S0	MEP Rough-In & Interior Framing - Event Level Quad C4	80	09-May-19	30-Aug-19	72
S100-8S00	MEP Rough-In & Interior Framing - Event Level (Summary)	225	24-Oct-18	16-Sep-19	62
S1D4-8S0	MEP Rough-In & Interior Framing - Event Level Quad D4	80	23-May-19	16-Sep-19	62
S1AB2-8S0	MEP Rough-In & Interior Framing - Event Level Quad Inner AB1	50	19-Sep-19	02-Dec-19	12
S1A3-8S0	MEP Rough-In & Interior Framing - Event Level Quad Inner A1	55	04-Oct-19	24-Dec-19	11
S1B3-8S0	MEP Rough-In & Interior Framing - Event Level Quad Inner B1	55	07-Oct-19	26-Dec-19	10
S1CD2-8S0	MEP Rough-In & Interior Framing - Event Level Quad Inner CD1	45	13-Nov-19	20-Jan-20	24
S1C5-8S0	MEP Rough-In & Interior Framing - Event Level Quad Inner C1	65	29-Oct-19	03-Feb-20	4
S1D5-8S0	MEP Rough-In & Interior Framing - Event Level Quad Inner D1	65	29-Oct-19	03-Feb-20	4
S101-8S00	MEP Rough-In & Interior Framing - Event Level Inner Bowl (Summary)	103	19-Sep-19	18-Feb-20	4
S1D6-8S0	MEP Rough-In & Interior Framing - Event Level Quad Inner D2	65	13-Nov-19	18-Feb-20	4
050 Lower Mezz Level					
S2A1-8S0	MEP Rough-In & Interior Framing - Lower Mezz Level Quad A1 / A3	80	02-Oct-18	28-Jan-19	135
S2B1-8S0	MEP Rough-In & Interior Framing - Lower Mezz Level Quad B1 / B3	80	02-Oct-18	28-Jan-19	86
S2A2-8S0	MEP Rough-In & Interior Framing - Lower Mezz Level Quad A2	80	30-Oct-18	26-Feb-19	135
S2B2-8S0	MEP Rough-In & Interior Framing - Lower Mezz Level Quad B2	80	30-Oct-18	26-Feb-19	86
S2BC1-8S0	MEP Rough-In & Interior Framing - Lower Mezz Level Quad BC1	65	31-Dec-18	02-Apr-19	86
S2AD1-8S0	MEP Rough-In & Interior Framing - Lower Mezz Level Quad AD1	65	04-Jan-19	05-Apr-19	112
S2AB1-8S0	MEP Rough-In & Interior Framing - Lower Mezz Level Quad AB1	90	20-Feb-19	26-Jun-19	101
S2C1-8S0	MEP Rough-In & Interior Framing - Lower Mezz Level Quad C1	110	22-Jan-19	26-Jun-19	86
S200-8S00	MEP Rough-In & Interior Framing - Lower Mezz Level (Summary)	188	02-Oct-18	01-Jul-19	112
S2D1-8S0	MEP Rough-In & Interior Framing - Lower Mezz Level Quad D1	110	25-Jan-19	01-Jul-19	112
100 Main Concourse					
S3AB1-8S0	MEP Rough-In & Interior Framing - Main Concourse Quad AB1	80	20-Nov-18	18-Mar-19	62
S3A1-8S0	MEP Rough-In & Interior Framing - Main Concourse Quad A1	80	13-Dec-18	08-Apr-19	72
S3B1-8S0	MEP Rough-In & Interior Framing - Main Concourse Quad B1	80	13-Dec-18	08-Apr-19	62
S3B2-8S0	MEP Rough-In & Interior Framing - Main Concourse Quad B2	75	07-Jan-19	22-Apr-19	62
S3A2-8S0	MEP Rough-In & Interior Framing - Main Concourse Quad A2	75	09-Jan-19	24-Apr-19	70
S3B3-8S0	MEP Rough-In & Interior Framing - Main Concourse Quad B3	90	28-Jan-19	04-Jun-19	62
S3A3-8S0	MEP Rough-In & Interior Framing - Main Concourse Quad A3	90	30-Jan-19	06-Jun-19	70
S3C1-8S0	MEP Rough-In & Interior Framing - Main Concourse Quad C1	90	19-Feb-19	25-Jun-19	62
S3D1-8S0	MEP Rough-In & Interior Framing - Main Concourse Quad D1	90	21-Feb-19	27-Jun-19	70
S3C2-8S0	MEP Rough-In & Interior Framing - Main Concourse Quad C2	75	19-Mar-19	02-Jul-19	62
S3D2-8S0	MEP Rough-In & Interior Framing - Main Concourse Quad D2	75	21-Mar-19	05-Jul-19	70
S300-8S00	MEP Rough-In & Interior Framing - Main Concourse (Summary)	215	20-Nov-18	26-Sep-19	32
S3C3-8S0	MEP Rough-In & Interior Framing - Main Concourse Quad C3	80	05-Jun-19	26-Sep-19	22
S3D3-8S0	MEP Rough-In & Interior Framing - Main Concourse Quad D3	80	05-Jun-19	26-Sep-19	32
150 Lower Suite Level					
S4B1-8S0	MEP Rough-In & Interior Framing - Lower Suite Level Quad B1	50	10-Dec-18	20-Feb-19	85
S4A1-8S0	MEP Rough-In & Interior Framing - Lower Suite Level Quad A1	50	21-Jan-19	01-Apr-19	36
S4B3-8S0	MEP Rough-In & Interior Framing - Lower Suite Level Quad B3	65	21-Jan-19	22-Apr-19	105
S4B2-8S0	MEP Rough-In & Interior Framing - Lower Suite Level Quad B2	90	28-Dec-18	06-May-19	105
S4A2-8S0	MEP Rough-In & Interior Framing - Lower Suite Level Quad A2	80	04-Feb-19	28-May-19	79
S4A3-8S0	MEP Rough-In & Interior Framing - Lower Suite Level Quad A3	65	26-Feb-19	28-May-19	79
S4C2-8S0	MEP Rough-In & Interior Framing - Lower Suite Level Quad C2	65	26-Feb-19	28-May-19	107
S4C1-8S0	MEP Rough-In & Interior Framing - Lower Suite Level Quad C1	90	04-Feb-19	11-Jun-19	105
S4D2-8S0	MEP Rough-In & Interior Framing - Lower Suite Level Quad D2	50	02-Apr-19	11-Jun-19	91
S4D1-8S0	MEP Rough-In & Interior Framing - Lower Suite Level Quad D1	95	12-Mar-19	24-Jul-19	79

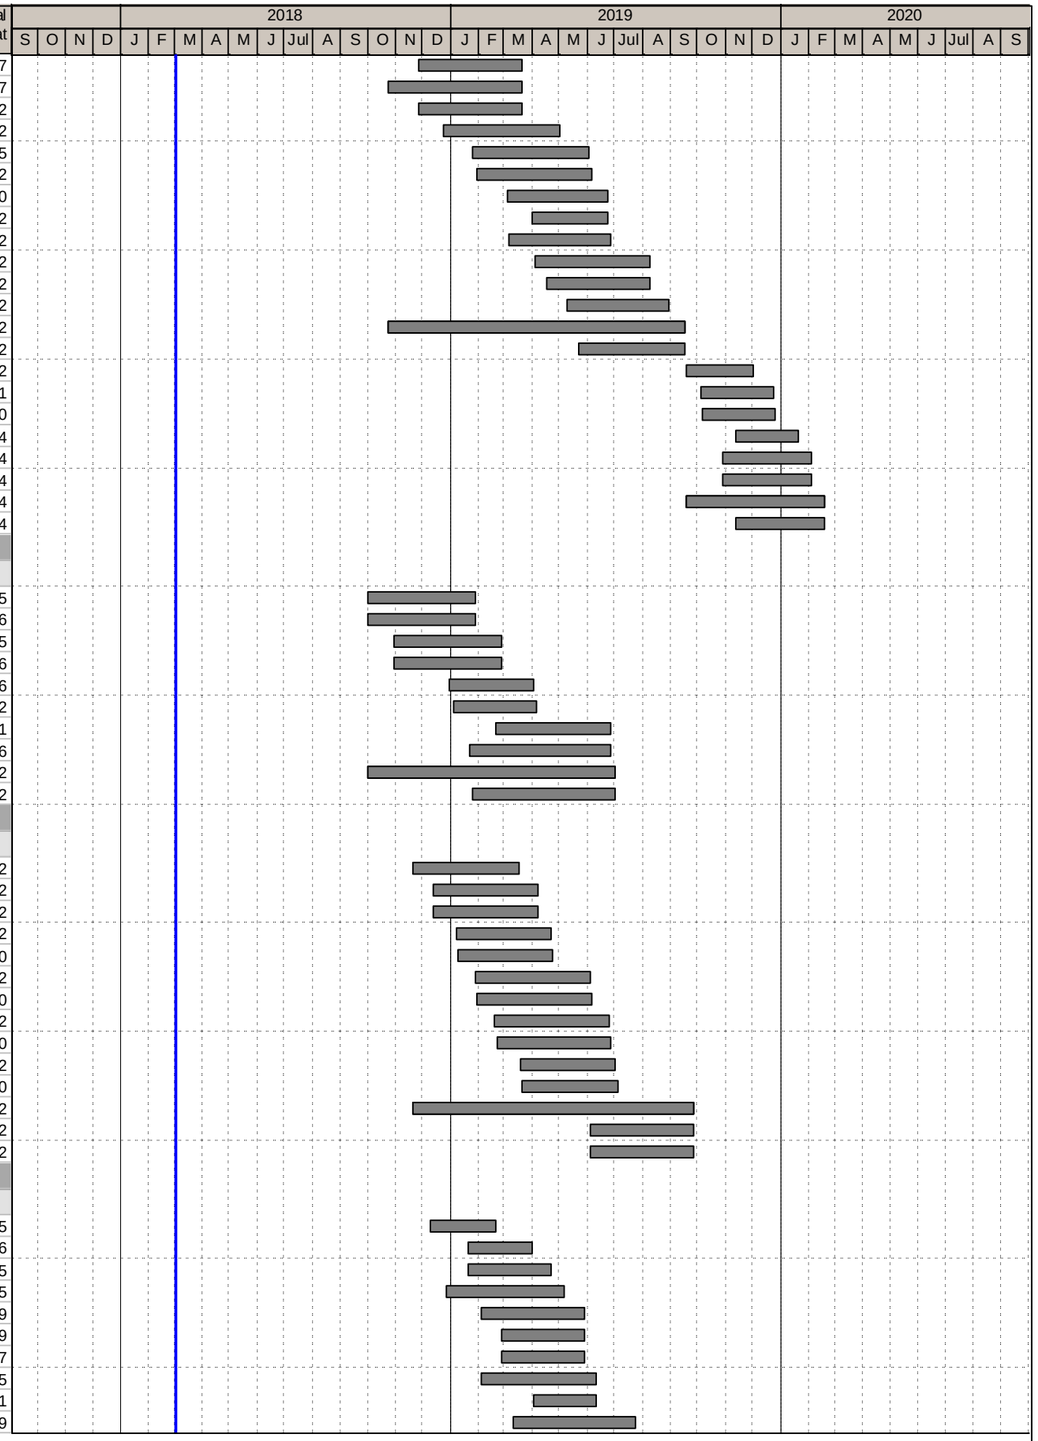

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S4C3-8S0	MEP Rough-In & Interior Framing - Lower Suite Level Quad C3	85	29-Mar-19	29-Jul-19	94
S400-8S00	MEP Rough-In & Interior Framing - Lower Suite Level (Summary)	173	10-Dec-18	14-Aug-19	91
S4D3-8S0	MEP Rough-In & Interior Framing - Lower Suite Level Quad D3	85	16-Apr-19	14-Aug-19	91
200 Upper Suite Level					
S5B1-8S0	MEP Rough-In & Interior Framing - Upper Suite Level Quad B1	95	02-Jan-19	15-May-19	85
S5B2-8S0	MEP Rough-In & Interior Framing - Upper Suite Level Quad B2	75	30-Jan-19	15-May-19	85
S5B3-8S0	MEP Rough-In & Interior Framing - Upper Suite Level Quad B3	65	13-Feb-19	15-May-19	85
S5C1-8S0	MEP Rough-In & Interior Framing - Upper Suite Level Quad C1	80	28-Feb-19	20-Jun-19	85
S5C2-8S0	MEP Rough-In & Interior Framing - Upper Suite Level Quad C2	65	21-Mar-19	20-Jun-19	85
S5A1-8S0	MEP Rough-In & Interior Framing - Upper Suite Level Quad A1	95	11-Feb-19	25-Jun-19	36
S5A2-8S0	MEP Rough-In & Interior Framing - Upper Suite Level Quad A2	80	05-Mar-19	25-Jun-19	36
S5A3-8S0	MEP Rough-In & Interior Framing - Upper Suite Level Quad A3	65	26-Mar-19	25-Jun-19	36
S5C3-8S0	MEP Rough-In & Interior Framing - Upper Suite Level Quad C3	90	04-Apr-19	09-Aug-19	85
S5D1-8S0	MEP Rough-In & Interior Framing - Upper Suite Level Quad D1	90	09-Apr-19	14-Aug-19	36
S5D2-8S0	MEP Rough-In & Interior Framing - Upper Suite Level Quad D2	65	14-May-19	14-Aug-19	36
S500-8S00	MEP Rough-In & Interior Framing - Upper Suite / Club Level (Summary)	203	02-Jan-19	17-Oct-19	37
S5D3-8S0	MEP Rough-In & Interior Framing - Upper Suite Level Quad D3	100	29-May-19	17-Oct-19	36
250 Mid Bowl Mezz Level					
S6B1-8S0	MEP Rough-In & Interior Framing - Mid Bowl Mezz Quad B1	60	23-Jan-19	17-Apr-19	150
S6A1-8S0	MEP Rough-In & Interior Framing - Mid Bowl Mezz Quad A1	60	05-Mar-19	28-May-19	112
S6C1-8S0	MEP Rough-In & Interior Framing - Mid Bowl Mezz Quad C1	75	09-Apr-19	24-Jul-19	112
S6D1-8S0	MEP Rough-In & Interior Framing - Mid Bowl Mezz Quad D1	75	09-Apr-19	24-Jul-19	102
S6D2-8S0	MEP Rough-In & Interior Framing - Mid Bowl Mezz Quad D2	70	30-Apr-19	07-Aug-19	107
300 Upper Concourse					
S7B1-8S0	MEP Rough-In & Interior Framing - Upper Concourse Quad B1	75	18-Apr-19	02-Aug-19	11
S7A1-8S0	MEP Rough-In & Interior Framing - Upper Concourse Quad A1	80	12-Apr-19	05-Aug-19	52
S7A2-8S0	MEP Rough-In & Interior Framing - Upper Concourse Quad A2	80	30-Apr-19	21-Aug-19	52
S7B2-8S0	MEP Rough-In & Interior Framing - Upper Concourse Quad B2	85	06-May-19	04-Sep-19	11
S7C1-8S0	MEP Rough-In & Interior Framing - Upper Concourse Quad C1	85	28-May-19	25-Sep-19	11
S7D1-8S0	MEP Rough-In & Interior Framing - Upper Concourse Quad D1	90	21-May-19	26-Sep-19	52
S7D2-8S0	MEP Rough-In & Interior Framing - Upper Concourse Quad D2	80	12-Jun-19	03-Oct-19	62
S7C2-8S0	MEP Rough-In & Interior Framing - Upper Concourse Quad C2	80	18-Jun-19	09-Oct-19	11
S700-8S00	MEP Rough-In & Interior Framing - Upper Concourse (Summary)	153	12-Apr-19	18-Nov-19	31
S7CD1-8S0	MEP Rough-In & Interior Framing - Upper Concourse Quad CD1	95	05-Jul-19	18-Nov-19	11
350 Upper Mezz Level					
S8A1-8S0	MEP Rough-In & Interior Framing - Upper Mezz Level Quad A1	70	26-Apr-19	05-Aug-19	58
S8B1-8S0	MEP Rough-In & Interior Framing - Upper Mezz Level Quad B1	70	02-May-19	09-Aug-19	85
S8D1-8S0	MEP Rough-In & Interior Framing - Upper Mezz Level Quad D1	80	22-May-19	13-Sep-19	71
S8C1-8S0	MEP Rough-In & Interior Framing - Upper Mezz Level Quad C1	80	28-May-19	18-Sep-19	68
400 Press Level					
S9A1-8S0	MEP Rough-In & Interior Framing - Press Level Quad A1	75	26-Apr-19	12-Aug-19	58
S9D1-8S0	MEP Rough-In & Interior Framing - Press Level Quad D1	75	17-May-19	03-Sep-19	58
S900-8S00	MEP Rough-In & Interior Framing - Press Level	110	12-Apr-19	17-Sep-19	41
Steel Stairs					
000 Event Level					
S1FC2-8S2A2	Steel Stairs - Erect - Event to Lower Mezz - Core #2 Stair A2	2	13-Aug-18	14-Aug-18	109
S1AC3-8S2A2	Steel Stairs - Erect - Event to Lower Mezz - Core #3 Stair B2	2	15-Aug-18	16-Aug-18	98
S1BC4-8S2A2	Steel Stairs - Erect - Event to Lower Mezz - Core #4 Stair B1	2	06-Sep-18	07-Sep-18	98
S1EC1-8S2A2	Steel Stairs - Erect - Event to Lower Mezz - Core #1 Stair A1	2	17-Sep-18	18-Sep-18	95
S1BC5-8S2A2	Steel Stairs - Erect - Event to Lower Mezz - Core #5 Stair C1	2	22-Oct-18	23-Oct-18	90
S1EC8-8S2A2	Steel Stairs - Erect - Event to Lower Mezz - Core #8 Stair D1	2	02-Nov-18	05-Nov-18	92
S1CC6-8S2A2	Steel Stairs - Erect - Event to Lower Mezz - Core #6 Stair C2	2	13-Nov-18	14-Nov-18	95
S1DC7-8S2A2	Steel Stairs - Erect - Event to Lower Mezz - Core #7 Stair D2	2	13-Nov-18	14-Nov-18	95
050 Lower Mezz Level					

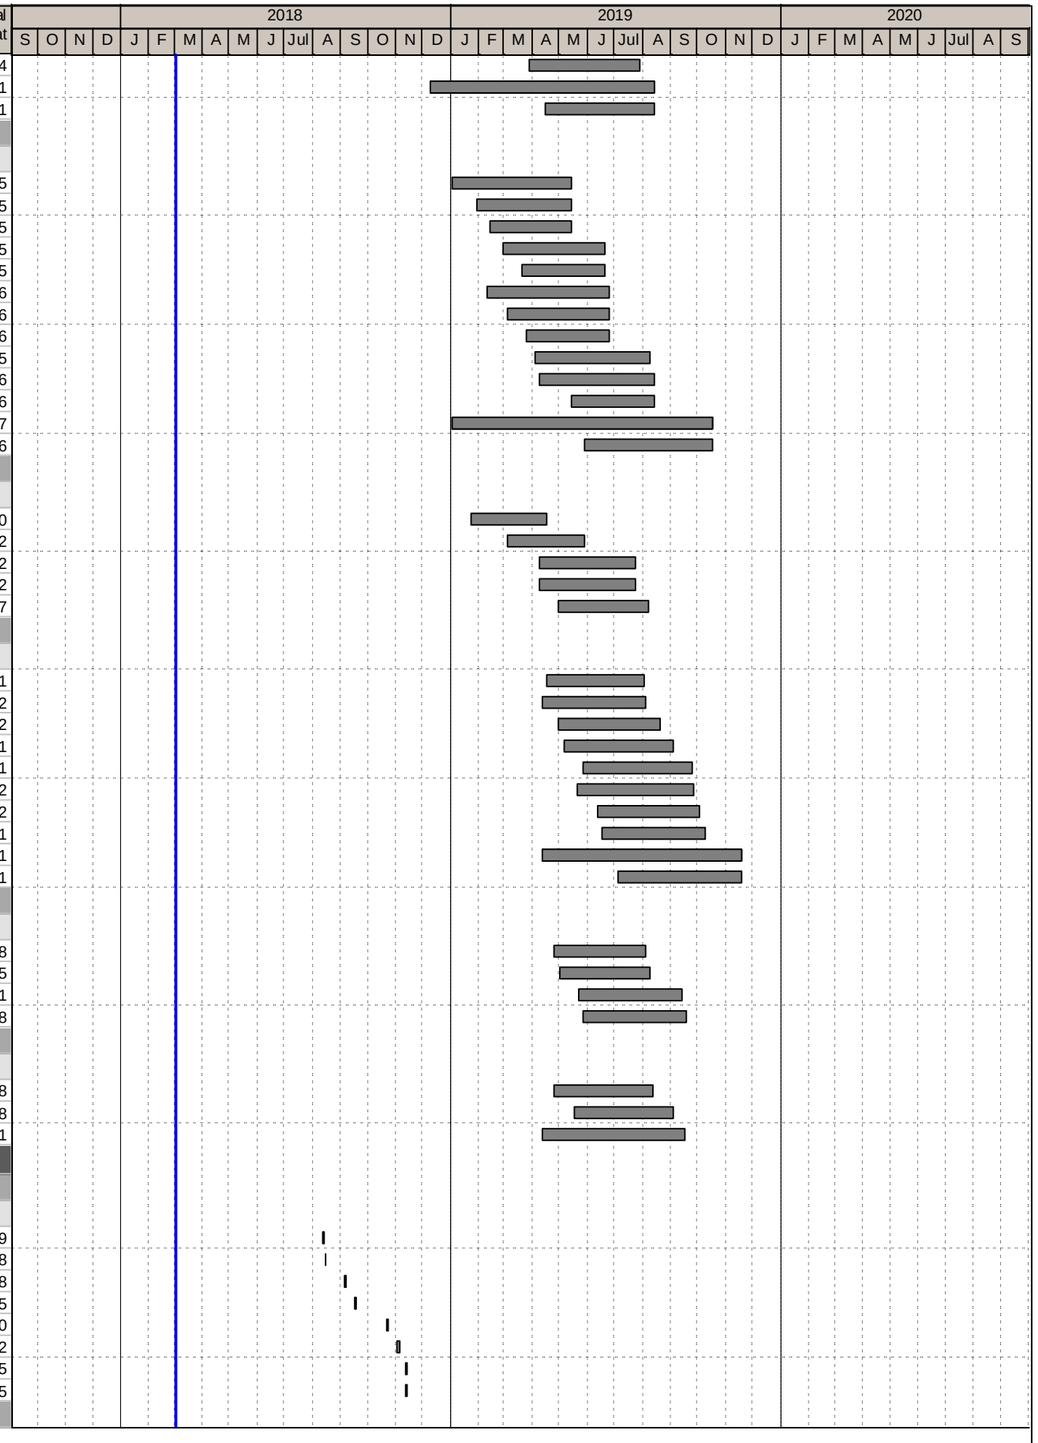

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S2FC2-8S2A2	Steel Stairs - Erect - Lower Mezz to Main Conc - Core #2 Stair A2	2	15-Aug-18	16-Aug-18	109
S2AC3-8S2A2	Steel Stairs - Erect - Lower Mezz to Main Conc - Core #3 Stair B2	2	17-Aug-18	20-Aug-18	98
S2BC4-8S2A2	Steel Stairs - Erect - Lower Mezz to Main Conc - Core #4 Stair B1	2	10-Sep-18	11-Sep-18	98
S2EC1-8S2A2	Steel Stairs - Erect - Lower Mezz to Main Conc - Core #1 Stair A1	2	19-Sep-18	20-Sep-18	95
S2BC5-8S2A2	Steel Stairs - Erect - Lower Mezz to Main Conc - Core #5 Stair C1	2	24-Oct-18	25-Oct-18	90
S2EC8-8S2A2	Steel Stairs - Erect - Lower Mezz to Main Conc - Core #8 Stair D1	2	06-Nov-18	07-Nov-18	92
S2CC6-8S2A2	Steel Stairs - Erect - Lower Mezz to Main Conc - Core #6 Stair C2	2	15-Nov-18	16-Nov-18	95
S2DC7-8S2A2	Steel Stairs - Erect - Lower Mezz to Main Conc - Core #7 Stair D2	2	15-Nov-18	16-Nov-18	95
100 Main Concourse					
S3FC2-8S2A2	Steel Stairs - Erect - Main Conc to Lower Suite - Core #2 Stair A2	2	17-Aug-18	20-Aug-18	109
S3AC3-8S2A2	Steel Stairs - Erect - Main Conc to Lower Suite - Core #3 Stair B2	2	21-Aug-18	22-Aug-18	98
S3BC4-8S2A2	Steel Stairs - Erect - Main Conc to Lower Suite - Core #4 Stair B1	2	12-Sep-18	13-Sep-18	98
S3EC1-8S2A2	Steel Stairs - Erect - Main Conc to Lower Suite - Core #1 Stair A1	2	21-Sep-18	24-Sep-18	95
S3BC5-8S2A2	Steel Stairs - Erect - Main Conc to Lower Suite - Core #5 Stair C1	2	26-Oct-18	29-Oct-18	90
S3EC8-8S2A2	Steel Stairs - Erect - Main Conc to Lower Suite - Core #8 Stair D1	2	08-Nov-18	09-Nov-18	92
S3CC6-8S2A2	Steel Stairs - Erect - Main Conc to Lower Suite - Core #6 Stair C2	2	19-Nov-18	20-Nov-18	95
S3DC7-8S2A2	Steel Stairs - Erect - Main Conc to Lower Suite - Core #7 Stair D2	2	19-Nov-18	20-Nov-18	95
150 Lower Suite Level					
S4FC2-8S2A2	Steel Stairs - Erect - Lower Suite to Upper Suite - Core #2 Stair A2	2	21-Aug-18	22-Aug-18	109
S4AC3-8S2A2	Steel Stairs - Erect - Lower Suite to Upper Suite - Core #3 Stair B2	2	23-Aug-18	24-Aug-18	98
S4BC4-8S2A2	Steel Stairs - Erect - Lower Suite to Upper Suite - Core #4 Stair B1	2	14-Sep-18	17-Sep-18	98
S4EC1-8S2A2	Steel Stairs - Erect - Lower Suite to Upper Suite - Core #1 Stair A1	2	25-Sep-18	26-Sep-18	95
S4BC5-8S2A2	Steel Stairs - Erect - Lower Suite to Upper Suite - Core #5 Stair C1	2	30-Oct-18	31-Oct-18	90
S4EC8-8S2A2	Steel Stairs - Erect - Lower Suite to Upper Suite - Core #8 Stair D1	2	13-Nov-18	14-Nov-18	92
S4CC6-8S2A2	Steel Stairs - Erect - Lower Suite to Upper Suite - Core #6 Stair C2	2	21-Nov-18	26-Nov-18	95
S4DC7-8S2A2	Steel Stairs - Erect - Lower Suite to Upper Suite - Core #7 Stair D2	2	21-Nov-18	26-Nov-18	95
200 Upper Suite Level					
S5FC2-8S2A2	Steel Stairs - Erect - Upper Suite to Mid Bowl Mezz - Core #2 Stair A2	2	23-Aug-18	24-Aug-18	109
S5AC3-8S2A2	Steel Stairs - Erect - Upper Suite to Mid Bowl Mezz - Core #3 Stair B2	2	27-Aug-18	28-Aug-18	98
S5BC4-8S2A2	Steel Stairs - Erect - Upper Suite to Mid Bowl Mezz - Core #4 Stair B1	2	18-Sep-18	19-Sep-18	98
S5EC1-8S2A2	Steel Stairs - Erect - Upper Suite to Mid Bowl Mezz - Core #1 Stair A1	2	27-Sep-18	28-Sep-18	95
S5BC5-8S2A2	Steel Stairs - Erect - Upper Suite to Mid Bowl Mezz - Core #5 Stair C1	2	01-Nov-18	02-Nov-18	90
S5EC8-8S2A2	Steel Stairs - Erect - Upper Suite to Mid Bowl Mezz - Core #8 Stair D1	2	15-Nov-18	16-Nov-18	92
S5CC6-8S2A2	Steel Stairs - Erect - Upper Suite to Mid Bowl Mezz - Core #6 Stair C2	2	27-Nov-18	28-Nov-18	95
S5DC7-8S2A2	Steel Stairs - Erect - Upper Suite to Mid Bowl Mezz - Core #7 Stair D2	2	27-Nov-18	28-Nov-18	95
250 Mid Bowl Mezz Level					
S6FC2-8S2A2	Steel Stairs - Erect - Mid Bowl Mezz to Upper Conc - Core #2 Stair A2	2	27-Aug-18	28-Aug-18	109
S6AC3-8S2A2	Steel Stairs - Erect - Mid Bowl Mezz to Upper Conc - Core #3 Stair B2	2	29-Aug-18	30-Aug-18	98
S6BC4-8S2A2	Steel Stairs - Erect - Mid Bowl Mezz to Upper Conc - Core #4 Stair B1	2	20-Sep-18	21-Sep-18	98
S6EC1-8S2A2	Steel Stairs - Erect - Mid Bowl Mezz to Upper Conc - Core #1 Stair A1	2	01-Oct-18	02-Oct-18	95
S6BC5-8S2A2	Steel Stairs - Erect - Mid Bowl Mezz to Upper Conc - Core #5 Stair C1	2	05-Nov-18	06-Nov-18	90
S6EC8-8S2A2	Steel Stairs - Erect - Mid Bowl Mezz to Upper Conc - Core #8 Stair D1	2	19-Nov-18	20-Nov-18	92
S6CC6-8S2A2	Steel Stairs - Erect - Mid Bowl Mezz to Upper Conc - Core #6 Stair C2	2	29-Nov-18	30-Nov-18	95
S6DC7-8S2A2	Steel Stairs - Erect - Mid Bowl Mezz to Upper Conc - Core #7 Stair D2	2	29-Nov-18	30-Nov-18	95
300 Upper Concourse					
S7AC3-8S2A2	Steel Stairs - Erect - Upper Conc to Top - Core #3 Stair B2	5	08-Jan-19	14-Jan-19	77
S7BC4-8S2A2	Steel Stairs - Erect - Upper Conc to Top - Core #4 Stair B1	2	06-Feb-19	07-Feb-19	71
S7EC1-8S2A2	Steel Stairs - Erect - Upper Conc to Top - Core #1 Stair A1	5	12-Feb-19	19-Feb-19	105
S7BC5-8S2A2	Steel Stairs - Erect - Upper Conc to Top - Core #5 Stair C1	3	01-Mar-19	05-Mar-19	69
S7EC8-8S2A2	Steel Stairs - Erect - Upper Conc to Top - Core #8 Stair D1	5	19-Mar-19	25-Mar-19	92
S7CC6-8S2A2	Steel Stairs - Erect - Upper Conc to Top - Core #6 Stair C2	2	05-Apr-19	08-Apr-19	60
S7DC7-8S2A2	Steel Stairs - Erect - Upper Conc to Top - Core #7 Stair D2	2	05-Apr-19	08-Apr-19	107
AHUs					
050 Lower Mezz Level					

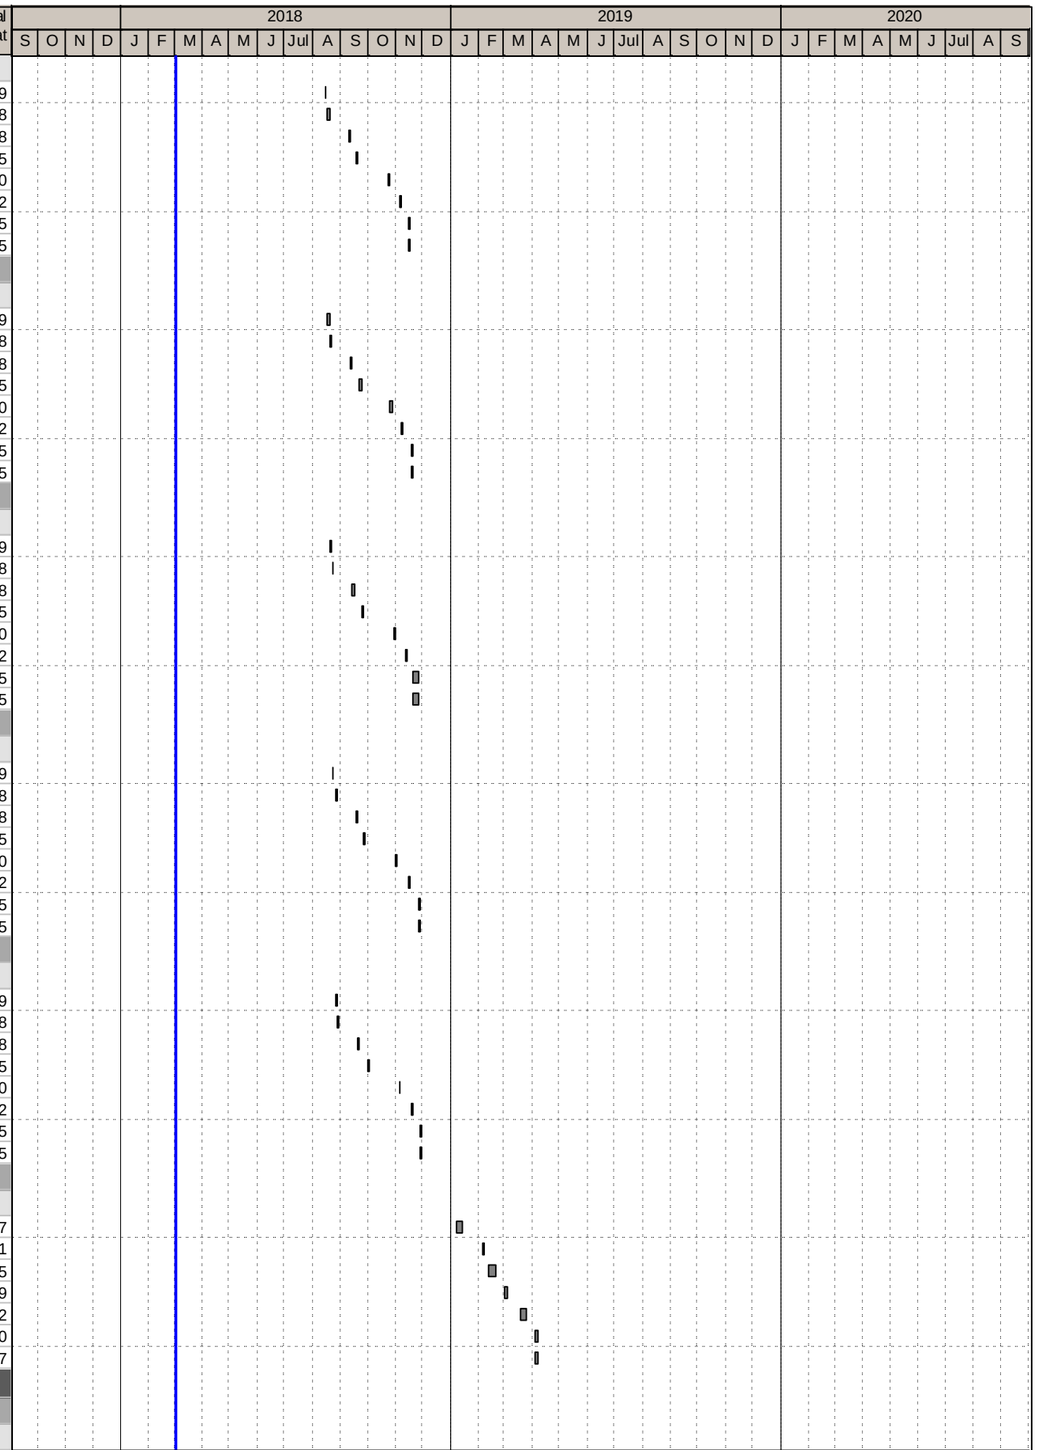

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S2A1-8T1B0	Set AHU on Deck - Lower Mezz Level Quad A (AHU-050-A-1)	1	13-Aug-18	13-Aug-18	25
S2A2-8T1B0	Set AHU on Deck - Lower Mezz Level Quad A (AHU-050-A-2)	1	13-Aug-18	13-Aug-18	25
S2A3-8T1B0	Set AHU on Deck - Lower Mezz Level Quad A (AHU-050-A-3)	1	13-Aug-18	13-Aug-18	25
S2B1-8T1B0	Set AHU on Deck - Lower Mezz Level Quad B (AHU-050-B-1)	1	15-Aug-18	15-Aug-18	18
S2B2-8T1B0	Set AHU on Deck - Lower Mezz Level Quad B (AHU-050-B-2)	1	15-Aug-18	15-Aug-18	18
S2B3-8T1B0	Set AHU on Deck - Lower Mezz Level Quad B (AHU-050-B-3)	1	15-Aug-18	15-Aug-18	18
S2B4-8T1B0	Set AHU on Deck - Lower Mezz Level Quad B (AHU-050-B-4)	1	15-Aug-18	15-Aug-18	18
S2D1-8T1B0	Set AHU on Deck - Lower Mezz Level Quad D (AHU-050-D-1)	1	01-Nov-18	01-Nov-18	48
S2C1-8T1B0	Set AHU on Deck - Lower Mezz Level Quad C (AHU-050-C-1)	1	06-Nov-18	06-Nov-18	19
S2C2-8T1B0	Set AHU on Deck - Lower Mezz Level Quad C (AHU-050-C-3)	1	06-Nov-18	06-Nov-18	19
150 Lower Suite Level					
S4A1-8T1B0	Set AHU on Deck - Lower Suite Level Quad A (AHU-150-A-1)	1	28-Dec-18	28-Dec-18	138
S4B1-8T1B0	Set AHU on Deck - Lower Suite Level Quad B (AHU-150-B-1)	1	04-Jan-19	04-Jan-19	150
S4C1-8T1B0	Set AHU on Deck - Lower Suite Level Quad C (AHU-150-C-1)	1	25-Jan-19	25-Jan-19	150
S4D1-8T1B0	Set AHU on Deck - Lower Suite Level Quad D (AHU-150-D-1)	1	06-Mar-19	06-Mar-19	127
250 Mid Bowl Mezz Level					
S6B1-8T1B0	Set AHU on Deck - Mid Bowl Mezz Level Quad B (AHU-250-B-1)	3	27-Dec-18	31-Dec-18	23
S6B2-8T1B0	Set AHU on Deck - Mid Bowl Mezz Level Quad B (AHU-250-B-2)	3	27-Dec-18	31-Dec-18	23
S6C1-8T1B0	Set AHU on Deck - Mid Bowl Mezz Level Quad C (AHU-250-C-1)	3	08-Jan-19	10-Jan-19	42
S6A1-8T1B0	Set AHU on Deck - Mid Bowl Mezz Level Quad A (AHU-250-A-1)	3	22-Jan-19	24-Jan-19	13
S6A2-8T1B0	Set AHU on Deck - Mid Bowl Mezz Level Quad A (AHU-250-A-2)	3	22-Jan-19	24-Jan-19	13
S6D1-8T1B0	Set AHU on Deck - Mid Bowl Mezz Level Quad D (AHU-250-D-1)	3	01-Feb-19	05-Feb-19	28
350 Upper Mezz Level					
S8B1-8T1B0	Set AHU on Deck - Upper Mezz Level Quad B (AHU-350-B-1)	1	18-Dec-18	18-Dec-18	24
S8A1-8T1B0	Set AHU on Deck - Upper Mezz Level Quad A (AHU-350-A-1)	1	02-Jan-19	02-Jan-19	24
S8C1-8T1B0	Set AHU on Deck - Upper Mezz Level Quad C (AHU-350-C-1)	1	25-Mar-19	25-Mar-19	21
S8D1-8T1B0	Set AHU on Deck - Upper Mezz Level Quad D (AHU-350-D-1)	1	28-Mar-19	28-Mar-19	18
400 Press Level					
S9A1-8T1B0	Set AHU on Deck - Press Level Quad A (AHU-400-A-1)	1	06-Feb-19	06-Feb-19	9
Specialty Equipment					
Upper Seating Bowl					
S000-8T70	Signature Tower	66	05-Dec-19	10-Mar-20	20
Sports Equipment					
S000-8T7P	Scoreboards/Ribbon Boards & Video Walls	125	01-Oct-19	31-Mar-20	0
Drywall and Interior Finishes					
000 Event Level					
S1AB1-8U0	Drywall and Interior Finishes - Event Level Quad AB1	100	21-Mar-19	09-Aug-19	47
S1A1-8U0	Drywall and Interior Finishes - Event Level Quad A1	90	18-Apr-19	23-Aug-19	47
S1B1-8U0	Drywall and Interior Finishes - Event Level Quad B1	90	18-Apr-19	23-Aug-19	57
S1B2-8U0	Drywall and Interior Finishes - Event Level Quad B2	120	09-May-19	28-Oct-19	57
S1A2-8U0	Drywall and Interior Finishes - Event Level Quad A2	120	04-Jun-19	21-Nov-19	35
S1D1-8U0	Drywall and Interior Finishes - Event Level Quad D1	90	17-Jul-19	21-Nov-19	35
S1D2-8U0	Drywall and Interior Finishes - Event Level Quad D2	60	28-Aug-19	21-Nov-19	35
S1C1-8U0	Drywall and Interior Finishes - Event Level Quad C1	120	07-Jun-19	26-Nov-19	57
S1C2-8U0	Drywall and Interior Finishes - Event Level Quad C2	100	08-Jul-19	26-Nov-19	57
S1C3-8U0	Drywall and Interior Finishes - Event Level Quad C3	110	12-Aug-19	20-Jan-20	52
S1C4-8U0	Drywall and Interior Finishes - Event Level Quad C4	75	01-Oct-19	20-Jan-20	52
S1D3-8U0	Drywall and Interior Finishes - Event Level Quad D3	100	19-Sep-19	12-Feb-20	35
S1D4-8U0	Drywall and Interior Finishes - Event Level Quad D4	75	24-Oct-19	12-Feb-20	35
S1AB2-8U0	Drywall and Interior Finishes - Event Level Quad Inner AB1	50	03-Dec-19	12-Feb-20	27
S1A3-8U0	Drywall and Interior Finishes - Event Level Quad Inner A1	60	26-Dec-19	20-Mar-20	21
S1B3-8U0	Drywall and Interior Finishes - Event Level Quad Inner B1	60	27-Dec-19	23-Mar-20	20

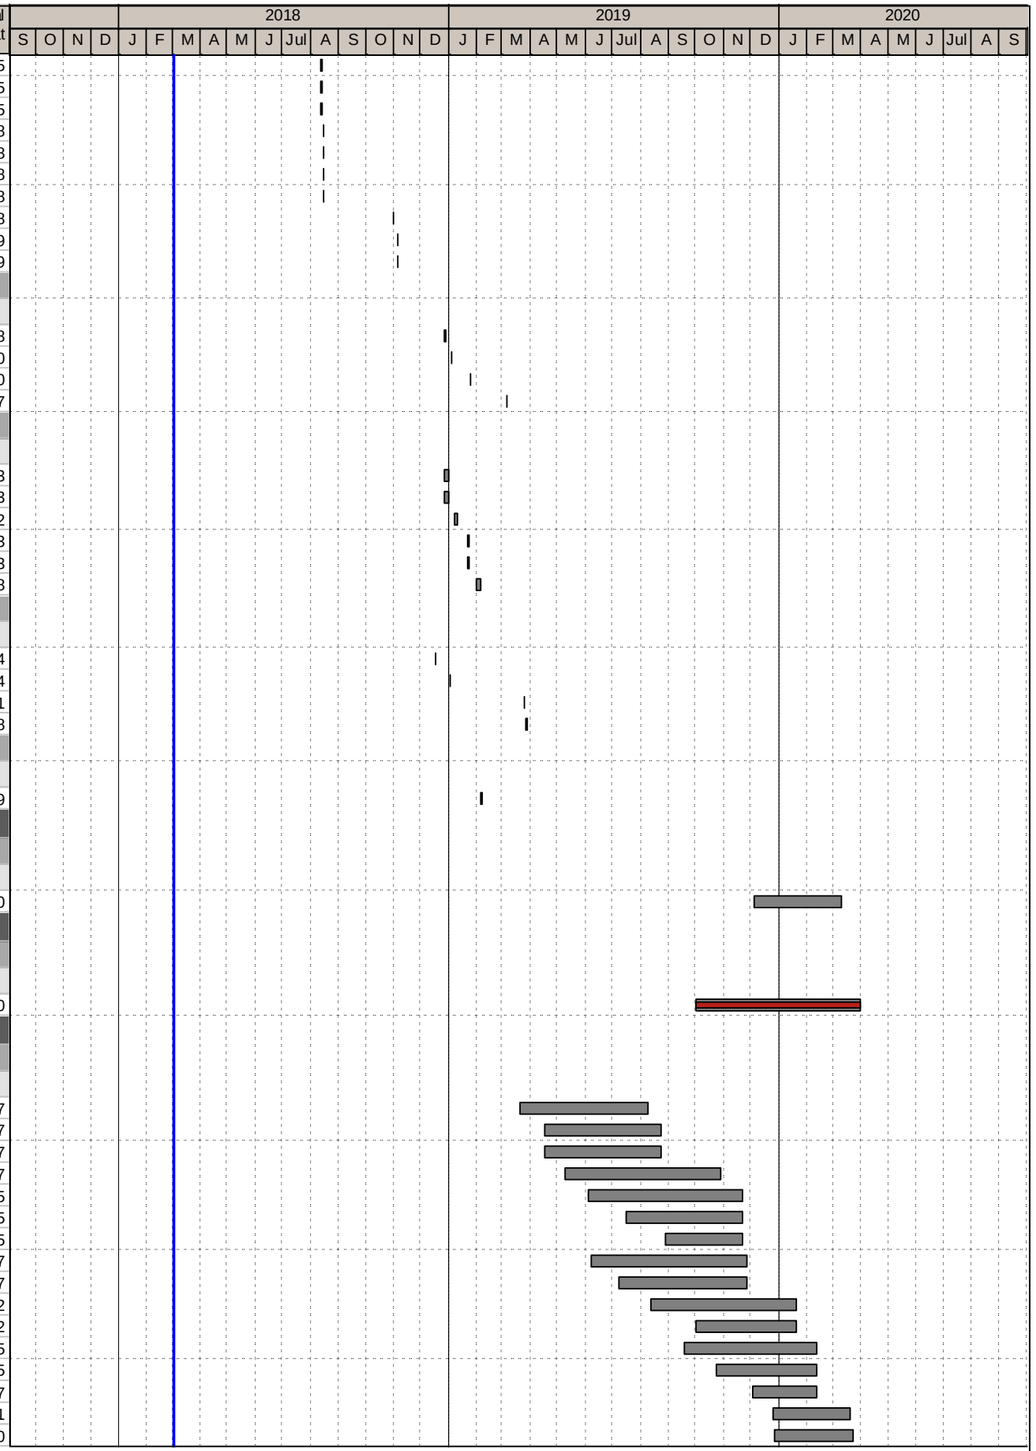

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S1D5-8U0	Drywall and Interior Finishes - Event Level Quad Inner D1	60	04-Feb-20	28-Apr-20	4
S1C5-8U0	Drywall and Interior Finishes - Event Level Quad Inner C1	65	04-Feb-20	05-May-20	4
S1CD2-8U0	Drywall and Interior Finishes - Event Level Quad Inner CD1	60	19-Feb-20	12-May-20	4
S1D6-8U0	Drywall and Interior Finishes - Event Level Quad Inner D2	60	19-Feb-20	12-May-20	4
S100-8U00	Drywall and Interior Finishes - Event Level (Summary)	227	21-Mar-19	12-Feb-20	35
S101-8U00	Drywall and Interior Finishes - Event Level Inner Bowl (Summary)	113	03-Dec-19	12-May-20	4
050 Lower Mezz Level					
S2A1-8U0	Drywall and Interior Finishes - Lower Mezz Level Quad A1	80	24-Jun-19	15-Oct-19	63
S2B1-8U0	Drywall and Interior Finishes - Lower Mezz Level Quad B1	80	24-Jun-19	15-Oct-19	34
S2B2-8U0	Drywall and Interior Finishes - Lower Mezz Level Quad B2	80	16-Jul-19	05-Nov-19	34
S2B3-8U0	Drywall and Interior Finishes - Lower Mezz Level Quad B3	50	27-Aug-19	05-Nov-19	34
S2A2-8U0	Drywall and Interior Finishes - Lower Mezz Level Quad A2	80	06-Aug-19	27-Nov-19	48
S2A3-8U0	Drywall and Interior Finishes - Lower Mezz Level Quad A3	50	18-Sep-19	27-Nov-19	48
S2BC1-8U0	Drywall and Interior Finishes - Lower Mezz Level Quad BC1	65	27-Aug-19	27-Nov-19	34
S2AD1-8U0	Drywall and Interior Finishes - Lower Mezz Level Quad AD1	65	30-Sep-19	03-Jan-20	40
S2C1-8U0	Drywall and Interior Finishes - Lower Mezz Level Quad C1	90	11-Sep-19	21-Jan-20	34
S2AB1-8U0	Drywall and Interior Finishes - Lower Mezz Level Quad AB1	90	02-Oct-19	11-Feb-20	34
S2D1-8U0	Drywall and Interior Finishes - Lower Mezz Level Quad D1	90	14-Oct-19	24-Feb-20	40
S200-8U00	Drywall and Interior Finishes - Mezz Level (Summary)	168	24-Jun-19	24-Feb-20	40
100 Main Concourse					
S3A1-8U0	Drywall and Interior Finishes - Main Concourse Quad A1	90	13-Jun-19	18-Oct-19	46
S3B1-8U0	Drywall and Interior Finishes - Main Concourse Quad B1	90	13-Jun-19	18-Oct-19	36
S3B2-8U0	Drywall and Interior Finishes - Main Concourse Quad B2	80	01-Jul-19	22-Oct-19	36
S3A2-8U0	Drywall and Interior Finishes - Main Concourse Quad A2	80	06-Aug-19	27-Nov-19	21
S3B3-8U0	Drywall and Interior Finishes - Main Concourse Quad B3	100	16-Jul-19	06-Dec-19	36
S3C1-8U0	Drywall and Interior Finishes - Main Concourse Quad C1	100	02-Aug-19	26-Dec-19	36
S3C2-8U0	Drywall and Interior Finishes - Main Concourse Quad C2	80	03-Sep-19	27-Dec-19	35
S3A3-8U0	Drywall and Interior Finishes - Main Concourse Quad A3	100	04-Sep-19	28-Jan-20	11
S3D1-8U0	Drywall and Interior Finishes - Main Concourse Quad D1	100	23-Sep-19	14-Feb-20	11
S3D2-8U0	Drywall and Interior Finishes - Main Concourse Quad D2	80	21-Oct-19	14-Feb-20	11
S3AB1-8U0	Drywall and Interior Finishes - Main Concourse Quad AB1	80	22-Oct-19	18-Feb-20	20
S3C3-8U0	Drywall and Interior Finishes - Main Concourse Quad C3	95	08-Oct-19	25-Feb-20	20
S3D3-8U0	Drywall and Interior Finishes - Main Concourse Quad D3	95	04-Nov-19	23-Mar-20	11
S300-8U00	Drywall and Interior Finishes - Main Concourse (Summary)	195	13-Jun-19	23-Mar-20	11
150 Lower Suite Level					
S4A1-8U0	Drywall and Interior Finishes - Lower Suite Level Quad A1	55	25-Jun-19	11-Sep-19	68
S4B1-8U0	Drywall and Interior Finishes - Lower Suite Level Quad B1	55	25-Jun-19	11-Sep-19	64
S4B2-8U0	Drywall and Interior Finishes - Lower Suite Level Quad B2	90	10-Jul-19	14-Nov-19	64
S4B3-8U0	Drywall and Interior Finishes - Lower Suite Level Quad B3	80	24-Jul-19	14-Nov-19	64
S4C1-8U0	Drywall and Interior Finishes - Lower Suite Level Quad C1	90	09-Aug-19	18-Dec-19	64
S4C2-8U0	Drywall and Interior Finishes - Lower Suite Level Quad C2	80	23-Aug-19	18-Dec-19	64
S4A2-8U0	Drywall and Interior Finishes - Lower Suite Level Quad A2	80	13-Sep-19	09-Jan-20	22
S4C3-8U0	Drywall and Interior Finishes - Lower Suite Level Quad C3	85	13-Sep-19	16-Jan-20	62
S4A3-8U0	Drywall and Interior Finishes - Lower Suite Level Quad A3	80	27-Sep-19	23-Jan-20	22
S4D1-8U0	Drywall and Interior Finishes - Lower Suite Level Quad D1	95	15-Oct-19	03-Mar-20	22
S4D2-8U0	Drywall and Interior Finishes - Lower Suite Level Quad D2	80	05-Nov-19	03-Mar-20	22
S4D3-8U0	Drywall and Interior Finishes - Lower Suite Level Quad D3	85	22-Nov-19	26-Mar-20	22
S400-8U00	Drywall and Interior Finishes - Lower Suite Level (Summary)	190	25-Jun-19	26-Mar-20	22
200 Upper Suite Level					
S5B2-8U0	Drywall and Interior Finishes - Upper Suite Level Quad B2	75	29-Jul-19	12-Nov-19	55
S5A1-8U0	Drywall and Interior Finishes - Upper Suite Level Quad A1	95	08-Jul-19	19-Nov-19	54
S5B1-8U0	Drywall and Interior Finishes - Upper Suite Level Quad B1	95	08-Jul-19	19-Nov-19	55
S5B3-8U0	Drywall and Interior Finishes - Upper Suite Level Quad B3	80	12-Aug-19	05-Dec-19	55

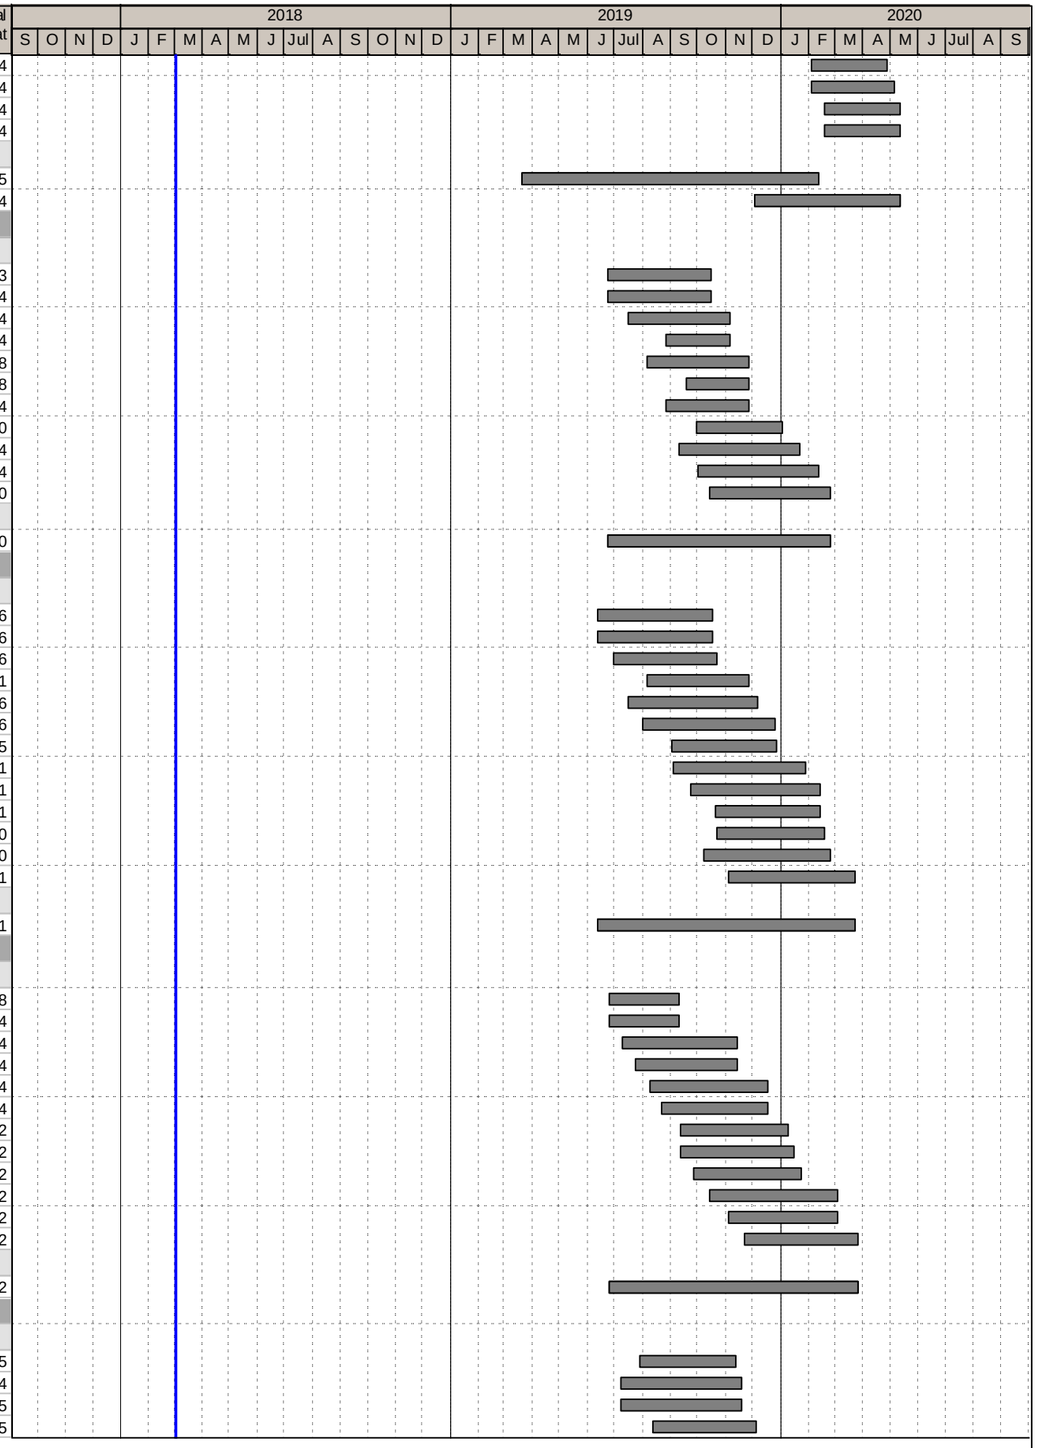

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S5C1-8U0	Drywall and Interior Finishes - Upper Suite Level Quad C1	80	26-Aug-19	19-Dec-19	55
S5C2-8U0	Drywall and Interior Finishes - Upper Suite Level Quad C2	80	10-Sep-19	06-Jan-20	55
S5A2-8U0	Drywall and Interior Finishes - Upper Suite Level Quad A2	80	24-Sep-19	20-Jan-20	14
S5A3-8U0	Drywall and Interior Finishes - Upper Suite Level Quad A3	80	08-Oct-19	03-Feb-20	14
S5C3-8U0	Drywall and Interior Finishes - Upper Suite Level Quad C3	90	25-Sep-19	04-Feb-20	54
S5D1-8U0	Drywall and Interior Finishes - Upper Suite Level Quad D1	90	22-Oct-19	03-Mar-20	14
S5D2-8U0	Drywall and Interior Finishes - Upper Suite Level Quad D2	80	05-Nov-19	03-Mar-20	14
S5D3-8U0	Drywall and Interior Finishes - Upper Suite Level Quad D3	100	20-Nov-19	14-Apr-20	14
S500-8U00	Drywall and Interior Finishes - Upper Suite / Club Level (Summary)	195	08-Jul-19	14-Apr-20	14
250 Mid Bowl Mezz Level					
S6B1-8U0	Drywall and Interior Finishes - Mid Bowl Mezz Quad B1	65	04-Sep-19	06-Dec-19	69
S6A1-8U0	Drywall and Interior Finishes - Mid Bowl Mezz Quad A1	65	03-Oct-19	08-Jan-20	38
S6C1-8U0	Drywall and Interior Finishes - Mid Bowl Mezz Quad C1	80	07-Oct-19	31-Jan-20	61
S6D1-8U0	Drywall and Interior Finishes - Mid Bowl Mezz Quad D1	80	24-Oct-19	20-Feb-20	38
S6D2-8U0	Drywall and Interior Finishes - Mid Bowl Mezz Quad D2	75	15-Nov-19	05-Mar-20	38
300 Upper Concourse					
S7B1-8U0	Drywall and Interior Finishes - Upper Concourse Quad B1	80	27-Aug-19	20-Dec-19	29
S7A1-8U0	Drywall and Interior Finishes - Upper Concourse Quad A1	85	30-Aug-19	03-Jan-20	51
S7B2-8U0	Drywall and Interior Finishes - Upper Concourse Quad B2	90	13-Sep-19	23-Jan-20	27
S7C1-8U0	Drywall and Interior Finishes - Upper Concourse Quad C1	90	27-Sep-19	06-Feb-20	27
S7A2-8U0	Drywall and Interior Finishes - Upper Concourse Quad A2	85	16-Oct-19	19-Feb-20	29
S7C2-8U0	Drywall and Interior Finishes - Upper Concourse Quad C2	85	17-Oct-19	20-Feb-20	23
S7D1-8U0	Drywall and Interior Finishes - Upper Concourse Quad D1	95	30-Oct-19	18-Mar-20	29
S7D2-8U0	Drywall and Interior Finishes - Upper Concourse Quad D2	80	21-Nov-19	18-Mar-20	29
S7CD1-8U0	Drywall and Interior Finishes - Upper Concourse Quad CD1	100	19-Nov-19	13-Apr-20	11
S700-8U00	Drywall and Interior Finishes - Upper Concourse (Summary)	158	27-Aug-19	13-Apr-20	11
350 Upper Mezz Level					
S8A1-8U0	Drywall and Interior Finishes - Upper Mezz Level Quad A1	75	30-Sep-19	17-Jan-20	61
S8B1-8U0	Drywall and Interior Finishes - Upper Mezz Level Quad B1	75	02-Oct-19	21-Jan-20	59
S8C1-8U0	Drywall and Interior Finishes - Upper Mezz Level Quad C1	85	08-Nov-19	13-Mar-20	32
S8D1-8U0	Drywall and Interior Finishes - Upper Mezz Level Quad D1	85	05-Dec-19	06-Apr-20	16
400 Press Level					
S9A1-8U0	Drywall and Interior Finishes - Press Level Quad A1	90	01-Nov-19	13-Mar-20	6
S9D1-8U0	Drywall and Interior Finishes - Press Level Quad D1	90	18-Nov-19	27-Mar-20	6
S900-8U00	Drywall and Interior Finishes - Press Level (Summary)	88	18-Sep-19	24-Jan-20	41
Specialties					
000 Event Level					
S100-8U80	Playing Field - Erect & Assemble	100	06-Dec-19	28-Apr-20	0
S101-8U80	Playing Field - Wheel in Playing Position	5	29-Apr-20	05-May-20	0
Multiple Seating					
Upper Seating Bowl					
SS00-8U9E	Stadium Seating	180	09-Aug-19	27-Apr-20	5
SS01-8U9E	Retractable Seating Systems	88	24-Dec-19	28-Apr-20	0
Site Improvements					
Site					
SS00-8V00	Site Improvements	232	29-May-19	28-Apr-20	0
Project Close-Out					

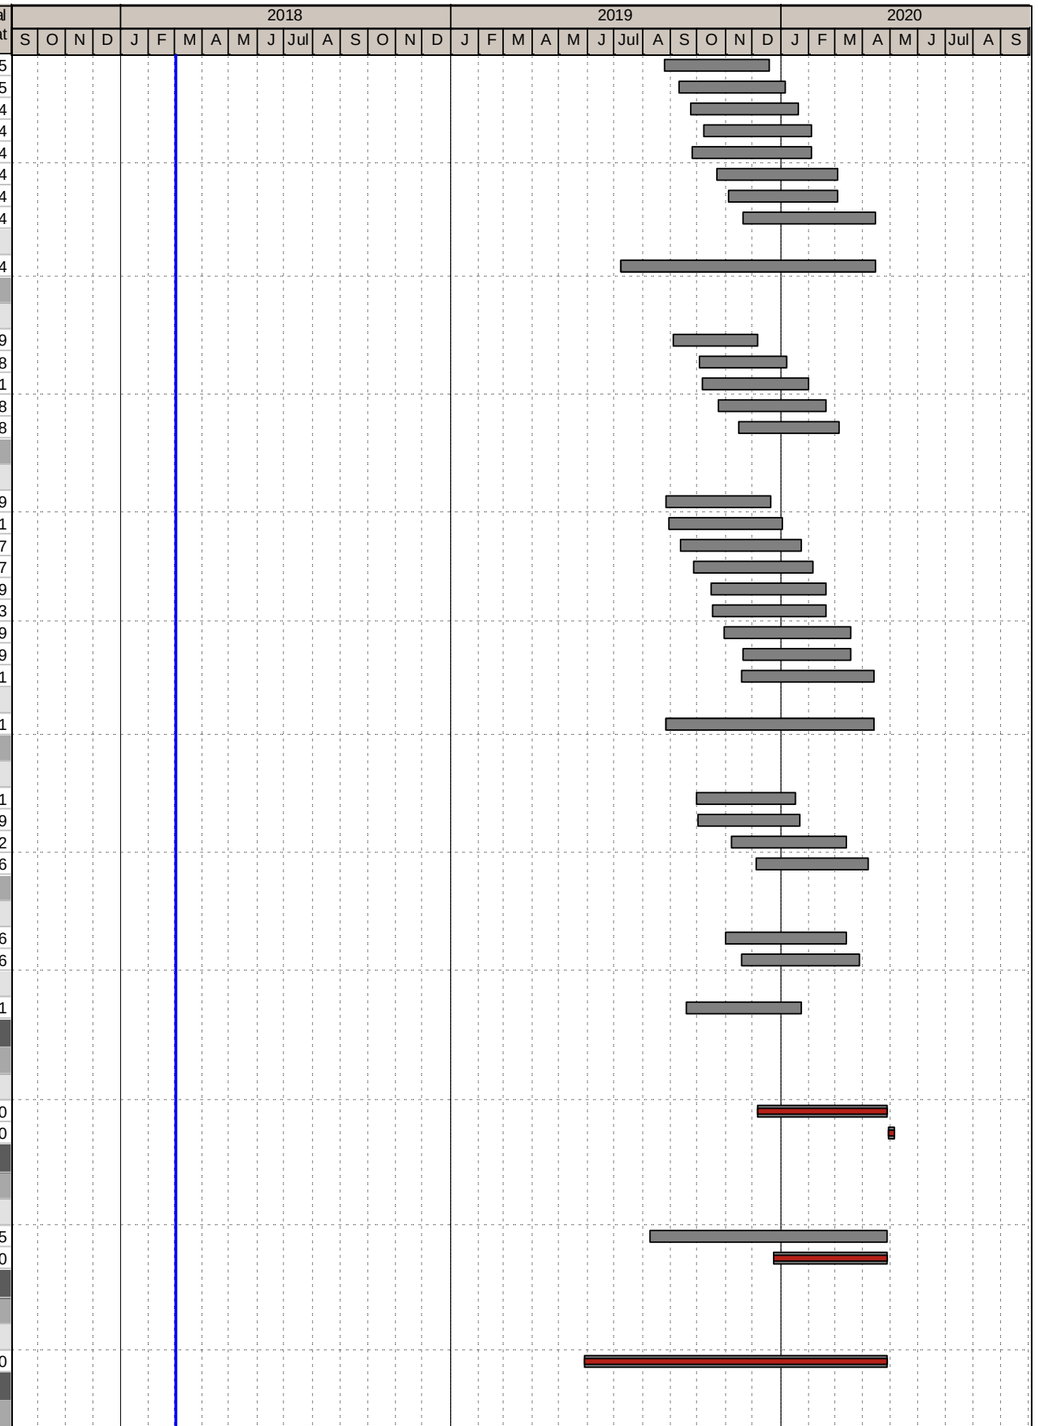

Activity ID	Activity Name	Orig. Dur'n	Start	Finish	Total Float
S000-8X20	Systems Start-up and Testing	105	02-Jan-20	29-May-20	0
S001-8X20	Authority Having Jurisdication Inspections	22	01-Jun-20	30-Jun-20	0
S000-8X30	Soft Opening / Game Prep	30	02-Jul-20	31-Jul-20	0
S001-8X30	Opening Game	0		01-Aug-20*	0
Site					
SST0-8X00	Clean-up & Pre-Punchlist - Site Detailment	44	29-Apr-20	30-Jun-20	0
SST0-8X10	Project Punchlist - Site Detailment	22	01-Jul-20	31-Jul-20	0
000 Event Level					
S100-8X00	Clean-up & Pre-Punchlist - Event Level	44	23-Apr-20	24-Jun-20	4
S100-8X10	Project Punchlist - Event Level	22	25-Jun-20	27-Jul-20	4
050 Lower Mezz Level					
S200-8X00	Clean-up & Pre-Punchlist - Mezz Level	44	24-Mar-20	22-May-20	6
S200-8X10	Project Punchlist - Mezz Level	22	26-May-20	24-Jun-20	6
100 Main Concourse					
S300-8X00	Clean-up & Pre-Punchlist - Main Concourse	44	31-Mar-20	01-Jun-20	6
S300-8X10	Project Punchlist - Main Concourse	22	02-Jun-20	01-Jul-20	6
150 Lower Suite Level					
S400-8X00	Clean-up & Pre-Punchlist - Lower Suite Level	44	07-Apr-20	08-Jun-20	6
S400-8X10	Project Punchlist - Lower Suite Level	22	09-Jun-20	09-Jul-20	6
200 Upper Suite Level					
S500-8X00	Clean-up & Pre-Punchlist - Upper Suite / Club Level	44	14-Apr-20	15-Jun-20	6
S500-8X10	Project Punchlist - Upper Suite / Club Level	22	16-Jun-20	16-Jul-20	6
300 Upper Concourse					
S700-8X00	Clean-up & Pre-Punchlist - Upper Concourse	44	20-Apr-20	19-Jun-20	7
S700-8X10	Project Punchlist - Upper Concourse	22	23-Jun-20	23-Jul-20	6
400 Press Level					
S900-8X00	Clean-up & Pre-Punchlist - Press Level	44	17-Mar-20	15-May-20	6
S900-8X10	Project Punchlist - Press Level	22	18-May-20	17-Jun-20	6
Upper Seating Bowl					
SS00-8X00	Clean-up & Pre-Punchlist - Field / Seating Bowl	44	29-Apr-20	30-Jun-20	0
SS00-8X10	Project Punchlist - Field / Seating Bowl	22	01-Jul-20	31-Jul-20	0

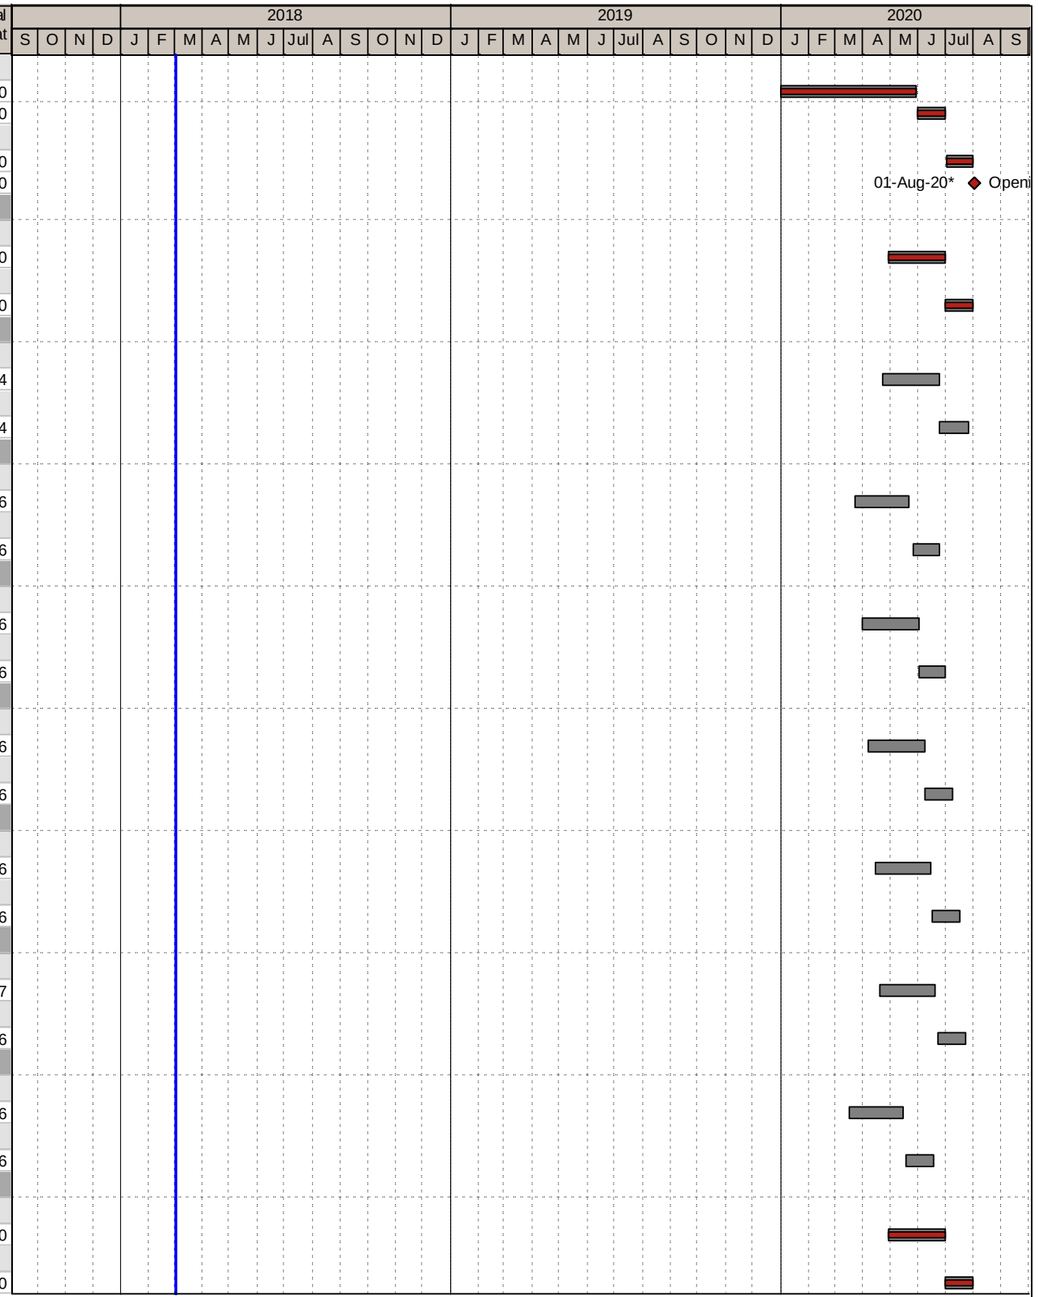

EXHIBIT L

Parent Guaranty

GUARANTY

This **GUARANTY AGREEMENT** ("Guaranty") dated as of the 22nd day of March, 2018, by Mortenson Construction Holdings, Inc., a corporation duly organized and existing under the laws of the State of Minnesota, U.S.A., with its head office situated at 700 Meadow Lane North, Minneapolis, Minnesota, U.S.A. ("MCH") and McCarthy Holdings, Inc., a corporation duly organized and existing under the laws of the State of Delaware, U.S.A. ("McCarthy Holdings"), with its head office situated at 1341 N. Rock Hill Road, St. Louis, Missouri, U.S.A. (MCH and McCarthy Holdings are each sometimes referred to herein as a "Guarantor" and collectively as the "Guarantors"), jointly and severally, for the benefit of LV Stadium Events Company, LLC, a Nevada limited liability company ("Developer"), Bank of America, N.A., as administrative agent under the Credit Agreement (as defined below) for the Secured Parties (as defined in the Credit Agreement) (the "Administrative Agent") and the Clark County Stadium Authority, a political subdivision of Clark County, Nevada, and a separate governmental entity established pursuant to Senate Bill 1 of the 30th Special Session of the Nevada State Legislature, also known as the "Las Vegas Stadium Authority" and the "Las Vegas Stadium Authority Board" (the "Authority") (Developer, the Administrative Agent, and the Authority are each sometimes referred to herein as a "Beneficiary" and collectively referred to herein as the "Beneficiaries"; Guarantors and Beneficiaries are individually referred to herein as a "Party" and collectively as the "Parties").

RECITALS:

WHEREAS M. A. Mortenson Company, a Minnesota corporation ("Mortenson") is a wholly-owned subsidiary of MCH;

WHEREAS McCarthy Building Companies, Inc., a Missouri corporation, ("McCarthy") is a wholly-owned subsidiary of McCarthy Holdings;

WHEREAS Mortenson and McCarthy have entered into a Joint Venture Agreement to jointly pursue and complete the contract for a new football stadium located in Las Vegas, Nevada and certain other improvements and infrastructure (the "Stadium Project") under the name Mortenson-McCarthy Las Vegas Stadium, a Joint Venture (the "Joint Venture");

WHEREAS Developer and the Joint Venture have entered into a Guaranteed Maximum Price Design-Build Agreement, dated and effective as of February 20, 2017 (together with the schedules, annexes, and exhibits thereto and as the same may be amended from time-to-time, herein called the "Agreement");

WHEREAS under the Agreement, Mortenson and McCarthy have agreed to be jointly and severally liable for all of the Joint Venture's duties and obligations under the Agreement;

WHEREAS the Agreement requires that the Joint Venture cause to be provided a parent guaranty from Mortenson and McCarthy that guaranties, jointly and severally, performance of the Joint Venture's obligations under the Agreement (including any obligations to make payment),

and MCH and McCarthy Holdings are willing to enter into this Guaranty to satisfy this condition of the Agreement;

WHEREAS the Authority and Developer entered into a development agreement (the "Development Agreement") which, among other things, requires the Authority be named as a beneficiary under the Guaranty;

WHEREAS, on September 14, 2017, Financing Trust I, a Delaware statutory trust ("FinanceCo"), entered into a Credit Agreement (as amended, restated, supplemented or otherwise modified from time to time, the "Credit Agreement") with the lenders party thereto (the "Lenders"), the Administrative Agent and the collateral agent pursuant to which the Lenders agreed, subject to the terms and conditions contained therein, to extend credit to FinanceCo, the proceeds of which will be used to fund a portion of the costs and expenses of the Stadium Project;

WHEREAS the Credit Agreement requires that certain conditions be satisfied prior to the Lenders agreeing to extend further credit to FinanceCo, including the condition that the Joint Venture demonstrate to the satisfaction of the Administrative Agent sufficient financial resources to meet its obligations under the Agreement, and MCH and McCarthy Holdings are willing to enter into this Guaranty to satisfy such condition of the Credit Agreement; and

WHEREAS, in consideration of and as a material inducement to Developer entering into the Agreement, and to the Lenders agreeing to extend further credit to FinanceCo, the Guarantors have agreed to provide this Guaranty to Beneficiaries pursuant to the terms and conditions set forth herein, and the Guarantors acknowledge and agree that Developer would not have entered into the Agreement and the Lenders would not have agreed to extend further credit to FinanceCo without receiving this Guaranty from Guarantors.

NOW, THEREFORE, in consideration of the premises and mutual covenants set forth herein and Developer entering into the Agreement and the Lenders agreeing to extend further credit to FinanceCo, the Parties hereto agree as follows:

1. The Guarantors jointly and severally hereby irrevocably and unconditionally guarantee to the Beneficiaries and their respective successors and permitted assigns: (i) the complete performance and discharge of all obligations (including, without limitation, all indemnification obligations and any obligations to make payment) of the Joint Venture under the Agreement; (ii) the due performance by such Guarantors of their obligations under this Guaranty; and (iii) the payment of all expenses incurred by the Beneficiaries to enforce this Guaranty, including without limitation, reasonable attorneys' fees and litigation expenses (items (i) through (iii) are referred to collectively herein as the "Guaranteed Obligations").

2. If the Joint Venture fails in any respect to perform or observe any of the Guaranteed Obligations in Section 1(i) above, notice and demand having first been provided to the Joint Venture and the Joint Venture having failed to perform or observe the applicable Guaranteed Obligation(s) within thirty (30) days of having received notice from a Beneficiary, each Guarantor shall thereafter and upon five (5) calendar days of first demand in writing by a Beneficiary to such Guarantor, duly and punctually perform or take such steps as are necessary to achieve performance or observance, as applicable, of each of the Guaranteed Obligations subject to the terms and conditions of the Agreement (including without limitation any limitations of liability under the Agreement, Developer's payment obligations under the Agreement, and the absence of any uncured material breach of the Agreement by Developer), without any requirement that the Beneficiaries first proceed against the Joint Venture. Notwithstanding the previous sentence, a

Beneficiary shall give the Joint Venture ten (10) calendar days' notice, to the individuals and in the manner described in the notice provision of the Agreement, of its intention to make a demand on such Guarantor prior to making any such demand. Notice or demand by a Beneficiary shall be deemed as a notice or demand (as the case may be) by all Beneficiaries.

3. Each Guarantor agrees that: (i) this Guaranty is as a continuing, absolute and unconditional (except as otherwise provided herein) guaranty of performance of the obligations of the Joint Venture under the Agreement (including the obligation to make payment) and not of collection; and (ii) the obligations of each Guarantor hereunder are independent of the obligations of the Joint Venture and the obligations of any other guarantor (including the other Guarantor) of the obligations of the Joint Venture, and a separate action or actions may be brought and prosecuted against such Guarantor whether or not any action is brought against the Joint Venture or any of such other guarantors and whether or not the Joint Venture is joined in any such action or actions.

4. The obligations of each Guarantor hereunder shall not be reduced or discharged by: (i) any alteration in the relationship between the Joint Venture and Developer; (ii) any change in ownership of any interest of Mortenson, McCarthy or the Joint Venture or any change in the relationship of Mortenson, McCarthy, any Guarantor and the Joint Venture or any termination of such relationship; (iii) the release of all or any part of the Guaranteed Obligations without the prior consent of the Administrative Agent or the substitution or release of any person or entity primarily or secondarily liable for the Guaranteed Obligations; (iv) any voluntary or involuntary bankruptcy, insolvency, reorganization, arrangement, readjustment, assignment for the benefit of creditors, receivership, conservatorship, custodianship, liquidation, marshaling of assets and liabilities or similar proceedings with respect to Mortenson, McCarthy, the Joint Venture or the Guarantors, or any action taken by any trustee or receiver or by any court in any such proceeding; (v) the impairment of any collateral securing the Guaranteed Obligations, including without limitation the failure to perfect or preserve any rights or remedies the Beneficiaries might have in such collateral or the substitution, exchange, surrender, release, loss or destruction of any such collateral, or (vi) any failure of the Joint Venture, Mortenson or McCarthy to conform with any provision of the Agreement or any other agreement. Further, the liability of the Guarantors hereunder shall not be reduced or discharged by any forbearance or indulgence by the Beneficiaries towards the Joint Venture, Mortenson, McCarthy or the Guarantors whether as to payment, time, performance, or otherwise, to any degree greater than such forbearance or indulgence would reduce or discharge the liability of the Joint Venture.

5. Each Guarantor expressly and unconditionally waives (i) notice of any of the matters referred to in Section 4 above, (ii) notice of the commencement of the work under the Agreement, and notice of the status of the Guaranteed Obligations from time to time; (iii) all notices which may be required to be given to Guarantors by statute, rule of law or otherwise, now or hereafter in effect, to preserve intact any rights against the Guarantors, including, without limitation, any demand, presentment and protest, proof of notice of non-payment under the Agreement and notice of any default or any failure on the part of Joint Venture (except for the notice required by Section 1 above); (iv) any right or claim of right to cause a marshalling of the assets of the Joint Venture or the Guarantors; (v) any right to require the Beneficiaries to exhaust or take any action against the Joint Venture or other person (including the other Guarantor) or entity prior to or contemporaneously with proceeding to exercise any right or remedy against the Guarantors under this Guaranty, or otherwise pursue any other remedy available to the Beneficiaries, including proceeding against or exhausting any bond, insurance or other security held by the Beneficiaries or any other party; (vi) all other defenses of a surety (except to the extent any such defenses are expressly permitted under this Guaranty); and (vii) any right of subrogation, contribution,

reimbursement, or indemnity whatsoever (except as between Guarantors), or any right of recourse to or with respect to the assets or property of the Joint Venture until all Guaranteed Obligations have been paid and satisfied in full, and in connection with the foregoing, hereby waives any and all rights of subrogation to the Beneficiaries against the Joint Venture, and each Guarantor hereby waives any rights to enforce any remedy that the Beneficiaries may have against the Joint Venture.

6. The obligations of each Guarantor hereunder shall continue in full force and effect until all Guaranteed Obligations have been irrevocably paid, performed and discharged in full.

7. This Guaranty and the undertakings herein contained shall be binding upon the successors and assigns of the Guarantors. This Guaranty shall extend to and inure to the benefit of the successors and permitted assigns of Developer under the Agreement and the Administrative Agent under the Credit Agreement and the Authority under the Development Agreement. This Guaranty may not be assigned by the Guarantors without the prior written consent of the Beneficiaries. Any attempted assignment without the Beneficiaries' prior written consent shall be void. No person other than the Beneficiaries, their successors and permitted assigns under the terms of the Agreement, Credit Agreement, and the Development Agreement, as applicable, are beneficiaries of this Guaranty nor shall any such person have any rights hereunder.

8. Notwithstanding anything to the contrary in this Guaranty, in the event of any claim under this Guaranty, Guarantors shall be entitled to assert any defense or counterclaim that the Joint Venture could assert under the Agreement.

9. Each Guarantor hereby waives any right to assert against the Beneficiaries any defense, counterclaim, set-off or cross claim, or any other claim that such Guarantor may now or at any time hereafter have against the Joint Venture. Any disputes between the Guarantors and the Beneficiaries arising under this Guaranty, including breach thereof, shall be handled in the same manner as set out in the disputes provision of the Agreement.

10. This Guaranty shall be governed by and construed in accordance with the laws of the State of Nevada without regard to principles of conflicts of law.

11. THE VENUE FOR ANY LEGAL ACTION TO ENFORCE, INTERPRET, OR OTHERWISE LITIGATE DISPUTES RELATING TO THIS GUARANTY SHALL BE ANY COURT HAVING PROPER JURISDICTION THAT IS LOCATED CLARK COUNTY, NEVADA, AND EACH PARTY HEREBY CONSENTS TO PERSONAL JURISDICTION OF AND VENUE IN SUCH COURT. EACH PARTY HEREBY IRREVOCABLY WAIVES, TO THE FULLEST EXTENT PERMITTED BY LAW, ANY OBJECTION WHICH IT MAY NOW OR HEREAFTER HAVE TO THE LAYING OF VENUE OF ANY SUCH PROCEEDING BROUGHT IN ANY SUCH COURT AND ANY CLAIM THAT ANY SUCH PROCEEDING HAS BEEN BROUGHT IN AN INCONVENIENT FORUM.

12. Each Guarantor represents and warrants to the Beneficiaries that it is organized, validly existing, and in good standing under the laws of the jurisdiction of its formation; it is authorized to guaranty the Guaranteed Obligations; that it has all of the rights and powers necessary to do so; that the individual signing below is authorized to bind such Guarantor to its obligations under this Guaranty; that the execution, delivery and performance by such Guarantor of this Guaranty do not and will not (i) violate (a) any provision of any law or any governmental rule or regulation applicable to such Guarantor, (b) any of the organizational documents of such Guarantor, or (c) any order, judgment or decree of any court or other agency of government binding on such

Guarantor; (ii) conflict with, result in a breach of or constitute (with due notice or lapse of time or both) a default under any contractual obligation of such Guarantor; (iii) result in or require the creation or imposition of any lien upon any of the properties or assets of such Guarantor; or (iv) require any approval of stockholders, members or partners or any approval or consent of any person under any contractual obligation of such Guarantor, except for such approvals or consents which will be obtained on or before the date hereof and disclosed in writing to the Beneficiaries; this Guaranty has been duly executed and delivered by such Guarantor and is the legally valid and binding obligation of such Guarantor or such Persons, enforceable against such Guarantor in accordance with its respective terms, except as may be limited by bankruptcy, insolvency, reorganization, moratorium or similar laws relating to or limiting creditors' rights generally or by equitable principles relating to enforceability, or under applicable law.

13. No amendment of this Guaranty shall be effective unless signed by the Guarantors and the Beneficiaries.

14. This Guaranty constitutes the entire agreement, and supersedes and terminates all prior written agreements and understandings, and oral agreements, between the Guarantors and the Beneficiaries with respect to the subject matter hereof.

15. Notwithstanding any term or condition to the contrary set forth above, and except for the obligations under Section 1(iii) above, it is the express intent of the Parties, and the provisions of this Guaranty shall be interpreted such that the Guaranteed Obligations of the Guarantors are no greater or less than the obligations of the Joint Venture under the Agreement.

IN WITNESS WHEREOF, this Guaranty is executed by an authorized representative of each of the Guarantors as of the date first written above.

MORTENSON CONSTRUCTION HOLDINGS, INC.

By: _____
Name: Daniel L. Johnson
Title: President & Chief Executive Officer

MCCARTHY HOLDINGS, INC.

By: _____
Name: J. Douglas Audiffred
Title: Chief Financial Officer

EXHIBIT M

BIM Implementation Plan

BIM PROJECT EXECUTION PLAN

FOR

LAS VEGAS STADIUM

DEVELOPED BY

Mortenson construction | McCARTHY®

HNTB

Note: This BIM Project Execution Plan, including all exhibits, is subject to being modified in a manner acceptable to Mortenson-McCarthy and HNTB, and the parties commit to agreeing to such modification by March 30, 2018

TABLE OF CONTENTS

Table of Contents ii
Project Overview 4
Mission statement 4
Overview 4
Project Information 5
Project Name 5
Project Description 5
Definitions 5
Contract Type 5
Project Location and Address 5
Project Numbers 5
Key Project Contacts 5
BIM Project Execution Plan Overview And Goals 9
Introduction 9
Key Objectives and Potential BIM Uses 9
Project BIM Uses by Phase: 10
Project Approach 9
BIM and Facility Data Requirements 14
Record Modeling 14
Organizational Roles / Staff and meetings 15
BIM Roles and Responsibilities 15
Collocation 17
Meetings 17
Project deliverables 20
Design Project Deliverables 20
Construction Project Deliverables 20
Format 22
BIM Process Guidelines 23
Process Overview Map 23
Design Assist Process Overview and Acknowledged Risk 24
Design Model vs. Trade Model Usage 24
Ownership and Use of the Design Models 24
Right of Reliance ..... **Error! Bookmark not defined.**
Basics Rules and Guidelines 24
Coordination 30
4D Simulation Project Approach 30
Design Information Exchange 31
Construction Information Exchange 31
3D Coordination Process 31
Quality Control 34

Overall Strategy for Quality Control During Design 34
Overall Strategy for Quality Control During Construction 34
Quality Control Checks 34
Model Accuracy and Tolerances 35
Coordinate System 35
Building Levels 38
Attachments 38
List 47

PROJECT OVERVIEW

Mission statement

Develop a unified focus on how VDC/BIM and related technologies will be utilized on the **LAS VEGAS STADIUM** project to achieve the greatest value for all parties involved.

Overview

1. The Owner, Architect and Design Builder, in the effort to improve the collaboration on the project define the project's building information models (BIM) and Virtual Design and Construction requirements for the project. The resulting BIM PxP document references exhibit "Attachment 05a - MEA LOD Specification" (MEA as in Model Element Author and LOD as in Level of Development). As such, these two documents, BIM PxP and the "Attachment 05a - MEA LOD Specification" establish the baseline minimum for the BIM deliverables on the project.
2. Key members of the project: Owner, Architect, Design Consultants, Design Builder and Trade Partner teams have developed this BIM Project Execution Plan, (BIM PxP) to understand how each party intends to use 3D modeling technology on the project. This plan provides an implementation strategy for meeting the project's BIM requirements as well as to provide a unified approach. The utilization of 3D modeling technology on this project will have the highest rate of success when all parties adhere to the procedures, guidelines and scope definitions described herein. the BIM scope divided amongst different parties with separate contracts, this document will allocate responsibilities for those involved through their contracted phases. As such, deviations from this plan requires approval by the VDC/BIM Managers from HNTB and Mortenson-McCarthy.
3. In developing the BIM Project Execution Plan, the project team first identified each of their respective BIM Goals for the project.
4. This BIM PxP is a living document and will continue to develop throughout the course of the project. This document will be maintained and updated throughout the project by the primary leaders of BIM/VDC utilization of Mortenson McCarthy JV and HNTB. Any proposed changes must be submitted to Project BIM Manager who will coordinate review of proposed changes with stakeholders. Once a consensus is reached an updated document will be distributed to the team. Iterations of the main document will be tracked by version number and date as displayed in the header of the document. Attachments will each be dated independently and may or may not be issued concurrently with the main document. The main document and each attachment may have a different date.

   The current version of the BIM Execution Plan along with appendixes will be posted to the project BOX site in the: **"Box Sync\...\Las Vegas Stadium Building Coordination\Documents\BIM Project Execution Plan – Current"** folder.

   (Direct link to Box - https://mortenson.box.com/s/nwgz9ol1onc8peqitp7bwzasj0sqjd8s)

PROJECT INFORMATION

Project Name

Las Vegas Stadium

Project Description

Las Vegas Stadium is the sports and events center that will be home to the NFL Raiders Football Team.

Definitions

Owner – LV Stadium Events Company, LLC
Design Team – Manica Architecture - Lead Design Architect (LDA) / HNTB - Architect of Record (AOR) and Associated Consultants – Engineers of Record - (EORs)
Design Builder – Mortenson - McCarthy Las Vegas Stadium, a Joint Venture
Trade Partners –Refer to Project Key Contacts Section
Project Team – Design Team, Design Builder, Trade Partners and any Tiered Parties Managed by a Trade Partner

Contract Type

Design Build

Project Location and Address

5617 Dean Martin Dr. Las Vegas, NV 89118

Project Numbers

ORGANIZATION	PROJECT NUMBER
Mortenson McCarthy JV	17150004
HNTB	65787

Key Project Contacts

The Services to be performed require the coordination of a multitude of consultants working together harmoniously. The team shall respond fully and promptly to each other's requests for information and advice, and each shall give due consideration to the advice, suggestions of the other and shall cooperate with one another in all matters. If the team disagrees on any matter, they shall quickly refer the issue to the project's BIM Team for resolution. The project's BIM Team, identified below, includes BIM Managers and leads for each Design Consultant, Trade Partner and Design Builder teams.

ROLE	ORGANIZATION	CONTACT NAME	LOCATION	E-MAIL	PHONE
Project Leads (Design Builder Team)	MMC (GC)	Adam Hardy	Las Vegas, NV	Adam.Hardy@mmcjvlv.com	480.748.0603
	MMC (GC)	Brian Fitzpatrick	Las Vegas, NV	Brian.Fitzpatrick@mmcjvlv.com	480.294.0793
	MMC (GC)	Paul Dudzinski	Las Vegas, NV	Paul.Dudzinski@mmcjvlv.com	702.830.4343
Project Leads (Design Team)	HNTB (AOR)	Lanson Nichols	Kansas City, MO	LNichols@HNTB.com	816.527.2728
	ARUP (Structure)	Atila Zekioglu	Los Angeles, CA	Atila.Zekioglu@arup.com	310.404.1879
	SSR (MEPF EOR)	Kevin Graham	Nashville	kgraham@ssr-inc.com	615.514.6172

BIM Leads (Design Builder Team)	MMC (Project Lead)	Joel Jacobson	Las Vegas, NV	Joel.Jacobson@mmcjvlv.com	815.404.1946
	MMC (Project Support)	Michal Wojtak	Minneapolis, MN	Michal.wojtak@mortenson.com	763.287.3502

ROLE	ORGANIZATION	CONTACT NAME	LOCATION	E-MAIL	PHONE
BIM Leads (Design Team)	HNTB (AOR)	Allyn Polancic	Los Angeles, CA	rborszich@hntb.com	816.527.2304
	HNTB (AOR)	Ryan Borszich	Kansas City, MO	apolancic@hntb.com	213.403.1019
	MANICA (Designer)	Beau Beashore	Kansas City, MO	bbeashore@manicaarchitecture.com	816.421.8890
	ARUP (Structure)	Frank Freudenberger	Los Angeles, CA	frank.freudenberger@arup.com	310.578.4549
	ARUP (Structure)	Pedro Mejia	Los Angeles, CA	Pedro.Mejia@arup.com	310.578.4487
	SSR (MEPF EOR)	Ryan Eggers	Nashville, TN	reggers@ssr-inc.com	615.460.0450
	SSR (MEPF EOR)	Abe Morris	Nashville, TN	Amorris@ssr-inc.com	615.514.6142
	SSR (MEPF EOR)	Stacy Webb	Nashville, TN	Swebb@ssr-inc.com	615.514.6176
	Kimley-Horn (Civil)	Jody Belsick	Las Vegas, NV	Jody.belsick@kimley-horn.com	702.327.2367
	Lloyd (Civil)	Tish Lance	Phoenix, AZ	tlance@lloydengineers.com	206.858.8548
	WJHW (A/V Designer)	Jennifer Joseph		jjoseph@wjhw.com	972.934.3700
	Rios Clementi Hale (Designer)	Andres Montemayor	Los Angeles, CA	andres@rchstudios.com	323.785.1800 Ext. 271
	Duray (Food Service)	Pasha Meier		pasham@durayco.com	
	FP&C (FP Consultants)	Paul Villotti		pvillotti@fpc-consultants.com	816.931.3377
	CPP Wind	Jessica Standard	Fort Collins, CO	jstandard@cppwind.com	970.416.6208

ROLE	ORGANIZATION	CONTACT NAME	LOCATION	E-MAIL	PHONE
Fabrication Detailer Leads (Trade Partner Team)	Mechanical Duct				
	Plumbing				
	Electrical				
	Fire Protection				
	Low Voltage / Audio Visual				
	Metal Panel				
	Precast Stadia				
	Structural Steel				
	Curtain Wall				
	ETFE				
	Precast Walls				
	Concrete Foundations				
	Concrete Slabs				
	Vertical Concrete				
	Misc. Metals				
	Food Service				
	Masonry				
	Interior Framing				

BIM PROJECT EXECUTION PLAN OVERVIEW AND GOALS

Introduction

Mortenson McCarthy JV in collaboration with HNTB will be the primary leader of BIM/VDC utilization for the entirety of the Las Vegas Stadium project. This document will serve as the guideline for Design Consultants, Trade Partners' involvement and Project Team management of model content throughout the project's lifecycle. The Design Team, Design Builder and Trade Partners Team acknowledge that the BIM/VDC Project Execution Plan is a living document and will be updated as deemed reasonable. It is expected that all team members, including the Trade Partners, will follow the BIM Project Execution Plan herein, but will also contribute to the modification of the document as collectively agreed upon. It is pertinent that the Project's BIM/VDC is approached as a collaborative process and that all parties involved will gain significant value from successful BIM/VDC implementation.

Key Objectives

The key objectives for the Project's BIM/VDC Execution Plan are given in the table below. These objectives are to be pursued by the entire Project Team, from design through project closeout

OBJECTIVES
✓ Drive Early Decisions During both Design Phase and Construction
✓ Engage the Trade Partners in the Construction Documents development through Design Assist early engagement
✓ Ensure Effective Project Team Communication and Collaboration Environment
✓ PR & Community Engagement
✓ High Quality Performance
✓ Ensure Cost Conformance
✓ Ensure Schedule Conformance
✓ Support Safety and Zero Injury Policy

Project Approach

Below is a summary level overview of the project team in (5) main areas of focus:

1. Mortenson McCarthy JV will manage the construction BIM/VDC process and associated Trade Partners. Mortenson McCarthy JV shall serve as the primary conduit for information between the Design Team and the construction team, and each project stakeholder shall staff the appropriate personnel to fulfill BIM/VDC goals and requirements as stated herein.
2. BIM/VDC will be used as a real-time coordination, collaboration, and communication tool. It is anticipated that there will be engagement in BIM/VDC technology from the entire project team to provide real time access to the most current, accurate information to help drive timely decisions.
3. There will be open and shared access to model information during the Design Assist partnership. The Design Team is primarily leveraging "Collaboration for Revit" and are sending weekly published models for the Trade Partner's use. The Trade Partners are uploading weekly to "BOX" cloud environment for the Design Team's use. Each party is responsible for their content as defined in the **"Attachment 05a - MEA LOD Specification"** and agrees to make shared content as current and accurate as possible. All parties understand that individual members of the project team will utilize shared content as provided by the Model Element Author (MEA), to assist in issue avoidance and resolution. The **"Attachment 05a - MEA LOD Specification"** is structured using the UniFormat 2010 structure. Please refer to the **"Attachment 05c - UniFormat2010."**

4. There will be proactive, early engagement of MEPF, Steel Structure, Enclosure, Precast Stadia and Vertical Transportation Trade Partners. It is the intent that the MEPFP Design Assist partner's model content will be integrated into the Construction Documents as defined in the **"Attachment 05a - MEA LOD Specification."** At the minimum slab and structural openings, sleeves, hangers, and seismic support locations will be coordinated prior to and confidently placed as structure is designed. Effective 3D Coordination with all disciplines can ensure that Mechanical, Electrical, Plumbing and Fire Protection (MEPF) systems are 100% accessible and this approach will maximize the use of trades' prefabrication and expedited installation on the Project.
5. BIM/VDC will be used to help communicate the progress across all Project Stakeholders. Applications of 3D visualizations will not only provide design and schedule certainty; it will also permit the client to showcase the project to key stakeholders. Trade partner supplied model content will ensure that project team meets all critical path milestone dates through 4D phase planning process and sequence presentation. It is the intent that in the same operation, fabrication and lead times for material tracking will also be deduced from sequence coded by MEA model content. 2D, 3D, and 4D BIM/VDC processes for phase planning are outlined at a summary level in "Attachment 07b -Phase Planning Process Map."

Project BIM Uses by Phase:

Mortenson McCarthy JV, in agreement with Las Vegas Stadium, has further devised a table noting each objective's relative importance to the success of the Project. Alongside each objective are potential BIM use(s) for project implementation.

PRIORITY (HIGH/ MED/ LOW)	OBJECTIVE DESCRIPTION	POTENTIAL BIM USES
HIGH	Drive Early Decisions, Design Assist partner's integration into Construction Documents development. Improve construction readiness of Construction Documents at each design package deliverable	Design Authoring Design Review Phase Planning 3D Coordination 3D Visualization
HIGH	Ensure effective communication and collaboration environment for all project stakeholders throughout the project lifecycle	Design Authoring Design Review Site Utilization Planning Construction System Design 3D Coordination
HIGH	PR & Community Engagement	Phase Planning Design Reviews 3D Visualization
HIGH	High Quality Performance	Construction System Design Digital Fabrication 3D Control and Planning
MED	Use Model based Take off techniques to ensure Cost Conformance	Design Review Cost Estimation Construction System Design
MED	Use 4D model to ensure Schedule Conformance	Phase Planning
LOW	Facilities Management	Record Modeling Asset Management
LOW	Support Safety and Zero Injury Policy	Site Utilization Planning Phase Planning Construction System Design 3D Coordination

The Design Team will coordinate 3D BIM Design Models to the Level of Design and scope as indicated in the LOD Specification. BIM will be delivered to the Owner, in the form of a design "For Record" model and a construction "As-Built" deliverable. Once delivered, the Owner will assume responsibility for the maintenance and update of the BIM to be used for all post-construction related activities. Construction Models are to be defined as models generated by general or trade contractors used for constructability analysis, construction sequencing, cost analysis, or other purposes related to construction of the project.

The following matrix defines BIM goals and uses as applied to project Design Models (authored by the Design Team) versus Construction Models (authored by the Design Builder and/or Project Team). This table supersedes all other definitions within this document relating to BIM use.

● = REQUIRED 3D CONTENT
○ = 2D INFORMATION ONLY
x = NOT REQUIRED

Planning		
Description	**Design Team Responsibility**	**Construction Team Responsibility**
Existing Conditions	x	x
2D o BIM (Arch)	○	○
2D to BIM (Struc)	○	○
Laser Scanning	x	x
Room / Program Management	●	●
Site Analysis	●	x
Phase Planning (4D Model)	x	●
Cost Estimation (For Baseline Checks)	x	●
Design		
Description	**Design Team Responsibility**	**Construction Team Responsibility**
Design Authoring	●	x
Design Reviews	●	●
3D Coordination	●	●
Structural Analysis	○	○
Lighting Analysis	○	○
Energy Analysis	○	○
Mechanical Analysis	○	○
Phase Planning (4D Model)	x	●
Cost Estimation (For Baseline Checks)	x	●
Construction / Operations		
Description	**Design Team Responsibility**	**Construction Team Responsibility**
Site Utilization Planning	x	●
Construction System Design	x	●
3D Coordination	●	●
Digital Fabrication	x	●
3D Control and Planning	x	●
3D Visualization	●	●
Phase Planning (4D Model)	x	●
Cost Estimation (For Baseline Checks)	x	●
Asset Management	x	○
Space Management / Tracking	x	○
Record Modeling	●	●

BIM AND FACILITY DATA REQUIREMENTS

Design Team Protocol

Area calculation for Revit Rooms will use the default Revit settings. Specific BOMA requirements are outside the scope of this document.

Record Modeling

The owner does not have any BIM requirements defined at this time, however in the expectation that future project specifications will require As-Built models to be tailored in some fashion for Operations and Facilities Management's use, Mortenson McCarthy JV requires the following of their Trade Partners:

1. At the conclusion of the project, as part of the project close-out phase, the Design Team will provide the owner with the BIM developed to the level as indicated within the LOD Specification. The Design Team will update the BIM to include construction changes documented through RFI, ASI, Addendum and Bulletin and deliver this as a Record Model to the level defined within the LOD Specification. The Design Team is not responsible for incorporating construction changes which are undocumented or are the result of Design Builder means and methods of construction. Record Drawings will be based on and created from the Record Model and delivered in Revit format. (.rvt)
2. The owner deliverable from the construction team will be Navisworks Models (.nwd), one overall and one per level. Navis models shall include record models with additional requirements per scope along with the native authoring models including Tekla, Revit, AutoCAD and Civil3D
3. Model review meetings with owner facilities staff and BIM involved project team members may occur to identify equipment access issues and confirm post construction usability.
4. Trade foremen should review what is being modeled/coordinated prior to and during coordination. "Install what is modeled" is the rule unless the trade foremen know the model/field installation drawing is wrong and requires correction. In the latter case, the area in question may need additional coordination and edits to trade models, and does not constitute grounds for compensation.
5. Trades' foremen will need to coordinate daily with each other and with the collective BIM Staff (see Key Project Contacts). Composite models will have shared ownership, other trades will require the ability to see where each other's system routing. Sharing and/or swapping reserved space is acceptable if discussed between Trade Partners and the appropriate authority from Mortenson McCarthy JV prior to installation.
6. 2D As-Builts, created from record models are required for Steel and MEPF for this project. The coordination model will be updated per field coordinated locations in what shall be understood as a record model.

A process flow-chart for record modeling is included in **"Attachment 07c - Record Modeling Process Map."**

ORGANIZATIONAL ROLES / STAFF AND MEETINGS

BIM Roles and Responsibilities

Design BIM Manager / Coordinator – HNTB's BIM/VDC Manager / Coordinators will manage the BIM development and coordination for the Design Team and their consultants. They will manage their internal Design Team's meetings, while participating in external coordination meetings led by the MMC team. The HNTB team, and its consultants will be responsible for implementing the guidelines documented within this BIMxP and associated attachments are delivered by the Design Team.

Design Builder VDC Manager / VDC Coordinator – Mortenson McCarthy JV VDC Coordinators will manage model storage and model exchange for the construction team. The MMC team will facilitate meetings and coordination of multiple trades in conjunction with MMC team members, whom are responsible for contract management of specific trades. VDC Coordinators will also work with superintendents and project managers to support the field's quality assurance, scheduling and safety.

Design Builder Project Engineers – Mortenson McCarthy JV team members (MEPF, Concrete Structure, Steel, Misc. Metals, Enclosure, Interiors) - All project engineers involved in these contracts will be involved to some degree in virtual coordination of these items. Reviewing shop drawing submittals with BIM Manager/Engineer and coordination models is required.

Trade Partner Project Manager - This person is responsible for ensuring production efficiency from the detailing team by providing information distribution, schedule updates, RFI analysis, and other management related decisions in a timely fashion to support their detailing team. This person shall be in frequent communication with trade partner detailers and empowered to make prompt decisions as they relate to coordination. Project managers are responsible to properly staff their support team to meet the coordination and construction schedules. The field installation schedule will not be held up to accommodate a coordination schedule that falls behind and thus may require additional resources to meet field construction requirements. Refer to previously agreed upon "Exhibit J" and associated Trade Specific Provisions for Additional Requirements.

Trade Superintendent or Foreman - As part of Mortenson McCarthy JV sign-off procedures, foremen are required to review models prior to sign-off, agree upon final sign-off, participate in interactive review, and be involved in the BIM coordination process as needed for coordination support as a field liaison. Foremen should be available for coordination meetings to provide input on coordination, sequencing and constructability of their scope. Foreman are also required to assure that sign-off models are utilized downstream in the form of shop drawings, material procurement, total station layout and field installation. Refer to previously agreed upon "Exhibit J" and associated Trade Specific Provisions for Additional Requirements.

Trade Partner Job Captain - There shall be one, self-appointed person (per trade) identified to proactively resolve coordination issues between MEPF trades. Only major issues will be discussed in coordination meetings. (Note; Incidental clashes will not be resolved in a group setting, and 'offline' resolution is the responsibility of the Job Captains). A strong Job Captain is critical to efficient MEPF Coordination. Refer to previously agreed upon "Exhibit J" and associated Trade Specific Provisions for Additional Requirements.

Trade Partner Detailer - Person(s) responsible for the detailing of each trade partner's BIM content. This person will need to be a full-time member of the project team for the duration of coordination through final sign-off. Staffing should be planned so as not to overload the Detailer and to provide additional resources as deemed necessary. This is not in our Exhibit contract language, but will be required. Each trade partner should consider a backup staffing (detailer) plan in event of vacation, illness, overlap coordination vs.

fabrication/field drawing schedule. Refer to previously agreed upon "Exhibit J" and associated Trade Specific Provisions for additional requirements.

Support Trades - These are non-model contributors whose input on constructability is required for the project. They will attend special coordination meetings to review their scope and issues that were identified during regular coordination meetings.

Collocation

For the duration of construction 3D Coordination, Mortenson McCarthy JV will require that trade partner job captains and detailers for each scope to be located on-site in the BIM section of the project trailer, as full-time members of the project team. Trade superintendents, trade foremen are required to oversee routing and coordination of their trade, confirming what is modeled can be installed effectively. MMC VDC Managers/VDC coordinators, trade partner detailers and job captains are to be collocated at a construction trailer provided at 5617 Dean Martin Dr. Las Vegas, NV. All roles above, apart from support trades, will be required to attend at a minimum all weekly coordination meetings and all other meetings scheduled as required. Trade Partner project managers and foreman will be required to check-in routinely with their detailers in addition to the formal weekly coordination meetings. It is the expectation that all roles on site (and, or collocated in the BIM trailer) will have the appropriate hardware, software, licensing, access to data, servers, plotters/printers etc., required for their participation in the 3D Coordination effort. Trade Partners are required to come to the project site prepared to fulfill their roles.

Members of the design team will be present at the Project office as separately agreed by Design-Builder or the Architect. They are to support the efforts by sending team members who have the project knowledge and are empowered to make decisions efficiently and effectively. During construction 3D Coordination, Mortenson McCarthy JV will work to eliminate redundant meetings that may occur during Design Assist and will combine the meetings where applicable, leading up front with design coordination followed up with construction coordination issues.

Meetings

1. Design Team, including consultants, are required to collaborate with each trade through electronic means, email, telephone, and in person to resolve basic issues outside of the bi-weekly coordination meetings. It is expected that the weekly coordination meetings are held to address difficult areas that are not able to be coordinated between the multiple disciplines themselves not to review individual clashes. These meetings may be part of the Design BIM Coordination Meeting or separate and where applicable will be included in the construction 3D Coordination meetings. During construction, the expectation is that the Design Team is informed and engaged throughout the coordination process.
2. Construction 3D Coordination meetings will include superintendents, MMC BIM leads, BIM manager/engineer, PMs and foremen. These will take place in the MMC jobsite conference room as well as streamed virtually via online meeting software. Monitors/projectors will be used to display models for discussion and generate markups for proposed routing changes. Trade job captains are expected to attend this meeting and foreman are expected to attend critical area review meetings. If issues are not being resolved outside these meetings or progress is too slow, review meetings will be held at quicker intervals and correspondence will be initiated with the trade partner's project manager.
3. Design Builders are required to monitor and coordinate system accessibility. An initial meeting will be held between the Design Builder, Trade Partners, Design Team, and the owner to review accessibility guidelines and expectations. A database file will be created and maintained to capture access requirements for the project, per applicable scope
4. At coordination sign-off for all trades on a given level, area, or section of the building, accessibility review meetings will be held by the on-site MMC lead to confirm accessibility for future maintenance and service. Both the engineers of record and owner will be present in this meeting, for review of the serviceability of systems. Comments will be discussed and recorded for incorporation into construction models prior to field install. Access panel drawings will be produced and provided at the end of coordination of each coordination area. Each scope will be provided to MMC as a formal deliverable.
5. At the Sign-Off of each area the construction team will produce the composite model and send to the Design Team as a for record only submittal. The Trade Partners will submit their shop drawings as

typical; however, there is to be no expectation for the Design Builder to provide the Design Team with composite 2D drawings a submittal for review.

6. Coordination and issue resolution may extend beyond the period of collocation for those in the BIM trailer on-site. In this event, it is the expectation that each role remains as dedicated and involved in the 3D Coordination effort as necessary to meet the Critical Path (CPM) schedule. Coordination meetings and issue resolution may move from in-person meetings to virtual work sessions and will require the mandatory attendance of each role as noted in this section.

Below is a list of on-going meetings with a list of required attendees:

MEETING TYPE	PROJECT STAGE	FREQUENCY	MEETING MANAGER / PARTICIPANTS	LOCATION
Design BIM Requirements Kick-off Meeting	Design GMP	Once	**HNTB** / All Design Discipline BIM Leads and Project Leadership	
Design BIM Coordination Meeting/Large Group	Design GMP/CD	Bi-Weekly	**HNTB** / All Design Discipline BIM Leads and Project Leadership as Required	
Design BIM Coordination Meeting/Small Group	Design GMP/CD	As Needed	**HNTB** / All Disciplines Along with BIM Leads	
Design GMP Hand-off	Design GMP	Once	**HNTB** / All Design Discipline BIM Leads and Project Leadership	
Design CD Hand-off	Design CD	Once	**HNTB** / All Design Discipline BIM Leads and Project Leadership	
Design Record Model Preparation	Design CA	Once	**HNTB** / All Design Discipline BIM Leads and Project Leadership	
Construction 3D Coordination Kickoff	Construction	Once per Bid Package	**MMC** / MMC BIM Leads, Trade Partner BIM Leads; Trade Partner Detailers	Las Vegas, NV
Construction 3D Coordination Meetings	Construction	Weekly/Daily	**MMC** / MMC BIM Leads, Trade partner BIM Leads, Design Team as necessary, Trade Partner Foreman as necessary, Owner as necessary	Las Vegas, NV
Construction Schedule Review Meetings	Construction	Weekly	**MMC** / MMC PMs, Supt, BIM Lead, Trade partner BIM Leads and Foreman	Las Vegas, NV
Constructability Review Meetings	Construction	As Necessary, Daily	**MMC** / MMC PMs, Supt, BIM Lead, Trade partner BIM Leads and Foreman	Las Vegas, NV
Access and FM Review	Construction	2 Weeks Before Each Sign-Off	**MMC** / MMC BIM Leads, Design Team, Owner, Trade Partner Foreman as necessary	Las Vegas, NV

PROJECT DELIVERABLES

Design Project Deliverables

Design documents will be categorized into (2) separate tasks: GMP Procurement Package Task and Construction Package Task.

Each of these tasks will be comprised of multiple design progress packages outlined in the Program Deliverables Schedule. The Owner will review each submittal and conduct a technical review meeting with the Designer and various Owner Departments. PDF and native authoring models (BIM) will be required deliverables at each project Milestone.

Prior to official deliverables (including BIM deliverables), Design Consultants must participate in and complete the Quality Assurance Plan as managed by the AOR. For each required Model deliverable or exchange, Design Consultants shall participate in and complete the Program Quality Management Plan as it pertains to that specific deliverable or exchange prior to delivery to ensure BIM Deliverables meet the Program requirements.

At the conclusion of the project, as part of the project close-out phase, the Design Team will provide the Owner with the BIM developed to the level as indicated by the LOD Specification. The design team is not responsible for incorporating construction changes which are undocumented or are the result of contractor means and methods of construction. Record Drawings will be based on and created from the Record Model. Refer to the Project Schedule for actual deliverable dates for project deliverables.

.DESCRIPTION	PHASE	SUBMITTED TO	FROM
Design Package	Design 62.5% GMP	MMC & Owner	Design Team
Design Package	Design 100% GMP	MMC & Owner	Design Team
Design Package	Foundation Permit Set	MMC & Owner	Design Team
Design Package	Structural Permit Set	MMC & Owner	Design Team
Design Package	100% CDs – Permit Set	MMC & Owner	Design Team

Construction Project Deliverables

Refer to the Project Schedule for actual deliverable dates. Many of the deliverables are part of the critical path and imperative that they are submitted per schedule. Mortenson McCarthy JV project managers and superintendents will enforce the coordination schedule, and reserves the right to modify as necessary to meet the construction schedule.

DESCRIPTION	PHASE	SUBMITTED TO	FROM
Foundation/Concrete/CMU Wall Penetration Drawings	Wall penetration phase and at minimum 2 weeks prior to Concrete/CMU installation whichever comes first	MMC & EOR	MEPF Trades
Elevated Deck Penetration Drawings	Slab penetration phase and at minimum 2 weeks prior to Concrete/CMU installation whichever comes first	MMC & EOR	MEPF Trades
Deck Point Load Drawings	Post Sign-Off Phase	MMC & EOR	MEPF Trades
Access panels drawings	2 Weeks Prior to Area's Sign-Off	MMC, Owner, AOR & EOR	MEPF Trades
Trade Partner Progress Models	Construction Coordination	MMC & EOR	MEPF Trades & MMC
Construction Sign-Off Models	Construction Coordination	MMC & EOR	MEPF Trades & MMC

Final As-Built Models and As-Built Points	Post Construction	MMC & Owner	AOR, EOR, MEPF Trades and MMC
Field Collected Data	During/Post Construction	MMC & Owner	MEPF Trades & MMC

Intermediate sign-off deliverables may be determined and added to the table above during construction to meet CPM milestones.

Format of Construction Deliverables

Refer to table below for the potential file formats of the submitted deliverables.

SUBMITTAL ITEM	FORMAT	NOTES
2D/3D Concrete Coordination Drawings	.ifc .nwc .dwg	Export to .nwc and .dwg or .ifc if using Tekla or SDS2
2D/3D Steel Shop Drawing Submittal	.ifc .dwg .nwc	Provide connection model of all steel to match 2D erection and piece mark sheets.
Virtual Mockup - Enclosure	.skp .rvt .dwg .pdfs	Virtual Mockups will be created prior to physical mockup to iron out issues and constructability. At a minimum, the areas referenced in the Mockup Specification will be reviewed.
2D/3D MEP Shop Drawing Submittals	.nwc .dwg	Provide nwc and .dwg. All dwg's will be exported in the format that does not require object enablers.
Virtual Mockups	.skp .rvt .dwg .pdfs	Virtual Mockup will be created prior to physical mockup to iron out issue areas. At a minimum, the areas referenced in the Mockup Specification will be reviewed.
2D As-Builts and 3D "Record Models" for Building Turnover	.pdf .dwg .rvt .nwc .nwd	Provide 2D As-Builts per specification requirement. A composite .nwd Navis file will be delivered to owner. Models must include field coordinated changes. All dwg's will be exported in the format that does not require enablers. All native authoring models will also be delivered to the owner and project closeout. All As-Built points, aka "Shots" are to be in State Plane Coordinates.

BIM PROCESS GUIDELINES

Process Overview Map

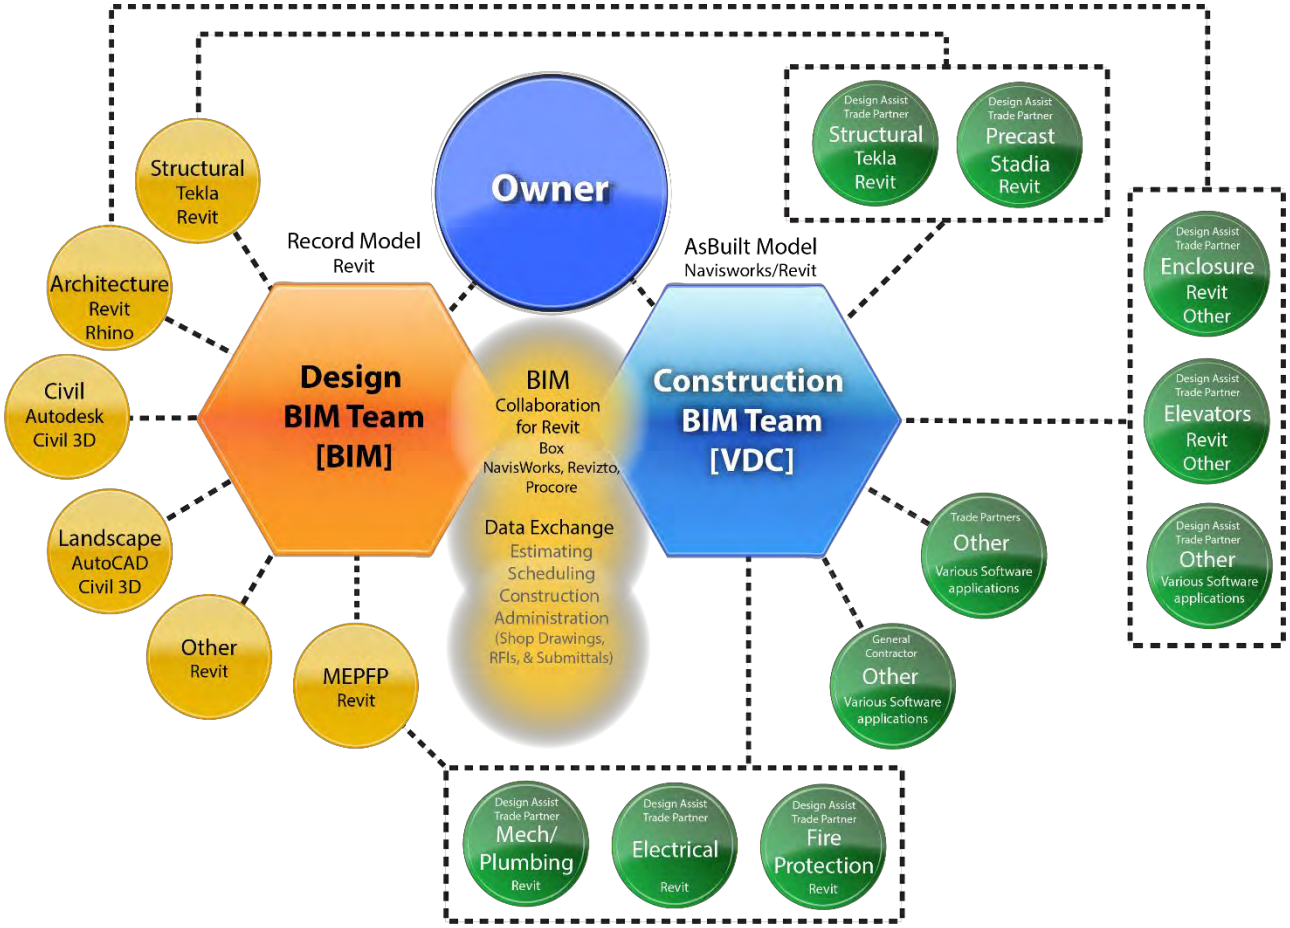

The process map indicates an overview example of the collaborative BIM/VDC process between the Design Team, Design Builder and Trade Partners. The final deliverable to the owner will be a fully coordinated and sufficiently detailed BIM for the project, as an as-built model communicated by the MMC team. As shown, the Design Team will provide several models in conjunction with the Contract Documents to the Design Builder. Mortenson McCarthy JV will use these models for estimating (visualization and verification), baseline 4D scheduling, and guidance in construction administration.

Following the award of Trade Partners, they will be designated as project participants and will be included with the project's BIM/VDC Execution Plan. All team members of the roles indicated above will meet for the 3D Coordination Kick-off Meeting and will transition to collocated full-time members on the project. Processes for 3D Coordination and other BIM/VDC efforts are outlined in detail on process maps provided within this document as **Attachments**. See the **Attachments** section of this document for the full list of all attachments.

The Design Team has detailed technical processes and approach to BIM development and delivery to the project team, [**"Attachment 09 - HNTB production standards"**]. The Design Team will remain in-control of this document.

Design Assist Process Overview and Acknowledged Risk

It is the intent of this project team to produce the Construction Documents with the Design Assist Trade Partners assistance provided during the Design Phase. During this phase, systems will be modeled per the directions given by the EOR by the Design Assist Trade Partners. The Architect of Record and Engineers of Record (Design Team) is to take 100% full responsibility of all design assist authored content that shows up on the Contract Documents and design models.

Design Model vs. Trade Model Usage

The required content of the Building Information Model prepared by the Design Team at certain points in time is set forth in the MEA LOD Specification. The rights of the Design Builder and its Subcontractors, Sub-Subcontractors, and Vendors with respect to the Building Information Models prepared by the Design Team are described in Section 3.22 of the Architect of Record Agreement and, for Subcontractors, the applicable Subcontract Agreement.

Ownership and Use of the Design Models

AOR will prepare (and will cause the AOR Consultants at every tier to prepare) building information models ("Design Models") as described in the BIM Execution Plan, and will share Design Models with Design-Builder and its Subcontractors as described in the BIM Execution Plan.

Design Model Updates and Right of Reliance

At the stages of development of the Design Documents described in the MEA LOD Specification attached as Exhibit 5a to the BIM Execution Plan (the "LOD Specification") as "100% GMP" or later, AOR will include (and cause AOR Consultants at every tier to include) in the Design Models the elements described in the LOD Specification. To the extent those elements are identified in the column labeled "Reliance Permitted" in the LOD Specification, they will be modeled at least to the degree of completeness and accuracy set forth in the LOD Specification. The information in Design Models described in the LOD Specification as "100% GMP" will be subject to the provisions of the Prose Statement and the GMP Clarifications and Assumptions.

At such time(s) as any Construction Documents are issued or updated by AOR or the AOR Consultants (at any tier), AOR will cause any information in a Design Model that is (a) also contained in the Construction Documents and (b) identified in the column labeled "Reliance Permitted" in the LOD Specification to be consistent with the information in the Construction Documents, provided the Parties recognize that particular design elements may be depicted in greater detail in the Construction Documents versus the Design Model. In the event of any conflict between the provisions of this Section 3.22.2.2 and Section 3.22.2.1, the provision of this Section 3.22.2.2 shall control

Design-Builder is an express third-party beneficiary of Section 3.22.

Without limiting the rights of Design-Builder under this Section 3.22, nothing in this Section 3.22 shall be deemed to limit Design-Builder's obligation to perform its Work in a manner consistent with the Construction Documents approved by Stadco.

In the event that AOR or an AOR Consultant at any tier intends that information in a Design Model ("Superseding Model Information") supersede or add to information in the Construction Documents, AOR will identify in the Construction Documents the Superseding Model Information and the Design Model in which it is contained.

Basics Rules and Requirements

Design Team Model Software

- Autodesk Revit 2017 – All team members must work in the same version of Revit. All Revit updates must be coordinated with entire project team and approved by Program and Project BIM Leads. Updates will be evaluated only after milestone deliverables.
- BIM 360 Team (C4R) – refer to section 7 for details.
- Autodesk Navisworks – While some users may require Navisworks Manage for clash detection, most users should be able to suffice with the Navisworks exporters.
- Autodesk Civil 3D (C3D) 2017 – Civil design and documentation will be in C3D.
- Tekla – The structural design team will be in modeling in Tekla and converting to Revit using native Revit geometry for collaboration with the rest of the design team. This converted geometry will follow the LOD requirement for the current phase of work. To maintain model efficiency, steel connection details will be excluded from this conversion.

Computers / Hardware

Refer to the Autodesk recommended hardware specification for Revit 2017. Note that for a project of this size and complexity, the minimum recommendation will likely not be sufficient.

Design Team Use of BIM360 Collaboration for Revit (C4R)

Each design team member will work in Autodesk BIM 360 Team using Autodesk Collaboration for Revit. The Design Team's project models must be live in the cloud at all times.

When uploading files to the BIM 360 Team collaboration site, please send out an email to all affected parties including the following:

- Uploaded files (list of file names)
- Summary and purpose of contents
- Location (if placed in specific folder)

HNTB will manage the Design Team's models and "Collaboration for Revit" cloud host for work-sharing. The design models will be developed to the level of detail outlined within the LOD Specification. **"Attachment 05a - MEA LOD Specification."** MMC and trade partner access to the "live" design models on "C4R" will not be allowed with exception to MMC's VDC Manager Joel Jacobson. To meet the demands of an aggressive design & construction schedule, "real-time" access is required. This access is provided only for exporting purposes and/or saving offline for downstream access and reference.

In order to facilitate collaboration on an individual Revit model across offices, Autodesk provides a service BIM 360 Collaboration for Revit (C4R) which enables cloud-based worksharing in Revit, accessible from anywhere with an internet connection. Instead of the Central file residing on a Local Network Fileserver, it is hosted in the Autodesk Cloud. Individual users continue to work locally similarly to the traditional process while synchronization happens between the local computers and the cloud service.

Due the large number of geographically distributed stakeholders, scope splits, and incremental hand-off, the design team will be leveraging this service across all disciplines. The AOR will host the BIM 360 Team Hub, however, each and every member of the design team working in Revit will require license access to BIM 360 C4R.

All parties with C4R permissions are not to open or access another discipline's or author's live file without prior approval from the Design Team AOR BIM Lead

There are (3) tiers of access within the BIM 360 Team environment:

BIM 360 Team Hub (Viewer)

BIM 360 viewers are limited to view only access to the files on the Autodesk BIM 360 NLVS Team Hub website.

- There are no additional licensing or costs associated with this level of BIM 360 access.
- The Revit models available on the Team Hub are NOT the "live" C4R cloud models. Instead, these models are "snapshots" of the models as published from the live C4R models.
- Team members with Viewer access will require download links to be sent from another Team Member with Editor access.

BIM 360 Team Hub (Editor)

BIM 360 Editors will have full upload/download access to the files on the Autodesk BIM 360 NLVS Team Hub website.

- There are no additional licensing or costs associated with this level of BIM 360 access.
- The Revit models available on the Team Hub are NOT the "live" C4R cloud models. Instead, these models are "snapshots" of the models as published from the live C4R models.
- The Revit models available on the Team Hub may be downloaded and viewed locally for reference only.
- Any changes made in these downloaded models will not be visible to the rest of the team and will not be reflected in the live C4R models.
- When downloading a model from the Team Hub, all linked models from the live models will be included in the download. You should not have to download the files individually.
- When uploading files to the Team Hub, information should be organized in dated folders or a ZIP file.
- When uploading files to the Team Hub, notification emails should be sent to all affected parties and include:
  - List of uploaded file names
  - Summary and purpose of contents
  - Location of folder & files on the Team Hub

BIM 360 Team Hub (Editor) + C4R *Additional license fees apply*

In addition to the standard BIM 360 Editor access described above, BIM 360 Editors with C4R Entitlements assigned to their Autodesk account will also have access to all "live" C4R models for this project.

- Revit version parity is critical to the seamless operation of C4R. Before working in C4R all team members shall verify that they are updated to the Revit build as coordinated by the BIM Leadership Team. Installation files for the current Revit build will be made available on the BIM 360 Team Hub.
- The live C4R models are ONLY accessible through the Revit 2017 "Open" dialogue.
- All work done in the C4R models will be sync'd to the cloud and visible to all other team members working in C4R.
- When working in the C4R models, the usual protocols for working in a Revit worksharing environment do apply. These include, but are not limited to:
  - Never close a model without first "Syncing" or "Relinquishing All Borrowed Elements".
  - If you want to exit the model without Syncing, close the model and when prompted, choose "Do not save the project" and "Relinquish all elements and worksets".
  - When working in the models, all team members shall use the "Revit Communicator" to monitor other users and activity in the model.
  - Before syncing, users should ALWAYS manually "Reload Latest" (RL).

- Before syncing, check Revit Communicator's "Timeline" tab to verify no other users are syncing. NEVER "Sync" over the top of another user.
- Never leave a C4R model open when not working for extended periods of time (overnight, etc.)

Base Models:
Mortenson McCarthy JV will manage the Base Models created from:

- 2D construction documents (Architectural and Structural Design Models).
- 3D Revit exports from Architect and Structural Engineer (exported by level).
- Supplemental Detail (i.e. No-Fly Zones) not shown in Revit models but beneficial for Building Coordination.

Trade Models:
Shop Drawing / Fabrication Models (Trade models) - steel, metal stud framing, other framing elements (rated enclosures, etc.) misc. metals, concrete, plumbing, HVAC dry, HVAC wet, Electrical, Fire Protection, Curtain wall, Specialty Equipment (food service, laundry, A/V, etc.) models provided by Trade Partners.

2D/3D Backgrounds:
For modeling with respect to other systems, background exports from models should be made available upon Mortenson McCarthy JV's. Guidelines for 2D/3D background exports are included in **"Attachment 03 - Meeting-Coordination Process."**

File Naming:
For all Trade Partners, 2D & 3D files provided to Mortenson McCarthy JV will be saved per the Schema in **"Attachment 02 - BIM Coordination File Name Schema."** The File Naming Schema is required and must be maintained throughout the project. Schema also provides guidelines in the file naming convention for identifying Author, File Type, Phase (of design), and Date (or sign-off deliverable). Color schemes and layer naming will also be consistent among Trade Partners as noted in **"Attachment 02 - BIM Coordination File Name Schema."**

File Set-up:
Project insertion point/origin and general elevations and zoning will be included in **"Attachment 03 - Meeting-Coordination Process."** Mortenson McCarthy JV will request from Trade Partners a "Test Model" that confirms accurate units, origin and general 3D content legibility. All models/files utilized for robotic total station field and/or as-built documentation must be created and maintained in State Plane Coordinates.

Design Data Information Exchange:
HNTB hosted Newforma InfoExchange will be used for official transmittals and transferring large files between team members. Project BIM Manager or Project Document Control will provide access.

The AOR will host the BIM 360 Team Hub Project where all shared design files will be kept. These files include, but are not limited to:

- Published model progress from C4R
- Civil 3d drawings
- Keynote text file
- Shared parameter files
- Families
- Title blocks
- Progress pdfs

Coordination

Trade Partners shall be prepared to accommodate coordination meetings to resolve model conflicts and sign-off on a "Composite Coordination Model." Trade models are expected to be the source content for Shop Drawings submitted to the Design Team, "For Record Only." Trade Partner shall incorporate Design Team comments and install (as modeled/fabricated) with Mortenson McCarthy JV directive first. Deviations within normal construction tolerances will be adjusted per traditional field coordination practices. The models submitted by the Trade Partner for overall coordination are required to be checked and coordinated with structure, architecture, metal stud framing, and the trade partner's own work prior to posting. At a minimum, the model shall be pre-coordinated by the Trade Partner with knowledge of major, outstanding issues. Smaller issues should be identified and resolved by Trade Partners outside of coordination meetings. Each Trade Partner is responsible for reviewing the Composite Model to ensure "reserved" spaces.

Coordinated submittal data is to be posted per the Coordination Schedule (revised as needed). Multiple areas are being worked on in each week; each area will be coordinated per the phase which is current that week. Work ahead as time permits (in conjunction with other trades).
"Attachment 04 - Sign-Off Process" will be used for record sign-off deliverables. This attachment will also have a separate form for coordination post Addendums, Change Orders and RFIs. This form may be revised to support electronic signatures. Occasionally, work cannot be fully coordinated because a follow-on trade is not on board yet, or an RFI issue remains unresolved, etc. Trade Partner shall be prepared to coordinate to best known conditions, and follow-up later when information is available, or at the direction of Mortenson McCarthy JV to meet the coordination and/or construction schedule. This may include rerouting systems per field conditions that could not be foreseen. If sign-off is reached in this type of instance exclusions for portions of system that cannot be fully coordinated are to be noted on "Exclusions Sheet" section of the Sign-off Sheet.

When resolving an issue by way of moving portion(s) of a system, the Priority of Systems hierarchy included in **"Attachment 06 - Priority of Systems"** is to serve a general "rule of thumb" and to the best ability of the Trade Partners' roles, the issue is to be resolved between parties involved in the clash groupings through collocation.

4D Simulation Project Approach

The 4D modeling program will implement model information to assist in the linking and management of sequenced visualization. Among the benefits for using 4D modeling includes: schedule conformance / validation, effective Site Utilization Planning and Material Tracking (where reasonable). Synchro files and video file exports produced by Mortenson McCarthy JV will be made available to the entire project team and may be used by the owner to communicate with stakeholders. This process is outlined in **"Attachment 08 - 4D Simulation Project Approach."**

Model elements (based on general scope descriptions) incorporated, and the author (trade or Design Builder models) from which this sequence/schedule information and coding would be derived from are noted in **"Attachment 08 - 4D Simulation Project Approach."** Trade Partners will need these elements to have an attribute that aligns with the CPM schedule's "Task ID" for the respective work in place. Instructions for creating this attribute for each model element or grouping is noted for Sketchup and Revit files in the attachment. If the creation of this "Task ID" attribute is a limitation of the model's authoring software (i.e., Tekla) Trade Partners will need to provide sequenced based, independent model exports in one of the following formats in order to achieve the 4D simulation: either; *.dwg; *.dxf; *.fbx; *.dwf; *.dwfx; *.skp.

To be noted again for clarity, Trade Partners will not need to participate in any activity linking or creation of the 4D simulations beyond tagging model elements with Task IDs or exporting sequenced based independent models.

Design Information Exchange

The Design Team is sending all the Revit design models to MMC in the form of a link to download as a ZIP folder, originating from HNTB's BIM 360 Team collaboration site. MMC is responsible for downloading, extracting and uploading to BOX as outlined within **"Attachment 01b - DA Box File Management."** Arup, as the Structural Engineer of Record, is uploading their weekly Tekla models directly to BOX and following the requirements noted in **"Attachment 01b - DA Box File Management."** Arup is also to maintain an identical Revit translation from Tekla throughout Design that gets communicated via the weekly published Revit models being provided to MMC by HNTB.

During the Design Assist process, Trade Partners are to make available all model information on MMC's "BOX" site for the Design Team's incorporation into the design deliverables. When at all possible, Design Team members and Trade Partners are to share model content in the native authoring software to avoid fragmented and/or missing geometry. This does not diminish the need for certain scopes to continue to develop and share Revit concurrently when another authoring tool is being leveraged.

Construction Information Exchange

All coordination files will be stored and exchanged between the entire project team through MMC's "Glue" project cloud site, including design authoring models. All parties involved are required to post each file to the designated folder as per the folder structure agreed upon in Kick-off Meetings. Example Folder Structure for the collaboration "Glue" site is noted in **"Attachment 03 - Meeting-Coordination Process."**

The formal design model delivery schedule, aligning with the Design Team's 2D document issuances, is noted in **"Attachment 05a - MEA LOD Specification."** The Design Team will update construction documents throughout the construction phase, i.e. ASI's, CCD's, and PR's. RFI's, etc. The Design Team will provide updated models after each issuance; however, Trade Partners will be required to update models and resolve issues as new information is provided. It is to be restated that 2D documents will always govern over the 3D models. Trade Partners are expected to keep their models and files current and post updates as needed to support the overall CPM schedule.

3D Design Team Coordination Process

This section defines 3D computer coordination (Spatial Coordination) as it relates to Architecture, Structure, Mechanical, Electrical, Plumbing, Fire Protection, Fire Alarm, and Special Systems during the design phase of the project. Spatial Coordination shall be defined as the coordination of 3D design files by the design teams. This process differs from Clash Detection in that some clashes may be allowable depending on the systems that are intersecting. Spatial Coordination is to be performed on major systems and design elements to a level of detail appropriate to the current phasing of the project. Beginning midway between the 30% and 60% deliverables, Design Consultants will be required to participate in formal Spatial Coordination efforts, and continue until the design is sufficiently coordinated between disciplines.

Design Consultants are required to collaborate with each other's trade through electronic means, email, telephone, and in person to resolve basic clashes outside of the weekly Coordination meetings. It is expected that the weekly Coordination meetings are held to address difficult areas that are not able to be coordinated between the multiple disciplines themselves. These meetings may be part of the BIM Coordination Meeting or separate. All disciplines are responsible to update and post the changes agreed upon at the meeting within one week after the coordination meeting.

3D Construction Coordination Process

For detail into the workflow and the 3D Coordination process, review in detail **"Attachment 03 - Meeting-Coordination Process"** and **"Attachment 07a - 3D Coordination Process Map." "Attachment 03 - Meeting-Coordination Process"** provides the project team's objectives, approach, milestones, and technical

rules for data creation and management as it relates to 3D Building Coordination during construction. **"Attachment 07a - 3D Coordination Process Map"** provides a general process overview map, project specific process maps and standards of work guidelines for collaboration.

Note: that the construction 3D coordination process is explicitly detailed in **"Exhibit J"** of the Trade Partner's Contract Manual. For further detail, beyond what is shown below, refer to **"Attachment 07a - 3D Coordination Process Map."**

3D Project Specific Process Maps

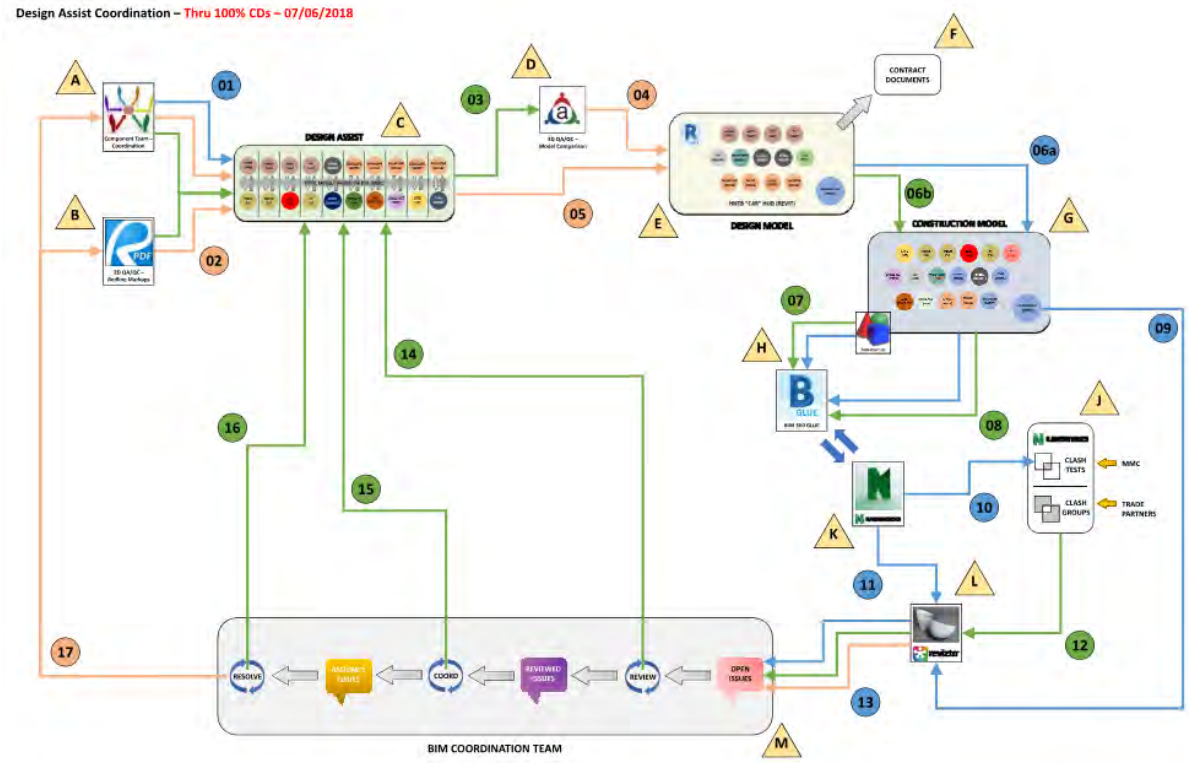

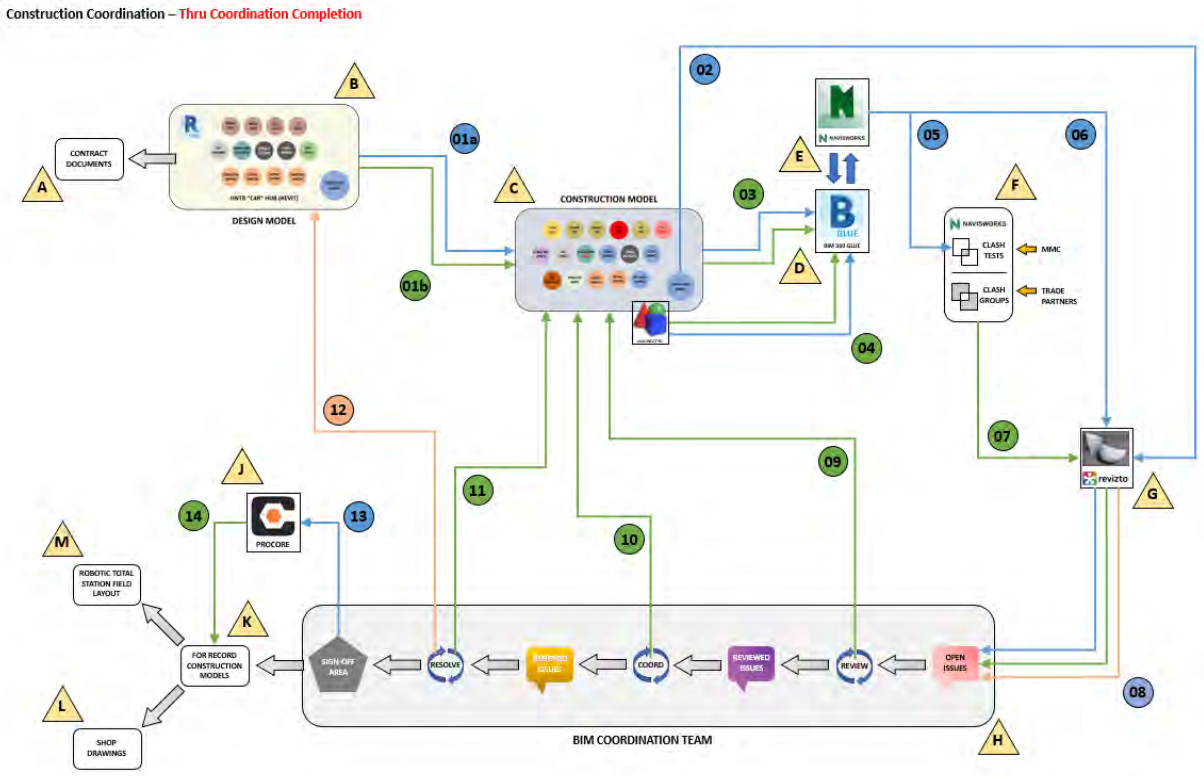

QUALITY CONTROL

Design Team's Overall Strategy for Quality Control During Design

Each participating office will be responsible for ensuring the integrity of their models/drawings as well as compliance with the established project BIM standards. All discipline models will be regularly reviewed against these guidelines for quality assurance an adherence to the BIM Project Execution Plan. Reviews will take place prior to the document QA/QC reviews that occur at major project milestones. Since model changes can affect the quality of the documentation, it is expected that model review comments will be picked up along with document review comments. Due to the collaborative nature of BIM, each party needs to rely on the content submitted for use on the project. Each discipline is responsible to review their own files in accordance to their internal QA/QC programs, and if requested, be prepared to provide proof that their work has been reviewed and is compliant with their own QA/QC programs.

Model Progress checks:

Models will be checked against Program standards and modeling practices on a biweekly basis (every other week). Reports may be distributed documenting findings.

Milestone Deliverable Review:

Models submitted with Project Milestone deliverables will be checked against Program standards and modeling practices. Detailed reports may be distributed documenting findings.

Construction Administration Checks:

Models used for Construction Administration activities will be checked upon issuance of significant bulletins against Program standards and modeling practices. Reports may be distributed documenting findings.

Record Model Checks:
Models submitted as Record Models will be checked against Program standards and modeling practices. Detailed reports may be distributed documenting findings.

Design Builder & Trade Partner's Overall Strategy for Quality Control During Construction

It is not critical that everyone use the same layer name standard, as long as the layers have descriptive names, and files are submitted to "Glue" with correct layers thawed/visible (Navisworks will not read frozen layers). Specific layer naming conventions will be provided and discussed during the 3D Coordination Kickoff Meeting.

There should not be random geometry placed off the site in the model. Work in progress should be kept on separate layer(s) that are frozen when submitted to "Glue." Notes, dimensions, and other 2D geometry or background files should be located on separate layers which are frozen when the model is submitted to "Glue."

Each Trade Partner's role as defined in this document is responsible for maintaining the quality and completeness of their models. Trade Partner Superintendents/Foremen and Project Managers are to be continually auditing the quality control of the model.

Quality Control Checks

Below is a table of different checks' definitions and the roles responsible for conducting each quality control check. Please note that the frequency of each "check" will be as required to support the project schedule, however a minimum is noted here.

CHECKS	DEFINITION	RESPONSIBLE PARTY	SOFTWARE PROGRAM(S)	FREQUENCY
VISUAL CHECK	Ensure there are no unintended model components and the design intent has been followed	ALL	Navisworks, Revit	Daily
INTERFERENCE CHECK	Detect problems in the model where two or more building components are clashing including soft and hard	Design Builder and Trade Partner	Navisworks	Daily
STANDARDS CHECK	CAD Standards per firm are acceptable. Use descriptive layer names with further definition provided in 3D Coordination kickoff meeting.	ALL	Various	Weekly
BASE MODEL INTEGRITY CHECKS	Design Builder will NOT duplicate design model data if it can be used as is. Design Builder will generate check dimensions that match paper Construction Documents.	ALL	Design Builder and Trade Partners	Daily

General Design Modeling Requirements

In general, the Design Team's scope is to create a BIM from which 2D documentation will be created (i.e. BIM and 2D documents will be congruent). The BIM will be used for coordination and documentation. The extent of the building model shall depict all areas being documented.

Refer to the Model Progression Specification (LOD Specification) attachments. Once a model is delivered as an Issued for Construction file, it may be repurposed by the construction team for their efforts, however reliance upon modeled content is limited to that described in this document.

Model Accuracy and Tolerances

The design BIM will use the imperial measurement system, with the default units being feet and inches. The Civil and Site Models are the exception and are to be in Decimal Feet, to a tolerance of .001 Ft. Models should include all appropriate dimensioning needed for the design intent, analysis, and construction tolerances consistent with the project phase. All wall types to be modeled using actual constructed dimensions, no nominal rounding and casework, is to be recorded in inches. Documents are to take precedence over the BIM.

Design Model(s) and Model Elements must be within 1/8" of theoretical dimensions. Tolerances for specific items and systems will be determined as necessary. Model tolerances are not to be construed as construction tolerances. Design Models should be modeled to include all appropriate dimensioning as needed for design intent, analysis, and construction. Level of development and included model elements are provided in the LOD Specification Attachment and the Model Element Stipulation section within this document.

All Trade Partners are to produce models to the accuracy and tolerances as defined in the Project specifications, the contract agreement between themselves and Mortenson McCarthy JV, or to the standards of their industry; whichever is more stringent. For the majority of instances, the model is to be exact within reason and construction tolerances are field relevant.

Coordinate System

All models must be in the correct location in 3D Space (x, y, and z coordinates and GIS World Coordinates). These coordinates have been set by the architect in conjunction with the Civil Engineer and will be distributed to all Design Team members and Trade Partners for their use. This includes correct floor elevation(s) (z coordinates) based on elevation above sea level.

To ensure that each model aligns properly for the master aggregate model, without modification or manipulation, all models shall be linked via "Auto – Origin to Origin) and in proper alignment of its "Shared Coordinates System" with "State Plane Coordinates." All Revit models, both Design and Trade Partners, are to have identical "Internal Coordinates" settings in addition to identical "Shared Coordinates" with "True Rotation" incorporated. This will ensure the ability for coordinating in alignment with both the 2D Contract Documents (Internal) and Civil State Plane Coordinates. (Shared)

Internal Origin vs Survey Point

The Project Base Point, for exporting using "Internal," is located at the center of the playing field, within the stadium, on the 50-yard line at the Lower Mezzanine Level (Level 050 = 2,181 feet above sea-level) When exporting using the "Internal Coordinates" setting the resulting file will have an origin point of 0,0,0 with that point relative to the project as described above and a rotation that matches what is shown on the Design Team's 2D Contract Documents.

The project's Survey Point, for exporting using "Shared," is located 100375.2586' away from the Project Base Point in the "X" direction and 99499.1089' away from the Project Base Point in the "Y" direction. At the Lower Mezzanine Level (050) the Project Base Point is documented as 0'-0" in elevation. The Lower Mezzanine Level using "Shared" export setting will change the Lower Mezzanine Level to its sea-level equivalent of 2,181'-0" in the "Z" axis. When exporting using the "Shared Coordinates" setting the resulting file will have the Project Base Point (center of field) relocated 99499.1089' North, 100375.2586' East, and 2,181' in elevation. Exporting using the "Shared" setting will also export with Revit's "True North" assignment. Angle from True North to Project North is 65° West of North.
Note: All current and future Revit models are to match what is setup within HNTB's Architectural Master Model, named "65787_NLVS_ARCH_MA_HNTB_A17." As shown below, when exporting using "Internal" the units should be set to "Inches" and when exporting as "Shared" the units should be set to "Feet."

Survey Point:
The survey point selected on the project site for use in all BIM models is:
Reference Point:
Northing: 0' - 0" (0.0000')
Easting: 0' - 0" (0.0000')
Elevation: 0' - 0" (0.0000')

Project Base Point:
The Project Base Point (PBP) for this project is the center of the playing field, in the event position, on the 50-yard line at the Lower Mezzanine Level (Level 050).
Reference Point:

Northing: 99499' - 1 79/256" (99499.1089')
Easting: 100375' - 3 13/128" (100375.2586')
Elevation: 2181' - 0" (2181.0000')
Angle to True North: 295°

Project North:

Angle from True North to Project North is 65° West of North.

Grids:

The structural grid will be defined by the architectural design model(s) with input from other disciplines. All other disciplines must copy/monitor the grids from the architectural design model(s) necessary for their scope of work. Upon finalization of the grid placement, control of the grid layout will be transferred to the structural design model(s).

Building Levels

LEVEL NAME	ELEVATION
LEVEL 000	-20′ – 0″ (2161′ – 0″)
LEVEL 050	0′ – 0″ (2181′ – 0″)
LEVEL 100	16′ – 0″ (2197′ – 0″)
LEVEL 150	32′ – 0″ (2213′ – 0″)
LEVEL 200	52′ – 0″ (2233′ – 0″)
LEVEL 250	70′ – 0″ (2251′ – 0″)
LEVEL 300	88′ – 0″ (2269′ – 0″)
LEVEL 350	100′ – 0″ (2281′ – 0″)
LEVEL 400	136′ – 7″ (2317′ – 7″)
LEVEL 450	146′ – 0″ (2327′ – 0″)
LEVEL 500	157′ – 0″ (2338′ – 0″)
LEVEL 600	206′ – 8″ (2387′ – 8″)

Stipulations for Design Model Elements

The level of detail defined in each section below is the minimum level of detail required in the model. Greater detail than the minimum should be incorporated in the model only when necessary to convey design intent.

Any further model development or scope deemed necessary and not previously defined will be addressed as they are identified. The BIM Team will determine the effect on the model(s) and scope, and propose the appropriate response to accommodate the noted Model development and/or coordination.

Architectural:

- All exterior walls, doors, windows, steps, railings and roofs will be modeled.
- All interior walls, including non-rated walls separating rooms, will be modeled. Studs will not be modeled.
- Risers and sloped floors will be modeled.
- Bollards and protective railing will be modeled.
- Interior doors and windows will be modeled to the extent that the walls that they are associated with are included in the model.
- All interior ceilings, soffits, stairs, and ornamental railings will be modeled.
- Walls, ceilings, and soffits will be modeled as the overall thickness including elevation changes and termination points. Overall thickness to be determined by their actual total composite assemblies.
- Doors, window leaves, and frames will be modeled. Door and window hardware will not be modeled.
- The overall extent of stairs and loading docks will be modeled including railings; intermediate railing members do not have to be modeled.
- Light fixtures will be modeled to the overall height, width, depth and access through the interstitial space.
- Elevator shaft clear space will be modeled to the worst case clear width, depth and height only from preferred possible vendors; elevator cabs, equipment, etc. will not be modeled. Nominal elevator cab size and overrun shall be modeled, including hoist beam.
- Escalators and moving sidewalks shall be modeled to the worst case clear width, depth and height only from preferred possible vendors
- All Way Finding, Room Identification, and Code required signage shall be modeled.
- Fixed furnishings including systems furniture will be modeled. Equipment will be modeled. Casework, including upper and lower cabinets will be modeled. Carpet, paint, wall coverings, tile, wall base and

trim carpentry are not required to be modeled. Non-fixed furniture can be modeled as 2D graphics within a 3D component family.

Structural:

- All cast-in-place concrete, including all penetrations and openings identified in the construction documents, will be modeled. Slab camber will not be modeled. Chamfers at corners will not be modeled.
- Edges of all slabs and penetrations of structural systems will be accurately located in the model.
- All primary and secondary structural steel members will be modeled, including standard steel member sizes, gusset plates, braces, kickers and major/primary equipment supports. Reinforcing steel and embeds will not be modeled.
- Metal, wood and concrete decks will be modeled as the overall thickness of the slab; ribs in metal decks will not be modeled. Bolts, clip angles, etc. will not be modeled.
- Miscellaneous metals such as elevator hoist beams, rails and intermediate rail support steel for the elevator, structural support for signage and ceiling hung elements will be modeled.
- Identify reinforcing or penetration "no-fly" zones as applicable.

HVAC:

- All ducts and air handling equipment will be modeled. Ducts will be modeled to the outside face dimension of the flanges/insulation. Duct joints and hangers do not have to be modeled.
- Equipment will be modeled to its worst-case overall height, width and depth. Equipment access zones will be modeled as solids.
- Any piping associated with the mechanical equipment will be modeled. Pipes will be modeled to the outside diameter of the pipe or pipe insulation (whichever is greater). Fittings and connections will not be modeled.
- Mechanical Piping 2" or greater or smaller pipe if in ganged runs will be modeled.
- Any electrical associated with HVAC will be modeled per the electrical modeling requirements as outlined in Electrical, below.
- The intent of this model is to show the ductwork and piping, etc. in as true representation of the actual condition at construction completion. Specific dimensional location of ductwork and piping may not be included in the construction documents. To the extent that location can be determined from the construction documents, the model will reflect that location.
- Identify "no-fly zones" with solid placeholder clearance object for: access issues, code issues, and/or constructability.

Electrical:

- Conduits or smaller conduits in ganged runs greater than 2" will be modeled as required to communicate design intent.
- Ganged runs may be modeled as a solid representing the overall cross section.
- Cable tray, access zones, and equipment to be included in the model.
- Light fixture locations and space requirements to be included in the model.
- Consider modeling switches and outlets where coordination with architectural FFE or interior elevations is a concern.
- Any access zones requirements will be modeled as solids.
- "No-fly zones" above electrical panels shall be modeled as solids

Plumbing:

- Piping 2" or greater or smaller pipe if in ganged runs will be modeled.
- Pipe size must be accurately modeled, but pipe curves are not required to be exact.
- Plumbing piping and gas piping, including specialty gas and equipment will be modeled. Pipes will be modeled to the outside diameter of the pipe or the pipe insulation, whichever is greater.
- Pipe slope will be incorporated in the model. Fittings and connections will not be modeled.
- All plumbing equipment will be modeled to its overall height, width and depth.

- All valves and clean outs will be modeled along with all access to valves/cleanouts.
- Any access zone requirements will be modeled as solids.

Fire Protection (Sprinkler & Fire Alarm):

- All major components of the fire protection system will be modeled. This includes all piping, valves, fire pump, and sprinkler heads.
- Any access zone requirements will be modeled as solids.
- "No-fly zones" above control panels shall be modeled as solids.
- Fire alarm modeling requirements shall follow the requirements of the Electrical Section.

Civil / Site:

- Existing and new topography should be modeled, with reference to 1' contour lines.
- All roadways, bridges, curbs, shored walls/structures shall be modeled.
- All light poles, and roadway or other signage that requires power, data or foundations shall be modeled.
- All built in place, fixed in place, hardscape, non-vegetative elements shall be modeled.
- All piping, structures, and underground conduit banks (if applicable) will be modeled. Pipes will be modeled to the outside diameter of the pipe. Pipe slope will be incorporated in the model. Model all proposed installations including but not limited too; piping, joints, sump basins, storage tanks, and free draining material wraps or bedding around piping.
- All survey points should be spatially located and identified, based on agreed Coordinate System detailed above.

Security and IT Systems:

- Electrical/wiring associated with Security and IT Systems are to be modeled per the electrical modeling requirements
- Security devices, cameras, card readers, and sensors, etc. are to be modeled to the overall maximum size of each device and in locations representing installation points in 3D space.
- Equipment and server racks are to be modeled as solid objects to their overall height, width, and depth.
- "No-fly zones" above control panels shall be modeled as solids.

Design Team's Model Structure and Standards:

This section will describe how the individual models are structured or divided, naming conventions, reference to official standards, and include an official list as an attachment.
Model Structure

Each building or project within the program will be comprised of separate (BIM) models. Primary separation of modeled elements will be by discipline, i.e. Architectural, Structural, Mechanical, Electrical, Plumbing and Fire Protection models. Further separation as needed will be determined as the model progresses. Upon further separation (either by Workset or Linked Model), the BIM Lead for each discipline is to alert other leads to verify updates are integrated.

Design Team's File Naming Structure:

<project number>_<project short name>_<sub building abbreviation if applicable>_<firm abbreviation>_<discipline><Revit version>.rvt

Ex. 00000_NLVS_Garage_HNTB_A17.rvt

Adding the firm abbreviation is two-fold: To distinguish between models of the same discipline authored by different firms and to easily understand who to contact regarding a specific model.

Phase Names:

Use of Revit Phases will be managed by the AOR and based on the design packages as they are established. All phasing within the Revit architectural files must be coordinated with all disciplines and Phases/Phase Filters are to be exactly the same from one model to the next.

Views:
Revit views are to be categorized as one of the following:

Working
All modeling must be done on views clearly indicated as "Working" to ensure that all information appears as required on the Linked and Sheet Views.

Coordination
Each model must contain views specifically set up for export to Navisworks / Glue in which only the model author's scope is visible, e.g. no linked content. These views may be limited to specific geographic areas, by floor, and/or an entire building depending on the specific project. Geographic specifics of these views must be coordinated for each discipline participation in the project, i.e. they should all match.

Linked
As required, each discipline should set up views to be linked into other discipline's work for accurate graphic representation of backgrounds. These views are to be individually coordinated amongst consultants so that only pertinent information is visible as reference.

Sheet
Refer to Level naming standards for more information on associated levels and their view names. All View Names are to appear in all caps.

Sheets

All drawings shall be on 36"x48" sheets unless specifically approved otherwise in writing by the Owner. The first sheet in each drawing set shall be the Owner's standard cover sheet which will include the project name and address, the project number, the Designer's and Sub-consultant's name, addresses and phone numbers and other project information. The cover sheet background and title block will be included in the Revit Template file.

Shared Parameters

A shared parameters file is included as part of the standards defined by this project. It is the understanding that this file, NLVS Shared Parameters.txt, will provide all required shared parameters, and any additional shared parameters required will be distributed to the team. This file will reside on the BIM 360 Team Hub and will be managed by the Project BIM Manager. Any additions or modifications to Shared Parameters much be approved by the Project BIM Manager and incorporated into the global Shared Parameters File.
Worksets

Required Worksets

Workset1
Default Revit workset. Do not rename this workset or use for model geometry.

Shared Levels and Grids
All Matchlines, Levels and Grids are to reside on this workset.

Scope Boxes_Off
(Not visible in all views) All Scope Boxes are to reside on this workset. This workset shall have "Visible in all views" unchecked.

Linked RVT_[DISCIPLINE]
All linked Revit models are to reside on discipline specific worksets.
(ex. Linked RVT_Arch, Linked RVT_Plumb, etc.)

Additional Worksets

[WORKSETNAME]_Off
The _Off naming suffix shall be used for any workset with "Visible in all views" unchecked.
(ex. Entourage_Off, Site_Off, etc.)

Shared [CATEGORY]
Any geometry that is duplicated across more than one model must reside on a workset with the Shared prefix. This allows teams to globally unload this workset via Manage Links>Manage Worksets to avoid the display of duplicated geometry.
(ex. Shared Slabs, Shared Plumb, Shared Foundations, etc.)

Linked CAD_Off
(Not visible in all views) All linked CAD files are to reside on this workset. If additional Linked CAD worksets are needed, Linked CAD should be followed by a descriptor. All linked CAD worksets shall have "Visible in all views" unchecked.
(ex. Linked CAD Civil_Off, Linked CAD Skp_Off)

Floor Finishes_Off
(Not visible in all views) All interiors floor finishes are to reside on this workset. This workset shall have "Visible in all views" unchecked.

Design Team CAD Deliverables

In addition to PDF deliverables, all deliverables produced in Autocad shall include the native Autocad files, in DWG format, for each sheet being issued. All CAD deliverables shall fulfill the following requirements:

- All DWG deliverables shall follow the National CAD Standards layering convention; the default export routine supplied in Autodesk Revit.
- All external reference files (X-Ref) shall be attached as overlays and without device or directory specifications (i.e. no path). Any unused x-refs are to be detached prior to issuing.
- Include all files, both graphic and text, required for the project (e.g. plotting tables, user command files, etc.). Provide an eTransmit of all CAD drawings for the project.
- Make sure all support files are in the same directory and that any references to those files do not include device or directory specifications.
- All CAD deliverables exported from Revit shall have all External Reference Files (x-refs) bound. To export DWG files from Revit without X-refs, the "Export views on sheets and links as external references" within the Save To dialog box should remain unchecked

DEFINITIONS

AOR	Architect (AORs = Plural)
Construction Model	The equivalent of shop drawings and other information useful to construction. Consists of data imported from a design model and/or from a fabrication model. Author may manipulate the data to facilitate constructability.
Design Model	A model that has reached the stage of completion that would customarily be expressed by an architect or engineer in two-dimension construction documents. (Revit Model)
Fabrication Model or Trade Contractor Model	3D Model provided by a sub consultant containing the 3D geometry used to construct actual building components.
EOR	Engineer of Record (EORs = Plural)
Federated Model	Distinct component models linked together in such a manner that the linked data sources do not lose their identity or integrity by being so linked. Also known as a combined model. An example of such model would be a Navisworks model linking in all relevant design, construction, and fabrication models. Content may be shifted, but not added. Federated models are used in clash detection and trade coordination. There may be multiple iterations of the federated model, one that is created during design, and one that is created during construction. Each relies on the content provided by other disciplines or contractors at a point in time on the design/construction timeline.
Record Model	A Record Model is a Design Model that includes specific documented modifications to the design that occurred during construction of the project.
GC/CM	General Contractor/Construction Manager
IFC	'Industry Foundation Classes' file format. A platform neutral file format that allows for the exchange of model data across varied BIM management software.
LDA	Lead Design Architect
MMCJV	Mortenson/McCarthy JV
Model Element Author	The individual(s) who originated the BIM content. For example, if the design firm 'A' initiates the BIM model and uses it throughout the design process, firm 'A' is the Model Element Author

ATTACHMENTS

List

Attachment 00 - Trade Partner Exhibit J (PDF)

Attachment 01 - Box Sync File Management (Word)

Attachment 02 - BIM File Name Schema (Excel)

Attachment 03 - Meeting-Coordination Process (Word)

Attachment 04 - Sign-Off Process (Word)

Attachment 05a - MEA LOD Specification (Excel)

Attachment 05b - 2017 BIM Forum LOD Specifications (PDF)

Attachment 06 - Priority of Systems (Word)

Attachment 07a - 3D Coordination Process Map (Excel)

Attachment 07b - Phase Planning Process Map (Excel)

Attachment 07c - Record Modeling Process Map (Excel)

Attachments 07d - 3D Control Process Map

Attachment 08 - 4D Simulation Project Approach

Attachment 09 - HNTB production standards

EXHIBIT N

Specific Arbitration Procedures

1. All Arbitration pleadings shall conform to Nevada Rules of Civil Procedure; RCCOs and respective defenses thereto shall be consistent with Notice of RCCO and Notice of Denial requirements contained in this Agreement.

2. An Answer and/or Counterclaim shall be due within twenty (20) days after receipt of a Demand for Arbitration. A response to a Counterclaim shall be due within ten (10) days after receipt of a Counterclaim.

3. Both StadCo and the Design-Builder consent to the joinder or consolidation of any RRCOs and Disputes that arise out of or are related the factual or legal issues in any Arbitration, including but not limited to any RRCOs or Disputes involving StadCo's Representative, the Architect, the Design Consultant, any Subcontractor, or any Vendor. The Arbitrator assigned to the Arbitration into which joinder or consolidation is sought shall have jurisdiction to determine, on an expedited basis and in response to a motion by any Party, whether consolidation or joinder shall be permitted. Design-Builder shall ensure that all Subcontracts and Vendor agreements relating to the Work shall provide for the joinder or consolidation of all parties and claims in any dispute resolution proceedings initiated pursuant to **Article 16** of this Agreement.

4. Early Arbitration Disclosures and Preliminary Hearing:

    a. Within thirty (30) days after service of the last responsive pleading (either the Answer or the response to Counterclaim), the Parties shall hold an Early Case Conference in a manner that fully complies at a minimum with applicable Nevada Rules of Civil Procedure. At the Early Case Conference, the Parties shall:

        i. produce all Project files and records or other documents that relate to a Party's claims or defenses in paper or electronic format;

        ii. produce all subpoenas for third-party document productions; and

        iii. agree upon an electronic discovery protocol, which shall identify search terms and parameters for the production of emails and other electronically stored information.

    b. Within fifteen (15) days after appointment of an Arbitrator or Arbitration Panel, the Arbitrator(s) shall hold a Preliminary Conference pursuant to Rule 16 of the JAMS Engineering and Construction Arbitration Rules and Procedures.

5. All disputes relating to discovery which cannot immediately be resolved by the Parties shall be submitted to the Arbitrator, whose decision on such matters shall be final and binding upon the Parties. The following limitations and timeframes shall apply to discovery:

    a. All electronically stored information (**"ESI"**) shall be produced within forty-five (45) days after the Early Case Conference.

    b. Documents requested shall be produced or made available and requests for admissions admitted or denied, as the case may be, within twenty-one (21) days after service of the requests. All fact discovery shall be completed within one hundred-twenty (120) days after the Early Case Conference is held and shall be completed no later than thirty (30) days before the first hearing date established by the Arbitrator.

c. The Arbitrator may adjourn the start of the arbitration and extend discovery: (i) upon the motion of any Party to the proceedings and a good cause showing; or (ii) in the event of a Party's failure or refusal to provide discovery as required by this provision and the Nevada Rules of Civil Procedure. No Party shall be entitled to "priority" in conducting discovery.

d. The Parties shall exchange preliminary witness lists identifying all fact witnesses they anticipate calling at the arbitration hearings within twenty-one (21) days prior to the Early Case Conference. As to each lay witness identified, the Parties shall provide a short summary of the expected testimony of the witness. Within this same time period, the claimant also shall identify any expert witness that it may or will call as a witness at the hearings; the Parties shall comply with applicable Nevada Rules of Civil Procedure and Title 4, Witnesses and Evidence, of the NRS pertaining to experts. Within fourteen (14) days following receipt of the names of claimant's expert(s), the respondent shall furnish the claimant with a list of its expert(s). The Arbitrator shall set the date for the filing of final witness lists when the hearing dates are scheduled.

e. All expert discovery shall be completed within one hundred-eighty (180) days after the Early Case Conference is held.

f. Fact discovery shall be limited to thirty (30) interrogatories, and thirty (30) request for admissions.

g. The Parties shall agree to conduct site inspections and destructive testing on the Project in the least intrusive manner to the Project.

h. Any destructive testing shall be through a jointly administered testing protocol.

i. Upon fourteen (14) days' prior written notice, depositions may be taken by stipulation of the Parties or with the approval of the Arbitrator based on a showing of good cause therefor. Each Party to the arbitration is limited to thirty-five (35) hours of noticed deposition time. At least ten (10) days prior to the deposition of any expert witness, the Party proposing to call such witness shall deliver to the other Party(ies) a full written report concerning the matters about which the expert is expected to testify. Each expert report shall: (i) list all information, documents, or other materials that the expert relied upon in formulating his opinions and conclusions set forth in the report; and (ii) list all information, documents, or other materials that the expert requested, but was not available at the time the report was prepared, that might influence the conclusions or opinions of the expert as set forth in the report. Expert depositions shall be limited to five (5) hours of questioning of each expert by each Party.

6. Arbitration Hearing:

a. The Arbitrator(s) shall commence the Arbitration Hearing within twelve (12) months of the date of the initial Demand for Arbitration.

b. A Party's insurance carrier or surety shall not be considered a separate party for the purpose of calculating the presentation time limit and not entitled to a separate allocation of time in addition that of the Design-Builder or StadCo.

c. The Arbitration hearing shall be reported by a Certified Court Reporter, whose fees shall be borne equally by the Parties. The court reporter fees may be awarded as a cost to the prevailing Party.

d. At the conclusion of the hearing, the Arbitrator(s) shall declare the closure of evidence. Once the evidence has closed, no Party may present any further evidence, including as part of post-hearing briefs.

7. The Arbitrator(s) shall render a decision within thirty (30) days after the close of evidence, unless the Arbitrator(s) requests closing briefs. If closing briefs are requested, the Arbitrator(s) shall render a decision within ninety (90) days after the close of evidence.

   a. The decision of the Arbitrator(s) shall be in the form of a reasoned award (**"Initial Award"**) that shall dispose of all of the controversies, disputes and claims of the Parties that are the subject of the arbitration. The Initial Award shall be final and binding on the Parties and not subject to appeal unless otherwise provided by applicable law.

   b. The Initial Award shall be interim, and the prevailing Party shall have thirty (30) days from the date of service of the Initial Award to submit an application for legal fees and costs.

   c. The Arbitrator(s) shall set briefing on legal fees and costs, and shall render a final award (**"Arbitration Award"**) with any legal fees and costs included in the award within sixty (60) days after being served with an application for legal fees.

   d. If no application for legal fees is submitted, the Initial Award shall be memorialized in a Final Award by the Arbitrator(s) on the 31st day after serving the Initial Award.

   e. The prevailing Party in any Arbitration shall be entitled to enforce the Arbitration Award as a judgment in any court of competent jurisdiction and shall be authorized to disclose the Arbitration Award to the court without violating the General Provisions Applying to **Articles 15** and **16** of this Agreement.

8. The Arbitrator shall have no authority to make any ruling, finding or award that does not conform to the terms and conditions of the Agreement. The Arbitrator shall be empowered to enter equitable as well as legal relief as provided by this Agreement and to provide for temporary and/or provisional remedies, if necessary.

EXHIBIT O-1

Conditional Waiver and Release upon Progress Payment

Property Name: _____

Property Location: _____

Undersigned's Customer: _____

Invoice/Payment Application Number: _____

Payment Amount: _____

Upon receipt by the undersigned of a check in the above-referenced Payment Amount payable to the undersigned, and when the check has been properly endorsed and has been paid by the bank on which it is drawn, this document becomes effective to release and the undersigned shall be deemed to waive any notice of lien, any private bond right, any claim for payment and any rights under any similar ordinance, rule or statute related to payment rights that the undersigned has on the above-described Property to the following extent:

This release covers a progress payment for the work, materials or equipment furnished by the undersigned to the Property or to the Undersigned's Customer which are the subject of the Invoice or Payment Application, but only to the extent of the Payment Amount or such portion of the Payment Amount as the undersigned is actually paid, and does not cover any retention withheld, any items, modifications or changes pending approval, disputed items and claims, or items furnished that are not paid. Before any recipient of this document relies on it, he should verify evidence of payment to the undersigned. The undersigned warrants that he either has already paid or will use the money he receives from this progress payment promptly to pay in full all his laborers, subcontractors, materialmen and suppliers for all work, materials or equipment that are the subject of this waiver and release.

Dated: _____

(Company Name)

By:_____

Its:_____

Exhibit O-2

Unconditional Waiver and Release upon Progress Payment

Property Name: _____

Property Location: _____

Undersigned's Customer: _____

Invoice/Payment Application Number: _____

Payment Amount: _____

The undersigned has been paid and has received a progress payment in the above-referenced Payment Amount for all work, materials and equipment the undersigned furnished to his Customer for the above-described Property and does hereby waive and release any notice of lien, any private bond right, any claim for payment and any rights under any similar ordinance, rule or statute related to payment rights that the undersigned has on the above-described Property to the following extent:

This release covers a progress payment for the work, materials and equipment furnished by the undersigned to the Property or to the Undersigned's Customer which are the subject of the Invoice or Payment Application, but only to the extent of the Payment Amount or such portion of the Payment Amount as the undersigned is actually paid, and does not cover any retention withheld, any items, modifications or changes pending approval, disputed items and claims, or items furnished that are not paid. The undersigned warrants that he either has already paid or will use the money he receives from this progress payment promptly to pay in full all his laborers, subcontractors, materialmen and suppliers for all work, materials or equipment that are the subject of this waiver and release.

Dated: _____

(Company Name)

By:_____

Its:_____

Exhibit O-3

Conditional Waiver and Release upon Final Payment

Property Name: _____

Property Location: _____

Undersigned's Customer: _____

Invoice/Payment Application Number: _____

Payment Amount: _____

Upon receipt by the undersigned of a check in the above-referenced Payment Amount payable to the undersigned, and when the check has been properly endorsed and has been paid by the bank on which it is drawn, this document becomes effective to release and the undersigned shall be deemed to waive any notice of lien, any private bond right, any claim for payment and any rights under any similar ordinance, rule or statute related to payment rights that the undersigned has on the above-described Property to the following extent:

This release covers the final payment to the undersigned for all work, materials or equipment furnished by the undersigned to the Property or to the Undersigned's Customer and does not cover payment for Disputed Claims, if any. Before any recipient of this document relies on it, he should verify evidence of payment to the undersigned. The undersigned warrants that he either has already paid or will use the money he receives from the final payment promptly to pay in full all his laborers, subcontractors, materialmen and suppliers for all work, materials or equipment that are the subject of this waiver and release.

Dated: _____

(Company Name)

By:_____

Its:_____

Exhibit O-4

Unconditional Waiver and Release upon Final Payment

Property Name: _____

Property Location: _____

Undersigned's Customer: _____

Invoice/Payment Application Number: _____

Payment Amount: _____

Payment Period:_____

Amount of Disputed Claims:_____

The undersigned has been paid in full for all work, materials and equipment furnished to his Customer for the above-described Property and does hereby waive and release any notice of lien, any private bond right, any claim for payment and any rights under any similar ordinance, rule or statute related to payment rights that the undersigned has on the above-described Property, except for the payment of Disputed Claims, if any, noted above. The undersigned warrants that he either has already paid or will use the money he receives from this final payment promptly to pay in full all his laborers, subcontractors, materialmen and suppliers for all work, materials and equipment that are the subject of this waiver and release.

Dated: _____

(Company Name)

By:_____

Its:_____

Notice: This document waives rights unconditionally and states that you have been paid for giving up those rights. This document is enforceable against you if you sign it, even if you have not been paid. If you have not been paid, use a conditional release form.

EXHIBIT P

Travel Policy

Business Travel Policy

Examples of Business Travel Expenses

The following types of expenses fall within the scope of the Business Travel Policy.

Travel and Entertainment Expenses - Examples		
Airfare	Meals	Personal Auto Mileage
Lodging	Team Member Relations	Gifts & Awards
Car Rental	Event Tickets	Advertising
Taxis or Limousines	Outside Services	Valet Services
Parking Fees & Tolls	Proposals and Presentations	Misc. Travel Expenses
Construction Permits	Trade Shows	Other Entertainment Expense
Train or Public Transport	Office Supplies	Licensing Expense
Gasoline for Rental Car	Postage & Freight	Seminar Expense
Laundry while away > 5 days	Dues or Subscriptions	Phone/Internet Charges
Tips & Gratuities	Trade Publications	

Detailed Travel and Entertainment Policies

Domestic Airline Travel

Travel by air should comply with the following policies:

- Fourteen day advance purchase is required, except in circumstances where the travel could not have been anticipated. Traveling team members are responsible for planning travel as far in advance as possible to assure sufficient time for the approval process, and to assure availability of advance-purchase pricing.
- All flight arrangements will be coach, unless an upgrade is available at no additional cost over the lowest available coach fare.
- Traveler or Travel Agent will select the specific airline and flights based on the traveler's arrival and departure requirements utilizing the most cost-efficient options. Travelers may select among equally priced options, if they exist. A flight selection is considered acceptable if the flight arrives up to three hours prior to the target arrival time, and has no more than one layover.
- For flights between any two locations, if connecting flights are the lowest cost option, they will be selected as long as departure and arrival requirements can be met. Alternatively, a direct flight may be selected if the cost of the one-way flight-segment does not exceed the cost of the connecting flight by more than $100.

International Travel

For international flights that require flight times of seven hours or more, not including layovers or connection times, the company will allow the purchase of upgradable tickets up to full coach fare to allow the traveler to upgrade by paying an upgrade fee or by using frequent flyer miles. Payment of

upgrade fees or use of frequent flyer miles is the responsibility of the traveler.
Fees related to currency conversion are paid and/ or reimbursed for team members traveling internationally.

Travel Clubs

Memberships to an airline club (e.g. Delta Sky Club) will not be reimbursed by the company. Team members may join loyalty programs that are free to the traveler (e.g. Hilton Honors).

Automobile Usage

Personal Automobile Use

Team members using personal cars on company business will be reimbursed for actual miles driven in excess of normal commute, at a rate of not more than the maximum rate determined by the governing tax authority.

- Team members will not be reimbursed for any repairs to their personal car even if these costs result from business travel.
- Team members must have a valid driver's license.

Automobile Rental

Auto rental should be used when the total cost including parking and fuel is less than that of other available transportation, such as a taxi, airport limousine, airport shuttle, public transportation, or Uber or Lyft.

- Arrangements for auto rental must be booked with preferred vendor(s) selected by the company. If no preferred vendor, lowest cost option.
- Auto rentals should be standard sedan automobiles unless business circumstances warrant a different type of vehicle. If the rental expense is deemed to be lavish, extravagant, or excessively costly, reimbursement will be limited to the standard rate for a standard vehicle.
- Team members should decline personal accident insurance and the collision damage waiver for auto rentals. Mortenson or McCarthy will pay the maximum liability for direct or accidental loss or damage to a vehicle rented in the U.S. (not paid by the team member's automobile insurance) as long as the team member complied with all terms and conditions of the rental agreement.
- Rented vehicles may be driven only by the team member who signed the rental agreement and any other team members included on the rental agreement as additional drivers.
- The team member must abide by all terms and conditions of the rental agreement. Additionally, the team member is not authorized to propel or tow any vehicle, trailer, or other object with the rented vehicle.
- The vehicle must be returned immediately upon conclusion of company business to avoid any unnecessary additional charges.
- Team members must not choose the "prepaid fuel" option on the rental agreement. When a rental car is used, make sure to fill the gas tank before returning the vehicle. Gasoline costs are considerably higher when purchased from the rental company.

Parking, Tolls, and Fines

- Applicable tolls and parking fees while traveling will be paid and/ or reimbursed.
- Traveling team members should make reasonable efforts to avail themselves of discount off-airport parking.

- Valet parking will be paid and/ or reimbursed when it is the best parking option from a combined logistics and cost standpoint.
- The team member is responsible for any fines in connection with parking and travel violations incurred while on company business. Such fines are not reimbursable by the company.
- Any toll charges incurred while traveling for business should be submitted as an out-of-pocket expense within Concur for the team member to be reimbursed.

Lodging

Hotel reservations should be booked with preferred vendor(s) selected by the company or locations where an established corporate rate exists.

- Travelers will be reimbursed for reasonable hotel room costs, including reasonable and customary gratuities to hotel staff. Travelers should stay in a standard room with single occupancy.
- Hotel reservations for business travel are guaranteed for late arrival. If travel plans change, the traveler is responsible for canceling hotel rooms. Contact the travel agent or the hotel directly in order to avoid cancellation or "no show" charges. Travelers should always record and retain the cancellation number in case of billing disputes.
- Discount or group-rate accommodations available in connection with a business meeting, industry association meeting or professional association meeting should be arranged for as provided by the event sponsor, and do not need to be made through the travel agent.

Meals

- Team member expenses are paid and/ or reimbursed for properly documented meals while traveling on company business more than 50 miles from the team member's assigned work location or overnight.
- Team member expenses are paid and/ or reimbursed for properly documented business meals attended by more than one person, including any mix of vendors, customers, or other Mortenson/McCarthy team members, at which business matters are discussed.
- Team member expenses are paid and/ or reimbursed for reasonable gratuities. Detailed supporting documentation, including an itemized receipt is required for reimbursement of meal expenses.

Phone Charges

Travelers should avoid using hotel room phones while traveling on business, due to excessive costs and surcharges. Instead, travelers should either phone from our local offices/ job sites or use their company-reimbursed mobile phone.

Non-Reimbursable Expenses

Team members will not be reimbursed for the following expenses, which are outside of company policy:

- Lodging expenses in excess of the rate for a standard room with single occupancy (e.g. extra cost for a suite);
- Cancellation or "no show" charges, unless the traveler a) contacted the travel agent or the hotel directly and b) kept a record of the cancellation number;
- Hotel phone charges for calls to the team member's home, if the team member has a company-provided mobile phone;
- Laundry or valet services, unless the trip exceeds five business days;

- Mini-bar or other in-room refreshments;
- Movies and video games (including in-flight fees, portable movie player or game rental fees, and hotel in-room programming or video game charges) (does not apply to in-flight wi-fi for business purposes);
- Fines resulting from infractions of laws or regulations.

In addition, team members will not be reimbursed for the following miscellaneous personal expenses indirectly related to travel:

- Baby-sitting
- Barbers, hairdressers, and shoe shines
- Expenses for travel companions/family members
- Kennel or boarding fees for pets
- Home care and maintenance (including lawn care and snow removal)
- Magazines or books
- Toiletry items

Expense Reimbursement Methods

Concur® is the company authorized tool for all non-craft and superintendent team members to electronically submit their travel and entertainment expenses and related receipts regardless of whether or not team members have been issued a corporate Travel & Entertainment credit card. Team members who have been issued a corporate Travel & Entertainment (T&E) credit card are expected to use the corporate card whenever possible for business travel and entertainment expenses to minimize the need to request reimbursement for out-of-pocket expenses.

Team member without Concur access and craftworkers should continue to request reimbursement for any travel and entertainment expenses via a paper Expense Reimbursement Report or applicable company policy.

As a general rule, team members should not incur out-of-pocket expenses to purchase small tools and consumables such as nails, drywall compound, fuels and lubricants, welding supplies, etc. used on a construction site. In situations that require that these purchases be made outside of the company's approved Procurement processes, a paper Expense Reimbursement Report, located in the Accounting Catalog within ServiceNow, must be submitted to request reimbursement.

As a best practice, a separate expense report should be created for each project or trip. This approach will prevent one customer from seeing expenses incurred for another customer's project when invoice back-up is provided with a customer billing.

In all cases, expense reports must be submitted within 30 days after the expenses were incurred.

Supporting Documentation

Supporting documentation for corporate credit card charges and out-of-pocket expenses must include:

- Date(s) of travel or date expense was incurred
- Location of the meal, activity, or trip
- Business purpose of the meal, activity, or trip
- Name and company affiliation of all attendees for whom expense was incurred

- Team members must provide receipts for all expenses in order to be reimbursed. All receipts need to be legible and complete and must include the signature line on credit card receipts. For incidental expenses not evidenced by a written receipt, such as hotel tips, best practice is to maintain a daily record of such expenses. The Concur® mobile application makes it easy for team members to make

an image of and attach receipts electronically, eliminating the need to retain paper copies. If a copy of the receipt is unavailable, the receipt affidavit function within Concur® can be used to substitute for the actual receipt. The receipt affidavit function should be used sparingly and only in cases when a receipt is unavailable.

- For each meal expense (including room service), team members must provide an itemized listing of all food and beverage served, on a cash register receipt or other third-party document. A simple receipt for the amount only is not considered adequate for this purpose. An attendee list is required if more than one person was present for the meal.
- Any team member submitting a paper Expense Reimbursement Report should tape all receipts smaller than half a standard sheet of paper to 8-1/2" x 11" sheets of paper, using as many sheets as necessary to allow all receipts to be legible. Each receipt should be taped firmly on blank areas of all four borders to facilitate high-speed scanning and ensure continuing legibility of receipts. Multiple receipts may be attached to one sheet of paper, as long as this does not impair the ability to read and understand the detail. Receipts should not be stapled directly to the expense report, nor to the supplemental sheets of paper.

EXHIBIT Q

Community Benefits Plan

COMMUNITY BENEFITS PLAN

I. BACKGROUND

This community benefits plan (this "Plan") has been developed by LV Stadium Events Company, LLC ("Developer") pursuant to §§ 29.5 and 31.5 of the Southern Nevada Tourism Improvements Act (the "Act") to ensure the greatest possible participation by all segments of the local community in the economic opportunities available in connection with the design, construction, and operation of the National Football League stadium being developed by Developer (collectively, the "Project").

II. COMMUNITY OVERSIGHT AND ACCOUNTABILITY

2.1 Benefits Oversight Committee. Pursuant to the Act, the Clark County Stadium Authority ("CCSA") shall, in consultation with Developer, create a benefits oversight committee (the "BOC"). The BOC shall meet at the call of the chair or as requested by the chair of the CCSA. The BOC shall post its meeting agendas and conduct its meetings in a manner consistent with the Nevada Open Meeting Law. The BOC shall not have an annual budget, shall not open or maintain any financial accounts, shall not take on any debt or otherwise encumber itself or the CCSA in anyway, and shall not enter into any contracts or other agreements obligating it or the CCSA.

2.2 Appointment of Members to the BOC; No Compensation. The BOC shall consist of seven members. The CCSA shall appoint one member to the BOC, with such member serving as the chair of the BOC. Developer shall appoint three members to the BOC. The Governor of Nevada, Nevada State Senate Majority Leader, and the Nevada State Assembly Speaker shall each appoint one member to the BOC. Each member of the BOC must have the education, experience, and skills necessary to effectively execute the duties and responsibilities of a member of the BOC. Consistent with the Act, members of the BOC are not entitled to receive any compensation for serving as a member of the BOC or as an officer or employee of the CCSA. The Local Chambers, as defined below, will have an opportunity to provide input to the appointing persons regarding the proposed members of the BOC.

2.3 Role and Responsibility of the Benefits Oversight Committee. The BOC shall oversee Developer's compliance with the terms and conditions of this Plan and will provide monitoring, oversight, and accountability in connection with the performance of this Plan. In furtherance of this responsibility, the BOC shall receive and review reports from Developer and its Community Benefits Director or designated liaison (as appointed or designated and during the periods specified in Section 2.5 below), as set forth in this Plan, relative to this Plan's progress and Developer's commercially reasonable efforts to implement the programs contemplated by this Plan. The BOC shall report to the CCSA its findings as to whether Developer is making commercially reasonable efforts to implement the programs contemplated by this Plan.

2.4 BOC Removal and Vacancy. The appointing person may remove its members of the BOC with or without cause. Members shall also be removed from the BOC in the event the member dies or resigns. Vacancies on the BOC shall be promptly filled by the person entitled to appoint such member in accordance with the preceding paragraphs.

2.5 Developer Monitoring and Administration. Developer will monitor this Plan and institute, and/or cause its prime contractor, stadium manager, and concessionaire to institute, commercially reasonable internal controls and monitoring procedures related to the implementation of and compliance with this Plan. During construction, report forms for tracking Local Small Business Enterprise (as defined in Section 3.1.3) participation, workforce utilization, and local participation will be required monthly from the prime contractor and all subcontractors and are a condition of each subcontract and such reports shall be made available to the CCSA. Each prime contractor and subcontractor shall be required to maintain all records related to Local Small Business Enterprise (as defined in Section 3.1.3) participation, workforce utilization, and local participation for not less five years after the expiration of the applicable subcontract and to make such records available to the CCSA upon request. After completion of construction of the Project, Developer will require its stadium manager and concessionaire submit periodic reports detailing the efforts and status of the Project with respect to this Plan. Developer will appoint a Community Benefits Director during the construction phase to provide leadership in the implementation and monitoring of this Plan. After completion of construction of the Project, Developer will designate an individual to serve as Developer's liaison regarding any issues related to compliance with this Plan.

2.6 Public Reporting. Developer will provide quarterly reports that will identify Developer's efforts to comply with this Plan during construction of the Project, and after conclusion of construction of the Project, Developer will continue to provide such quarterly reports until two consecutive reports demonstrate compliance with this Plan. Thereafter, Developer shall continue to provide such reports on an annual basis. For the avoidance of doubt, public reports will reflect efforts by the Developer as well as its various contractors charged with constructing, operating, and servicing the Project. Reports shall include identification of any programs created pursuant to this Plan and performance metrics related thereto, including, the share of the stadium construction undertaken by Local Small Business Enterprises pursuant to Section 3.2.1; minority and women workforce hiring pursuant to Section 3.3.1(I); and WMBE (as defined in section 3.1.1) hiring, purchasing and contracting shares pursuant to Section 3.1.7 and Section 3.3.4. One time (a) during the year that construction is concluded; (b) during the year after the second year of operations following Project completion; and (c) during every fifth year thereafter, the Developer's compliance with this Plan may be included in the annual audit performed by the CCSA pursuant to the stadium lease between the CCSA and the Developer, pursuant to the terms of such lease. Such audit may be requested by the BOC in its discretion; and, if requested, Developer agrees to comply with such request by providing appropriate information.

2.7 Cost of Compliance. Developer acknowledges and agrees that the implementation of, and compliance with, its commitments as set forth in this Plan will require the commercially reasonable expenditure of funds, foregoing certain revenue

streams, incurring higher operating expenses, and distributing other meaningful resource allocations (e.g., volunteer hours), either directly by Developer or by those charged with carrying the various provisions of this Plan on Developer's behalf. All parties acknowledge the resource allocations necessary to effectuate this Plan are significant and some may not be readily quantifiable. As such, nothing in this Section 2.7 or any other section of this Plan shall require Developer to allocate resources or otherwise incur costs other than on a commercially reasonable basis.

2.8 Compliance.

2.8.1 Developer Determines Noncompliance. To the extent Developer determines it is not in compliance with its obligations to implement this Plan, Developer shall prepare and submit a remedial plan to achieve compliance outlining the compliance issue or issues it has identified and specifying actions that will be undertaken to remedy areas of noncompliance. Such remedial plan may not reduce requirements of the Plan without approval of the BOC. To the extent the BOC believes that the remedial plan reduces or eliminates any of Developer's obligation under this Plan, the BOC shall work in good faith with Developer to negotiate specific remedial actions that will be taken to achieve compliance with this Plan in a manner that does not reduce or eliminate Developer's obligations within forty-five (45) days of receiving such Plan.

2.8.2 BOC Determines Noncompliance. To the extent the BOC reasonably determines Developer has failed to make commercially reasonable efforts to implement this Plan, after having received two consecutive reports from Developer indicating such noncompliance or after receiving an audit report pursuant to Section 2.6 indicating noncompliance, the BOC shall provide notice of such noncompliance to the Developer. To the extent the BOC determines that Developer is not in compliance with its obligations to implement this Plan, the BOC shall provide guidance, as necessary and appropriate, to Developer and its Community Benefits Director or its designated liaison (as appointed or designated and during the periods specified in Section 2.5) and may request specific information related to issues identified to ensure that commercially reasonable efforts are being made to implement all aspects of this Plan as specified in this Section 2.8.2. To the extent the Developer does not concur with such finding of noncompliance, Developer shall submit an explanation as to why Developer believes it is compliant with the Plan to the BOC. To the extent the Developer concurs that such noncompliance occurred, the Developer shall prepare and submit a remedial plan to achieve compliance specifying actions that will be taken to remedy areas of noncompliance. Such remedial plan may not reduce or eliminate Developer's requirements of the Plan without approval of the BOC. To the extent the BOC believes that the remedial plan reduces or eliminates any of Developer's obligation under this Plan, the BOC shall work in good faith with Developer to determine specific remedial actions that will be taken to achieve compliance with this Plan in a manner that does not reduce or eliminate Developer's obligations within forty-five (45) days of receiving such remedial plan. To the extent the parties cannot come to a resolution,

notice will be provided to the Stadium Authority and the parties will agree on a process to resolve the dispute.

III. COMMUNITY BENEFITS

Developer understands how critically important community participation is. Developer is committed, both through its own efforts and through the efforts of its contractors, to provide opportunities to participate in and benefit from the design, construction, and operation of the Project to a broad and diverse membership of the community. This Plan is a multi-faceted program to achieve participation in the Project by the local community, including people of color; women, minority and women owned businesses, veterans and other targeted members of the community (the "Targeted Groups").

This Plan includes the following benefits directed at such Targeted Groups within the community: (1) local small, woman and minority business enterprise participation; (2) community engagement; (3) workforce diversity; and (4) technical assistance and an internship program.

3.1 Local Small and WMBE Participation.

3.1.1 Overview. Strengthening the local small, minority, and female business community economically contributes to the overall economic growth and expansion of the community. Developer's program is designed to achieve meaningful and lasting benefits to the community through business opportunity that enable Local Small Business Enterprises (as defined in Section 3.1.3) and women and minority owned business enterprises ("WMBEs") to enhance and further develop and grow their businesses.

3.1.2 Commitment and Participation. The Developer and its prime contractor for the Project anticipate entering into a "guaranteed maximum price" contract (the "GMP Contract") which will integrate into that contract all aspects of the design, development, and construction of the stadium. The GMP Contract shall require that 15% of the aggregate value of the construction work performed be subcontracted to Local Small Business Enterprises, and provide that failure to comply with such requirement shall be deemed a material breach of the GMP Contract. In addition to the Local Small Business Enterprise commitment, Developer shall use reasonable commercial efforts to implement initiatives for maximizing participation in construction of the Project that include:

A. Contacting those vendors who have signed up via CCSA's website to be on CCSA's vendor list for the Project.

B. Structuring bid packages to encourage participation by WMBE firms, including defining, segmenting or sizing bid packages at levels to increase the likelihood WMBEs can successfully undertake such projects; allowing for contract partnering and encouraging larger bidders to include WMBEs as co-bidders or project subcontractors; and streamlining the bid submittal process to reduce the time and cost of submittal for WMBEs.

C. Collaborating with local small, women, and minority business organizations to identify firms for participation on the Project, including: Latin Chamber of Commerce, National Association of Minority Contractors, Women Business Enterprise Council, Nevada Contractor's Association, Western Region Minority Supplier Development Council, Asian Chamber of Commerce, Urban Chamber, and the Gay and Lesbian Chamber of Commerce Nevada (collectively, the "Local Chambers"). This shall include providing bid packages and other stadium-related contracting opportunities to the Local Chambers, so they may circulate the same to their respective members.

D. Using commercially reasonable efforts to engage and provide opportunities to WMBEs consistent with the availability of WMBE firms in the marketplace.

E. Facilitating partnerships between WMBE vendors and other vendors, including encouraging vendors to partner with WMBEs, encouraging larger vendors to subcontract work to WMBEs, and encouraging business mentorship programs that might provide professional development opportunities for WMBEs

F. Developing an accelerated payment process for small businesses to ease the cash flow difficulties such firms may experience.

G. Collaborating with its prime contractor for the Project to develop a program that encourages long-term relationships with Local Small Business Enterprises and WMBEs; that provides meaningful feedback to contractors, subcontractors and vendors relative to performance-related issues and encourages continued development of skills and abilities; that puts systems into place to ensure larger contractors and vendors are aware of Local Small Business Enterprises and WMBEs that have successfully undertaken stadium related work.

3.1.3 Definition of "Local Small Business Enterprise". A "Local Small Business Enterprise" is defined as: (1) an independent business; (2) has been in operation for a minimum of 4 years; (3) its principal place of business is in a fixed location in the state of Nevada; (4) has all necessary Nevada licenses and registrations; and (5) annual revenues in each of the immediately preceding three fiscal years has not exceeded: (i) $20,000,000 in public works projects, (ii) $10,000,000 in other construction, goods, materials, equipment and general services contracts, (iii) $2,500,000 in professional services, including, without limitation, architectural and engineering services, or (iv) $3,500,000 in trucking.

3.1.4 Certification. To ensure that the Local Small Business Enterprise program benefits only those businesses that are owned and controlled by local small business enterprises as identified in the Act, Developer will require its prime contractor to verify that firms demonstrate whether they meet the requirements for a Local Small Business Enterprise outlined above. To ensure that the WMBE program benefits only businesses owned and controlled by women and minority business owners, Developer will

require its prime contractor, stadium operator, and stadium concessionaire to verify that a recognized agency or organization has certified them. WMBE firms will be considered eligible and meeting the requirements for WMBE participation credit if they are able to show proof of certification by a recognized third-party verification service (e.g., Western Regional Minority Supplier Development Council, Women's Enterprise Business Council - West or any other similar providers of business certification cited by the Nevada Department of Business and Industry) or certification by the U.S. Small Business Administration's 8a Program, or existing minority purchasing councils, states, cities, municipalities, airport authorities, state departments of transportation or transit authorities.

3.1.5 Modification to Local Small Business Enterprise Contracting Targets. The CCSA may waive or modify the Local Small Business Enterprise hiring requirements as set forth in Section 3.1.2 if the Developer or its prime contractor presents proof satisfactory to the CCSA that there is an insufficient number of Local Small Business Enterprises available and qualified to subcontract for the work to be performed. Such proof must include evidence that: (a) reasonable efforts were made to notify small local businesses of the availability of work to be performed, which must include evidence of public advertisement calling for bids for a period of not less than 20 days before the date on which such bids must be submitted; and (b) in considering the availability and qualifications of a Local Small Business Enterprises to perform work described in Section 3.1.2, a contractor reasonably considered the work experience, safety history, and financial stability of the Local Small Business Enterprise.

3.1.6 Local Business Support. Developer will support the CCSA's efforts to accept information from interested local contractors and vendors to participate in the construction of the Project. Developer's prime contractor shall host an outreach event to local businesses, including contacting construction firms that have signed up on the CCSA website.

3.1.7 Prime Contractor Requirements. Developer shall require its Prime Contractor do each of the following:

A. Allow a Local Small Business Enterprise to which work is subcontracted to be covered by any bond or insurance of the prime contractor, provided however the prime contractor may require that such contractor or subcontractor pay its proportionate share of the cost of such bond or insurance coverage.

B. Ensure that a Local Small Business Enterprise to which work is subcontracted hire its employees in a manner that does not discriminate against any person on any basis prohibited by law.

C. Not impose any requirement on a Local Small Business Enterprise to which work is subcontracted related to the employees selected by the Local Small Business Enterprise to perform the subcontracted work.

D. Provide the mentorship program set forth in Section 3.4.1 to assist Local Small Business Enterprises to develop the skills necessary to carry out the work that is subcontracted.

3.1.8 Success of Participation. Developer shall require its prime contractor to make available to the CCSA on a periodic basis the level of participation of Local Small Business Enterprises and WMBEs in the Project. The periodic basis of such reporting shall not be less than the public reporting periods set forth in Section 2.6.

3.2 Community Engagement.

3.2.1 Overview and Participation. Developer believes in focused relationship-building and active, visible, and sustained outreach to the community. Developer's outreach approach is aimed at identifying, attracting, qualifying, and building interest and enthusiasm for the Project to the local and WMBE contracting community. Developer shall accomplish this through the following strategies during construction of the Project:

A. Developer open houses to explain the bid packages, procurement schedule and process to interested bidders.

B. Conduct pre-bid informational meetings to inform and advise Local Small Business Enterprises and WMBEs of the potential opportunities on the Project.

C. Meeting regularly with the Local Chambers to update them on the Project. Developer shall also encourage input and recommendations from Local Chambers relative to strategies that might support this Plan, increase awareness or otherwise be helpful in effectuating this Plan.

D. Communication via Internet, radio, newspaper, and other media.

E. Liaison with community organizations, neighborhood groups, elected officials, community leaders, and agencies.

3.2.2 Community Access Programs. Developer will encourage and support community programs for veterans and military families, disadvantaged and at-risk youth, and low-income residents. Such community programs may include offering no cost or discounted admission tickets for the benefit of veterans and military families, disadvantaged and at-risk youth, and low-income residents.

3.3 Workforce and Business Diversity.

3.3.1 Overview and Participation. Developer is committed to ensuring that the community participates in the construction and operation through employment opportunities. Developer has created initiatives that have led to and will continue to lead to opportunities for women, people of color and other Targeted Groups. Developer will

undertake the following initiatives to maximize employment opportunities on the Project for Targeted Groups during design, construction, and operations as specified:

A. *Collaboration* – Collaborating with community based organizations throughout the design, construction and operation phase of the Project, which may include Local Chambers and similar organizations, to assist with the recruitment and referral of workers and businesses and the development of strategies that might support this Plan, increase awareness or otherwise be helpful in effectuating this Plan.

B. *Low Income* – Developer will implement the Community Workforce Program, which provides construction entry-level employment opportunities for low-income residents through short-term "hands on" industry experience from which participants can learn and identify a career path should they desire to pursue opportunities within the construction industry.

C. *Veterans* – Developer will partner with transition agencies, including Helmets to Hardhats, Developer will endeavor to promote and provide relevant employment opportunities to veterans.

D. *Faith Based Leaders* – Developer will maintain relationships with the faith based community leaders throughout the design, construction, and operation phases of the Project, utilizing their relationship with the communities they serve to communicate employment and business development opportunities on the Project.

E. *Apprenticeship Training* – Developer will work closely with the building trade unions to enable women and minorities to enter into apprenticeship programs during construction.

F. *Work Readiness Support* – Developer will partner with local sourcing agencies to ensure disadvantaged individuals are prepared for construction work by providing basic work clothes, boots, and tools.

G. *Union Partnership* – Partnering with unions to facilitate entry of women and minorities into apprenticeship programs during construction. To the extent Developer enters into a project labor agreement, such agreement shall be consistent with this Plan.

H. *LGBTQ Community* – Developer will maintain relationships with the Gay and Lesbian Chamber of Commerce Nevada and community leaders throughout the design, construction, and operation phases of the Project, to communicate employment and business development opportunities on the Project.

I. *Diversity* – Developer's contract with its prime contractor, Mortensen-McCarthy, shall require a workforce participation target of not less than a combined total of thirty-eight percent (38%) of construction work hours shall be performed by minority and female workers. With respect to operations after the opening of the Project,

Developer's contracts with any concessionaire and any stadium manager overseeing operations shall require such contractors to set a workforce participation target of not less than a combined total of fifty-five percent (55%) work hours on days in which an event takes place, including setup and tear down, shall be performed by minority and female workers.

3.3.2 First Source Employment. Developer will consider Targeted Groups for employment in connection with the construction and operation of the Project, including considering referrals of qualified Targeted Groups that have completed training and apprenticeship programs offered pursuant to this Plan.

3.3.3 Livable Wage Requirements. Developer will encourage and support livable wage programs for employees working on the construction and operation of the Project. All employees working on the Project will be paid and receive benefits to the extent required by and in full compliance with any applicable laws, rules or regulations. Service contracts shall not be subdivided into two or more contracts that logically should be made a single transaction if the purpose of subdividing is to avoid the requirements of this paragraph.

3.3.4 Utilization of Certified Business Enterprises; Minority Workforce. Throughout the design, construction, and operation of the Project, Developer will encourage and support: (i) opportunities for minority and women owned businesses and other Targeted Groups, and (ii) purchasing opportunities for minority and women owned businesses and other Targeted Groups for direct services, goods, procurement, and vendor opportunities. Further, Developer will utilize reasonable good faith efforts to encourage and support equal employment hiring opportunities that include: (a) minority hiring opportunities; (b) hiring opportunities for low income residents; (c) hiring opportunities for individuals with disabilities; (d) hiring opportunities for veterans; and (e) hiring opportunities for members of the LGBTQ community. The Developer, the CCSA, and the BOC acknowledge that the design of the stadium itself was largely adapted from a prior project, with substantial design work completed prior to the creation of this Plan. Developer agrees to utilize good faith efforts to encourage the participation of local businesses, minority and women owned businesses, and other Targeted Groups in the remaining design work occurring after implementation of this Plan on projects on the stadium site itself, pre-construction infrastructure supporting the Project, including the Developer's temporary office space, preview and sales center, landscape design, construction training centers, and environmental and engineering work.

3.3.5 Encouraging Opportunities for WMBEs During Stadium Operations. In a manner generally similar to that set forth in Sections 3.1.2 (B), (E) and (G) for the construction phase of the project, the Developer will encourage the design of bid packages, facilitation of partnership, and business retention programs for contracting, subcontracting, purchasing, and procurement opportunities during the operations phase of the Project where it is commercially reasonable to do so.

3.3.6 Annual Stadium Opportunity Community Outreach. At least once each calendar year during the construction and operations phases of the Project, the Developer shall host an employment and business development opportunity fair, or host or participate in a similar event, designed to inform and encourage participation in stadium-related employment and business opportunities for small businesses, WMBEs, and other Targeted Groups. The Developer will use reasonable commercial efforts to ensure that the event is appropriately publicized and will encourage participation by the stadium manager, stadium concessionaire, and other major Project contractors and vendors.

3.3.7 Soliciting Feedback from Local Chambers. At least once each calendar year throughout the construction and operations phases of the Project, the Developer shall solicit input from Local Chambers relative to the effectiveness of the employment and business development initiatives set forth in this plan. The Developer agrees to use reasonable good faith efforts to integrate such input where it might increase, improve or enhance employment or business development opportunities contemplated by this plan where it is commercially reasonable to do so.

3.4 Mentoring/Technical Assistance/Internships.

3.4.1 Local Small Business Enterprise Resource Center. To address capacity building of small local, women and minority owned businesses, Developer will develop a Local Small Business Enterprise Resource Center as a tool to strengthen and expand local small, women and minority owned businesses in the community during the construction process. The resource center will provide a knowledge base and technical assistance in all facets of the construction business, with Developer personnel and consultants utilized as construction experts providing guidance and support. The services of the resource center will be concentrated around business development, business administration, project management, and technical services for Local Small Business Enterprise firms to develop and enhance their capabilities and competencies for future growth. The center services would be available to firms involved with the Project.

3.4.2 Workforce Training and Development; Apprenticeship Participation. During the construction and operation of the Project, Developer will work with local community partners, such as unions, prime contractors, applicable subcontractors, universities, its concessionaire, its stadium manager overseeing operations, and other organizations to train a diverse and competent workforce to prepare Targeted Groups to become pre-apprentices in the construction and operation-related trades (e.g., engineering, facility operations, sales and marketing, and information technology). Developer will provide support services for Targeted Groups taking classes. Developer shall consider training programs recommended by the BOC from time to time and shall specifically consider career workshop programs, individual employment, service plan programs, vocational skills training, work support services, and job placement services.

3.4.3 Internship Program. Developer's internship program during construction will offer high school and college students the opportunity to participate in paid summer internships that will expose them to the construction industry and will give students the

opportunity to gain experience in varied aspects of the construction business. Developer will use reasonable commercial efforts to include participation in the internship program with any contract with its prime contractor and any such prime contractor that subcontracts work to a Local Small Business Enterprise shall provide a mentorship program to assist the Local Small Business Enterprise to develop the skills necessary to carry out the work that is subcontracted.

IV. CHARITABLE AND CIVIC ENDEAVORS

4.1 Raiders Community Relations. Developer will work with the Raiders to continue its long-time tradition of community outreach through the Raiders Community Relations department, a department within the Raiders organization devoted to ensuring that the organization serves as an asset to Clark County, above and beyond the civic and economic benefits flowing to a host community for a storied National Football League club. Developer will work with the Raiders to continue annual production of the Raiders annual community report, in a format substantially similar to the report produced for 2016. All members of the Raiders organization, including members of the Raiders NFL team, are encouraged to reach out to the local community to support local charitable and civic causes. The Raiders' community outreach programs have included events such as, for example:

- Player participation in programs at local schools designed to encourage students to sharpen their skills both on the field and in the classroom;
- Player participation in Breast Cancer Awareness Day and fundraising;
- Player participation in programs designed to encourage young children develop a healthy lifestyle through proper diet and exercise;
- Player participation in efforts to raise awareness and/or fundraise for various charitable causes through the My Cleats program and other initiatives;
- Player participation in local food drives and bringing holiday meals and gifts to members of the local community who would not otherwise have an opportunity to celebrate the holidays;
- Hosting multiple visits by the Make-A-Wish Foundation that provided children the opportunity to spend time with their favorite players;
- Hosting player safety clinics for area youth football coaches; and
- Providing to charitable donations to numerous organizations including local scholarship funds, Toys For Tots, and youth and veteran organizations.

4.2 NFL Grants and Funding. The Raiders will work with the National Football League to obtain grants to fund facilities improvements for local community athletic and educational organizations.

4.3 Raiders Foundation. The Raiders Foundation, the primary charitable arm of the Raiders, will be active in Clark County to increase community and civic health through military support and youth development.

Exhibit R

Assignment and Assumption Agreement

THIS ASSIGNMENT AND ASSUMPTION AGREEMENT ("Agreement") is made as of the ___ day of _____, 2018 (the "Effective Date"), by, LV STADIUM EVENTS COMPANY, LLC, a Nevada limited liability company ("StadCo"), MORTENSON-McCARTHY LAS VEGAS STADIUM, A JOINT VENTURE, comprised of M. A. Mortenson Company, a Minnesota Corporation, and McCarthy Building Companies, Inc., a Missouri Corporation ("MMJV"), and HNTB NEVADA, INC., a Nevada corporation ("HNTB") (each of the forgoing entities is referred to herein individually as a "Party" and together the "Parties").

W I T N E S S E T H:

WHEREAS, StadCo and HNTB have entered into that certain Agreement for Architectural and Engineering Services Agreement, dated as of _____, 2017 (the "AOR Agreement") relating to the Las Vegas Raiders Stadium Project (the "Project"), a fully executed copy of which has been provided to the Parties;

WHEREAS, StadCo has engaged MMJV as the design-builder for the Project pursuant to that certain Guaranteed Maximum Price Design-Build Agreement dated as of _____, 2017 (the "Design-Build Agreement"), a fully executed copy of which has been provided to the Parties;

WHEREAS, pursuant to the Design-Build Agreement, StadCo has agreed that upon the execution of the GMP Amendment (as defined in the Design-Build Agreement) by StadCo and MMJV it will assign to MMJV, and MMJV has agreed to assume, as of the Effective Date, the AOR Agreement; and

WHEREAS, HNTB and MMJV have agreed to make certain amendments to the AOR Agreement following assignment of the AOR Agreement from StadCo to MMJV, as set forth in Section 6 below and Schedule 1 attached hereto.

NOW, THEREFORE, for valuable consideration, the receipt and sufficiency of which is hereby acknowledged, Parties agree as follows:

1. Defined Terms. Except as otherwise expressly defined herein, all capitalized words and phrases used herein shall have the same meanings as ascribed to such words and phrases in the AOR Agreement.

2. Assignment and Delegation. StadCo hereby assigns all of its rights and delegates all of its duties and obligations under the AOR Agreement to MMJV, provided the responsibilities and obligations of StadCo set forth in Article 6 of the AOR Agreement shall, after the Effective Date, remain the responsibilities and obligations of StadCo and not Design-Builder.

3. Assumption. MMJV hereby accepts the foregoing assignment and delegation, and in consideration thereof, hereby covenants and agrees that, from and after the Effective Date, MMJV will assume such rights, duties and obligations that are to be observed and performed by StadCo on and after the Effective Date.

4. Consent and Agreement of HNTB. HNTB consents to the foregoing assignment and assumption and confirms that, from and after the Effective Date, all obligations and duties it owed to StadCo or StadCo's Representative under the AOR Agreement are now owed to MMJV, including obligations and duties that accrued and were performed prior to the Effective Date; provided, however, those specific duties or obligations that are referenced in the amendments set forth in the attached Schedule 1 as being owed to StadCo (or owed jointly to StadCo and MMJV) shall be for the benefit of, and may be enforced by, StadCo and/or MMJV, as the case may be.

5. Representations and Warranties of HNTB and StadCo.

a. HNTB and StadCo each represent and warrant that as of the Effective Date, (i) HNTB has been paid:

- $_____ in total for all Basic Services performed,
- $_____ in total for Reimbursable Expenses,
- [redacted] in total for the Project Specific Professional Liability Insurance policy,

through _____, 2018, and accordingly, the unpaid balance of the Fixed Fee under the AOR Agreement is $_____ and the unpaid balance of the Reimbursable Expenses is $_____; (ii) that there currently are no outstanding amounts due or payable by StadCo to HNTB under the AOR Agreement; and (iii) there are no executed or pending Requests For Change Order, AOR Change Directives, AOR Change Orders or Additional Services Directives except as follows: _____. Except as noted in part (iii) of the preceding sentence, HNTB warrants and represents that as of the Effective Date it is not aware of any facts or events that would form the basis of a request for Additional Services.

b. HNTB warrants and represents that it is not in default under or breach of the AOR Agreement and that it is not aware of any default or breach, or of any event that with the giving of notice would constitute a default or breach, on the part of StadCo under the AOR Agreement.

c. StadCo warrants and represents that it is not in default under or breach of the AOR Agreement and that it is not aware of any default or breach, or of any event that with the giving of notice would constitute a default or breach, on the part of HNTB under the AOR Agreement.

6. Amendments to AOR Agreement. Simultaneously with the execution of this Agreement, MMJV and HNTB hereby agree to amend the AOR Agreement using the form included as Schedule 1 attached hereto and made a part hereof. Once executed, the amendments in Schedule 1 shall be deemed an executed AOR Change Order.

7. Governing Law. This Agreement shall be governed by the laws of the State of Nevada without regard to principles of conflicts of law. Any litigation under this Agreement shall be brought in any court having proper jurisdiction that is located in Clark County, Nevada, and all Parties hereto consent to personal jurisdiction and venue in such court.

8. Assignment. No Party shall assign any rights or obligations under this Agreement without the prior written consent of each of the other Parties hereto; provided, however, that this Agreement may be assigned by either MMJV or HNTB in connection with an assignment of the AOR Agreement that is permitted pursuant to the terms and conditions of the AOR Agreement.

9. Miscellaneous. The captions contained in this Agreement are for convenience and reference only and in no way define, describe, extend or limit the scope or intent of this Agreement or the intent of any provision contained herein.

10. Authority. Each Party represents to the other Parties that it has full power and authority to enter into this Agreement and the persons signing on behalf of the respective Parties hereto are authorized to do so.

11. Counterparts. This Agreement may be executed by the Parties in separate counterparts, each of which when so executed and delivered shall be an original, but all such counterparts shall together

constitute but one and the same instrument. The counterparts of this Agreement may be executed and delivered by facsimile or other electronic signature by any of the Parties to any other Party and the receiving Party may rely on the receipt of such document so executed and delivered by facsimile or other electronic means as if the original had been received.

[SIGNATURES ON NEXT PAGE]

IN WITNESS WHEREOF, each of the parties hereto have caused this Assignment and Assumption Agreement to be executed as of the Effective Date.

STADCO:

LV STADIUM EVENTS COMPANY, LLC

By: _____
Name: _____
Title: _____

[Signatures continued on next page]

MORTENSON-MCCARTHY LAS VEGAS STADIUM, A JOINT VENTURE
M. A. Mortenson Company, a Minnesota Corporation, (0072732)

By: _____
Name: _____
Title: _____

MORTENSON-MCCARTHY LAS VEGAS STADIUM, A JOINT VENTURE
McCarthy Building Companies, Inc., a Missouri Corporation (0066125)

By: _____
Name: _____
Title: _____

[Signatures continued on next page]

HNTB NEVADA, INC.

By: _____
Name: _____
Title: _____

[End of signature pages]

Schedule 1
[Begins on Next Page]

AMENDMENT/CHANGE ORDER TO THE AOR AGREEMENT

This amendment to the AOR Agreement ("Amendment") is entered between MORTENSON-McCARTHY LAS VEGAS STADIUM, A JOINT VENTURE, comprised of M. A. Mortenson Company, a Minnesota Corporation, and McCarthy Building Companies, Inc., a Missouri Corporation ("MMJV" or "Design-Builder") and HNTB NEVADA, INC., a Nevada corporation ("HNTB" or "AOR") as of the ___ day of _____, 2018 as set forth herein.

WHEREAS HNTB entered into the AOR Agreement with LV STADIUM EVENTS COMPANY, LLC, a Nevada limited liability company ("StadCo") to provide professional design services relating to the new Las Vegas Stadium.

WHEREAS StadCo assigned all its rights, duties and obligations under the AOR Agreement to MMJV;

WHEREAS MMJV and HNTB now desire to make modifications to the AOR Agreement following the assignment:

NOW, THEREFORE, for valuable consideration, the receipt and sufficiency of which is hereby acknowledged, MMJV and HNTB agree as follows:

Amendments to the AOR Agreement

The below referenced provisions of the AOR Agreement are modified as follow (all references are to the AOR Agreement):

1. Replace, in every instance (a) "StadCo" with "Design-Builder" and, as applicable, (b) "StadCo's Representative" with "Design-Builder" in the following Sections/Articles:

    - Section 2.5,
    - Section 2.6,
    - Section 2.64,
    - Section 3.1,
    - Section 3.13.1,
    - Section 3.13.2 (excluding sub-sections),
    - Section 3.13.2.1,
    - Sections 3.13.2.4 through 3.13.4,
    - Sections 3.14.1 through 3.14.2,
    - Section 3.16.1 (limited to Subcontracts with an effective date subsequent to the Effective Date of this amendment),
    - Sections 3.16.2 through 3.17,
    - Section 3.21,
    - Section 3.24.2,
    - Sections 5.1 through 5.2.2,
    - Sections 5.2.4 through 5.2.20,
    - Sections 5.2.22 through 5.5.1,
    - Section 6.1.10,
    - Sections 7.1 through 7.5,
    - Sections 7.7 through 7.13,
    - Sections 8.1 through 8.2.2,
    - Sections 8.2.4 through 8.4.3,
    - Section 10.1,
    - Section 10.4,
    - Sections 10.6 through 10.10,

- Article 14,
- Section 15.2,
- Sections 15.4 through 15.7, and
- Section 15.18.

All Section references include any and all Sub-Sections unless indicated otherwise above.

2. The following sentences are hereby added to the end Section 3.1:

> AOR acknowledges that Design-Builder is relying on AOR's special skill and expertise in projects of the type described herein. Design-Builder and AOR agree the Services provided by AOR pursuant to this AOR Agreement shall be performed in accordance with the Standard of Care.

3. The following *italicized* language is added to the first sentence in Section 3.2.1:

> The parties accept the relationship of trust, good faith, and confidences established by this Agreement, and agree to cooperate with each other and take all actions reasonably necessary to enable each other to perform this Agreement in a timely, efficient, and commercially reasonable manner (however nothing in this Agreement shall be construed as creating a fiduciary relationship between AOR and StadCo *-or- AOR and Design-Builder*).

4. The following sentences are hereby added to the end Section 4.9.1:

> During the preparation of final Construction Documents and bid packages, including, but not limited to, final Drawings and final Specifications, and AOR shall incorporate any comments, in accordance with the Standard of Care, submitted by StadCo and StadCo's Representative in the Construction Documents. Any such incorporation of comments submitted by StadCo and StadCo's Representative will be made without adjustments to AOR's compensation, except as provided in Article 5. AOR shall submit the final Construction Documents to StadCo for approval in an electronic format acceptable to StadCo and consistent with the BIM Execution Plan. Construction Documents submitted by AOR to StadCo for final bidding and construction purposes shall be signed and stamped by AOR and AOR's Consultants responsible for preparing same, all in accordance with Applicable Laws.

5. The following sentence is hereby added to the end of Section 4.9.9:

> The foregoing documents will be delivered to StadCo at the same time that such documents are delivered to the Design-Builder.

6. The following two sentences in Section 4.10.3 are modified to remove the words stricken-through as shown below:

> ~~StadCo shall require each Contractor to~~ Design-Builder shall provide to AOR prior to the commencement of its construction work a schedule of the dates for delivery to AOR of its Submittals. Such schedules shall be priority based and, to the extent permitted by the Master Project Schedule, Submittals will be spaced so as not to unduly overburden AOR or the AOR's Consultants. ~~StadCo shall require each Contractor to~~ Design-Builder shall review for completeness and correctness and approve all of its Submittals and those of its Subcontractors before they are sent to AOR for review and approval.

7. The following sentence is hereby added to the end of Section 4.10.3:

It shall be the responsibility of StadCo to require its Separate Contractors (other than Design-Builder) to review for completeness and correctness and approve all of its submittals and those of its subcontractors before they are sent to AOR for review and approval.

8. The last two sentences of Section 4.10.7 are hereby deleted.

9. Section 4.10.13 is deleted and replaced with the following new Section 4.10.13:

4.10.13 On or before the 27th day of any given month, Design-Builder shall submit to and review with StadCo and AOR a preliminary, draft version of Design-Builder's Application for Payment, together with the required supporting data (the **"Pencil Draft"**). On or before the 6th day of the following month, Design-Builder, StadCo and AOR shall meet to review the Pencil Draft. AOR shall consult with and obtain the concurrence of any AOR's Consultants with respect to any elements of the Work covered by the Application for Payment falling within their respective areas of specialization. Design-Builder shall revise the Pencil Draft in accordance with any objection or recommendation of StadCo and AOR that is consistent with the requirements of the Contract Documents, and AOR shall certify the Application for Payment prior to the time it is transmitted to StadCo or any Construction Lender by StadCo's Representative. By certifying the Application for Payment, AOR agrees that the percentage complete identified by the Design-Builder is appropriate and to the best of AOR's and AOR's Consultants knowledge, information, and belief: (i) the Work has progressed to the point indicated in the Application for Payment; (ii) the Work has been performed in accordance with the Contract Documents (subject to an evaluation of the Work for conformity with the Contract Documents upon Substantial Completion, to the results of any subsequent tests required by or performed under the Contract Documents, to minor deviations from the Contract Documents correctable prior to completion, and to any specific qualifications stated in the Application for Payment and approved by StadCo's Representative); and (iii) that the Design-Builder is entitled to payment in the amount sought in the Application for Payment. The certification of AOR on an Application for Payment shall not be a representation that AOR has (1) made exhaustive or continuous on-site inspections to check the quality or quantity of the Work, (2) reviewed construction means, methods, techniques, sequences or procedures, (3) reviewed copies of requisitions received from Subcontractors and material suppliers and other data requested by StadCo to substantiate the Contractor's right to payment or (4) ascertained how or for what purpose Design-Builder has used money previously paid to it by StadCo.

10. Add the words "and Design-Builder" after StadCo in the last sentences of Section 4.10.14.

11. The following sentence is hereby added to the end of Section 4.10.16:

The punch-list shall be submitted to StadCo for its review and approval.

12. Section 5.2.3 is deleted and replaced with the following new Section 5.2.3:

5.2.3 Making material revisions in Design Documents previously approved or directed by StadCo (which after the execution of the GMP Amendment shall mean the GMP Documents or 100% Construction Documents as applicable) or Design-Builder when such revisions (i) are inconsistent with written approvals or directions previously given by StadCo or Design-Builder or (ii) are due to causes beyond the control of AOR;

13. Section 5.2.21 is deleted and replaced with the following new Section 5.2.21:

5.2.21 Providing services necessitated by any modification to the Construction Cost Budget;

14. Notwithstanding anything herein to the contrary, the responsibilities and obligations of StadCo set forth in Article 6 (excluding Section 6.1.10) shall, after the Effective Date, remain the responsibilities and obligations of StadCo and not Design-Builder.

15. Section 6.1.10 is deleted.

16. The following Section 6.3 is hereby added to Article 6:

6.3 Design-Builder's Responsibilities. Design-Builder shall have the following responsibilities and obligations:

6.3.1 Reliance by AOR. AOR's right to rely upon the information furnished by Design-Builder shall be limited to the same extent that Design-Builder is entitled to rely on such information by the original provider, unless such information was created by Design-Builder or it Subcontractors and provided to AOR for the specific purpose of AOR's use for the Project; provided, however, if AOR becomes aware or, in the exercise of its Standard of Care, should have become aware, of any defect, error, or omission in information furnished by Design-Builder, AOR shall not be entitled to rely upon the defective or erroneous information. To the extent AOR becomes aware that there is a defect in the information furnished by Design-Builder, AOR shall immediately inform Design-Builder. If Design-Builder observes or otherwise becomes aware of any fault or defect in the Project or nonconformance with the Contract Documents, prompt written notice thereof shall be given by Design-Builder to AOR.

6.3.2 Design-Builder's Approvals and Estimates. Design-Builder shall ensure that AOR is timely provided all applicable reviews, authorizations, approvals (including any applicable third-party approvals), and construction estimates and pricing, all of which is required to be provided to AOR by Design-Builder

6.3.3 Communications with Others. Design-Builder shall include the AOR in all communications with StadCo, Contractors or other Project Team members that relates to or potentially impact the AOR's Services or professional responsibilities. Design-Builder shall promptly notify AOR of the substance of any direct communications. Design-Builder shall also promptly provide AOR with copies of any Construction Change Directives, Change Orders, and any Amendments to the Design-Build Agreement that impact or relate to the Services.

6.3.4 Project Site Access. Design-Builder shall provide the AOR with safe and secure access to the Project Site and the Work as necessary for the performance of the Services, provided AOR shall be responsible for ensuring its employees have the adequate personal safety equipment.

6.3.5 Other Subcontractors. Design-Builder shall coordinate the Work of its Subcontractors with those services provided by AOR and AOR's Consultant(s).

6.3.6 Request for Changes, Additional Services Directive, and AOR Change Orders. Design-Builder shall process all Requests for AOR Change Orders, Additional Services Directives, and AOR Change Orders (as further defined in Article 5). Design-Builder shall respond within five (5) days to all AOR change-related requests/communications, unless the Parties agree in writing to longer response time duration.

17. Add the following new paragraph to Section 10.11:

> Notwithstanding any other provision of this Agreement, neither Design-Builder nor AOR shall be liable to the other party for Consequential Damages or punitive damages (excepting the Liquidated Damages contained within the Design-Build Agreement which are subject to the limitation set forth above in Section 10.10) regardless of whether it has been advised of the possibility of such damages, whether based upon contract, tort, breach of warranty, negligence, strict liability or otherwise. It is understood that this constitutes a

mutual waiver of all Consequential Damages and punitive damages for any claims or disputes or other matters in question arising out of or relating to this Agreement. Notwithstanding the foregoing, nothing contained herein shall limit or invalidate any insurance coverage otherwise required under this Agreement

18. Add the following new paragraph to Section 10.12:

The Design-Builder and AOR mutually agree that the obligations and limitations set forth in this Article, including all indemnity obligations and the limitations of liability, (the "Article 10 Provisions") shall be construed to retroactively apply as of the Effective Date. Both Design-Builder and AOR expressly waive the right to assert any defenses, claims, counterclaims, crossclaims or other similar causes of action in any legal proceedings or arbitrations premised on any allegation that the Article 10 Provisions do not apply to all services or work performed subsequent to the Effective Date, including any services or work that may have been performed under the Letter of Engagement. Design-Builder agrees to be bound to the representations and commitments set forth in this Section to the same extent as StadCo.

19. Notwithstanding anything in Article 13 to the contrary, where a dispute or controversy does not involve StadCo or a claim that would be presented to StadCo, then AOR and Design-Builder will resolve the dispute or controversy using the following procedures:

In the event of a dispute between Design-Builder and AOR arising out of or related to this Agreement, the aggrieved party shall notify the other party of the dispute in writing within a reasonable time after such dispute arises. If the parties cannot thereafter resolve the dispute within seven (7) days after the initial notification, each party shall nominate a senior officer of its management to meet to resolve the dispute by direct negotiation.

If the parties are unable to resolve the dispute through direct negotiations within twenty-one (21) days after the initial notification, then all disputes shall be submitted to mediation pursuant to JAMS Dispute Resolution in effect as of the effective date of this Agreement. The parties agree to conduct a mediation session as soon as reasonably practicable and in no event later than thirty (30) days following selection of a mediator. Regardless of which party initiates the mediation, the parties shall share the filing fees and mediator fees equally. The parties agree that submission of the dispute to mediation pursuant to this provision shall be a condition precedent to the ability to file an arbitration demand.

Should such negotiation and mediation efforts fail to resolve the dispute, then the parties agree to pursue resolution of the dispute by arbitration in accordance with the JAMS Engineering and Construction Arbitration Rules and Procedures.

20. Section 15.1 is deleted and replaced with the following new Section 15.1:

15.1 Assignment of this Agreement. Subsequent to the assignment of this Agreement to from StadCo to Design-Builder, Design-Builder may assign this Agreement only in connection with an assignment by Design-Builder of the Design-Build Agreement as permitted by the Design-Build Agreement. AOR shall not assign or transfer any or all of its interest in this Agreement, or any claim under this Agreement, or delegate any of its duties under this Agreement without the express written consent of StadCo, and any such assignment or delegation shall be null and void and of no effect. Any Construction Lender or other lender taking an assignment for security purposes of this Agreement shall not have any liability to AOR under this Agreement, unless and until such lender forecloses or otherwise becomes the owner of StadCo's interest in the Project and then only for services requested by such lender during its period of ownership. Promptly but in no event more than ten (10) days after delivery of a request to AOR, AOR shall deliver to any Construction Lender or any other lender of StadCo a consent to the assignment of this Agreement to

such lender in form reasonably required by such lender, including but not limited to an agreement of AOR to perform its remaining obligations under this Agreement for the benefit of such lender or any party which becomes the developer or StadCo of the Project by virtue of a foreclosure or deed in lieu of foreclosure, so long as AOR is compensated for its Services in accordance with this Agreement, including all outstanding amounts owed. Subject to the foregoing, this Agreement shall be binding upon and inure to the benefit of the Parties and their respective heirs, successors, assigns, and legal representatives.

21. In Section 15.3 delete the notice parties and addresses for StadCo and replace with the following:

If delivered to Design-Builder:

Mortenson-McCarthy Las Vegas Stadium, a Joint Venture
700 Meadow Lane North
Minneapolis, Minnesota 55422
Attn: John V. Wood, Senior Vice President

With a copy to:

(a) M. A. Mortenson Company
700 Meadow Lane North
Minneapolis, Minnesota 55422
Attn: Dwight A. Larson, SVP & General Counsel

(b) McCarthy Building Companies, Inc.
6225 No. 24th Street, Ste. 200
Phoenix, Arizona 85016
Attn: Alison Stahl, Regional Counsel

22. Add the following new paragraph to Section 15.8:

If a Design-Builder or AOR brings an action, including, but not limited to, any arbitration or litigation proceeding (including, without limitation, any related appeals thereof), to enforce or interpret any of the terms of this Agreement or to recover damages as a result of a breach of this Agreement, the prevailing party shall be entitled to recover from the party not prevailing the costs and expenses, including but not limited to reasonable attorneys' fees, actually incurred by the prevailing party in prosecuting or defending the action. In the case of multiple claims or claims involving multiple parts, the prevailing party shall only be entitled to attorneys' fees under this provision which are attributable to the particular claim or part of the claim on which the party prevailed. Both Design-Builder or AOR waives its attorney-client privilege only to the extent of disclosing information necessary for the determination of the reasonableness of any attorneys' fees claimed by a prevailing party.

23. Add the following new paragraph to Section 15.9:

The rights, duties and obligations of Design-Builder and AOR to this Agreement which imply performance under this Agreement beyond its termination or expiration, including but not limited to any and all indemnification provisions and limitations of liability, shall survive the termination of this Agreement.

24. Add the following new paragraph to Section 15.12:

In the event of a default under this Agreement, each Design-Builder and AOR shall look solely to the assets of the other party for payment, and none of the members or affiliated Persons of the other party shall under any circumstances be liable to the other party for

any amount that may be due and owing for any judgment obtained. Neither party shall name any member or affiliated Person of the other party in any suit to enforce this Agreement.

25. Section 15.14 are deleted and replaced with the following new Section 15.14:

This Agreement, including any amendments hereto, shall not be construed against the drafter.

26. Section 15.16 is deleted and replaced with the following new Section 15.16:

To the maximum extent permitted by law, each Design-Builder and AOR waives the right to trial by jury in any litigation between them relating to this Agreement or the Project.

27. Section 15.17 is deleted and replaced with the following new Section 15.17:

No waiver by either Design-Builder and AOR of any breach of any term, provision, or condition contained in this Agreement, or the failure to insist upon strict performance thereof shall be deemed to be a waiver of such term, provision or condition as to any subsequent breach thereof or a waiver of any other term, provision, or condition contained in this Agreement. None of the provisions of this Agreement or rights provided herein shall be deemed waived by either party unless waived in writing by such party. The exercise of any right or remedy hereunder shall not be deemed to preclude or affect the exercise of any other right or remedy provided herein.

[End of Amendments]

This Amendment may be executed by Design-Builder or AOR in separate counterparts, each of which when so executed and delivered shall be an original, but all such counterparts shall together constitute but one and the same instrument. The counterparts of this Amendment may be executed and delivered by facsimile or other electronic signature by either party to the other party and the receiving party may rely on the receipt of such document so executed and delivered by facsimile or other electronic means as if the original had been received.

IN WITNESS WHEREOF, each of the parties hereto have caused this Amendment to be executed as of the date set forth above.

[Signatures On Next Page]

MORTENSON-MCCARTHY LAS VEGAS STADIUM, A JOINT VENTURE
M. A. Mortenson Company, a Minnesota Corporation, (0072732)

By: _____
Name: _____
Title: _____

MORTENSON-MCCARTHY LAS VEGAS STADIUM, A JOINT VENTURE
McCarthy Building Companies, Inc., a Missouri Corporation (0066125)

By: _____
Name: _____
Title: _____

[Signatures continued on next page]

HNTB NEVADA, INC.

By: _____
Name: _____
Title: _____

[End of signature pages]
